



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 22, 2023
WEATHER:	Temp: 46 – 56°F Cloudy, RH: 47% Pressure: 30.41" Hg Wind: SE @ 13 mph
TIME:	07:00 – 15:30

Project Team

General Contractor and Subcontractors:

- Mega Contracting Group, LLC
- Creamer Environmental, Inc. (CEI)

Engineers and Consultants:

- Roux Environmental Engineering and Geology, D.P.C.
- GZA GeoEnvironmental, Inc.

Remedial Action Work Summary

Work Activities Performed Onsite:

- Pre-trench work continued in preparation of steel sheet piles installation associated with support of excavation (SOE) in Parcel III and Parcel IV.

Contractor Work Performed Onsite:

CEI continued pre-trench work for sheet pile alignment in waste characterization grid WC-9 between Gas Holder 3 and Gas Holder 4. Pre-trench work also occurred along the east side of Gas Holder 4. Construction debris and other obstructions for SOE sheet pile installation were removed and stockpiled for future disposal offsite. Excavated soil was placed back in the trenched areas and exposed soil was covered with plastic liner at the end of the day. Dust control measurements (wetting, tarping, limiting vehicle speeds, etc.) and odor suppression (foam application) were conducted to ensure dust and odors did not impact the neighborhood. No work was conducted inside the tension fabric structure (TFS) and the vapor managements system (VMS) was not operated.

Air Monitoring:

- No community air monitoring program (CAMP) exceedances were observed during the day.
- GZA GeoEnvironmental Inc. will provide a summary report for CAMP activities.

Erosion and Sediment Control

- Erosion and sediment controls were inspected to ensure that silt fence and filter sock were undamaged and operational.

Sampling Conducted:

- None.

Other Items of Note:

- Utility work unrelated to this project continued offsite along Nevins and Degraw Streets.

Imported Material

Name - Location	Source	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Vulcan ASTM #3 (1 ½" Stone)	Vulcan Hamburg Quarry		26.03	7	179.3
Vulcan General Fill	Vulcan Wantage Quarry		231.12	95	2417.38

**DAILY STATUS REPORT**

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 22, 2023
WEATHER:	Temp: 46 – 56°F Cloudy, RH: 47% Pressure: 30.41" Hg Wind: SE @ 13 mph
TIME:	07:00 – 15:30

Exported Material

Material	Facility	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Concrete for Recycling	Bayshore			20	421.87
Concrete for Landfill	WM Fairless			41	~960.59
TCE Impacted Haz Hot Spot	CWM Emelle			7	161.72
Cd Impacted Haz Material from WC-5	CWM Emelle			3	49.45
Cd Impacted Haz Material from WC-5	Clean Earth NJ			16	397.75
Non-Haz Contaminated Urban Fill	WM Fairless			99	~2,090
MGP soil with TCE>25 ppm	Clean Earth ESMI			112	~2,472

Exported Material Truck Log

Number	Excavation Grid	Disposal Facility	Disposal Profile	Manifest Number	Trucking Company	Truck License Plate

Dewatering


Time	Totalizer Volume (gallons)*
NA	2,364,306
Water treated and discharged since last report:	0 gallons

Anticipated Upcoming Work Activities

Continued pre-trenching around former Gas Holder 3 and 4 to remove obstructions for upcoming installation of steel sheeting for support of excavation. Load out of stockpiled concrete from Parcel IV for disposal at Waste Management Fairless.


PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 22, 2023
WEATHER:	Temp: 46 – 56°F Cloudy, RH: 47% Pressure: 30.41" Hg Wind: SE @ 13 mph
TIME:	07:00 – 15:30

Site Layout

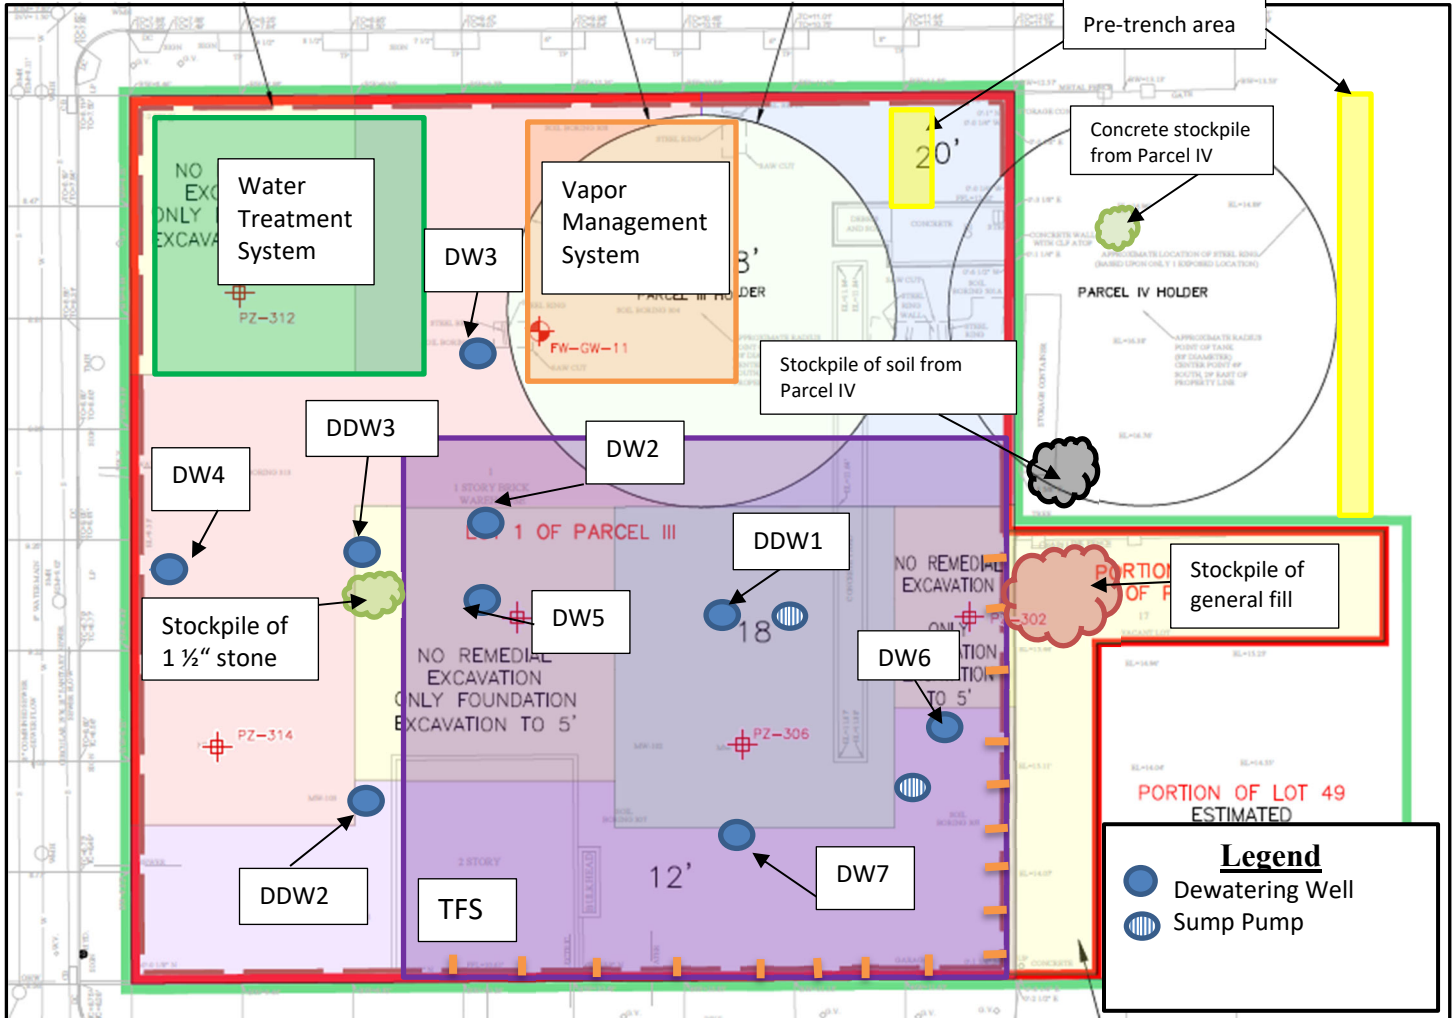

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 22, 2023
WEATHER:	Temp: 46 – 56°F Cloudy, RH: 47% Pressure: 30.41" Hg Wind: SE @ 13 mph
TIME:	07:00 – 15:30

Excavation Diagram

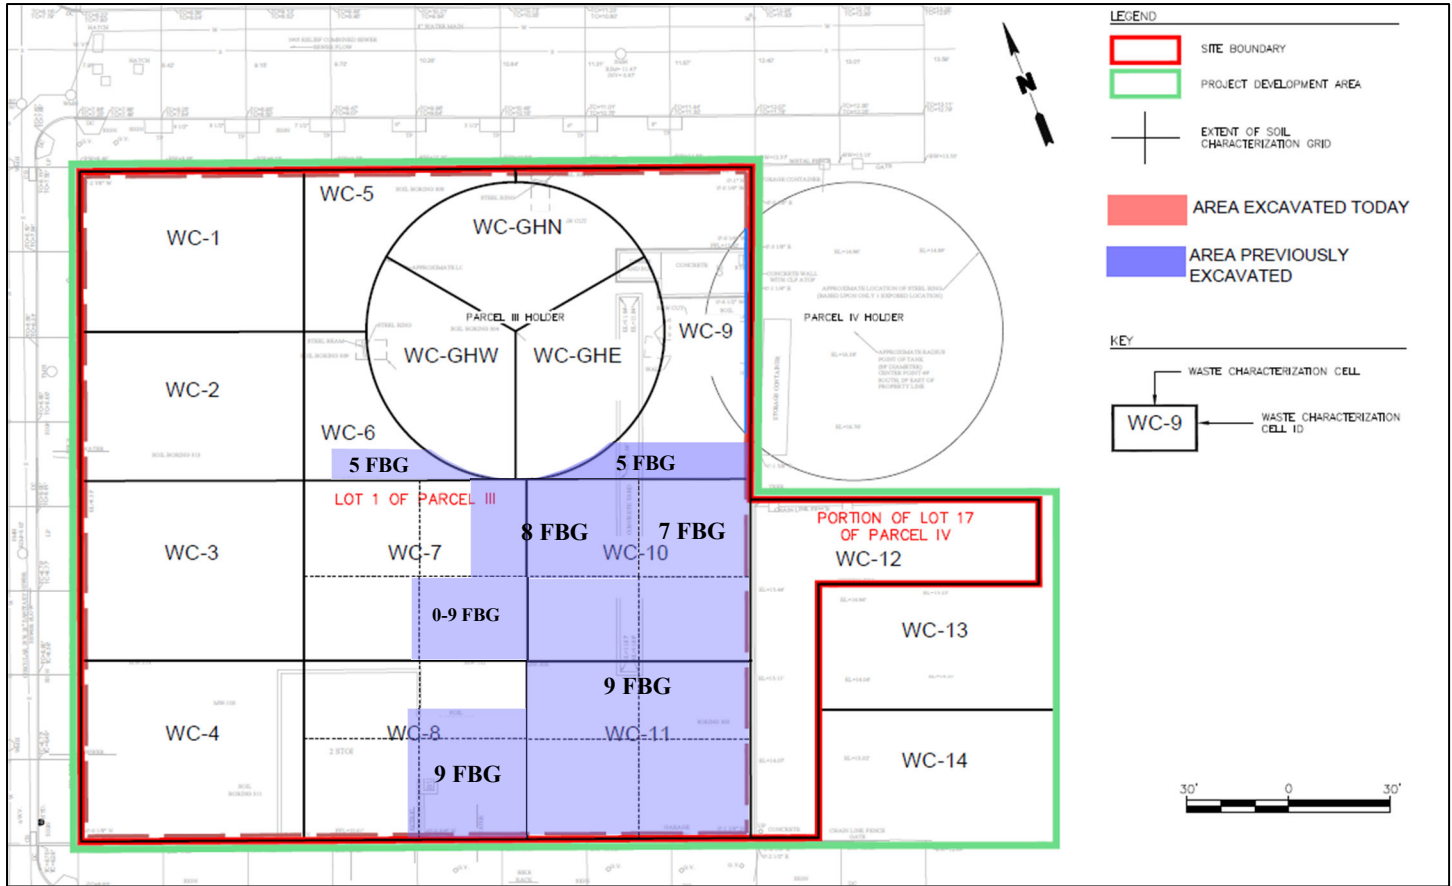

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 22, 2023
WEATHER:	Temp: 46 – 56°F Cloudy, RH: 47% Pressure: 30.41" Hg Wind: SE @ 13 mph
TIME:	07:00 – 15:30

Photographs of Onsite Work



Photo 1:

CEI pre-trenching along the east side of Gas Holder 4.



Photo 2:

Exposed soil covered with plastic liner at the end of the day.
