

<b>PROJECT:</b>	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
<b>ADDRESS:</b>	545 Sackett St., Brooklyn, NY
<b>PREPARED BY:</b>	Roux Environmental Engineering and Geology, D.P.C.
<b>DATE:</b>	January 26, 2024
<b>WEATHER:</b>	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
<b>TIME:</b>	07:00 – 15:30

### Project Team

#### General Contractor and Subcontractors:

- Mega Contracting Group, LLC (Mega)
- Creamer Environmental, Inc. (CEI)
- Weber Surveying

#### Engineers and Consultants:

- Roux Environmental Engineering and Geology, D.P.C. (Roux)
- GZA GeoEnvironmental Inc. of New York (GZANY)
- WSP USA (WSP)

### Remedial Action Work Summary

#### Work Activities Performed Onsite:

- Import of clean fill and backfill in waste characterization grids WC-1 and WC-2.
- Installation of support of excavation (SOE).

#### Contractor Work Performed Onsite:

Creamer Environmental, Inc. (CEI) imported 16 trucks (406.27 tons) of general fill from Vulcan Wantage New Jersey to be used as the 1' thick backfill cap in waste characterization grid WC-1 and WC-2. Prior to backfilling, Weber Surveying collected completed excavation dimensions and elevations. CEI continued breaking surface concrete and downsizing material for future load out and disposal in grids WC-2 and WC-3. CEI continued installation and welding the SOE walers/ bracing in the Gas Holder 3 excavation area and began installing the lagging wall between Gas Holder 3 and 4.

The vapor management system (VMS) associated with the tension fabric structure (TFS) was operated throughout the day. Dust and odor control measures (wetting, tarping, limiting vehicle speeds, etc.) were performed as needed, to ensure there were no impacts to the neighborhood. All truck tires were cleaned before leaving the Site, to ensure no material was tracked onto the surrounding streets. Exposed soils were covered with Atmos odor suppressing foam and/or poly sheeting at the end of the day.

#### Air Monitoring:

- No VOC or dust exceedances were observed from the community air monitoring program (CAMP).
- GZANY to provide a summary report of CAMP activities separately.

#### Erosion and Sediment Control:

- None.

#### Sampling Conducted:

- None.

#### Other Items of Note:

- Construction activities were observed as part of the ongoing combined sewer overflow (CSO) project west of Nevins Street.

**DAILY STATUS REPORT**

<b>PROJECT:</b>	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
<b>ADDRESS:</b>	545 Sackett St., Brooklyn, NY
<b>PREPARED BY:</b>	Roux Environmental Engineering and Geology, D.P.C.
<b>DATE:</b>	January 26, 2024
<b>WEATHER:</b>	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
<b>TIME:</b>	07:00 – 15:30

**Imported Material**

Name - Location	Source	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Vulcan ASTM #3 (1 ½" Stone)	Vulcan Hamburg Quarry			10	255.36
Vulcan ASTM #57 (3/4" Stone)	Vulcan Hamburg Quarry			5	126.76
Vulcan General Fill	Vulcan Wantage Quarry	16	406.27	655	16,518.42

**Exported Material**

Material	Facility	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
TCE Impacted Haz Hot Spots	CWM Emelle			7	161.72
Cd Impacted Haz Material from WC-5	CWM Emelle			3	49.45
Pb Impacted Haz from Parcel IV Hot Spot	CWM Emelle			25	536.72
Cd Impacted Haz Material from WC-5	Clean Earth NJ			16	397.75
Concrete for Recycling	Bayshore			23	421.87
Concrete for Landfill	WM Fairless			63	~1,415.93
Urban Fill for CVOC Orange Zone (Lot 17)	WM Fairless Urban Fill-OZ			47	~1034
Urban Fill for CVOC Orange Zone (Lot 49)	WM Fairless Urban Fill-OZ			24	~528
Non-Haz Urban Fill (Lot 17)	Clean Earth Carteret			42	~924
Non-Haz Urban Fill (Lot 49)	Clean Earth Carteret			73	~1,606
MGP soil with TCE>25 ppm	Clean Earth ESMI			181	~3,906
	CE Southeast Pennsylvania			8	~176
Non-Haz MGP Impacted (TCLP Benzene > 0.5)	CE Southeast Pennsylvania			8	~237.97
Non-Haz MGP Impacted (TCLP Benzene < 0.5)	CE Southeast Pennsylvania			58	~1,276
Non-Haz Contaminated Urban Fill	WM Fairless			240	~5,120.69
Non-Haz Urban Fill	Clean Earth Carteret -BZ			40	~857
Non-Haz MGP Impacted	Clean Earth of New Castle			35	~770
MGP Impacted (TCLP Benzene 0.2<x<0.5 mg/l)	CE Southeast Pennsylvania			5	~110

**Exported Material Truck Log**

Number	Excavation Grid	Disposal Facility	Disposal Profile	Manifest Number	Trucking Company	Truck License Plate

**Dewatering**

Time	Totalizer Reading
7:00	40,131,200
15:30	40,131,200
Water treated and discharged since last report:	0 gallons

**DAILY STATUS REPORT**


<b>PROJECT:</b>	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
<b>ADDRESS:</b>	545 Sackett St., Brooklyn, NY
<b>PREPARED BY:</b>	Roux Environmental Engineering and Geology, D.P.C.
<b>DATE:</b>	January 26, 2024
<b>WEATHER:</b>	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
<b>TIME:</b>	07:00 – 15:30

**Anticipated Upcoming Work Activities**

Resume excavation in WC-2 and WC-3 and load out of material for offsite disposal. Continued installation of SOE in Gas Holder 3 area and prep work for future material load out from Gas Holder 3 excavation area.


<b>PROJECT:</b>	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
<b>ADDRESS:</b>	545 Sackett St., Brooklyn, NY
<b>PREPARED BY:</b>	Roux Environmental Engineering and Geology, D.P.C.
<b>DATE:</b>	January 26, 2024
<b>WEATHER:</b>	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
<b>TIME:</b>	07:00 – 15:30

### Site Layout

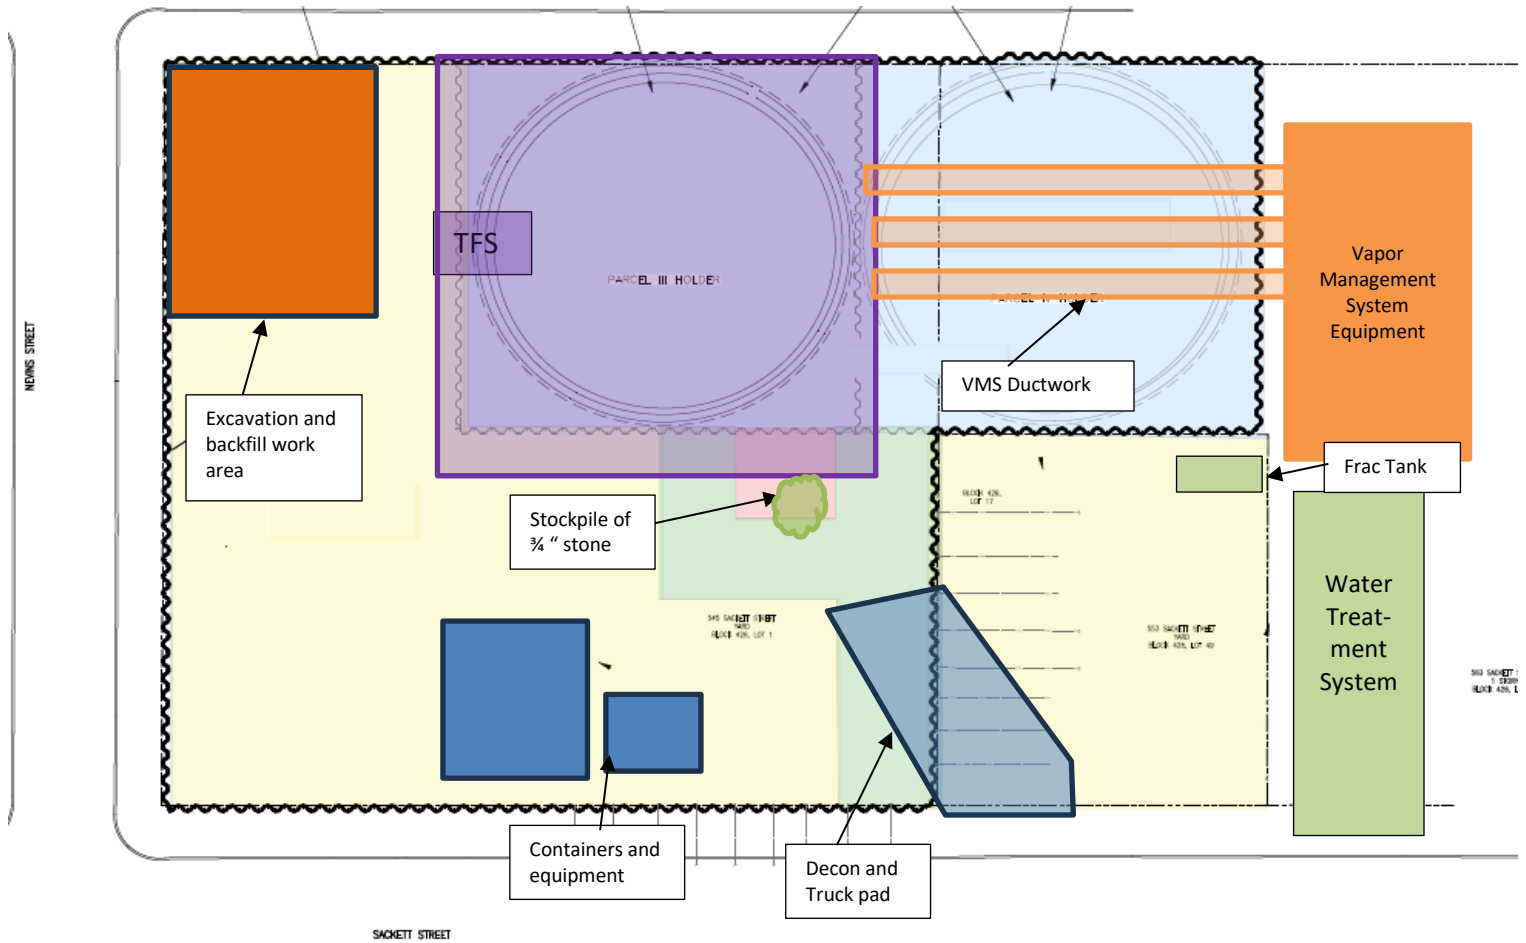

<b>PROJECT:</b>	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
<b>ADDRESS:</b>	545 Sackett St., Brooklyn, NY
<b>PREPARED BY:</b>	Roux Environmental Engineering and Geology, D.P.C.
<b>DATE:</b>	January 26, 2024
<b>WEATHER:</b>	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
<b>TIME:</b>	07:00 – 15:30

### Excavation Diagram

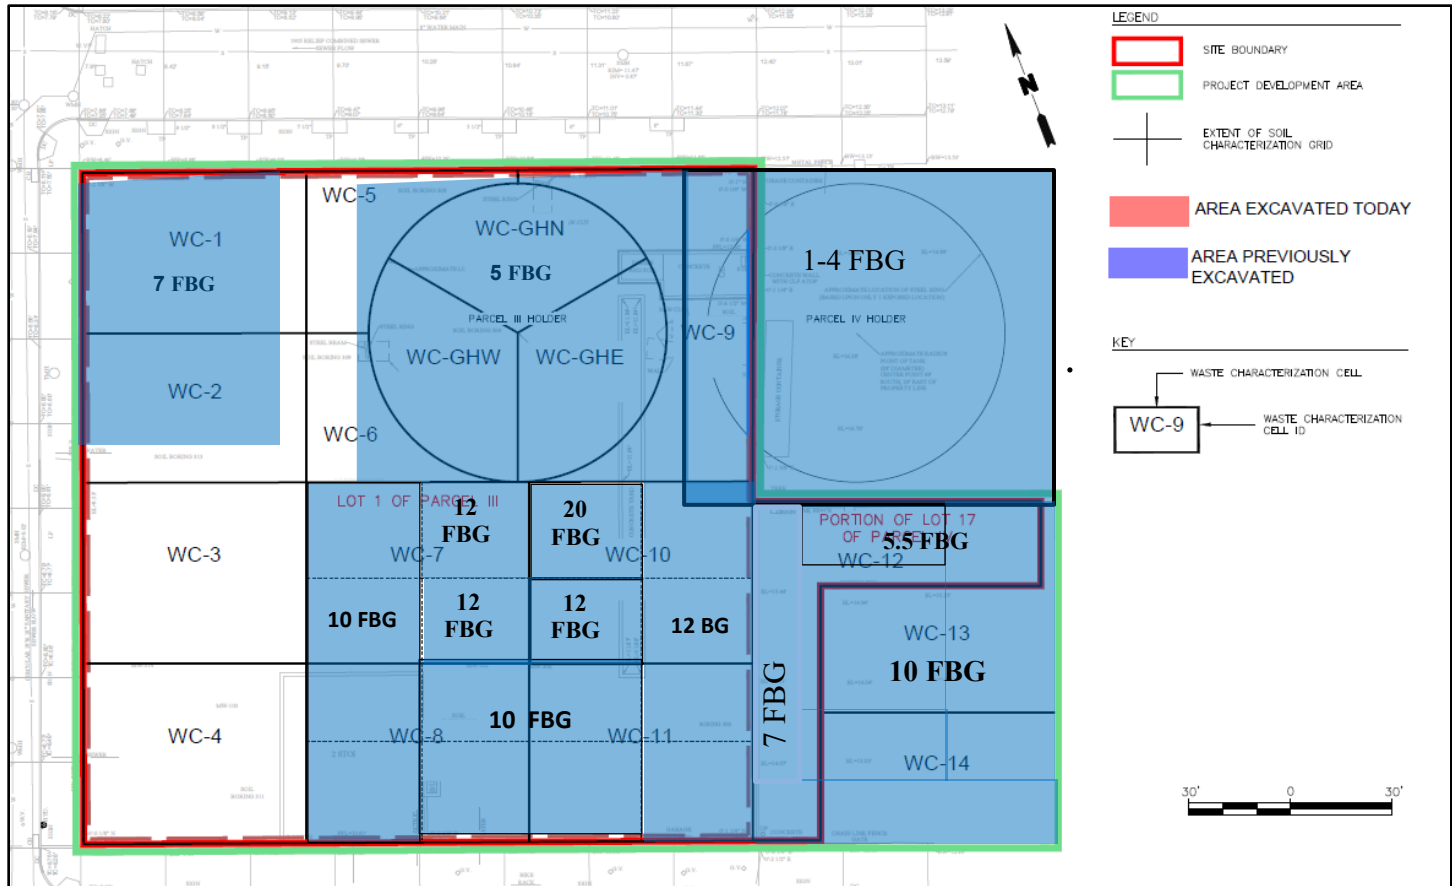



PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	January 26, 2024
WEATHER:	Temp: 43-53°F, Overcast, RH: 94% Pressure: 30.07" in Hg Wind: @ 7 mph
TIME:	07:00 – 15:30



**Photo 1:**

Looking west, view of CEI importing general fill.



**Photo 2:**

Looking southwest, view of CEI spreading general fill in WC-1 and WC-2 excavation area and compacting material with trench roller.
