



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

Project Team

General Contractor and Subcontractors:

- Mega Contracting Group, LLC (Mega)
- Creamer Environmental, Inc. (CEI)
- Earth Construction Services, LLC (ECS)

Engineers and Consultants:

- Roux Environmental Engineering and Geology, D.P.C. (Roux)
- GZA GeoEnvironmental Inc. of New York (GZANY)
- WSP USA (WSP)

Remedial Action Work Summary

Work Activities Performed Onsite:

- Excavation and loadout of material for offsite disposal at CMW Emelle.
- Demolition of Gas Holder 3 foundation and structure.
- Backfill of completed excavation sections in Gas Holder 3.
- Dewatering operations for Gas Holder 3 excavation area.

Contractor Work Performed Onsite:

Creamer Environmental Inc. (CEI) excavated the last of the former Gas Holder 3 material from within the cofferdam and loaded out for disposal 5 triaxle trucks (approximately 100 tons) of MGP impacted material with TCE>25 ppm from waste characterization grid WC-GHW (13-20) for to Chemical Waste Management (CMW) Emelle. CEI imported 2 trucks (49.29 tons) of general fill from Vulcan Wantage, New Jersey. Imported general fill was used as backfilling in the completed sections in the Gas Holder 3 excavation area. No native soil remains exposed within the cofferdam around former Gas Holder 3.

Earth Construction Services, LLC (ECS) continued 24-hour operation of the dewatering system for the Gas Holder 3 excavation area and CEI operated the WTS. Since the last reporting period, CEI treated approximately 544,700 gallons of recovered construction wastewater through the WTS and discharged the treated water to the New York City Department of Environmental Protection (NYCDEP) combined sewer system. Routine maintenance to onsite dewatering and water treatment systems was performed.

The vapor management system (VMS) associated with the tension fabric structure (TFS) was operated throughout the day. Other dust and odor control measures (wetting, tarping, limiting vehicle speeds, covering trucks inside TFS, spraying loaded material with odor suppressant, etc.) continued to be performed to ensure there were no impacts to the neighborhood. Truck tires were washed to ensure material was not being tracked offsite. Exposed soils were covered with Atmos odor suppressing foam during the work operations.

Air Monitoring:

- No VOC or dust exceedances were observed from the community air monitoring program (CAMP).
- GZANY to provide a summary report of CAMP activities separately.

Erosion and Sediment Control:

- Roux performed weekly SWPPP inspection.

Sampling Conducted:

- None.

**DAILY STATUS REPORT**

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

Other Items of Note:

- Construction activities were observed as part of the ongoing combined sewer overflow (CSO) project west of Nevins Street.

Imported Material

Name - Location	Source	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Vulcan ASTM #3 (1 ½" Stone)	Vulcan Hamburg Quarry			11	279.71
Vulcan ASTM #57 (3/4" Stone)	Vulcan Hamburg Quarry			6	152.05
Vulcan General Fill	Vulcan Wantage Quarry	2	49.29	855	21,520.05

Exported Material

Material	Facility	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
TCE Impacted Haz Hot Spots	CWM Emelle			7	161.72
Cd Impacted Haz Material from WC-5	CWM Emelle			3	49.45
Pb Impacted Haz from Parcel IV Hot Spot	CWM Emelle			25	536.72
Cd Impacted Haz Material from WC-5	Clean Earth (CE) NJ			16	397.75
Concrete for Recycling	Bayshore			27	~509.87
Concrete for Landfill	WM Fairless			63	~1,415.93
Urban Fill for CVOC Orange Zone (Lot 17)	WM Fairless Urban Fill-OZ			47	~1034
Urban Fill for CVOC Orange Zone (Lot 49)	WM Fairless Urban Fill-OZ			24	~528
Non-Haz Urban Fill (Lot 17)	CE Carteret			42	~924
Non-Haz Urban Fill (Lot 49)	CE Carteret			73	~1,606
MGP soil with TCE>25 ppm	CE ESMI			181	~3,906
	CE Southeast Pennsylvania			10	~220
	CMW Emelle	5	~100	404	~7,880
Non-Haz MGP Impacted (TCLP Benzene > 0.5)	CE Southeast Pennsylvania			8	~237.97
Non-Haz MGP Impacted (TCLP Benzene < 0.5)	CE Southeast Pennsylvania			119	~2,614
Non-Haz Contaminated Urban Fill	WM Fairless			387	~8,134.69
Non-Haz Urban Fill	CE Carteret -BZ			71	~1,562
Non-Haz MGP Impacted	CE of New Castle			35	~770
MGP Impacted (TCLP Benzene 0.2<x<0.5 mg/l)	CE Southeast Pennsylvania			5	~110

Exported Material Truck Log

Number	Excavation Grid	Disposal Facility	Disposal Profile	Manifest Number	Trucking Company	Truck License Plate
1	WC-GHW (13-20)	CMW Emelle	MGP soil with TCE >25 ppm	007466832 GBF	Horwith	AH53761
2	WC-GHW (13-20)	CMW Emelle	MGP soil with TCE >25 ppm	007466833 GBF	Horwith	AH31897
3	WC-GHW (13-20)	CMW Emelle	MGP soil with TCE >25 ppm	007466834 GBF	Horwith	AH15528
4	WC-GHW (13-20)	CMW Emelle	MGP soil with TCE >25 ppm	007466835 GBF	Horwith	AH53761
5	WC-GHW (13-20)	CMW Emelle	MGP soil with TCE >25 ppm	007466836 GBF	Horwith	AH31897



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

Dewatering


Date	Time	Totalizer Reading
5/30/2024	15:18	96,955,300
5/31/2024	7:05	97,310,000
5/31/2024	10:30	97,403,900
5/31/2024	15:10	97,500,000
Water treated and discharged to NYCDEP sewer since last report:		544,700

Anticipated Upcoming Work Activities

- Continue backfilling Gas Holder 3.
- Continue dewatering for Gas Holder 3 excavation area and operation of water treatment system.


PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

Site Layout

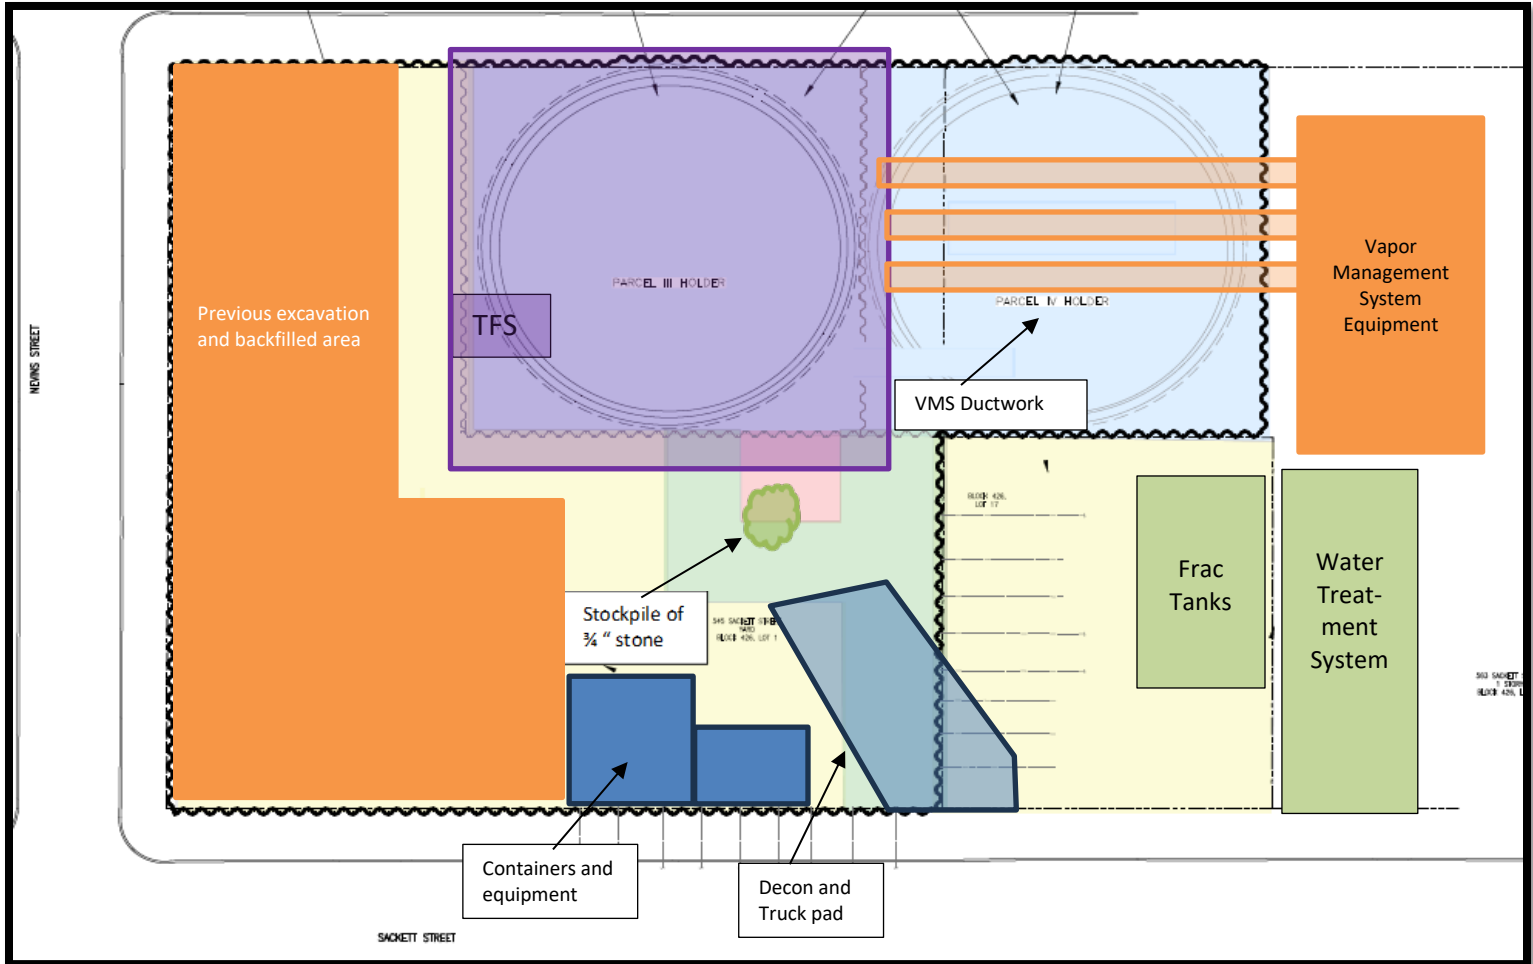

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

Excavation Diagram

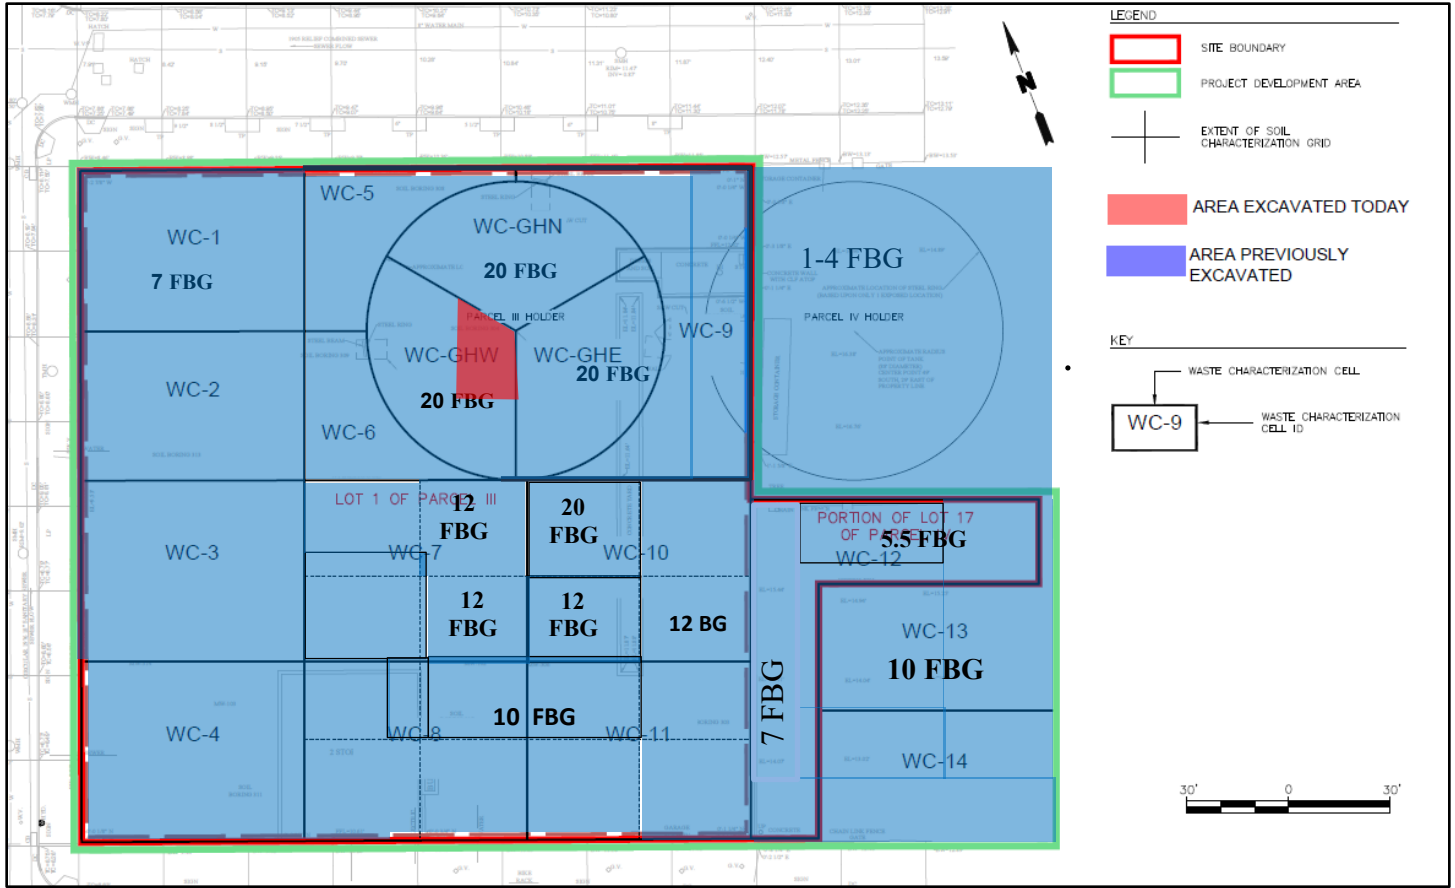

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00


**Photo 1:**

Looking north, view of CEI securing the TFS around the triaxle truck prior to being loaded with soil material for offsite disposal.

**Photo 2:**

Looking east, view of CEI applying Atmos odor suppressant foam on exposed soil inside the TFS to mitigate odors during excavation activities.

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	May 31, 2024
WEATHER:	Temp: 58-76°F, Sunny, RH: 42% Pressure: 30.16 inHg Wind: NNW @10 mph
TIME:	07:00 – 15:00

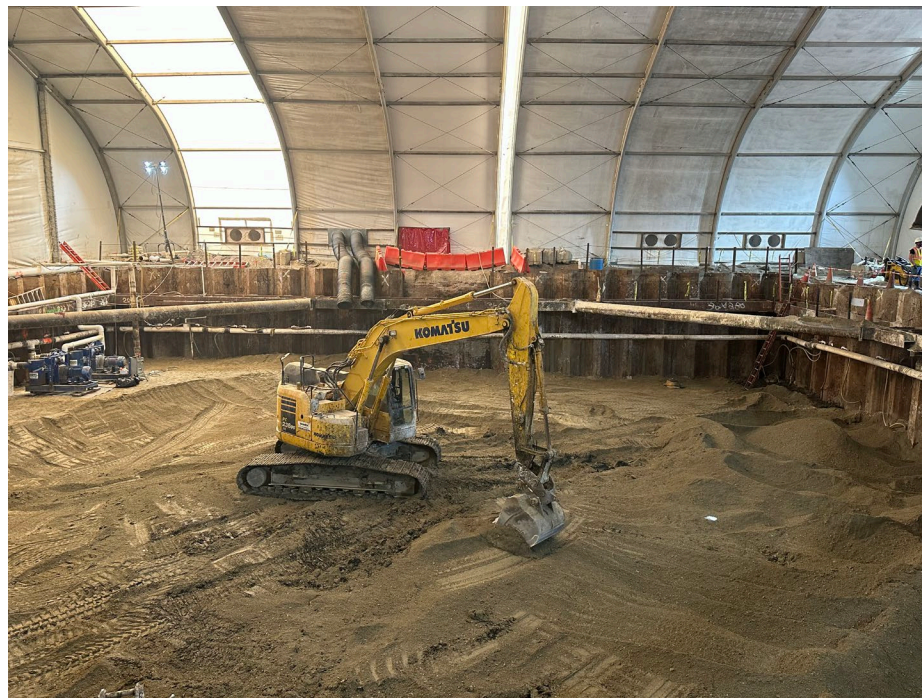**Photo 3:**

Looking east, view of CEI backfilling the center portion of the TFS with previously imported material. No native soil remains exposed within the cofferdam around former Gas Holder 3.
