



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

Project Team

General Contractor and Subcontractors:

- Mega Contracting Group, LLC (Mega)
- Creamer Environmental, Inc. (CEI)
- Earth Construction Services, LLC (ECS)

Engineers and Consultants:

- Roux Environmental Engineering and Geology, D.P.C. (Roux)
- GZA GeoEnvironmental Inc. of New York (GZANY)
- WSP USA (WSP)

Remedial Action Work Summary

Work Activities Performed Onsite:

- Continued grading activities and setup to relocate temporary fabric structure.

Contractor Work Performed Onsite:

Grading activities were performed east of former Gas Holder 4 and inside the temporary fabric structure (TFS) in preparation of future onsite work and relocation of the TFS. CEI removed all light towers from the interior of the TFS. CEI continued to remove sandbags and weights in preparation of TFS relocation. CEI mobilized two manlifts to the site to installed steel cables on the TFS to facilitate upcoming crane lift. CEI began to remove steel pins from the TFS baseplates. Dust and odor control measures (wetting, tarping, limiting vehicle speeds, etc.) continued to be performed to ensure there were no impacts to the neighborhood.

Air Monitoring:

- No VOC or dust exceedances were observed from the community air monitoring program (CAMP).
- GZANY to provide a summary report of CAMP activities separately.

Erosion and Sediment Control:

- None.

Sampling Conducted:

- None.

Other Items of Note:

- Construction activities were observed as part of the ongoing combined sewer overflow (CSO) project west of Nevins Street.

Imported Material

Name - Location	Source	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Vulcan ASTM #3 (1 ½" Stone)	Vulcan Hamburg Quarry			11	279.71
Vulcan ASTM #57 (3/4" Stone)	Vulcan Hamburg Quarry			6	152.05
Vulcan General Fill	Vulcan Wantage Quarry			1,200	29,913.85



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

Exported Material

Material	Facility	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
TCE Impacted Haz Hot Spots	CWM Emelle			7	161.72
Cd Impacted Haz Material from WC-5	CWM Emelle			3	49.45
Pb Impacted Haz from Parcel IV Hot Spot	CWM Emelle			25	536.72
Cd Impacted Haz Material from WC-5	Clean Earth (CE) NJ			16	397.75
Concrete for Recycling	Bayshore			27	~509.87
Concrete for Landfill	WM Fairless			63	~1,415.93
Urban Fill for CVOC Orange Zone (Lot 17)	WM Fairless Urban Fill-OZ			47	~1034
Urban Fill for CVOC Orange Zone (Lot 49)	WM Fairless Urban Fill-OZ			24	~528
Non-Haz Urban Fill (Lot 17)	CE Carteret			42	~924
Non-Haz Urban Fill (Lot 49)	CE Carteret			73	~1,606
MGP soil with TCE>25 ppm	CE ESMI			181	~3,906
	CE Southeast Pennsylvania			10	~220
	CMW Emelle			404	~7,880
Non-Haz MGP Impacted (TCLP Benzene > 0.5)	CE Southeast Pennsylvania			8	~237.97
Non-Haz MGP Impacted (TCLP Benzene < 0.5)	CE Southeast Pennsylvania			119	~2,614
Non-Haz Contaminated Urban Fill	WM Fairless			387	~8,134.69
Non-Haz Urban Fill	CE Carteret -BZ			71	~1,562
Non-Haz MGP Impacted	CE of New Castle			35	~770
MGP Impacted (TCLP Benzene 0.2<x<0.5 mg/l)	CE Southeast Pennsylvania			5	~110

Exported Material Truck Log

Number	Excavation Grid	Disposal Facility	Disposal Profile	Manifest Number	Trucking Company	Truck License Plate
None						

Dewatering


Date	Time	Totalizer Reading
6/21/24	15:15	100,823,700
Water treated and discharged to NYCDEP sewer since last report:		0

Anticipated Upcoming Work Activities

- Continued Site preparation for future onsite work and relocation of the TFS.


Site Layout

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

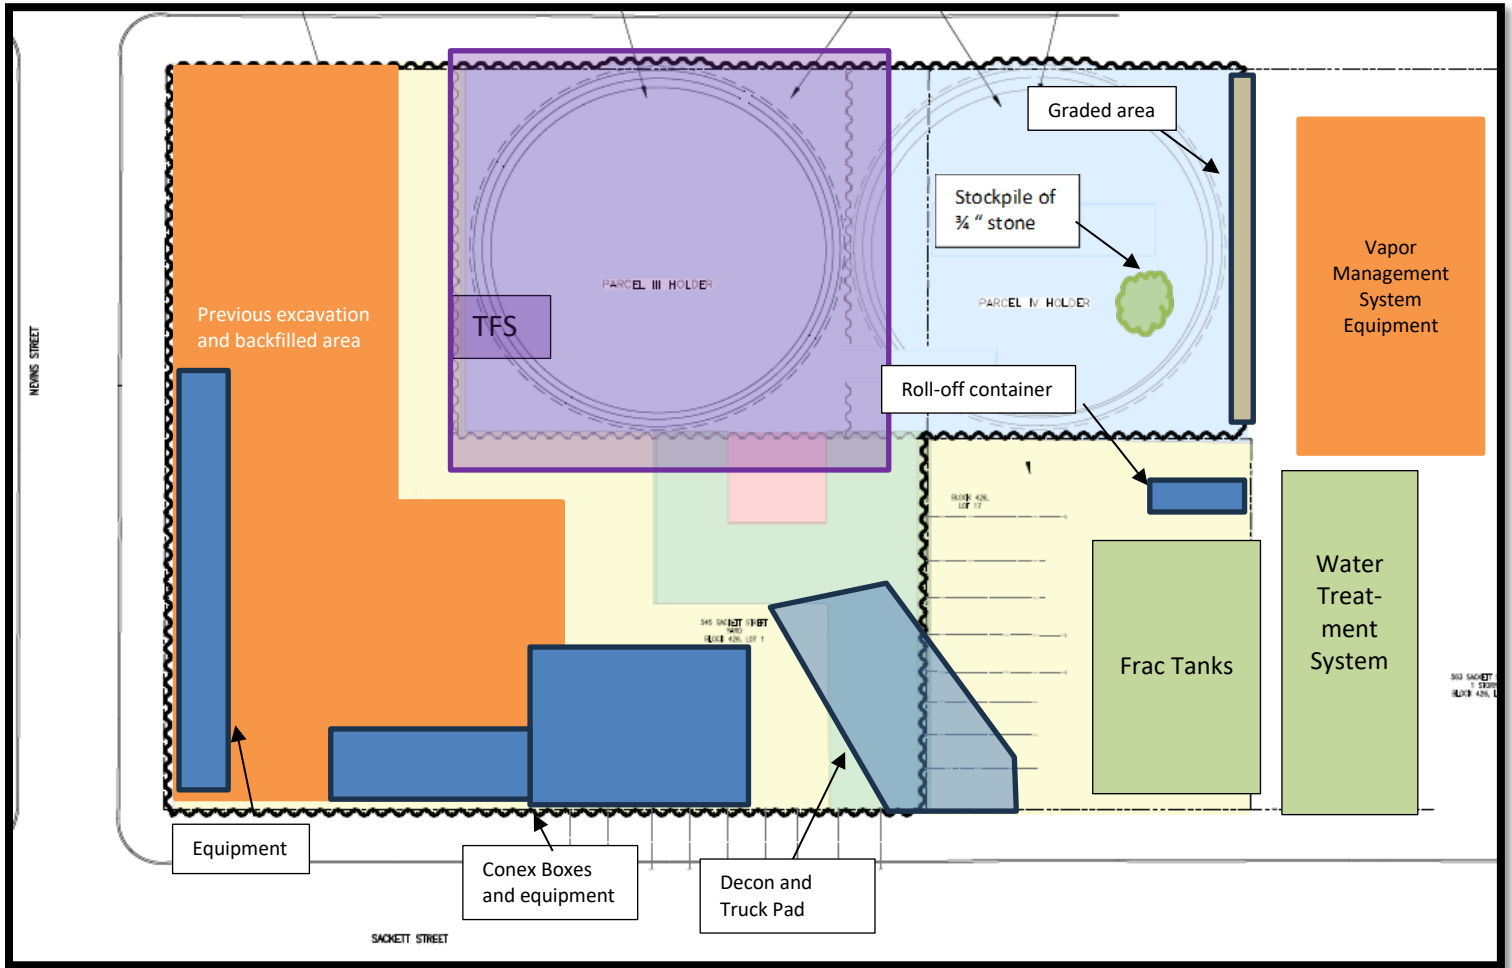

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

Excavation Diagram

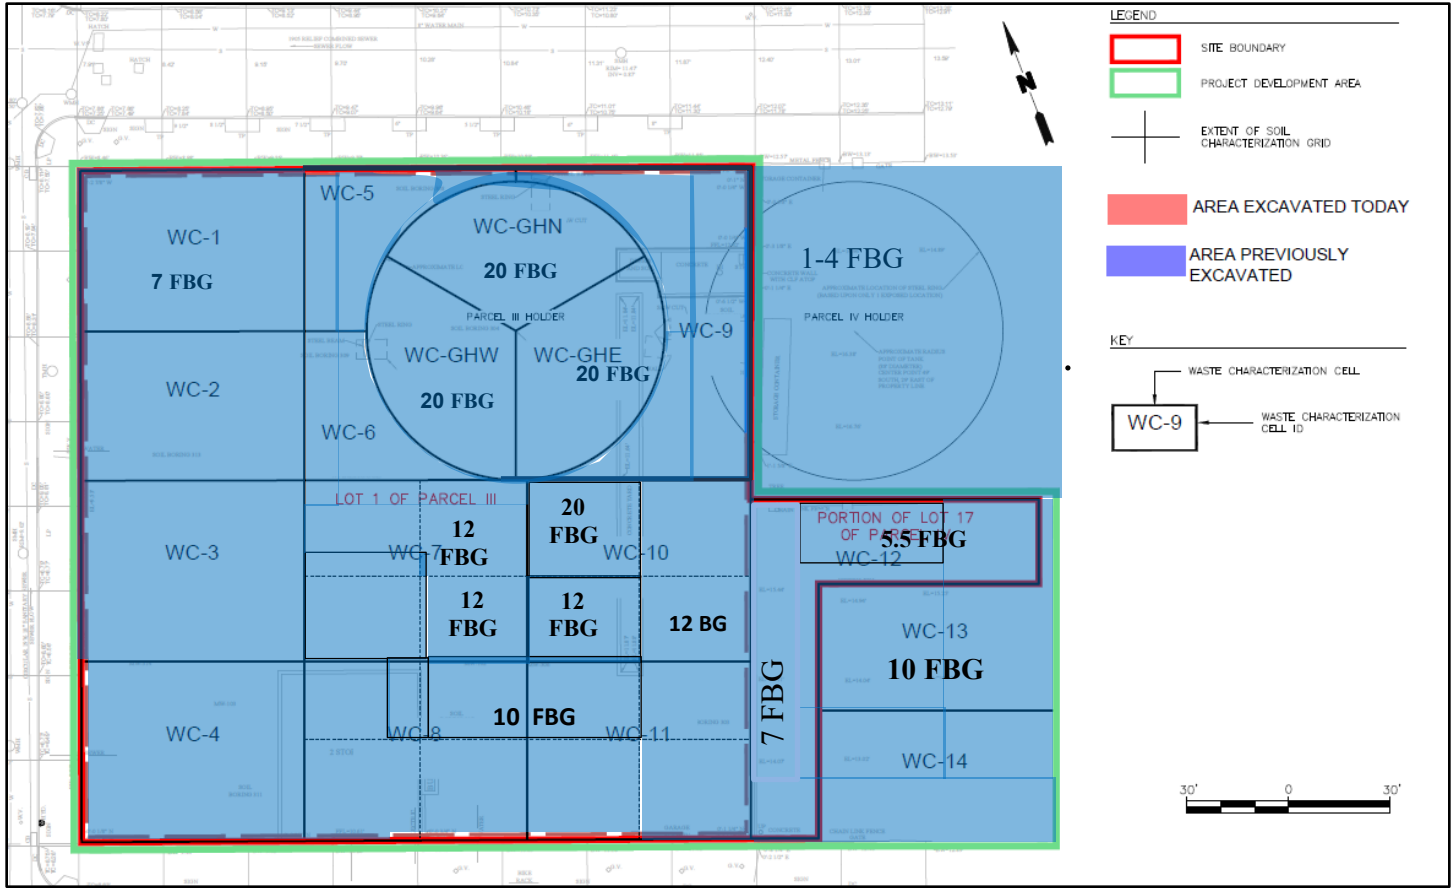

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

**Photo 1:**

Looking northeast, view of CEI performing grading activities southeast of Gas Holder 4 for upcoming TFS installation.

**Photo 2:**

Looking north, view of CEI installing steel cables on the TFS for upcoming relocation.

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	June 21, 2024
WEATHER:	Temp: 75-92°F, Sunny, RH: 71% Pressure: 30.20 in Hg Wind: WSW @ 7 mph
TIME:	07:00 – 15:00

**Photo 3:**

Looking northwest, view of CEI removing steel pins from the baseplates from the northeastern corner of the TFS.
