




FLUSH-MOUNT WELL CONSTRUCTION LOG

WELL: KTZ-MW-1

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-1
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/7/2016	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/12/16 - 7/13/16	GAUGING DATE:	7/12/2016
ELEVATION ¹ :	403.58	DEPTH TO WATER ² :	6.20
DATUM:	NGVD88	DEPTH TO PRODUCT ² :	N/A
CASING MATERIAL:	PVC	DEPTH TO BOTTOM ² :	12.50
FILTER PACK TYPE:	Sand #2	SCREEN MATERIAL:	PVC
		SEAL TYPE:	Grout

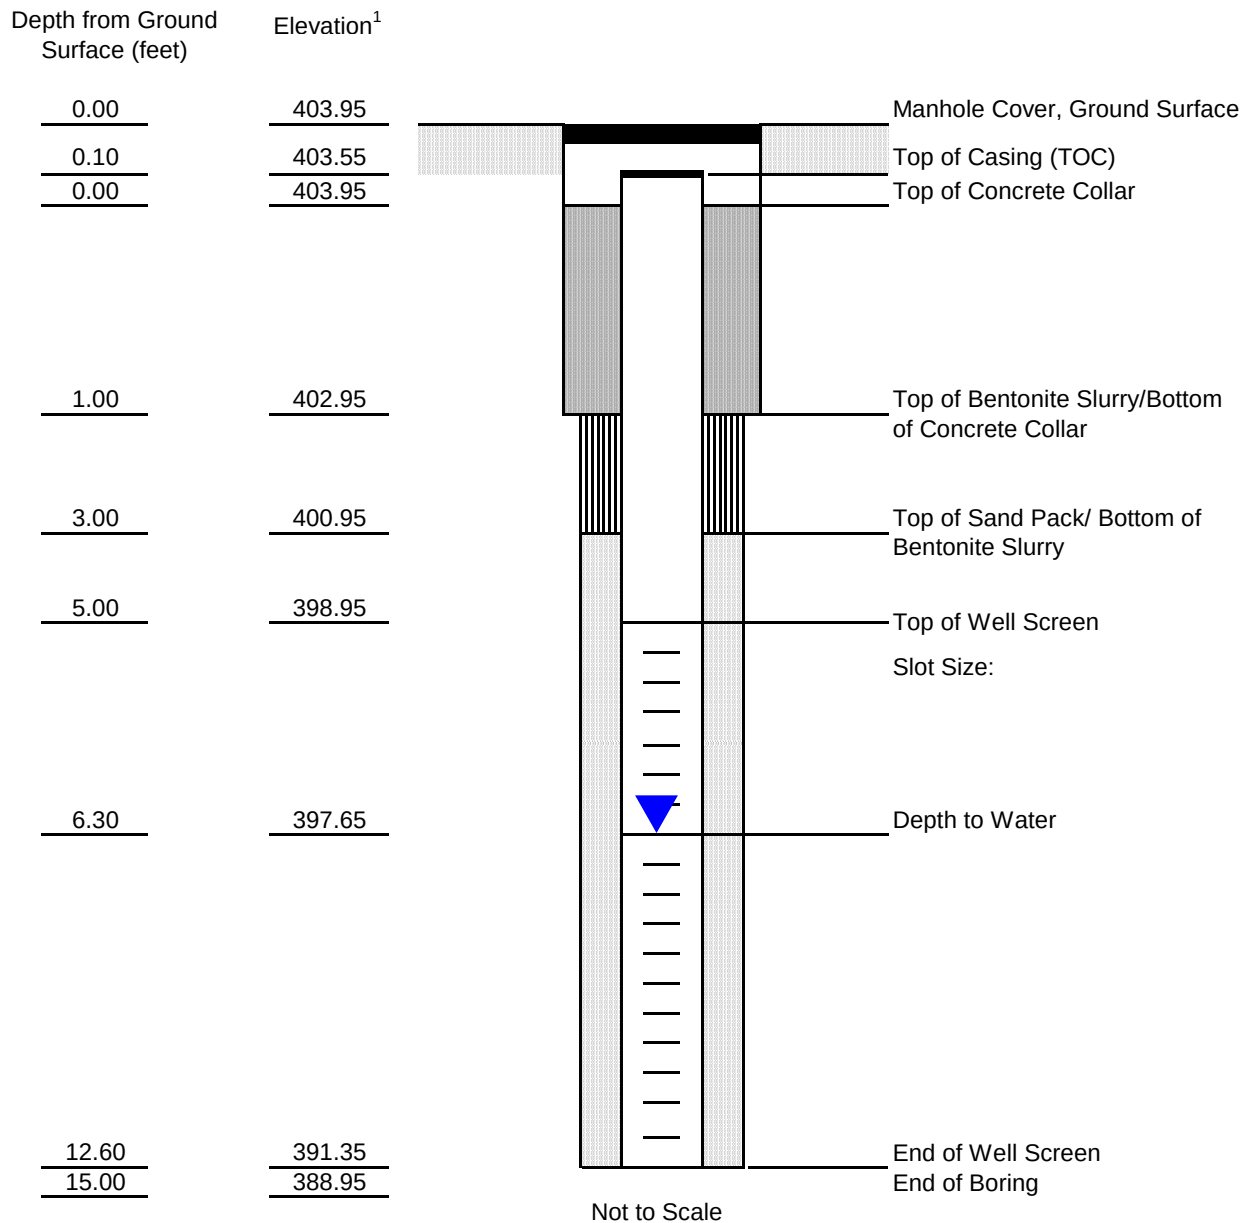

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE



STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-2


SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-2
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/5/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/12/16	GAUGING DATE:	7/12/16
HEIGHT OF STICK-UP:	2.78	DEPTH TO WATER ² :	11.50
ELEVATION ¹ :	420.74	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	17.55
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	Sand #2	SEAL TYPE:	Grout

Depth from Ground
Surface (feet)

Elevation¹

2.88	420.84
2.78	420.74
0.00	417.96
1.00	416.96
3.00	414.96
5.00	412.96
8.72	409.24
14.77	403.19
15.00	402.96

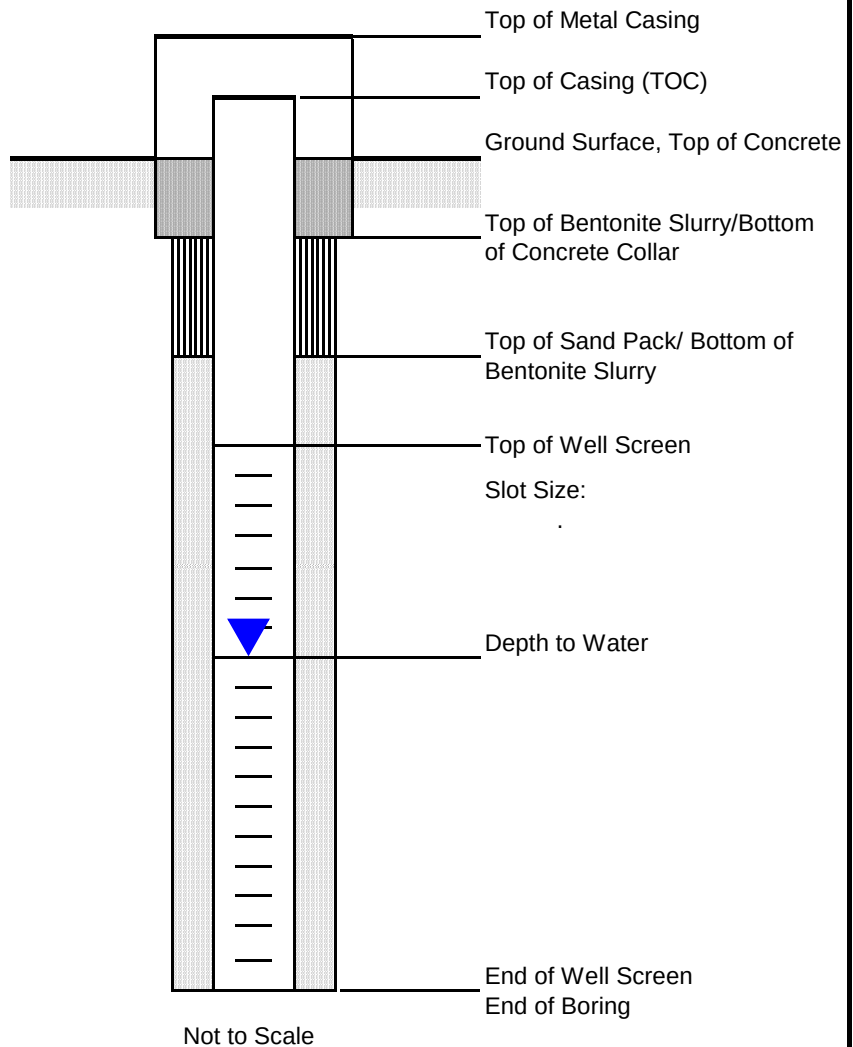

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE




STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-3

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-3
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/6/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/12/16	GAUGING DATE:	7/12/17
HEIGHT OF STICK-UP:	2.52	DEPTH TO WATER ² :	15.35
ELEVATION ¹ :	424.88	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	17.60
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

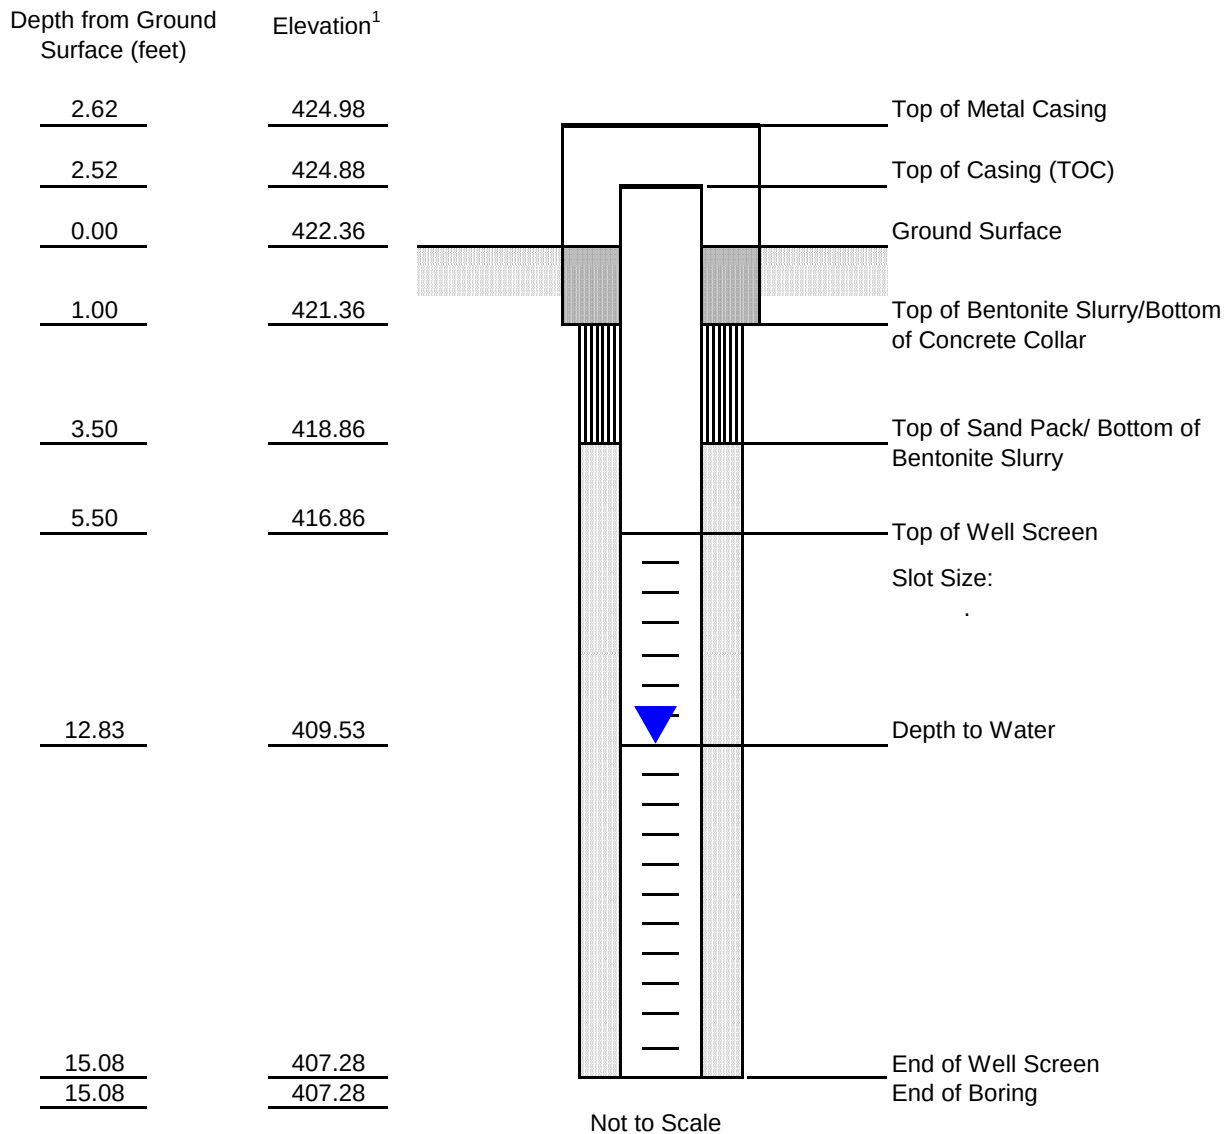

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE




STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-4

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-4
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/6/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/12/16	GAUGING DATE:	7/12/16
HEIGHT OF STICK-UP:	2.53	DEPTH TO WATER ² :	15.77
ELEVATION ¹ :	428.71	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	17.68
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

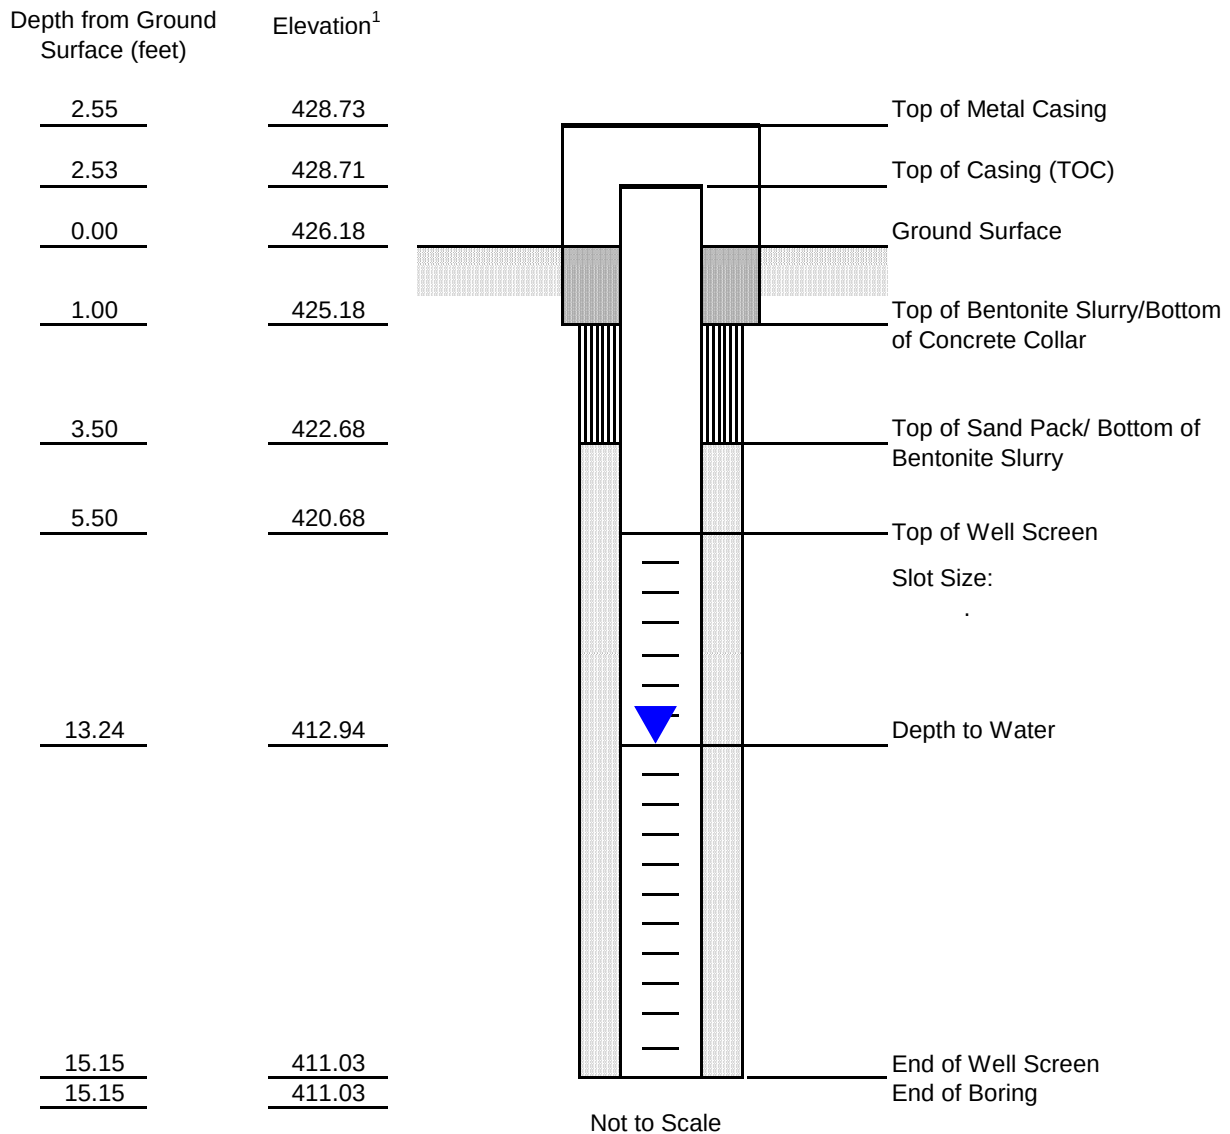

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE




STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-5

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-5
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/6/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/12/16	GAUGING DATE:	7/12/16
HEIGHT OF STICK-UP:	2.72	DEPTH TO WATER ² :	12.70
ELEVATION ¹ :	423.25	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	17.80
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

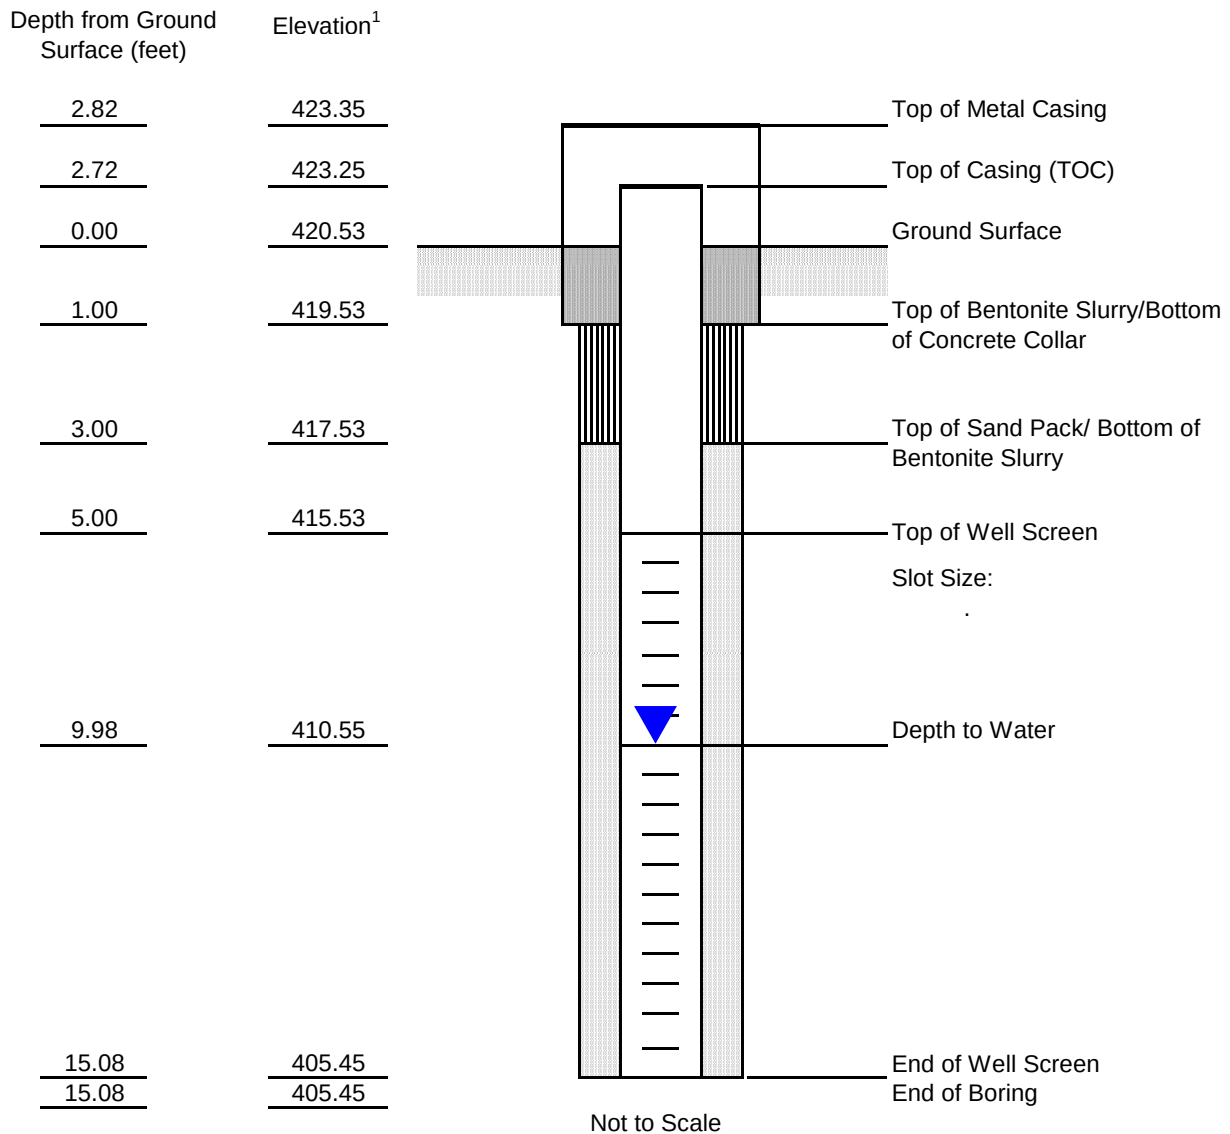

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE



STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-6

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-6
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/8/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/13/16	GAUGING DATE:	7/13/16
HEIGHT OF STICK-UP:	2.74	DEPTH TO WATER ² :	4.27
ELEVATION ¹ :	399.48	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	18.10
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

Depth from Ground
Surface (feet)

Elevation¹

2.84 399.58

2.74 399.48

0.00 396.74

1.00 395.74


3.00 392.74

5.00 391.74

1.53 395.21

15.36 381.38

15.36 381.38

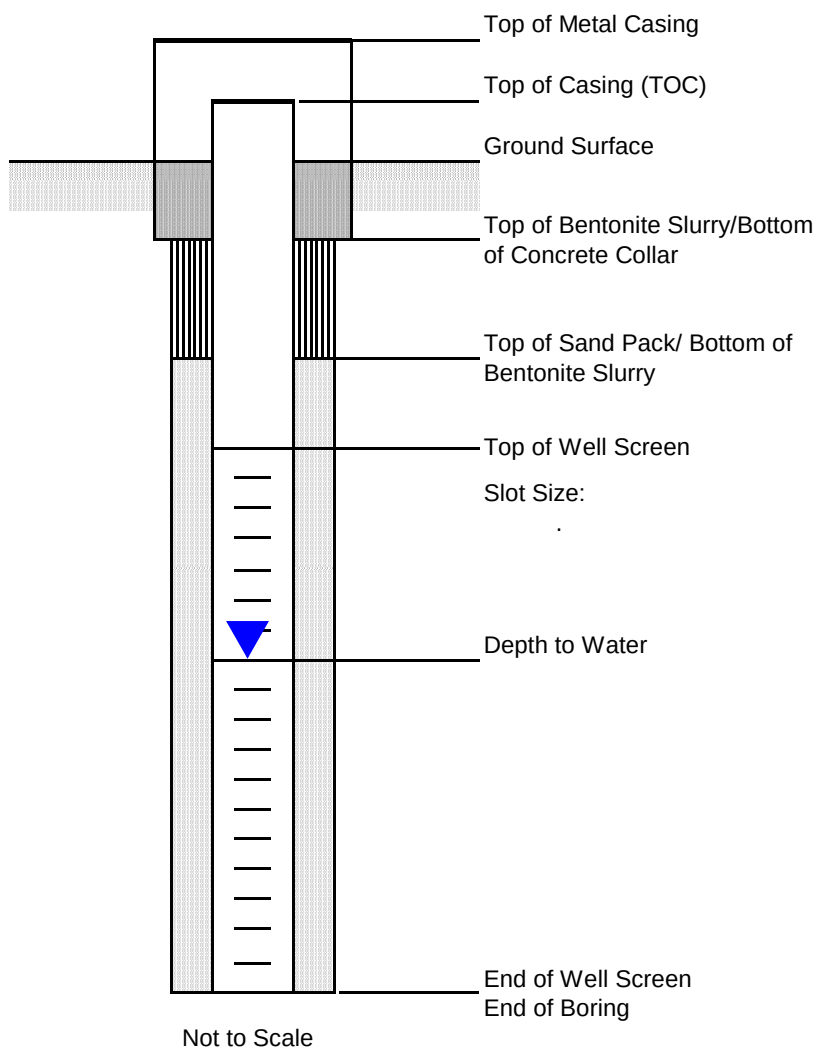

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE




STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-7

SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-7
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/11/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/13/16	GAUGING DATE:	7/13/16
HEIGHT OF STICK-UP:	3.14	DEPTH TO WATER ² :	6.20
ELEVATION ¹ :	398.61	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	17.70
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

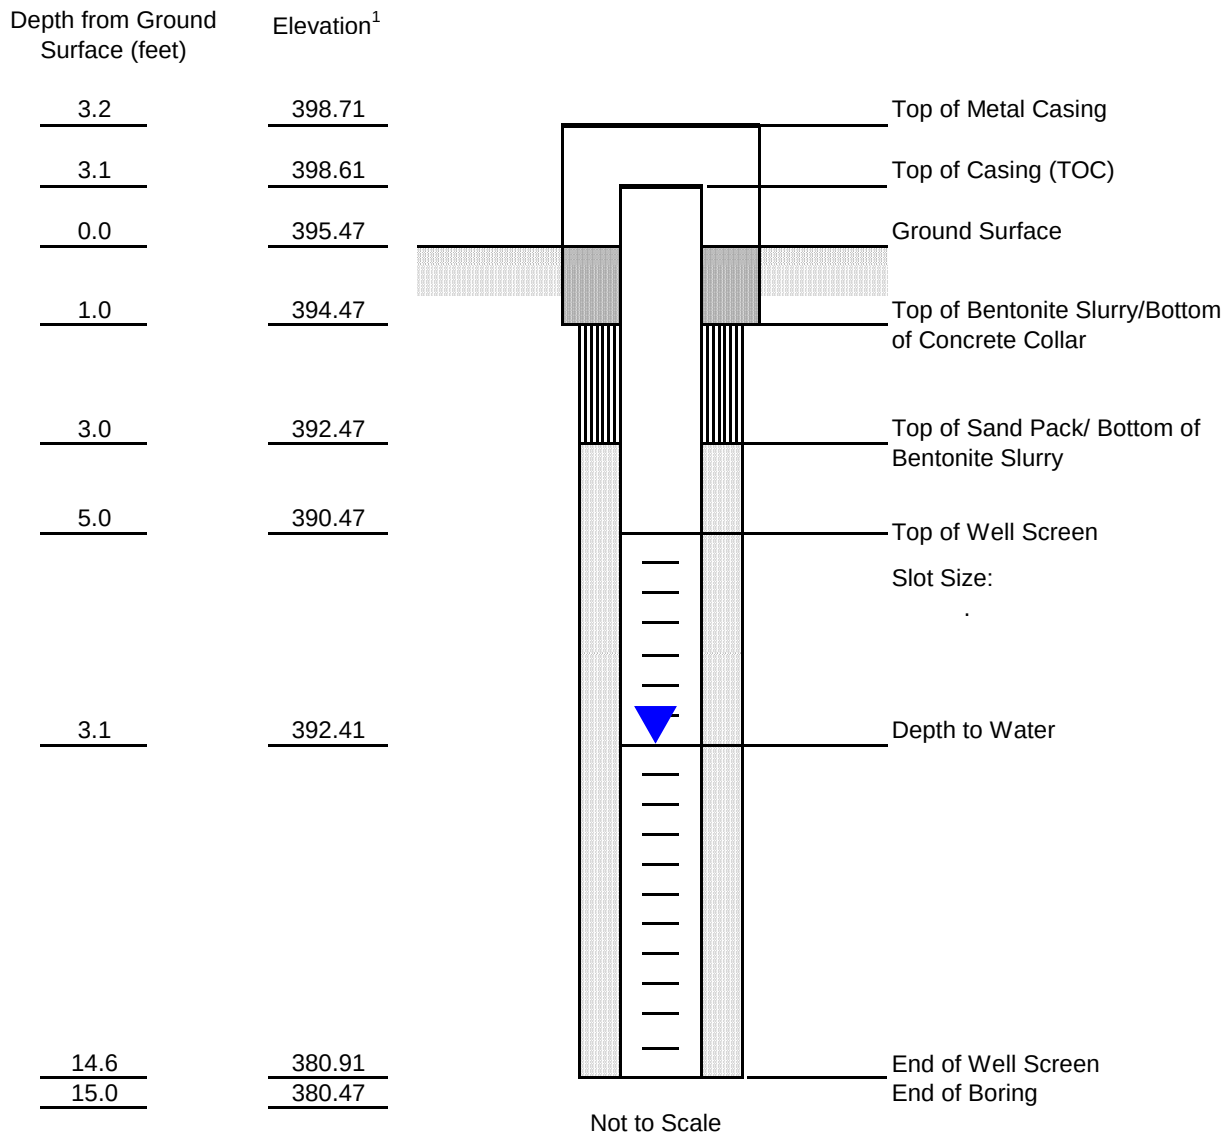

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE



STICK-UP WELL CONSTRUCTION LOG

WELL: KTZ-MW-8


SHEET 1 OF 1

PROJECT NAME:	NYSDEC Katzman Recycling	WELL NUMBER:	KTZ-MW-8
ADDRESS:	Granville, NY	DRILLING METHOD:	Hollow Stem Auger
INSTALLATION DATE:	7/7/16	DRILLER:	Parratt-Wolff, Inc.
DEVELOPMENT DATE:	7/13/16	GAUGING DATE:	7/13/16
HEIGHT OF STICK-UP:	1.63	DEPTH TO WATER ² :	3.95
ELEVATION ¹ :	415.5	DEPTH TO PRODUCT ² :	N/A
DATUM:	NGVD88	DEPTH TO BOTTOM ² :	6.15
CASING MATERIAL:	PVC	SCREEN MATERIAL:	PVC
FILTER PACK TYPE:	#2 Sand	SEAL TYPE:	Grout

Depth from Ground
Surface (feet)

Elevation¹

N/A	N/A
1.63	415.50
0.00	413.87
N/A	N/A
0.00	413.87
1.00	412.87
2.32	411.55
4.52	409.35
5.00	408.87

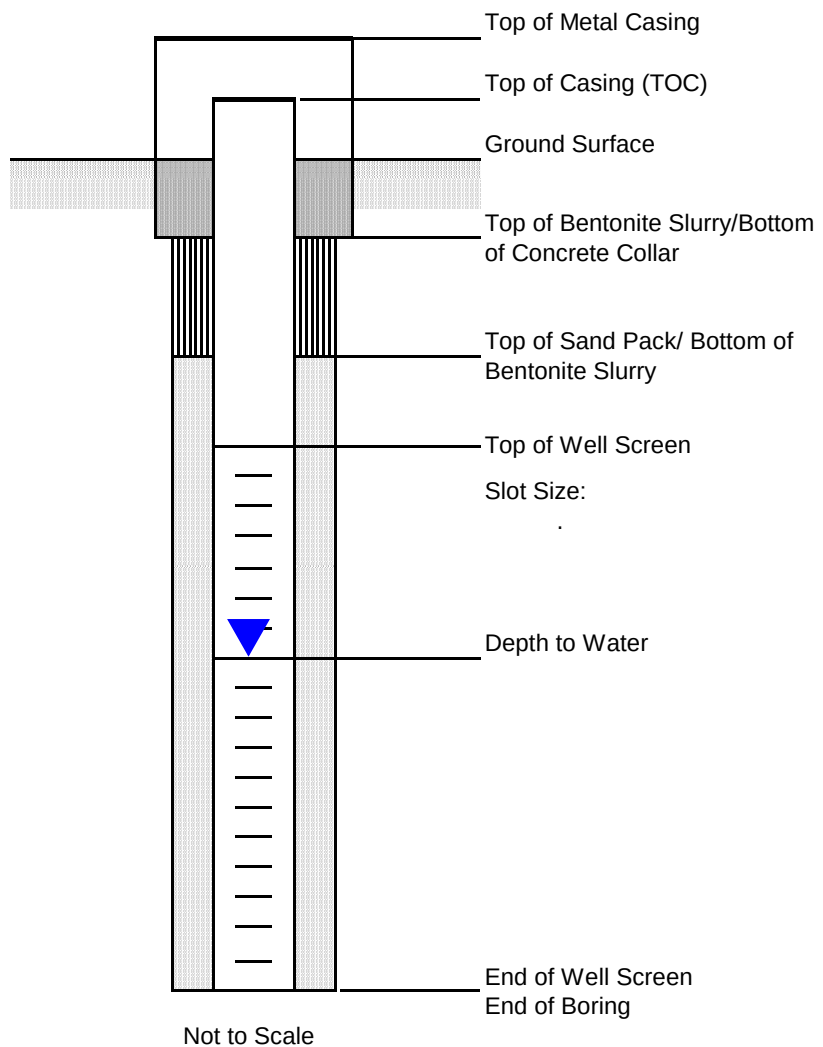

Notes:

¹Feet above datum

²Feet below top of casing

NOT TO SCALE
