



June 16, 2005

Stephen J. DeNardis, P.E.  
Resident Engineer  
West Point Area Office  
New York District  
U.S. Army Corps of Engineers  
Building 667A 3<sup>rd</sup> Floor  
West Point, New York 10996

Attention: Mr. Nicholas Patsis, P.E.

RE: May Monthly Progress Report  
Contract # DACW41-01-D-001-0006  
Vestal Wellfield 1-1, Area 4, Vestal, New York

Sirs:

Enclosed is the May Monthly Progress Report for the referenced contract. This report covers system operations from 1 May 2005 through 31 April 2005. O&M activities for the period as well as sampling activities are summarized in this report. Copies of the analytical data are included.


Please email me at [cmarshall@sevensonphilly.com](mailto:cmarshall@sevensonphilly.com) or call at 610-388-0721 if you've any questions.

Sincerely,  
Sevenson Environmental Services, Inc.

  
Cassandra T. Marshall  
Project Manager

CTM/1

cc: N. Patsis (USACE)  
A. LaGreca (Sevenson)  
J. Singer (Sevenson)  
D. Callahan (Envirogen)  
B. Buckrucker (USACE)  
F. Bales (USACE)  
S. Trocher (USEPA)  
M. Dunham (NYSDEC)



<b>TRANSMITTAL OF SHOP DRAWINGS, EQUIPMENT DATA, MATERIAL SAMPLES, OR MANUFACTURER'S CERTIFICATES OF COMPLIANCE</b> (Read Instructions on the reverse side prior to initiating this form)	DATE 6/16/05	<input checked="" type="checkbox"/> New Submittal <input type="checkbox"/> Resubmittal
--	--------------	---

**Section I REQUEST FOR APPROVAL OF THE FOLLOWING ITEMS (This section will be initiated by the contractor)**

TO: USACE West Point Area Office New York District Building 667A 3rd Floor West Point, New York 10996	FROM: Sevenson Environmental Services Inc. 2749 Lockport Rd. Niagara Falls, N.Y. 14302	CONTRACT NO. DACW-41-01-D- 0001 T.O.# 0006	TRANSMITTAL NO. 41  PREVIOUS TRANS. NO. (If Any)
---	---	---	--

SPECIFICATION SEC. NO. (Cover only one section with each transmittal)	PROJECT TITLE AND LOCATION: Vestal Well 1-1 Superfund Site, Area 2 Soil Vapor Extraction System, Broome County, New York
---	--

ITEM NO.  <i>a.</i>	DESCRIPTION OF ITEMS SUBMITTED (Type, size, model number, etc.)  <i>b.</i>	MFG. OR CONTR. CAT., CURVE DRAWING OR BROCHURE NO. (See instruction No. 8)  <i>c.</i>	NO. OF COPIES  <i>d.</i>	CONTRACT REFERENCE DOCUMENT		VARIATIONS (See instruction No. 6)  <i>g.</i>	FOR C E USE CODE  <i>h.</i>
				SPEC. PARA. NO.  <i>e.</i>	DRAWING SHEET NO.  <i>f.</i>		
1.	April 2005 Monthly Report		1				

<b>REMARKS:</b> Sent via Federal Express: 2 copies to CENWK 1 copy to USEPA Region II 1 copy to N.Patsis 1 copy to NYSDEC	I certify that the above submitted items have been reviewed in detail and are correct and in strict conformance with the contract drawings and specifications except as otherwise stated.   NAME AND SIGNATURE OF CONTRACTOR Sevenson Environmental Services
--	--

**Section II APPROVAL ACTION**

INCLOSURES RETURNED (List by Item No.)	NAME, TITLE AND SIGNATURE OF APPROVING AUTHORITY	DATE
--	--	------

**MONTHLY PROGRESS REPORT**  
**(May 1 through May 31, 2005)**

**IN-SITU SOIL VAPOR  
EXTRACTION SYSTEM  
VESTAL WATER SUPPLY WELL 1-1 SUPERFUND SITE,  
OPERABLE UNIT 2, AREA 4  
VESTAL, NEW YORK**

Prepared by:

ENVIROGEN/SHAW E&I, Inc.  
103 College Ave SE  
Grand Rapids, MI 49503

Submitted to:

Sevenson Environmental Services, Inc.  
2749 Lockport Road  
Niagara Falls, NY 14305

June 16, 2005

## TABLE OF CONTENTS

1.0	INTRODUCTION .....	1
2.0	SUMMARY OF ACTIVITIES CONDUCTED DURING THE REPORTING PERIOD.....	1
3.0	SVE SYSTEM MONITORING AND ADJUSTMENTS .....	2
3.1	Process Air Flows .....	2
3.1.1	Total System Process Air Flow .....	2
3.1.2	SVE Well Process Air Flow .....	2
3.2	Process Air VOC Concentrations .....	2
4.0	VOC YIELD .....	3
4.1	Total System VOC Yield.....	3
5.0	PROBLEMS ENCOUNTERED DURING THE REPORTING PERIOD AND RESPECTIVE CORRECTIVE MEASURES .....	3
6.0	ANTICIPATED ACTIVITIES .....	3

## LIST OF FIGURES

1	Site Plan with SVE System
2	Concentration (ppmv) and Yield Rate (lbs/day) of Total Target VOCs Vs. Time Total System Sample -- Vestal Area 4
3	Total Target Contaminant Yield Start-Up to Date (lbs) vs. Time Total System Sample – Vestal Area 4

## LIST OF TABLES

Table 1	SVE Well Status Vestal Area 4 – May 25, 2005
Table 2	Target Contaminant Yield — Vestal Area 4
Table 3	Total Target Contaminant Yield to Date — Vestal Area 4

## LIST OF APPENDICES

Appendix A	Sampling and Analytical Data - Process Air Data (Including Laboratory Data Summary Sheets and Chain-of-Custody Forms)
Appendix B	Summary of Operation Data/Contaminant Yield Calculation

## **1.0 INTRODUCTION**

Envirogen/Shaw E&I, Inc. has prepared this Monthly Progress Report for the operation of the Soil Vapor Extraction System (SVE system or System) for the Vestal Well 1-1 Superfund Site, Area 4 in Vestal, NY. This report was prepared under a subcontract to Severson Environmental Services, Inc, under contract DACA41-01-D-0001-0006. Severson's remedial action work is under supervision of the U.S. Environmental Protection Agency (USEPA) and the U.S. Army Corps of Engineers (USACE).

Figure 1 is a Site plan showing the SVE System treatment area, comprised of Cells 1 and 2 and other major components of the System. Construction of the SVE System began in early April and was completed in late June 2003. Start-up of the SVE System began on June 23, 2003. The SVE System is operated in accordance the Final Design documents, O&M Manual and subsequent correspondence with the USEPA and USACE. This report covers the time from May 1 to May 31, 2005.

Section 2.0 of this report summarizes general activities conducted during the reporting period. Section 3.0 summarizes System monitoring and adjustments. Section 4.0 discusses volatile organic compound (VOC) contaminant yields based on process air analytical data and flow rates. Section 5.0 discusses problems encountered during the reporting period and their respective corrective measures. Section 6.0 lists anticipated future activities.

## **2.0 SUMMARY OF ACTIVITIES CONDUCTED DURING THE REPORTING PERIOD**

The monthly O&M inspection was performed on May 10 and 25, 2005. Airflow, pressure/vacuum, and PID readings were measured throughout the System on May 25, 2005. Process air sampling of the System (influent, mid-carbon and effluent) was performed on May 10 and 25, 2005.

The SVE System at the Vestal Area 4 Site ran approximately 31 days without incident during the period 5/1/05 to 5/31/05.

Physical monitoring of the System parameters, such as vacuum/pressure, temperature, PID readings, and air flow measurements, along with routine maintenance of the System, was conducted during the May reporting period in accordance with the O&M Manual. These O&M measurements and site activities were recorded on daily O&M logs, which are available on-site.

The System was operational approximately 31 days from May 1 to May 31, 2005. This brings the total operational time to approximately 587 days since the June 23, 2003 start-up.

### **3.0 SVE SYSTEM MONITORING AND ADJUSTMENTS**

This section summarizes monitoring of and adjustments to the SVE System during the reporting period. Monitoring of the System included pressure/vacuum and temperature measurements, air flow measurements, and process air sampling and associated VOC analysis. The locations of the SVE wells are illustrated in Figure 1. System parameters were recorded on O&M daily log sheets, available on-site. The chain-of-custody forms and laboratory data summary sheets are provided in Appendix A. All monitoring and/or adjustments were performed in accordance with the O&M Manual.

#### **3.1 Process Air Flows**

This section discusses process air flow measurements and balancing throughout the entire System and for the individual SVE wells. Individual SVE withdrawal and injection well process airflow measurements and PID readings were taken on May 25 and are provided in Table 1.

##### **3.1.1 Total System Process Air Flow**

During the reporting period, airflow throughout the entire System was measured as outlined in the O&M Manual. The airflow through the System was calculated by measuring amount of vacuum, temperature, speed of the SVE blower, and elevation, then using these values to obtain the air flow from the blower curve computer model supplied by the manufacturer (Roots Inc.). Based on this data, the calculated airflow through the entire System on May 10 and 25, 2005 averaged 512 cubic feet per minute (cfm). This data is shown in Appendix B. The bypass airflow for May 2005 was approximately 210 scfm.

##### **3.1.2 SVE Well Process Air Flow**

Individual SVE withdrawal well process airflow measurements were recorded on May 25, 2005. In addition, PID readings were recorded when process air samples were taken. During the May 25, 2005 System sampling event, PID readings were also taken on the individual SVE withdrawal wells. This data is contained in Table 1.

#### **3.2 Process Air VOC Concentrations**

Process air samples were collected during the reporting period on May 10 and 25, 2005. Samples were collected and analyzed in accordance with the O&M Manual. The system process air analytical results are contained in Appendix A.

## **4.0 VOC YIELD**

This section details the System VOC yield based on System sampling events performed during the May 1 to May 31, 2005 reporting period. Discussed in this section is the estimated Total Targeted Contaminant (TTC) VOC yield, based on the airflow through the blowers and the composite/total system VOC analytical results. Table 2 shows the total target contaminant yield for each sampling period.

### **4.1 Total System VOC Yield**

The total System VOC yield was calculated using the total system airflow rates and contaminant concentrations. Cumulative system contaminant yields for the reporting period are shown in Table 3. Based on these calculations, the System yielded approximately zero (0) pounds of VOCs from April 27, 2005 to May 25, 2005. The average yield rate of the System per operational day between May 1, 2005 and May 31, 2005 is 0.00 lbs/day. TCE constitutes approximately 0 percent and 1, 1, 1-TCA approximately 0 percent of the total VOC yield over the reporting period. The total TTC yield from start-up (June 23, 2003) to May 25, 2005 is 2,075.64 pounds. The mass of TTC VOCs removed from the treatment area is illustrated in Figure 2. The cumulative contaminant yield is calculated utilizing the data and formulas found in Appendix B. Figure 3 graphically depicts cumulative yield over system operational time. As noted in the SVE System analytical data, the percent concentration of TCE within the influent process air is 46 percent and the concentration of 1,1,1-TCA is 54 percent from startup to May 25, 2005.

## **5.0 PROBLEMS ENCOUNTERED DURING THE REPORTING PERIOD AND RESPECTIVE CORRECTIVE MEASURES**

With the exceptions of problems discussed in Section 2.0 and in this section the System operated well throughout the month of May.

## **6.0 ANTICIPATED ACTIVITIES**

The following activities are anticipated for the next reporting period.

- Quarterly sampling at the beginning of June 2005.
- Once current operating funds run out, shut the System down at the beginning of June 2005 (anticipated 7 June 2005). A proposal to continue operations was submitted to USACE and negotiated, awaiting funding and a contract modification.

# FIGURES AND TABLES

NO.	DATE	ISSUED FOR	ISSUED BY
1	4-26-03	ISSUED FOR CLIENT REVIEW	ISSUED FOR

**S** Severson Environmental Services Inc.  
 6740 LANSING ROAD  
 GRAND RAPIDS, MI 49503

**Shaw** 103 COLLEGE AVE. SE  
 GRAND RAPIDS, MICHIGAN 49503

**US Army Corps of Engineers**  
 Kansas City District  
 CONTRACT NO. DACW41-01-D-0001

STUDENT ENGINEER'S NAME  
 NEW YORK PROFESSIONAL ENGINEER LICENSE NUMBER OTHER

DESIGNED BY	DC
CHECKED BY	DC
APPROVED BY	SA
DATE	5-25-03


SITE: VESTAL AREA 4  
 TOWN OF VESTAL, BROOME COUNTY, NEW YORK  
**FIGURE 1**  
 Site Plan with SVE System

SCALE	AS SHOWN
REVISION	
PERMIT NUMBER	081086
DRAWING NUMBER	VES A4 - 1
SHEET	1 OF 3

BASE MAP PROVIDED BY JOYCE SURVEYING AND MAPPING

**LEGEND**

- A5 ● - INJECTION SVE well
- D3 O - VACUUM SVE well
- D3 ⊕ - Nested VACUUM SVE well
- H2 ▽ - SVE well shut off

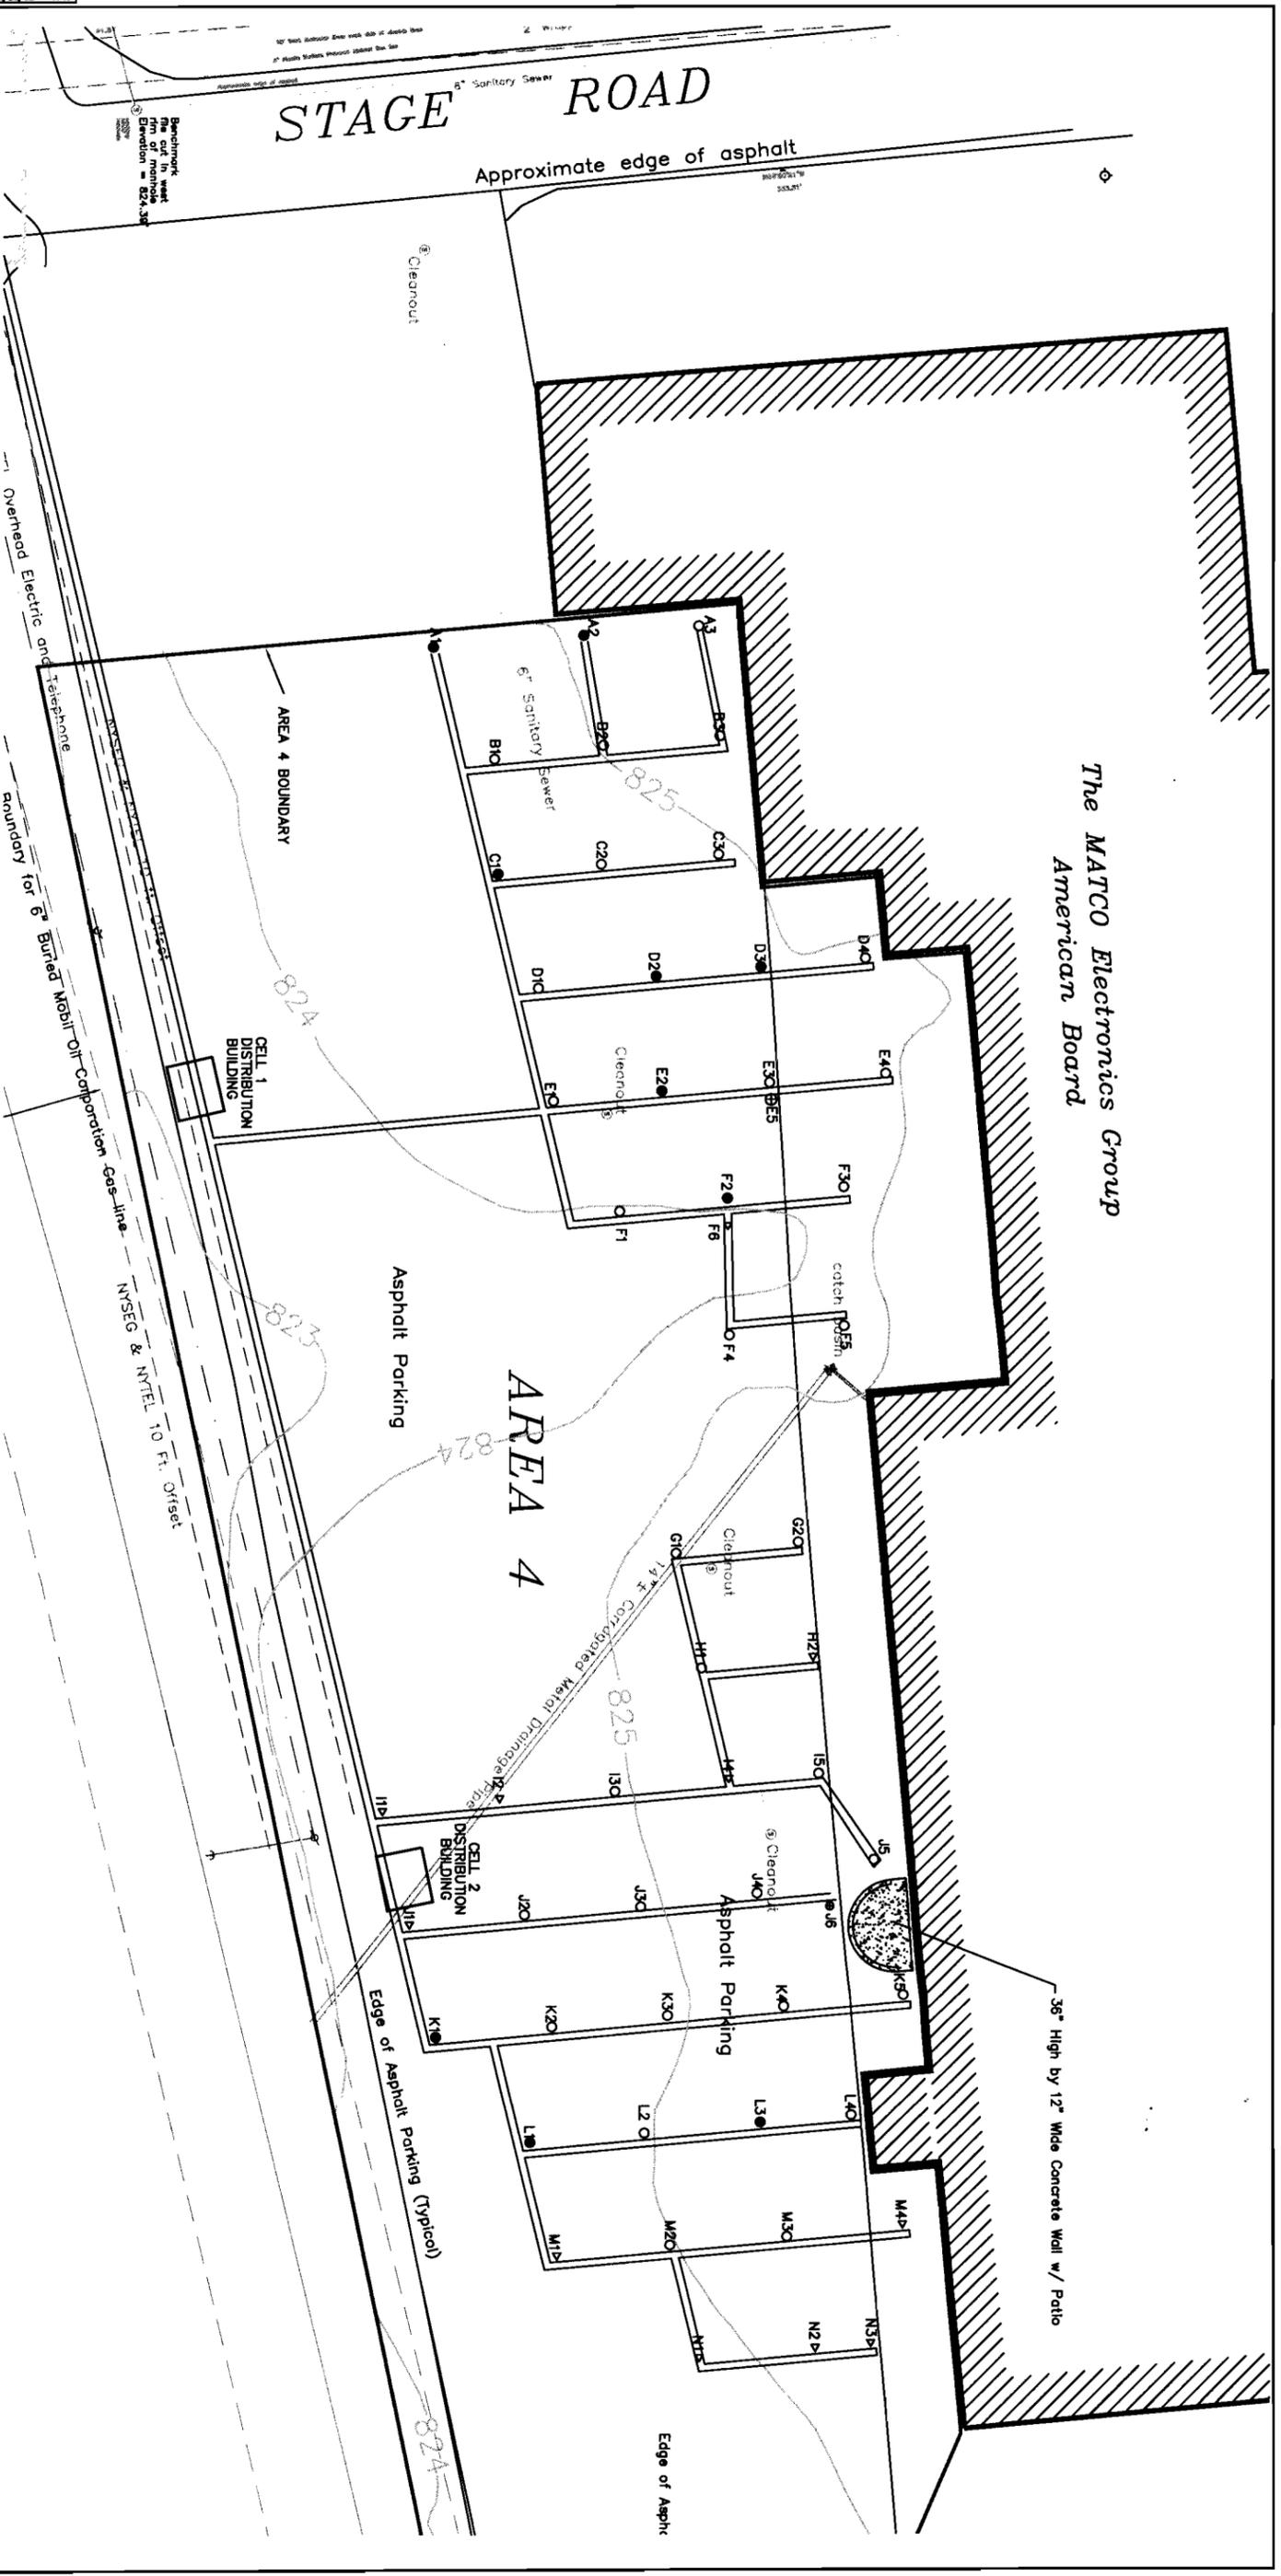

**FIGURE 2**  
**CONCENTRATION (ppmv) AND YIELD RATE (lbs/day)**  
**OF TOTAL TARGET VOCs Vs. TIME**  
**TOTAL SYSTEM SAMPLE**  
**VESTAL AREA 4**


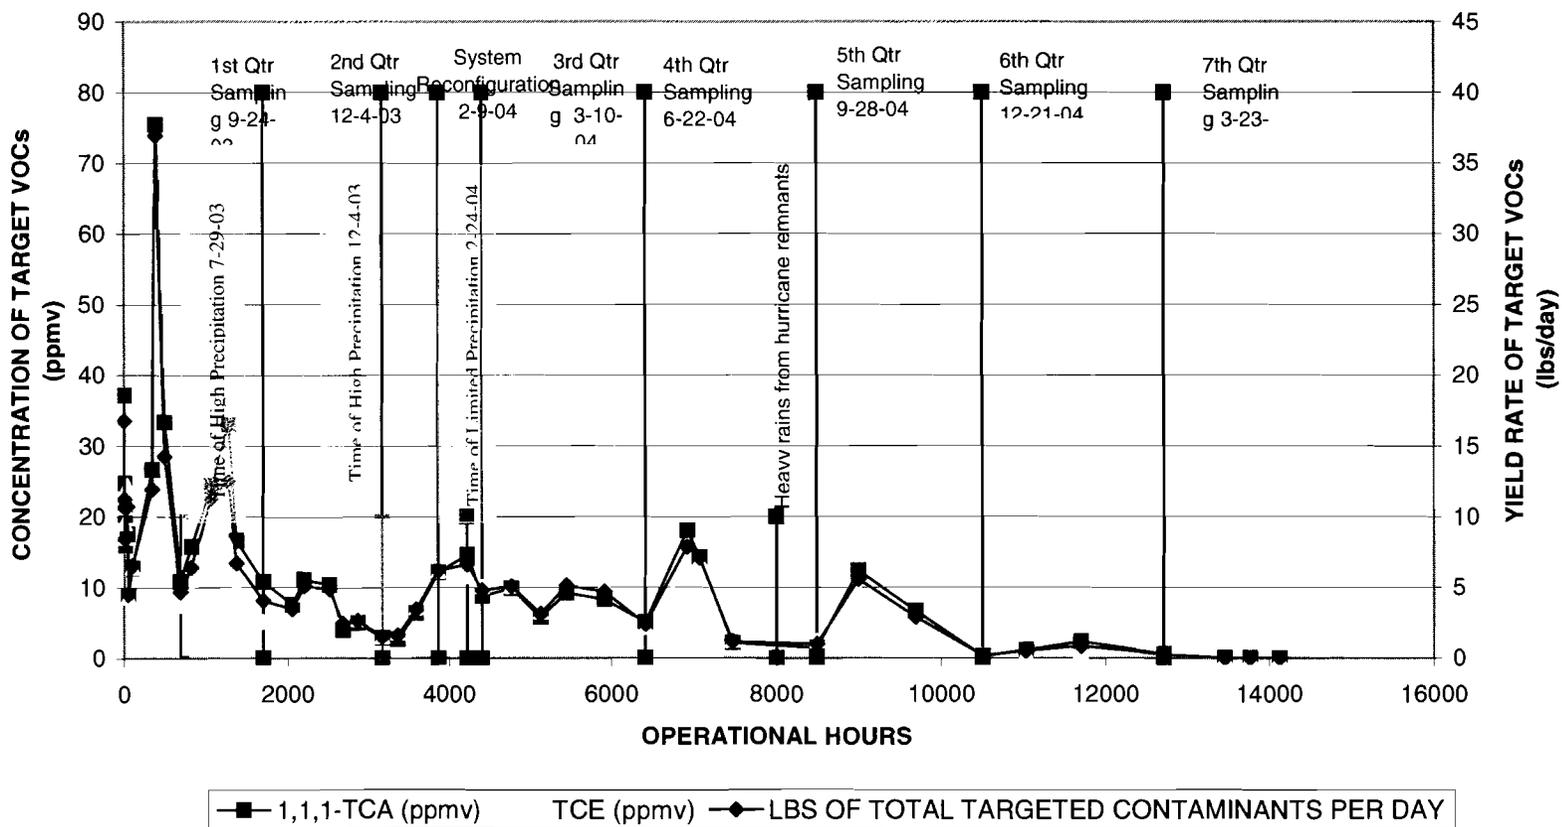


FIGURE 3  
TOTAL TARGET CONTAMINANT YIELD START-UP TO DATE (lbs) Vs. TIME  
TOTAL SYSTEM SAMPLE  
VESTAL, AREA 4

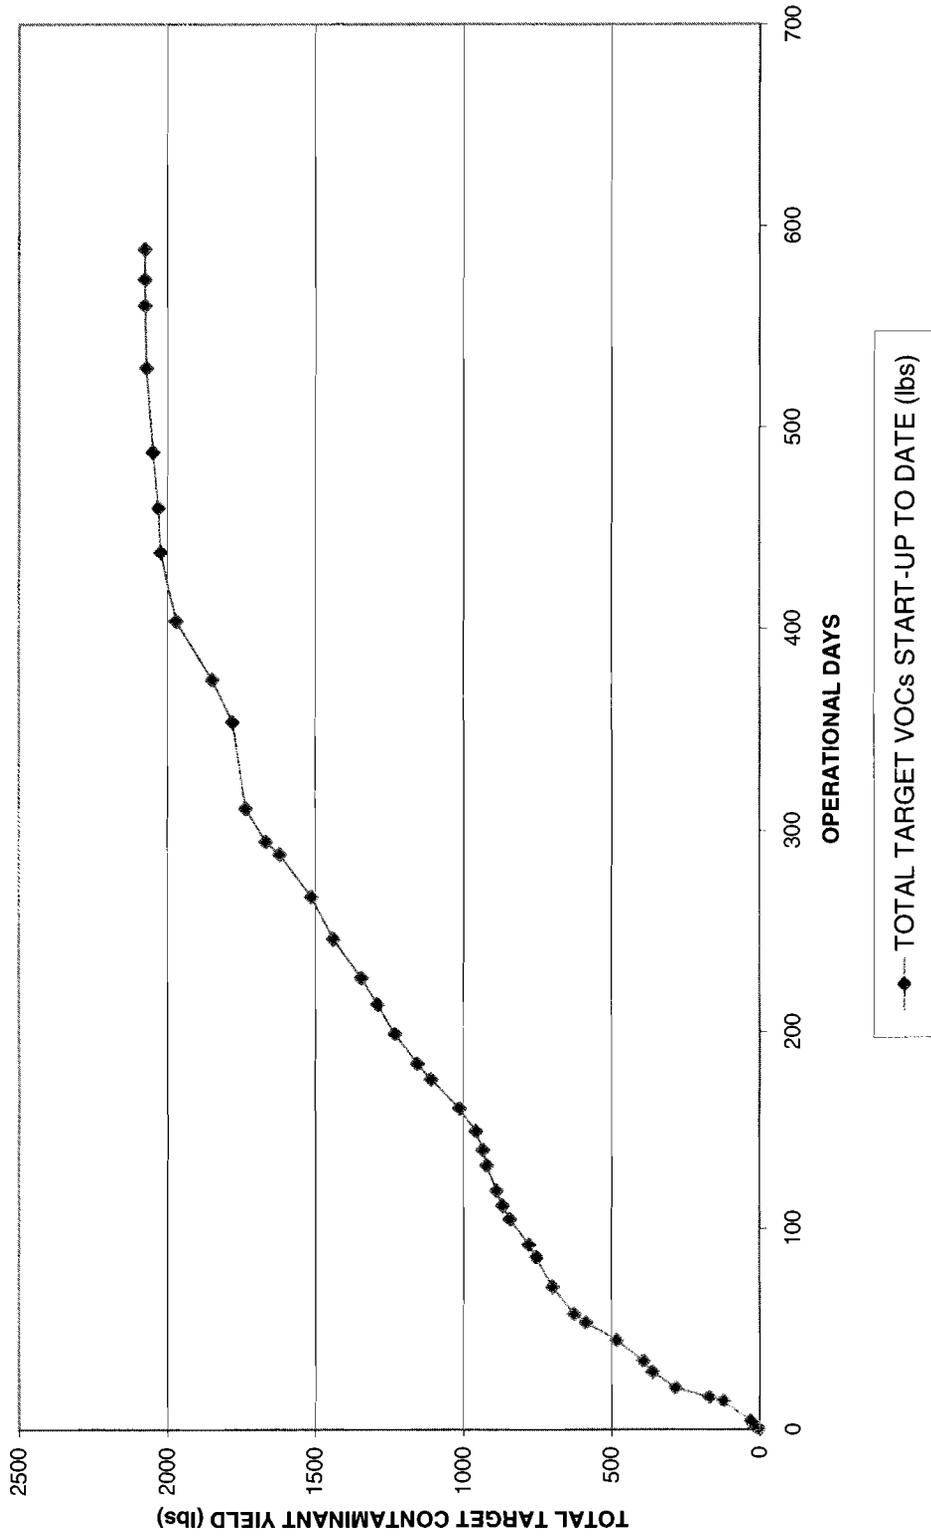

**TABLE 1**  
**SVE WELL STATUS**  
**VESTAL AREA 4**  
**May 25, 2005**

SVE WELL #	VAC WELL	INJ WELL	FLOW RATE	STATUS	PID READINGS	SOIL CONCENTRATION
Bypass Flow Rate			210			
INFLUENT			512		1.0	
MIDDLE			512		2.1	
EFFLUENT			512		0.6	
A1		X	9	OPEN	NA	LOW
A2		X	8	OPEN	NA	LOW
A3	X		6	OPEN	11.6	LOW
B1	X		7	OPEN	9.5	LOW
B2	X		7	OPEN	5.3	LOW
B3	X		10	OPEN	11.3	LOW
C1		X	8	OPEN	NA	LOW
C2	X		8	OPEN	1.4	MEDIUM
C3	X		7	OPEN	5.6	MEDIUM
D1	X		5	OPEN	3.8	LOW
D2		X	7	OPEN	NA	MEDIUM
D3		X	9	OPEN	NA	HIGH
D4	X		<5	LF	2.2	HIGH
E1	X		9	OPEN	2.5	LOW
E2		X	10	OPEN	NA	MEDIUM
E3	X		16	OPEN	4.0	HIGH
E4	X		15	OPEN	7.6	HIGH
E5	X		<5	LF	9.9	HIGH
F1	X		8	OPEN	5.7	LOW
F2		X	10	OPEN	NA	MEDIUM
F3	X		<5	LF	11.2	MEDIUM
F4	X		7	OPEN	4.3	LOW
F5	X		<5	LF	4.9	LOW
F6	X		5	OPEN	6.1	LOW
G1	X		9	OPEN	12.3	LOW
G2	X		18	OPEN	20.1	LOW
H1	X		9	OPEN	8.4	LOW
H2			NA	OFF	NA	LOW
I1	X		6	OPEN	4.2	LOW
I2			NA	OFF	NA	LOW
I3	X		5	OPEN	6.2	MEDIUM
I4			NA	OFF	NA	MEDIUM
I5	X		5	OPEN	14.3	HIGH
J1			NA	OFF	NA	LOW
J2	X		<5	LF	2.5	MEDIUM
J3	X		7	OPEN	13.8	HIGH
J4	X		5	OPEN	15.8	HIGH
J5	X		6	OPEN	4.1	HIGH

**TABLE 1**  
**SVE WELL STATUS**  
**VESTAL AREA 4**  
**May 25, 2005**

SVE WELL #	VAC WELL	INJ WELL	FLOW RATE	STATUS	PID READINGS	SOIL CONCENTRATION
J6	X		5	OPEN	3.5	HIGH
K1		X	5	OPEN	NA	LOW
K2	X		5	OPEN	9.4	LOW
K3	X		5	OPEN	4.2	MEDIUM
K4	X		6	OPEN	1.8	MEDIUM
K5	X		5	OPEN	3.8	HIGH
L1		X	5	OPEN	NA	LOW
L2	X		5	OPEN	1.2	HIGH
L3		X	5	OPEN	NA	LOW
L4	X		<5	LF	2.2	LOW
M1			NA	OFF	NA	LOW
M2	X		5	OPEN	1.2	LOW
M3	X		NA	WATER	NA	LOW
M4			NA	OFF	NA	LOW
N1			NA	OFF	NA	LOW
N2			NA	OFF	NA	LOW
N3			NA	OFF	NA	LOW

NOTE: Total System Flow calculated by Roots Blower program with climate variables of the day of sampling.

LF= limited airflow

**TABLE 2**  
**TARGET CONTAMINANT YIELD**  
**VESTAL AREA 4**

SAMPLE DATE	SAMPLE NUMBER	WELL NUMBER	1,1,1 TCA (lbs/day)	TCE (lbs/day)	TOTAL TARGET VOCs (lbs/day)
6/23/2003	VS-SS-INFL-062303-0	INF	9.58	7.18	16.76
6/23/2003	VS-SS-INFL-062303-1	INF	6.37	4.85	11.22
	INFLUENT AVG PER DAY FOR PERIOD		7.98	6.02	13.99
	TOTAL YIELD (lbs) FOR PERIOD (6/23-6/23)				0.56
6/23/2003	VS-SS-INFL-062303-1	INF	6.37	4.85	11.22
6/23/2003	VS-SS-INFL-062303-4	INF	5.23	5.42	10.66
	INFLUENT AVG PER DAY FOR PERIOD		5.80	5.14	10.94
	TOTAL YIELD (lbs) FOR PERIOD (6/23-6/23)				1.42
6/23/2003	VS-SS-INFL-062303-4	INF	5.23	5.42	10.66
6/23/2003	VS-SS-INFL-062303-8	INF	4.10	4.33	8.43
	INFLUENT AVG PER DAY FOR PERIOD		4.67	4.88	9.55
	TOTAL YIELD (lbs) FOR PERIOD (6/23-6/23)				1.62
6/23/2003	VS-SS-INFL-062303-8	INF	4.10	4.33	8.43
6/24/2003	VS-SS-INF-062403	INF	4.52	6.18	10.70
	INFLUENT AVG PER DAY FOR PERIOD		4.31	5.26	9.57
	TOTAL YIELD (lbs) FOR PERIOD (6/23-6/24)				11.19
6/24/2003	VS-SS-INF-062403	INF	4.52	6.18	10.70
6/25/2003	VS-SS-INF-062503	INF	2.28	2.21	4.48
	INFLUENT AVG PER DAY FOR PERIOD		3.40	4.20	7.59
	TOTAL YIELD (lbs) FOR PERIOD (6/24-6/25)				4.40
6/25/2003	VS-SS-INF-062503	INF	2.28	2.21	4.48
6/27/2003	VS-SVE-INF-062703	INF	3.28	3.26	6.53
	INFLUENT AVG PER DAY FOR PERIOD		2.78	2.74	5.51
	TOTAL YIELD (lbs) FOR PERIOD (6/25-6/27)				10.79
6/27/2003	VS-SVE-INF-062703	INF	3.28	3.26	6.53
7/7/2003	VS-SVE-INF-070703-0001	INF	6.87	5.04	11.91
	INFLUENT AVG PER DAY FOR PERIOD		5.08	4.15	9.22
	TOTAL YIELD (lbs) FOR PERIOD (7/27-7/7)				92.57
7/7/2003	VS-SVE-INF-070703-0001	INF	6.87	5.04	11.91
7/9/2003	VS-SVE-INF-070903-0006	INF	19.45	17.96	36.92
	INFLUENT AVG PER DAY FOR PERIOD		13.16	11.50	24.42
	TOTAL YIELD (lbs) FOR PERIOD (7/7-7/9)				47.85
7/9/2003	VS-SVE-INF-070903-0006	INF	19.45	17.96	36.92
7/17/2003	VS-SVE-INF-071703-0011	INF	8.60	5.65	14.25
	INFLUENT AVG PER DAY FOR PERIOD		14.03	11.81	25.59
	TOTAL YIELD (lbs) FOR PERIOD (7/9-7/17)				114.11

**TABLE 2**  
**TARGET CONTAMINANT YIELD**  
**VESTAL AREA 4**

SAMPLE DATE	SAMPLE NUMBER	WELL NUMBER	1,1,1 TCA (lbs/day)	TCE (lbs/day)	TOTAL TARGET VOCs (lbs/day)
7/17/2003	VS-SVE-INF-071703-0011	INF	8.60	5.65	14.25
7/29/2003	VS-SVE-INF-072903-0016	INF	2.70	1.88	4.67
	INFLUENT AVG PER DAY FOR PERIOD		5.65	3.77	9.46
	TOTAL YIELD (lbs) FOR PERIOD (7/17-7/29)				76.91
7/29/2003	VS-SVE-INF-072903-0016	INF	2.70	1.88	4.67
8/12/2003	VS-SVE-INF-081203-0026	INF	4.07	2.34	6.40
	INFLUENT AVG. PER DAY FOR PERIOD		3.39	2.11	5.54
	TOTAL YIELD (lbs) FOR PERIOD (7/29-8/12)				30.33
8/12/2003	VS-SVE-INF-081203-0026	INF	4.07	2.34	6.40
8/25/2003	VS-SVE-INF-082503-0031	INF	6.23	5.06	11.28
	INFLUENT AVG. PER DAY FOR PERIOD		5.15	3.70	8.84
	TOTAL YIELD (lbs) FOR PERIOD (8/12-8/25)				90.08
8/25/2003	VS-SVE-INF-082503-0031	INF	6.23	5.06	11.28
9/3/2003	VS-SVE-INF-090303-0036	INF	8.45	4.01	12.46
	INFLUENT AVG. PER DAY FOR PERIOD		7.34	4.54	11.87
	TOTAL YIELD (lbs) FOR PERIOD (8/25-9/3)				103.74
9/3/2003	VS-SVE-INF-090303-0036	INF	8.45	4.01	12.46
9/8/2003	VS-SVE-INF-090803-0041	INF	4.23	2.46	6.70
	INFLUENT AVG. PER DAY FOR PERIOD		6.34	3.24	9.58
	TOTAL YIELD (lbs) FOR PERIOD (9/3-9/8)				38.51
9/8/2003	VS-SVE-INF-090803-0041	INF	4.23	2.46	6.70
9/24/2003	VS-SVE-INF-092403-0099	INF	2.74	1.30	4.04
	INFLUENT AVG. PER DAY FOR PERIOD		3.48	1.88	5.37
	TOTAL YIELD (lbs) FOR PERIOD (9/8-9/24)				72.89
9/24/2003	VS-SVE-INF-092403-0099	INF	2.74	1.30	4.04
10/9/2003	VS-SVE-INF-100903-0109	INF	1.91	1.51	3.42
	INFLUENT AVG. PER DAY FOR PERIOD		2.32	1.40	3.73
	TOTAL YIELD (lbs) FOR PERIOD (9/24-10/9)				55.77
10/9/2003	VS-SVE-INF-100903-0109	INF	1.91	1.51	3.42
10/15/2003	VS-SVE-INF-101503-0114	INF	2.82	2.26	5.08
	INFLUENT AVG. PER DAY FOR PERIOD		2.37	1.89	4.25
	TOTAL YIELD (lbs) FOR PERIOD (10/9-10/15)				25.50
10/15/2003	VS-SVE-INF-101503-0114	INF	2.82	2.26	5.08
10/28/2003	VS-SVE-INF-102803-0119	INF	2.65	2.21	4.86
	INFLUENT AVG. PER DAY FOR PERIOD		2.74	2.24	4.97
	TOTAL YIELD (lbs) FOR PERIOD (10/15-10/28)				64.91
10/28/2003	VS-SVE-INF-102803-0119	INF	2.65	2.21	4.86
11/11/2003	VS-SVE-INF-111103-0124	INF	0.99	1.46	2.45
	INFLUENT AVG. PER DAY FOR PERIOD		1.82	1.84	3.66
	TOTAL YIELD (lbs) FOR PERIOD (10/28-11/11)				25.11

**TABLE 2**  
**TARGET CONTAMINANT YIELD**  
**VESTAL AREA 4**

SAMPLE DATE	SAMPLE NUMBER	WELL NUMBER	1,1,1 TCA (lbs/day)	TCE (lbs/day)	TOTAL TARGET VOCs (lbs/day)
11/11/2003	VS-SVE-INF-111103-0124	INF	0.99	1.46	2.45
11/19/2003	VS-SVE-INF-111903-0129	INF	1.27	1.39	2.65
	INFLUENT AVG. PER DAY FOR PERIOD		1.13	1.43	2.55
	TOTAL YIELD (lbs) FOR PERIOD (11/11-11/19)				19.74
11/19/2003	VS-SVE-INF-111103-0124	INF	1.27	1.39	2.65
12/4/2003	VS-SVE-INF-111903-0129	INF	0.74	0.76	1.50
	INFLUENT AVG. PER DAY FOR PERIOD		1.01	1.08	2.08
	TOTAL YIELD (lbs) FOR PERIOD (11/19-12/4)				32.56
12/4/2003	VS-SVE-INF-111903-0129	INF	0.74	0.76	1.50
1/14/2004	VS-SVE-INF-011404-0197	INF	0.69	0.90	1.59
	INFLUENT AVG. PER DAY FOR PERIOD		0.72	0.83	1.55
	TOTAL YIELD (lbs) FOR PERIOD (12/4-1/14)				12.13
1/14/2004	VS-SVE-INF-011404-0197	INF	0.69	0.90	1.59
1/26/2004	VS-SVE-INF-012604-0202	INF	1.63	1.79	3.42
	INFLUENT AVG. PER DAY FOR PERIOD		1.16	1.35	2.51
	TOTAL YIELD (lbs) FOR PERIOD (1/14-1/26)				24.17
1/26/2004	VS-SVE-INF-012604-0202	INF	1.63	1.79	3.42
2/9/2004	VS-SVE-INF-020904-0207	INF	3.09	3.10	6.20
	INFLUENT AVG. PER DAY FOR PERIOD		2.36	2.45	4.81
	TOTAL YIELD (lbs) FOR PERIOD (1/26-2/9)				55.27
2/9/2004	VS-SVE-INF-020904-0207	INF	3.09	3.10	6.20
2/24/2004	VS-SVE-INF-022404-0212	INF	3.72	2.91	6.63
	INFLUENT AVG. PER DAY FOR PERIOD		3.41	3.01	6.42
	TOTAL YIELD (lbs) FOR PERIOD (2/9-2/24)				95.58
2/24/2004	VS-SVE-INF-022404-0212	INF	3.72	2.91	6.63
3/10/2004	VS-SVE-INF-031004-0262	INF	2.23	2.54	4.78
	INFLUENT AVG. PER DAY FOR PERIOD		2.98	2.73	5.71
	TOTAL YIELD (lbs) FOR PERIOD (2/24-3/10)				45.58
3/10/2004	VS-SVE-INF-031004-0262	INF	2.23	2.54	4.78
4/5/2004	VS-SVE-INF-040504-0267	INF	2.51	2.56	5.07
	INFLUENT AVG. PER DAY FOR PERIOD		2.37	2.55	4.93
	TOTAL YIELD (lbs) FOR PERIOD (3/10-4/5)				75.11
4/5/2004	VS-SVE-INF-040504-0267	INF	2.51	2.56	5.07
4/27/2004	VS-SVE-INF-042704-0272	INF	1.47	1.64	3.11
	INFLUENT AVG. PER DAY FOR PERIOD		1.99	2.10	4.09
	TOTAL YIELD (lbs) FOR PERIOD (4/5-4/27)				60.45
4/27/2004	VS-SVE-INF-042704-0272	INF	1.47	1.64	3.11
5/11/2004	VS-SVE-INF-051104-0277	INF	2.35	2.77	5.12
	INFLUENT AVG. PER DAY FOR PERIOD		1.91	2.21	4.12
	TOTAL YIELD (lbs) FOR PERIOD (4/27-5/11)				54.36

**TABLE 2**  
**TARGET CONTAMINANT YIELD**  
**VESTAL AREA 4**

SAMPLE DATE	SAMPLE NUMBER	WELL NUMBER	1,1,1 TCA (lbs/day)	TCE (lbs/day)	TOTAL TARGET VOCs (lbs/day)
5/11/2004	VS-SVE-INF-051104-0277	INF	2.35	2.77	5.12
6/1/2004	VS-SVE-INF-060104-0282	INF	2.10	2.59	4.69
	INFLUENT AVG. PER DAY FOR PERIOD				4.91
	TOTAL YIELD (lbs) FOR PERIOD (5/11-6/1)				94.18
6/1/2004	VS-SVE-INF-060104-0282	INF	2.10	2.59	4.69
6/22/2004	VS-SVE-INF-062204-0332	INF	1.30	1.11	2.40
	INFLUENT AVG. PER DAY FOR PERIOD				3.55
	TOTAL YIELD (lbs) FOR PERIOD (6/1-6/22)				73.91
6/22/2004	VS-SVE-INF-062204-0332	INF	1.30	1.11	2.40
7/13/2004	VS-SVE-INF-071304-0337	INF	4.61	3.23	7.84
	INFLUENT AVG. PER DAY FOR PERIOD				5.12
	TOTAL YIELD (lbs) FOR PERIOD (6/22-7/13)				107.37
7/13/2004	VS-SVE-INF-071304-0337	INF	4.61	3.23	7.84
7/22/2004	VS-SVE-INF-072204-0342	INF	3.63	3.46	7.09
	INFLUENT AVG. PER DAY FOR PERIOD				7.47
	TOTAL YIELD (lbs) FOR PERIOD (7/13-7/22)				46.95
7/22/2004	VS-SVE-INF-072204-0342	INF	3.63	3.46	7.09
8/16/2004	VS-SVE-INF-081604-0347	INF	0.54	0.63	1.17
	INFLUENT AVG. PER DAY FOR PERIOD				4.13
	TOTAL YIELD (lbs) FOR PERIOD (7/22-8/16)				68.02
8/16/2004	VS-SVE-INF-081604-0347	INF	0.54	0.63	1.17
9/28/2004	VS-SVE-INF-092804-0423	INF	0.37	0.62	0.98
	INFLUENT AVG. PER DAY FOR PERIOD				1.08
	TOTAL YIELD (lbs) FOR PERIOD (8/16-9/28)				46.06
9/28/2004	VS-SVE-INF-092804-0423	INF	0.37	0.62	0.98
10/19/2004	VS-SVE-INF-101904-0428	INF	3.15	2.40	5.56
	INFLUENT AVG. PER DAY FOR PERIOD				3.27
	TOTAL YIELD (lbs) FOR PERIOD (9/28-10/19)				68.67
10/19/2004	VS-SVE-INF-101904-0428	INF	3.15	2.40	5.56
11/17/2004	VS-SVE-INF-111704-0433	INF	1.69	1.20	2.89
	INFLUENT AVG. PER DAY FOR PERIOD				4.23
	TOTAL YIELD (lbs) FOR PERIOD (10/19-11/17)				122.53
11/17/2004	VS-SVE-INF-111704-0433	INF	1.69	1.20	2.89
12/21/2004	VS-SVE-INF-122104-0493	INF	0.07	0.12	0.19
	INFLUENT AVG. PER DAY FOR PERIOD				1.54
	TOTAL YIELD (lbs) FOR PERIOD (11/17-12/21)				52.22

**TABLE 2**  
**TARGET CONTAMINANT YIELD**  
**VESTAL AREA 4**

SAMPLE DATE	SAMPLE NUMBER	WELL NUMBER	1,1,1 TCA (lbs/day)	TCE (lbs/day)	TOTAL TARGET VOCs (lbs/day)
12/21/2004	VS-SVE-INF-122104-0493	INF	0.07	0.12	0.19
1/12/2005	VS-SVE-INF-011205-0498	INF	0.29	0.20	0.49
	INFLUENT AVG. PER DAY FOR PERIOD		0.18	0.16	0.34
	TOTAL YIELD (lbs) FOR PERIOD (12/21-1/12)				7.49
1/12/2005	VS-SVE-INF-011205-0498	INF	0.29	0.20	0.49
2/9/2005	VS-SVE-INF-020905-0503	INF	0.58	0.24	0.82
	INFLUENT AVG. PER DAY FOR PERIOD		0.44	0.22	0.66
	TOTAL YIELD (lbs) FOR PERIOD (1/12-2/9)				18.29
2/9/2005	VS-SVE-INF-020905-0503	INF	0.58	0.24	0.82
3/23/2005	VS-SVE-INF-032305-0551	INF	0.14	0.12	0.25
	INFLUENT AVG. PER DAY FOR PERIOD		0.36	0.18	0.54
	TOTAL YIELD (lbs) FOR PERIOD (2/9-3/23)				22.46
3/23/2005	VS-SVE-INF-032305-0551	INF	0.14	0.12	0.25
4/27/2005	VS-SVE-INF-042705-0556	INF	0.00	0.00	0.00
	INFLUENT AVG. PER DAY FOR PERIOD		0.07	0.06	0.13
	TOTAL YIELD (lbs) FOR PERIOD (3/23-4/27)				3.86
4/27/2005	VS-SVE-INF-042705-0556	INF	0.00	0.00	0.00
5/10/2005	VS-SVE-INF-051005-0563	INF	0.00	0.00	0.00
	INFLUENT AVG. PER DAY FOR PERIOD		0.00	0.00	0.00
	TOTAL YIELD (lbs) FOR PERIOD (4/27-5/10)				0.00
5/10/2005	VS-SVE-INF-051005-0563	INF	0.00	0.00	0.00
5/25/2005	VS-SVE-INF-052505-0568	INF	0.00	0.00	0.00
	INFLUENT AVG. PER DAY FOR PERIOD		0.00	0.00	0.00
	TOTAL YIELD (lbs) FOR PERIOD (5/10-5/25)				0.00
<b>TOTAL YIELD TO REPORTED DATE</b>					<b>2075.24</b>

Note 1: Beginning and ending period influent yields are averaged and then multiplied by the number of operational days during the reporting period.

Note 2: 1,1,1 TCA= 1,1,1-Trichloroethane  
 TCE= Trichloroethene

Note 3: INF= Influent

**TABLE 3**  
**TOTAL TARGET CONTAMINANT YIELD TO DATE**  
**VESTAL AREA 4**

SAMPLE DATE	1,1,1 TCA (lbs)	TCE (lbs)	TOTAL TARGET VOCs (lbs)
6/23/2003	0.00	0.00	0.00
6/23/2003	0.33	0.25	0.58
6/23/2003	1.06	0.89	1.95
6/23/2003	1.84	1.71	3.54
6/24/2003	6.87	7.83	14.70
6/25/2003	8.85	10.28	19.13
6/27/2003	14.28	15.63	29.92
7/7/2003	65.21	57.31	122.52
7/9/2003	90.98	79.35	170.33
7/17/2003	153.51	130.86	284.38
7/29/2003	199.85	161.45	361.30
8/12/2003	218.64	172.99	391.63
8/25/2003	271.09	210.67	481.76
9/3/2003	335.21	250.27	585.48
9/8/2003	360.71	263.28	623.99
9/24/2003	408.05	288.83	696.88
10/9/2003	442.85	309.83	752.68
10/15/2003	457.04	321.14	778.18
10/28/2003	492.69	350.33	843.02
11/11/2003	505.20	362.94	868.14
11/19/2003	513.95	373.96	887.91
12/4/2003	529.68	390.80	920.48
1/14/2004	535.30	397.32	932.62
1/26/2004	546.51	410.29	956.80
2/9/2004	573.66	438.42	1012.08
2/24/2004	624.45	483.19	1107.65
3/10/2004	648.24	504.97	1153.22
4/5/2004	684.38	543.87	1228.25
4/27/2004	713.77	574.92	1288.69
5/11/2004	739.02	604.07	1343.09
6/1/2004	781.81	655.48	1437.29
6/22/2004	817.27	693.97	1511.24
7/13/2004	879.24	739.47	1618.71
7/22/2004	905.17	760.52	1665.69
8/16/2004	939.55	794.17	1733.72
9/28/2004	959.14	820.79	1779.93
10/19/2004	996.13	852.47	1848.60
11/17/2004	1066.51	904.73	1971.24
12/21/2004	1096.44	927.00	2023.44
1/12/2005	1100.43	930.44	2030.87
2/9/2005	1112.63	936.50	2049.13
3/23/2005	1127.81	943.89	2071.71

<b>SAMPLE DATE</b>	<b>1,1,1 TCA (lbs)</b>	<b>TCE (lbs)</b>	<b>TOTAL TARGET VOCs (lbs)</b>
4/27/2005	1129.95	945.69	2075.64
5/10/2005	1129.95	945.69	2075.64
5/25/2005	1129.95	945.69	2075.64

NOTE 1:                   1,1,1 TCA= 1,1,1-Trichloroethane  
                              TCE= Trichloroethene

# **APPENDIX A**

## **Sampling and Analytical Data**

QA/QC Report for Vestal Samples  
(Sample Date: 5/10/05)

1. Sample Receipt

The samples arrived at the lab were carefully packed in coolers. All of the sample bags in the coolers arrived intact and the labels on the bags were found to be complete. The information on the sample labels agreed with the information on the chain-of-custody forms placed inside the shipping coolers.

2. Sample Holding Times

The required holding times were met according to the lab SOP.

3. Instrument Blank Analysis

The instrument blank analysis indicated the instruments did not contain any target compounds.

4. Lab Duplicate Analysis

Vestal Duplicate Sample RPD Report					
Sample ID: VS-SVE-EFF-051005-0565					
Sample Date	Analytes	Data1	Data2	RPD (%)	RPD Acceptable?
5/10/2005	1,1,1-TCA	1.762	1.587	10.5	YES

5. GC Calibrations

The instruments performed target compound standards calibration check each analysis day, or re-run the standards. The results met the requirement in the lab SOP.

6. Lab Authentication Statement

I certify, to the best of my knowledge, that the information in this QA/QC report is true, accurate and complete.



Yixin Li  
Chemist  
Shaw E & I  
14155 Farmington Rd.  
Livonia, MI 48154

QA/QC Report for Vestal Samples  
(Sample Date: 5/25/05)

1. Sample Receipt

The samples arrived at the lab were carefully packed in coolers. All of the sample bags in the coolers arrived intact and the labels on the bags were found to be complete. The information on the sample labels agreed with the information on the chain-of-custody forms placed inside the shipping coolers.

2. Sample Holding Times

The required holding times were met according to the lab SOP.

3. Instrument Blank Analysis

The instrument blank analysis indicated the instruments did not contain any target compounds.

4. Lab Duplicate Analysis

Vestal Duplicate Sample RPD Report					
Sample ID: VS-SVE-MID-052505-0569					
Sample Date	Analytes	Data1	Data2	RPD (%)	RPD Acceptable?
5/25/2005	1,1,1-TCA	1.008	1.084	7.3	YES

5. GC Calibrations

The instruments performed target compound standards calibration check each analysis day, or re-run the standards. The results met the requirement in the lab SOP.

6. Lab Authentication Statement

I certify, to the best of my knowledge, that the information in this QA/QC report is true, accurate and complete.



Yixin Li  
Chemist  
Shaw E & I  
14155 Farmington Rd.  
Livonia, MI 48154

SAMPLE DATE	SAMPLE ID	1,1,1-TCA (ppm)	TCE (ppm)	Detection Limits (ppm)
10-May-05	INSTRUMENT BLANK	0.00	0.00	0.05
10-May-05	VS-SVE-TB-051005-0567	0.00	0.00	0.05
25-May-05	INSTRUMENT BLANK	0.00	0.00	0.05
25-May-05	VS-SVE-TB-052505-0572	0.00	0.00	0.05

Notes: 0.00 indicates below detection limit.

# Shaw E & I Lab Analytical Results

**Client:** Severson/USACE  
**Analysis Date:** 5/11/2005  
**Detection Limit:** See below  
**Analyst:** YL

**Client Code:** 681086  
**Sample Date:** 5/10/2005  
**Units:** ppmv  
**Project Manager:** D. Callahan

<i>SAMPLE ID</i>	<i>1,1,1-TCA</i>	<i>TCE</i>	<i>DL</i>
VS-SVE-INF-051005-0563	0.00	0.00	0.05
VS-SVE-MID-051005-0564	1.07	0.00	0.05
VS-SVE-EFF-051005-0565	1.27	0.00	0.05
VS-SVE-SP-051005-0566	0.00	0.00	0.05
VS-SVE-TB-051005-0567	0.00	0.00	0.05

**Notes:**

- [1] TVOC: estimated value. TVOC was calculated by the average response factor of the known contaminants.
- [2] 0.00 indicates BELOW DETECTION LIMIT. (For TVOC, the Detection Limit is 1.0 ppmv.)
- [3] DL = Detection Limit.

## CHAIN - OF - CUSTODY for AIR SAMPLES

Hour Meter: 13762.3 HR

Client: SEVENSON / USACE Client Code: #681086

Flow Meter- Type: \_\_\_\_\_ Range (cfm): \_\_\_\_\_

Site Address: 210 STAGE RD, VESTAL, NY

Withdrawal blower - Vacuum: \_\_\_\_\_ Pressure: \_\_\_\_\_

Project Manager: D. CAWAHAN

Injection blower - Vacuum: \_\_\_\_\_ Pressure: \_\_\_\_\_

System Status: "OPERATING"

Sample ID.	Date	Time	Indicated Flow (cfm)	Carbon Dioxide P <sub>50</sub> (ppm)P <sub>50</sub> -	Analysis Requested	Notes
1 US-SVE-0563	5-10-05	0845		1.5	TO14, A	INFLUENT
2 US-SVE-0564	}	0857		2.1	}	MID CARBON
3 US-SVE-0565		0910		0.3		EFFLUENT
4 US-SVE-0566		0830				SAMPLE PUMP
5 US-SVE-0567		TRIP BLANK				TRIP BLANK
6						
7						
8						
9						
10						
11						
12						

Collected By: Colquhoun / McGuire Date: 5-10-05 Time: 0830 **Envirogen, Inc.**

Delivered By: \_\_\_\_\_ Date: \_\_\_\_\_ Time: \_\_\_\_\_ New Solutions to Hazardous Waste Problems

Received By: CP Date: 5/11/05 Time: 9230 5126 West Grand River, Lansing, Michigan. 48906

Remarks: \_\_\_\_\_ Phone #: (517) 886-5600 Fax #: (517) 886-5700

White copy = Laboratory Yellow copy = Technical Analyst Pink copy = Operation Technicians

# Shaw E & I Lab Analytical Results

**Client:** Severson/USACE  
**Analysis Date:** 5/26/2005  
**Detection Limit:** See below  
**Analyst:** YL

**Client Code:** 681086  
**Sample Date:** 5/25/2005  
**Units:** ppmv  
**Project Manager:** D. Callahan

<i>SAMPLE ID</i>	<i>1,1,1-TCA</i>	<i>TCE</i>	<i>DL</i>
VS-SVE-INF-052505-0568	0.00	0.00	0.05
VS-SVE-MID-052505-0569	0.73	0.00	0.05
VS-SVE-EFF-052505-0570	0.00	0.00	0.05
VS-SVE-SP-052505-0571	0.00	0.00	0.05
VS-SVE-TB-052505-0572	0.00	0.00	0.05

**Notes:**

- [1] TVOC: estimated value. TVOC was calculated by the average response factor of the known contaminants.
- [2] 0.00 indicates BELOW DETECTION LIMIT. (For TVOC, the Detection Limit is 1.0 ppmv.)
- [3] DL = Detection Limit.

## CHAIN - OF - CUSTODY for AIR SAMPLES

Hour Meter: 14121.3 hrs.  
 Flow Meter: Type: \_\_\_\_\_ Range (cfm): \_\_\_\_\_  
 Withdrawl blower - Vacuum: \_\_\_\_\_ Pressure: \_\_\_\_\_  
 Injection blower - Vacuum: \_\_\_\_\_ Pressure: \_\_\_\_\_

Client: SEWISON/USACE Client Code: 4681086  
 Site Address: 210 STAGE B, VESTAL, NY  
 Project Manager: D. CALLAHAN  
 System Status: "OPERATING"

Sample ID.	Date	Time	Indicated Flow (cfm)	Carbon Dioxide <del>ppm</del> (ppm) <del>As</del>	Analysis Requested	Notes
1	ISSVE - 0568	5-25-05	0915	1.2	TO14, A	INFLUENT
2	ISSVE - 0569	}	0935	1.5	}	MID CARBON
3	ISSVE - 0570		0950	0.3		EFFLUENT
4	ISSVE - 0571		0845			Sample Pump
5	ISSVE - 0572		_____			Trip Blank
6						
7						
8						
9						
10						
11						
12						

Collected By: CARLUCCI / M. BURE Date: 5-25-05 Time: 0845

Delivered By: \_\_\_\_\_ Date: \_\_\_\_\_ Time: \_\_\_\_\_

Received By: [Signature] Date: 5/26/05 Time: 9:30

Remarks: \_\_\_\_\_

**Envirogen, Inc.**  
 SFW ENCON / CWT, INC.  
 New Solutions to Hazardous Waste Problems  
 103 GLEBE AVE, SE  
 5136 West Grand River, Lansing, Michigan 48906  
 GRAND RAPIDS, MI 49503  
 Phone #: (517) 886-5600 Fax #: (517) 886-5700  
 616-774-3522

White copy = Laboratory    Yellow copy = Technical Analyst    Pink copy = Operation Technicians

# **APPENDIX B**

## **Summary of Operation Data/ Contaminant Yield Calculation**

**Appendix B**  
**Summary of Operation Data**  
**Vestal, Area 4**

SAMPLE DATE	SAMPLE ID	REPORT SAMPLE ID	FLOW (CFM)	1,1,1-TCA (ppmv)	TCE (ppmv)	TOTAL TARGETED CONTAMINANTS (ppmv)	LBS OF 1,1,1-TCA per day	LBS OF TCE per day	LBS OF TOTAL TARGETED CONTAMINANTS PER DAY	OPERATION DAYS	STATION HOUR METER	NUMBER OF DAYS IN PERIOD
6/27/03	INF	VS-SVE-INF-062703	517	12.70	12.83	25.53	3.28	3.26	6.53	4.04	97.0	1.96
7/7/2003	INF	VS-SVE-INF-070703-0001	517	26.62	19.87	46.49	6.87	5.04	11.91	14.08	338	10.04
7/9/2003	INF	VS-SVE-INF-070903-0006	517	75.42	68.79	144.21	19.45	17.46	36.92	16.04	385	1.96
7/17/2003	INF	VS-SVE-INF-071703-0011	517	33.34	22.24	55.58	8.60	5.65	14.25	20.50	492	4.46
7/29/2003	INF	VS-SVE-INF-072903-0016	517	10.83	7.39	18.22	2.79	1.88	4.67	28.63	687.2	8.13
8/12/2003	INF	VS-SVE-INF-081203-0026	517	15.77	9.20	24.97	4.07	2.34	6.40	34.11	818.7	5.48
8/25/2003	INF	VS-SVE-INF-082503-0031	512	24.37	20.12	44.49	6.23	5.06	11.28	44.30	1063.3	10.19
9/3/2003	INF	VS-SVE-INF-090303-0036	512	33.08	15.94	49.02	8.45	4.01	12.46	53.0	1273	8.74
9/8/2003	INF	VS-SVE-INF-090803-0041	512	16.57	9.80	26.37	4.23	2.46	6.70	57.1	1369.5	4.02
9/24/2003	INF	VS-SVE-INF-092403-0099	512	10.72	5.16	15.88	2.74	1.30	4.04	70.6	1695.5	13.58
10/15/2003	INF	VS-SVE-INF-101503-0114	512	11.02	8.98	20.00	2.82	2.26	5.07	91.6	2,198.6	20.96
10/15/2003	INF	VS-SVE-INF-101503-0114	512	11.02	8.98	20.00	2.82	2.26	5.07	91.6	2198.6	0.00
10/28/2003	INF	VS-SVE-INF-102803-0119	512	10.36	8.80	19.16	2.65	2.21	4.86	104.7	2512.0	13.06
11/11/2003	INF	VS-SVE-INF-111103-0124	512	3.89	5.81	9.70	0.99	1.46	2.45	111.5	2,676.9	6.87
11/19/2003	INF	VS-SVE-INF-111903-0129	512	4.96	5.51	10.47	1.27	1.39	2.65	119.3	2,862.7	7.74
12/4/2003	INF	VS-SVE-INF-120403-0187	512	2.89	3.03	5.92	0.74	0.76	1.50	132.0	3167.2	15.69
1/14/2004	INF	VS-SVE-INF-011404-0197	512	2.71	3.57	6.28	0.69	0.90	1.59	139.8	3,355.7	7.85
1/26/2004	INF	VS-SVE-INF-012604-0202	512	6.39	7.13	13.52	1.63	1.79	3.42	149.5	3,587.2	9.65
2/9/2004	INF	VS-SVE-INF-020904-0207	512	12.11	12.34	24.45	3.09	3.10	6.20	161.0	3,863.0	11.49
2/24/2004	INF	VS-SVE-INF-022404-0212	512	14.57	11.56	26.13	3.72	2.91	6.63	175.9	4,220.7	14.90
3/10/2004	INF	VS-SVE-INF-031004-0262	512	8.74	10.12	18.86	2.23	2.54	4.78	183.9	4,412.5	7.99
4/5/2004	INF	VS-SVE-INF-040504-0267	512	9.82	10.18	19.99	2.51	2.56	5.07	199.1	4,778.4	15.25
4/27/2004	INF	VS-SVE-INF-042704-0272	512	5.76	6.54	12.30	1.47	1.64	3.11	213.9	5133	14.78
5/11/2004	INF	VS-SVE-INF-051104-0277	512	9.21	11.02	20.23	2.35	2.77	5.12	227.1	5,450.0	13.21
6/1/2004	INF	VS-SVE-INF-060104-0282	512	8.24	10.29	18.53	2.10	2.59	4.69	246.3	5,910.7	19.20
6/22/2004	INF	VS-SVE-INF-062204-0332	512	5.08	4.40	9.48	1.30	1.11	2.40	267.1	6,411.0	20.85
7/13/2004	INF	VS-SVE-INF-071304-0337	512	18.05	12.86	30.91	4.61	3.23	7.84	288.1	6,914.3	20.97
7/22/2004	INF	VS-SVE-INF-072204-0342	512	14.22	13.76	27.98	3.63	3.46	7.09	294.4	7,065.3	6.29
8/16/2004	INF	VS-SVE-INF-081604-0347	512	2.13	2.49	4.63	0.54	0.63	1.17	310.9	7,460.5	16.47
9/28/2004	INF	VS-SVE-INF-092804-0423	512	1.45	2.45	3.89	0.37	0.62	0.98	353.7	8,489.0	42.85
10/19/2004	INF	VS-SVE-INF-101904-0428	512	12.35	9.55	21.90	3.15	2.40	5.56	374.7	8,993.0	21.00
11/17/2004	INF	VS-SVE-INF-111704-0433	512	6.63	4.76	11.39	1.69	1.20	2.89	403.8	9,690.0	29.04
12/21/2004	INF	VS-SVE-INF-122104-0493	512	0.29	0.46	0.74	0.07	0.12	0.19	437.7	10,503.8	33.91
1/12/2005	INF	VS-SVE-INF-011205-0498	512	1.13	0.79	1.92	0.29	0.20	0.49	459.7	11,032.5	22.03

**Summary of Operation Data**

**Vestal, Area 4**

SAMPLE DATE	SAMPLE ID	REPORT SAMPLE ID	FLOW (CFM)	1,1,1-TCA (ppmv)	TCE (ppmv)	TOTAL TARGETED CONTAMINANTS (ppmv)	LBS OF 1,1,1-TCA per day	LBS OF TCE per day	LBS OF TOTAL TARGETED CONTAMINANTS PER DAY	OPERATION DAYS	STATION HOUR METER	NUMBER OF DAYS IN PERIOD
2/9/2005	INF	VS-SVE-INF-020905-0503	512	2.29	0.94	3.23	0.58	0.24	0.82	487.6	11,702.8	27.93
3/23/2005	INF	VS-SVE-INF-032305-0551	512	0.54	0.46	1.00	0.14	0.12	0.25	529.6	12,710.4	41.98
4/27/2005	INF	VS-SVE-INF-042705-0556	512	0.00	0.00	0.00	0.00	0.00	0.00	560.50	13,452.1	30.90
5/10/2005	INF	VS-SVE-INF-051005-0563	512	0.00	0.00	0.00	0.00	0.00	0.00	573.43	13,762.3	12.93
5/25/2005	INF	VS-SVE-INF-052505-0568	512	0.00	0.00	0.00	0.00	0.00	0.00	588.39	14,121.3	14.96

## Appendix B

### Example Calculations

#### Vestal, Area 4

Example: 8/25/03

1,1,1 TCA (ppm) to 1,1,1 TCA (lbs/day)

$$0.00000374(\text{conversion constant}) * 24.37(\text{ppm}) * 512(\text{flow}) * 133.4(\text{molecular weight}) = 6.23 \text{ lbs}$$

Example: 8/12/03 to 8/25/03 'Total Target VOCs'

$$[6.40 (8/12) + 11.28 (8/25)] / 2 = 8.84 \text{ avg. lbs per day for the period}$$
$$8.84 (\text{lbs per day}) * 10.19 (\text{days}) = 90.08 \text{ pounds per reporting period}$$

Calculated Flow Rate:

Vacuum Pressure (inches Hg) = 6

Blower Speed (RPM) = 2000

Temperature (degrees F) = 72

Elevation = 1200 feet

Based on proprietary Roots, Inc flow rate software for Roots 68 blower,  
the CFM for these parameters is 512 on 8/25/03

||

**Appendix B**  
**Influent Sample Parameters**  
**Vestal, Area 4**

SAMPLE DATE	SAMPLE ID	VACUUM PRESSURE (inches Hg)	RPM	TEMPERATURE (degrees F)	FLOW (cfm)	PID	OPERATION DAYS	STATION HOUR METER
6/27/03	VS-SVE-INF-062703	6	2000	68	517	34.0	4.0	97.0
7/7/2003	VS-SVE-INF-070703-0001	6	2000	72	517	153.4	14.1	338
7/9/2003	VS-SVE-INF-070903-0006	6	2000	75	517	87.0	16.0	385
7/17/2003	VS-SVE-INF-071703-0011	6	2000	80	517	79.5	20.5	492
7/29/2003	VS-SVE-INF-072903-0016	6	2000	75	517	20.3	28.6	687.2
8/12/2003	VS-SVE-INF-081203-0026	6	2000	73	517	45.6	34.1	818.7
8/25/2003	VS-SVE-INF-082503-0031	6	2000	72	512	27.5	44.3	1063.3
9/3/2003	VS-SVE-INF-090303-0036	6	2000	70	512	21.3	53.0	1273.0
9/8/2003	VS-SVE-INF-090803-0041	6	2000	70	512	22.8	57.1	1369.5
9/24/2003	VS-SVE-INF-092403-0099	6	2000	70	512	12.6	70.6	1695.5
10/15/2003	VS-SVE-INF-101503-0114	6	2000	62	512	14.2	91.6	2,198.6
10/15/2003	VS-SVE-INF-101503-0114	6	2000	68	512	13.7	91.6	2198.6
10/28/2003	VS-SVE-INF-102803-0119	6	2000	65	512	16.4	104.7	2512.0
11/11/2003	VS-SVE-INF-111103-0124	6	2000	54	512	7.9	111.5	2676.9
11/19/2003	VS-SVE-INF-111903-0129	6	2000	50	512	12.1	119.3	2862.7
12/4/2003	VS-SVE-INF-120403-0187	6	2000	48	512	7.7	132.0	3167.2
1/14/2004	VS-SVE-INF-011404-0197	6	2000	50	512	7.7	139.8	3,355.7
1/26/2004	VS-SVE-INF-012604-0202	6	2000	50	512	12.9	149.5	3,587.2
2/9/2004	VS-SVE-INF-020904-0207	6	2000	40	512	21.3	161.0	3,863.0
2/24/2004	VS-SVE-INF-022404-0212	6	2000	45	512	19.5	175.9	4,220.7
3/10/2004	VS-SVE-INF-031004-0262	6	2000	48	512	10.3	183.9	4,412.5
4/5/2004	VS-SVE-INF-040504-0267	6	2000	66	512	11.9	199.1	4,778.4
4/27/2004	VS-SVE-INF-042704-0272	6	2000	68	512	5.0	213.9	5,133
5/11/2004	VS-SVE-INF-051104-0277	6	2000	64	512	13.4	227.1	5,450.0
6/1/2004	VS-SVE-INF-060104-0282	6	2000	62	512	14.8	246.3	5,910.7
6/22/2004	VS-SVE-INF-062204-0332	6	2000	68	512	7.7	267.1	6,411.0
7/13/2004	VS-SVE-INF-071304-0337	6	2000	76	512	15.4	288.1	6,914.3
7/22/2004	VS-SVE-INF-072204-0342	6	2000	80	512	16.1	294.4	7,065.3
8/16/2004	VS-SVE-INF-081604-0347	6	2000	75	512	5.4	310.9	7,460.5
9/28/2004	VS-SVE-INF-092804-0423	6	2000	60	512	17.4	353.7	8,489.0
10/19/2004	VS-SVE-INF-101904-0428	6	2000	50	512	66.9	374.7	8,993.0
11/17/2004	VS-SVE-INF-111704-0433	6	2000	51	512	47.9	403.75	9,690.0
12/21/2004	VS-SVE-INF-122104-0493	6	2000	54	512	9.9	437.7	10,503.8
1/12/2005	VS-SVE-INF-011205-0498	6	2000	50	512	10.9	459.7	11,032.5

### Influent Sample Parameters

#### Vestal, Area 4

SAMPLE DATE	SAMPLE ID	VACUUM PRESURE (inches Hg)	RPM	TEMPERATURE (degrees F)	FLOW (cfm)	PID	OPERATION DAYS	STATION HOUR METER
2/9/2005	VS-SVE-INF-020905-0503	6	2000	52	512	12.3	487.6	11,702.8
3/23/2005	VS-SVE-INF-032305-0551	6	2000	60	512	9.6	529.6	12,710.4
4/27/2005	VS-SVE-INF-042705-0556	6	2000	62	512	2.6	560.50	13,452.1
5/10/2005	VS-SVE-INF-051005-0563	6	2000	65	512	1.5	573.43	13,762.3
5/25/2005	VS-SVE-INF-052505-0568	6	2000	70	512	1.0	588.39	14,121.3
