



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026

Leak Detector			
Equipment #	Grade	Pump Type	Result
001	Regular	Mechanical (MLLD)	● Pass
002	Premium	Mechanical (MLLD)	● Pass
Overfill			
Equipment #	Grade	Overfill Type	Result
002	Premium	Overfill Drop Tube	● Pass
001	Regular	Overfill Drop Tube	● Fail
Precision Line Tightness Test			
Equipment #		Grade	Result
001		Regular	● Pass
002		Premium	● Pass
Shear Valve			
Form Name			Result
Shear Valve			● Pass
UST / AST Monitor			
Form Name			Result
UST / AST Monitor			● Pass

Troy Kocher



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026

Service Items

Item	Qty
Combos	
All Lines and Leak Detectors	2.00
Expenses	
Fuel Surcharge	1.00
Miscellaneous Consumables Misc Consumables	1.00
Report Management & Data Storage Fee	1.00
Test Management and Admin Processing Auto schedule/compliance management /processing fee	1.00
Services	
Monitor System Inspection Automatic Tank Gauging System / Monitor System Inspection	1.00
All Shear Valves	1.00
Overfill Verification	1.00

Notes

Overfill verification: Incomplete

- The technician reported he was unable to inspect the overfill drop tube on the regular unleaded tank. The fill adapter was seized. The technician did not receive authorization to chisel off the adapter to possibly gain access.

MECHANICAL AND ELECTRONIC LINE LEAK DETECTORS PERFORMANCE TESTS

Facility Name: East Ave Auto	Owner: Marones East Avenue ARCO Inc., DBA East Ave Auto				
Address: 1656 East Avenue	Address:				
City, State, Zip Code: Rochester NY 14610	City, State, Zip Code:				
Facility I.D. #: 8-071226	Phone #: 5852717610				
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 7/1/2026			

This data sheet can be used to test mechanical line leak detectors (MLLD) and electronic line leak detectors (ELLD) with submersible turbine pump (STP) systems. See PEI/RP1200 Sections 9.1 and 9.2 for test procedures.

Line Number	001	002				
Product Stored	Regular	Premium				
Leak Detector Manufacturer	Red Jacket	Red Jacket				
Leak Detector Model	FX1V	FX1V				
Type of Leak Detector	☒ MLLD ☐ ELLD	☒ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD

MLLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure	26	27				
Check Valve Holding Pressure	26	27				
Line Resiliency (ml) (line bleed back volume as measured from check valve holding pressure to 0 psig)	109.78	117.35				
Step Through Time in Seconds (time the MLLD hesitates at metering pressure before going to full operating pressure as measured from 0 psig with no leak induced on the line)	3	3				
Metering Pressure (STP pressure when simulated leak rate 3 gph at 10 psig)	14	16				
Opening Time in Seconds (the time the MLLD opens to allow full pressure after simulated leak is stopped)	2	2				
Does the STP pressure remain at or below the metering pressure for at least 60 seconds when the simulated leak is induced?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Does the leak detector reset (trip) when the line pressure is bled off to zero psig?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Does the STP properly cycle on/off under normal fuel system operation conditions?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

A "No" answer to either of the above questions indicates the MLLD fails the test.

ELLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure						
How many test cycles are observed before alarm/shutdown occurs?						
Does the simulated leak cause an alarm?	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
A "No" answer to the above question indicates the ELLD fails the test.						
Does the simulated leak cause an STP shutdown?	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA
Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail

Comments: Testing was conducted in accordance with PEI/RP1200

Tester Signature: *Troy Kocher*

Tester Name: Troy Kocher

UST OVERFILL EQUIPMENT INSPECTION AUTOMATIC SHUTOFF DEVICE

Facility Name: East Ave Auto	Owner: Marones East Avenue ARCO
Address: 1656 East Avenue	Address:
City, State, Zip Code: Rochester NY 14610	City, State, Zip Code:
Facility I.D. #: 8-071226	Phone #:
Testing Company: Owl Services USA	Phone #: 800-646-3161 Date: 7/1/2026

This data sheet is for inspecting automatic shutoff devices. See PEI/RP1200 Section 7 for inspection procedures.

Product Grade	Premium	Regular				
Tank Number	002	001				
Tank Volume, gallons	15000	15000				
Tank Diameter, inches	120	120				
Overfill Prevention Device Brand	OPW	OPW				

AUTOMATIC SHUTOFF DEVICE INSPECTION

1. Drop tube removed from tank? If No, test fails, no need to answer questions 2-5.	☒ Yes ☐ No	☐ Yes ☒ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
2. Drop tube and float mechanisms free of debris?	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
3. Float moves freely without binding and poppet moves into flow path?	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
4. Bypass valve in the drop tube open and free of blockage (if present)?	☒ Yes ☐ No ☐ Not Present	☐ Yes ☐ No ☐ Not Present	☐ Yes ☐ No ☐ Not Present	☐ Yes ☐ No ☐ Not Present	☐ Yes ☐ No ☐ Not Present	☐ Yes ☐ No ☐ Not Present
5. Flapper adjusted to shut off flow at 95% capacity?*	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

A "No" to any item in Lines 2-5 indicates a test failure.

Test Results	☒ Pass ☐ Fail	☐ Pass ☒ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
--------------	--	--	---	---	---	---

Comments:

*Use manufacturer's suggested procedure for determining if automatic shutoff device will shut off flow at 95% capacity.

Tester's Name (print) Troy Kocher Tester's Signature *Troy Kocher*

Testing was conducted in accordance with PEI/RP1200

East Ave Auto
1656 East Avenue
Rochester
NY 14610

Purpora Engineering
Petro-Tite Line Tightness Test Form

Work Visit # 157296

UST Registration #
8-071226

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE		VOLUME			REMARKS																				
			PSI		READING		NET CHANGE	SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS																				
			BEFORE	AFTER	BEFORE	AFTER																						
001	14:00	Connected line tester to: Shear						Material <u>Fiberglass</u> Wall Type <u>Double</u> Line Length (feet) <u>75</u> Diameter (inches) <u>2</u> Pressure/Suction <u>Pressure</u> Allowable Bleedback $(PL \times Ba) + (FC \times Bb(.006)) + B(.05) = N$ $(75 \quad * \quad 0 \quad)$ $+ (3 \quad * 0.006) + 0.05 = 0.068$																				
Regular	14:10	Started line test		60		.072																						
	14:20	Line Test Continued	60	60	.072	.072	0																					
	14:30	Line Test Continued	60	60	.072	.072	0																					
	14:40	Line Test Continued	60	60	.072	.072	0																					
	14:40	Bleed Back	60	0	.072	.1	0.028																					
Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows: <table border="1" style="width:100%; border-collapse: collapse;"> <thead> <tr> <th>Line Identification</th> <th>Meets Criteria (Yes/No)</th> <th>Net Volume Change Per Hour</th> <th>Date Tested</th> </tr> </thead> <tbody> <tr> <td>001 Regular</td> <td>Yes</td> <td>0</td> <td>7/1/2026</td> </tr> <tr><td> </td><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td><td> </td></tr> </tbody> </table>								Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested	001 Regular	Yes	0	7/1/2026													CONTRACTOR CERTIFICATION Technician: <u>Troy Kocher</u> 642f19b7 Certification # _____
Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested																									
001 Regular	Yes	0	7/1/2026																									

Notes:

Purpora Engineering
Petro-Tite Line Tightness Test Form

Work Visit # 157296

UST Registration #
8-071226

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE		VOLUME			REMARKS
			PSI		READING		NET CHANGE	SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS
			BEFORE	AFTER	BEFORE	AFTER		
002	14:00	Connected line tester to: Shear						Material <u>Fiberglass</u> Wall Type <u>Double</u> Line Length (feet) <u>75</u> Diameter (inches) <u>2</u> Pressure/Suction <u>Pressure</u> Allowable Bleedback (PL x Ba) + (FC x Bb(.006)) + B(.05) = N (75 * 0) + (3 * 0.006) + 0.05 = 0.068
Premium	14:10	Started line test		60		.068		
	14:20	Line Test Continued	60	60	.068	.068	0	
	14:30	Line Test Continued	60	60	.068	.068	0	
	14:40	Line Test Continued	60	60	.068	.068	0	
	14:41	Bleed Back	60	0	.068	.1	0.032	
Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows:								
Line Identification		Meets Criteria (Yes/No)	Net Volume Change Per Hour		Date Tested			
002	Premium	Yes	0		7/1/2026			
CONTRACTOR CERTIFICATION								
Technician:								
Troy Kocher								
642f19b7								
Certification #								

Notes:

SHEAR VALVE OPERATION INSPECTION

Facility Name: East Ave Auto	Owner: Marones East Avenue ARCO Inc., DBA
Address: 1656 East Avenue	Address
City, State, Zip Code: Rochester NY 14610	City, State, Zip Code:
Facility I.D. #: 8-071226	Phone #: 5852717610
Testing Company: Owl Services USA	Phone #: 610-278-7203

This data sheet is for inspecting shear valves located inside dispensers. See PEI/RP1200 Section 10 for the inspection procedure.

Product Grade	Regular	Premium	Regular	Premium	Regular	Premium			
Dispenser ID#	1/2	1/2	3/4	3/4	5/6	5/6			
Shear Valve Type (Product/Vapor)	Product	Product	Product	Product	Product	Product			
1. Is the shear valve rigidly anchored to the dispenser box frame or dispenser island?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
2. Is the shear section positioned between 1/2 inch above or below the top surface of the dispenser island?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
3. Is the lever arm free to move?	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA
4. Does the lever arm snap shut the poppet valve?	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☒ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA
5. Can any product be dispensed when the product shear valve is closed?	☐ Yes ☒ No ☐ NA	☐ Yes ☒ No ☐ NA	☐ Yes ☒ No ☐ NA	☐ Yes ☒ No ☐ NA	☐ Yes ☒ No ☐ NA	☐ Yes ☒ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA

A "No" to Lines 1-4 or a "Yes" for Line 5 indicates a test failure.

Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
--------------	---	---	---	---	---	---	--	--	--

Comments:

Tester's Name (print) Troy Kocher Tester's Signature *Troy Kocher* 7/1/2026

Testing was conducted in accordance with PEI/RP1200

AUTOMATIC TANK GAUGE OPERATION INSPECTION

Facility Name: East Ave Auto	Owner: Marones East Avenue ARCO Inc., DBA East	
Address: 1656 East Avenue	Address:	
City, State, Zip Code: Rochester NY 14610	City, State, Zip Code:	
Facility I.D. #: 8-071226	Phone #: 5852717610	
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 7/1/2026

This procedure is to determine whether the automatic tank gauge (ATG) is operating properly. See PEI/RP1200 Section 8.2 for the inspection procedure. This procedure is applicable to tank level monitor probes that touch the bottom of the tank when in place.

Tank Number	001	002		
Product Stored	Regular	Premium		
ATG Brand and Model	Veeder Root TLS-350	Veeder Root TLS-350		
1. Tank Volume, gallons	15000	15000		
2. Tank Diameter, inches	120	120		
3. The ATG probe was removed from the tank and inspected for damage and residual buildup.	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
4. Float moves freely on the stem without binding?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
5. Fuel float level agrees with the value programmed into the console?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
6. Water float level agrees with the value programmed into the console?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
7. Inch level from bottom of probe when 90% alarm is triggered.	106	106		
8. Inch level at which the overfill alarm activates corresponds with value programmed in the gauge?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
9. Inch level from the bottom when the water float first triggers an alarm.	2	2		
10. Inch level at which the water float alarm activates corresponds with value programmed in the gauge?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

If any answers in Lines 3, 4, 5, or 6 are "No," the system has failed the test.

If internal ATG battery backup is present, was it functional per manufacturer's specifications. ☒ Yes ☐ No ☐ None

Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
---------------------	--	--	---	---

Comments:

Tester's Name (print) Troy Kocher

Tester's Signature



LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: East Ave Auto		Owner: Marones East Avenue ARCO Inc., DBA East Ave	
Address: 1656 East Avenue		Address:	
City, State, Zip Code: Rochester NY 14610		City, State, Zip Code:	
Facility I.D. #: 8-071226		Phone #: 5852717610	
Testing Company: Owl Services USA		Phone #: 800-646-3161	Date: 7/1/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	001 STP Sump	002 STP Sump					
Product Stored	Regular	Premium					
Type of Sensor	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating
Test Liquid	☒ Water ☐ Product	☒ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Is the sensor alarm circuit operational?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Has sensor been inspected and in good operating condition?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When placed in the test liquid, does the sensor trigger an alarm?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When an alarm is triggered, is the sensor properly identified on the ATG console?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

Any "No" answers indicates a test failure.

Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
---------------------	--	--	---	---	---	---	---

Comments:

Tester's Name (print) Troy Kocher Tester's Signature *Troy Kocher*

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: East Ave Auto	Owner: Marones East Avenue ARCO Inc., DBA East Ave	
Address: 1656 East Avenue	Address:	
City, State, Zip Code: Rochester NY 14610	City, State, Zip Code:	
Facility I.D. #: 8-071226	Phone #: 5852717610	
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 7/1/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	001 Tank Interstitial	002 Tank Interstitial					
Product Stored	Regular	Premium					
Type of Sensor	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating
Test Liquid	☒ Water ☐ Product	☒ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Is the sensor alarm circuit operational?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Has sensor been inspected and in good operating condition?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When placed in the test liquid, does the sensor trigger an alarm?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When an alarm is triggered, is the sensor properly identified on the ATG console?	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

Any "No" answers indicates a test failure.

Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
---------------------	--	--	---	---	---	---	---

Comments:

Tester's Name (print) Troy Kocher Tester's Signature *Troy Kocher*

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: East Ave Auto		Owner: Marones East Avenue ARCO Inc., DBA East Ave	
Address: 1656 East Avenue		Address:	
City, State, Zip Code: Rochester NY 14610		City, State, Zip Code:	
Facility I.D. #: 8-071226		Phone #: 5852717610	
Testing Company: Owl Services USA		Phone #: 800-646-3161	Date: 7/1/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	Dispenser 1/2	Dispenser 3/4	Dispenser 5/6				
Product Stored	Regular, Premium	Regular, Premium	Regular, Premium				
Type of Sensor	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☒ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating	☐ Discriminating ☐ Non-discriminating
Test Liquid	☒ Water ☐ Product	☒ Water ☐ Product	☒ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product	☐ Water ☐ Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Is the sensor alarm circuit operational?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Has sensor been inspected and in good operating condition?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When placed in the test liquid, does the sensor trigger an alarm?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
When an alarm is triggered, is the sensor properly identified on the ATG console?	☒ Yes ☐ No	☒ Yes ☐ No	☒ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No

Any "No" answers indicates a test failure.

Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail
---------------------	--	--	--	---	---	---	---

Comments:

Tester's Name (print) Troy Kocher Tester's Signature *Troy Kocher*



Images



IMG_6409.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026



IMG_6410.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026



IMG_6411.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026



IMG_6412.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026




IMG_6413.jpeg



IMG_6414.jpeg



IMG_6415.jpeg

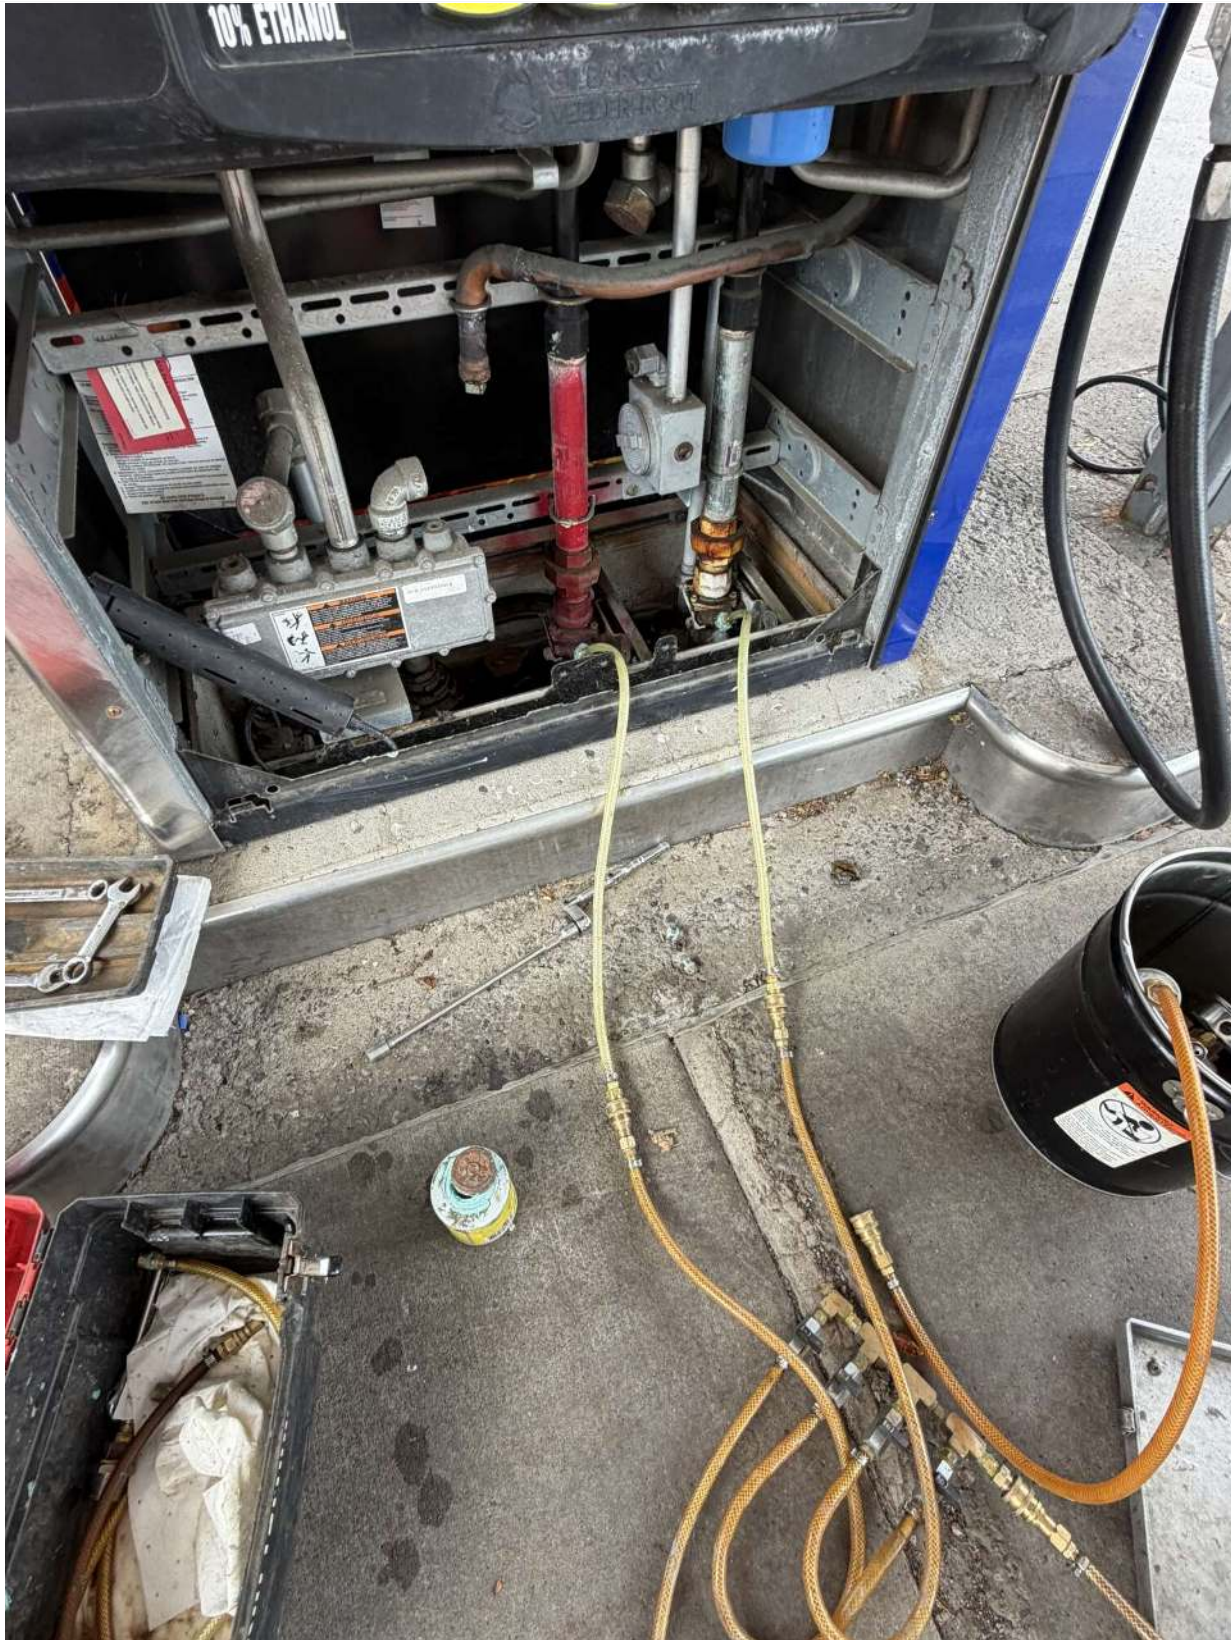

IMG_6416.jpeg



IMG_6417.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026



IMG_6418.jpeg



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610



W-155039 Visit #157296 7/01/2026



IMG_6419.jpeg



Diagram - Site Diagram (v2)

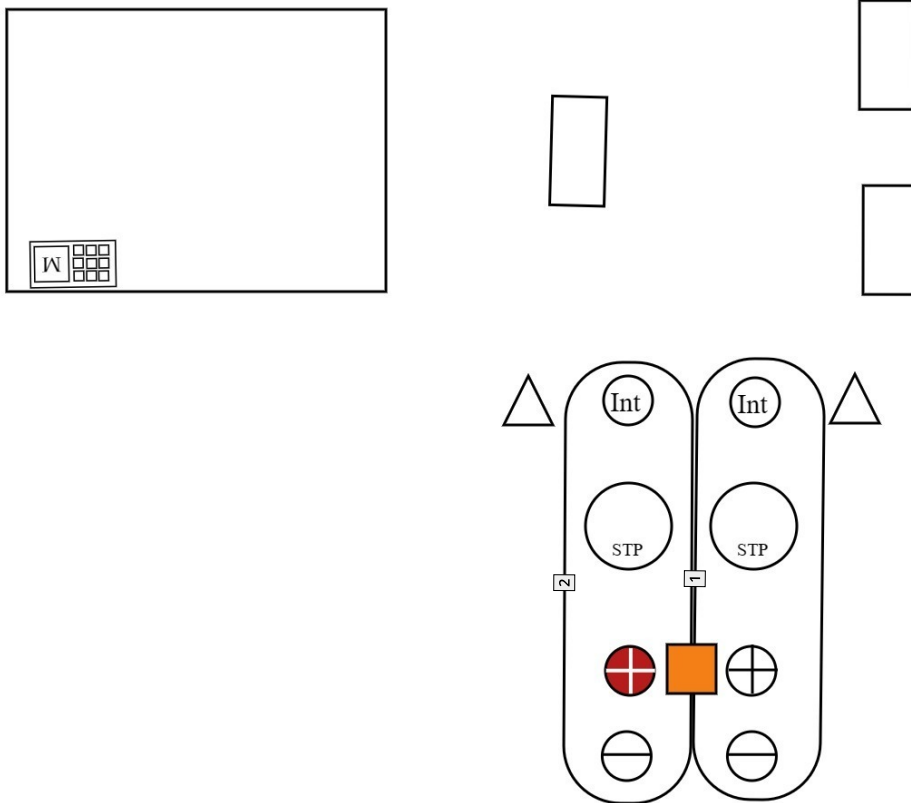

1: Fiberglass Tank - 001 Reg 15K

2: Fiberglass Tank - 002 Prem 15K



Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

Marones East Avenue ARCO Inc., DBA East Ave Auto
Location #8-071226

1656 East Avenue
Rochester, NY 14610
+1 585-271-7610

W-155039 Visit #157296 7/01/2026

Visit Verification

CUSTOMER
Marones East Avenue ARCO Inc., DBA East Ave Auto

LOCATION
#8-071226
1656 East Avenue
Rochester, NY 14610

CONTACT
Marones East Avenue ARCO Inc., DBA East Ave Auto

SCHEDULED
07/01/2026 12:00am (EDT)

ASSIGNED TO
Troy Kocher

SERVICE REASON
Compliance

PRODUCTS & SERVICES

Item	Qty
Combos	
All Lines and Leak Detectors	2.00
Expenses	
Fuel Surcharge	1.00
Miscellaneous Consumables Misc Consumables	1.00
Report Management & Data Storage Fee	1.00
Test Management and Admin Processing Auto schedule/compliance management /processing fee	1.00
Services	
Monitor System Inspection Automatic Tank Gauging System / Monitor System Inspection	1.00
All Shear Valves	1.00
Overfill Verification	1.00

CONFIRMATION
By signing this verification you are agreeing that we have performed and/or provided services and parts listed above.

Approver's Name
Unknown

Email

Signature Status
Nobody available to sign
