

August 19, 2025

Ms. Kathryn Lovell
New York State Department of Environmental Conservation
Division of Environmental Remediation, Region 8
6272 East Avon-Lima Road
Avon, New York 14414

Re: Monthly Monitoring Report – July 2025 1000 Turk Hill Road, Fairport, New York NYSDEC Site ID No. 828161

Dear Ms. Lovell:

On behalf of New Coleman Holdings, Inc., Roux Environmental Engineering and Geology, D.P.C. (Roux) has prepared this Monthly Monitoring Report (MMR) to summarize the ongoing monitoring and remediation activities, including operation and maintenance of the sub-slab depressurization systems (SSDSs), at 1000 Turk Hill Road, Fairport, New York. Roux has engaged a local subcontractor (Trec Environmental Inc. [Trec]) to perform the monthly monitoring of the SSDSs.

The MMR for June 2025 was submitted to the New York State Department of Environmental Conservation (NYSDEC) and the New York State Department of Health (NYSDOH) on July 25, 2025.

SSDS Monitoring

The monthly SSDS monitoring event was performed by Trec on July 30, 2025. Nine of the 12 SSDS vacuum monitoring points were inspected, measured, and confirmed to be operating within the pre-established parameters. During the visit, the monitoring points associated with Systems C1 and C2 in Building 1 (located in the vacant spaces formerly occupied by Nat's Nuts) and System C in Building 3 (located in the vacant tenant space formerly occupied by Spartacus Construction) could not be accessed. The vacuum measurements from all accessible monitoring points were consistent with previous monitoring events and within the required performance ranges for those systems.

The exterior components of each of the five SSDSs on Building 1 and Building 3 were also inspected. As previously noted, the mounting brackets for System A in Building 3 are broken, but the vent pipe remains fastened and will continue to be inspected monthly to ensure operation is not impacted. Vegetation growth on the north side of Building 1 is being monitored monthly to confirm that damage to the discharge piping does not occur.

The vacuum measurements and other pertinent information documented during the inspection are provided on the attached Monthly SSDS Monitoring and Inspection Checklist – July 2025 (Table 1). The locations and designations of the various SSDS systems and monitoring points are shown on the attached SSDS As-Built Drawings prepared by Envirosafe Inspections & Consulting (Attachment 1).

The next SSDS monitoring event is planned to occur during the week of August 25, 2025, and will be documented in a future Monthly Monitoring Report.

Remedial Injection Program

The 2nd Phase of the remedial injection program was performed July 1 through July 14, 2025, followed by a groundwater performance monitoring event that occurred during July 30 through August 1, 2025. A Groundwater Monitoring Report is being prepared to summarize the most recent sampling event and will be submitted to you once it is complete.

If you have any questions or require additional information, please do not hesitate to contact me at (917) 825-1108 or via email at masmith@rouxinc.com.

Sincerely,

ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

Matthew\Smith Senior Scientist I

ROUX ASSOCIATES, INC.

Christopher Battista **Principal Scientist**

Chin Batter

Attachments

cc: Anthony Perretta, NYSDOH Charlotte Theobald, NYSDEC Charles J. Sgro, New Coleman Holdings, Inc. Allie LeBlanc, New Coleman Holdings, Inc. Steve Russo, Esq., Greenberg Traurig, LLP Omar Ramotar, P.E., Roux Associates, Inc.

Table 1. Monthly SSDS Monitoring and Inspection Checklist - July 2025

Turk Hill Park, 1000 Turk Hill Road, Fairport, New York - NYSDEC Site No. 828161

7/30/2025

7/30/2025

10:30 AM

10:00 AM

2.8

2.8

2.6

2.5

Building 1

Building 3

Building 1	Tenant / Location	Date	Time	Baseline Manometer Reading (In. W.C.) 1/29/18	Current Manometer Reading (In. W.C.)	Evidence of Water/ Condensation Accumulation	Is The Fan Operating as Expected?	Is Any of The Piping Damaged or Disconnected?	Comments
System A	Canal Metalsmith	7/30/2025	12:05 PM	2.4	2.2	N	Y	N	
System B1	Wonder Repair & Floor Coverings	7/30/2025	11:55 AM	1.0	1.2 & 1.0	N	Υ	N	Fairport Computer is now Floor Coverings.
System B2	Vacant (Formerly Wonder Repair)	7/30/2025	11:40 AM	1.0	1.0	N	Υ	N	
System C1	Vacant (Formerly Nat's Nuts)	7/30/2025	11:35 AM	0.9	N/A	N	Υ	N	No access to the vacant tenant space.
System C2	Vacant (Formerly Nat's Nuts)	7/30/2025	11:35 AM	1.0	N/A	N	Υ	N	No access to the vacant tenant space.
System D	Amazing Grains Bread Company	7/30/2025	11:20 AM	2.8	2.4	N	Υ	N	
System E	Amazing Grains Bread Company	7/30/2025	11:15 AM	1.9	1.8	N	Υ	N	

Building 3	Tenant / Location	Date	Time	Baseline Manometer Reading (In. W.C.) 1/29/18	Current Manometer Reading (In. W.C.)	Evidence of Water / Condensation Accumulation	Is The Fan Operating as Expected?	Is Any of The Piping Damaged or Disconnected?	Comments
	Men's Bathroom	7/30/2025	11:00 AM	2.5	2.5	N	Y	N	
System B	Loading Dock	7/30/2025	10:45 AM	1.9	2.0	N	Y	N	
System C	Former Spartacus (tenant space)	7/30/2025	10:20 AM	2.2	N/A	N	Υ	N	Tenant does not maintain consistent hours. No access during O&M visit.

Υ

Υ

Ν

Ν

Ν

N

Notes:

System D

System E

N/A - Not Available


NM - Not Measured

In W.C. - inches of water column

Millwork Shop

CrossFit Fairport



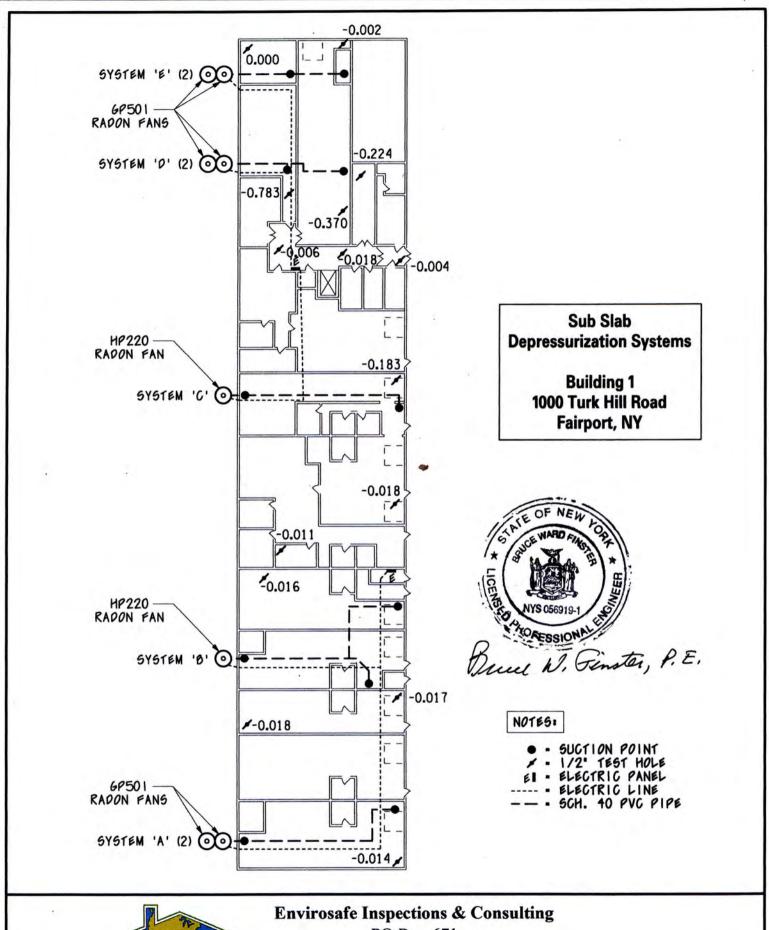




PO Box 671 Honeoye, NY 14471 585-704-4385

www.envirosafeinspections.com

Figure 1

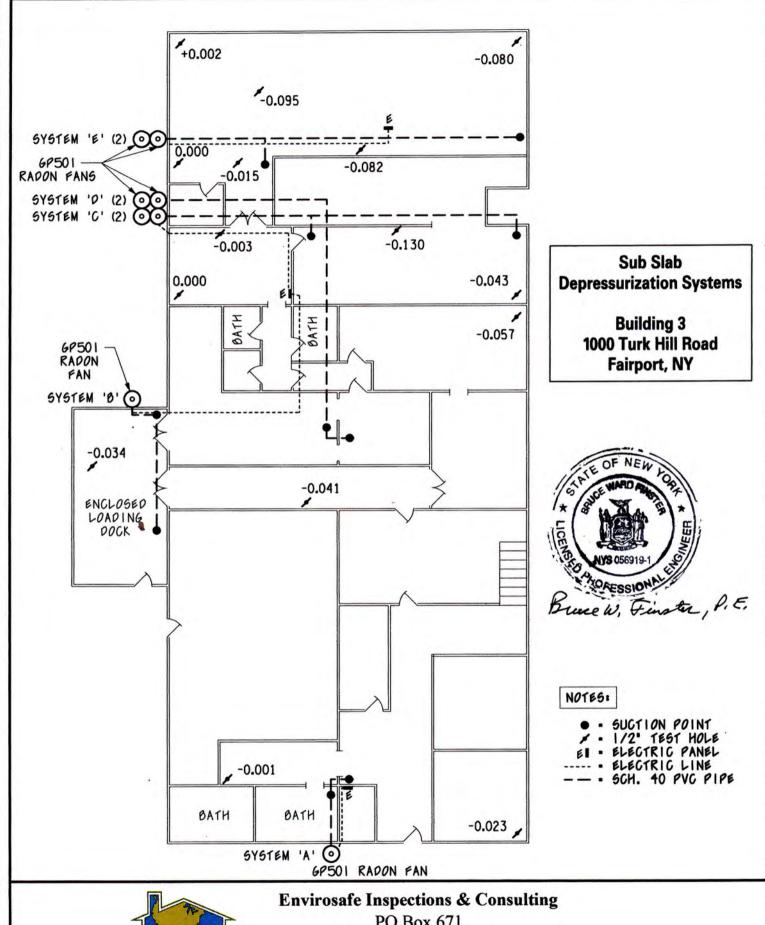



PO Box 671 Honeoye, NY 14471 585-704-4385

www.envirosafeinspections.com

Figure 2
