

## Daily Status Report

Prepared by: C. Zaccheo

Date: 07/12/2022

Weather: 85 deg F., Sunny

**Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053**

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ECC NY

### Work Activities Performed:

- 1) ECD continuing sheet pile installation for the bulkhead;
- 2) ECD continuing to install piles along Kent Avenue;
- 3) ECD continued installing sheet piles, and;
- 4) Disposal of 29 truck loads (approximately 580 CY) of C&D to the Coplay Quarry in Whitehall, PA.


**Samples Collected (Since Last Report):** None.

**Air Monitoring (Since Last Report):** CAMP graphs and tables are included below.

**Problems Encountered:** None.

**Planned Work Activities for Next Day/Week:** Continue pile installation, C&D and soil disposal & bulkhead demolition and installation.

Site Layout Map

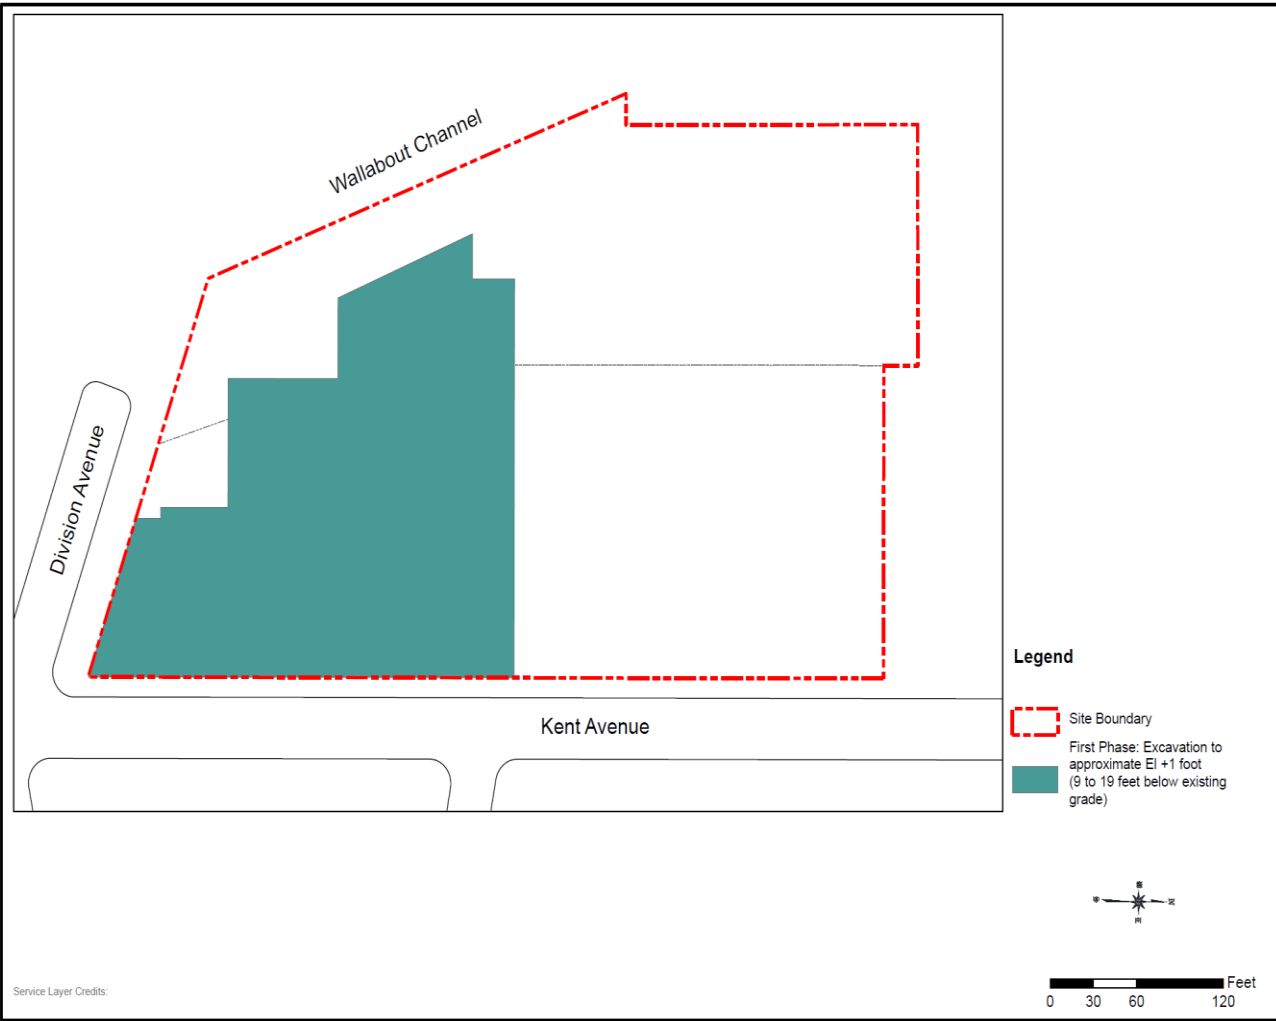

**Photo 1:**

Loading a truck with  
C&D for disposal offsite.



**Photo 2:**


View of stockpiled  
concrete for disposal.



**CAMP:  
Downwind  
Particulates**

**Dust Levels**


0.04 mg/m<sup>3</sup> 0.029 mg/m<sup>3</sup>

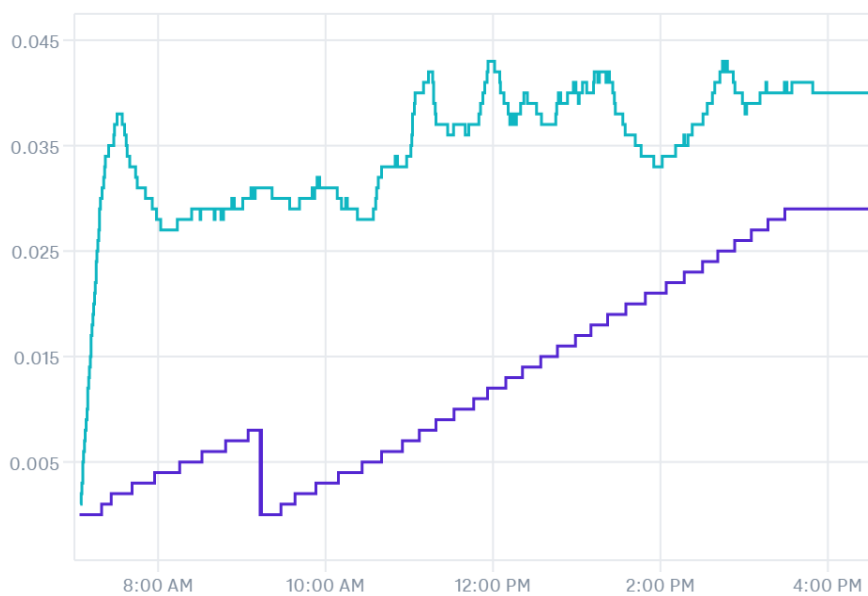

**CAMP:  
Downwind VOCs**

**VOC Levels**

0 ppm 0 ppm

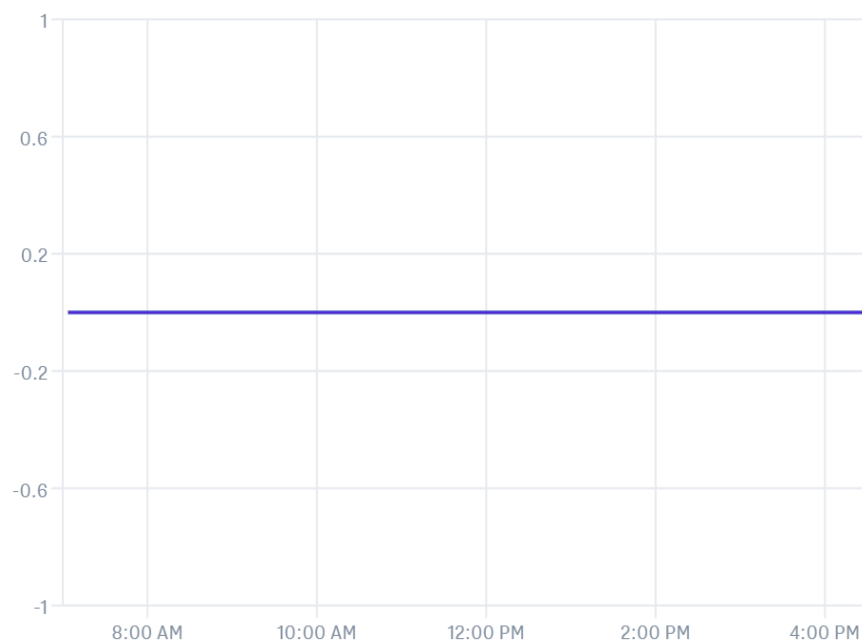

**CAMP:**  
**Upwind Particulates**

**Dust Levels**

0.043 mg/m<sup>3</sup>    0.029 mg/m<sup>3</sup>

