

DAILY ACTIVITY REPORT
FYN Paint & Lacquer Co.
Site No. C224154
Sheet 1 of 4

Project/Site Name: FYN Paint & Lacquer Co.
Location: 230 Kent Ave Brooklyn,
NY
Date: July 14, 2026
Weather:
Temperature: Low: 73F High: 96F
Precipitation: 0.0"
Site Owner: Kent Riverview LLC
Cloud Cover: Partial/Haze
Wind: SW -> NN

Personnel on Site:		
Name	Representing	Time: On Site / Off Site
Aidan Kidd	WSP	0715/1300
Tom Musser	ISOTEC	0730/1500
Michael Rodriguez	ISOTEC	0730/1500

Summary of Today's Activities
0730 Start of Work. Daily safety meeting, receive sodium per-sulfate delivery (5 pallets). Mixing of sodium persulfate and water within respective totes, concentration of treatment chemicals raised to 20%, prior injections have been at 15%. A total of 1,200 gallons of chemical treatment was injected across 10 injection wells at a rate of 0.5-1.5 gpm. Treatment was injected into four wells at a time, today's treated wells include: IW-2, 8, 14, 15/ IW-5, 6, 9, 16/ IW-3, and IW-13. End of Work 1515

Work Delays (Due to Weather, Maintenance, Breakdowns, Waiting for Decisions)
• None

Summary of Problems, Work Plan Deviation, and Resolutions:
Continued injections of 120 gallons of treatment into the 10 injection wells which have not surfaced, no surfacing has occurred in today's injections.

Written and Verbal Instruction by NYSDEC (Include name of NYSDEC representative)
None.

New Safety Issues
None.

DAILY ACTIVITY REPORT

FYN Paint & Lacquer Co.

Site No. C224154

Sheet 2 of 4

Summary of Activities		
Equipment Used	Task	Activities Performed
Water Totes, Hoses, Pipe Manifold, air compressor, and Pumps	Remedial chemical injections into injection wells.	Perform injections on 10 injection wells.
Bobcat Forklift	Movement of chemicals.	Unload and store Per-sulfate delivery.

Field Tests Performed (Samples, Field Screening, Chemical Testing, etc.)
ISCO injections
Investigation-Derived Waste Generated
None
Planned Activities for Next Workday
Continued injection of chemical treatment.
Remarks: (Visitors, Completion of Fieldwork, etc.)
Above builders site visit

DAILY ACTIVITY REPORT
FYN Paint & Lacquer Co.
Site No. C224154
Sheet 3 of 4

Site Photographs July 14, 2026



Photo 1 – Per-sulfate delivery, 5 pallets

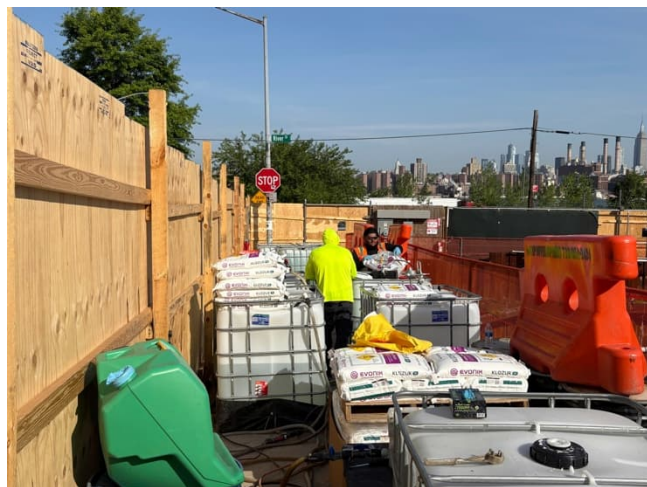


Photo 2 – Mixing of chemical treatment.



Photo 3 – Injections at IW-14.

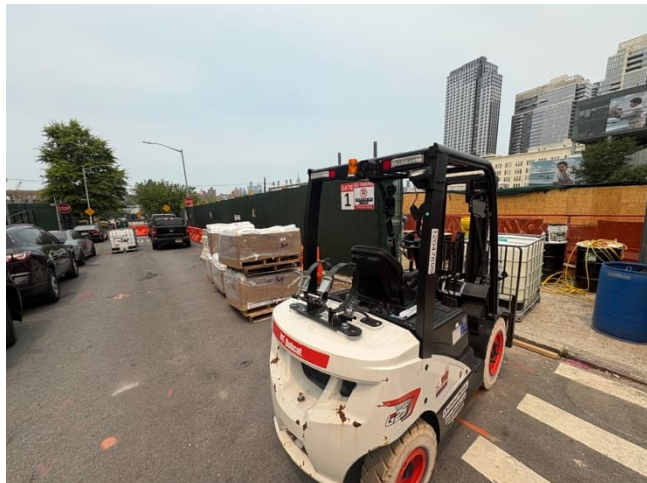


Photo 4 – Reorganization of materials stored onsite/
movement of sodium per-sulfate for onsite storage.

Site Inspector: AK

Date: 7/14/26

DAILY ACTIVITY REPORT
FYN Paint & Lacquer Co.
Site No. C224154
Sheet 4 of 4



July 15, 2026

Project Manager Signature

Date
