



DAILY STATUS REPORT

Prepared By:

Thomas Jensen

| | | | | | | | | | | | |
|---------|------|--|-------|---|----------|--|---------------|--|------------|--|-------------|
| WEATHER | Snow | | Rain | X | Overcast | | Partly Cloudy | | Bright Sun | | Wind |
| TEMP. | < 32 | | 32-50 | X | 50-70 | | 70-85 | | >85 | | NE – 10 mph |

| | | | | | |
|------------------------|--------------------------------|----------------------------|---------|--------------|---------|
| IEC Project No: | 14729 | NYSDEC BCP Site No: | C224329 | Date: | 1/23/23 |
| Project: | 585 Union Street, Brooklyn, NY | | | | |

| | |
|---|---|
| <p>Consultant: Impact Environmental Engineering and Geology, PLLC (IEEG)</p> <p>Time On: 06:30 Time Out: 13:30</p> | <p>Personnel On Site: IEEG (Environmental) –Chris Evertz Broadway Construction Group, Shannon Dowling Raptor – Foundation Contractor ABC Repair and Lining Inc. – UST and Hydraulic lift Cleanout and Removal Contractor ECD, NY– Dill drilling contractors</p> <p>Equipment On Site: Cat325C, Cat 311C, MC15 Pile Rig, MC22 Pile Rig, Minirae 3000 PID, DustTrak II, Bauer BG 36 H</p> |
|---|---|

Scope of Work:

- Community Air Monitoring Program (CAMP) implementation in accordance with the NYSDEC-approved Remedial Action Work Plan (RAWP);
- Oversight of excavation/foundation removal;
- Oversight of excavation/loading of fill materials; and
- Oversight of hot spot excavations

Site Activities:

- ECD installing structural pile in WC-5;
- Installation of lagging along Union Street;
- Removed trucking pad from WC-4/WC-5, and created a new trucking pad in WC-3;
- Took samples from hotspot stockpile-5 (6’-9’) for facility disposal purposes;
- Six (6) concrete trucks throughout the day came on Site to grout structural piles; and
- Three (3) truckloads of material were loaded out for off-Site disposal at CENJ: two (2) trucks from hotspot stockpile-3 from the 3-6’ interval and one (1) truck load of material was live loaded in WC-1 from the 6-9’ interval.

Community Air Monitoring Program (CAMP)

CAMP was run due to heavy rain throughout the day.

Notable Site Conditions:

- See Site Activities.

Planned Activities for the Next Day:

- Continuation of installation of structural piles;
- Continuation of lagging across the site;
- Loadout of material from the 6-9' interval for offsite disposal to Bayshore of Keasbey, NJ on Wednesday;
- Collect sample from stockpile proximal SB-19 (6'-9') requested by disposal facility for off-Site disposal purposes.

PHOTO LOG

585 Union Street, Brooklyn,
NY



Photo 1 –
Representative
photo of
installation of
structural
piles.



Photo 2 –
Representative
photo of
stockpiled
material from
the 6-9'
interval
proximal to
SB-19.
Material
placed on top
of poly, where
it will remain
until sample
collection and
analytical
results for off-
site disposal.



Photo 3 –
Representative
photo of
lagging along
Union Street.




Photo 4–
Representative
view of truck
being sprayed
down on track
pad prior to
exiting the
Site.



SITE PLAN

585 Union Street, Brooklyn,
NY



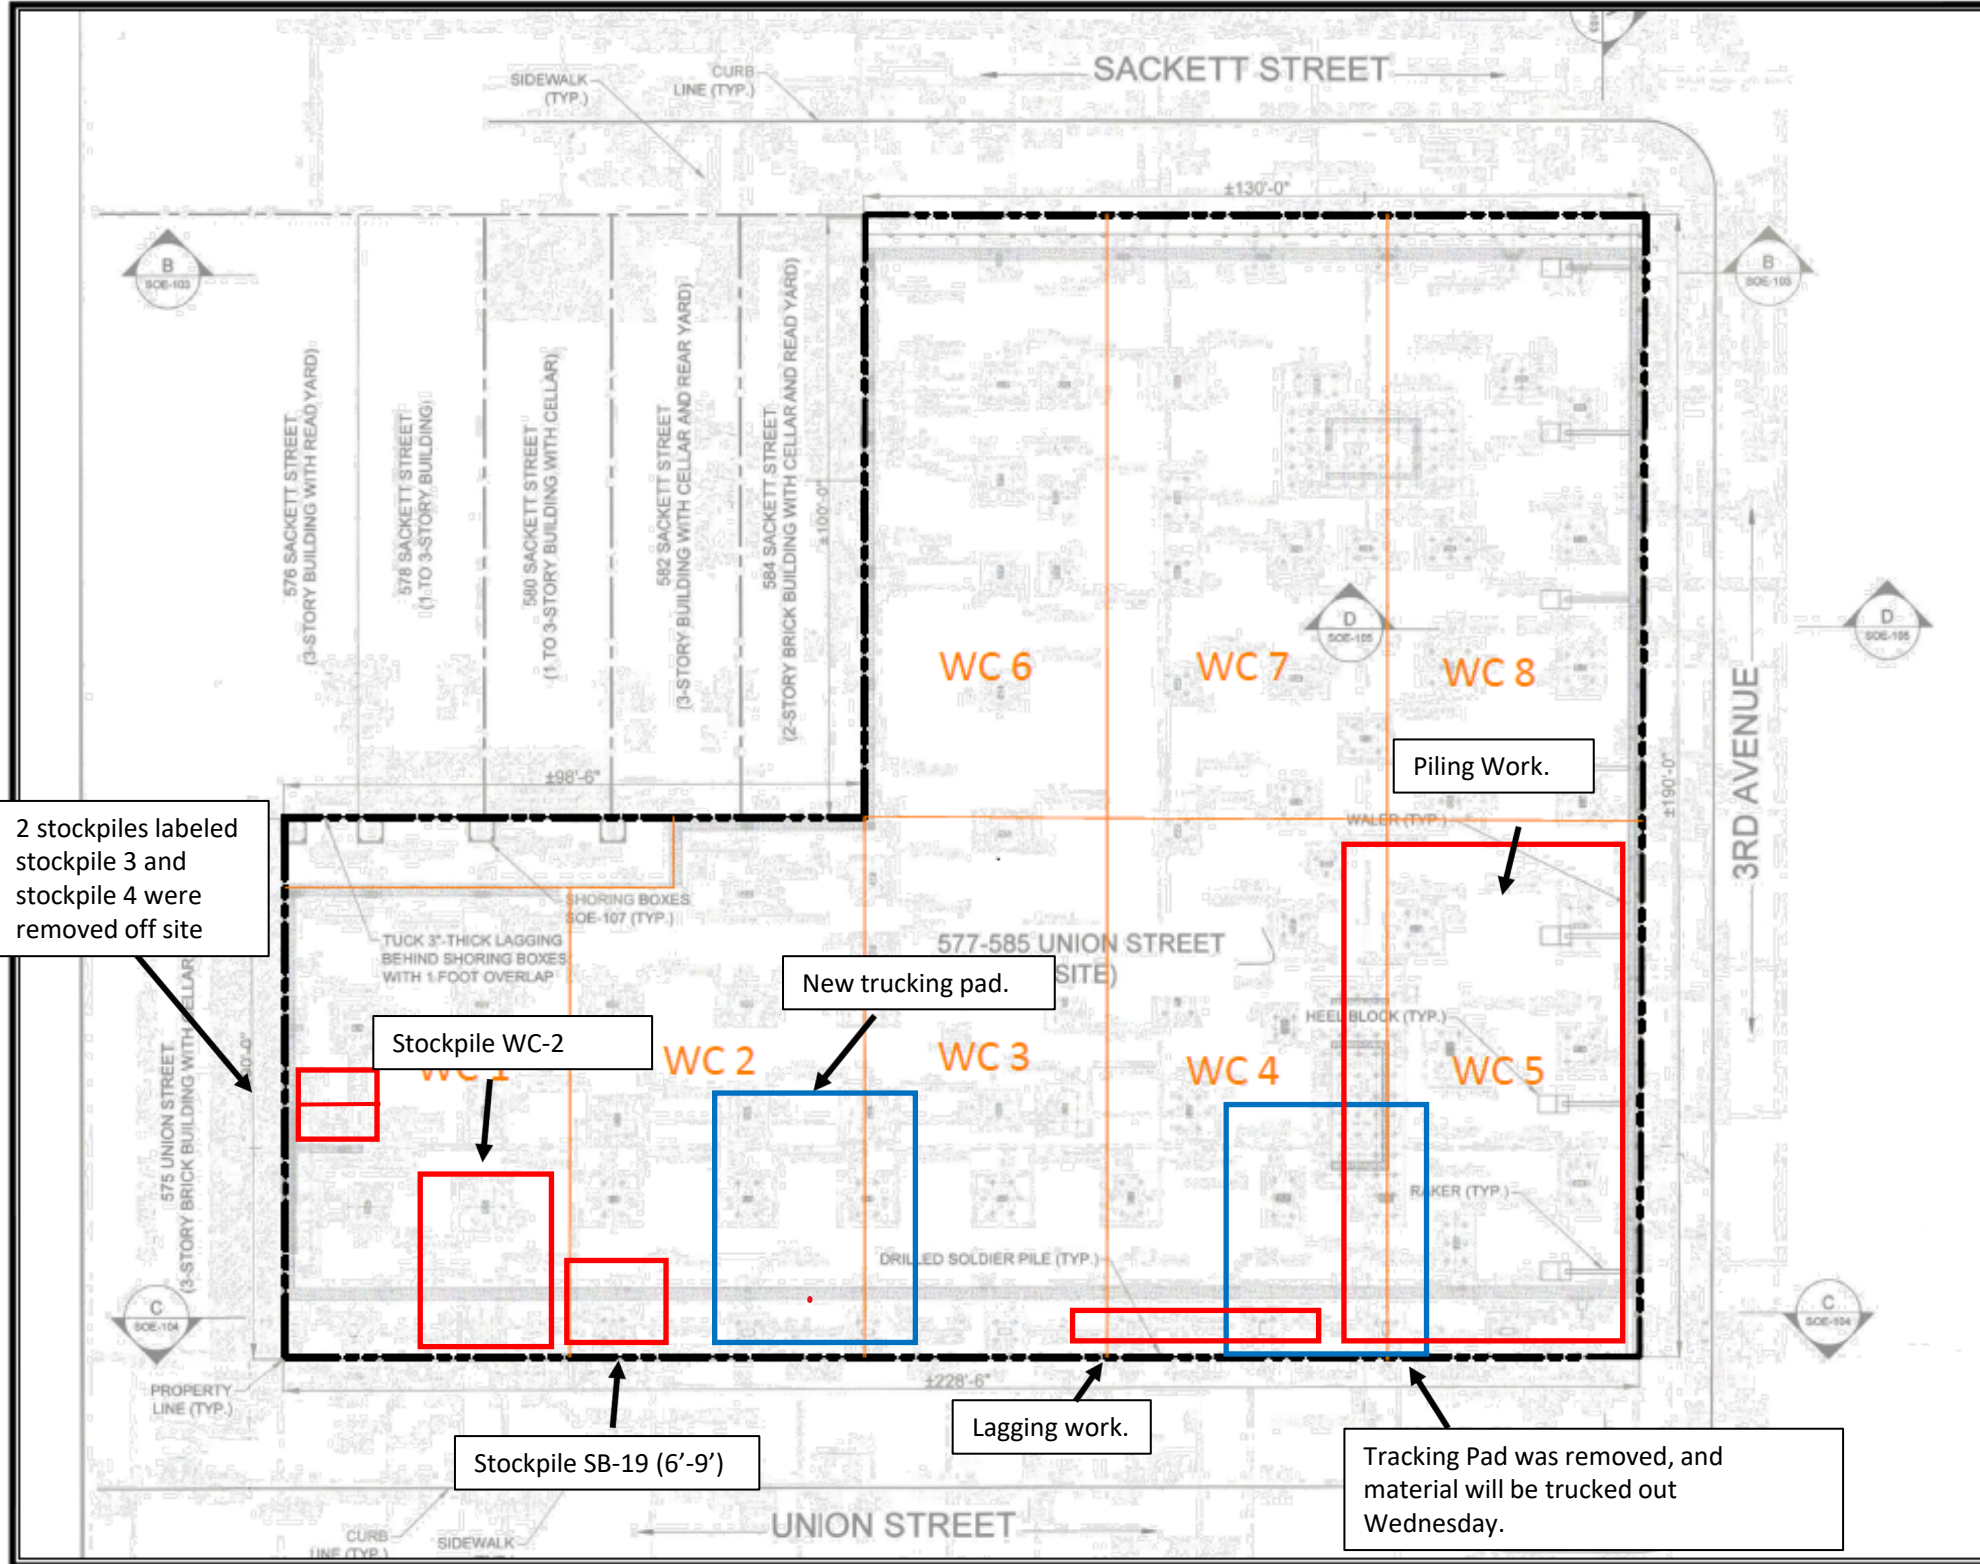

2 stockpiles labeled stockpile 3 and stockpile 4 were removed off site

Stockpile WC-2


New trucking pad.

Lagging work.

Piling Work.

Tracking Pad was removed, and material will be trucked out Wednesday.

NOTES:
 1. BASE MAP TAKEN FROM "SUPPORT OF EXCAVATION PLAN" (DRAWING NO. SOE-102.01) PREPARED BY GEOTECHNICAL ENGINEERING SERVICES, P.C., DATED 12/21/2021.



LEGEND

SITE PLAN

606 UNION STREET
 BROOKLYN, NY
 BLOCK 433, LOT 20

| | |
|-------------|-----------|
| SHEET NO. | 14729 |
| PROJECT NO. | 14729 |
| DESIGNED BY | ME |
| DRAWN BY | ME |
| CHECKED BY | ME |
| DATE | 1/10/2023 |
| SCALE | 1" = 30' |
| REVISIONS | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |



IMPACT ENVIRONMENTAL
 170 KAYLAND COURT
 BOHemia, New York, 11716
 TEL: (516) 265-8800 FAX: (516) 265-1566
 1000 PRIDE AVENUE
 LINDHURST, New Jersey 07037
