

DAILY STATUS REPORT

Prepared By: Daniel Horvath

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70	X	70-85		>85	

Langan Project No:	100688803	Project:	12074 Flatlands Avenue p/o Lot 1	Date:	05/01/2025
NYSDEC BCP Site No:	C224353	NYCOER Site No.:	Lot 1: 23TMP1319K / 23EHAN210K Lot 100: 25TMP1084K, 25EHAN206K	Time:	06:15 – 17:15

Consultant:

Langan Engineering, Environmental, Surveying, Landscape Architecture and Geology, D.P.C.

PERSONNEL ON SITE:

Langan: Daniel Horvath (Environmental), Lakshman Dontha (Geotechnical)

Monadnock: Seamus Lavin (Superintendent)

United Concrete: Claudio Cappiello, Miguel Flores and laborers

RYC Turbos: Ronan Cooke & crew

EQUIPMENT ON SITE: Komatsu PC490 LC Excavator (2), Komatsu PC360 LC Excavator, Komatsu PC138US LC Excavator, Komatsu PC78US Excavator, Bobcat 740 Skid Steer, JLG 800AJ Boom Lift, ABI Mobilram TM18/22 HD Drill Rig (2), Caterpillar 335F L CR Excavator (2), STS Scheltzke MPS 510-D-C-AUT Mix-Pump-Unit, Delmag RH34 Drill Rig

Site Activities

BCP Site Activities

- Langan provided oversight during implementation of the 1 May 2024 RAWP.
- United Concrete (United) removed 8 truckloads of non-hazardous material from stockpile ST-25, originally excavated from disposal grids WC38B, WC40AB, WC41AB, WC41C, and WC61B in the southern portion of the Site, for off-Site disposal to Clean Earth Carteret, for off-Site disposal to Clean Earth Carteret.
- United removed 10 truckloads of hazardous material from stockpile ST-29, originally excavated from disposal grids WC30F, WC31F, and WC32F in the northern portion of the Site, for off-Site disposal to Clean Earth of North Jersey.
- Stockpile ST-32, consisting of non-hazardous material excavated from disposal grid WW33F in the northern portion of the Site, was relocated to and staged on polyethylene sheeting in the central portion of the Site.
- United excavated an approximately 80-foot-long area ranging between 12- and 30-feet-wide from 6 and up to 11 feet bgs in disposal grid WC33F. Some staining and odors were observed, however no elevated PID readings were recorded during excavation. All excavated material was added to stockpile ST-32 in the central portion of the Site. Stockpile ST-32 was covered with polyethylene sheeting at the end of the day.
- RYC Turbos continued installing the soil mix wall along the western boundary of the Site for the construction of the Support of Excavation (SOE).
- RYC Turbos installed and poured concrete within the SOE guide wall formwork along the southwestern boundary of the Site for the construction of the SOE.

Lot 100 Site Activities

- None.

Samples Collected

- None.

Community Air Monitoring Program (CAMP)

- Langan implemented the community air monitoring program (CAMP) during soil disturbance. CAMP equipment consisted of an Aeroqual AQS 1 Air Quality Monitor at dedicated locations on the downwind and upwind perimeter of the site, as well as a personal DataRam (pDR) and PID at a work zone monitoring station.
 - No VOC or dust concentrations were detected in exceedance of the short-term exposure limit (STEL) at the downwind CAMP station.

Problems Encountered

- None.

Activities Scheduled for Next Day

- United will export material from the Site.
- Langan will collect waste characterization soil samples for disposal facility approval purposes in the southwestern portion of the Site.
- RYC Turbos will continue installing the soil mix wall along the western boundary of the Site for the SOE.

Two Week Outlook

- United will excavate and export material from the Site.
- RYC Turbos will install the SOE along the western boundary of the Site and within the building footprint for deep foundation elements.

Truck Count Log of Imported Material										
Facility/Material (BCP Site – NYSDEC Approved):	Tilcon New York Inc., Mount Hope Quarry (1.5-inch Clean Stone)		Tilcon New York Inc., Mount Hope Quarry (0.75-inch Clean Stone)		Braen Stone of Sparta Lafayette, New Jersey (1.5-inch Clean Stone)		Braen Stone of Sparta Lafayette, New Jersey (0.75-inch Clean Stone)		----	
Volume:	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yards	Trucks	Cu. Yards	Trucks	Cu. Yards
Today:	0	0	0	0	0	0	0	0	----	----
Total:	18	360	0	0	35	700	0	0	----	----
Approved Quantity:	----	500	----	500	----	3,500	----	3,500	----	----
Facility/Material (Lot 100 – NYCOER Approved):	Braen Stone of Sparta Lafayette, New Jersey (1.5-inch Clean Stone)		Braen Stone of Sparta Lafayette, New Jersey (0.75-inch Clean Stone)		----		----		----	
Volume:	Trucks	Cu. Yards	Trucks	Cu. Yds.	Trucks	Cu. Yards	Trucks	Cu. Yards	Trucks	Cu. Yards
Today:	0	0	0	0	----	----	----	----	----	----
Total:	6	120	1	20	----	----	----	----	----	----
Approved Quantity:	----	3,000	----	3,000	----	----	----	----	----	----

Note: 20 cubic yards assumed per truckload

Truck Count Log of Exported Material										
Facility/Material:	Clean Earth Philadelphia Philadelphia, Pennsylvania Approval # 243100026 (7,000 tons)		Clean Earth Carteret Carteret, New Jersey Approval #243070587 (4,000 tons)		Clean Earth Carteret Carteret, New Jersey Approval #253070241 (cumulative 83,450 tons)		Clean Earth Carteret Carteret, New Jersey Approval #253070242 (cumulative 83,450 tons)		Clean Earth New Castle New Castle, Delaware Approval #253020014 (cumulative 96,400 tons)	
Volume:	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.
Today:	0	0	0	0	8	160	0	0	0	0
Total:	175	3,500	51	1,020	588	11,760	71	1,420	277	5,540
Facility/Material:	Clean Earth New Castle New Castle, Delaware Approval #253020015 (cumulative 96,400 tons)		Clean Earth North Jersey Kearny, New Jersey Approval #2530804874 (6,000 tons)		Clean Earth North Jersey Kearny, New Jersey Approval #2530804878 (5,250 tons)		Clean Earth North Jersey Kearny, New Jersey Approval #2530804888 (1,500 tons)		Clean Earth North Jersey Kearny, New Jersey Pre-Approval #2530804828 (2,000 tons)	
Volume:	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.
Today:	0	0	0	0	10	200	0	0	0	0
Total:	1	20	0	0	19	380	0	0	1	20
Facility/Material:	Clean Earth North Jersey Kearny, New Jersey Approval #2530804872 (750 tons)		Clean Earth North Jersey Kearny, New Jersey Pre-Approval #2530804884 (50 tons)		Clean Earth North Jersey Kearny, New Jersey Approval #2530804880 (3,750 tons)		Clean Earth Carteret Carteret, New Jersey Approval #253070475 (cumulative 83,450 tons)		----	
Volume:	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.	Trucks	Cu. Yds.
Today:	0	0	0	0	0	0	0	0	----	----
Total:	2	40	0	0	0	0	91	1,820	----	----

Note: 20 cubic yards assumed per truckload

Photo Log

Photo 1 – United loading hazardous material from stockpile ST-29 for off-Site disposal to Clean Earth of North Jersey, facing northeast.



Photo 2 – United washing trucks at the truck wash station in the western portion of the Site, facing south.




Photo 3 – United spraying water as a preventative dust control measure in the southern portion of the Site, facing east.



Photo 4 – Stockpile ST-31 being covered with polyethylene sheeting at the end of the day, facing east.



SITE MAP

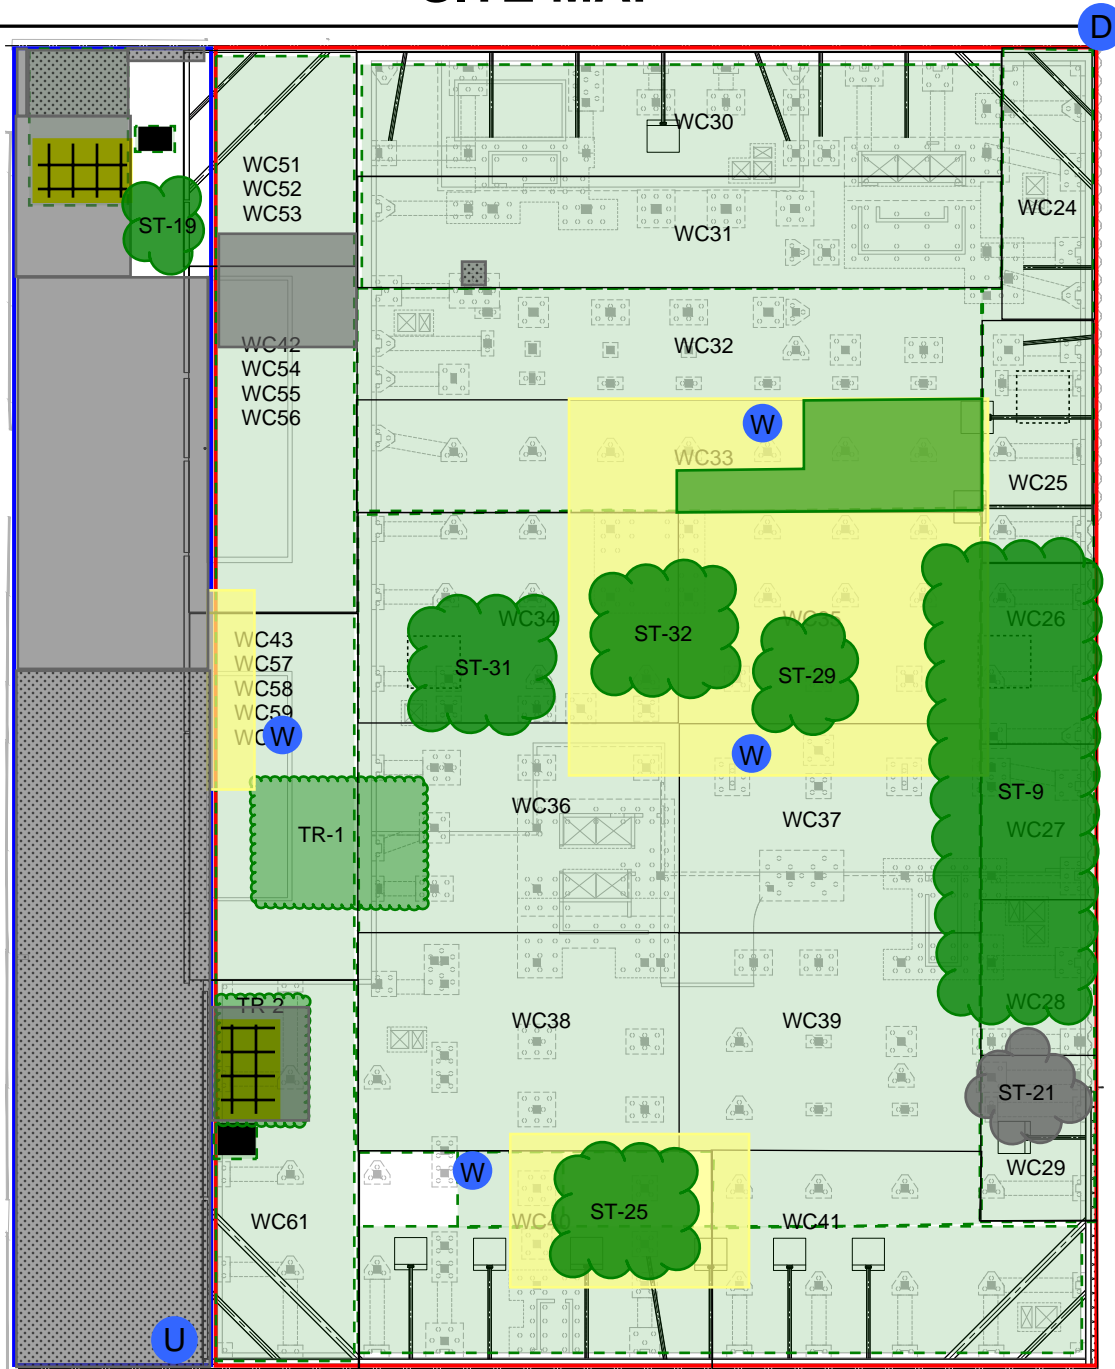

Approximate and Not to Scale

LEGEND

	12074 Flatlands Avenue Site Boundary (BCP Site No. C224353)		Work Zone Air Monitoring Station
	Lot 100 Site Boundary (NYCOER Site No. 25TMP1084K)		Downwind Perimeter Air Monitoring Station
	Disposal Grids		Upwind Perimeter Air Monitoring Station
	RAWP Hotspot Areas		Work Area
	Excavation Completed Today		Soil Stockpile
	Excavation Previously Completed		Clean Stone Stockpile
	Concrete		Asphalt Stockpile
	Clean Stone		Concrete Stockpile
	FODS Trackout		Truck Ramp
	Settling Tank for Truck Wash Station		




NOTES

1. Basemap from the "Support of Excavation Plan" drawing prepared by Langan dated 3/3/2025.
2. Waste characterization grids are shown as presented in the Draft Disposal Map prepared by Clean Earth.
3. Stockpile ST-9 contains hazardous material excavated from disposal grids WC30E, WC30F, WC31E, WC31F, WC32E, WC32F, WC33E, and WC33F in the northern portion of the Site for future off-Site disposal to Clean Earth North Jersey.
4. Stockpile ST-19 contains non-hazardous material excavated in the northern portion of Lot 100 for future off-Site disposal to Clean Earth New Castle.
5. Stockpile ST-21 contains previously imported 1.5-inch clean stone from Tilcon New York Inc. excavated from the Support of Excavation (SOE) slope for the adjacent Site to the east (BCP Site No. C224290).
6. Stockpile ST-25 contains non-hazardous material excavated from disposal grids WC38B, WC40AB, WC41AB, WC41C, and WC61B in the southern portion of the Site for off-Site disposal to Clean Earth Carteret.
7. Truck Ramp TR-1 contains non-hazardous material excavated from disposal grids WC57 and WC58 in the western portion of the Site for off-Site disposal to Clean Earth Carteret.
8. Truck Ramp TR-2 contains non-hazardous material excavated from disposal grids WC38B, WC38C, WC61B, WC61C, and WC61D in the western portion of the Site for off-Site disposal to Clean Earth Carteret.
9. Stockpile ST-29 contains hazardous material excavated from disposal grids WC30F, WC31F, and WC32F in the northern portion of the Site for off-Site disposal to Clean Earth North Jersey.
10. Stockpile ST-31 contains hazardous material excavated from disposal grids WC30F and WC32F in the northern portion of the Site for off-Site disposal to Clean Earth North Jersey.
11. Stockpile ST-32 contains non-hazardous material excavated from disposal grid WC33F in the northern portion of the Site for off-Site disposal to Clean Earth New Castle.


LANGAN	Site Contribution Report - CCC Phase 1B - 1 Report	100688803 - CCC - Phase 1B	
		Report Period	
		From:	5/1/2025 07:00
		To:	5/1/2025 19:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Windspeed (mph)	Prevailing wind direction
5/1/2025	53.8-68.7	22.5-45.9	30.1-30.2	0.3-6.2	SW

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2025	-22.9	08:00	-0.0433	14:45
Max Contribution (15 min avg.) - 5/1/2025	35.3	08:45	0.0483	13:30

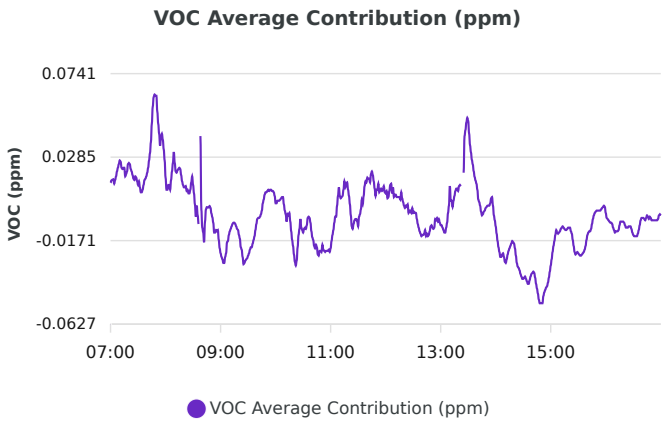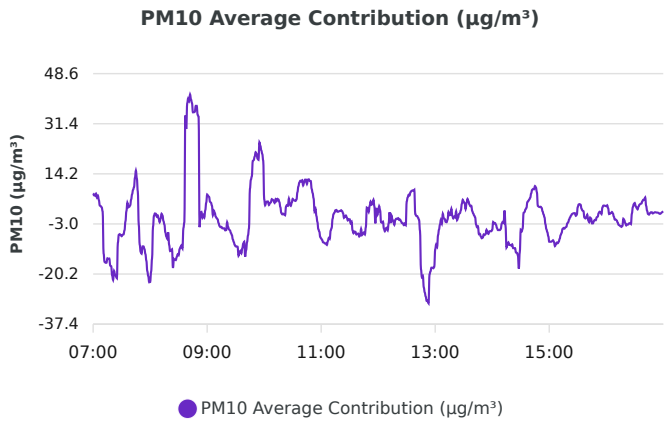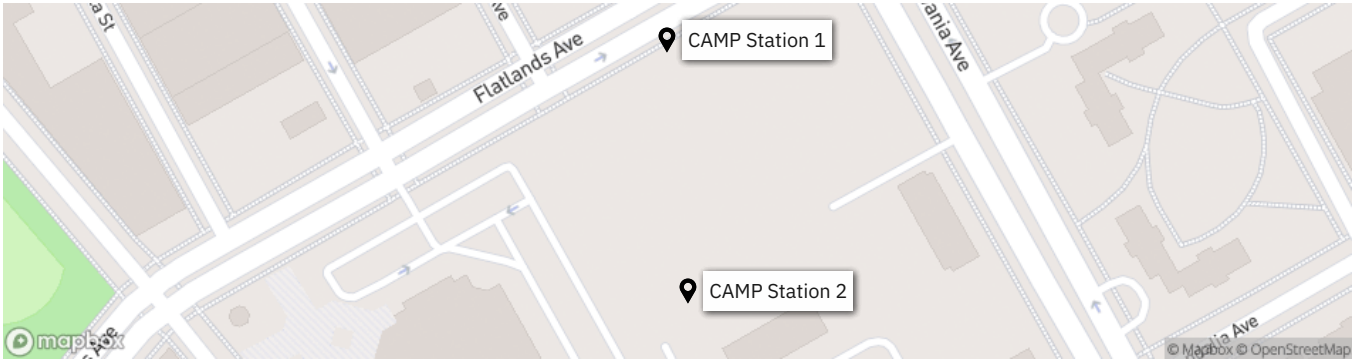

Wind rose (mph)

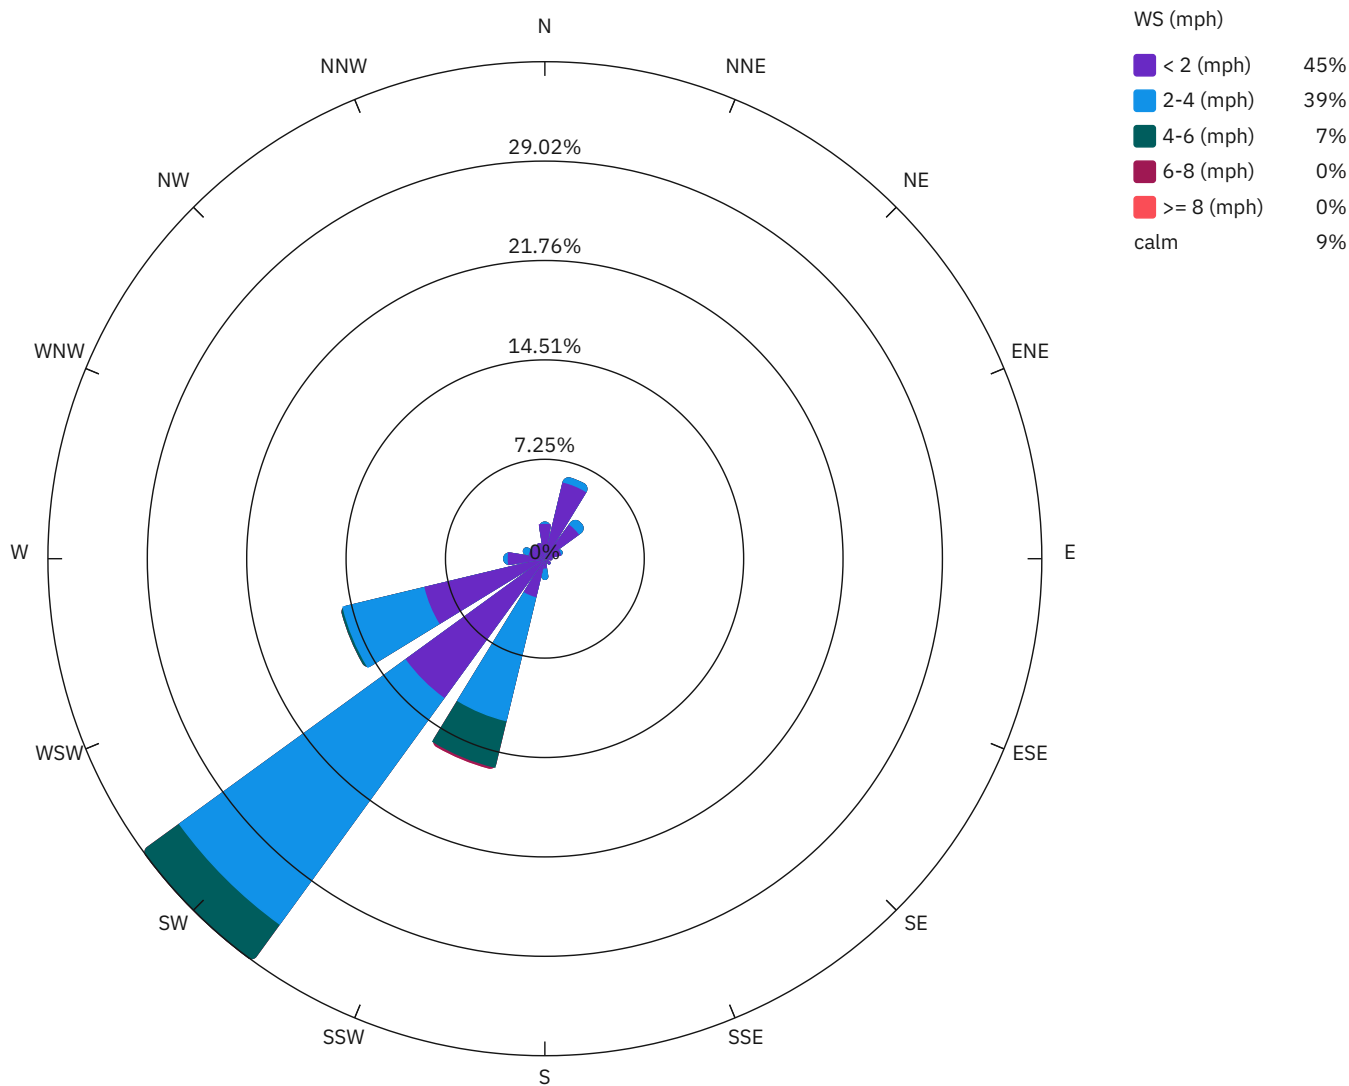

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed 15 min Avg	Wind Direction 15 min Avg
5/1/2025 07:00:00	11.2	18.7	7.5	0.0000	0.0145	0.0145	0.8	NE
5/1/2025 07:15:00	39.5	24.7	-14.8	0.0080	0.0307	0.0227	1.3	NE
5/1/2025 07:30:00	22.1	14.8	-7.2	0.0160	0.0293	0.0133	1.1	N
5/1/2025 07:45:00	14.1	29.4	15.3	0.0120	0.0587	0.0467	1.4	NNE
5/1/2025 08:00:00	41.6	18.7	-22.9	0.0300	0.0473	0.0173	0.7	NNE
5/1/2025 08:15:00	20.1	16.9	-3.2	0.0113	0.0340	0.0227	1.0	N
5/1/2025 08:30:00	32.0	18.3	-13.7	0.0160	0.0293	0.0133	0.5	N
5/1/2025 08:45:00	28.9	64.2	35.3	0.0250	0.0262	0.0012	0.4	WSW
5/1/2025 09:00:00	16.0	23.0	7.1	0.0480	0.0240	-0.0240	1.3	SW
5/1/2025 09:15:00	11.7	7.7	-4.0	0.0353	0.0280	-0.0073	2.0	SW
5/1/2025 09:30:00	16.7	6.1	-10.7	0.0407	0.0153	-0.0253	2.4	SW
5/1/2025 09:45:00	22.7	31.8	9.0	0.0213	0.0207	-0.0007	1.9	SW
5/1/2025 10:00:00	15.8	21.3	5.5	0.0193	0.0227	0.0033	1.0	WSW
5/1/2025 10:15:00	9.2	14.6	5.4	0.0433	0.0413	-0.0020	1.7	SW
5/1/2025 10:30:00	14.0	19.5	5.6	0.0453	0.0327	-0.0127	1.6	SW
5/1/2025 10:45:00	7.7	18.5	10.7	0.0500	0.0293	-0.0207	2.7	SW
5/1/2025 11:00:00	18.9	10.8	-8.0	0.0407	0.0193	-0.0213	2.4	SW
5/1/2025 11:15:00	13.0	14.7	1.7	0.0293	0.0447	0.0153	1.6	WSW
5/1/2025 11:30:00	12.7	11.3	-1.4	0.0427	0.0333	-0.0093	1.6	WSW
5/1/2025 11:45:00	18.3	12.4	-5.9	0.0433	0.0640	0.0207	1.4	SW
5/1/2025 12:00:00	21.7	22.7	1.0	0.0220	0.0307	0.0087	0.2	WSW
5/1/2025 12:15:00	11.3	9.8	-1.5	0.0193	0.0260	0.0067	1.3	WSW
5/1/2025 12:30:00	10.6	15.3	4.7	0.0207	0.0187	-0.0020	1.7	SW
5/1/2025 12:45:00	30.6	12.2	-18.5	0.0233	0.0100	-0.0133	2.1	SW
5/1/2025 13:00:00	25.1	13.4	-11.7	0.0173	0.0087	-0.0087	0.9	SW
5/1/2025 13:15:00	19.4	19.3	0.0	0.0227	0.0300	0.0073	1.0	W
5/1/2025 13:30:00	15.4	20.0	4.6	0.0050	0.0533	0.0483	2.1	SW
5/1/2025 13:45:00	14.3	10.4	-3.9	0.0207	0.0173	-0.0033	2.8	SW
5/1/2025 14:00:00	16.5	11.5	-5.0	0.0260	0.0167	-0.0093	2.5	SW
5/1/2025 14:15:00	29.4	18.4	-11.1	0.0280	0.0067	-0.0213	2.1	SW
5/1/2025 14:30:00	14.7	9.7	-5.0	0.0387	0.0007	-0.0380	3.1	SW
5/1/2025 14:45:00	6.9	16.9	10.0	0.0433	0.0000	-0.0433	2.6	SW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed 15 min Avg	Wind Direction 15 min Avg
5/1/2025 15:00:00	15.8	6.6	-9.1	0.0327	0.0020	-0.0307	1.7	WSW
5/1/2025 15:15:00	12.4	8.0	-4.4	0.0113	0.0007	-0.0107	2.0	SW
5/1/2025 15:30:00	11.5	14.3	2.8	0.0240	0.0000	-0.0240	3.1	SW
5/1/2025 15:45:00	12.3	9.5	-2.8	0.0107	0.0027	-0.0080	2.4	SW
5/1/2025 16:00:00	6.3	9.4	3.1	0.0100	0.0080	-0.0020	2.6	SW
5/1/2025 16:15:00	11.6	7.9	-3.8	0.0127	0.0040	-0.0087	3.5	SSW
5/1/2025 16:30:00	9.5	13.6	4.2	0.0153	0.0013	-0.0140	2.9	SW
5/1/2025 16:45:00	8.6	8.8	0.2	0.0093	0.0060	-0.0033	2.9	SW
5/1/2025 17:00:00	5.5	6.8	1.3	0.0107	0.0073	-0.0033	2.8	SW
