


SITE OBSERVATION REPORT

PROJECT No.: 170747001 PROJECT: C224398 – 1709 Surf Avenue LOCATION: 1709 Surf Avenue, Brooklyn, New York	CLIENT: Coney Island Associates Phase 3 LLC c/o BFC Partners	DATE: Thu, April 3, 2025 WEATHER: Rain, 44-47°F Wind: S at 2-6 mph TIME: 7:00am to 9:00am
CONTRACTOR'S EQUIPMENT: Doosan DL 300 Loader CAT 328DLCLC Excavator Doosan DX300LC Excavator Bobcat S590 Skid Steer CZM EK300LS Drill Rig CAT 314 CLCR Mini Excavator Bobcat E45 Mini Excavator CAT 345C Excavator	PRESENT AT SITE: RAWP Implementation Day 16 Environmental (Langan) – Michael Pinnella General Contractor (BFC Construction) Foundation Contractor (Precise Contracting [Precise]) Deep Foundation Contractor (RYC Turbos Corp.)	
OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.: <p>Langan was present to oversee implementation of the November 20, 2024 Remedial Action Work Plan (RAWP) for Brownfield Cleanup Program (BCP) Site No. C224398 at 1709 Surf Avenue. Observed activities were as follows:</p> <p>Site Activities</p> <ul style="list-style-type: none"> RYC Turbos Corp. excavated an about 3-foot-long by 3-foot-wide by 1-foot-deep area in the southeastern part of the site to support pile testing. Excavated material consisted of non-hazardous fill/soil and was screened for staining, odors, and instrumental evidence of contamination using a handheld photoionization detector (PID); evidence of impacts was not observed and the non-hazardous fill/soil was temporarily graded adjacent to the excavation area. <p>Sampling</p> <ul style="list-style-type: none"> No samples were collected. <p>CAMP Activities</p> <ul style="list-style-type: none"> Langan performed community air monitoring at the perimeter of the site at two locations (one downwind and one upwind) and included air monitoring for particulate matter for particulates less than 10 µm in diameter (PM10) and volatile organic compounds (VOC). Particulate and VOC concentrations did not exceed the action levels established in the site Community Air Monitoring Program (CAMP). Fugitive dust or odors associated with intrusive activities were not observed. <p>Anticipated Activities</p> <ul style="list-style-type: none"> RYC Turbos Corp. will continue to install piles across the site's footprint. <p>Material Tracking</p> <ul style="list-style-type: none"> No material was imported to the site. No material was exported from the site. 		
Cc: B. Gochenaur, K. Semon, M. Aronica (Langan)	By: Michael Pinnella LANGAN	


SITE OBSERVATION REPORT

FIGURE 1: SITE PLAN

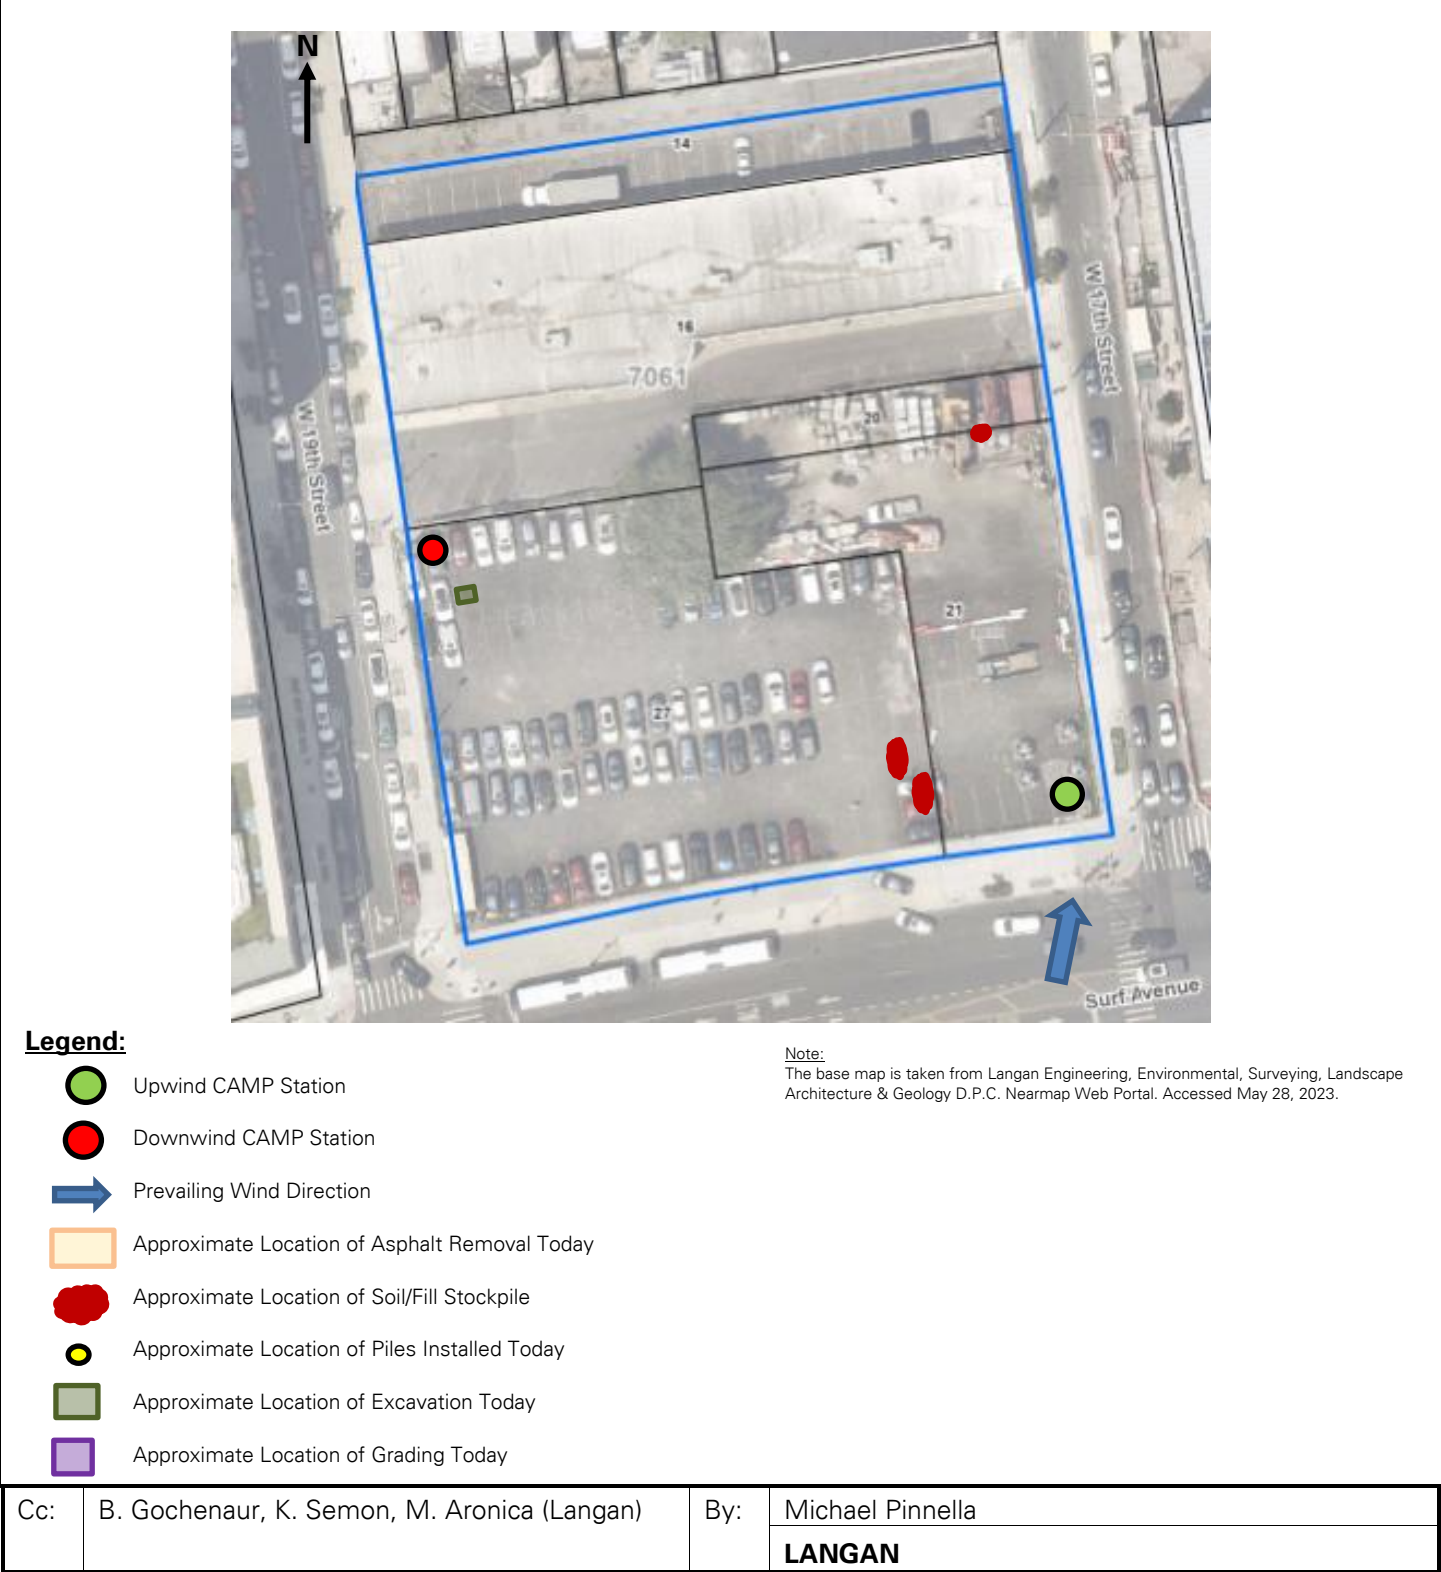

SITE OBSERVATION REPORT

FIGURE 2: ENDPOINT/SIDEWALL SAMPLE LOCATION MAP

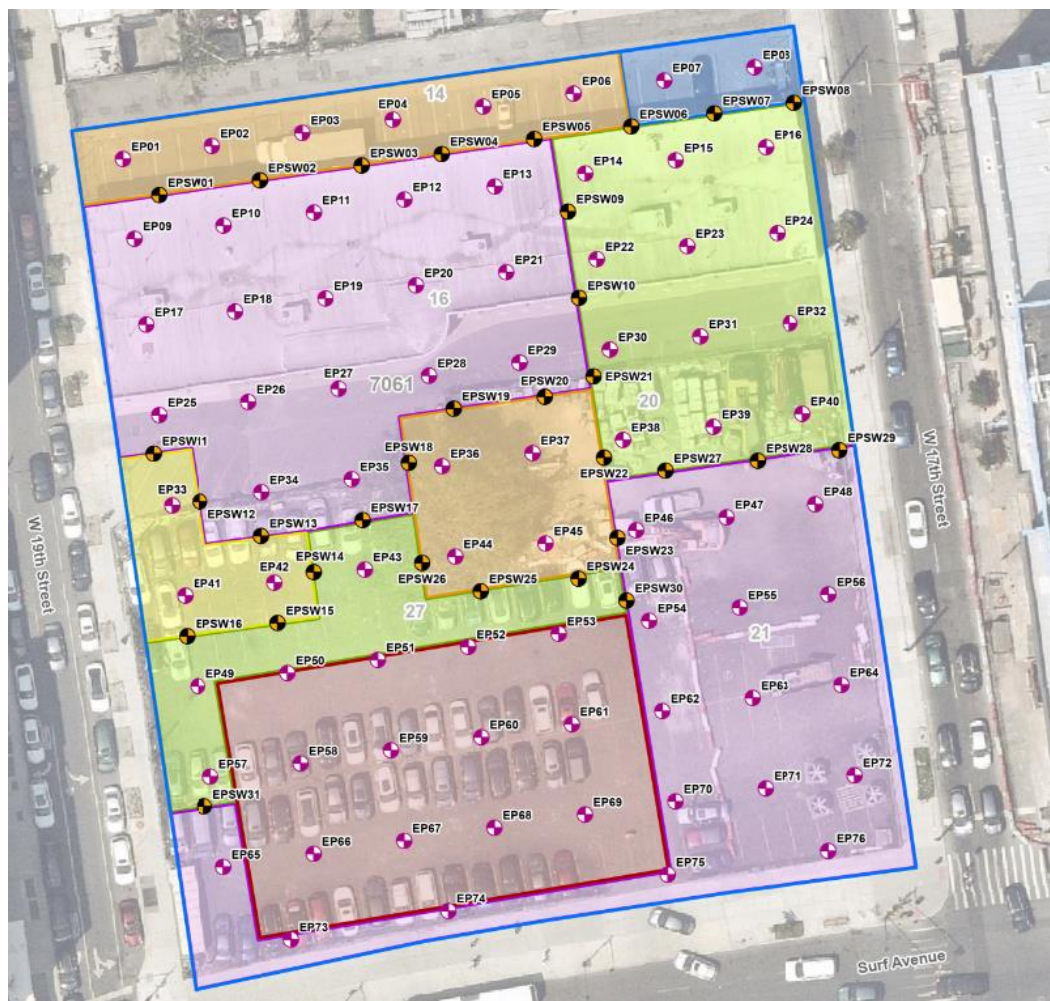

Legend

- Approximate Site Boundary
- Excavation to about 2 feet bgs
- Excavation to about 3 feet bgs
- Excavation to about 4 feet bgs
- Excavation to about 5 feet bgs
- Excavation to about 6 feet bgs
- Excavation to about 16 feet bgs to Remove Petroleum Impacts
- Proposed Endpoint Sample Location
- Proposed Sidewall Sample Location

Cc:	B. Gochenaur, K. Semon, M. Aronica (Langan)	By:	Michael Pinnella
			LANGAN

SITE OBSERVATION REPORT

SITE PHOTOGRAPHS



Photo 1: Excavation to support pile test in the western part of the site (facing southwest).

Cc:	B. Gochenaur, K. Semon, M. Aronica (Langan)	By:	Michael Pinnella
			LANGAN
