
Langan Engineering, Environmental, Surveying, Landscape Architecture and Geology, D.P.C.
360 West 31st Street, 8th Floor New York, NY 10001 T: 212.479.5400 F: 212.479.5444

To: Douglas MacNeal, NYSDEC

From: Kaitlyn Gioia, Langan

Info: 76 Eleventh Avenue Property Owner
Steven Ciambuschini (Langan)

Date: July 5, 2024

Re: Quarterly DNAPL Recovery Report: Q2 2024
17th Street Development Project (BCP Site No. C231036)
76 Eleventh Avenue New York, NY 10011
Langan Project No.: 100513103

Langan Engineering, Environmental, Surveying, Landscape Architecture and Geology, D.P.C. is pleased to submit this quarterly dense non-aqueous phase liquid (DNAPL) recovery report on behalf of 76 Eleventh Avenue Property Owner LLC (owner), summarizing DNAPL recovery at the 17th Street Development Project ("Site") for the second quarter of 2024 (April to June 2024), in accordance with the DNAPL Recovery Plan outlined in Section 4.4-DNAPL Recovery Program and Section 7.1-DNAPL Recovery Reporting of the September 17, 2020 draft Site Management Plan (post-construction update).

Background

The Site is located at 501 – 515 West 17th Street/76 Eleventh Avenue, New York, New York (Tax block 689, lot 17) in the West Chelsea neighborhood of Manhattan, New York. A figure showing the Site location is attached as Figure 1. The Site is approximately 76,440 square feet (1.755 acres). Ground elevations range from 8 feet above mean sea level (MSL) along 11th Avenue to 10 feet above MSL along 10th Avenue.

Remedial action was completed on July 8, 2014 and included shallow excavation and off-site soil disposal, installation of a subsurface containment wall, in situ stabilization, DNAPL recovery, and backfilling/capping. DNAPL recovery operations, which were discontinued during remedial action because of limited access to the wells, resumed in August 2014, and will continue until the NYSDEC approves the end of recovery activities. Following approval of the initial Site Management Plan and Final Engineering Report, the NYSDEC issued a Certificate of Completion (COC) on December 17, 2014. The COC was transferred to 76 Eleventh Avenue Property Owner LLC on May 7, 2015 and the Notice of Transfer of COC was recorded.

DNAPL Recovery Standard Operations

Post-remedial action DNAPL recovery from four on-site recovery wells began in August 2014. Prior to extraction, each well was gauged for product thickness and then the three wells with the largest DNAPL thickness received a steel bailer. The bailers remained undisturbed for about a two-week period to allow DNAPL to collect. The bailers were then pulled and the volume of DNAPL was measured. After extraction, each bailer was cleaned with a degreaser solvent and stored in polyethylene sheeting until the next monthly event. Recovered DNAPL was stored in labeled, 55-gallon steel drums.

MEMO

Construction began on May 19, 2016 with the pile installation program. Recovery wells RW-D and RW-J were decommissioned because of location conflicts with building foundation elements; replacement recovery wells were reinstalled between June 21 and 22, 2017. Foundation slab construction was completed on April 26, 2019; superstructure construction and interior fit out is ongoing.

The NYSDEC provided an April 13, 2020 email approval to modify DNAPL recovery reporting from monthly to quarterly reports, which will include the results of monthly recovery events for the months that make up the reporting quarter. For recovery events beginning in August 2020, the bailers are removed and the extracted DNAPL volume is measured; after measurement, the bailers are immediately returned to the wells to remain undisturbed until the next recovery event.

Current DNAPL Recovery Summary

The bailers were removed and DNAPL recovery was measured on April 29, May 29, and June 20, 2024. After measuring the recovered DNAPL, the bailers were returned to the wells until the next recovery period.


The following table summarizes the monthly DNAPL well thickness and recovery volumes for the 2024 second quarter (April to June) reporting period. The attached Table 1 includes a complete post-remedial action DNAPL recovery summary.

Recovery Well	DNAPL Recovery (gallons)			Quarterly DNAPL Recovery (gallons)
	April	May	June	April – June 2024
	4/29/2024	5/29/2024	6/20/2024	
RW-D	2.00	2.00	1.00	5.00
RW-E	1.75	2.5	2.25	6.50
RW-J	2.50	3.00	2.50	8.00
RW-K	4.00	3.00	0.25	7.25
Totals:	10.25	10.50	6.00	26.75

The volume of recovered DNAPL, since inception of recovery activities, is about 567 gallons.

Anticipated Activities for Next Period

76 Eleventh Avenue Property Owner LLC will conduct monthly bailing activities during construction, as practicable. The next recovery events are expected to take place in July, August, and September 2024.

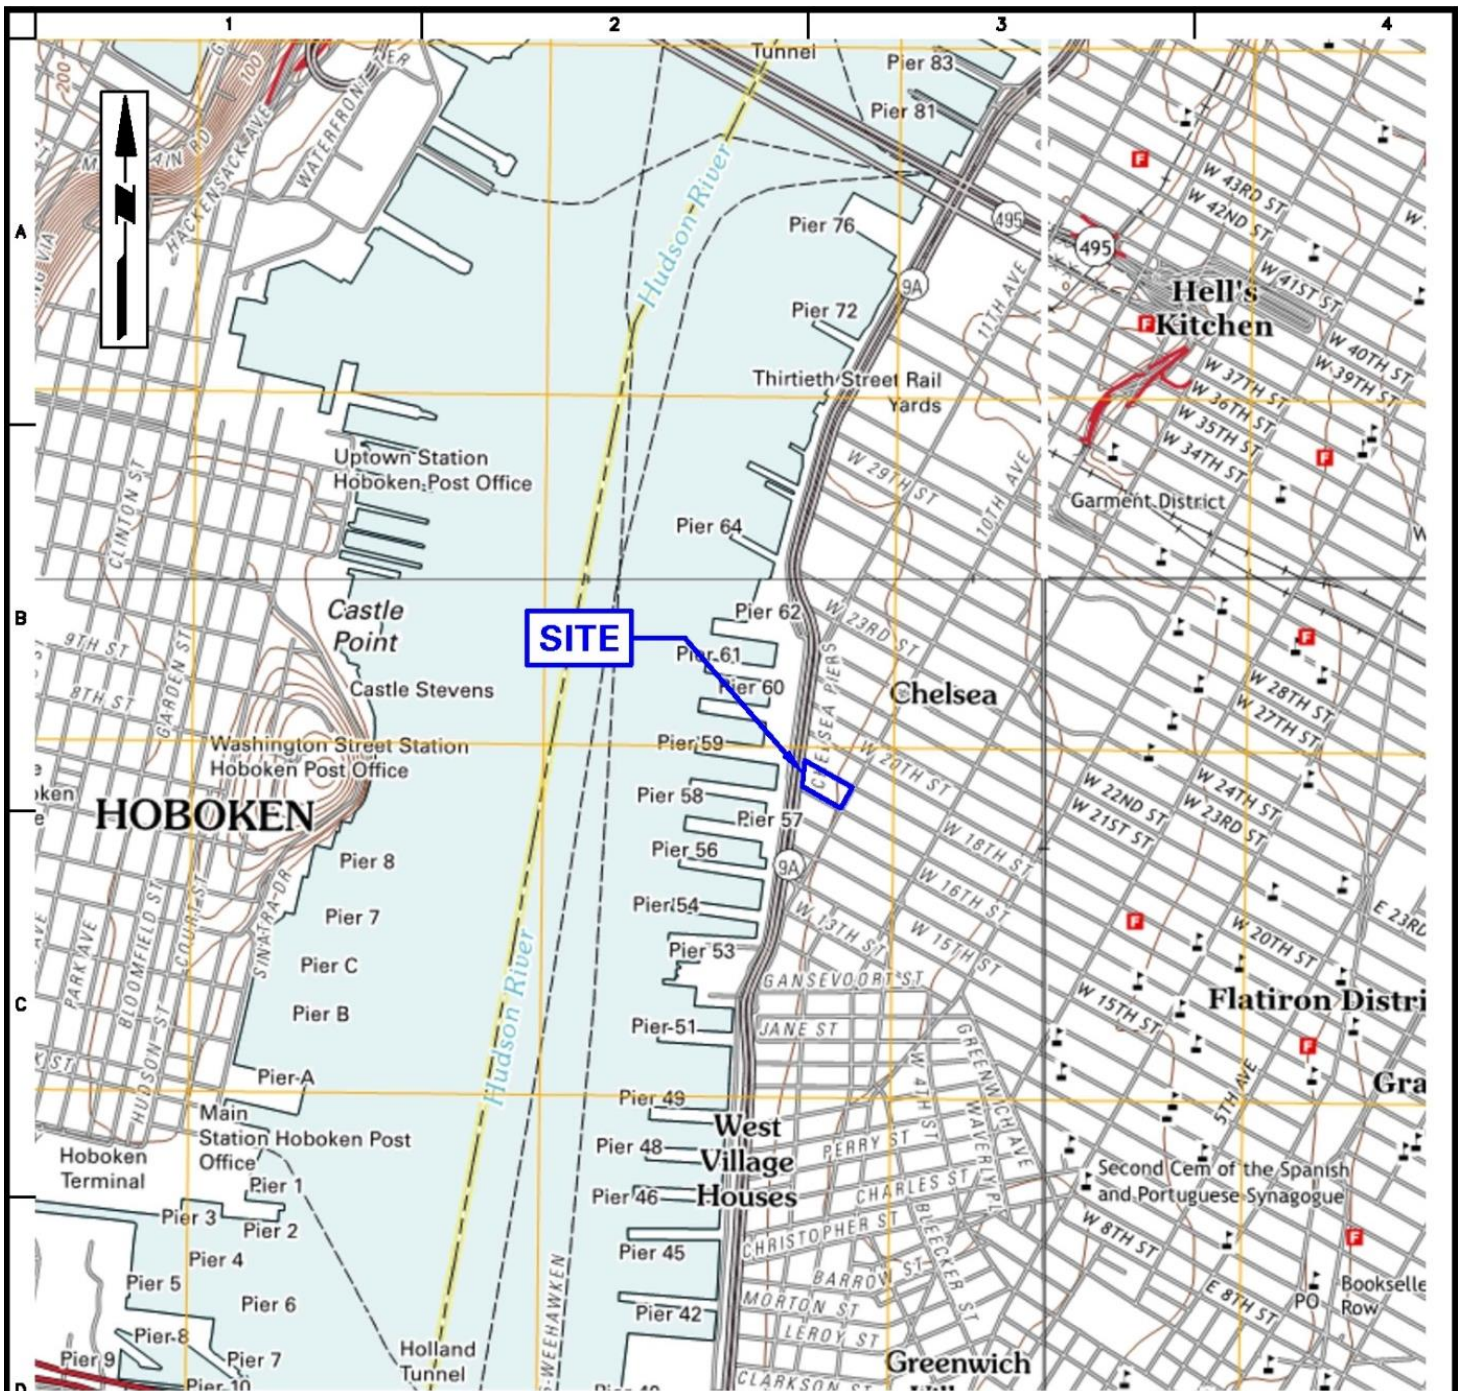

NOTE: BASE MAP IS TAKEN FROM USGS 7.5 MINUTE TOPOGRAPHIC MAPS FOR THE CENTRAL PARK, BROOKLYN, JERSEY CITY, AND WEEKHAWKEN QUADRANGLES.

LEGEND:



APPROXIMATE SITE BOUNDARY

<p>21 Pann Plaza, 360 West 31st Street, 8th Floor New York, NY 10001 T: 212.479.5400 F: 212.479.5444 www.langan.com Langan Engineering, Environmental, Surveying and Landscape Architecture, D.P.C. S.A. Langan Engineering, Environmental, Surveying and Landscape Architecture, D.P.C. Langan Engineering and Environmental Services, Inc. Langan CT, Inc. Langan International LLC Collectively known as Langan</p>	Project	Figure Title	Project No.	Figure No.	
	<p>76 ELEVENTH AVENUE</p> <p>BLOCK No. 689, LOT No. 17</p> <p>NEW YORK NEW YORK</p>	<p>SITE LOCATION MAP</p>	100513101	<p>1</p>	
			Date		11/17/2015
			Scale		N.T.S.
			Drawn By		Checked By
	AT	GN	Submission Date	NOVEMBER 2015	
			Sheet	1 of 8	
