

SITE OBSERVATION REPORT

<p>PROJECT No.: 170381202</p> <p>PROJECT: 250 Water Street</p> <p>LOCATION: New York, NY</p> <p>BCP SITE ID: C231127</p>	<p>CLIENT: 250 Seaport District, LLC c/o The Howard Hughes Corporation</p>	<p>DATE: Friday, June 23, 2023</p> <p>WEATHER: Overcast/Light Rain, 65 – 70 °F Wind: NE @ 3 – 7 mph</p> <p>TIME: 6:45 am – 12:30 pm</p> <p>MONITOR Jack Millman</p>	
<p>EQUIPMENT: CAT 335 Excavator ABI Mobilram Drill Rig Jerome J505 Mercury Vapor Analyzer RKI GX-6000 Photoionization Detector (PID) Aeroqual ASQ1 Air Monitoring Station</p>	<p>PRESENT AT SITE: Day 147 Langan (Environmental) Jack Millman and Isabella Legovich Suffolk Construction (Suffolk) (General Contractor) Anthony Galu East Coast Drilling, Inc. (ECD) (Foundation Contractor) Danny Rodgers New York State Department of Environmental Conservation (NYSDEC) Rafi Alam and Jared Donaldson</p>		
<p>OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:</p> <p>Langan was present to document remediation activities in accordance with the NYSDEC-approved November 2021 Remedial Action Work Plan (RAWP) at the 250 Water Street site (NYSDEC Brownfield Cleanup Program [BCP] Site No C231127).</p> <p>Site Activities</p> <ul style="list-style-type: none"> Suffolk and ECD continued mobilizing equipment in preparation for the next phase of remediation. 			
<p>Cc:</p>	<p>M. Raygorodetsky, P. McMahon, M. Au, J. Frey</p>	<p>By:</p>	<p>Jack Millman LANGAN</p>

SITE OBSERVATION REPORT

Material Tracking

- No material was exported from the site.
- No material was imported to the site.

Material Import Summary								
Facility Name Location Type of Material	Stone Industries, Inc. Haledon, NJ 1.5/2.5-inch Virgin Stone		Stone Industries, Inc. Haledon, NJ 0.75-inch Virgin Stone		Impact Reuse & Recovery Center or Impact Materials Jersey City, Lyndhurst/Jersey City, NJ 1.5-inch Clean Bluestone		Impact Reuse & Recovery Center, Lyndhurst, NJ General Fill	
Quantities	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)
Today	0	0	0	0	0	0	0	0
Project Total	8	184.42	0	0	15	339.65	336	8,216.79
NYSDEC Approved:	1,800 tons*				720 tons*		19,500 tons*	

*0.75-inch, 1.5-inch, and 2.5-inch virgin stone from the Stone Industries, Inc. facility and 1.5-inch clean bluestone from the Impact Reuse & Recovery Center (IRRC) facility were approved for import of 1,000 cubic yards (CY) and 400 CY, respectively. Assuming a conversion factor of 1.8, each quantity was converted to tons in order to accurately compare with import weight tickets. General fill from the IRRC facility was approved for import of 13,000 CY and a conversion factor of 1.5 is applied.

Material Export Summary (1 of 2)								
Facility Name Location Type of Material	Allocco Recycling Brooklyn, NY Construction & Demolition (C&D) Debris		IRRC Lyndhurst, NJ Construction & Demolition (C&D) Debris		Clean Earth of North Jersey Kearny, NJ Hazardous Lead-Impacted Soil/Fill		Clean Earth of North Jersey Kearny, NJ Non-hazardous Soil/Fill	
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)
Today	0	0	0	0	0	0	0	0
Project Total	5	85	42	840	95	1,900	216	4,320

Material Export Summary (2 of 2)							
Facility Name Location Type of Material	Middlesex County Landfill East Brunswick, NJ Non-hazardous Soil/Fill		Bayshore Soil Management Keasbey, NJ Petroleum-Impacted Soil/Fill		Clean Earth of Carteret, NJ Carteret, NJ Non-hazardous Soil/Fill		
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	
Today	0	0	0	0	0	0	
Project Total	261	5,220	267	5,340	66	1,320	

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey	By:	Jack Millman
			LANGAN

SITE OBSERVATION REPORT

Sampling

- No samples were collected.

CAMP Activities


- The community air monitoring plan (CAMP) was not implemented because no ground-intrusive activities were performed.

Anticipated Activities

- Suffolk and ECD will continue mobilization in preparation for the next phase of remediation.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey	By:	Jack Millman
			LANGAN

SITE OBSERVATION REPORT

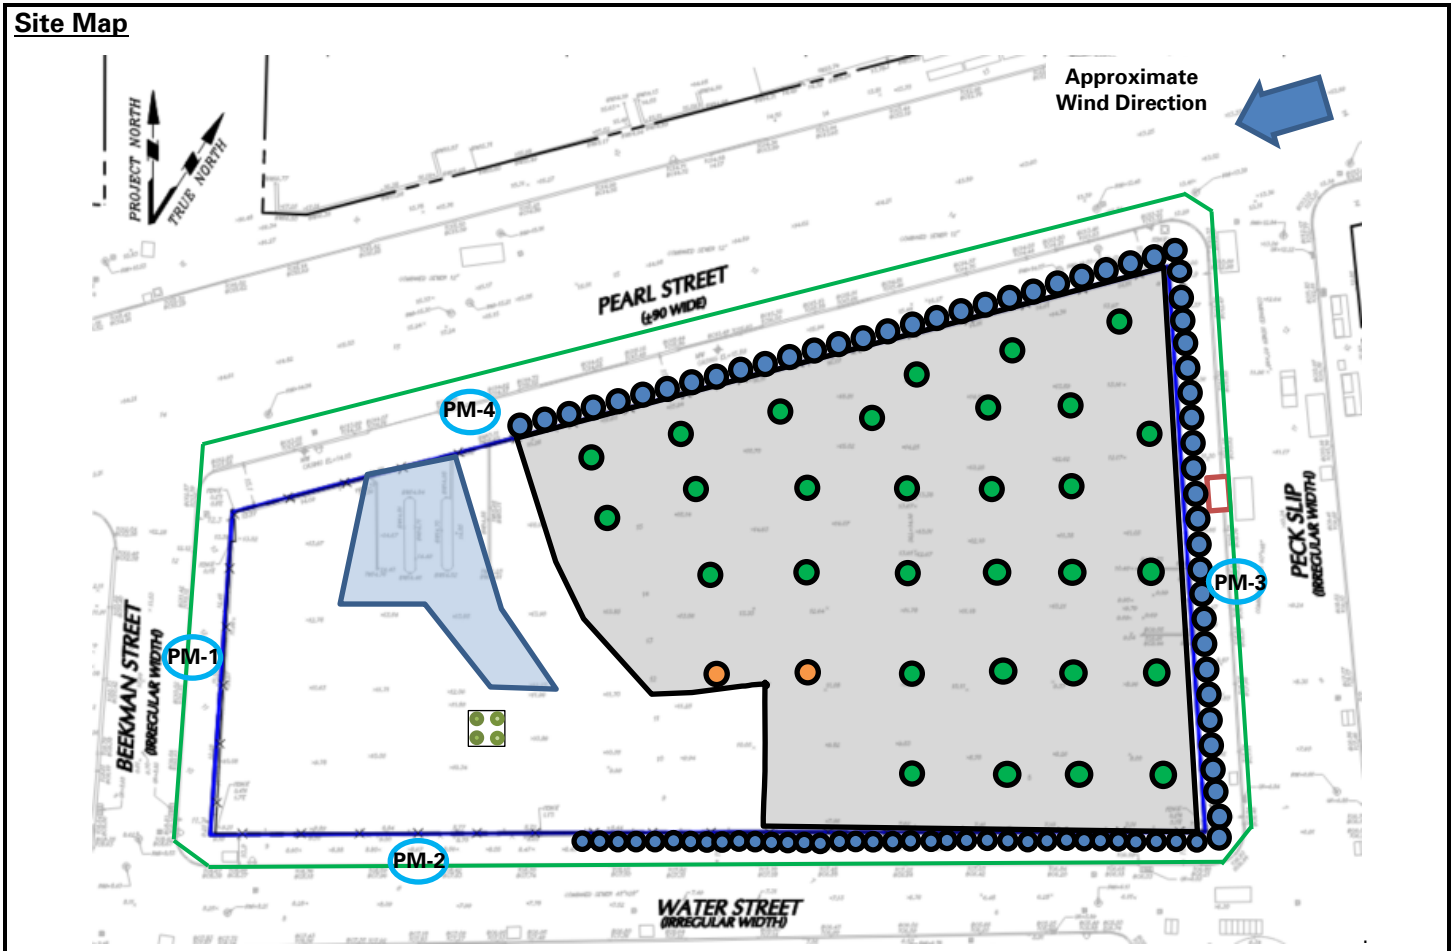

Notes:
1) Locations of air monitoring stations are approximate.

Legend:

- PM-1 Approximate Location of Air Monitoring Station
- Approximate Work Area
- Approximate Location of Installed Pile Cap
- Approximate Location of Foundation Piles Completed
- Approximate Location of Truck Tracking Pad
- Approximate Location of Underground Storage Tank
- Approximate Location of Soldier Pile
- Approximate Perimeter Construction Fence Location
- Previous Excavation Area
- Approximate Location of Documentation Sample
- Approximate Location of Previously Collected Endpoint Sample

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey	By:	Jack Millman LANGAN
-----	--	-----	-------------------------------

SITE OBSERVATION REPORT

Select Site Photographs:



Photo 1: General view of the site (facing northeast)



Photo 2: ECD mobilizing equipment to the site (facing southwest)

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey	By:	Jack Millman
		LANGAN	
