

SITE OBSERVATION REPORT

PROJECT No.: 170381202

CLIENT:

LLC

DATE: Friday October 6, 2023

PROJECT:

250 Water Street

Overcast/Rain, 66 - 70° F

WEATHER:

Wind: NNW @ 0.1 - 1.2 mph

LOCATION:

New York, NY

TIME:

5:45am - 5:30pm

BCP SITE ID:

C231127

MONITOR

Jack Millman

EQUIPMENT:

CAT 335 Excavator CAT 328 Excavator

Komatsu PC210 Excavator

Delmag Drill Rig Bauer RTG RG 27S Bauer BG45 Drill Rig

Casagrande M6A-1 Tieback Drill Rig Jerome J505 Mercury Vapor Analyzer RKI GX-6000 Photoionization Detector (PID) Aeroqual ASQ1 Air Monitoring Station

PRESENT AT SITE:

250 Seaport District.

Hughes Corporation

c/o The Howard

Day 219 Langan (Environmental/Geotechnical) Jack Millman, Michael Cole,

Pradeep Pandey

Suffolk Construction (Suffolk) (General Contractor) Anthony Galu,

Wyatt Favia

East Coast Drilling, Inc. (ECD) (Foundation Contractor) Danny Rodgers

New York State Department of Environmental Conservation

(NYSDEC) Rafi Alam

Earth Efficient (Soil Broker) Henry Batista

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:

Langan was present to document remediation activities in accordance with the NYSDEC-approved November 2021 Remedial Action Work Plan (RAWP) at the 250 Water Street site (NYSDEC Brownfield Cleanup Program [BCP] Site No C231127).

Site Activities

- ECD used a Bauer RTG RG 27S drill rig to pre-drill two boreholes in the northern part of the site to loosen the underlying soil in preparation for soil mix column installation.
- ECD used a Bauer BG45 drill rig to install two deep soil mix columns for support-of-excavation (SOE) system installation in the northern part of the site (along Pearl Street). ECD's drill rig advanced a steel rod with two cutter blades at the bottom of the rod, while concurrently injecting grout through the cutting head and spinning and advancing the blades downward to depths of about 107 and 110 feet below grade surface (bgs), respectively.
 - o No drilling spoils were generated during installation of the soil mix columns.
 - o Excess grout was contained within a temporary containment area in the eastern part of the site and will be managed as construction and demolition (C&D) debris at a later date.
- ECD excavated an about 75-foot-long by 20-foot-wide area to a maximum depth of about 14 feet bgs in the central part of the site (waste characterization cells WC01, WC02, WC04, WC0405, and WC06) for removal and off-site disposal of soil/fill.
 - o Excavated soil/fill was screened for odors, staining, organic vapors, and mercury vapor using a handheld PID and handheld Jerome® J505 mercury vapor analyzer, respectively. Evidence of impacts was not observed and the excavated soil/fill was separated from C&D debris using a sifting bucket. The soil/fill and C&D debris were separately loaded into securely covered tri-axle dump trucks for offsite disposal.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 2 of 7

SITE OBSERVATION REPORT

- Mercon-X® mercury vapor suppressant was actively applied to the soil/fill during excavation as a precautionary measure.
- ECD graded soi/fill in an about 60-foot-long by 100-foot-wide area and an about 20-foot-long by 60-foot-wide area to stabilize the surface for SOE installation in the southeast and northern parts of the site, respectively.
 - o Graded soil/fill was screened for odors, staining, organic vapors, and mercury vapor using a handheld PID and handheld Jerome® J505 mercury vapor analyzer, respectively. Evidence of impacts was not observed and the soil/fill generated from grading activities was added to the soil stockpile in the central part of the site for future off-site disposal.

Material Tracking

- ECD exported seven truckloads (about 140 cubic yards [CY]) of C&D debris for off-site disposal at the Earth Efficient MSM facility located in East Stroudsburg, PA.
- ECD exported ten truckloads (about 200 CY) of non-hazardous soil/fill for off-site disposal at the Middlesex County Landfill, located in East Brunswick, NJ.
- No material was imported to the site.

	Material Import Summary							
Facility Name Location Type of Material Stone Industries, Inc. Haledon, NJ 1.5/2.5-inch Virgin Stone		Stone Industries, Inc. Haledon, NJ 0.75-inch Virgin Stone		Impact Reuse & Recovery Center or Impact Materials Jersey City, Lyndhurst/Jersey City, NJ 1.5-inch Clean Bluestone		Impact Reuse & Recovery Center, Lyndhurst, NJ General Fill		
Quantities	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)
Today	0	0	0	0	0	0	0	0
Project Total	12	283.91	0	0	15	339.65	374	9,157.85
NYSDEC Approved:		1,800	tons*		720	tons*	19,500	tons*

*0.75-inch, 1.5-inch, and 2.5-inch virgin stone from the Stone Industries, Inc. facility and 1.5-inch clean bluestone from the Impact Reuse & Recovery Center (IRRC) facility were approved for import of 1,000 cubic yards (CY) and 400 CY, respectively. Assuming a conversion factor of 1.8, each quantity was converted to tons in order to accurately compare with import weight tickets. General fill from the IRRC facility was approved for import of 13,000 CY and a conversion factor of 1.5 is applied.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 3 of 7

SITE OBSERVATION REPORT

Material Export Summary (1 of 3)								
Facility Name Location Type of Material Allocco Recycling Brooklyn, NY Construction & Demolition (C&D) Debris		Lyndh	RRC urst, NJ Debris	East Stro	icient MSM udsburg, PA Debris	Clean Earth of North Jersey Kearny, NJ Hazardous Lead-Impacted Soil/Fill		
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)
Today	0	0	0	0	7	140	0	0
Project Total	5	85	42	840	131	2,620	101	2,020

Material Export Summary (2 of 3)							
Facility Name Middlesex County Landfill Location East Brunswick, NJ Type of Material Non-hazardous Soil/Fill		ınswick, NJ	Bayshore Soil Management Keasbey, NJ Petroleum-Impacted Soil/Fill		Clean Earth of Carteret, NJ Carteret, NJ Non-hazardous Soil/Fill		
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	
Today	10	200	0	0	0	0	
Project Total	311	6,220	267	5,340	66	1,320	

	Material Export Summary (3 of 3)								
Facility Name Location Type of Material	Kear	of North Jersey ny, NJ dous Soil/Fill	Eliz	chem, Inc. abeth, NJ d - Impacted Soil/Fill	Harmony Foul Rift (HFR) Belvidere, NJ Non-hazardous Soil/Fill				
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)			
Today	0	0	0	0	0	0			
Project Total	201	4,020	10	200	13	260			

Sampling

• No samples were collected.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



SITE OBSERVATION REPORT

CAMP Activities

Langan performed air monitoring at the perimeter of the site, at the northern sidewalk of Pearl Street, at the western sidewalk of Beekman Street, at the eastern sidewalk of Peck Slip, and at the southern sidewalk of Water Street at eight total locations for mercury vapor, volatile organic compounds (VOCs), and particulate matter less than 10 microns in diameter (PM10) from about 7:12am to 4:25pm. There were no fifteen-minute average concentrations for mercury vapor, VOCs or PM10 that approached or exceeded the action levels established by the CAMP (1.00 μ g/m³, 5.0 ppm, or 0.100 mg/m³, respectively).

Background Concentrations

Prior to implementation of CAMP, instantaneous background concentrations of mercury vapor and VOCs were recorded using a handheld Jerome® J505 mercury vapor analyzer and a handheld PID, respectively.

- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 μg/m³.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Perimeter and Work Zone Concentrations

Daily Average Concentrations

Station ID	Particulate (mg/m³)	Organic Vapor (ppm)	Mercury Vapor (µg/m³)
PM-1	0.010	0.00	0.02
PM-2	0.011	0.00	0.01
PM-3	0.010	0.00	0.00
PM-4	0.016	0.00	0.02
WZ-1	0.009	0.00	0.00
WZ-2	0.009	0.00	0.00
WZ-3	0.009	0.00	0.00
WZ-4	0.010	0.00	0.01

Maximum 15-Minute-Average Concentrations

Station ID	Particulate (mg/m³)	Organic Vapor (ppm)	Mercury Vapor (µg/m³)
PM-1	0.021	0.01	0.06
PM-2	0.032	0.02	0.08
PM-3	0.028	0.00	0.01
PM-4	0.051	0.08	0.09
WZ-1	0.016	0.00	0.01
WZ-2	0.017	0.00	0.01
WZ-3	0.018	0.00	0.02
WZ-4	0.019	0.01	0.02

•mg/m³ = milligrams per cubic meter •ppm = parts per million •µg/m³ = micrograms per cubic meter

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 5 of 7

SITE OBSERVATION REPORT

Ambient Air (Handheld Jerome® J505 and Handheld PID)

- The dedicated mobile monitor (Langan) used a handheld Jerome® J505 mercury vapor analyzer to monitor ambient air conditions at various heights throughout the site. Instantaneous mercury vapor concentrations throughout the site ranged from 0.00 µg/m³ to 0.09 µg/m³.
- The dedicated mobile monitor (Langan) used a handheld PID to monitor VOC concentrations throughout the site. Instantaneous VOC concentrations were not detected above background concentrations throughout the workday.

Off-site CAMP Stations

- CAMP station WZ-1 was placed on the western sidewalk of Beekman Street from about 7:07am to 4:42pm.
- CAMP station WZ-2 was placed on the southern sidewalk of Water Street from about 7:05am to 4:46pm.
- CAMP station WZ-3 was placed on the eastern sidewalk of Peck Slip from about 7:03am to 4:53pm.
- CAMP station WZ-4 was placed on the northern sidewalk of Pearl Street from about 6:59am to 5:01pm.

Prior to CAMP Shutdown

Prior to discontinuing CAMP, mercury vapor and VOC concentrations were confirmed to return to background conditions at each perimeter station using the handheld Jerome® J505 mercury vapor analyzer and handheld PID, respectively. Perimeter CAMP stations were discontinued sequentially between 4:25pm and 4:30pm.

- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 µg/m³.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Anticipated Activities


- ECD will continue exporting C&D and soil/fill from the western part of the site for off-site disposal.
- ECD will continue installing soil mix columns and/or soldier piles for SOE installation along Pearl Street, Water Street, and Peck Slip.
- ECD will continue installing tiebacks for the SOE system along Beekman and Pearl Streets.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 6 of 7

SITE OBSERVATION REPORT

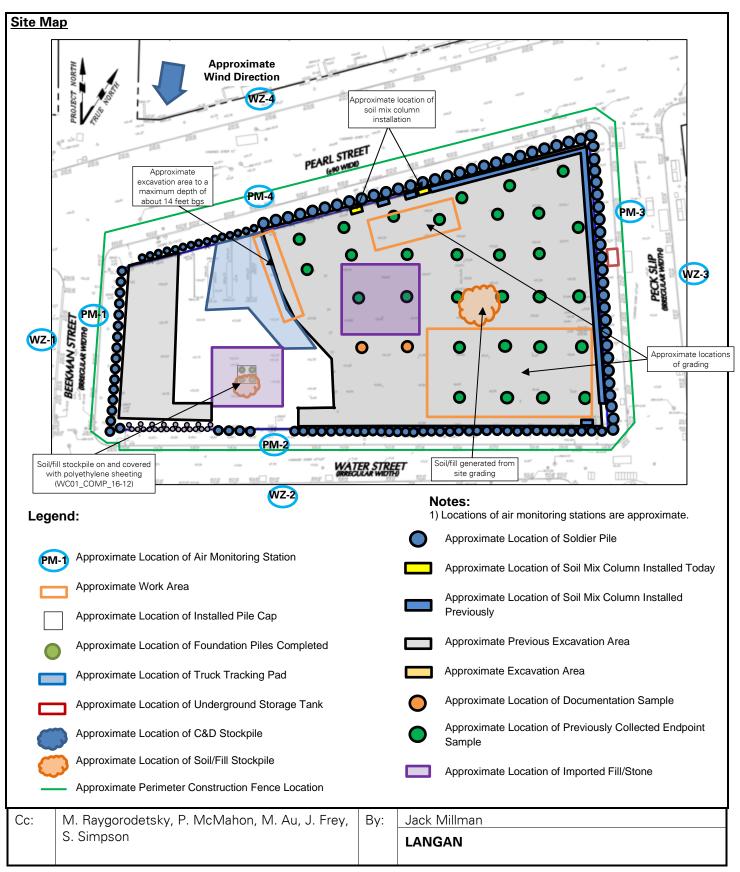



Page 7 of 7

SITE OBSERVATION REPORT

Select Site Photographs:



Photo 1: ECD installing a soil mix column in the northern part of the site (facing west)



Photo 2: ECD loading a truck with soil/fill for off-site disposal (facing northeast)

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN
