

SITE OBSERVATION REPORT

PROJECT No.: 170381202 PROJECT: 250 Water Street LOCATION: New York, NY BCP SITE ID: C231127	CLIENT: 250 Seaport District, LLC c/o The Howard Hughes Corporation	DATE: Monday, October 23, 2023 WEATHER: Sunny, 47 – 58° F Wind: ENE @ 0.1 – 2.3 mph TIME: 5:45am – 4:45pm MONITOR Gabriella DeGennaro
EQUIPMENT: CAT 335 Excavator CAT 328 Excavator Komatsu PC210 Excavator Delmag Drill Rig Bauer RTG RG 27S Bauer BG45 Drill Rig Casagrande M6A-1 Tieback Drill Rig Jerome J505 Mercury Vapor Analyzer RKI GX-6000 Photoionization Detector (PID) Aeroqual ASQ1 Air Monitoring Station	PRESENT AT SITE: Day 230 Langan (Environmental/Geotechnical) Gabriella DeGennaro, Michael Cole, Pradeep Pandey Suffolk Construction (Suffolk) (General Contractor) Wyatt Favia East Coast Drilling, Inc. (ECD) (Foundation Contractor) Mike Brosnan New York State Department of Environmental Conservation (NYSDEC) Meghan Medwid Earth Efficient (Soil Broker) Yinette Batista AKRF, Inc. (Archaeologist) Elizabeth Meade	
OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:		
<p>Langan was present to document remediation activities in accordance with the NYSDEC-approved November 2021 Remedial Action Work Plan (RAWP) at the 250 Water Street site (NYSDEC Brownfield Cleanup Program [BCP] Site No C231127).</p>		
Site Activities		
<ul style="list-style-type: none"> • ECD used a Bauer RTG RG 27S drill rig to pre-drill one borehole in the southeast part of the site to loosen the underlying soil in preparation for soil mix column installation. • ECD used a Bauer BG45 drill rig to install one deep soil mix column for support-of-excavation (SOE) system installation in the southeast part of the site (along Water Street). ECD’s drill rig advanced a steel rod with two cutter blades at the bottom of the rod, while concurrently injecting grout through the cutting head and spinning and advancing the blades downward to a depth of about 106 feet below grade surface (bgs). <ul style="list-style-type: none"> ○ No drilling spoils were generated during installation of the soil mix column. ○ Excess grout was contained within a temporary containment area in the eastern part of the site and will be managed as construction and demolition (C&D) debris at a later date. • ECD excavated an about 40-foot-long by 25-foot-wide area to a maximum depth of about 7 feet bgs in the western part of the site (waste characterization cell WC03 and WC11) for removal and off-site disposal of hazardous lead-impacted soil/fill. <ul style="list-style-type: none"> ○ Excavated soil/fill was screened for odors, staining, organic vapors, and mercury vapor using a handheld PID and handheld Jerome® J505 mercury vapor analyzer, respectively. Evidence of impacts was not observed and the excavated soil/fill was live-loaded into securely covered tri-axle dump trucks for off-site disposal. • ECD graded soil/fill in an about 100-foot-long by 100-foot-wide area in the eastern part of the site to stabilize the surface for SOE system installation. 		
Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By: Gabriella DeGennaro LANGAN

SITE OBSERVATION REPORT

- Graded soil/fill was screened for odors, staining, organic vapors, and mercury vapor using a handheld PID and handheld Jerome® J505 mercury vapor analyzer, respectively. Evidence of impacts was not observed and the soil/fill generated from grading activities was added to the stockpile in the northeast part of the site for future off-site disposal.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro LANGAN
-----	---	-----	--------------------------------------

SITE OBSERVATION REPORT

Material Tracking

- ECD exported eight truckloads (about 160 CY) of hazardous lead-impacted soil/fill for off-site disposal at the Clean Earth of North Jersey (CENJ) facility in Kearny, NJ.
- No material was imported to the site.

Material Import Summary								
Facility Name Location Type of Material	Stone Industries, Inc. Haledon, NJ 1.5/2.5-inch Virgin Stone		Stone Industries, Inc. Haledon, NJ 0.75-inch Virgin Stone		Impact Reuse & Recovery Center or Impact Materials Jersey City, Lyndhurst/Jersey City, NJ 1.5-inch Clean Bluestone		Impact Reuse & Recovery Center, Lyndhurst, NJ General Fill	
Quantities	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)
Today	0	0	0	0	0	0	0	0
Project Total	13	309.28	0	0	15	339.65	374	9,157.85
NYSDEC Approved:	1,800 tons*				720 tons*		19,500 tons*	

*0.75-inch, 1.5-inch, and 2.5-inch virgin stone from the Stone Industries, Inc. facility and 1.5-inch clean bluestone from the Impact Reuse & Recovery Center (IRRC) facility were approved for import of 1,000 cubic yards (CY) and 400 CY, respectively. Assuming a conversion factor of 1.8, each quantity was converted to tons in order to accurately compare with import weight tickets. General fill from the IRRC facility was approved for import of 13,000 CY and a conversion factor of 1.5 is applied.

Material Export Summary (1 of 3)								
Facility Name Location Type of Material	Allocco Recycling Brooklyn, NY Construction & Demolition (C&D) Debris		IRRC Lyndhurst, NJ C&D Debris		Earth Efficient MSM East Stroudsburg, PA C&D Debris		Clean Earth of North Jersey Kearny, NJ Hazardous Lead-Impacted Soil/Fill	
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)
Today	0	0	0	0	0	0	8	160
Project Total	5	85	42	840	252	5,040	115	2,300

Material Export Summary (2 of 3)							
Facility Name Location Type of Material	Middlesex County Landfill East Brunswick, NJ Non-hazardous Soil/Fill		Bayshore Soil Management Keasbey, NJ Petroleum-Impacted Soil/Fill		Clean Earth of Carteret, NJ Carteret, NJ Non-hazardous Soil/Fill		
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	
Today	0	0	0	0	0	0	
Project Total	324	6,480	267	5,340	66	1,320	

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro LANGAN
-----	---	-----	--------------------------------------

SITE OBSERVATION REPORT

Material Export Summary (3 of 3)						
Facility Name Location Type of Material	Clean Earth of North Jersey Kearny, NJ Non-hazardous Soil/Fill		Cycle Chem, Inc. Elizabeth, NJ Hazardous Lead - Impacted Soil/Fill		Harmony Foul Rift (HFR) Belvidere, NJ Non-hazardous Soil/Fill	
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)
Today	0	0	0	0	0	0
Project Total	201	4,020	10	200	27	540

Sampling

- No samples were collected.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro LANGAN
-----	---	-----	--------------------------------------

SITE OBSERVATION REPORT

CAMP Activities

Langan performed air monitoring at the perimeter of the site, at the northern sidewalk of Pearl Street, at the western sidewalk of Beekman Street, at the eastern sidewalk of Peck Slip, and at the southern sidewalk of Water Street at eight total locations for mercury vapor, volatile organic compounds (VOCs), and particulate matter less than 10 microns in diameter (PM10) from about 7:10am to 4:09 pm. There were no fifteen-minute average concentrations for mercury vapor, VOCs or PM10 that approached or exceeded the action levels established by the CAMP (1.00 $\mu\text{g}/\text{m}^3$, 5.0 ppm, or 0.100 mg/m^3 , respectively).

Background Concentrations

Prior to implementation of CAMP, instantaneous background concentrations of mercury vapor and VOCs were recorded using a handheld Jerome® J505 mercury vapor analyzer and a handheld PID, respectively.

- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 $\mu\text{g}/\text{m}^3$.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Perimeter and Work Zone Concentrations

Daily Average Concentrations

Station ID	Particulate (mg/m^3)	Organic Vapor (ppm)	Mercury Vapor ($\mu\text{g}/\text{m}^3$)
PM-1	0.005	0.00	0.02
PM-2	0.003	0.00	0.01
PM-3	0.002	0.00	0.00
PM-4	0.003	0.00	0.02
WZ-1	0.003	0.00	0.00
WZ-2	0.002	0.00	0.00
WZ-3	0.001	0.00	0.02
WZ-4	0.002	0.00	0.01

Maximum 15-Minute-Average Concentrations

Station ID	Particulate (mg/m^3)	Organic Vapor (ppm)	Mercury Vapor ($\mu\text{g}/\text{m}^3$)
PM-1	0.017	0.02	0.06
PM-2	0.006	0.02	0.02
PM-3	0.002	0.00	0.01
PM-4	0.005	0.09	0.04
WZ-1	0.008	0.01	0.01
WZ-2	0.004	0.03	0.01
WZ-3	0.002	0.00	0.38
WZ-4	0.003	0.00	0.03

• mg/m^3 = milligrams per cubic meter •ppm = parts per million • $\mu\text{g}/\text{m}^3$ = micrograms per cubic meter

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro
			LANGAN

SITE OBSERVATION REPORT

Ambient Air (Handheld Jerome® J505 and Handheld PID)

- The dedicated mobile monitor (Langan) used a handheld Jerome® J505 mercury vapor analyzer to monitor ambient air conditions at various heights throughout the site. Instantaneous mercury vapor concentrations throughout the site ranged from 0.00 $\mu\text{g}/\text{m}^3$ to 0.08 $\mu\text{g}/\text{m}^3$.
- The dedicated mobile monitor (Langan) used a handheld PID to monitor VOC concentrations throughout the site. Instantaneous VOC concentrations were not detected above background concentrations throughout the workday.

Off-site CAMP Stations

- CAMP station WZ-1 was placed on the western sidewalk of Beekman Street from about 6:43am to 3:51pm.
- CAMP station WZ-2 was placed on the southern sidewalk of Water Street from about 6:42am to 4:18pm.
- CAMP station WZ-3 was placed on the eastern sidewalk of Peck Slip from about 6:36am to 4:02pm.
- CAMP station WZ-4 was placed on the northern sidewalk of Pearl Street from about 6:52am to 4:00pm.

Prior to CAMP Shutdown

Prior to discontinuing CAMP, mercury vapor and VOC concentrations were confirmed to return to background conditions at each perimeter station using the handheld Jerome® J505 mercury vapor analyzer and handheld PID, respectively. Perimeter CAMP stations were discontinued sequentially between 4:09pm and 4:16pm.


- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 $\mu\text{g}/\text{m}^3$.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Anticipated Activities

- ECD will continue exporting C&D and soil/fill from the eastern part of the site for off-site disposal.
- ECD will continue installing soil mix columns and/or soldier piles for SOE installation along Pearl Street and Water Street.
- ECD will continue installing tiebacks for the SOE system along Beekman and Pearl Streets.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro LANGAN
-----	---	-----	--------------------------------------

SITE OBSERVATION REPORT

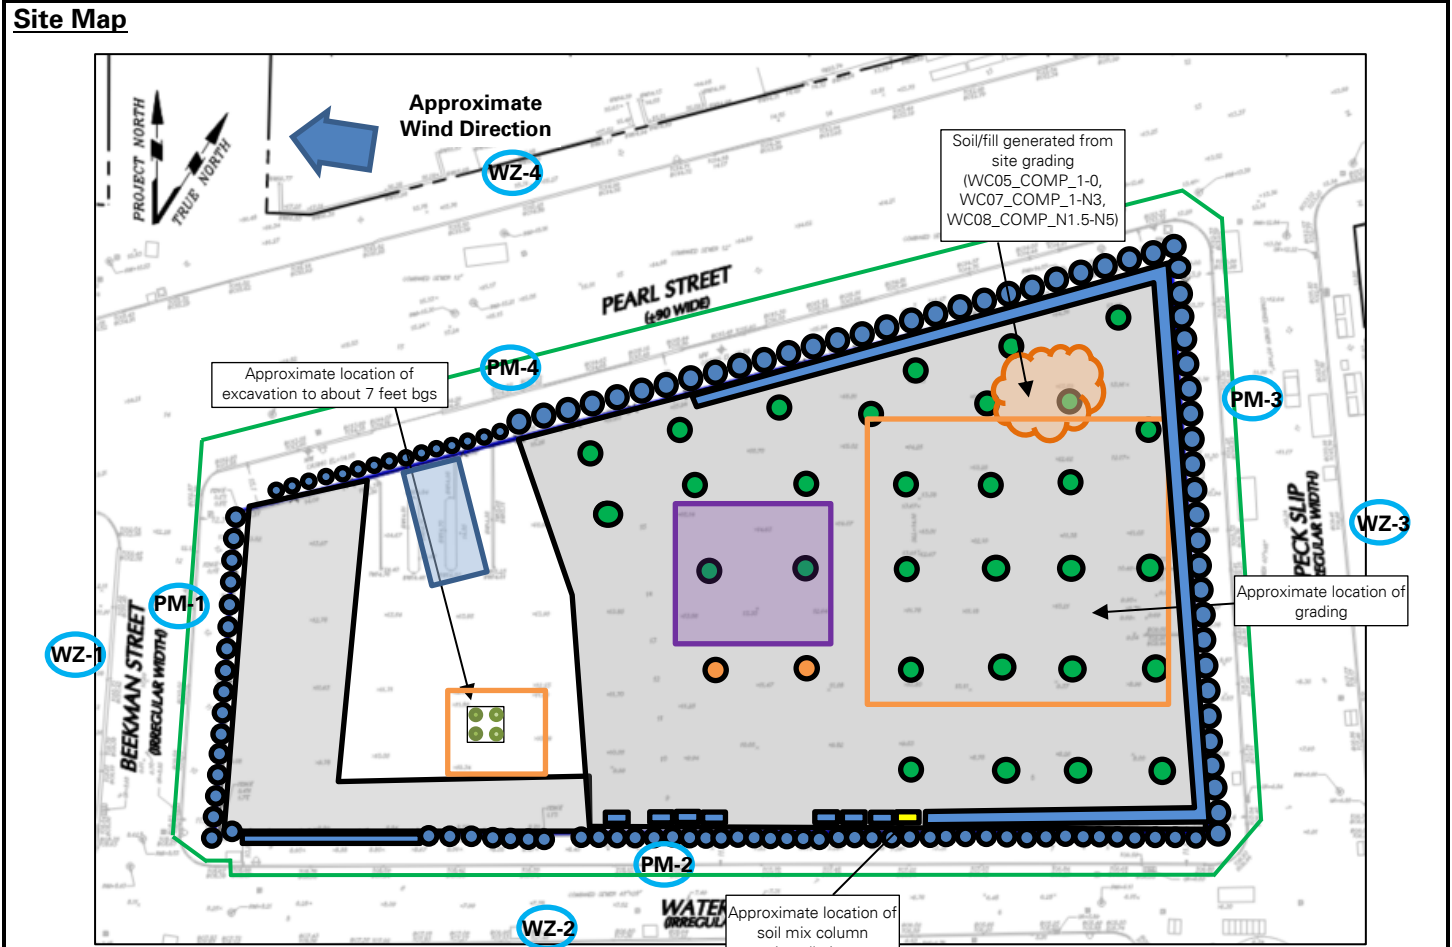

Legend:

- PM-1 Approximate Location of Air Monitoring Station
- Approximate Work Area
- Approximate Location of Installed Pile Cap
- Approximate Location of Foundation Piles Completed
- Approximate Location of Truck Tracking Pad
- Approximate Location of Underground Storage Tank
- Approximate Location of C&D Stockpile
- Approximate Location of Soil/Fill Stockpile
- Approximate Perimeter Construction Fence Location

Notes:

1) Locations of air monitoring stations are approximate.

- Approximate Location of Soldier Pile
- Approximate Location of Soil Mix Column Installed Today
- Approximate Location of Soil Mix Column Installed Previously
- Approximate Previous Excavation Area
- Approximate Excavation Area
- Approximate Location of Documentation Sample
- Approximate Location of Previously Collected Endpoint Sample
- Approximate Location of Imported Fill/Stone

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabiella DeGennaro LANGAN
-----	--	-----	-------------------------------------

SITE OBSERVATION REPORT

Select Site Photographs:



Photo 1: ECD excavating soil/fill in the western part of the site (facing east)



Photo 2: ECD loading a truck with soil/fill for off-site disposal (facing southeast)

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey, S. Simpson	By:	Gabriella DeGennaro LANGAN
-----	--	-----	--------------------------------------
