



DAILY SITE INSPECTION/FIELD ACTIVITY REPORT

BCP Site No.:	C224148	AUTHOR:	Sven Carlstrom
PROJECT NO.:	3165.0006R000	DATE:	1/26/2023
PROJECT:	Sunset Industrial Park 74 20 th St., Brooklyn, NY	WEATHER:	Cloudy, 33-52°F, Wind: W @ 17 mph, Humidity: 71%, Pressure: 29.59" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	7:00 AM – 3:30 PM

CONTRACTOR AND EQUIPMENT:	PERSONNEL PRESENT AT SITE AND AFFILIATION:
<u>Blakeslee (Superstructure/Crane Contractor)</u> <ul style="list-style-type: none"> Crawler Crane Manlift Forklift 	<u>Roux Environmental Engineering & Geology, D.P.C</u> Sven Carlstrom, Staff Assistant Scientist Robert McSweeney, Roux <u>Kingdom</u> Dawid Szmuc, Foreman <u>Suffolk</u> Caled Ho, Supervisor
<u>Kingdom (Excavation/Foundation Contractor)</u> <ul style="list-style-type: none"> Komatsu Excavator PC240LC Komatsu Mini Excavator Bobcat T770 Skid Steer 	

GENERAL COMMENTS:

As part of the of the NYSDEC-approved Remedial Action Work Plan and modifications, Roux Environmental Engineering and Geology D.P.C. (Roux) performed environmental oversight and operated air monitoring equipment in compliance with the Community Air Monitoring Plan (CAMP) during foundation installation activities.

RAWP Activities Performed:

- Blakeslee continued to operate a crawler crane on top of a designated crane pad constructed of RCA and wooden planks. The crane is being used to offload precast building materials from trailers and precast concrete erection continued onsite. Crane pad is located outside of the site perimeter to the west. Concrete erection stopped due to high winds at 10:30 AM.
- Kingdom continued installing vapor barrier in grid B3. Vapor barrier is being installed in accordance with manufacturer’s specifications and Roux will continuously inspect to certify proper installation.

CAMP Performed:

- CAMP was performed for the duration that Roux was onsite observing intrusive work. No exceedances of particulates or VOCs were recorded.

Other Relevant Comments or Issues:

- No relevant comments or issues.

Upcoming work activities:

- Blakeslee will continue precast concrete erection, moving south to north across the site. The superstructure erection phase of construction is estimated to continue through approximately February 2023.
- Kingdom will remain onsite through approximately the end of February 2023 to complete SSDS, vapor barrier, and foundation slab installation.
- Roux will continue to perform full-time oversight and CAMP during intrusive construction activities and perform inspections during installation of engineering controls.

Submitted By: Sven Carlstrom of Roux Environmental Engineering and Geology, D.P.C.	Approved By: Levi Curnutte of Roux Environmental Engineering and Geology, D.P.C.
---	---

DAILY SITE INSPECTION/FIELD ACTIVITY REPORT

BCP Site No.:	C224148	AUTHOR:	Sven Carlstrom
PROJECT NO.:	3165.0006R000	DATE:	1/26/2023
PROJECT:	Sunset Industrial Park 74 20 th St., Brooklyn, NY	WEATHER:	Cloudy, 33-52°F, Wind: W @ 17 mph, Humidity: 71%, Pressure: 29.59" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	7:00 AM – 3:30 PM

PHOTOS:



Photo 1: Facing south, superstructure status at beginning of day.



Photo 2: Detail of vertical vapor barrier installation against precast wall; applying double-sided tape prior to securing the vapor barrier to the tape with a termination bar in grid B3.

Submitted By: Sven Carlstrom of
Roux Environmental Engineering and Geology, D.P.C.

Approved By: Levi Curnutte of
Roux Environmental Engineering and Geology, D.P.C.

DAILY SITE INSPECTION/FIELD ACTIVITY REPORT

BCP Site No.:	C224148	AUTHOR:	Sven Carlstrom
PROJECT NO.:	3165.0006R000	DATE:	1/26/2023
PROJECT:	Sunset Industrial Park 74 20 th St., Brooklyn, NY	WEATHER:	Cloudy, 33-52°F, Wind: W @ 17 mph, Humidity: 71%, Pressure: 29.59" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	7:00 AM – 3:30 PM



Photo 3: Progress of vapor barrier installation along south side of grid B3.



Photo 4: Facing south, progress superstructure at the end of the day.

Submitted By: Sven Carlstrom of
Roux Environmental Engineering and Geology, D.P.C.

Approved By: Levi Curnutte of
Roux Environmental Engineering and Geology, D.P.C.

Site Map



Approximately extent of crane pad installation (located offsite)



Current area of active grading

Submitted By: Sven Carlstrom of
Roux Environmental Engineering and Geology, D.P.C.

Approved By: Levi Curnutte of
Roux Environmental Engineering and Geology, D.P.C.

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - Particulate Monitoring

Project: 74 20th Street, Brooklyn, NY
 Project Number: 3165.0006R000
 Project Manager: Levi Curnutte
 Location: 74 20th Street, Brooklyn, NY
 Date: 1/26/2023

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m ³)	Time	15-min Avg. (mg/m ³)	
7:00 AM	0.002	7:00 AM	0.002	0.000
7:15 AM	0.001	7:15 AM	0.002	0.001
7:30 AM	0.001	7:30 AM	0.003	0.002
7:45 AM	0.001	7:45 AM	0.004	0.003
8:00 AM	0.001	8:00 AM	0.006	0.005
8:15 AM	0.001	8:15 AM	0.010	0.009
8:30 AM	0.002	8:30 AM	0.007	0.005
8:45 AM	0.002	8:45 AM	0.010	0.008
9:00 AM	0.002	9:00 AM	0.012	0.010
9:15 AM	0.002	9:15 AM	0.009	0.007
9:30 AM	0.002	9:30 AM	0.004	0.002
9:45 AM	0.002	9:45 AM	0.003	0.001
10:00 AM	0.002	10:00 AM	0.003	0.001
10:15 AM	0.002	10:15 AM	0.003	0.001
10:30 AM	0.002	10:30 AM	0.003	0.001
10:45 AM	0.002	10:45 AM	0.005	0.003
11:00 AM	0.002	11:00 AM	0.009	0.007
11:15 AM	0.002	11:15 AM	0.006	0.004
11:30 AM	0.002	11:30 AM	0.012	0.010
11:45 AM	0.002	11:45 AM	0.005	0.003
12:00 PM	0.002	12:00 PM	0.003	0.001
12:15 PM	0.003	12:15 PM	0.004	0.001
12:30 PM	0.002	12:30 PM	0.004	0.002
12:45 PM	0.002	12:45 PM	0.006	0.004
1:00 PM	0.002	1:00 PM	0.006	0.004
1:15 PM	0.002	1:15 PM	0.006	0.004
1:30 PM	0.002	1:30 PM	0.007	0.005
1:45 PM	0.002	1:45 PM	0.007	0.005
2:00 PM	0.002	2:00 PM	0.010	0.008
2:15 PM	0.002	2:15 PM	0.008	0.006
2:30 PM	0.003	2:30 PM	0.008	0.005
2:45 PM	0.002	2:45 PM	0.007	0.005
3:00 PM	0.002	3:00 PM	0.005	0.003
3:15 PM	0.002	3:15 PM	0.005	0.003
3:30 PM	0.002	3:30 PM	0.006	0.004

mg/m³ - milligrams per meters cubed

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - VOC Monitoring



Project: 74 20th Street, Brooklyn, NY
 Project Number: 3165.0006R000
 Project Manager: Levi Curnutte
 Location: 74 20th Street, Brooklyn, NY
 Date: 1/26/2023

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:00 AM	0.01	7:00 AM	0.00	-0.01
7:15 AM	0.01	7:15 AM	0.01	0.00
7:30 AM	0.01	7:30 AM	0.02	0.01
7:45 AM	0.00	7:45 AM	0.01	0.01
8:00 AM	0.00	8:00 AM	0.01	0.01
8:15 AM	0.00	8:15 AM	0.02	0.02
8:30 AM	0.00	8:30 AM	0.01	0.01
8:45 AM	0.01	8:45 AM	0.01	0.00
9:00 AM	0.01	9:00 AM	0.00	-0.01
9:15 AM	0.01	9:15 AM	0.00	-0.01
9:30 AM	0.01	9:30 AM	0.01	0.00
9:45 AM	0.00	9:45 AM	0.00	0.00
10:00 AM	0.00	10:00 AM	0.00	0.00
10:15 AM	0.00	10:15 AM	0.00	0.00
10:30 AM	0.00	10:30 AM	0.00	0.00
10:45 AM	0.00	10:45 AM	0.00	0.00
11:00 AM	0.00	11:00 AM	0.00	0.00
11:15 AM	0.00	11:15 AM	0.00	0.00
11:30 AM	0.00	11:30 AM	0.00	0.00
11:45 AM	0.00	11:45 AM	0.00	0.00
12:00 PM	0.00	12:00 PM	0.00	0.00
12:15 PM	0.00	12:15 PM	0.00	0.00
12:30 PM	0.00	12:30 PM	0.00	0.00
12:45 PM	0.00	12:45 PM	0.00	0.00
1:00 PM	0.00	1:00 PM	0.00	0.00
1:15 PM	0.00	1:15 PM	0.00	0.00
1:30 PM	0.00	1:30 PM	0.00	0.00
1:45 PM	0.00	1:45 PM	0.00	0.00
2:00 PM	0.00	2:00 PM	0.00	0.00
2:15 PM	0.00	2:15 PM	0.00	0.00
2:30 PM	0.00	2:30 PM	0.00	0.00
2:45 PM	0.00	2:45 PM	0.00	0.00
3:00 PM	0.00	3:00 PM	0.00	0.00
3:15 PM	0.00	3:15 PM	0.00	0.00
3:30 PM	0.00	3:30 PM	0.00	0.00

VOC - Volatile Organic Compound
 PPM - parts per million

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - Meter Locations

Project: 74 20th Street, Brooklyn, NY
Project Number: 3165.0006R000
Project Manager: Levi Curnutte
Location: 74 20th Street, Brooklyn, NY
Date: 1/26/2023
Times: 7:00 AM to 3:30 PM

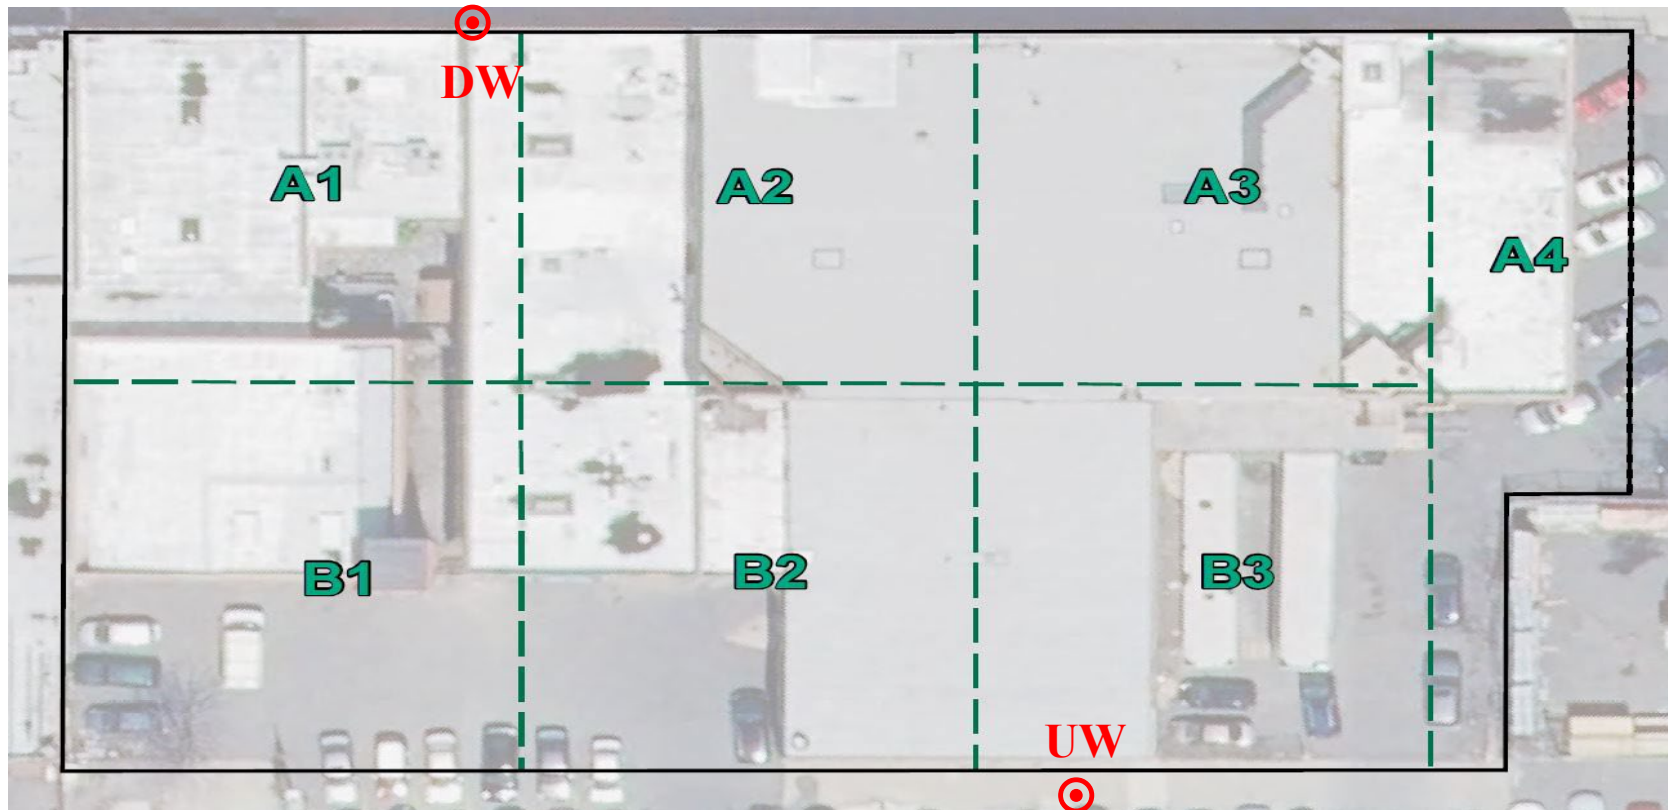

Notes: CAMP - Community Air Monitoring Program
UW - Upwind CAMP Station
DW - Downwind CAMP Station
