From: "Underhill, Scott" <Scott.Underhill@aecom.com>
To: John Spellman <jtspellm@gw.dec.state.ny.us>
CC: "Blazicek, Tracy" <tlblazicek@nyseg.com>
Date: 1/18/2012 8:22 PM
Subject: FW: NYSEG Mechanicville Central Avenue 3rd Quarterly Report
Attachments: Mechanicville Quarterly Report_Dec 2011.pdf

John/Tracy,

This was sent last night, but received a message stating that you did not receive. Please confirm receipt.

Thank you,

Scott

Scott Underhill, PE

Project Engineer

Environment

D 518.951.2208 M 518.396.7638

scott.underhill@aecom.com <mailto:scott.underhill@aecom.com>

AECOM

40 British American Blvd, Latham, NY 12110

T 518.951.2200 F 518.951.2300

www.aecom.com <http://www.aecom.com/>

From: Underhill, Scott
Sent: Tuesday, January 17, 2012 9:31 PM
To: John Spellman
Cc: Blazicek, Tracy
Subject: NYSEG Mechanicville Central Avenue 3rd Quarterly Report

John,

Attached is the third quarterly monitoring report for the NYSEG Mechanicville Central Ave former MGP site. Should you have any questions on this report, please let me know.

Also, as we discussed today, the title search has been completed and currently is being reviewed by NYSEG's legal department to ensure compliance with the Department's EE checklist. Once the review has been completed, the signed EE will be forwarded on to the Department for signature, or further work if the review indicates checklist has not been completed.

Thanks,

Scott

Scott Underhill, PE

Project Engineer

Environment

D 518.951.2208 M 518.396.7638

scott.underhill@aecom.com <mailto:scott.underhill@aecom.com>

AECOM

40 British American Blvd, Latham, NY 12110

T 518.951.2200 F 518.951.2300

www.aecom.com <http://www.aecom.com/>

AECOM
40 British American Boulevard
Latham, NY 12110
www.aecom.com

518-951-2200 tel
518-951-2300 fax

January 17, 2012 **SENT VIA ELECTRONIC MAIL**

Mr. John Spellman
Division of Environmental Remediation
New York State Department of Environmental Conservation
625 Broadway
Albany, New York 12233-7014

Subject: **Mechanicville Site Management**
3rd Quarterly Status Report (Oct-Dec 2011)
Site #: 546033
NYSEG – Mechanicville Central Avenue Former MGP Site

Dear Mr. Spellman,

On behalf of New York State Electric and Gas Corporation (NYSEG), AECOM has prepared this letter to describe events associated with site management activities at the Mechanicville Central Avenue Former Manufactured Gas Plant (Site) in Mechanicville, NY. The report summarizes activities performed at the Site between October 2011 and December 2011 in accordance with the site management plan (SMP) approved by the New York State Department of Conservation (NYSDEC) in April 2011.

The Mechanicville former MGP Site is located on North Central Avenue in Mechanicville, Saratoga County, NY. The Site is bordered on the east by North Central Avenue (formerly the Champlain Canal); on the south by Ferris Lane; on the west by G. A. Bove & Sons, a fuel distributor; and on the north by the Anthony Kill, a small tributary that flows eastward into the Hudson River.

The SMP requires select wells be measured for non aqueous phase liquids (NAPL) and the Anthony Creek be monitored for NAPL blebs quarterly for the first year; monitoring frequency will be evaluated thereafter. The SMP requires removal of NAPL from wells with greater than 6 inches (0.5 feet) of measureable NAPL; annual streambank stabilization observations; and groundwater sampling of selected wells once every two years until the results meet the groundwater standards, criteria, and guidance's (SCGs) for at least two consecutive sampling events. The first biannual groundwater sampling event is scheduled for the spring of 2012. Indoor air quality sampling is required prior to change in site usage or site development; no indoor air sampling was performed since no buildings are presently located at the site.

NAPL Monitoring

On December 12, 2011, monitoring wells TW-1, TW-2I, TW-3, MW-1D, MW-10D, MW-33D, MW-34D, MW-35I, MW-42D, MW-44I, and MW-45I were monitored to measure the presence of NAPL in each well. The well locations are depicted in Figure 1. A weighted string was lowered down the monitoring well casing until the bottom of the monitoring well was reached. The string was then removed from the well and the amount of NAPL present on the string was measured.

Table 1 summarizes the NAPL thickness in select monitoring wells in December 2011. Recent NAPL monitoring data is included in Attachment 1 as Tables 2 and 3 and historical NAPL monitoring data is included as Attachment 2.

Table 1 - Summary of NAPL Monitoring (December 2011)

Monitoring Well	NAPL Thickness (inches)	NAPL Removed (Gallons)
TW-1	0.5	0
TW-2I	0.25	0
TW-3	NM	0
MW-1D	NM	0
MW-10D	NM	0
MW-33D	0.25	0
MW-34D	NM	0
MW-35I	2.0	0
MW-42D	0.25	0
MW-44I	0.25	0
MW-45I	4.0	0

NM = No measureable NAPL observed

NAPL RECOVERY

Removal of NAPL did not occur this quarter as none of the wells had measureable NAPL thicknesses exceeding 6 inches. In June – the first quarter of monitoring – MW-35I and MW-45I were manually bailed to recover 5 gallons and 10 gallons of NAPL/water, respectively (estimated to be apprioximately 1.5 gallons and 4 gallons of only NAPL). Less than 6 inches of NAPL was measured in both these wells in last two quarters; therefore no NAPL was bailed. Measured NAPL in MW-35I showed a decrease in NAPL thickness from 4 inches to 2 inches over the past quarter while MW-45I showed an increase from non measured to 4 inches.

STREAMLINE AND CREEK OBSERVATION

The Anthony Kill was observed for signs of visible NAPL blebs on December 12, 2011. No NAPL blebs were observed at the location where the sediment removal occurred.

Dead wood and debris that blocked partial culvert during the heavy rainfall in September 2011, as documented in the second quarterly monitoring report (AECOM, November 18, 2011), were removed by Mechanicville's Department of Public Works. Pictures taken during the site inspection showing the cleared culverts are included in the Attachment 3.

STREAMBANK STABILIZATION

The stream bank appeared to be completely vegetated with grass and clovers. Some areas of the bank were gelatinous, but stable. The annual streambank analysis was performed in June 2011 and was not performed during this visit. However, beavers have removed 15 trees and damaged three others along the streambank; several undamaged trees remain. Pictures of the damaged trees are oncluded in the photo log in the Attachment 3.

BUILDING DEMOLITION

The former mechanic's shop and repair building were demolished prior to June as documented in the first quarterly monitoring event (AECOM, August 8, 2011) and presently remains in the same condition. The concrete building slab remains in place, preventing human exposure the underlying soils. No significant erosion was noticed at the site. Approximately 30 feet of fencing removed during the building demolition was re-installed during this quarter. A picture of the new fence is included in the photo log in Attachment 3.

If you have any questions please contact me at (518) 396-7638, or contact me via email at Scott.Underhill@aecom.com.

Yours sincerely,

Scott Underhill

Scott Underhill, P.E.
Project Manager

cc: T. Blazicek, NYSEG

FIGURES

MW-36I
MW-36D
MW-20D
A'
MW-35I
MW-34D
ANTHONY KILL
MW-32D
NORTH CENTRAL AVENUE
TW-4
MW-15IR
MW-22IR
TW-2I
TW-3
MW-29IR
TW-2S
MW-14
MW-14S
MW-14D
BLOCK / BRICK STRUCTURE
MW-46I
MW-2
MW-44I
MW-25I
MW-25D
MW-2I
MW-12S
MW-45I
MW-13
MW-12
TW-1
MW-30D
MW-30S
FERRIS LANE
MW-19I
MW-1I
MW-1
MW-1D
WEST WAY
JAMES STREET
MW-10D
MW-10
MW-10I
MW-40D
ELECTRIC SUB-STATION
A
BURKE STREET
EAST WAY
MW-42D
MW-41D
MW-37I
MW-37D
GROVE STREET
MW-17D
MW-17I
MW-17
MW-18
MW-33D
MW-38D
MW-38I
MW-39D
FRANCES STREET
WILLIAM STREET
MW-43D
MW-31S
MW-31D
CANAL S
N STREET

LEGEND

- MW-12S — MONITORING WELL LOCATION
- MW-12S — DECOMISSIONED MONITORING WELL
- WELL USED FOR NAPL MONITORING
- WELL USED FOR SAMPLING
- APPROXIMATE LOCATION OF FRACTURES
- EXTENT OF 2009 SOIL REMOVAL LIMITS
- X — ANTHONY KILL OBSERVATION LOCATION

0' 40' 80' 160'

AECOM

SITE MANAGEMENT PLAN

Figure 1

NEW YORK STATE ELECTRIC AND GAS
MECHANICVILLE, NEW YORK

FILE NAME:	DRN	PROJECT NO.	DATE	FIGURE NO.
	—	60135689	4 / 2011	3

Plotted By: meisterk
Layout-Sheet Name: SM-MW
Plot File Date Created: May/31/2011 2:19 PM

Filename: L:\WORK\94560\CADD\SITE_MANAGEMENT_PLAN\94560-POST-REMEDIATION-MW.DWG

ATTACHMENT 1

Table 2 - Summary of Quarterly NAPL Monitoring
Former NYSEG Mechanicville Central Avenue MGP Site
Mechanicville, New York

	NAPL Thickness (Inches)		
Date	6/20/2011 Q1: Apr-Jun 2011	9/23/2011 Q2: Jul-Sep 2011	12/12/2011 Q3: Oct-Dec 2011
TW-1	3.6	0.0	0.5
TW-2I	0.6	0.6	0.25
TW-3	0.6	0.6	0.0
MW-1D	0.0	0.0	0.0
MW-10D	1.0	1.0	0.0
MW-33D	0.0	0.0	0.0
MW-34D	0.0	0.5	2.0
MW-35I	9.6	4.0	2.0
MW-42D	0.6	0.5	0.25
MW-44I	0.2	0.5	0.25
MW-45I	33.6	0.0	4.0
Anthony Kill Observations			
Blebs Counted	0	0	0
Time spent watching river (min)	60	60	60
Bleb Frequency (blebs/hour)	0	0	0

Notes:
1) NAPL Thickness determined using weighted string.
2) NAPL is manually bailed if gauged thickness of NAPL is 6 inches (0.5 feet) or greater.
3) Rip Rap Elevation along Anthony Kill Bank is 76 ft msl.
4) NM - Not Measured.

Table 3 - Summary of NAPL Removal
Former NYSEG Mechanicville Central Avenue MGP Site
Mechanicville, New York

	NAPL Recovered (Gallons)					
Well\Date	Prior to Remediation Up to Feb 2008	Post remediation Jul-Dec 2009	1st Quarter Monitoring Apr-Jun 2011	2nd Quarter Monitoring Jul-Sep 2011	3rd Quarter Monitoring Oct-Dec 2011	TOTAL to Date
TW-1	NP	23.00	0.00	0.00	0.00	23.00
TW-2I	NP	1.00	0.00	0.00	0.00	1.00
TW-3	NP	0.00	0.00	0.00	0.00	0.00
MW-1D	0.53	0.00	0.00	0.00	0.00	0.53
MW-10D	113.89	0.00	0.00	0.00	0.00	113.89
MW-33D	0.00	0.00	0.00	0.00	0.00	0.00
MW-34D	0.00	0.00	0.00	0.00	0.00	0.00
MW-35I	0.93	NM	1.50	0.00	0.00	2.43
MW-42D	72.59	3.50	0.00	0.00	0.00	76.09
MW-44I	NP	1.25	0.00	0.00	0.00	1.25
MW-45I	NP	2.00	4.00	0.00	0.00	6.00
TOTAL	187.93	30.75	5.50	0.00	0.00	224.18

NAPL recovered from well when gauged thickness of NAPL is 6 inches or greater
NP - Well Not Present at time
NM - NAPL was not monitored

AECOM

ATTACHMENT 2

Summary of Weekly NAPL Observations
Former NYSEG Mechanicville Central Avenue MGP Site
Mechanicville, New York

	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)	NAPL Thickness (Inches)
Date	3/5/2010	3/12/2010	3/18/2010	3/25/2010	4/2/2010	4/9/2010	4/15/2010	4/22/2010	4/30/2010	5/6/2010	5/13/2010	5/20/2010	5/27/2010	10/4/2010	10/13/2010	10/21/2010	10/28/2010
MW-1D	0	0	<1	0	NM	<1	NM	NM	NM	NM	0	0	0	NM	NM	NM	NM
TW-1	1	<1	<1	<1	<1	1	<1	<1	3	2	2	1	1	NM	NM	NM	NM
TW-2I	2	1	1	2	2	2	3	<1	<1	<1	<1	<1	1	NM	NM	NM	NM
TW-3	0	0	0	0	0	0	0	<1	0	0	0	0	0	NM	NM	NM	NM
MW-30D	<1	0	<1	0	0	1	<1	0	NM	0	0	0	0	NM	NM	NM	NM
MW-42D	<1	0[2]	0	<1	<1	1.7	<1	<1	0	0	0	0	0	NM	NM	NM	NM
MW-44I	<1	0	0	<1	0	<1	0	0	0	0	0	0	0	NM	NM	NM	NM
MW-45I	<1	<1	<1	<1	<1	<1	<1	1	<1	2	<1	2	3	NM	NM	NM	NM
Anthony Kill Observations																	
Anthony Kill Water Elevation[3]	75.4	74.0	73.8	74.5	74.8	74.0	73.2	73.9	72.7	72.9	72.7	72.7	72.5	74.5	NM	NM	NM
Blebs Counted	0	0	24	15	36	23	5	3	21	9	106	120	71	0	0	0	0
Time spent watching river (min)	30	30	30	30	60	30	30	30	30	30	60	60	30	60	60	60	60
Bleb Frequency (blebs/hour)	0	0	48	30	36	46	10	6	42	18	106	120	142	0	0	0	0

Notes:
1) NAPL Thickness determined using weighted string.
2) Obstruction in well prohibited accurate reading.
3) Rip Rap Elevation along Anthony Kill Bank is 76 ft msl.
4) NM - Not Measured

Groundwater Elevations
Former Mechanicville MGP Site
Mechanicville, New York

		March 18, 2010		March 25, 2010		April 2, 2010		April 9, 2010		April 15, 2010		April 22, 2010		April 30, 2010		May 6, 2010		May 13, 2010		May 20, 2010		May 27, 2010	
Well	MP Elevation	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water	Depth to Water	Elevation of Water
MW 1	90.84	7.75	83.09	7.55	83.29	7.52	83.32	7.69	83.15	NM	NM	7.80	83.04	7.90	82.94	7.91	82.93	7.93	82.91	7.98	82.86	8.07	82.77
MW 1I	90.62	7.90	82.72	7.75	82.87	7.73	82.89	NM	NM	NM	NM	8.00	82.62	8.13	82.49	8.20	82.42	8.22	82.40	8.21	82.41	8.37	82.25
MW 1D	90.46	NM	NM	NM	NM	NM	NM	7.79	82.67	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 2	90.79	5.20	85.59	5.05	85.74	5.14	85.65	NM	NM	5.40	85.39	5.55	85.24	5.79	85.00	5.85	84.94	5.89	84.90	6.03	84.76	6.23	84.56
MW 10	91.66	8.93	82.73	8.95	82.71	8.77	82.89	8.99	82.67	NM	NM	9.20	82.46	9.35	82.31	9.35	82.31	9.35	82.31	9.41	82.25	9.51	82.15
MW 10I	92.21	10.30	81.91	10.95	81.26	10.03	82.18	10.05	82.16	NM	NM	10.35	81.86	10.45	81.76	10.50	81.71	10.50	81.71	10.51	81.70	10.61	81.60
MW 10D	92.73	9.10	83.63	9.60	83.13	9.86	82.87	9.99	82.74	NM	NM	10.20	82.53	10.33	82.40	10.42	82.31	10.48	82.25	11.64	81.09	10.56	82.17
MW 12	95.95	14.10	81.85	13.90	82.05	13.93	82.02	14.01	81.94	NM	NM	14.20	81.75	14.25	81.70	14.30	81.65	14.40	81.55	14.37	81.58	14.69	81.26
MW 12S	95.97	13.55	82.42	13.50	82.47	13.54	82.43	13.64	82.33	NM	NM	13.85	82.12	13.97	82.00	14.00	81.97	14.03	81.94	14.03	81.94	14.13	81.84
MW 13	96.04	OBS	OBS	14.10	81.94	14.13	81.91	14.23	81.81	NM	NM	14.40	81.64	14.51	81.53	14.55	81.49	14.55	81.49	14.58	81.46	14.68	81.36
MW 14	96.95	15.80	81.15	15.50	81.45	15.50	81.45	16.23	80.72	NM	NM	15.81	81.14	15.90	81.05	15.90	81.05	15.90	81.05	15.93	81.02	16.04	80.91
MW 14S	96.91	16.40	80.51	15.20	81.71	16.19	80.72	13.39	83.52	NM	NM	16.40	80.51	16.47	80.44	16.48	80.43	16.47	80.44	16.52	80.39	16.61	80.30
MW 14D	96.66	13.50	83.16	13.60	83.06	NM	NM	NM	NM	NM	NM	13.58	83.08	13.65	83.01	13.75	82.91	13.90	82.76	13.89	82.77	13.95	82.71
MW 15IR	87.47	3.50	83.97	6.30	81.17	6.92	80.55	6.31	81.16	6.60	80.87	6.70	80.77	6.89	80.58	6.86	80.61	6.98	80.49	7.00	80.47	7.31	80.16
MW 17	93.53	12.55	80.98	12.75	80.78	12.85	80.68	5.79	87.74	NM	NM	12.70	80.83	12.68	80.85	12.75	80.78	NM	NM	12.64	80.89	12.68	80.85
MW 17I	93.10	13.30	79.80	13.25	79.85	13.21	79.89	15.59	77.51	NM	NM	13.40	79.70	13.47	79.63	13.37	79.73	NM	NM	13.46	79.64	NM	NM
MW 17D	93.29	2.85	90.44	4.20	89.09	4.68	88.61	13.30	79.99	NM	NM	6.90	86.39	7.24	86.05	7.68	85.61	NM	NM	8.51	84.78	NM	NM
MW 18	93.54	12.00	81.54	11.75	81.79	11.88	81.66	12.77	80.77	NM	NM	12.10	81.44	12.25	81.29	12.04	81.50	NM	NM	12.28	81.26	12.34	81.20
MW 21	90.82	5.20	85.62	5.10	85.72	5.16	85.66	NM	NM	5.40	85.42	5.50	85.32	5.77	85.05	5.87	84.95	5.90	84.92	6.03	84.79	6.34	84.48
MW 22IR	87.05	7.50	79.55	7.20	79.85	7.31	79.74	7.33	79.72	7.70	79.35	7.75	79.30	7.86	79.19	7.88	79.17	7.89	79.16	7.94	79.11	8.21	78.84
MW 25S	96.03	14.55	81.48	14.45	81.58	14.36	81.67	14.41	81.62	NM	NM	14.62	81.41	14.70	81.33	14.69	81.34	14.72	81.31	14.74	81.29	14.82	81.21
MW 25I	88.74	14.85	73.89	14.70	74.04	14.60	74.14	14.71	74.03	NM	NM	14.85	73.89	15.00	73.74	14.99	73.75	15.03	73.71	15.02	73.72	15.11	73.63
MW 29IR	86.42	8.00	78.42	7.55	78.87	7.73	78.69	7.78	78.64	8.10	78.32	8.20	78.22	8.28	78.14	8.23	78.19	8.30	78.12	8.32	78.10	8.48	77.94
MW 30S	95.62	13.70	81.92	13.40	82.22	13.40	82.22	12.59	83.03	NM	NM	13.90	81.72	14.10	81.52	14.11	81.51	14.20	81.42	14.21	81.41	14.32	81.30
MW 30D	95.76	13.70	82.06	13.70	82.06	NM	NM	NM	NM	NM	NM	NM	NM	14.16	81.60	NM	NM	NM	NM	NM	NM	NM	NM
MW 32D	90.14	54.80	35.34	54.85	35.29	54.65	35.49	54.65	35.49	NM	NM	54.45	35.69	54.32	35.82	54.26	35.88	NM	NM	54.04	36.10	53.91	36.23
MW 33D	93.83	8.95	84.88	10.00	83.83	10.63	83.20	11.01	82.82	NM	NM	11.40	82.43	11.58	82.25	11.72	82.11	NM	NM	11.84	81.99	11.96	81.87
MW 34D	93.67	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 35I	80.43	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 40D	93.95	11.50	82.45	11.50	82.45	11.24	82.71	11.17	82.78	NM	NM	11.48	82.48	11.60	82.35	11.61	82.34	11.68	82.27	11.64	82.31	11.81	82.14
MW 42D	93.45	NM	NM	NM	NM	10.87	82.58	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 44I	87.37	5.20	82.17	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 45I	88.83	4.80	84.03	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW 46I	87.93	8.90	79.03	8.60	79.33	8.68	79.25	8.71	79.22	9.00	78.93	9.10	78.83	9.20	78.73	9.22	78.71	9.25	78.68	9.31	78.62	9.54	78.39
TW 1	89.33	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
TW 2S	86.34	6.05	80.29	8.55	77.79	5.90	80.44	5.59	80.75	6.15	80.19	6.28	80.06	6.37	79.97	6.36	79.98	6.36	79.98	6.41	79.93	6.57	79.77
TW 2I	86.25	MN	MN	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
TW 3	87.15	7.65	79.50	7.30	79.85	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
TW 4	87.17	8.20	78.97	7.90	79.27	7.95	79.22	7.98	79.19	8.30	78.87	8.38	78.80	8.48	78.69	8.50	78.67	8.55	78.62	8.60	78.57	8.82	78.35
Anthony Kill	75.92	2.08	73.84	1.40	74.52	1.11	74.81	1.92	74.00	2.75	73.17	2.00	73.92	3.20	72.72	3.00	72.92	3.25	72.67	3.25	72.67	3.42	72.50

Notes:
1) NM - Not Measured
2) OBS - Obstruction in well

TABLE 1
SUMMARY OF NAPL OBSERVATIONS

NYSEG
MECHANICVILLE, NEW YORK

Well Number	Screen Interval (feet bgs)	Type of Screen	Date Checked	NAPL Observation/Recovery (L)	Total NAPL Recovered To Date (L)
MW-10[5]	8.7 to 19.5	Screen	13-Jun-08	NAPL Not Present	Trace NAPL
MW-12	14.5 to 25.5	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-12S	11 to 26	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-14S	10 to 25	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-15S	5 to 10	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-16[1]	6 to 16	Screen	05-Jul-06	NAPL Not Present	NAPL Not Present
MW-17	13 to 23	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-21S	5 to 10	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-23S	7.5 to 12.5	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-25S	11 to 26	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-26S[5]	7.5 to 22.5	Screen	13-Jun-08	Trace NAPL	20.77
MW-30S	10 to 25	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-31S	8 to 18	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
RH-1S[1]	1.8 to 17.3	Screen	10-Jan-08	NAPL Not Present	72.035
MW-1[5]	11.6 to 16.85	Screen	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-10I[5]	22 to 43	Open Hole	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-11[1]	9.5 to 15	Screen	31-Aug-06	NAPL Not Present	NAPL Not Present
MW-13[2]	44.7 to 55.5	Screen	13-Jun-08	NAPL Not Present	Trace NAPL
MW-14[2]	30 to 41	Screen	13-Jun-08	NAPL Not Present	Trace NAPL
MW-15I	12.5 to 22.5	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-17I	23 to 45	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-18	28 to 38	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-19I	18 to 38.5	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-1I[5]	45 to 75	Open Hole	13-Jun-08	Trace NAPL	35.6
MW-2[5]	11.2 to 14.35	Screen	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-22I	17 to 32	Screen	18-Aug-08	NAPL Not Present	Trace NAPL
MW-25I	27 to 47	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-26I[5]	24.5 to 45.5	Open Hole	13-Jun-08	NAPL Not Present	Trace NAPL
MW-28I	15 to 25	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-29I	11.5 to 26	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-2I[5]	11.28 to 32.2	Open Hole	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-35I[3]	12.5 to 38	Open Hole	29-Feb-08	NAPL Not Present	3.51
MW-36I	20 to 45	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-37I	30 to 50	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-38I	90 to 120	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-10D[5]	82 to 114	Open Hole	13-Jun-08	0.25	431.39
MW-14D	91 to 121.7	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-15D	96 to 105.8	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-17D	121 to 142.5	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-1D[5]	121 to 155.2	Open Hole	13-Jun-08	NAPL Not Present	2
MW-20D[4]	90 to 110.1	Open Hole	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-21D	48.7 to 59.4	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-23D	56 to 80	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-29D	90 to 110	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-30D	90 to 121	Open Hole	18-Aug-08	Trace NAPL	7.82
MW-31D[2]	120 to 150	Screen	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-32D	91 to 111.5	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-33D	119.7 to 140.5	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-34D[4]	100 to 120.5	Open Hole	13-Jun-08	NAPL Not Present	NAPL Not Present
MW-36D	140 to 161	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-37D	155 to 185	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-38D	150 to 170.1	Open Hole	18-Aug-08	NAPL Not Present	Trace NAPL
MW-39D	130.4 to 150.4	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-40D	140 to 170	Screen	18-Aug-08	NAPL Not Present	23.771
MW-41D	120 to 140	Open Hole	18-Aug-08	NAPL Not Present	NAPL Not Present
MW-42D	140 to 175	Open Hole	25-Aug-08	2.6	274.97
MW-43D	120 to 150	Screen	18-Aug-08	NAPL Not Present	NAPL Not Present
RH-1D[5]	86.5 to 107.5	Open Hole	13-Jun-08	NAPL Not Present	NAPL Not Present

[1]Well was destroyed by snow plow (RH-1S was abandoned in December 2007).

[2]Well was inaccessible due to water in the top of the casing.

[3]Well could not be located due to presence of debris and sediment.

[4]Well was inaccessible due to overgrown brush.

[5]Well was inaccessible. NYSEG crew working around well.

TABLE 2
SUMMARY OF GROUNDWATER ELEVATIONS

NYSEG
MECHANICVILLE, NEW YORK

WELL NUMBER	Water Level (feet msl)																								
	10/10/2001	10/31/2001	12/4/2001	1/7/2002	2/6/2002	3/6/2002	4/3/2002	5/1/2002	6/12/2002	7/2/2002	8/5/2002	9/6/2002	10/3/2002	11/7/2002	12/2/2002	1/9/2003	1/30/2003	4/3/2003	5/9/2003	6/5/2003	7/3/2003	8/15/2003	9/9/2003	10/10/2003	11/7/2003	12/10/2003
MW-10	80.70	80.58	80.79	80.70	81.04	81.07	81.53	81.35	81.11	80.96	80.13	80.56	80.90	80.93	80.93	NM	80.25	81.28	80.73	80.90	80.54	81.16	80.66	80.64	81.01	80.73
MW-12	80.10	79.99	79.88	79.87	80.14	80.17	80.49	80.51	79.48	80.37	80.13	80.27	80.56	80.66	80.71	80.39	80.10	80.89	80.53	80.65	80.27	80.88	80.38	80.28	80.70	81.36
MW-12S	78.60	78.52	78.59	78.47	78.79	78.83	79.06	79.48	79.70	79.65	79.19	79.36	79.62	79.77	79.81	79.52	79.23	80.07	79.72	79.88	79.44	79.85	79.57	79.53	79.96	79.62
MW-14S	78.30	78.18	78.30	78.12	78.44	78.45	78.70	78.95	79.05	79.05	78.70	78.81	78.99	79.10	79.07	78.85	78.51	79.27	78.96	79.18	78.82	79.35	78.98	78.92	79.29	79.01
MW-15S	79.20	79.54	79.72	79.70	79.86	79.71	80.00	80.06	79.99	79.99	79.76	79.84	79.92	80.04	80.07	80.10	80.00	80.31	80.18	80.23	80.07	80.53	80.16	80.08	80.36	80.21
MW-16	85.78	85.82	86.10	85.95	86.20	86.16	86.47	86.36	86.41	86.23	85.98	86.34	86.52	86.52	86.60	NM	NM	86.59	86.29	86.36	86.00	86.92	86.12	86.03	86.50	86.23
MW-17	79.01	78.73	78.68	79.01	79.29	79.39	79.73	79.64	79.67	79.60	79.23	79.39	79.68	79.72	79.81	79.59	79.20	79.91	79.73	79.84	79.53	80.03	79.67	79.59	79.95	79.75
MW-21S	80.19	80.32	80.90	80.59	80.80	80.84	81.28	81.97	80.95	80.94	80.70	83.84	80.93	81.82	81.09	77.76	80.66	82.13	80.84	80.98	80.63	81.47	79.79	80.62	81.47	80.75
MW-23S	77.38	77.25	77.44	77.15	77.51	77.55	77.88	78.10	78.06	78.07	77.77	77.37	78.07	78.16	78.04	77.90	77.43	78.35	77.96	78.16	77.88	78.43	78.11	77.95	78.34	77.83
MW-25S	78.69	78.62	78.79	78.56	79.39	79.40	80.25	80.35	80.30	80.19	75.60	80.03	80.32	80.46	80.44	80.18	79.51	80.81	80.33	80.50	79.97	80.74	80.17	80.04	80.57	80.14
MW-26S	79.80	79.65	79.81	79.68	80.07	80.11	80.51	80.97	80.93	80.83	80.22	80.39	80.82	81.05	81.11	NM	80.45	81.50	81.04	81.11	80.68	NM	NM	80.63	80.95	NM
MW-30S	79.28	79.02	79.13	79.01	79.38	79.44	79.73	80.20	80.28	80.18	79.70	79.93	80.25	80.32	80.36	80.13	79.78	80.78	80.37	80.49	80.15	80.81	80.14	80.08	80.55	80.17
MW-31S	80.81	80.74	80.67	80.70	80.72	80.94	81.12	80.95	81.10	81.08	80.97	81.08	81.08	81.05	81.13	81.06	81.01	81.18	81.43	81.53	81.34	80.59	81.30	81.22	81.39	81.39
RH-1S	82.09	82.06	81.78	82.24	82.56	82.61	82.87	82.69	82.60	82.49	81.82	81.99	82.46	82.57	82.57	82.49	82.17	NM	82.59	83.65	NM	82.64	82.27	82.18	82.50	NM
MW-1	82.35	82.34	82.60	82.57	82.76	82.80	82.95	82.89	82.78	82.67	82.23	82.41	82.58	82.78	82.74	82.65	82.33	82.98	82.70	82.72	82.45	82.74	82.46	82.38	82.74	82.63
MW-10I	79.35	79.22	79.35	79.29	79.59	79.67	79.93	80.34	80.47	80.40	79.93	80.11	80.37	80.49	80.44	80.20	79.86	80.70	80.37	80.53	80.12	80.70	80.20	80.16	80.56	80.33
MW-11	81.06	81.20	81.67	81.65	81.94	81.87	82.22	82.12	81.90	81.75	81.48	81.38	82.16	82.36	82.22	NM	NM	81.88	81.83	81.99	81.59	82.64	81.78	81.71	82.30	81.86
MW-13	78.56	78.49	78.55	78.54	78.76	78.82	79.03	79.47	80.63	79.49	79.12	79.37	79.52	79.65	79.73	79.54	79.63	79.90	79.63	79.69	79.35	80.07	79.60	79.48	79.82	79.44
MW-14	78.24	78.16	78.22	78.09	78.42	78.45	78.70	79.07	79.23	79.15	78.74	78.89	79.11	79.28	79.33	79.06	78.75	79.55	79.18	79.37	78.88	79.54	79.02	79.01	79.43	79.13
MW-15I	78.22	78.23	78.49	78.35	78.54	78.60	78.75	78.85	78.91	78.85	78.59	78.84	78.91	79.09	79.05	78.89	77.62	81.96	78.98	78.91	78.66	79.39	80.19	78.90	79.29	78.85
MW-17I	78.21	78.12	78.19	78.47	78.78	78.85	79.22	79.18	79.23	79.15	78.74	78.86	80.53	79.22	79.31	79.17	78.70	81.94	79.33	79.37	79.07	79.57	79.19	79.09	79.46	79.24
MW-18	78.69	78.54	78.64	78.67	78.92	79.01	79.27	79.64	79.72	79.67	79.23	79.44	79.69	79.77	79.85	79.61	79.22	76.64	79.76	79.86	79.50	80.07	79.63	79.54	79.94	79.66
MW-19I	86.61	86.74	87.15	86.97	87.30	87.30	87.61	87.35	87.38	NM	NM	87.23	87.47	87.41	87.47	NM	NM	85.21	87.17	87.17	86.81	87.82	86.92	NM	87.36	87.10
MW-1I	NI	NI	NI	NI	NI	NI	NI	NI	82.06	81.17	80.56	80.78	79.96	81.12	81.23	81.02	80.69	81.60	81.09	81.19	80.75	81.43	80.81	NM	81.18	80.89
MW-2	83.35	83.39	83.92	83.58	84.10	84.22	84.58	84.54	84.34	84.23	83.59	84.03	84.20	84.50	84.38	84.35	83.46	85.01	84.30	84.41	83.90	84.87	84.03	83.90	84.46	84.10
MW-22I	74.97	74.99	75.15	74.89	75.24	75.31	75.89	75.81	76.65	76.45	75.81	75.26	76.23	76.53	76.61	76.26	75.75	76.85	76.33	76.52	75.80	77.16	76.16	76.01	76.75	75.30
MW-25I	78.46	78.37	78.43	78.31	78.64	78.69	78.93	79.30	79.47	79.40	79.00	79.18	79.39	79.52	79.55	79.32	NM	79.78	79.41	79.58	79.17	79.80	79.32	79.29	79.70	79.35
MW-26I	79.49	79.38	79.50	79.38	79.72	79.79	80.03	80.84	80.74	80.67	80.09	80.38	80.67	80.77	80.70	80.45	80.15	80.97	80.55	80.69	80.29	80.93	80.42	80.36	80.79	80.47
MW-28I	73.85	74.10	74.15	73.99	74.25	74.43	74.92	74.85	74.93	74.49	74.02	74.24	74.39	74.73	74.83	74.89	74.48	75.29	74.77	74.78	74.09	75.33	74.16	74.11	74.90	74.39
MW-29I	75.06	75.02	75.09	74.99	75.21	75.22	75.76	75.87	76.02	75.82	75.38	75.49	75.59	75.87	75.84	75.69	75.29	76.19	75.74	75.85	75.29	76.28	75.47	75.46	76.04	75.78
MW-2I	83.34	83.37	83.95	83.57	84.14	84.21	84.70	84.50	84.54	84.25	83.46	84.20	84.48	84.44	84.70	84.33	84.14	85.01	84.47	84.52	83.89	85.06	83.98	83.89	84.58	84.01
MW-35I	NI	74.22	74.78	74.27	74.98	75.00	75.56	75.56	75.57	75.42	74.68	74.79	75.20	75.42	75.65	76.05	75.19	75.75	75.27	75.50	75.75	76.15	75.14	75.14	75.89	NM
MW-36I	NI	NI	NI	NI	NI	NI	NI	NI	88.63	75.70	81.63	81.80	82.16	82.55	82.71	82.70	82.38	84.11	86.23	85.38	84.27	82.78	82.36	87.71	82.90	82.55
MW-37I	NI	NI	NI	NI	NI	NI	NI	NI	NM	77.53	82.23	82.50	82.64	83.03	83.00	82.67	NM	82.96	82.30	82.48	82.06	82.86	82.35	82.15	82.73	82.41
MW-38I	NI	NI	NI	NI	NI	NI	NI	NI	73.39	73.07	72.26	71.84	72.04	72.72	72.82	72.64	NM	73.23	72.82	72.92	72.02	73.30	72.08	66.62	72.98	72.44
MW-10D	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	-18.07	NM	NM	NM	-17.15	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW-14D	-2.46	22.79	47.02	61.96	67.69	72.14	75.53	77.96	80.15	80.76	81.32	81.56	81.79	82.10	82.46	82.56	82.50	61.16	77.61	80.81	81.78	82.29	82.46	82.28	82.54	82.69
MW-15D	-3.78	18.40	44.22	59.96	67.27	71.24	73.51	74.68	75.82	76.11	76.29	76.32	76.50	76.87	77.58	77.31	77.01	32.31	51.51	60.93	67.13	71.73	73.17	74.17	74.97	75.62
MW-17D	-13.08	35.65	73.71	78.79	79.18	79.47	79.79	79.56	80.22	80.33	80.05	80.09	79.49	80.62	80.84	80.85	80.56	82.28	80.34	80.55	80.19	80.76	80.39	80.34	80.86	80.78
MW-1D	NI	NI	NI	NI	NI	NI	NI	NI	NI	-59.63	-59.33	-59.16	-58.81	-58.56	-58.38	NM	NM	NM	-50.86	-50.67	-50.45	-49.44	-50.09	-49.96	-49.79	-49.64
MW-20D	NI	79.03	79.36	79.72	80.00	80.34	81.19	80.44	80.84	80.39	79.52	79.63	80.18	80.51	81.13	80.82	80.37	81.44	80.69	80.61	79.88	81.40	80.13	79.99	81.09	80.62
MW-21D	76.63	76.69	76.93	76.94	77.17	77.46	77.98	77.89	78.09	77.70	76.98	76.96	77.91	78.07	78.20	81.10	77.49	78.86	77.95	77.97	77.22	78.57	77.48	77.40	78.28	76.66
MW-23D	5.63	7.55	10.60	13.73	16.36	18.77	20.77	22.60	25.33	26.61	28.46	29.99	31.10	32.48	33.48	34.96	35.69	8.73	11.24	13.36	15.55	18.61	20.37	22.22	23.92	25.87
MW-29D	80.25	80.43	80.80	81.12	81.28	81.46	82.13	81.67	81.85	81.43	80.85	81.16	81.59	81.97	82.46	82.34	81.66	82.28	81.97	81.98	81.45	82.61	81.61	81.50	82.33	81.84
MW-30D	22.72	26.58	31.46	36.90	41.29	45.32	49.53	52.84	58.29	60.71	63.96	66.86	68.97	71.39	72.87	74.46	75.17	80.76	80.44	80.26	79.99	80.17	80.16	80.02	80.94	79.90
MW-31D	80.42	80.33	80.52	80.49	80.74	80.77	81.02	80.68	80.68	80.78	80.46	80.69	80.90	80.78	80.59	80.68	67.69	80.99	80.74	80.75	80.67	81.01	80.99	80.95	81.01	80.78
MW-32D	-19.02	-15.78	-12.06	-9.12	-6.85	-4.80	-3.28	-2.13	0.15	1.24	2.98	4.36	5.51	6.76	7.59	NM	9.02	NM	-20.94	-19.95	-18.75	-16.79	-15.48	-14.16	-13.03	-11.93
MW-33D	34.25	51.18	67.43	74.62	77.09	78.35	79.00	80.24	80.56	80.55	79.99	80.16	80.45	80.53	80.67	80.56	NM	80.81	80.54	75.52	79.76	80.94	79.41	80.25	80.76	80.45
MW-34D	81.05	81.19	81.56	81.86	81.96	82.15	82.88	82.39	82.72	82.28	81.72	82.26	83.00	83.01	83.55	NM	NM	83.04	82.78	82.74	82.19	83.44	82.40	82.33	83.16	82.71
MW-36D	NI	NI	NI	NI	NI	NI	NI	NI	82.63	82.50	82.17	82.21	82.45	82.78	82.94	82.77	83.02	83.41	83.02	83.01	NM	83.66	82.69	87.91	83.40	82.90
MW-37D	NI	NI	NI	NI	NI	NI	NI	NI	NI	88.87	88.25	87.60	88.60	88.62	88.55	88.31	88.08	89.19	88.69	88.91	88.46	89.52	88.54	88.32	89.06	88.65
MW-38D	NI	NI	NI	NI	NI	NI	NI	NI	73.58	72.85	72.52	72.09	72.37	72.92	73.04	72.82	73.51	73.41	73.04	73.08	72.24	73.45	72.33	66.93	73.17	72.62
MW-39D	NI	NI	NI	NI	NI	NI	NI	NI	75.50	75.42	75.28	75.42	75.97	75.68	75.85	75.69	76.59	75.95	75.70	75.79	75.30	76.12	75.48	75.45	76.04	75.79
MW-40D	NI	NI	NI	NI	NI	NI	NI	NI	80.56	80.57	80.03	80.20	80.37	80.60	81.01	80.91	NM	79.14	81.05	81.14	80.63	81.28	80.58	80.59	81.14	80.89
MW-41D	NI	NI	NI	NI	NI	NI	NI	NI	81.39	78.25	77.00	77.83	78.08	78.43	78.73	78.00	77.82	78.29	78.03	78.18	77.68	78.59	77.97	77.94	78.60	78.33
MW-42D	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	-30.88	50.81	62.74	NM	71.04	NM	NM	NM	NM	NM	NM	NM
MW-43D	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	NI	87.20	86.07	86.54	87.36	86.79	86.89	86.43	87.55	86.59	86.46	87.12	86.75
RH-1D	-20.65	-19.16	-18.83	-21.31	-20.98	-20.68	-20.37	-19.93	-19.47	-19.22	-18.84	-18.50	-18.22	-17.79	-17.51	-17.04	-16.78	NM	-15.94	-15.64	-15.31	-14.34	-14.02	-11.48	-11.15	-10.80
SG-1	72.32	72.40	NM	72.65	73.15	73.32	73.98	73.82	73.82	75.42	72.24	72.19	NM	73.37	73.43	NM	NM	74.23	72.77	73.39	72.00	NM	NM	NM	NM	NM
SG-2	73.20	73.27	73.44	73.52	73.87	73.97	74.52	74.37	74.37	73.75	73.19	73.13	NM	NM	NM	NM	NM	74.87	74.32	74.22	73.29	NM	NM	NM	NM	NM
SG-3	74.22	74.28	74.37	74.57	74.67	74.77	75.22	75.07	75.11	75.68	74.25	74.17	NM	74.82	74.88	NM	NM	75.57	75.63	74.97	NM	NM	NM	NM	NM	NM

TABLE 2
SUMMARY OF GROUNDWATER ELEVATIONS

NYSEG
MECHANICVILLE, NEW YORK

WELL NUMBER	Water Level (feet msl)																					
	1/8/2004	2/2/2004	3/8/2004	4/16/2004	5/6/2004	6/8/2004	7/20/2004	8/10/2004	9/23/2004	10/4/2004	11/18/2004	12/14/2004	1/5/2005	2/17/2005	3/22/2005	4/8/2005	5/4/2005	5/27/2005	6/16/2005	7/27-28/2005	8/18/2005	9/23/2005	10/20/2005
MW-10	80.99	80.27	80.58	80.90	80.87	81.03	81.10	80.77	80.88	80.69	80.45	81.14	80.71	81.77	80.96	81.29	80.79	80.74	80.98	80.49	80.36	80.32	80.76
MW-12	80.65	80.19	80.72	79.64	NM	80.48	80.75	80.46	80.67	80.41	80.21	80.76	80.36	NM	80.47	79.75	80.42	80.40	80.46	80.27	80.23	81.10	80.53
MW-12S	79.84	79.23	80.24	80.53	79.55	79.59	79.75	79.59	79.80	79.65	79.40	79.92	79.56	79.65	79.66	79.86	79.50	79.53	79.61	79.39	79.27	78.87	79.47
MW-14S	79.19	78.56	79.23	78.98	78.93	79.00	79.25	79.15	79.26	79.11	78.83	79.33	78.99	79.17	79.17	79.39	78.95	79.03	79.08	78.88	78.87	78.81	79.24
MW-15S	80.42	80.08	80.46	80.37	80.32	80.25	80.47	80.34	80.32	80.32	80.28	80.49	80.46	80.61	80.48	80.46	80.32	80.45	80.38	80.28	80.41	80.33	80.47
MW-16	86.47	85.91	NM	86.12	86.16	86.34	86.46	86.28	86.50	86.20	85.92	86.58	86.12	NM	NM	86.51	86.10	85.99	86.21	86.37	NM	85.88	86.38
MW-17	79.96	79.53	80.05	79.79	79.75	79.91	79.97	79.79	80.00	79.85	79.61	79.98	79.78	79.79	79.93	80.01	79.79	79.79	79.98	79.58	79.40	80.34	79.77
MW-21S	81.23	80.45	81.43	81.19	81.07	80.78	82.05	80.88	81.06	80.85	80.62	81.73	81.84	81.10	81.61	81.57	80.82	80.91	80.91	NM	80.76	80.71	81.10
MW-23S	78.22	77.43	78.24	77.94	77.91	78.01	78.39	78.22	78.31	78.14	77.77	78.35	78.05	78.24	78.34	78.30	77.98	78.02	78.17	78.00	78.00	77.93	78.26
MW-25S	80.54	79.66	80.60	80.35	78.77	80.32	80.64	80.31	80.48	80.18	79.93	79.58	80.18	80.32	80.33	80.59	80.22	80.22	80.28	79.89	79.91	79.75	80.40
MW-26S	81.43	80.51	81.18	NM	81.02	81.19	81.10	80.95	81.06	80.84	80.66	81.72	81.01	81.02	81.06	81.61	81.05	80.96	80.91	80.78	80.33	80.30	81.01
MW-30S	80.50	79.82	80.57	80.27	80.18	80.25	80.63	80.21	80.61	80.39	80.21	80.74	80.30	80.55	80.41	80.77	80.26	80.18	80.36	80.30	80.19	80.09	80.59
MW-31S	81.50	81.37	81.40	81.38	81.26	81.36	81.37	81.18	81.32	81.23	81.19	81.46	81.34	81.46	81.49	81.45	81.29	81.24	81.41	80.97	80.87	80.80	80.47
RH-1S	82.69	81.99	83.09	NM	NM	NM	NM	NM	NM	82.32	82.11	82.72	NM	NM	NM	82.65	NM	NM	NM	82.15	81.95	81.99	81.35
MW-1	82.84	82.33	82.79	82.73	82.64	82.56	82.73	82.50	82.70	82.53	82.39	82.81	82.36	82.76	82.43	82.68	82.53	82.53	82.48	82.11	82.05	82.26	82.58
MW-10I	80.53	79.97	80.57	80.25	80.23	80.23	80.46	80.22	80.45	80.26	81.02	80.56	80.21	80.34	80.50	80.48	80.11	80.21	80.32	79.97	79.83	79.79	80.22
MW-11	82.22	81.69	NM	82.06	81.96	81.76	82.33	81.90	82.22	81.97	81.73	82.43	82.16	82.20	NM	82.36	81.88	82.01	82.06	81.57	81.69	81.70	82.16
MW-13	79.88	79.09	79.85	79.48	79.42	79.46	79.59	79.47	79.70	79.53	79.29	79.77	79.42	79.49	79.48	79.85	79.48	79.41	79.58	79.21	79.17	79.11	79.80
MW-14	79.38	NM	79.47	79.05	78.99	79.04	79.24	79.13	79.30	79.16	78.91	79.46	79.04	79.19	79.13	79.33	79.00	79.00	79.09	78.79	78.74	78.67	79.16
MW-15I	77.97	77.48	79.19	78.90	78.90	79.03	79.42	79.16	78.39	79.22	79.17	79.52	79.40	78.56	78.42	78.33	78.24	78.40	78.44	78.23	78.32	78.24	78.49
MW-17I	NM	NM	79.54	79.24	79.21	79.37	79.44	79.29	79.57	79.33	79.05	78.66	79.23	79.18	79.39	79.64	79.30	79.22	79.43	79.08	78.89	78.87	79.39
MW-18	79.88	79.26	81.33	79.58	79.51	79.88	79.85	79.59	79.88	79.72	79.48	79.93	79.54	79.63	79.68	79.80	79.47	79.54	79.70	79.38	79.26	79.22	79.71
MW-19I	87.36	86.73	85.37	87.14	87.07	87.30	87.43	87.19	87.42	87.06	86.73	87.50	86.98	87.07	NM	86.52	87.08	86.98	87.18	86.87	86.77	86.70	87.29
MW-1I	81.13	80.41	81.15	80.93	80.88	80.93	81.04	80.86	81.05	80.88	80.62	81.23	80.81	80.97	80.91	81.18	80.75	80.77	80.87	80.60	80.41	80.31	80.87
MW-2	84.49	83.89	84.97	84.41	84.32	84.29	84.68	84.14	84.36	84.16	83.86	84.59	83.73	84.49	84.55	84.54	84.16	84.24	84.32	83.79	83.87	83.80	84.24
MW-22I	75.61	74.87	76.21	75.45	75.35	75.37	75.64	75.33	75.70	75.33	75.06	76.21	75.46	75.72	75.59	75.89	75.13	75.27	75.42	74.96	NM	74.76	75.65
MW-25I	79.60	78.93	79.58	79.27	NM	NM	79.80	79.26	79.55	79.35	79.07	79.62	79.25	79.78	79.36	79.72	79.22	79.29	79.32	79.12	79.03	78.95	79.43
MW-26I	80.68	80.11	80.78	80.49	80.43	80.45	80.71	80.43	80.69	80.48	80.23	79.78	80.40	80.48	80.51	80.71	80.27	80.37	80.39	80.16	80.08	80.00	80.44
MW-28I	74.71	73.96	75.45	74.61	74.41	74.37	74.70	74.23	74.64	74.24	74.09	75.24	74.64	74.96	74.75	74.98	74.45	74.26	74.61	73.78	73.74	73.76	74.49
MW-29I	75.82	75.10	76.13	75.59	75.48	75.52	75.82	75.52	75.79	75.47	75.21	76.12	75.55	75.80	75.64	75.91	75.44	75.47	75.64	75.21	75.15	75.03	75.65
MW-2I	84.57	83.58	84.82	84.33	84.25	84.50	84.60	84.51	84.63	84.19	83.84	84.80	84.79	84.23	84.41	85.08	84.16	84.11	84.32	83.61	83.84	83.87	84.70
MW-35I	NM	NM	NM	NM	75.15	75.30	75.68	75.22	75.65	75.19	74.85	76.26	75.32	75.49	75.25	75.76	75.29	75.28	75.42	74.77	74.90	74.68	75.58
MW-36I	NM	NM	82.06	82.45	82.34	82.55	82.16	82.56	82.67	82.41	82.01	82.03	82.40	82.75	82.75	82.84	82.73	82.71	82.82	82.66	82.07	81.75	82.69
MW-37I	82.70	82.13	83.09	82.70	82.64	82.35	83.37	82.32	82.71	82.40	82.14	83.06	82.37	82.73	82.62	82.90	82.55	82.77	82.70	82.21	82.38	82.16	82.43
MW-38I	NM	NM	73.24	72.43	72.34	72.46	72.52	71.75	72.64	72.19	71.98	73.01	72.39	NM	69.53	72.82	72.25	72.20	72.53	71.86	71.57	71.54	72.45
MW-10D	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW-14D	82.88	82.39	82.10	82.55	78.55	82.60	82.19	81.65	82.73	82.69	82.27	82.62	82.54	83.00	82.46	82.73	82.64	82.45	82.44	82.46	82.13	81.95	82.30
MW-15D	76.06	76.15	76.24	76.52	76.52	76.65	76.53	76.70	76.87	76.80	76.52	76.68	76.63	76.69	76.54	76.84	76.72	76.53	76.45	76.54	76.32	76.16	76.46
MW-17D	81.87	81.18	81.35	81.39	81.29	81.58	81.41	81.96	81.74	81.66	81.12	82.00	81.49	81.88	81.20	81.85	81.30	81.26	81.49	81.45	81.20	82.21	81.70
MW-1D	-49.50	-49.39	-48.20	-48.03	-47.92	-47.58	-47.66	-47.60	-47.46	-47.34	-47.19	-47.12	-46.75	-46.29	-35.22	-34.91	-34.77	-34.94	-34.79	-34.57	-34.48	-34.40	-34.27
MW-20D	80.99	80.04	80.80	80.49	80.37	80.79	80.33	80.62	80.88	80.49	79.98	81.32	80.34	NM	80.40	81.33	80.39	80.06	80.29	80.05	79.52	79.50	80.82
MW-21D	77.82	77.48	78.12	77.58	77.53	77.66	77.67	77.68	77.97	77.60	77.29	78.26	77.59	77.81	77.69	78.01	77.34	77.42	77.52	77.18	77.26	76.90	77.99
MW-23D	27.47	28.62	30.12	31.69	32.37	33.51	34.71	35.35	36.78	37.01	38.25	38.93	39.47	40.70	41.43	41.76	42.30	42.77	43.26	43.81	44.13	45.40	45.02
MW-29D	82.10	81.14	82.08	81.68	81.72	81.92	81.81	82.04	82.83	81.82	81.51	82.55	81.79	81.93	81.68	82.47	81.61	81.52	81.87	81.39	81.16	81.17	82.02
MW-30D	80.45	79.90	79.78	80.05	NM	80.04	80.13	80.37	80.73	80.22	79.69	80.11	79.84	79.87	79.64	80.08	79.87	79.72	80.31	80.18	79.78	79.60	80.30
MW-31D	81.12	80.65	80.96	81.09	80.96	80.78	80.61	80.69	83.23	81.24	81.08	81.12	80.85	81.16	81.10	80.84	80.79	80.58	80.82	80.27	80.14	80.03	80.33
MW-32D	-11.15	-10.32	-9.78	-8.87	-8.41	-7.40	NM	-4.74	-3.25	-2.98	-1.78	-1.18	-0.42	0.08	0.59	0.90	1.39	1.89	2.43	4.08	4.42	5.51	6.34
MW-33D	81.59	79.22	80.60	80.31	80.25	80.54	80.48	80.39	80.69	80.33	80.04	80.85	80.22	80.25	80.23	80.75	80.25	80.12	80.33	80.06	79.96	79.89	80.45
MW-34D	83.01	82.01	82.93	82.51	82.50	82.80	82.62	82.77	83.04	82.71	82.32	83.47	83.94	92.81	83.67	84.97	84.12	85.29	86.09	83.55	84.02	82.28	83.39
MW-36D	NM	NM	83.11	82.87	NM	NM	82.81	83.09	83.16	82.97	82.41	NM	82.75	82.87	82.73	NM	82.83	82.60	82.86	82.66	82.21	82.18	83.28
MW-37D	88.99	87.84	88.73	88.36	88.48	88.76	88.85	88.88	89.20	88.98	88.38	89.25	88.63	88.42	88.64	88.91	88.26	88.33	88.67	88.32	88.34	88.16	89.11
MW-38D	NM	NM	73.39	72.60	72.53	72.63	72.76	72.26	72.85	72.46	72.17	73.19	72.59	NM	69.74	73.05	72.46	72.38	72.74	72.12	71.89	71.77	72.74
MW-39D	75.97	75.36	76.20	75.68	NM	75.84	75.84	75.71	76.07	75.76	75.52	76.23	75.77	75.84	NM	76.15	75.62	75.62	75.88	75.47	75.10	75.17	75.86
MW-40D	81.00	80.28	81.07	80.64	80.61	80.87	80.78	80.77	80.98	80.82	80.49	81.07	80.71	80.85	NM	81.07	80.51	80.55	80.84	NM	80.21	80.26	80.75
MW-41D	78.61	77.88	78.52	78.15	78.21	78.45	78.50	78.50	78.81	78.50	78.23	79.03	78.54	81.63	79.92	79.34	78.45	78.33	78.81	78.44	78.32	78.26	78.81
MW-42D	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW-43D	87.10	86.55	86.80	86.46	86.48	86.75	86.98	86.12	87.00	86.67	86.54	87.25	86.73	86.88	86.82	87.26	86.72	86.64	86.87	86.48	86.37	86.37	87.05
RH-1D	42.74	-11.08	-2.87	-2.44	-2.32	-1.98	-1.62	-1.39	-0.97	-0.84	-0.43	-0.21	-0.14	0.25	0.46	0.61	0.77	0.92	1.04	1.28	1.48	1.69	20.11
SG-1	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	72.80	NM	72.56	NM	NM	NM	NM	NM	NM	NM	NM
SG-2	NM	NM	NM	74.17	74.22	74.10	NM	73.75	NM	73.71	74.68	NM	75.04	NM	74.90	NM	75.34	75.30	75.14	NM	NM	NM	NM
SG-3	NM	NM	NM	69.07	68.92	NM	74.49	NM	74.59	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM

TABLE 2
SUMMARY OF GROUNDWATER ELEVATIONS

NYSEG
MECHANICVILLE, NEW YORK

WELL NUMBER	Water Level (feet msl)																
	3/1/2006	5/31-6/1 2006	7/5/2006	8/28/2006	9/21/2006	10/19/2006	11/30/2006	1/29-30/2007	4/2-4/3/2007	6/21/2007	7/24/2007	8/24/2007	11/28/2007	2/29/2008	4/25/2008	6/12/2008	8/18/2008
MW-10	80.28	79.79	81.06	80.64	80.39	80.88	80.64	80.51	81.83	80.6	80.66	80.15	81.11	NM[6]	80.55	80.7	NM[10]
MW-12	80.13	80.37	80.54	80.25	79.32	81.46	80.64	80.73	80.09	80.31	80.35	79.98	80.75	NM[6]	80.22	80.3	80.8
MW-12S	79.10	79.36	79.61	79.38	79.23	79.64	79.4	79.24	79.72	79.37	79.28	78.93	79.74	NM[6]	NM[7]	79.24	80.98
MW-14S	79.60	78.98	79.18	79.01	78.91	82.27	78.96	78.85	79.36	79.08	80.07	78.66	79.35	78.92	78.96	78.99	79.6
MW-15S	80.28	80.4	80.49	79.55	80.55	80.72	80.52	80.4	80.21	80.38	80.56	80.3	80.78	80.27	80.00	80.24	80.82
MW-16	NM	NM	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]	NM[1]
MW-17	79.38	78.69	79.84	79.58	79.44	79.75	79.54	79.39	79.95	79.62	79.55	79.2	79.74	79.58	79.54	79.49	79.79
MW-21S	77.17	80.83	80.12	80.91	80.83	81.8	80.84	80.66	81.43	80.82	80.85	80.32	81.71	81.54	80.47	80.62	81.54
MW-23S	77.62	77.95	78.14	78.03	77.93	78.3	77.88	77.8	78.28	78.02	78.05	78.24	78.33	77.34	77.82	77.84	78.44
MW-25S	79.80	80.24	80.4	79.76	79.85	80.44	80.02	79.02	80.59	80.15	79.77	79.37	80.61	NM[3]	78.99	78.57	79.07
MW-26S	80.63	81.07	81.3	81.02	80.37	81.17	80.98	80.88	81.49	82.08	81.01	80.23	81.93	81.13	81.12	81.06	NM[10]
MW-30S	79.94	80.22	81.36	80.12	81.48	80.46	80.23	80.13	80.68	80.12	80.15	79.71	80.6	80.1	80.14	81.01	80.57
MW-31S	80.84	80.89	81.02	80.87	80.79	80.76	80.89	80.84	80.97	80.91	80.78	80.72	80.94	80.89	80.87	80.78	80.67
RH-1S	82.12	82.34	82.18	82.25	82.09	82.45	82.2	82.19	82.66	82.23	82.24	82.36	NM	NM[1]	NM[1]	NM[1]	NM[1]
MW-1	82.14	82.58	81.29	82.45	82.13	82.64	82.5	82.22	82.66	82.48	82.23	82.75	82.73	82.53	85.45	82.6	NM[10]
MW-10I	79.77	79.91	80.22	80.01	80.76	82.19	80.02	79.35	81.79	80.01	79.98	80.57	80.35	NM[6]	79.92	80.9	NM[10]
MW-11	81.57	80.89	82.88	83.14	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM[1]	NM[1]	NM[1]
MW-13	78.91	NM	NM[2]	NM[2]	NM[2]	NM[2]	NM[2]	NM[2]	NM[2]	NM[2]	79.32	78.9	81.11	79.45	79.12	79.14	NM[3]
MW-14	78.58	78.79	NM[3]	81.98	NM[2]	NM[2]	NM[2]	NM[2]	NM[2]	NM[3]	NM[3]	NM[3]	NM[3]	NM[3]	NM[3]	NM[3]	NM[3]
MW-15I	78.10	79.62	78.46	78.34	78.61	78.54	78.28	78.03	78.28	78.09	78.21	77.7	78.43	78.07	77.23	77.89	78.49
MW-17I	78.94	79.2	79.49	81.06	78.97	79.28	78.58	79.13	79.7	79.14	79.09	78.74	79.25	NM[6]	79.15	78.37	79.31
MW-18	79.18	79.47	79.67	79.43	77.29	79.68	79.46	79.34	79.89	79.42	79.33	79.03	79.72	79.37	79.26	79.38	79.61
MW-19I	86.86	87.14	86.35	87.02	87.01	87.15	86.85	86.97	86.97	87.02	86.9	86.61	87.28	87.71	86.95	86.98	86.68
MW-1I	80.36	82.68	82.02	80.54	80.41	80.8	80.67	80.49	81.24	80.6	80.5	80.22	NM[5]	NM[2]	NM	NM	NM[10]
MW-2	83.87	84.21	84.11	83.81	83.97	84.51	84.06	83.93	84.43	84.19	84.09	83.47	84.64	84.31	83.92	83.98	NM[10]
MW-22I	75.88	75.54	75.56	75.12	74.89	75.55	75.46	75.12	76.15	75.37	75.37	74.58	75.83	74.61	75.12	75.05	75.96
MW-25I	78.91	79.27	79.61	79.2	80.42	78.5	79.29	77.37	79.93	79.42	79.48	78.8	80.93	NM[3]	80.60	78.94	79.63
MW-26I	79.95	80.31	80.45	80.21	80.06	80.45	80.26	80.12	80.66	80.2	79.17	80.03	80.49	NM[2]	80.03	79.74	NM[10]
MW-28I	74.05	74.54	74.63	73.89	73.9	74.64	74.39	74.16	75.27	74.32	74.25	73.49	74.88	74.53	74.27	74.02	74.78
MW-29I	74.97	75.51	76.04	75.34	75.18	76.06	75.43	75.25	75.96	75.43	75.46	74.82	75.78	75.85	75.08	74.15	75.92
MW-2I	83.87	84.38	84.83	84.12	84.02	85.38	84.13	84.07	84.98	84.22	84.09	83.59	84.43	84.78	84.06	84.02	NM[10]
MW-35I	74.87	75.22	75.59	75.09	75.21	75.47	75.21	NM[2]	75.86	75.02	75.12	74.19	75.69	NM[6]	NM[7]	NM[7]	NM[7]
MW-36I	83.30	82.8	82.8	82.26	81.96	81.99	82.48	82.29	84.52	88.63	84.04	82.21	81.87	85.29	85.78	83.23	83.27
MW-37I	82.07	82.59	82.67	81.22	82.19	82.62	82.09	81.96	81.64	82.14	82.32	81.64	88.71	82.26	81.94	82.18	82.27
MW-38I	71.84	72.71	72.58	71.97	71.66	72.33	72.33	72.18	73.12	NM	71.94	72.8	72.75	NM[6]	72.13	71.71	72.25
MW-10D	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM[10]
MW-14D	82.50	82.65	82.72	80.48	82.1	81.17	82.53	82.55	83.27	92.47	81.19	81.79	82.14	81.65	82.59	82.15	81.59
MW-15D	76.77	76.83	76.92	76.43	76.31	76.37	76.78	76.73	76.87	76.7	76.31	76	76.4	76.84	76.98	76.62	76.89
MW-17D	81.55	81.74	79.71	79.4	80.35	79.73	81.88	81.98	87.07	80.99	80.62	79.77	82.55	NM[6]	90.04	86.29	84.9
MW-1D	-33.85	-33.5	-33.42	-33.28	-33.17	-33.08	-32.92	-32.75	-30.2	-29.91	-29.82	-29.77	-29.54	NM[6]	-23.74	-23.45	NM[10]
MW-20D	80.26	80.6	81.94	80.03	79.91	80.15	80.65	80.58	81.84	80.36	79.86	79.26	80.56	80.83	80.49	80.17	NM[9]
MW-21D	80.65	77.86	77.95	76.76	77.15	77.75	77.81	77.53	78.31	77.56	77.69	76.7	77.99	78.01	77.39	77.4	78.25
MW-23D	46.82	47.85	48.19	48.67	48.88	52.16	49.49	49.97	50.49	51.12	51.32	51.5	52.06	52.67	53.03	53.33	53.66
MW-29D	81.53	81.54	82.17	81.48	81.16	81.63	82.75	81.82	82.63	81.62	81.35	80.87	80.66	81.78	81.59	81.04	82.15
MW-30D	80.27	79.86	80.51	80.18	80.12	80.57	81.55	80.33	81.07	81.26	80.13	79.74	80.32	NM[6]	79.97	79.92	80.09
MW-31D	NM	80.83	80.68	80.64	82.66	80.39	83.75	80.24	80.52	NM[3]	NM[3]	NM[3]	NM[3]	NM[6]	NM[3]	NM[3]	NM[3]
MW-32D	8.95	11.67	11.95	13.53	14.17	14.52	15.69	16.21	47.1	73.42	NM	21.1	21.99	22.79	NM[8]	21.54	22.67
MW-33D	78.89	79.22	79.27	80.1	79.98	80.37	80.04	80.16	80.71	80.2	79.02	79.66	80.35	NM[3]	77.17	79.96	80.49
MW-34D	82.36	82.66	82.97	NM	82.31	NM	82.69	NM[4]	80.93	82.9	82.96	82.32	89.49	NM[3]	87.40	NM[4]	NM[9]
MW-36D	82.70	83.1	83.03	82.9	82.83	82.66	82.97	82.97	83.85	82.83	82.42	82.1	82.76	82.92	82.88	82.6	83.26
MW-37D	88.32	88.59	NM[3]	89.35	88.3	88.52	88.46	NM[2]	88.88	88.42	88.32	87.92	88.07	NM[6]	88.26	NM[3]	89.01
MW-38D	72.07	75.44	72.84	72.21	71.89	72.57	72.54	72.44	73.35	72.35	72.15	72.47	72.49	NM[6]	72.18	71.84	72.66
MW-39D	74.93	75.77	76.71	75.59	75.59	75.34	75.75	75.66	76.4	85.38	65.36	75.04	75.62	80.28	75.44	75.16	75.96
MW-40D	80.15	80.39	80.41	80.37	79.4	80.5	80.52	80.28	80.98	80.43	80.49	79.92	80.62	NM[6]	80.31	80.22	80.06
MW-41D	78.33	78.74	78.68	78.54	78.5	79.76	78.43	78.45	85.84	78.48	78.82	77.78	NM[4]	78.36	77.16	78.23	78.68
MW-42D	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
MW-43D	86.52	86.92	86.87	86.77	87.16	82.35	87.11	86.65	87.29	86.65	86.56	86.27	86.98	86.63	86.52	84.1	83.54
RH-1D	43.94	69.71	86.59	4.14	4.99	5.27	11.38	12.82	40.42	14.99	16.44	21.38	56.06	60.27	86.84	86.84	NM[10]
SG-1	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
SG-2	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
SG-3	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM

TABLE 2
SUMMARY OF GROUNDWATER ELEVATIONS


NYSEG
MECHANICVILLE, NEW YORK

Notes NM - not measured
NI - not installed
[1] - Well destroyed by snow removal equipment
[2] - Could not open the case
[3] - Water Filling the top of the Casing
[4] - Car parked over the well
[5] - Tubing in the well - not accessible
[6] - Inaccessible due to snow and ice
[7] - Inaccessible due to debris and sediment
[8] - Inaccessible - gate was locked
[9] - Inaccessible - overgrown brush
[10] - Inaccessible - NYSEG crew working around well

SUMMARY OF PRODUCT RECOVERY
MW-42D

Privileged & Confidential

NYSEG
MECHANICVILLE, NEW YORK

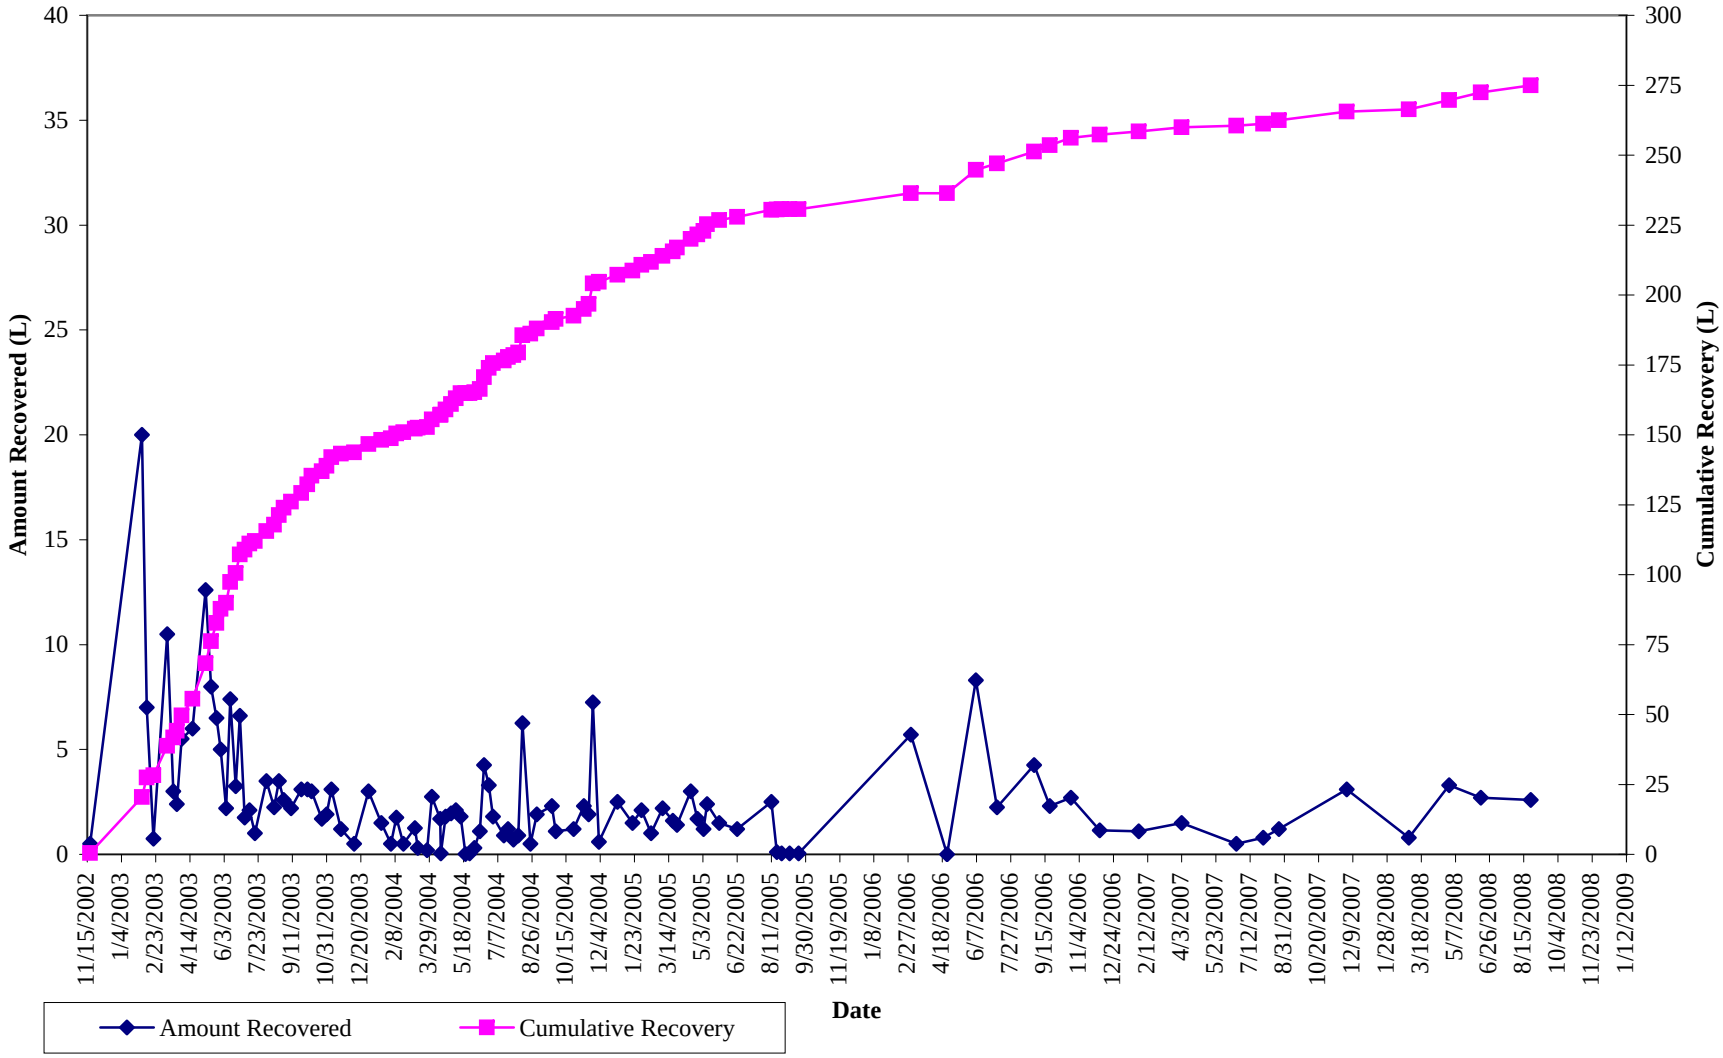

ATTACHMENT 3

AECOM

PHOTOGRAPHIC LOG

Client Name:	Site Location:	Project No.
Mechanicville Former MGP Site	Mechanicville, New York	94560

Photo No.	Date:
1	12/12/11

Direction Photo Taken:

North

Description:

View of tree cut down by beavers.



Photo No.	Date:
2	12/12/11

Direction Photo Taken:

Northeast

Description:

View of streambank, and damaged trees.



PHOTOGRAPHIC LOG

Client Name:	Site Location:	Project No.
Mechanicville Former MGP Site	Mechanicville, New York	94560

Photo No.	Date:
3	12/12/11

Direction Photo Taken:

Southwest

Description:

View of streambank and damaged trees.



Photo No.	Date:
4	12/12/11

Direction Photo Taken:

Northeast

Description:

View of damaged tree.



PHOTOGRAPHIC LOG

Client Name:	Site Location:	Project No.
Mechanicville Former MGP Site	Mechanicville, New York	94560

Photo No.	Date:
5	12/12/11

Direction Photo Taken:

North

Description:

View of damaged tree.



Photo No.	Date:
6	12/12/11

Direction Photo Taken:

West

Description:

Stream observation area.



AECOM

PHOTOGRAPHIC LOG

Client Name:	Site Location:	Project No.
Mechanicville Former MGP Site	Mechanicville, New York	94560

Photo No.	Date:
7	12/12/11

Direction Photo Taken:

Down

Description:

View of gelatinous area on streambank.



Photo No.	Date:
8	12/12/11

Direction Photo Taken:

Southeast

Description:

View of new chain link fence section recently installed

