DEPARTMENT OF THE AIR FORCE
AIR FORCE CIVIL ENGINEER CENTER

June 20, 2025

MEMORANDUM FOR: U.S. Environmental Protection Agency – Region 2
Attn: Mr. Daniel J. D'Agostino
Federal Facilities Section
290 Broadway, 18th Floor
New York, NY 10007-1866

New York State Department of Environmental Conservation
Attn: Ms. Heather Bishop
Bureau of Eastern Remedial Action
625 Broadway 12th Floor
Albany, NY 12233-7015

FROM: AFCEC/CZBE – Plattsburgh
8 Colorado Street, Suite 121
Plattsburgh NY 12903

SUBJECT: Final 2024 Well Inspection Survey and Well Maintenance Report
Former Griffiss Air Force Base, Rome, New York

Accompanying this letter, please find the following document for the former Griffiss Air Force Base for your information.

- Final 2024 Well Inspection Survey and Well Maintenance Report
Former Griffiss Air Force Base, Rome, New York

The following recommendations are presented within the report and will be completed by the Air Force.

- While monitoring well ANGMW-1 meets the criteria for removal from the Annual Well Inventory Report due to not being located for three or more consecutive years, it is not recommended. Instead, prioritization will be given during the 2025 inspection cycle to resolve access to this well. This well should be located and inspected, and any maintenance issues resolved at the time of inspection
- Maintenance and repair of wells as detailed above in "Well Maintenance Planned for 2025". Priority should be given to any maintenance tasks that were not addressed in 2024, such as the wells that need to have their vaults or surface completions cleaned out, repaired, or replaced.
- Three wells, G009-MW03, 789MW-103, and 789MW-64 have sustained severe damage, are not repairable, and should be properly abandoned and decommissioned. Any recommendation regarding the possible replacement of these wells is beyond the scope of this inventory. The

Air Force will address the abandonment and removal of these wells under a separate task order, with a timeline still to be determined.

Should you have any questions or concerns please contact me at 518-563-2871 or david.farnsworth@us.af.mil.

DAVID S. FARNSWORTH, DAF
Program Manager/BRAC Environmental Coordinator
BRAC Program Management Division

Attachment: Final 2024 Well Inspection Survey and Well Maintenance Report, Former Griffiss Air Force Base, Rome, New York (April 2025)

Cc: Ms. Christina Villanueva, CO, 772 ESS/PKS
Mr. Jose Flores, AFCEC/CZBE
Ms. Christiana Hewitt, Alt COR, AFCEC/CZBW
Mr. Richard Dugoh, CS, 772 ESS/PKS
Mr. Chance Pircher, AFIMSC/DST
Mr. Joe Tellez, Cherokee Federal
Mr. John Carr, Cherokee Federal
Mr. Allen Tevyaw, Cherokee Federal
Mr. Ted Volskay, Cherokee Federal
Mr. Mark Sergott, NYSDOH
BRAC DR

FINAL
2024 ANNUAL WELL INSPECTION SURVEY AND WELL MAINTENANCE
FORMER GRIFFISS AIR FORCE BASE
ROME, NEW YORK

Document Control No. NEBECOS-0486-GRI

PREPARED FOR: Mr. David Farnsworth/Former Griffiss Air Force Base, Base Realignment and Closure Environmental Coordinator and Contracting Officer's Representative

PREPARED BY: Bhate Environmental Associates, Inc.

COPIES: Mr. Daniel J. D'Agostino, United States Environmental Protection Agency
Ms. Heather Bishop, New York State Department of Environmental Conservation

DATE: 20 June 2025

INTRODUCTION AND OBJECTIVES

Bhate Environmental Associates, Inc. (Bhate), in association with Environmental Chemical Corporation (ECC), was retained by the Air Force Civil Engineer Center (AFCEC), under Contract Number FA8903-20-D-0001, to conduct environmental remediation activities at the former Griffiss Air Force Base (AFB). Under this contract, Bhate has prepared this document for the inspection and maintenance of existing groundwater wells at the former Griffiss AFB located in the City of Rome in Oneida County, New York (**Figure 1**). Site locations are presented on **Figure 2**. Well locations are shown on **Figures 3** through **14b.**

The purpose of this annual inspection is to note the presence or absence of wells, evaluate the condition of wells that are included in the current groundwater sampling program, identify deficiencies, make repairs, and ensure there has been no unauthorized usage, encroachment upon, or interference with the former Griffiss AFB wells. The inventoried wells include permanent monitoring wells, temporary monitoring wells, and remedial system process wells installed as part of the Air Force's Installation Restoration Program (IRP). However, this report does not include vapor monitoring wells or vapor probes. In addition to documenting results of the well inspection, this document presents the details of any well maintenance and repair activities performed in 2024 along with providing recommendations for future maintenance, repairs, and other activities.

WELL INVENTORY

A comprehensive list from the Final Technical Memorandum 2023 Annual Well Inspection Survey and Maintenance Report (Bhate, October 2024) containing 352 well locations formed the initial basis of this report. One well, 817MW-2, was removed from the list of well locations during the 2023 Annual Well Inspection for a total of 351 wells for the 2024 Well Inventory. The 2024 Well Inventory is the tenth comprehensive inventory or inspection reported for the former Griffiss AFB since the 2010 inspection (FPM Group Ltd. [FPM], January 2010).

Field activities associated with the well inventory were conducted throughout the year in conjunction with other activities, including a mobilization in May, September, and November 2023. Field personnel examined and noted the condition of each inspected well. Efforts were also made to locate some wells that were not found during the 2023 Well Inventory. The 2024 Well Inventory information is summarized in **Table 1**, the static well details (i.e., coordinates, elevations, construction details) are provided in **Table 2**.

Inspections and data collection for the former Griffiss AFB Well Inventory were separated into two categories:

1.) Wells sampled as part of the quarterly sampling program at SS067 [6 total], the biennial sampling program at SD052-01, SD052-02, SD052-04, SD052-05, and SS062 [41 total], and the 5-year sampling program at LF001, LF002, LF003, LF007, and LF009 [33 total].

2.) Wells not sampled in 2024 [271 total]

- Including a set of wells that were part of the aqueous film forming foam (AFFF) site inspection (Wood, November 2018) [33 total]

The details recorded during the well inspections and repairs included the presence/absence (where applicable) of the well itself; identification markings; a lock; a well cap; the type of surface completion; condition of concrete pad; and any maintenance issues completed or noted. Findings of the 2024 Well Inventory are presented in **Table 1** and summarized below.

Out of a possible 351 wells, inspection and/or repairs were performed at 338 wells at the former Griffiss AFB in 2024. The remaining 13 wells were not located during 2024 field activities. Reasons for not locating wells included: unavailability of an airfield escort, time constraints, dense/overgrown vegetation, other access issues, and the absence of any well at the given coordinates. The previously reported locations of wells not found or visited during the 2024 Well Inventory are included on **Figures 3** through **14b**. Efforts to locate and inspect these wells shall continue throughout the ensuing years of this contract and the well inventory will be updated accordingly. As noted in the 2023 Well Inspection Technical Memorandum (Bhate, October 2024), wells that are not located for three consecutive years will be removed from the well inventory. The 2024 Well Inventory for the former Griffiss AFB includes all 351 wells as presented in **Table 1**.

WELL MAINTENANCE PERFORMED IN 2024

Overgrown vegetation was removed from the well pads or surrounding areas at five wells as

detailed in **Table 1**.

WELL MAINTENANCE PLANNED FOR 2025

The 2024 Well Inventory inspections identified 69 wells that will require various maintenance or repairs in the future. The details are provided in **Table 1**. The following issues with wells at the former Griffiss AFB remain outstanding in 2025:

- Renew fading or indistinct ID markings or add new ID markings (26 locations)
- Locating or visiting the well should be prioritized (11 locations)
- Clean, repair, or replace vault / surface completion (10 locations)
- Add a new lock or remove and replace a lock (5 locations)
- Inspect the total depth and attempt to identify unknown wells (4 locations)
- Remove extensive vegetation to access the well (5 locations)
- Repair or replace a protective bollard(s) (2 locations)
- Add or replace a well plug or cap (4 locations)
- Repair concrete well pad (2 locations)
- Redevelop the well (2 locations)
- Add visibility marking for the well (1 location)
- Resurvey well location (1 location)
- Abandon wells (3 locations)

Some well locations have more than one of the issues listed above.

WELL DISCREPANCIES

In 2024, no new well discrepancies were identified.

Previously observed well discrepancies that are pending resolution are provided below.

- Three stickup wells not listed in the current well inventory were found at LF001 with locks keyed to the Air Force key path. Investigation of these wells is planned for 2025 which will include: total depths, stick up heights, and approximate GPS coordinates. The results will be compared to historical data in order to determine their identities.
- One well at LF002 was found with the same label as a known nearby well (LF2MW2-1). Investigation of this well is planned for 2025 which will include: total depth, stick up height, and approximate GPS coordinates. The results will be compared to historical data in order to determine its identity.

WELL INSTALLATIONS

No wells were installed during 2024 under the former Griffiss AFB IRP.

WELL DECOMMISSIONING

No former Griffiss AFB IRP wells were decommissioned during 2024.

WELLS RECOMMENDED FOR REMOVAL FROM THE INVENTORY

Three wells are recommended for removal from the 2025 Well Inventory (**Table 3**):

- Monitoring well AOC9TW-95, a 1-inch polyvinyl chloride (PVC) temporary monitoring well at SS062 has not been located in three consecutive years.
- Monitoring well MW10002, a 1-inch PVC monitoring well between SD052-05 and LF003, has not been located in five consecutive years.
- Monitoring well SD052-02_IW-14, a 2-inch PVC injection well at SD052-05, was found to be paved over in 2024.The lid is sealed shut and the monitoring well could not be properly abandoned without damaging the asphalt.

One other well was not located during the previous five annual well inventories: ANGWM-1. This well technically met the criteria for removal as it was not located for three or more consecutive years. However, the reason for not locating this well over those years was the lack of appropriate access to the area during the time of the inventory efforts. Additionally, field personnel's knowledge of this well indicates it is likely to still be present.

RECOMMENDATIONS

Well inventory activities for 2025 will focus on:

- While monitoring well ANGMW-1 meets the criteria for removal from the Annual Well Inventory Report due to not being located for three or more consecutive years, it is not recommended. Instead, prioritization will be given during the 2025 inspection cycle to resolving access to this well. This well should be located and inspected, and any maintenance issues resolved at the time of inspection.
- Maintenance and repair of wells as detailed above in "Well Maintenance Planned for 2025". Priority should be given to any maintenance tasks that were not addressed in 2024, such as the wells that need to have their vaults or surface completions cleaned out, repaired, or replaced.
- Three wells, G009-MW03, 789MW-103, and 789MW-64 have sustained severe damage, are not repairable, and should be properly abandoned and decommissioned. Any recommendation regarding the possible replacement of these wells is beyond the scope of this inventory. The Air Force will address the abandonment and removal of these wells under a separate task order, with a timeline still to be determined.

Following the 2025 Well Inventory, Bhate will compile a list of wells located throughout the former Griffiss AFB that have been proposed as candidates for decommissioning in the future. These proposals, if made, will be presented with the 2025 well inventory reporting.

Attachments:

Table 1 – 2024 Well Inventory
Table 2 – Static Well Details
Table 3 – Wells Removed 2024
Figure 1 – Former Griffis Air Force Base Location Map
Figure 2 – Site Locations
Figure 3 – Well Locations Associated with Site LF001
Figure 4 – Well Locations Associated with Site SS062
Figure 5 – Well Locations Associated with Site SD052-05
Figure 6 – Well Locations Associated with Sites LF002 and LF003
Figure 7 – Well Locations Associated with Sites SS008, SS025, and ST006,
Figure 8 – Well Locations Associated with Sites SD052-01, SD052-SVI Buildings 785 and 786, CSS681 – Apron 1 Area LCP-E9, and CSS682 – Building 785 Pipeline
Figures 9a and 9b– Well Locations Associated with Site SS067
Figure 10 – Well Locations Associated with Sites AOI66, LF007, SS060, and SS017
Figure 11 – Well Locations Associated with Sites SD052-02 and SD052-SVI Buildings 774 and 776
Figure 12 – Well Locations Associated with Site SD052-04
Figure 13 – Well Locations Associated with Site LF009
Figures 14a and 14b – Well Locations Associated with Site SS054

REFERENCES

Bhate. May 2018. *Final Technical Memorandum 2017 Annual Well-Inspection Survey and Well Maintenance Report Former Griffiss Air Force Base Rome, New York.*

Bhate. October 2024. *Final 2023 Well Inspection Survey and Well Maintenance, Former Griffiss Air Force Base, Rome, New York.*

FPM. January 2010, Revision 1.0. *Well Decommissioning Report Round 4 and Round 5 Long Term Monitoring Program Former Griffiss Air Force Base Rome, New York*. (AR 2091).

Wood. November 2018. *Final Site Inspection Report For Aqueous Film Forming Foam (AFFF) Areas Former Griffiss Air Force Base, New York.*

This page intentionally left blank

TABLES

This page intentionally left blank.

Table 1. 2024 Well Inventory

This page intentionally left blank.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
1	ANGMW-1	3	Not Visited	No	No	No	-	No	-	-		Visit. Add ID. Add lock.	Access.	Last visited in 2019.
2	LF1MW-UNK-01	3	9/20/2024	Yes	No	No	N/A	Yes	Yes	No		Identify.		
3	LF1MW-UNK-02	3	9/20/2024	Yes	No	No	N/A	Yes	Yes	No		Identify.		
4	LF1MW-UNK-03	3	9/20/2024	Yes	No	No	N/A	Yes	Yes	No		Identify.		
5	LF1P-2	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	No		Renew ID.		
6	LF1P-3	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
7	LF1P-5	3	Not Visited	No	No	-	-	-	-	Yes	In beaver pond.	Visit.	Access.	Access is difficult.
8	LF1MW-5	3	Not Visited	No	No	-	-	Yes	-	-	In beaver pond.	Visit. Cut and replace lock.	Access.	Access is difficult.
9	LF1MW-6	3	Not Visited	No	No	-	-	-	-	-	Beaver pond prevents access.	Visit.	Access.	Beaver pond prevents access during most of the year.
10	LF1MW-10	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Well is on the side of a hill.			
11	LF1MW-11	3	10/31/2024	Yes	No	-	-	-	-	-	J-plug prevents well lid from closing completely.	Replace J-plug.		Access is difficult. Riser too high for lid to close.
12	LF1MW-12	3	Not Visited	No	No	-	-	-	-	Yes		Visit.	Access.	Access is difficult.
13	LF1MW-13	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
14	LF1MW-14	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	No				Riser is too high for lid to close properly.
15	LF1MW-103	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	No				
16	MWSAR03	3	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Well is on the side of a hill.			
17	LF2MW-4	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
18	LF2MW-12	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
19	LF2MW-13	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	No				
20	LF2MW-14	6	9/20/2024	Yes	No	Yes	Good	Yes	-	-				
21	LF2MW2-1	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
22	LF2MW-UNK-01	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	-		Identify.		
23	LF2MW-100	6	9/20/2024	Yes	No	Yes	Good	Yes	Yes	No				
24	LF7MW-22	6	10/1/2024	Yes	No	-	Good	No	Yes	-				Vault prevents lock placement but well is inside airport fence line.
25	LF7MW-23	6	10/1/2024	Yes	No	-	Good	No	Yes	-	Cap/PVC is damaged. Cap was slightly open when visited.			Red plastic pipe at location. Vault prevents lock placement but well is inside airport fence line.
26	LF7MW-26	6	10/1/2024	Yes	No	Yes	Good	Yes	Yes	No				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
27	LF7MW-27	6	10/1/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
28	LF7MW-28	6	Not Visited	No	No	-	-	-	-	-	Overgrown at surface. No marker.	Locate. Add visibility marker.	Overgrown at surface. No marker.	
29	LF7MW-29	6	10/1/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
30	LF7MW-30	6	10/1/2024	Yes	No	No	Good	Yes	Yes	Yes				
31	LF7MW-100	6	10/1/2024	Yes	No	Yes	Good	Yes	Yes	No				No bollards present.
32	LF5MW-1A	10	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
33	LF5MW-3	10	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Cleared vegetation.			
34	LF5MW-4	10	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
35	LF5MW-5	10	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
36	MW49D07	10	9/19/2024	Yes	No	Yes	Undercut	Yes	Yes	No	Cleared vegetation.			
37	LF5MW-100R	10	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
38	SD052-04-IW01	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		TOC is female cam, cap is male cam plug.
39	SD052-04-IW02	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		TOC is female cam, cap is male cam plug.
40	SD052-04-IW03	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		TOC is female cam, cap is male cam plug.
41	SD052-04-IW04	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		TOC is female cam, cap is male cam plug.
42	LF6IW-01	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
43	LF6IW-02	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
44	LF6IW-03	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No	Well cap is not on. No J-plug.	Renew ID.		
45	LF6IW-04	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
46	LF6IW-05	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
47	LF6IW-06	12	9/18/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
48	LF6MW-1	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
49	LF6MW-12	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
50	LF6MW-13RD	12	9/18/2024	Yes	No	-	-	Yes	-	-				
51	LF6MW-14BR	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
52	LF6MW-16	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
53	LF6MW-17	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
54	LF6MW-18	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
55	LF6MW-19	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
56	LF6MW-20	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
57	LF6MW-27	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
58	LF6MW-28	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
59	LF6MW-29	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
60	LF6MW-30	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
61	LF6MW-31	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
62	LF6MW-32	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
63	LF6MW-39	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes		Renew ID.		
64	LF6TW-33	12	9/18/2024	Yes	No	Yes	Good	No	Yes	No				Bolted cap does not lock.
65	LF6TW-34	12	9/18/2024	Yes	No	Yes	Good	No	Yes	No				Painted red. Bolted cap does not lock.
66	LF6TW-35	12	9/18/2024	Yes	No	Yes	Good	No	Yes	No				Red marking tape. Bolted cap does not lock.
67	LF6TW-36	12	9/18/2024	Yes	No	No	Good	No	Yes	No				Red marking tape. Bolted cap does not lock.
68	LF6TW-37	12	9/18/2024	Yes	No	No	Good	No	Yes	No				Red marking tape. Bolted cap does not lock.
69	LF6TW-38	12	9/18/2024	Yes	No	Yes	Good	No	Yes	No				Red marking tape. Bolted cap does not lock.
70	LF6VMW-10R2	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
71	LF6VMW-13R	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
72	LF6VMW-14	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes		Cut and replace lock.		
73	LF6VMW-15R	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
74	LF6VMW-17D	12, 13	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
75	LF6VMW-17S	12, 13	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				SS riser is crushed inward ~1 ft down.
76	LF6VMW-18	13	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
77	LF6VMW-19	13	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
78	LF6VMW-20	13, 14b	9/18/2024	Yes	No	No	Good	Yes	Yes	Yes				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
79	LF6VMW-21	13, 14a	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
80	LF6VMW-22	12, 13	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
81	LF6VMW-23	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
82	LF6VMW-24	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
83	LF6VMW-25	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation has not been cleared. In a flower field with bees/wasps.			
84	LF6VMW-26	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
85	TMCMW-9	12	9/18/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation has not been cleared. In a flower field with bees/wasps.			
86	TMC-USGS-2	13	9/18/2024	Yes	No	No	Good	Yes	Yes	No	Well has been run over. Needs repair.	PVC and tubing snapped. Needs replacement.		PVC stick up only. No outer casing or bollards.
87	LAWMW-19	14b	9/19/2024	Yes	No	-	-	-	-	-				USGS monitoring equipment on well. No access to well head.
88	TMC-USGS-1	13	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				No protective casing.
89	782MW-1	8	9/23/2024	Yes	No	No	Good	N/A	Yes	No				Well listed in historical report as being "previously decommissioned" (AECOM/Cape, May 2016) but well was identified during 2016, 2017, 2018, 2020, 2021, 2023, and 2024 field inspections.
90	782MW-1R	8	9/23/2024	Yes	No	Yes	Good	N/A	Yes	No				
91	782MW-3	8	9/23/2024	Yes	No	No	Good	-	-	-				Well listed in historical report as being "previously decommissioned" (AECOM/Cape, May 2016) but well was identified during 2018, 2020, 2021, 2023, and 2024 field inspections.
92	782MW-3R	8	9/23/2024	Yes	No	No	Good	-	-	-				
93	782MW-5	8	9/23/2024	Yes	No	No	Good	-	Yes	-				
94	782MW-6D	8	9/23/2024	Yes	No	No	Good	Yes	Yes	Yes				
95	782MW-6R2	8	9/23/2024	Yes	No	Yes	Good	N/A	Yes	No				
96	782MW-9	8	9/23/2024	Yes	No	No	Good	-	-	-				
97	782MW-10	8	9/23/2024	Yes	No	No	Good	Yes	Yes	Yes				
98	782MW-11	8	9/23/2024	Yes	No	No	Good	Yes	Yes	No				
99	782MW-12	8	9/23/2024	Yes	No	Yes	Good	-	-	-				
100	782-MW184	8	9/23/2024	Yes	No	Yes	Good	-	-	-				84, 84D, and 184 are all located very close together.
101	782VMW-76	8	9/23/2024	Yes	No	No	Good	N/A	Yes	Yes		Renew ID.		Well completion prevents addition of a lock, however, the well is located within the airport's secured area.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
102	782VMW-78	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
103	782VMW-81	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
104	782VMW-82	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
105	782VMW-83	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				
106	782VMW-84	8	9/23/2024	Yes	No	Yes	Good	N/A	Yes	No		Replace vault.		84, 84D, and 184 are all located very close together. Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
107	782VMW-84D	8	Not Visited	No	No	-	-	-	-	-	Unable to locate.	Locate. Clear pad of vegetation.	Unable to locate.	84, 84D, and 184 are all located very close together.
108	782VMW-85	8	9/23/2024	Yes	No	No	Good	Yes	Yes	No		Renew ID.		
109	782VMW-86	8	9/23/2024	Yes	No	No	Good	Yes	Yes	No				
110	782VMW-87	8	9/23/2024	Yes	No	No	Good	Yes	Yes	No				
111	782VMW-88	8	Not Visited	No	No	No	Good	N/A	-	-	Unable to locate. May be covered.	Locate.	Unable to locate.	Center bolt lid. Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
112	782VMW-89	8	9/23/2024	Yes	No	No	Good	Yes	Yes	No		Repair surface completion. Repair bollards.		
113	782VMW-90	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No		Add bollard.		
114	782VMW-92	8	9/23/2024	Yes	No	No	Good	-	-	-				Need 5 point socket to open.
115	782VMW-93	8	9/23/2024	Yes	No	No	Good	N/A	Yes	No				Well completion prevents addition of a lock.
116	782VMW-94	8	Not Visited	No	No	-	-	-	-	-	Unable to locate. Possibly underneath pallets.	Locate.	Unable to locate.	
117	782VMW-95	8	9/23/2024	Yes	No	No	Good	N/A	Yes	No		Repair vault.		Well completion prevents addition of a lock.
118	782VMW-96	8	9/23/2024	Yes	No	No	Good	N/A	-	-				Vault lid is small, center bolt type. Vault is too small for a lock to be placed, however, well is located within secured airfield fence line.
119	782VMW-97	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
120	782VMW-98	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
121	782VMW-99	8	9/23/2024	Yes	No	No	Good	Yes	Yes	Yes				
122	782VMW-100	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
123	782VMW-101	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
124	782VMW-102	8	9/23/2024	Yes	No	No	Good	Yes	Yes	Yes				
125	782VMW-104	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
126	782VMW-105B	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				PVC is blistered ~6 ft btoc, preventing use of sub-pump. Peristaltic is needed to sample.
127	782VMW-121	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
128	782VMW-121D	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
129	AP2MW-3	8	9/23/2024	Yes	No	Yes	Good	N/A	-	-				Well completion prevents addition of a lock, however, the well is located within the airport's secured area. Vault can fill with sediment.
130	775EW-1	11	9/17/2024	Yes	No	No	Good	N/A	-	-				Well head completion does not allow for lock installation.
131	775EW-1R	11	9/17/2024	Yes	No	No	Good	N/A	-	-				Well head completion does not allow for lock installation.
132	775EW-3	11	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
133	775MW-2	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
134	775MW-6	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
135	775-MW20	11	9/17/2024	Yes	No	No	Good	Yes	Yes	Yes				
136	775-MW20R	11	9/17/2024	Yes	No	No	Good	Yes	No	No				
137	775-MW20RBR	11	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
138	775MW-27	11	9/17/2024	Yes	No	No	Good	-	-	Yes				Dedicated bladder pump has been lost in well and the associated tubing blocks deployment of pumps and water level measurement.
139	775MW-28	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
140	775VMW-4	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
141	775VMW-5	11	9/17/2024	Yes	No	Yes	Good	Yes	-	-				
142	775VMW-8	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
143	775VMW-9	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
144	775VMW-10	11	9/17/2024	Yes	No	Yes	Good	Yes	No	-				
145	775VMW-11	11	9/17/2024	Yes	No	No	Good	Yes	Yes	Yes				Large tree growing within bollard area.
146	775VMW-14	11	9/17/2024	Yes	No	No	Good	Yes	Yes	Yes				
147	775VMW-15R1	11	9/17/2024	Yes	No	No	Good	Yes	-	-		Cut lock.		Could not be opened in 2020, 2021, 2022, 2023, or 2024.
148	775VMW-16	11	9/17/2024	Yes	No	No	Bad	Yes	Yes	Yes		Repair concrete pad.		
149	775VMW-18R	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
150	775VMW-19R	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
151	775VMW-20R	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
152	775VMW-23	11	9/17/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
153	775VMW-24	11	9/17/2024	Yes	No	No	Good	Yes	Yes	Yes				Large tree growing within bollard area.
154	775VMW-25	11	9/17/2024	Yes	No	No	Good	No	Yes	No				Redevelop prior to any sampling.
155	SD052-02_IW-01	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
156	SD052-02_IW-02	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
157	SD052-02_IW-03	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
158	SD052-02_IW-04	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
159	SD052-02_IW-05	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
160	SD052-02_IW-06	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
161	SD052-02_IW-07	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
162	SD052-02_IW-08	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
163	SD052-02_IW-09	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
164	SD052-02_IW-12	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
165	SD052-02_IW-13	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A				Well head completion does not allow for lock installation.
166	SD052-02_IW-14	11	9/17/2024	Yes	No	No	Good	N/A	-	N/A	Paved over. Lid sealed shut.	Remove from inventory.		Well head completion does not allow for lock installation.
167	817IW-1	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
168	817IW-2	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
169	817IW-3	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
170	817IW-4	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
171	817IW-5	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
172	817IW-6	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
173	817IW-7	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
174	817IW-8	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	N/A				Well head completion does not allow for lock installation.
175	817MW-1	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	No				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
176	817MW-3	5	9/19/2024	Yes	No	No	N/A	N/A	Yes	No				
177	LAWMW-9	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
178	WSA-IW01	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				3/4" threaded male cap.
179	WSA-IW02	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				3/4" threaded male cap.
180	WSA-IW03	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				3/4" threaded male cap. TOC is too high for lid to easily close and lock.
181	WSA-IW04	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				3/4" threaded male cap.
182	WSAMW-2	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
183	WSAMW-3	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
184	WSAMW-8	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
185	WSAMW-9	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
186	WSAMW-11	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
187	WSAMW-12BR	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
188	WSAMW-13BR	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
189	WSAMW-14BR	5	9/19/2024	Yes	No	N/A	Good	N/A	N/A	N/A				USGS observation well. No access to well head.
190	WSA-MW-15	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No		Remove damaged ID and renew label.		Formerly mislabeled external ID as WSAMW-11BR.
191	WSAMW-16	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
192	WSAMW-18	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
193	WSAMW-19	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
194	WSAMW-21	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
195	WSAMW-23	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
196	WSAVMW-17	5	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				SS casing is bent ~6 ft bgs and prevents use of submersible pumps. Must be sampled with peristaltic pump.
197	781MW-1	14a	9/17/2024	Yes	No	No	Good	No	Yes	No	Missing lock. Well cap broken.	Replace lock and well cap.		Lid broken. Will not lock.
198	781MW-2	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No				
199	781MW-3	14a	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
200	781MW-4	14a	9/17/2024	Yes	No	Yes	Good	Yes	-	No				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
201	781MW-5	14a	9/17/2024	Yes	No	No	Good	No	No	No	No well cap.	Add cap.		Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation. Broken sparge in well. 7 " or 8" cast iron lid is missing.
202	781MW-6	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No	No protective casing lid.	Add cap.		
203	781MW-7	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No				
204	781MW-8	14a	9/17/2024	Yes	No	Yes	Good	No	Yes	No	No bolts.	Clean vault. Replace bolts.		
205	781MW-9	14a	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
206	781MW-10	14a	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
207	781MW-11	14a	9/17/2024	Yes	No	No	Poor	No	Yes	No		Replace vault.		
208	781MW-12	14a	9/17/2024	Yes	No	Yes	Good	No	Yes	No	No cap. No lock.			TOC is female threaded PVC so J-plug is not tightly fit. Missing lid prevents locking.
209	781MW-13	14a	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
210	781MW-13R	14a	9/17/2024	Yes	No	No	Good	Yes	Yes	No				
211	781MW-14	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No	No cap. No lock.			No lid present for outer protective casing.
212	781MW-15	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No				
213	781MW-16	14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No	No cap. No lock.			No lid present for outer protective casing.
214	781MW-17	13, 14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No	No cap. No lock.			No lid present for outer protective casing.
215	781MW-18	13, 14a	9/17/2024	Yes	No	Yes	Good	N/A	No	No	No cap. No lock.			Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation.
216	781MW-19	13, 14a	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No	No cap. No lock.			No lid present for outer protective casing.
217	781MW-20	13, 14a, 14b	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No				
218	781MW-21	13, 14b	9/17/2024	Yes	No	Yes	Good	Yes	Yes	No				
219	781PAIW-1	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation.
220	781PAIW-2	14a	9/17/2024	Yes	No	No	N/A	N/A	No	No				Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation.
221	781PPRW-1	13, 14a	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
222	781PPRW-2	13, 14a	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
223	781PPRW-3	14a	9/17/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
224	781PPRW-4	14a	9/17/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
225	781PPRW-5	14a	9/17/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation.
226	781PPRW-6	14a	9/17/2024	Yes	No	Yes	Good	N/A	No	No				Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater elevation.
227	781PPRW-7	14a	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head adapted for sparging.
228	781PPRW-8	14a	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible. TOC survey is inaccurate to calculate groundwater
229	781PPRW-9	14a	9/17/2024	Yes	No	No	Good	N/A	-	No				Well head adapted for sparging.
230	781VBS-1	14a	9/17/2024	Yes	No	Yes	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
231	781VBS-2	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
232	781VBS-3	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
233	781VBS-4	14a	9/17/2024	Yes	No	Yes	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
234	781VBS-5	13, 14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
235	781VBS-6	13, 14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
236	781VBS-7	13, 14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
237	781VBS-8	14a	9/17/2024	Yes	No	No	Good	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
238	781VBS-9	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
239	781VBS-10	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
240	781VBS-11	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
241	781VBS-12	14a	9/17/2024	Yes	No	No	N/A	N/A	Yes	No				Well head adapted for sparging. Lock is not compatible.
242	AOC9MW-05	4	9/19/2024	Yes	No	-	-	-	-	-	In safety area, need escort to access.			
243	AOC9MW-06	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
244	AOC9MW-07	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Area around well needs to be maintained. Used hedge trimmer to access.	Remove overgrown vegetation.		
245	AOC9MW-08	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
246	AOC9MW-9BR	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
247	AOC9MW-11BR	4	Not Visited	No	No	Yes	Good	Yes	Yes	Yes	Not located in vegetation next to Building 0913.	Locate. Remove overgrown vegetation.		
248	AOC9MW-12	4	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Vault does not allow for installation of a lock, however, well is located within secured airfield fence line.
249	AOC9MW-13	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
250	AOC9MW-14	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
251	AOC9MW-15	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
252	AOC9MW-16	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
253	AOC9MW-17	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes	Area around well needs to be maintained. Used hedge trimmer to access.	Remove overgrown vegetation.		
254	AOC9MW-18	4	10/7/2024	Yes	No	Yes	Good	Yes	Yes	Yes	In deployed resources area, need to call number on gate to access.			
255	AOC9MW-19	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
256	AOC9MW-20	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				Installed 2022.
257	AOC9MW-21	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				Installed 2022.
258	AOC9MW-22	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				Installed 2022.
259	AOC9MW-23	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				Installed 2022.
260	AOC9MW-24	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				Installed 2022.
261	AOC9TW-95	4	Not Visited	No	No	-	-	-	-	-	Well not found at given location, confirmed gone.	Remove from inventory.	Not found.	
262	G009-MW01	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
263	G009-MW02	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
264	G009-MW03	4	9/19/2024	Yes	No	Yes	Bad	No	Yes	Yes	Well is destroyed.	Abandon.		Well is destroyed. Recommend proper abandonment.
265	G009-MW04	4	9/19/2024	Yes	No	Yes	Poor	Yes	Yes	Yes				
266	WSAMW-4	4	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
267	789MW-46R	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
268	789MW-63R	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
269	789MW-64	9a	9/19/2024	Yes	No	Yes	Poor	No	Yes	No		Abandon.		Heavily damaged by mower in 2023.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
270	789MW-83	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No		Replace vault, redevelop, and resurvey.		Replace vault, redevelop, and re-survey prior to any groundwater elevation measurement and sampling. Well head completion does not allow for lock installation.
271	789MW-95	9a	9/19/2024	Yes	No	Yes	Bad	Yes	Yes	No		Repair heavily damaged concrete pad.		
272	789MW-96	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
273	789MW-97	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	Yes				
274	789MW-98	9a	9/19/2024	Yes	No	Yes	Good	No	Yes	No				
275	789MW-99	9a	9/19/2024	Yes	No	Yes	Good	No	Yes	No				
276	789MW-100	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
277	789MW-101	9b	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
278	789MW-102	9b	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
279	789MW-103	9b	9/19/2024	Yes	No	Yes	Destroyed	Yes	Yes	No		Abandon.		Suggest proper abandonment.
280	789MW-134	9a, 9b	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No	Flush mount is covered by a cone.	New vault.		Well head completion does not allow for lock installation. Vault threads damaged, could not bolt.
281	789MW-135	9a, 9b	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No	Flush mount is covered by a blue bucket.			Well head completion does not allow for lock installation.
282	789MW-214	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
283	789MW-215	9a, 9b	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
284	789MW-216	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
285	789MW-222	9a, 9b	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
286	789MW-223	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
287	789MW-250	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
288	789MW-251	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
289	789MW-252	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
290	789MW-253	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
291	789MW-254	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
292	789MW-255	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
293	789MW-256	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
294	789MW-257	9b	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
295	789RW-200	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
296	789RW-201	9a, 9b	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
297	789RW-202	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
298	789RW-203	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
299	789RW-204	9a	9/19/2024	Yes	No	No	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
300	789RW-205	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
301	789RW-206	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
302	789RW-207	9a	9/19/2024	Yes	No	No	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
303	789RW-208	9a, 9b	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
304	789RW-209	9a	9/19/2024	Yes	No	No	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
305	789RW-210	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
306	789RW-211	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
307	789RW-212	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
308	789RW-213	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
309	789RW-217	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
310	789RW-218	9a	9/19/2024	Yes	No	Yes	N/A	N/A	Yes	No		Redevelop.		Well head completion does not allow for lock installation. Soils and unknown debris have likely fallen into the well while the surface completion was damaged. The well must be cleared of potential debris and redeveloped prior to any use.
311	789RW-219	9a	9/19/2024	Yes	No	Yes	Good	Yes	Yes	No				
312	789RW-220	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
313	789RW-221	9a	9/19/2024	Yes	No	Yes	Good	N/A	Yes	No				Well head completion does not allow for lock installation.
314	MW01001	10	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				
315	MW01003	10	9/23/2024	Yes	No	Yes	Good	N/A	Yes	No				Vault does not allow for installation of a lock.
316	MW02001	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
317	MW02002	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
318	MW02003	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
319	MW02004	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
320	MW03001	7	9/23/2024	Yes	No	No	Good	N/A	-	-				Vault does not allow for installation of a lock.
321	MW03002	7	9/23/2024	Yes	No	Yes	Good	N/A	-	-				Vault does not allow for installation of a lock.
322	MW03003	7	9/23/2024	Yes	No	Yes	Good	N/A	-	-				Vault does not allow for installation of a lock.
323	MW05001	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
324	MW05002	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
325	MW05003	7	9/23/2024	Yes	No	-	-	N/A	-	-				Vault does not allow for installation of a lock.
326	MW06001	7	9/23/2024	Yes	No	No	Good	N/A	-	-		Add ID.		Vault does not allow for installation of a lock.
327	MW06002	7	9/23/2024	Yes	No	No	Good	N/A	-	-		Add ID.		Vault does not allow for installation of a lock.
328	MW07002	7	9/23/2024	Yes	No	No	Good	N/A	-	-		Add ID.		Vault does not allow for installation of a lock.
329	MW07003	7	9/23/2024	Yes	No	No	Good	N/A	-	-		Add ID.		Vault does not allow for installation of a lock.
330	MW07004	7	9/23/2024	Yes	No	No	Good	N/A	-	-		Add ID.		Vault does not allow for installation of a lock.
331	MW08001	7	9/23/2024	Yes	No	-	Good	-	-	-				
332	MW08002	7	9/23/2024	Yes	No	-	Poor	-	-	-		Repair/Replace vault.		Repair/replace vault and resurvey prior to water elevation measurement.
333	MW08003	7	9/23/2024	Yes	No	-	Poor	-	-	-		Repair/Replace vault.		Repair/replace vault and resurvey prior to water elevation measurement.
334	MW09001	4	10/7/2024	Yes	No	Yes	Good	N/A	Yes	No	In deployed resources area, call number on gate to access.			Vault does not allow for installation of a lock.
335	MW09004	4	10/7/2024	Yes	No	Yes	N/A	N/A	Yes	No	In deployed resources area, call number on gate to access.			Vault does not allow for installation of a lock.
336	MW10001	5	9/20/2024	Yes	No	-	-	N/A	-	-	In a clearing where the road/pathway curves.	Add ID. Remove overgrown vegetation.		Vault does not allow for installation of a lock.
337	MW10002	5	Not Visited	No	No	-	-	N/A	-	-		Remove from inventory.	Unable to locate.	Vault does not allow for installation of a lock.
338	MW10003	5	9/20/2024	Yes	No	-	-	N/A	-	-	Off the right hand side of the road/pathway, covered by grass. Only a sliver of the concrete pad was visible, vegetation was cleared.	Add ID.		Vault does not allow for installation of a lock.
339	MW11001	7	9/23/2024	Yes	No	-	-	N/A	-	-	Overgrown at surface. No Marker.	Add ID.		Vault does not allow for installation of a lock.
340	MW11002	7	9/23/2024	Yes	No	-	-	N/A	-	-	Overgrown at surface. No Marker.	Add ID.		Vault does not allow for installation of a lock.
341	MW11003	7	9/23/2024	Yes	No	-	-	N/A	-	-	Overgrown at surface. No Marker.	Add ID.		Vault does not allow for installation of a lock.

TABLE 1
2024 Well Inventory Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2024 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2024	General Comments and Comments Carried Over From Previous Well Inventories
342	MW14001	8	9/23/2024	Yes	No	Yes	N/A	N/A	Yes	No				1" PVC stick-up marker with 1" stick-up well.
343	MW14002	8	Not Visited	No	No	Yes	N/A	N/A	Yes	No	Found one bollard at location.	Locate.	Unable to locate.	1" PVC stick-up marker with 1" stick-up well.
344	MW14003	8	9/23/2024	Yes	No	Yes	N/A	N/A	Yes	No				1" PVC stick-up marker with 1" stick-up well.
345	MW14004	8	9/23/2024	Yes	No	Yes	Good	N/A	Yes	No				1" PVC stick-up marker with flush mount vault. Vault does not allow for installation of a lock.
346	MW14005	8	9/23/2024	Yes	No	Yes	N/A	N/A	Yes	No				1" PVC stick-up marker with 1" stick-up well.
347	AP1MW-1	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				
348	AP1MW-2	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				
349	AP1MW-3	8	9/23/2024	Yes	No	Yes	Good	-	-	-	Located only.			
350	AP1MW-4	8	9/23/2024	Yes	No	Yes	Good	-	-	-	Located only.			
351	AP1MW-5	8	9/23/2024	Yes	No	Yes	Good	Yes	Yes	No				

Total wells sampled in 2024:	80
Total wells not sampled in 2024:	271
AFFF wells inspected in 2024:	33
Total wells located in 2024:	338
Total wells not located in 2024:	13
Wells requiring maintenance in 2025:	65

Notes:

" = inch

bgs = below ground surface

ID = Identification

ft btoc = feet below top of casing

N/A = Not applicable

AFFF = Aqueous film forming foam

PVC = Polyvinyl chloride

SS = Stainless steel

TOC = Top of casing

USGS - United States Geological Survey

This page intentionally left blank.

Table 2. Static Well Details

This page intentionally left blank.

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
1	ANGMW-1	Monitoring Well	FT030 - Not Used	1182056.00	1130500.00	2" PVC	Flush mount	18.0	-	-	-	8.0 - 18.0	10.0
2	LF1MW-UNK-01	Monitoring Well	LF001 - Not Used	approx:	approx:	2" PVC	Stick-up	-	-	-	-	- - -	-
3	LF1MW-UNK-02	Monitoring Well	LF001 - Not Used	approx:	approx:	2" PVC	Stick-up	-	-	-	-	- - -	-
4	LF1MW-UNK-03	Monitoring Well	LF001 - Not Used	approx:	approx:	2" PVC	Stick-up	-	-	-	-	- - -	-
5	LF1MW-UNK-04	Monitoring Well	LF001 - LTM	1183682.00	1132543.00	4" PVC	Stick-up	13.0	502.31	504.18	1.87	8.0 - 13.0	5.0
6	LF1MW-UNK-05	Monitoring Well	LF001 - LTM	1183270.00	1132922.00	4" PVC	Stick-up	17.0	506.13	512.5	6.37	12.0 - 17.0	5.0
7	LF1P-5	Monitoring Well	LF001 - LTM	1183482.00	1132160.00	4" PVC	Stick-up	20.0	494.91	496.94	2.03	15.0 - 20.0	5.0
8	LF1MW-5	Monitoring Well	LF001 - LTM	1183506.00	1132374.00	4" PVC	Stick-up	20.0	494.74	496.51	1.77	10.0 - 20.0	10.0
9	LF1MW-6	Monitoring Well	LF001 - LTM	1183754.00	1132441.00	4" PVC	Stick-up	15.0	497.36	499.15	1.79	5.0 - 15.0	10.0
10	LF1MW-10	Monitoring Well	LF001 - LTM	1183544.31	1132764.36	2" SS	Stick-up	30.0	528.08	530.65	2.57	20.0 - 30.0	10.0
11	LF1MW-11	Monitoring Well	LF001 - LTM	1184166.39	1132207.50	2" SS	Stick-up	12.5	499.38	502.08	2.70	2.5 - 12.5	10.0
12	LF1MW-12	Monitoring Well	LF001 - LTM	1184381.05	1132127.83	2" SS	Stick-up	13.0	501.82	504.38	2.56	3.0 - 13.0	10.0
13	LF1MW-13	Monitoring Well	LF001 - LTM	1183192.36	1132127.04	2" SS	Stick-up	20.0	492.91	495.33	2.42	10.0 - 20.0	10.0
14	LF1MW-14	Monitoring Well	LF001 - LTM	1184033.70	1131755.80	2" SS	Stick-up	12.5	501.44	504.34	2.90	2.5 - 12.5	10.0
15	LF1MW-103	Monitoring Well	LF001 - LTM	1183707.24	1132550.91	2" SS	Stick-up	32.8	505.27	507.93	2.66	22.8 - 32.8	10.0
16	MWSAR03	Monitoring Well	LF001 - LTM	1183824.00	1133585.00	2" PVC	Stick-up	22.0	533.28	535.09	1.81	12.0 - 22.0	10.0
17	LF2MW-4	Monitoring Well	LF002 - LTM	1177293.00	1139871.00	2" PVC	Stick-up	38.8	553.54	555.02	1.48	28.9 - 38.8	10.0
18	LF2MW-12	Monitoring Well	LF002 - LTM	1176923.27	1139287.75	2" SS	Stick-up	18.0	527.14	529.50	2.36	8.0 - 18.0	10.0
19	LF2MW-13	Monitoring Well	LF002 - LTM	1177362.29	1139036.66	2" Steel	Stick-up	14.5	522.50	524.48	1.98	4.5 - 14.5	10.0
20	LF2MW-14	Monitoring Well	LF002 - LTM	1177793.86	1140216.73	2" SS	Stick-up	15.5	536.85	539.57	2.72	5.5 - 15.5	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
21	LF2MW2-1	Monitoring Well	LF002 - LTM	1177656.00	1139216.00	4" PVC	Stick-up	32.0	-	-	-	22.0 - 32.0	10.0
22	LF2MW-UNK-01	Monitoring Well	LF002 - Not Used	Approx:	Approx:	2"	Stick-up	-	-	-	-	- - -	-
23	LF2MW-100	Monitoring Well	LF002 - LTM	1176912.42	1139303.67	2" SS	Stick-up	64.0	526.58	529.20	2.62	54.0 - 64.0	10.0
24	LF7MW-22	Monitoring Well	LF003 - LTM	1178159.21	1136704.00	2" SS	Flush mount	10.9	485.10	486.63	1.53	6.0 - 10.9	4.9
25	LF7MW-23	Monitoring Well	LF003 - LTM	1177765.45	1137119.19	2" PVC	Flush mount	14.0	486.04	487.83	1.79	4.0 - 14.0	10.0
26	LF7MW-26	Monitoring Well	LF003 - LTM	1178060.22	1137047.43	2" SS	Stick-up	16.5	499.77	502.03	2.26	6.5 - 16.5	10.0
27	LF7MW-27	Monitoring Well	LF003 - LTM	1178508.55	1136580.51	2" SS	Stick-up	12.5	500.96	502.93	1.97	2.5 - 12.5	10.0
28	LF7MW-28	Monitoring Well	LF003 - LTM	1177972.90	1136790.61	2" SS	Flush mount	11.5	485.81	487.83	2.02	1.5 - 11.5	10.0
29	LF7MW-29	Monitoring Well	LF003 - LTM	1178541.35	1137510.34	2" Steel	Stick-up	21.0	522.46	525.56	3.10	11.0 - 21.0	10.0
30	LF7MW-30	Monitoring Well	LF003 - LTM	1177806.46	1137473.59	2" SS	Stick-up	11.5	494.39	496.17	1.78	1.5 - 11.5	10.0
31	LF7MW-100	Monitoring Well	LF003 - LTM	1178139.99	1136973.28	4" PVC	Stick-up	43.0	500.99	503.57	2.58	33.0 - 43.0	10.0
32	LF5MW-1A	Monitoring Well	LF007 - LTM	1173976.70	1133819.84	2" PVC	Stick-up	22.9	476.15	478.50	2.35	12.9 - 22.9	10.0
33	LF5MW-3	Monitoring Well	LF007 - LTM	1173953.00	1133260.00	2" PVC	Stick-up	13.2	460.31	462.45	2.14	3.2 - 13.2	10.0
34	LF5MW-4	Monitoring Well	LF007- Not Used	1173569.42	1133541.14	2" SS	Stick-up	14.8	457.43	459.66	2.23	2.0 - 12.0	10.0
35	LF5MW-5	Monitoring Well	LF007 - LTM	1173619.07	1133630.64	2" SS	Stick-up	12.0	459.58	461.49	1.91	2.0 - 12.0	10.0
36	MW49D07	Monitoring Well	LF007 - LTM	1173539.00	1133247.00	2" PVC	Stick-up	14.0	457.07	459.51	2.44	4.0 - 14.0	10.0
37	LF5MW-100R	Monitoring Well	LF007 - LTM	1173686.99	1133338.49	2" SS	Stick-up	67.4	447.63	450.76	3.13	57.4 - 67.4	10.0
38	SD052-04-IW01	Injection Well	SD052-04 - Injections Only	1172408.40	1134923.80	2" PVC	Stick-up	53.9	455.60	458.79	3.19	33.7 - 53.7	20.0
39	SD052-04-IW02	Injection Well	SD052-04 - Injections Only	1172389.80	1134939.70	2" PVC	Stick-up	55.3	455.00	457.13	2.13	35.1 - 55.1	20.0
40	SD052-04-IW03	Injection Well	SD052-04 - Injections Only	1172393.30	1134950.40	2" PVC	Stick-up	53.5	457.68	455.40	-2.28	33.3 - 53.3	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
41	SD052-04-IW04	Injection Well	SD052-04 - Injections Only	1172449.40	1134992.70	2" PVC	Stick-up	54.8	457.40	459.15	1.75	34.6 - 54.6	20.0
42	LF6IW-01	Injection Well	SD052-04 - Injections Only	1172402.36	1134947.75	2" PVC	Stick-up	47.0	455.70	457.69	1.99	37.0 - 47.0	10.0
43	LF6IW-02	Injection Well	SD052-04 - Injections Only	1172401.39	1134941.80	2" PVC	Stick-up	55.0	455.45	457.41	1.96	45.0 - 55.0	10.0
44	LF6IW-03	Injection Well	SD052-04 - Injections Only	1172396.27	1134953.35	2" PVC	Stick-up	55.0	455.80	457.62	1.82	45.0 - 55.0	10.0
45	LF6IW-04	Injection Well	SD052-04 - Injections Only	1172401.15	1134956.96	2" PVC	Stick-up	55.0	456.43	458.77	2.34	45.0 - 55.0	10.0
46	LF6IW-05	Injection Well	SD052-04 - Injections Only	1172400.69	1134930.30	2" PVC	Stick-up	47.0	455.26	456.97	1.71	37.0 - 47.0	10.0
47	LF6IW-06	Injection Well	SD052-04 - Injections Only	1172396.53	1134935.76	2" PVC	Stick-up	55.0	455.50	457.67	2.17	45.0 - 55.0	10.0
48	LF6MW-1	Monitoring Well	LF009 - LTM	1172661.00	1135717.00	2" PVC	Stick-up	67.3	518.12	519.33	1.21	57.3 - 67.3	10.0
49	LF6MW-12	Monitoring Well	LF009 - LTM	1172397.87	1134944.13	2" PVC	Stick-up	51.0	455.61	457.59	1.98	41.0 - 51.0	10.0
50	LF6MW-13RD	Monitoring Well	SD052-04 - LTM	1172084.49	1134909.71	2" PVC	Stick-up	40.0	451.51	453.41	1.90	20.0 - 40.0	20.0
51	LF6MW-14BR	Monitoring Well	LF009 - Not Used	1172017.01	1135059.12	2" PVC	Stick-up	112.5	454.17	456.61	2.44	102.5 - 112.5	10.0
52	LF6MW-16	Monitoring Well	SD052-04 - LTM	1172393.53	1134940.32	2" PVC	Stick-up	47.0	455.41	457.39	1.98	37.0 - 47.0	10.0
53	LF6MW-17	Monitoring Well	SD052-04 - LTM	1172392.96	1134947.91	2" PVC	Stick-up	55.0	456.04	457.96	1.92	45.0 - 55.0	10.0
54	LF6MW-18	Monitoring Well	SD052-04 - Not Used	1172377.76	1134946.07	2" PVC	Stick-up	47.0	455.59	457.47	1.88	37.0 - 47.0	10.0
55	LF6MW-19	Monitoring Well	SD052-04 - Not Used	1172384.58	1134953.47	2" PVC	Stick-up	55.0	455.83	457.70	1.87	45.0 - 55.0	10.0
56	LF6MW-20	Monitoring Well	SD052-04 - LTM	1172390.70	1134934.67	2" PVC	Stick-up	51.0	455.35	457.31	1.96	41.0 - 51.0	10.0
57	LF6MW-27	Monitoring Well	SD052-04 - Not Used	1172473.54	1134837.28	2" PVC	Stick-up	55.0	453.46	455.48	2.02	35.0 - 55.0	20.0
58	LF6MW-28	Monitoring Well	SD052-04 - Not Used	1172500.73	1134993.37	2" PVC	Stick-up	45.0	455.78	457.03	1.25	25.0 - 45.0	20.0
59	LF6MW-29	Monitoring Well	SD052-04 - Not Used	1172485.75	1135172.31	2" PVC	Stick-up	37.0	466.62	468.54	1.92	17.0 - 37.0	20.0
60	LF6MW-30	Monitoring Well	SD052-04 - Not Used	1172383.69	1135083.41	2" PVC	Stick-up	45.0	459.13	461.04	1.91	25.0 - 45.0	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
61	LF6MW-31	Monitoring Well	SD052-04 - LTM	1172368.48	1134875.43	2" PVC	Stick-up	55.0	453.20	455.17	1.97	35.0 - 55.0	20.0
62	LF6MW-32	Monitoring Well	SD052-04 - Not Used	1172224.69	1135166.03	2" PVC	Stick-up	44.5	462.67	464.56	1.89	34.5 - 44.5	10.0
63	LF6MW-39	Monitoring Well	SD052-04 - LTM	1172082.35	1135006.96	2" PVC	Stick-up	32.0	456.70	458.50	1.80	22.0 - 32.0	10.0
64	LF6TW-33	Temporary Monitoring Well	SD052-04 - LTM	1172409.41	1134923.99	1" PVC	Stick-up	39.0	456.17	459.74	3.57	19.0 - 39.0	20.0
65	LF6TW-34	Temporary Monitoring Well	SD052-04 - LTM	1172448.34	1134987.84	1" PVC	Stick-up	55.0	457.60	460.00	2.40	35.0 - 55.0	20.0
66	LF6TW-35	Temporary Monitoring Well	SD052-04 - LTM	1172393.30	1135014.77	1" PVC	Stick-up	55.0	457.39	459.27	1.88	35.0 - 55.0	20.0
67	LF6TW-36	Temporary Monitoring Well	SD052-04 - LTM	1172338.33	1134950.04	1" PVC	Stick-up	55.0	455.08	459.08	4.00	35.0 - 55.0	20.0
68	LF6TW-37	Temporary Monitoring Well	SD052-04 - Not Used	1172337.31	1135007.88	1" PVC	Stick-up	55.0	455.98	459.35	3.37	35.0 - 55.0	20.0
69	LF6TW-38	Temporary Monitoring Well	SD052-04 - LTM	1172288.45	1134986.99	1" PVC	Stick-up	55.0	457.35	460.53	3.18	35.0 - 55.0	20.0
70	LF6VMW-10R2	Monitoring Well	LF009 - LTM	1172210.55	1135288.97	2" PVC	Stick-up	35.0	464.20	466.14	1.94	25.0 - 35.0	10.0
71	LF6VMW-13R	Monitoring Well	SD052-04 - LTM	1172095.12	1134923.10	2" PVC	Stick-up	37.0	453.12	454.66	1.54	17.0 - 37.0	20.0
72	LF6VMW-14	Monitoring Well	SD052-04 - Not Used	1172000.51	1135036.68	2" PVC	Stick-up	42.0	452.69	454.87	2.18	22.0 - 42.0	20.0
73	LF6VMW-15R	Monitoring Well	SD052-04 - Not Used	1171960.35	1135290.01	2" PVC	Stick-up	40.0	464.42	466.61	2.19	30.0 - 40.0	10.0
74	LF6VMW-17D	Monitoring Well	LF009 - LTM	1172076.60	1135535.30	2" SS	Stick-up	50.0	465.10	467.18	2.08	40.0 - 50.0	10.0
75	LF6VMW-17S	Monitoring Well	LF009 - LTM	1172097.90	1135538.30	2" SS	Stick-up	16.0	464.88	466.69	1.81	6.0 - 16.0	10.0
76	LF6VMW-18	Monitoring Well	LF009 - LTM	1171848.40	1135825.10	2" SS	Stick-up	55.0	460.98	463.15	2.17	45.0 - 55.0	10.0
77	LF6VMW-19	Monitoring Well	LF009 - LTM	1171789.66	1136061.18	2" SS	Stick-up	30.0	459.73	461.34	1.61	20.0 - 30.0	10.0
78	LF6VMW-20	Monitoring Well	LF009 - LTM	1171846.50	1136385.50	2" SS	Stick-up	70.5	461.96	464.79	2.83	60.5 - 70.5	10.0
79	LF6VMW-21	Monitoring Well	LF009 - LTM	1172188.00	1136190.50	2" SS	Stick-up	70.5	495.43	497.74	2.31	60.5 - 70.5	10.0
80	LF6VMW-22	Monitoring Well	LF009 - LTM	1172260.50	1135381.60	2" SS	Stick-up	40.0	465.71	467.64	1.93	30.0 - 40.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
81	LF6VMW-23	Monitoring Well	LF009 - LTM	1172406.00	1135269.20	2" PVC	Stick-up	50.3	467.64	469.65	2.01	40.3 - 50.3	10.0
82	LF6VMW-24	Monitoring Well	LF009 - LTM	1172533.20	1135097.50	2" SS	Stick-up	51.0	463.25	465.76	2.51	41.0 - 51.0	10.0
83	LF6VMW-25	Monitoring Well	LF009 - LTM	1172589.50	1134850.20	2" SS	Stick-up	49.0	455.60	457.69	2.09	39.0 - 49.0	10.0
84	LF6VMW-26	Monitoring Well	SD052-04/LF009 - LTM	1172226.72	1134927.56	2" SS	Stick-up	55.0	455.08	457.90	2.82	45.0 - 55.0	10.0
85	TMCMW-9	Monitoring Well	LF009 - LTM	1172582.00	1134859.00	4" PVC	Stick-up	28.0	455.48	457.16	1.68	18.0 - 28.0	10.0
86	TMC-USGS-2	Monitoring Well	LF009 - LTM	1171618.05	1135664.49	2" PVC	Stick-up	26.5	452.13	454.50	2.37	24.0 - 26.5	2.5
87	LAWMW-19	Monitoring Well	USGS well - Not Used	1171023.00	1137732.00	2" PVC	Stick-up	51.8	489.97	491.76	1.79	41.8 - 51.8	10.0
88	TMC-USGS-1	Monitoring Well	None - Not Used	1171250.00	1135344.00	2" PVC	Stick-up	21.5	454.91	457.81	2.90	19.0 - 21.5	2.5
89	782MW-1	Monitoring Well	SD052-01 - Not Used	1175125.90	1137634.60	2" PVC	Flush mount	32.7	473.76	473.58	-0.18	22.7 - 32.7	10.0
90	782MW-1R	Monitoring Well	SD052-01 - PFC Investigation	1175131.00	1137630.00	2" PVC	Flush mount	28.3	473.62	473.38	-0.24	18.3 - 28.3	10.0
91	782MW-3	Monitoring Well	SD052-01 - Not Used	1175289.30	1137307.59	2" PVC	Flush mount	19.0	473.81	473.49	-0.32	9.0 19.0	10.0
92	782MW-3R	Monitoring Well	SD052-01 - PFC Investigation	1175294.00	1137315.00	2" PVC	Flush mount	31.6	473.67	473.33	-0.34	16.6 - 31.6	15.0
93	782MW-5	Monitoring Well	SD052-01 - Not Used	1174918.45	1136711.77	2" PVC	Flush mount	25.0	477.30	476.63	-0.67	15.0 - 25.0	10.0
94	782MW-6D	Monitoring Well	SD052-01 - Not Used	1174869.57	1137670.31	2" PVC	Stick-up	48.0	478.54	478.55	0.01	38.0 - 48.0	10.0
95	782MW-6R2	Monitoring Well	SD052-01 - Not Used	1174890.35	1137643.75	2" PVC	Stick-up	34.5	476.82	478.42	1.60	19.5 - 34.5	15.0
96	782MW-9	Monitoring Well	SD052-01 - PFC Investigation	1175045.31	1137985.45	2" PVC	Flush mount	30.0	476.51	476.54	0.03	15.0 - 30.0	15.0
97	782MW-10	Monitoring Well	SD052-01 - LTM	1174739.67	1137498.35	2" PVC	Flush mount	34.0	477.79	477.50	-0.29	19.0 - 34.0	15.0
98	782MW-11	Monitoring Well	SD052-01 - PFC Investigation	1175150.04	1137909.34	2" PVC	Stick-up	32.7	475.68	478.21	2.53	22.7 - 32.7	10.0
99	782MW-12	Monitoring Well	SD052-01 - PFC Investigation	1175304.72	1137742.26	2" PVC	Flush mount	33.0	475.81	475.56	-0.25	23.0 - 33.0	10.0
100	782-MW184	Monitoring Well	SD052-01 - Not Used	1174819.11	1138003.00	2" PVC	Flush mount	74.5	476.20	475.86	-0.34	64.5 - 74.5	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
101	782VMW-76	Monitoring Well	SD052-01 - LTM	1174418.22	1137171.89	2" PVC	Flush mount	43.0	477.86	477.59	-0.27	33.0 - 43.0	10.0
102	782VMW-78	Monitoring Well	SD052-01 - LTM	1174578.68	1137025.78	2" PVC	Stick-up	42.0	478.26	481.22	2.96	32.0 - 42.0	10.0
103	782VMW-81	Monitoring Well	SD052-01 - LTM	1174369.98	1136784.76	2" PVC	Stick-up	50.0	477.71	479.57	1.86	40.0 - 50.0	10.0
104	782VMW-82	Monitoring Well	SD052-01 - Not Used	1174499.71	1136644.46	2" PVC	Stick-up	48.0	475.49	478.06	2.57	38.0 - 48.0	10.0
105	782VMW-83	Monitoring Well	SD052-01 - Not Used	1174121.75	1136506.61	2" PVC	Stick-up	35.0	477.72	480.13	2.41	25.0 - 35.0	10.0
106	782VMW-84	Monitoring Well	SD052-01 - LTM	1174821.59	1137992.22	2" PVC	Flush mount	44.5	476.40	476.08	-0.32	34.5 - 44.5	10.0
107	782VMW-84D	Monitoring Well	SD052-01 - LTM	1174796.74	1138001.78	2" PVC	Flush mount	56.5	475.57	475.18	-0.39	41.5 - 56.5	15.0
108	782VMW-85	Monitoring Well	SD052-01 - Not Used	1175001.90	1137788.48	2" PVC	Stick-up	39.0	475.70	478.02	2.32	29.0 - 39.0	10.0
109	782VMW-86	Monitoring Well	SD052-01 - Not Used	1175194.30	1137587.73	2" PVC	Stick-up	37.0	475.65	477.68	2.03	27.0 - 37.0	10.0
110	782VMW-87	Monitoring Well	SD052-01 - Not Used	1174719.49	1138182.13	2" PVC	Flush mount	40.0	476.86	476.27	-0.59	30.0 - 40.0	10.0
111	782VMW-88	Monitoring Well	SD052-01 - Not Used	1174912.33	1138272.99	2" PVC	Flush mount	40.0	478.15	477.75	-0.40	30.0 - 40.0	10.0
112	782VMW-89	Monitoring Well	SD052-01 - Not Used	1175100.54	1137690.09	2" PVC	Stick-up	40.0	475.94	478.85	2.91	25.0 - 40.0	15.0
113	782VMW-90	Monitoring Well	SD052-01 - Not Used	1175018.57	1137506.82	2" PVC	Stick-up	30.0	476.23	478.95	2.72	20.0 - 30.0	10.0
114	782VMW-92	Monitoring Well	SD052-01 - Not Used	1174479.88	1137671.17	2" PVC	Flush mount	40.0	476.99	476.65	-0.34	30.0 - 40.0	10.0
115	782VMW-93	Monitoring Well	SD052-01 - Not Used	1174569.71	1137325.35	2" PVC	Flush mount	40.0	477.87	477.57	-0.30	30.0 - 40.0	10.0
116	782VMW-94	Monitoring Well	SD052-01 - Not Used	1174743.61	1137348.67	2" PVC	Flush mount	44.5	478.3	478.03	-0.27	34.5 - 44.5	10.0
117	782VMW-95	Monitoring Well	SD052-01 - Not Used	1174876.72	1137232.26	2" PVC	Flush mount	35.0	476.49	476.16	-0.33	20.0 - 35.0	15.0
118	782VMW-96	Monitoring Well	SD052-01 - LTM	1174603.52	1137545.52	2" PVC	Flush mount	43.0	477.13	476.73	-0.40	33.0 - 43.0	10.0
119	782VMW-97	Monitoring Well	SD052-01 - Not Used	1174073.12	1136622.81	2" PVC	Stick-up	35.0	478.52	480.76	2.24	25.0 - 35.0	10.0
120	782VMW-98	Monitoring Well	SD052-01 - Not Used	1173953.03	1136359.76	2" PVC	Stick-up	35.0	477.06	479.47	2.41	25.0 - 35.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
121	782VMW-99	Monitoring Well	SD052-01 - Not Used	1173703.09	1136597.73	2" PVC	Stick-up	35.0	477.83	480.89	3.06	20.0 - 35.0	15.0
122	782VMW-100	Monitoring Well	SD052-01 - LTM	1174894.76	1138716.31	2" PVC	Stick-up	25.0	457.10	459.94	2.84	10.0 - 25.0	15.0
123	782VMW-101	Monitoring Well	SD052-01 - LTM	1174658.16	1138910.74	2" PVC	Stick-up	22.0	451.11	453.95	2.84	7.0 - 22.0	15.0
124	782VMW-102	Monitoring Well	SD052-01 - LTM	1174386.72	1139063.60	2" PVC	Stick-up	23.0	448.82	451.84	3.02	8.0 - 23.0	15.0
125	782VMW-104	Monitoring Well	SD052-01 - LTM	1174163.56	1136567.00	2" PVC	Stick-up	33.0	477.04	479.63	2.59	18.0 - 33.0	15.0
126	782VMW-105B	Monitoring Well	SD052-01 - LTM	1174207.49	1136605.09	2" PVC	Stick-up	42.0	477.37	480.25	2.88	27.0 - 42.0	15.0
127	782VMW-121	Monitoring Well	SD052-01 - LTM	1174778.29	1138757.34	2" PVC	Stick-up	25.0	458.06	459.87	1.81	10.0 - 25.0	15.0
128	782VMW-121D	Monitoring Well	SD052-01 - LTM	1174761.65	1138752.45	2" PVC	Stick-up	31.0	458.81	460.71	1.90	21.0 - 31.0	10.0
129	AP2MW-3	Monitoring Well	SD052-01 - LTM	1174551.00	1138744.00	2" PVC	Flush mount	33.6	465.97	465.63	-0.34	19.0 - 33.6	14.6
130	775EW-1	Extraction Well converted to Injection Well	SD052-02 - Injections	1173032.34	1135795.01	4" SS	Flush mount	76.0	516.72	516.56	-0.16	56.0 - 76.0	20.0
131	775EW-1R	Extraction Well converted to Injection Well	SD052-02 - Injections	1172983.69	1135816.60	4" SS	Flush mount	-	516.40	515.55	-0.85	- - -	-
132	775EW-3	Extraction Well converted to Injection Well	SD052-02 - Injections	1172996.82	1135753.37	4" SS	Flush mount	-	516.02	515.16	-0.86	- - -	-
133	775MW-2	Monitoring Well	SD052-02 - Not Used	1173493.00	1135938.00	2" PVC	Stick-up	65.0	514.08	515.65	1.57	50.0 - 65.0	15.0
134	775MW-6	Monitoring Well	SD052-02 - LTM	1173123.00	1135631.00	2" PVC	Stick-up	78.0	517.18	518.02	0.84	68.0 - 78.0	10.0
135	775-MW20	Monitoring Well	SD052-02 - LTM	1172598.94	1135787.11	2" PVC	Stick-up	120.2	518.14	520.35	2.21	110.2 - 120.2	10.0
136	775-MW20R	Monitoring Well	SD052-02 - LTM	1172590.24	1135795.13	2" PVC	Stick-up	138.7	518.62	519.48	0.86	133.7 - 138.7	5.0
137	775-MW20RBR	Monitoring Well	SD052-02 - Not Used	1172492.89	1135900.74	2" PVC	Stick-up	169.7	518.58	519.50	0.92	159.7 - 169.7	10.0
138	775MW-27	Monitoring Well	SD052-02 - LTM	1173004.19	1135837.05	2" PVC	Flush mount	80.8	516.59	515.99	-0.60	60.8 - 80.8	20.0
139	775MW-28	Monitoring Well	SD052-02 - LTM	1172787.53	1135778.13	2" PVC	Stick-up	91.0	515.72	517.68	1.96	71.0 - 91.0	20.0
140	775VMW-4	Monitoring Well	SD052-02 - LTM	1173227.00	1135813.00	2" PVC	Stick-up	70.0	517.64	518.51	0.87	60.0 - 70.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
141	775VMW-5	Monitoring Well	SD052-02 - LTM	1173147.00	1135890.00	2" PVC	Stick-up	75.0	517.94	518.64	0.70	65.0 - 75.0	10.0
142	775VMW-8	Monitoring Well	SD052-02 - LTM	1172910.00	1135803.00	2" PVC	Stick-up	78.0	517.79	518.22	0.43	68.0 - 78.0	10.0
143	775VMW-9	Monitoring Well	SD052-02 - LTM	1172920.34	1135482.28	2" PVC	Stick-up	99.0	511.92	513.63	1.71	84.0 - 99.0	15.0
144	775VMW-10	Monitoring Well	SD052-02 - LTM	1172769.09	1135613.75	2" PVC	Stick-up	103.0	515.14	517.22	2.08	88.0 - 103.0	15.0
145	775VMW-11	Monitoring Well	SD052-02 - Not Used	1173630.84	1136124.93	2" PVC	Stick-up	57.0	484.66	486.60	1.94	47.0 - 57.0	10.0
146	775VMW-14	Monitoring Well	SD052-02 - Not Used	1173337.31	1136103.63	2" PVC	Stick-up	70.0	513.91	515.85	1.94	60.0 - 70.0	10.0
147	775VMW-15R1	Monitoring Well	SD052-02 - Not Used	1173477.86	1135425.48	2" PVC	Stick-up	104.0	516.54	518.82	2.28	94.0 - 104.0	10.0
148	775VMW-16	Monitoring Well	SD052-02 - Not Used	1172880.00	1136036.31	2" PVC	Stick-up	87.0	518.96	520.94	1.98	77.0 - 87.0	10.0
149	775VMW-18R	Monitoring Well	SD052-02/LF009 - LTM	1173166.52	1135300.79	2" PVC	Stick-up	95.0	508.67	510.71	2.04	85.0 - 95.0	10.0
150	775VMW-19R	Monitoring Well	SD052-02 - LTM	1172790.97	1135700.29	2" PVC	Stick-up	75.0	515.58	517.46	1.88	55.0 - 75.0	20.0
151	775VMW-20R	Monitoring Well	SD052-02/LF009 - LTM	1172499.98	1135888.24	2" PVC	Stick-up	115.0	518.85	521.11	2.26	105.0 - 115.0	10.0
152	775VMW-23	Monitoring Well	SD052-02 - Not Used	1173770.00	1135979.80	2" PVC	Stick-up	35.0	484.35	486.77	2.42	25.0 - 35.0	10.0
153	775VMW-24	Monitoring Well	SD052-02 - Not Used	1173495.87	1136265.91	2" PVC	Stick-up	67.0	483.79	485.40	1.61	57.0 - 67.0	10.0
154	775VMW-25	Monitoring Well	SD052-02 - Not Used	1173593.56	1135622.50	2" PVC	Flush mount	75.0	512.10	511.94	-0.16	65.0 - 75.0	10.0
155	SD052-02_IW-01	Injection Well	SD052-02 - Injections	1173188.90	1135887.00	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
156	SD052-02_IW-02	Injection Well	SD052-02 - Injections	1173178.30	1135912.30	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
157	SD052-02_IW-03	Injection Well	SD052-02 - Injections	1173127.90	1135662.50	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
158	SD052-02_IW-04	Injection Well	SD052-02 - Injections	1173108.00	1135698.10	2" PVC	Flush mount	84.0	-	-	-	64.0 - 84.0	20.0
159	SD052-02_IW-05	Injection Well	SD052-02 - Injections	1173108.90	1135819.70	2" PVC	Flush mount	84.0	-	-	-	64.0 - 84.0	20.0
160	SD052-02_IW-06	Injection Well	SD052-02 - Injections	1173056.80	1135873.60	2" PVC	Flush mount	83.0	-	-	-	63.0 - 83.0	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
161	SD052-02_IW-07	Injection Well	SD052-02 - Injections	1173147.50	1135624.00	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
162	SD052-02_IW-08	Injection Well	SD052-02 - Injections	1173121.50	1135550.20	2" PVC	Flush mount	92.0	-	-	-	72.0 - 92.0	20.0
163	SD052-02_IW-09	Injection Well	SD052-02 - Injections	1173063.10	1135598.80	2" PVC	Flush mount	92.0	-	-	-	72.0 - 92.0	20.0
164	SD052-02_IW-12	Injection Well	SD052-02 - Injections	1173019.30	1135523.30	2" PVC	Flush mount	100.0	-	-	-	80.0 - 100.0	20.0
165	SD052-02_IW-13	Injection Well	SD052-02 - Injections	1172971.00	1135552.50	2" PVC	Flush mount	100.0	-	-	-	80.0 - 100.0	20.0
166	SD052-02_IW-14	Injection Well	SD052-02 - Injections	1172939.20	1135801.90	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
167	817IW-1	Injection Well	SD052-05 - Injections	1180082.76	1135879.96	2" PVC	Stick-up	-	518.59	-	-	- - -	-
168	817IW-2	Injection Well	SD052-05 - Injections	1180076.77	1135885.76	2" PVC	Stick-up	-	518.88	-	-	- - -	-
169	817IW-3	Injection Well	SD052-05 - Injections	1180069.76	1135891.10	2" PVC	Stick-up	-	519.05	-	-	- - -	-
170	817IW-4	Injection Well	SD052-05 - Injections	1180064.86	1135898.52	2" PVC	Stick-up	-	519.23	-	-	- - -	-
171	817IW-5	Injection Well	SD052-05 - Injections	1180059.69	1135903.22	2" PVC	Stick-up	-	519.17	-	-	- - -	-
172	817IW-6	Injection Well	SD052-05 - Injections	1180054.25	1135908.66	2" PVC	Stick-up	-	519.12	-	-	- - -	-
173	817IW-7	Injection Well	SD052-05 - Injections	1180049.52	1135913.91	2" PVC	Stick-up	-	519.29	-	-	- - -	-
174	817IW-8	Injection Well	SD052-05 - Injections	1180043.77	1135917.10	2" PVC	Stick-up	-	519.40	-	-	- - -	-
175	817MW-1	Monitoring Well	SD052-05 - LTM	1180068.47	1135910.04	1" PVC	Stick-up	20.0	519.93	522.10	2.17	10.0 - 20.0	10.0
176	817MW-3	Monitoring Well	SD052-05 - LTM	1180034.09	1135874.52	1" PVC	Stick-up	20.0	517.72	519.80	2.08	10.0 - 20.0	10.0
177	LAWMW-9	Monitoring Well	SD052-05 - LTM	1179884.00	1135570.00	2" PVC	Stick-up	17.0	505.83	507.84	2.01	7.0 - 17.0	10.0
178	WSA-IW01	Injection Well	SD052-05 - Not Used	1179950.44	1135783.51	2" PVC	Stick-up	19.0	512.69	514.77	2.08	9.0 - 19.0	10.0
179	WSA-IW02	Injection Well	SD052-05 - Not Used	1179957.83	1135790.28	2" PVC	Stick-up	20.0	512.39	514.61	2.22	10.0 - 20.0	10.0
180	WSA-IW03	Injection Well	SD052-05 - Not Used	1179958.91	1135800.50	2" PVC	Stick-up	20.0	512.71	515.10	2.39	10.0 - 20.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
181	WSA-IW04	Injection Well	SD052-05 - Not Used	1179949.01	1135811.54	2" PVC	Stick-up	19.5	512.18	514.33	2.15	9.5 - 19.5	10.0
182	WSAMW-2	Monitoring Well	SD052-05 - Not Used	1180469.00	1136049.00	2" PVC	Stick-up	15.2	531.99	533.95	1.96	5.2 - 15.2	10.0
183	WSAMW-3	Monitoring Well	SD052-05 - Not Used	1180971.00	1134913.00	2" PVC	Stick-up	16.3	527.48	530.34	2.86	6.3 - 16.3	10.0
184	WSAMW-8	Monitoring Well	SD052-05 - LTM	1180198.23	1135971.00	2" PVC	Stick-up	14.0	520.37	521.88	1.51	4.0 - 14.0	10.0
185	WSAMW-9	Monitoring Well	SD052-05 - LTM	1179468.66	1135387.24	2" PVC	Stick-up	8.0	482.60	484.19	1.59	3.0 - 8.0	5.0
186	WSAMW-11	Monitoring Well	SD052-05 - Not Used	1179950.70	1135795.44	2" PVC	Stick-up	12.5	512.14	513.89	1.75	7.2 - 12.2	5.0
187	WSAMW-12BR	Monitoring Well	SD052-05 - Not Used	1179451.23	1135646.55	2" PVC	Stick-up	42.0	500.01	502.13	2.12	32.0 - 42.0	10.0
188	WSAMW-13BR	Monitoring Well	SD052-05 - Not Used	1179597.57	1135249.32	2" PVC	Stick-up	43.0	483.08	485.17	2.09	23.0 - 43.0	20.0
189	WSAMW-14BR	Monitoring Well	SD052-05 - Not Used	1180205.21	1135964.95	2" PVC	Stick-up	35.0	518.50	522.01	3.51	24.7 - 34.7	10.0
190	WSA-MW-15	Monitoring Well	SD052-05 - Not Used	1179944.44	1135792.40	2" PVC	Stick-up	21.0	512.04	514.40	2.36	10.0 - 20.0	10.0
191	WSAMW-16	Monitoring Well	SD052-05 - LTM	1179943.17	1135804.76	2" PVC	Stick-up	20.0	511.86	514.18	2.32	10.0 - 20.0	10.0
192	WSAMW-18	Monitoring Well	SD052-05 - LTM	1179990.61	1135831.91	2" PVC	Stick-up	16.0	515.23	516.89	1.66	11.0 - 16.0	5.0
193	WSAMW-19	Monitoring Well	SD052-05 - LTM	1179856.58	1135748.98	2" PVC	Stick-up	18.0	511.79	513.07	1.28	13.0 - 18.0	5.0
194	WSAMW-21	Monitoring Well	SD052-05 - LTM	1179643.16	1135642.04	2" PVC	Stick-up	25.0	509.72	511.68	1.96	15.0 - 25.0	10.0
195	WSAMW-23	Monitoring Well	SD052-05 - LTM	1179679.21	1135866.52	2" PVC	Stick-up	25.0	518.16	519.92	1.76	15.0 - 25.0	10.0
196	WSAVMW-17	Monitoring Well	SD052-05 - LTM	1179785.39	1135658.66	2" SS	Stick-up	25.0	508.83	511.39	2.56	15.0 - 25.0	10.0
197	781MW-1	Monitoring Well	SS054 - LTM	1172759.69	1136628.86	2" PVC	Stick-up	64.5	516.2	515.71	-0.49	49.5 - 64.5	15.0
198	781MW-2	Monitoring Well	SS054 - LTM	1172828.68	1136642.29	2" PVC	Stick-up	65.0	513.3	514.66	1.36	50.0 - 65.0	15.0
199	781MW-3	Monitoring Well	SS054 - LTM	1172754.51	1136721.46	2" PVC	Stick-up	69.0	513.5	514.30	0.80	54.0 - 69.0	15.0
200	781MW-4	Monitoring Well	SS054 - LTM	1172565.01	1136720.25	2" PVC	Stick-up	64.0	513.5	515.89	2.39	54.0 - 64.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
201	781MW-5	Monitoring Well	SS054 - LTM	1172499.44	1136657.45	2" PVC	Stick-up	65.0	515.5	517.04	1.54	55.0 - 65.0	10.0
202	781MW-6	Monitoring Well	SS054 - LTM	1172461.56	1136622.83	2" PVC	Stick-up	64.0	515.9	517.26	1.36	54.0 - 64.0	10.0
203	781MW-7	Monitoring Well	SS054 - LTM	1172555.49	1136524.14	2" PVC	Stick-up	68.0	515.7	517.79	2.09	58.0 - 68.0	10.0
204	781MW-8	Monitoring Well	SS054 - LTM	1172670.37	1136612.59	2" PVC	Flush mount	63.0	514.5	514.26	-0.24	53.0 - 63.0	10.0
205	781MW-9	Monitoring Well	SS054 - LTM	1172729.68	1136670.72	2" PVC	Stick-up	64.0	515.6	516.90	1.30	54.0 - 64.0	10.0
206	781MW-10	Monitoring Well	SS054 - LTM	1172684.63	1136737.68	2" PVC	Stick-up	63.0	513.77	515.26	1.49	53.0 - 63.0	10.0
207	781MW-11	Monitoring Well	SS054 - LTM	1172702.30	1136562.64	2" PVC	Flush mount	65.0	513.8	513.49	-0.31	55.0 - 65.0	10.0
208	781MW-12	Monitoring Well	SS054 - LTM	1172423.31	1136584.90	2" PVC	Stick-up	68.0	515.7	517.16	1.46	58.0 - 68.0	10.0
209	781MW-13	Monitoring Well	SS054 - LTM	1172356.88	1136714.54	2" PVC	Stick-up	65.0	510.5	512.49	1.99	55.0 - 65.0	10.0
210	781MW-13R	Monitoring Well	SS054 - LTM	1172359.00	1136710.40	2" PVC	Stick-up	66.5	512.2	515.22	3.02	55.5 - 65.5	10.0
211	781MW-14	Monitoring Well	SS054 - LTM	1172440.17	1136799.26	2" PVC	Stick-up	62.0	508.8	510.87	2.07	52.0 - 62.0	10.0
212	781MW-15	Monitoring Well	SS054 - LTM	1172570.50	1136859.95	2" PVC	Stick-up	64.0	513.4	515.29	1.89	54.0 - 64.0	10.0
213	781MW-16	Monitoring Well	SS054 - LTM	1172328.65	1136850.64	2" PVC	Stick-up	60.0	505.6	507.65	2.05	50.0 - 60.0	10.0
214	781MW-17	Monitoring Well	SS054 - LTM	1172267.74	1136601.31	2" PVC	Stick-up	67.0	512.6	515.20	2.60	57.0 - 67.0	10.0
215	781MW-18	Monitoring Well	SS054 - LTM	1172164.51	1136652.64	2" PVC	Stick-up	58.0	505.7	507.48	1.78	48.0 - 58.0	10.0
216	781MW-19	Monitoring Well	SS054 - LTM	1172189.84	1136794.56	2" PVC	Stick-up	51.0	495.7	497.41	1.71	41.0 - 51.0	10.0
217	781MW-20	Monitoring Well	SS054 - LTM	1172090.64	1136463.32	2" PVC	Stick-up	44.0	491.4	493.70	2.30	34.0 - 44.0	10.0
218	781MW-21	Monitoring Well	SS054 - LTM	1171993.28	1136578.55	2" PVC	Stick-up	34.0	482.4	484.86	2.46	24.0 - 34.0	10.0
219	781PAIW-1	Injection Well	SS054 - LTM	1172601.22	1136721.02	4" PVC	Stick-up	63.0	515.8	518.57	2.77	48.0 - 63.0	15.0
220	781PAIW-2	Injection Well	SS054 - LTM	1172741.51	1136680.88	4" PVC	Stick-up	-	514.56	-	-	- - -	-

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
221	781PPRW-1	Recovery Well	SS054 - LTM	1172345.47	1136716.56	4" PVC	Stick-up	63.0	510.7	513.44	2.74	48.0 - 63.0	15.0
222	781PPRW-2	Recovery Well	SS054 - LTM	1172357.03	1136702.25	4" PVC	Stick-up	64.0	512.2	514.54	2.34	49.0 - 64.0	15.0
223	781PPRW-3	Recovery Well	SS054 - LTM	1172446.25	1136690.41	4" PVC	Stick-up	64.0	513.6	516.85	3.25	49.0 - 64.0	15.0
224	781PPRW-4	Recovery Well	SS054 - LTM	1172360.83	1136725.48	4" PVC	Stick-up	63.0	510.5	513.51	3.01	48.0 - 63.0	15.0
225	781PPRW-5	Recovery Well	SS054 - LTM	1172476.70	1136729.99	4" PVC	Stick-up	-	512.3	515.80	3.50	- - -	-
226	781PPRW-6	Recovery Well	SS054 - LTM	1172499.30	1136683.81	4" PVC	Stick-up	-	514.3	517.76	3.46	- - -	-
227	781PPRW-7	Recovery Well	SS054 - LTM	1172549.26	1136681.02	4" PVC	Stick-up	-	514.6	517.85	3.25	- - -	-
228	781PPRW-8	Recovery Well	SS054 - LTM	1172578.19	1136634.82	4" PVC	Stick-up	-	515.1	518.58	3.48	- - -	-
229	781PPRW-9	Recovery Well	SS054 - LTM	1172697.50	1136592.62	4" PVC	Flush mount	56.0	513.0	512.77	-0.23	46.0 - 56.0	10.0
230	781VBS-1	Biosparge	SS054 - Biosparge	1172404.54	1136693.69	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
231	781VBS-2	Biosparge	SS054 - Biosparge	1172365.64	1136696.82	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
232	781VBS-3	Biosparge	SS054 - Biosparge	1172337.59	1136724.30	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
233	781VBS-4	Biosparge	SS054 - Biosparge	1172364.22	1136742.99	1" PVC	Stick-up	62.0	-	-	-	57.0 - 62.0	5.0
234	781VBS-5	Biosparge	SS054 - Biosparge	1172210.87	1136641.48	1" PVC	Stick-up	64.0	-	-	-	59.0 - 64.0	5.0
235	781VBS-6	Biosparge	SS054 - Biosparge	1172241.28	1136626.67	1" PVC	Stick-up	70.0	-	-	-	65.0 - 70.0	5.0
236	781VBS-7	Biosparge	SS054 - Biosparge	1172270.77	1136556.43	1" PVC	Stick-up	70.0	-	-	-	65.0 - 70.0	5.0
237	781VBS-8	Biosparge	SS054 - Biosparge	1172627.12	1136699.84	1" PVC	Stick-up	60.0	-	-	-	55.0 - 60.0	5.0
238	781VBS-9	Biosparge	SS054 - Biosparge	1172640.61	1136608.44	1" PVC	Flush mount	65.0	-	-	-	60.0 - 65.0	5.0
239	781VBS-10	Biosparge	SS054 - Biosparge	1172688.87	1136626.85	1" PVC	Flush mount	64.0	-	-	-	59.0 - 64.0	5.0
240	781VBS-11	Biosparge	SS054 - Biosparge	1172749.46	1136657.95	1" PVC	Stick-up	62.0	-	-	-	60.0 - 62.0	2.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
241	781VBS-12	Biosparge	SS054 - Biosparge	1172707.46	1136697.70	1" PVC	Stick-up	64.5	-	-	-	59.5 - 64.5	5.0
242	AOC9MW-05	Monitoring Well	SS062 - LTM	1181171.85	1133372.26	2" PVC	Flush mount	14.0	484.17	482.72	-1.45	4.0 - 14.0	10.0
243	AOC9MW-06	Monitoring Well	SS062 - LTM	1181035.53	1133815.84	2" PVC	Stick-up	14.2	482.57	484.10	1.53	4.2 - 14.2	10.0
244	AOC9MW-07	Monitoring Well	SS062 - LTM	1181437.34	1133545.46	2" PVC	Stick-up	9.2	482.75	484.83	2.08	4.2 - 9.2	5.0
245	AOC9MW-08	Monitoring Well	SS062 - LTM	1181830.99	1133888.39	2" PVC	Stick-up	20.4	498.47	499.73	1.26	15.4 - 20.4	5.0
246	AOC9MW-9BR	Monitoring Well	SS062 - Not Used	1181037.03	1133735.93	2" PVC	Stick-up	43.2	481.21	482.59	1.38	23.2 - 43.2	20.0
247	AOC9MW-11BR	Monitoring Well	SS062 - Not Used	1182007.19	1134127.47	2" PVC	Stick-up	57.5	524.21	525.85	1.64	37.5 - 57.5	20.0
248	AOC9MW-12	Monitoring Well	SS062 - LTM	1181781.27	1133845.24	2" PVC	Flush mount	19.7	509.09	508.83	-0.26	10.0 - 19.7	9.7
249	AOC9MW-13	Monitoring Well	SS062 - LTM	1181793.24	1133855.65	2" PVC	Stick-up	22.2	508.53	510.76	2.23	12.2 - 22.2	10.0
250	AOC9MW-14	Monitoring Well	SS062 - LTM	1181913.04	1134024.58	2" PVC	Stick-up	24.0	519.05	520.86	1.81	14.0 - 24.0	10.0
251	AOC9MW-15	Monitoring Well	SS062 - LTM	1181701.71	1133799.71	2" PVC	Stick-up	14.0	500.04	501.99	1.95	9.0 - 14.0	5.0
252	AOC9MW-16	Monitoring Well	SS062 - LTM	1181624.12	1133750.28	2" PVC	Stick-up	14.0	497.26	499.19	1.93	9.0 - 14.0	5.0
253	AOC9MW-17	Monitoring Well	SS062 - LTM	1181517.91	1133589.49	2" PVC	Stick-up	14.0	487.51	489.44	1.93	9.0 - 14.0	5.0
254	AOC9MW-18	Monitoring Well	SS062 - LTM	1182102.90	1134592.40	2" PVC	Stick-up	20.5	527.84	529.34	1.50	10.5 - 20.5	10.0
255	AOC9MW-19	Monitoring Well	SS062 - LTM	1182022.06	1134404.34	2" PVC	Flush mount	18.7	523.38	523.05	-0.33	8.7 - 18.7	10.0
256	AOC9MW-20	Monitoring Well	SS062 - LTM	1181976.16	1134253.47	2" PVC	Stick-up	18.0	516.67	519.31	2.64	6.0 - 18.0	12.0
257	AOC9MW-21	Monitoring Well	SS062 - LTM	1181922.73	1134088.13	2" PVC	Stick-up	24.0	520.55	523.22	2.67	9.0 - 24.0	15.0
258	AOC9MW-22	Monitoring Well	SS062 - LTM	1181963.73	1134040.39	2" PVC	Stick-up	24.0	519.60	522.47	2.87	9.0 - 24.0	15.0
259	AOC9MW-23	Monitoring Well	SS062 - LTM	1181969.33	1134158.06	2" PVC	Stick-up	21.0	516.66	519.55	2.89	6.0 - 21.0	15.0
260	AOC9MW-24	Monitoring Well	SS062 - LTM	1181892.44	1134120.57	2" PVC	Stick-up	24.0	520.52	523.20	2.68	9.0 - 24.0	15.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
261	AOC9TW-95	Temporary Monitoring Well	SS062 - Not Used	1182021.16	1134088.07	1" PVC	Flush mount	23.2	522.62	522.35	-0.27	13.2 - 23.2	10.0
262	G009-MW01	Monitoring Well	SS062 - LTM	1181715.74	1133596.78	2" PVC	Stick-up	9.0	492.39	494.42	2.03	4.0 - 9.0	5.0
263	G009-MW02	Monitoring Well	SS062 - LTM	1181543.01	1133716.02	2" PVC	Stick-up	9.0	494.02	495.58	1.56	4.0 - 9.0	5.0
264	G009-MW03	Monitoring Well	SS062 - LTM	1181440.42	1133617.19	2" PVC	Stick-up	9.0	485.10	485.10	0.00	4.0 - 9.0	5.0
265	G009-MW04	Monitoring Well	SS062 - LTM	1181305.07	1133496.60	2" PVC	Stick-up	16.7	483.66	484.87	1.21	6.7 - 16.7	10.0
266	WSAMW-4	Monitoring Well	SS062 - Not Used	1181718.00	1134023.00	2" PVC	Stick-up	17.2	516.86	518.72	1.86	7.2 - 17.2	10.0
267	789MW-46R	Monitoring Well	SS067 - LTM	1173946.46	1138241.59	4" PVC	Stick-up	29.0	476.68	479.09	2.41	14.0 - 29.0	15.0
268	789MW-63R	Monitoring Well	SS067 - LTM	1174345.41	1138378.63	2" PVC	Stick-up	29.0	478.42	480.21	1.79	14.0 - 29.0	15.0
269	789MW-64	Monitoring Well	SS067 - LTM	1174419.27	1138155.83	2" PVC	Stick-up	22.0	476.16	478.53	2.37	12.0 - 22.0	10.0
270	789MW-83	Monitoring Well	SS067 - LTM	1174133.67	1138394.51	2" PVC	Flush mount	31.0	479.29	478.79	-0.50	21.0 - 31.0	10.0
271	789MW-95	Monitoring Well	SS067 - LTM	1174293.54	1138106.77	2" PVC	Stick-up	20.5	477.28	479.39	2.11	10.5 - 20.5	10.0
272	789MW-96	Monitoring Well	SS067 - LTM	1174085.78	1138127.20	4" PVC	Stick-up	24.5	474.71	476.69	1.98	14.5 - 24.5	10.0
273	789MW-97	Monitoring Well	SS067 - LTM	1174144.38	1138027.15	4" PVC	Stick-up	25.0	475.88	478.06	2.18	15.0 - 25.0	10.0
274	789MW-98	Monitoring Well	SS067 - LTM	1174058.90	1137931.05	4" PVC	Flush mount	20.0	476.59	476.32	-0.27	10.0 - 20.0	10.0
275	789MW-99	Monitoring Well	SS067 - LTM	1173966.05	1138022.60	4" PVC	Stick-up	24.5	474.85	475.80	0.95	14.5 - 24.5	10.0
276	789MW-100	Monitoring Well	SS067 - LTM	1173833.09	1137798.88	2" PVC	Stick-up	21.0	476.11	478.08	1.97	11.0 - 21.0	10.0
277	789MW-101	Monitoring Well	SS067 - LTM	1174188.99	1139180.95	2" PVC	Stick-up	15.0	448.58	450.86	2.28	5.0 - 15.0	10.0
278	789MW-102	Monitoring Well	SS067 - LTM	1173999.60	1139292.87	2" PVC	Stick-up	15.0	448.23	451.03	2.80	5.0 - 15.0	10.0
279	789MW-103	Monitoring Well	SS067 - LTM	1173816.99	1139411.93	2" PVC	Stick-up	15.0	447.50	449.99	2.49	5.0 - 15.0	10.0
280	789MW-134	Monitoring Well	SS067 - LTM	1174176.94	1138621.97	2" PVC	Flush mount	33.0	481.26	480.74	-0.52	23.0 - 33.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
281	789MW-135	Monitoring Well	SS067 - LTM	1174061.91	1138663.65	2" PVC	Flush mount	33.0	482.02	481.54	-0.48	23.0 - 33.0	10.0
282	789MW-214	Monitoring Well	SS067 - LTM	1174312.86	1138288.48	2" PVC	Stick-up	28.0	476.42	479.13	2.71	23.0 - 28.0	5.0
283	789MW-215	Monitoring Well	SS067 - LTM	1174240.92	1138369.74	2" PVC	Stick-up	30.0	473.95	481.16	7.21	25.0 - 30.0	5.0
284	789MW-216	Monitoring Well	SS067 - LTM	1174172.52	1138265.59	2" PVC	Stick-up	29.0	476.75	477.98	1.23	19.0 - 29.0	10.0
285	789MW-222	Monitoring Well	SS067 - LTM	1174008.16	1138434.93	2" PVC	Stick-up	28.0	479.52	481.39	1.87	18.0 - 28.0	10.0
286	789MW-223	Monitoring Well	SS067 - LTM	1173858.16	1138102.37	2" PVC	Stick-up	23.0	474.13	475.79	1.66	13.0 - 23.0	10.0
287	789MW-250	Monitoring Well	SS067 - LTM	1174155.20	1138076.20	2" PVC	Stick-up	33.0	475.00	478.46	3.46	5.8 - 30.8	25.0
288	789MW-251	Monitoring Well	SS067 - LTM	1174163.20	1138122.70	2" PVC	Stick-up	30.0	475.60	478.50	2.90	4.8 - 29.8	25.0
289	789MW-252	Monitoring Well	SS067 - LTM	1174098.80	1138144.90	2" PVC	Stick-up	33.0	475.10	478.04	2.94	4.8 - 29.8	25.0
290	789MW-253	Monitoring Well	SS067 - LTM	1173900.06	1138010.67	2" PVC	Stick-up	26.0	474.98	477.92	2.94	11.0 - 26.0	15.0
291	789MW-254	Monitoring Well	SS067 - LTM	1174117.64	1137877.00	2" PVC	Stick-up	26.0	476.68	479.82	3.14	11.0 - 26.0	15.0
292	789MW-255	Monitoring Well	SS067 - LTM	1174170.09	1137948.01	2" PVC	Stick-up	26.0	476.51	478.82	2.31	11.0 - 26.0	15.0
293	789MW-256	Monitoring Well	SS067 - LTM	1174253.20	1138007.83	2" PVC	Stick-up	26.0	477.13	479.90	2.77	6.0 - 26.0	20.0
294	789MW-257	Monitoring Well	SS067 - LTM	1173900.00	1139010.95	2" PVC	Stick-up	48.0	481.21	483.72	2.51	33.0 - 48.0	15.0
295	789RW-200	Recovery Well	SS067 - LTM	1174168.62	1138106.95	6" PVC	Vault	-	476.18	475.34	-0.84	- - -	-
296	789RW-201	Recovery Well	SS067 - LTM	1174106.11	1138357.27	6" PVC	Vault	-	478.82	477.97	-0.85	- - -	-
297	789RW-202	Recovery Well	SS067 - LTM	1174069.02	1138199.55	6" PVC	Vault	-	476.68	475.37	-1.31	- - -	-
298	789RW-203	Recovery Well	SS067 - LTM	1174206.70	1138180.24	6" PVC	Vault	-	476.88	476.05	-0.83	- - -	-
299	789RW-204	Recovery Well	SS067 - LTM	1174066.47	1138283.07	6" PVC	Vault	-	477.82	477.10	-0.72	- - -	-
300	789RW-205	Recovery Well	SS067 - LTM	1174127.69	1138149.89	6" PVC	Vault	-	475.97	475.06	-0.91	- - -	-

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
301	789RW-206	Recovery Well	SS067 - LTM	1174118.30	1138222.76	6" PVC	Vault	-	476.83	475.57	-1.26	- - -	-
302	789RW-207	Recovery Well	SS067 - LTM	1174118.01	1138292.73	6" PVC	Vault	-	477.99	477.30	-0.69	- - -	-
303	789RW-208	Recovery Well	SS067 - LTM	1174121.19	1138404.09	6" PVC	Vault	-	479.35	478.69	-0.66	- - -	-
304	789RW-209	Recovery Well	SS067 - LTM	1174251.53	1138093.26	6" PVC	Vault	-	476.68	475.93	-0.75	- - -	-
305	789RW-210	Recovery Well	SS067 - LTM	1174086.89	1138320.61	6" PVC	Vault	-	478.45	478.42	-0.03	- - -	-
306	789RW-211	Recovery Well	SS067 - LTM	1174147.96	1138128.05	6" PVC	Vault	-	475.92	476.00	0.08	- - -	-
307	789RW-212	Recovery Well	SS067 - LTM	1174016.63	1138218.43	6" PVC	Stick-up	28.5	476.34	478.28	1.94	13.5 - 28.5	15.0
308	789RW-213	Recovery Well	SS067 - LTM	1174103.69	1138014.20	6" PVC	Stick-up	32.0	475.39	477.19	1.80	17.0 - 32.0	15.0
309	789RW-217	Recovery Well	SS067 - LTM	1174211.77	1138107.42	4" PVC	Vault	30.0	-	-	-	15.0 - 30.0	15.0
310	789RW-218	Recovery Well	SS067 - LTM	1174167.83	1138138.14	4" PVC	Stick-up	30.0	-	-	-	15.0 - 30.0	15.0
311	789RW-219	Recovery Well	SS067 - LTM	1174077.05	1138160.11	4" PVC	Stick-up	30.0	-	-	-	15.0 - 30.0	15.0
312	789RW-220	Recovery Well	SS067 - LTM	1174086.92	1138239.42	4" PVC	Stick-up	20.0	-	-	-	10.0 - 20.0	10.0
313	789RW-221	Recovery Well	SS067 - LTM	1174045.73	1138255.60	4" PVC	Stick-up	25.0	-	-	-	10.0 - 25.0	15.0
314	MW01001	Monitoring Well	PFC - Site Investigation	1175072.67	1134318.06	1" PVC	Flush mount	16.5	456.07	455.85	-0.22	6.5 - 16.5	10.0
315	MW01003	Monitoring Well	PFC - Site Investigation	1174983.47	1134397.45	1" PVC	Flush mount	16.0	455.94	455.80	-0.14	6.0 - 16.0	10.0
316	MW02001	Monitoring Well	PFC - Site Investigation	1175926.29	1136638.39	1" PVC	Flush mount	20.0	472.26	471.81	-0.45	10.0 - 20.0	10.0
317	MW02002	Monitoring Well	PFC - Site Investigation	1176095.48	1136689.17	1" PVC	Flush mount	20.0	472.50	472.17	-0.33	10.0 - 20.0	10.0
318	MW02003	Monitoring Well	PFC - Site Investigation	1176202.52	1136575.81	1" PVC	Flush mount	20.0	470.58	470.33	-0.25	10.0 - 20.0	10.0
319	MW02004	Monitoring Well	PFC - Site Investigation	1176073.02	1136489.55	1" PVC	Flush mount	20.0	466.89	466.61	-0.28	10.0 - 20.0	10.0
320	MW03001	Monitoring Well	PFC - Site Investigation	1177005.99	1135764.11	1" PVC	Flush mount	20.0	471.05	470.58	-0.47	10.0 - 20.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
321	MW03002	Monitoring Well	PFC - Site Investigation	1176752.10	1135663.95	1" PVC	Flush mount	20.0	468.56	468.45	-0.11	10.0 - 20.0	10.0
322	MW03003	Monitoring Well	PFC - Site Investigation	1176959.03	1135434.55	1" PVC	Flush mount	21.0	469.94	469.62	-0.32	11.0 - 21.0	10.0
323	MW05001	Monitoring Well	PFC - Site Investigation	1176007.32	1135862.16	1" PVC	Flush mount	20.0	466.90	466.30	-0.60	10.0 - 20.0	10.0
324	MW05002	Monitoring Well	PFC - Site Investigation	1176043.91	1135844.12	1" PVC	Flush mount	20.0	467.05	466.52	-0.53	10.0 - 20.0	10.0
325	MW05003	Monitoring Well	PFC - Site Investigation	1176026.77	1135832.21	1" PVC	Flush mount	20.0	467.22	466.81	-0.41	10.0 - 20.0	10.0
326	MW06001	Monitoring Well	PFC - Site Investigation	1177547.09	1133557.81	1" PVC	Flush mount	20.0	470.12	469.67	-0.45	10.0 - 20.0	10.0
327	MW06002	Monitoring Well	PFC - Site Investigation	1177523.66	1133815.65	1" PVC	Flush mount	20.0	469.71	469.26	-0.45	10.0 - 20.0	10.0
328	MW07002	Monitoring Well	PFC - Site Investigation	1177382.89	1132151.87	1" PVC	Flush mount	22.0	472.24	472.10	-0.14	12.0 - 22.0	10.0
329	MW07003	Monitoring Well	PFC - Site Investigation	1177399.09	1132847.80	1" PVC	Flush mount	22.0	472.46	472.37	-0.09	12.0 - 22.0	10.0
330	MW07004	Monitoring Well	PFC - Site Investigation	1177317.06	1133055.72	1" PVC	Flush mount	21.2	471.62	471.36	-0.26	11.2 - 21.2	10.0
331	MW08001	Monitoring Well	PFC - Site Investigation	1177252.69	1134675.31	1" PVC	Flush mount	20.0	471.09	470.98	-0.11	10.0 - 20.0	10.0
332	MW08002	Monitoring Well	PFC - Site Investigation	1177097.65	1134841.76	1" PVC	Flush mount	22.0	471.41	471.04	-0.37	12.0 - 22.0	10.0
333	MW08003	Monitoring Well	PFC - Site Investigation	1176971.29	1134977.32	1" PVC	Flush mount	20.0	471.55	471.15	-0.40	10.0 - 20.0	10.0
334	MW09001	Monitoring Well	PFC - Site Investigation	1182233.23	1134426.53	1" PVC	Flush mount	23.0	525.45	525.25	-0.20	13.0 - 23.0	10.0
335	MW09004	Monitoring Well	PFC - Site Investigation	1182184.89	1134490.51	1" PVC	Flush mount	20.0	524.94	524.72	-0.22	10.0 - 20.0	10.0
336	MW10001	Monitoring Well	PFC - Site Investigation	1179435.11	1136687.19	1" PVC	Flush mount	20.0	527.06	526.78	-0.28	10.0 - 20.0	10.0
337	MW10002	Monitoring Well	PFC - Site Investigation	1179319.74	1136742.11	1" PVC	Flush mount	20.0	527.66	527.51	-0.15	10.0 - 20.0	10.0
338	MW10003	Monitoring Well	PFC - Site Investigation	1179342.08	1136862.82	1" PVC	Flush mount	20.0	528.81	528.45	-0.36	10.0 - 20.0	10.0
339	MW11001	Monitoring Well	PFC - Site Investigation	1178745.23	1132360.90	1" PVC	Flush mount	25.0	478.81	478.30	-0.51	15.0 - 25.0	10.0
340	MW11002	Monitoring Well	PFC - Site Investigation	1178745.12	1132883.53	1" PVC	Flush mount	25.0	477.33	476.90	-0.43	15.0 - 25.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
341	MW11003	Monitoring Well	PFC - Site Investigation	1178773.92	1133625.95	1" PVC	Flush mount	25.0	475.76	475.38	-0.38	15.0 - 25.0	10.0
342	MW14001	Monitoring Well	PFC - Site Investigation	1175487.10	1138754.80	1" PVC	Stick-up	10.0	472.90	476.10	3.20	2.0 - 10.0	8.0
343	MW14002	Monitoring Well	PFC - Site Investigation	1175278.33	1138787.28	1" PVC	Stick-up	11.0	462.00	464.45	2.45	1.0 - 11.0	10.0
344	MW14003	Monitoring Well	PFC - Site Investigation	1175112.37	1138987.54	1" PVC	Stick-up	11.0	461.77	464.27	2.50	1.0 - 11.0	10.0
345	MW14004	Monitoring Well	PFC - Site Investigation	1174798.73	1138957.44	1" PVC	Flush mount	18.0	455.00	454.70	-0.30	8.0 - 18.0	10.0
346	MW14005	Monitoring Well	PFC - Site Investigation	1174591.33	1139070.07	1" PVC	Stick-up	12.0	447.16	449.83	2.67	2.0 - 12.0	10.0
347	AP1MW-1	Monitoring Well	CSS681 - LTM	1174225.00	1136299.00	2" PVC	Flush mount	20.0	476.73	476.46	-0.27	10.0 - 20.0	10.0
348	AP1MW-2	Monitoring Well	CSS681 - LTM	1174221.40	1136338.90	2" PVC	Flush mount	23.0	476.14	475.91	-0.23	13.0 - 23.0	10.0
349	AP1MW-3	Monitoring Well	CSS681 - LTM	1174226.00	1136253.40	2" PVC	Flush mount	21.0	478.12	477.88	-0.24	11.0 - 21.0	10.0
350	AP1MW-4	Monitoring Well	CSS681 - LTM	1174275.80	1136282.20	2" PVC	Flush mount	21.0	477.93	477.51	-0.42	11.0 - 21.0	10.0
351	AP1MW-5	Monitoring Well	CSS681 - LTM	1174194.20	1136295.50	2" PVC	Flush mount	20.0	476.57	476.27	-0.30	10.0 - 20.0	10.0

Notes:

amsl = above mean sea level, btoc = below top of casing

ft bgs = feet below ground surface, TOC = top of casing

ID = Identification, IRP = Installation Restoration Program

LTM = Long Term Monitoring

PFC = Perfluorinated compound

PVC = Polyvinyl chloride

SS = Stainless steel

Table 3. Wells Removed 2024

This page intentionally left blank.

Table 3
2024 Wells Removed From Inventory
Former Griffiss Air Force Base

Well ID	Reason For Removal
AOC9TW-95	Well not located for three consecutive years
MW10002	Well not located for five consecutive years
SD052-02_IW-14	Well paved over

Notes:

ID = Identification

This page intentionally left blank.


FIGURES


This page intentionally left blank.

Figure 1. Former Griffiss Air Force Base Location Map

This page intentionally left blank.



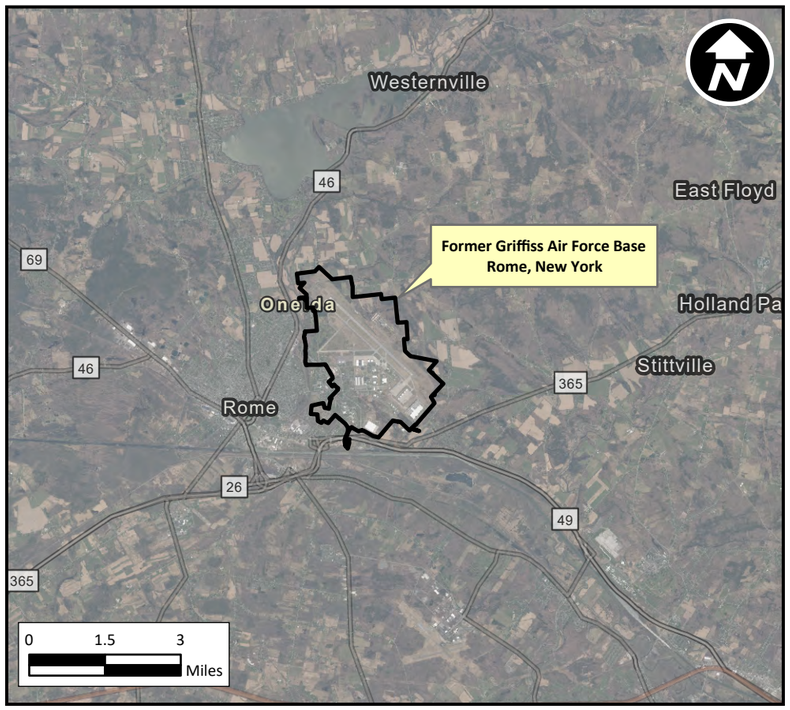

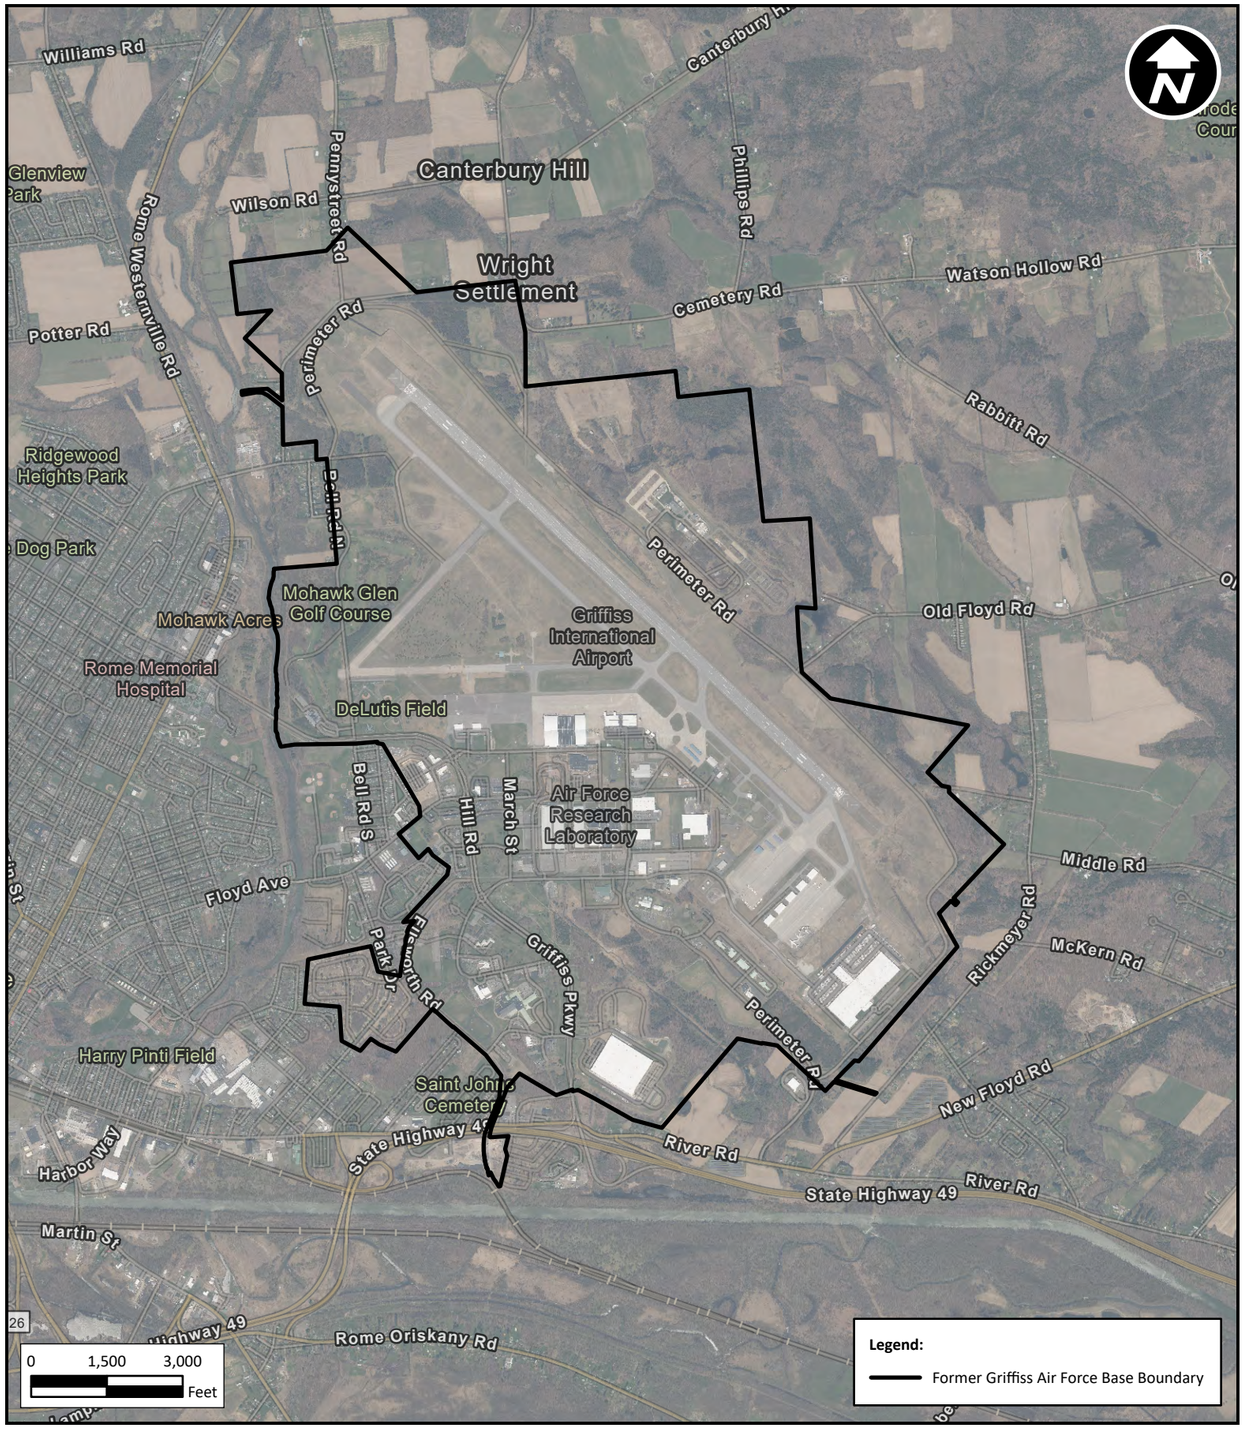

Service Layer Credits: Hybrid Reference Layer: Esri, TomTom, Garmin, SafeGraph, GeoTechnologies, Inc, METI/NASA, USGS, EPA, NPS, US Census Bureau, USDA, USFWS
NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS
World Imagery: Earthstar Geographics

Former Griffiss Air Force Base Location Map

Figure 1

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figure 2. Site Locations

This page intentionally left blank.

Figure 2

Site Locations

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY:	MRM
DATE:	3/24/2025
SCALE:	As Shown
PROJECT NO:	MSC2021.0012

0 1,000 2,000 Feet

LF001
SS062
SD052-05
LF003
LF002
ST006
DP022
SS008
SS025
CSS681 - Apron 1 Area LCP-E9
CSS682 - Building 785 Pipeline
SD052-01
SS060
SS017
AOI66
SS044
SD052-02
LF007
SS067
SD052-SVI Buildings 785 & 786
SD052-04
SS054
LF009
SD052-SVI Buildings 774 & 776

Wright Settlement
Griffiss International Airport
Air Force Research Laboratory
Rome
Ridgewood Heights Park
Rome Dog Park
Mohawk Acres
Mohawk Glen Golf Course
Rome Memorial Hospital
DeLutis Field
Harry Pinti Field
Freedom Plaza
Saint Johns Cemetery
Perimeter Rd
Cemetery Rd
Watson Hollow Rd
Rabbitt Rd
Old Floyd Rd
Hangar Rd
Ellsworth Rd
Middle Rd
McKern Rd
Rickmeyer Rd
New Floyd Rd
River Rd
State Highway 49
Floyd Ave
Wilson Rd
Bishop Rd
Potter Rd
Merrick Rd
Turin Rd
Rome Westernville Rd
Bell Rd
Hill Rd
March St
Bell Rd S
Park Ave
Union St
Kent St
Elm St
Croton St
Thomas St
Court St
W Park St
N Madison St
N George St
N James St
Black River Blvd N
E Garden St
E Bloomfield St
Railroad St
E Dominick St
Harbor Way
Martin St
Seneca St
Taft Ave
Craig St
W Cedar St
W Oak St
E Chestnut St
Park Ave
Griffiss Pkwy
Perimeter Rd
Ellsworth Rd
Middle R

Notes:
This information is depicted to provide visual aid within the context of this document and should not be used as a sole reference in precise dimensioning of features indicated. Please verify the location of all features including underground and aboveground utilities prior to conducting any subsurface exploration or site assessment.

Legend:
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

bhate
www.bhate.com

This page intentionally left blank.

Figure 3. Well Locations Associated with Site LF001

This page intentionally left blank.

0 125 250
Feet

Legend:

- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

LF1MW-12
LF1MW-11
LF1MW-14
LF1MW-6
LF1MW-103
LF1P-2
LF1P-5
LF1MW-5
LF1MW-10
LF1MW-UNK-01
LF1MW-UNK-02
LF1MW-UNK-03
LF1P-3
LF1MW-13
MWSAR03
ANGMW-1
Six Mile Creek
LF001
PERIMETER
Intermittent Stream
Pond
SS062
5950
5985
5525
6028
0854
6025
0738

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Figure 3

Well Locations Associated with Site LF001

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figure 4. Well Locations Associated with Site SS062

This page intentionally left blank.

0 75 150
Feet

Legend:

- Monitoring Well Location
- Monitoring Well Location recommended for removal in 2024
- Surface Water
- Installation Restoration Program Area

MW09001
MW09004
AOC9MW-18
AOC9TW-95
AOC9MW-11BR
AOC9MW-19
AOC9MW-22
AOC9MW-21
AOC9MW-20
AOC9MW-23
AOC9MW-14
AOC9MW-24
AOC9MW-08
AOC9MW-12
AOC9MW-13
G009-MW01
WSAMW-4
AOC9MW-15
SS062
AOC9MW-16
AOC9MW-17
G009-MW02
AOC9MW-07
G009-MW03
G009-MW04
AOC9MW-05
AOC9MW-9BR
AOC9MW-06
WSAMW-3

0906 0907 0930 0912 0913 0917 0915 0832 0829 CONNEX 6364 0916 0846 0838

PERIMETER
McPike
Pond
Intermittent Stream
Six Mile Creek

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Figure 4

Well Locations Associated with Site SS062

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM
DATE: 3/24/2025
SCALE: As Shown
PROJECT NO: MSC2021.0012

bhate
www.bhate.com

This page intentionally left blank.

Figure 5. Well Locations Associated with Site SD052-05

This page intentionally left blank.

0 60 120
Feet

Legend:

- Monitoring Well Location
- Monitoring Well Location recommended for removal in 2024
- Drainage Path
- Installation Restoration Program Area

WSAMW-2
WSAMW-14BR
WSAMW-8
817IW-2
817MW-1
817IW-3
817IW-1
817IW-6
817IW-4
817IW-7
817MW-3
817IW-5
817IW-8
WSAMW-11
WSAMW-18
WSA-IW02
WSA-IW04
WSA-IW01
WSA-IW03
WSAMW-16
WSA-MW15
WSAMW-19
SD052-05
LAWMW-9
WSAVMW-17
WSAMW-23
WSAMW-21
WSAMW-13BR
WSAMW-9
WSAMW-12BR
MW10001
MW10003
MW10002
0825
0826
6328
0810
0817
0818
0816
0830
0819
PERIMETER

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Figure 5

Well Locations Associated with Site SD052-05

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM
DATE: 3/24/2025
SCALE: As Shown
PROJECT NO: MSC2021.0012

bhate
www.bhate.com

This page intentionally left blank.

Figure 6. Well Locations Associated with Sites LF002 and LF003

This page intentionally left blank.

Figure 6

Well Locations Associated with Sites LF002 and LF003

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

0 150 300 Feet

MW10002
MW10003
Pond
LF7MW-27
LF7MW-29
LF003
5960
0802
LF7MW-22
LF7MW-100
5945
LF7MW-26
LF7MW-28
LF7MW-30
LF7MW-23
6235
5986
6242
5985
5525
LF2MW-14
LF2MW-UNK-01
LF002
LF2MW2-1
LF2MW-13
PERIMETER
LF2MW-4
5982
5326
LF2MW-12
LF2MW-100
Six Mile Creek
6204
N0797
33
0041
5887

Legend:


- Monitoring Well Location
- Monitoring Well Location recommended for removal in 2024
- Surface Water
- Drainage Path
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

This page intentionally left blank.

Figure 7. Well Locations Associated with Sites SS008, SS025, and ST006

This page intentionally left blank.

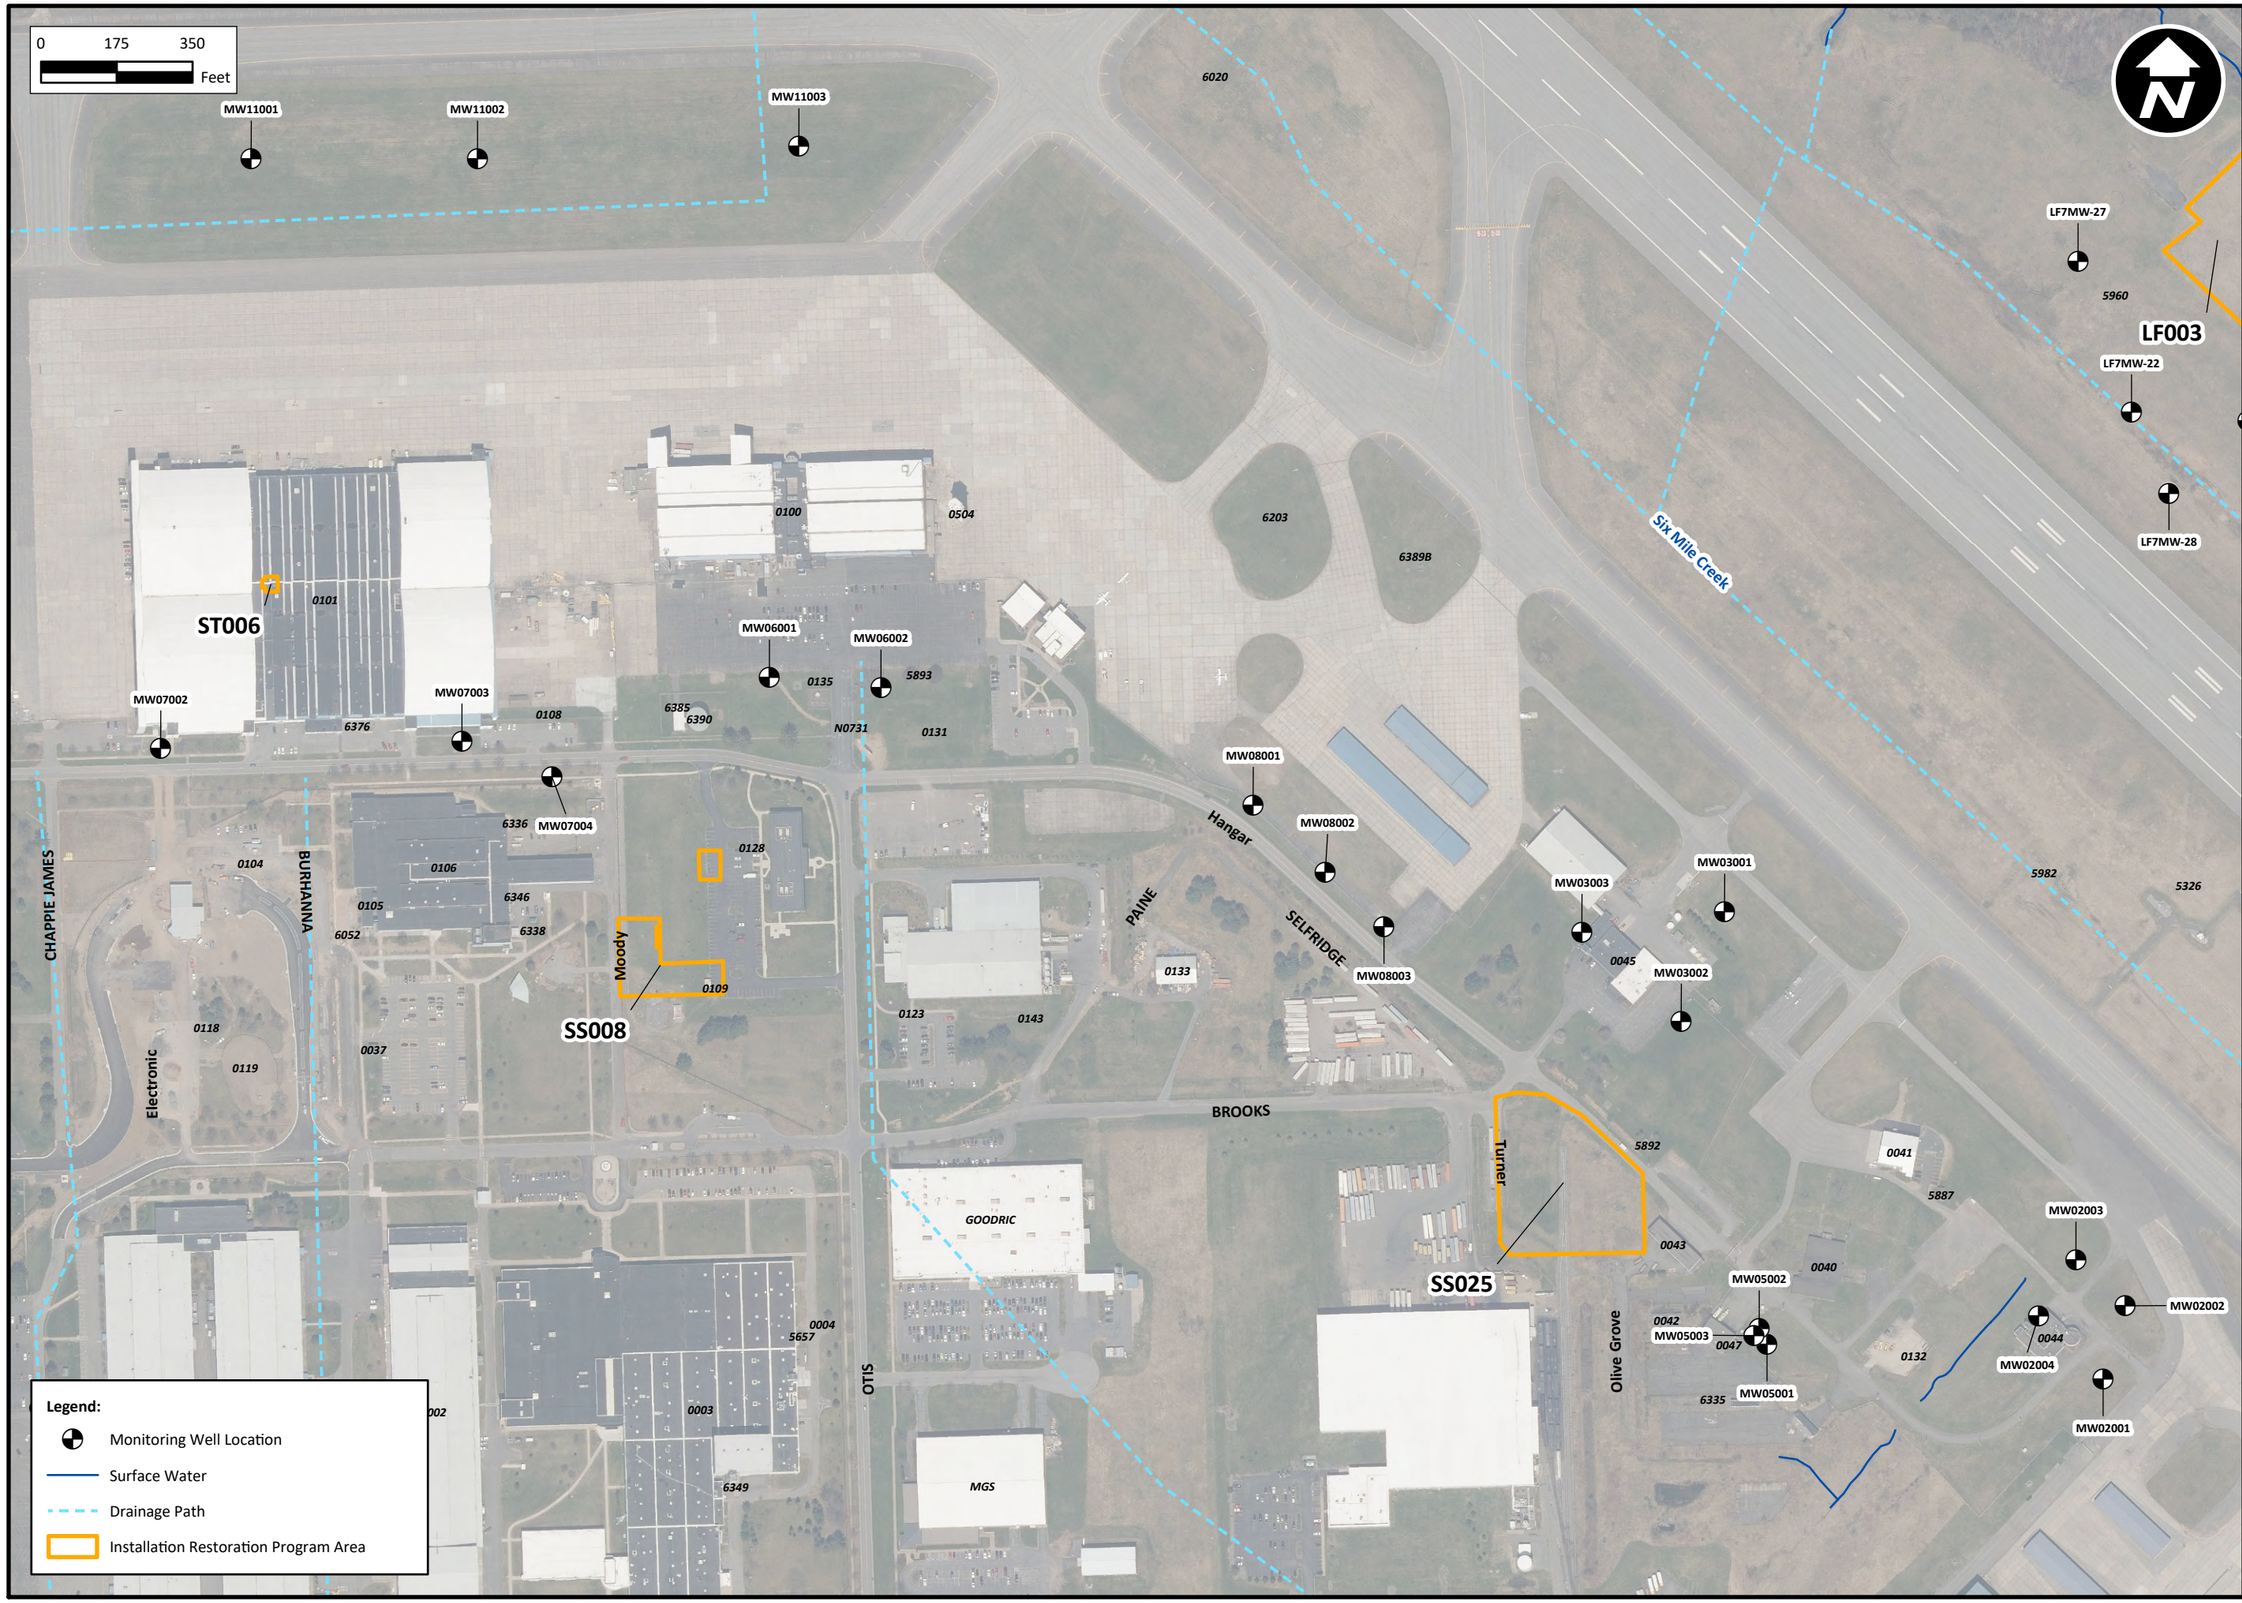

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Sites SS008, SS025, and ST006

Figure 7

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

SCALE: As Shown

DATE: 3/24/2025

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figure 8. Well Locations Associated with Sites SD052-01, SD052-SVI Buildings 785 and 786, CSS681 – Apron 1 Area LCP-E9, and CSS682 – Building 785 Pipeline

This page intentionally left blank.

0 120 240
Feet

Legend:

- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

782MW-3R
782MW-3
782VMW-86
782MW-12
782MW-11
782VMW-89
782MW-1R
782VMW-90
782MW-1
782MW-5
782VMW-95
782MW-6R2
6389C
782VMW-85
782MW-9
782VMW-88
782VMW-100
782VMW-121
782MW-184
782VMW-84
782VMW-84D
782VMW-87
782VMW-121D
AP2MW-3
782VMW-101
MW14001
MW14002
MW14003
MW14004
MW14005
782VMW-102
782VMW-94
782MW-10
782MW-6D
782VMW-78
782VMW-93
782VMW-96
782VMW-82
782VMW-76
782VMW-81
782VMW-92
782VMW-105B
782VMW-83
782VMW-104
782VMW-98
782VMW-97
782VMW-99
775VMW-11
775VMW-24
AP1MW-4
AP1MW-1
AP1MW-3
AP1MW-2
AP1MW-5
0782
0783
0784
0785
0786
8004
5989
5340
N0763
Six Mile Creek
BOMBER
PATROL
SD052-01
SD052-02
SD052-SVI Buildings
785 & 786
CSS682 - Building
785 Pipeline
CSS681 - Apron
1 Area LCP-E9
SS067

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Sites SD052-01, SD052-SVI Buildings 785 and 786, CSS681 – Apron 1 Area LCP-E9, and CSS682 – Building 785 Pipeline

Figure 8

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/28/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figures 9a and 9b. Well Locations Associated with Site SS067

This page intentionally left blank.

Figure 9a

Well Locations Associated with Site SS067

SD052-01

SS067

782VMW-92
789MW-64
789MW-63R
789MW-214
789MW-95
789MW-256
789RW-209
789MW-215
789RW-203
789RW-217
789MW-255
789MW-216
789MW-134
789RW-200
789MW-251
789RW-218
789MW-97
789MW-254
789RW-205
789RW-206
789RW-207
789MW-83
789RW-201
789MW-250
789RW-211
789RW-208
789MW-252
789MW-98
789RW-213
789MW-135
789MW-96
789RW-219
789RW-220
789RW-210
789RW-202
789RW-204
789MW-222
789RW-221
789RW-212
789MW-99
789MW-46R
789MW-253
789MW-223
789MW-100

N0763

0 40 80 Feet

Legend:

- Monitoring Well Location
- Drainage Path
- Installation Restoration Program Area

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

0 40 80 Feet

SD052-01

789MW-63R

789MW-215

N0763

789MW-134

789MW-83

789RW-201

789RW-208

SS067

789MW-135

789MW-222

782VMW-102

789MW-101

Six Mile Creek

SS067

789MW-102

789MW-257

789MW-103

Legend:

- Surface Water
- Drainage Path
- Installation Restoration Program Area

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Site SS067

Figure 9b

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

Figure 10. Well Locations Associated with Sites AOI66, LF007, SS060, and SS017

This page intentionally left blank.

0 100 200 Feet

Legend:

- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

MARKET
DONALDSON
Parking
Olive Grove
Otis
OTIS
Ellsworth
PERIMETER
RECREATION
PHOENIX
READY
CE ACCESS
SHELL
Three Mile Creek

SS017
SS060
AOI66
LF007
MW01001
MW01003
LF5MW-1A
LF5MW-3
LF5MW-4
LF5MW-5
LF5MW-100R
MW49D07
775VMW-15R1
SD052-02

0003 0019 0020 0011 0015 1300 0030 0035 0029 0036 0016 0024 8001 8002 8000 0772 0702 0701 0700 5470 0750 0770

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Sites AOI66, LF007, SS060, and SS017

Figure 10

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figure 11. Well Locations Associated with Sites SD052-02 and SD052-SVI Buildings 774 and 776

This page intentionally left blank.

0 75 150
Feet

Legend:

- Monitoring Well Location
- Monitoring Well Location recommended for removal in 2024
- Installation Restoration Program Area

SD052-SVI Buildings
785 & 786

SD052-SVI Buildings
774 & 776

SD052-02

SD052-04

LF009

SS054

0750 0769 0770 0774 0776 0777 0778 0780 0786 0788 0796 5660

READY PATROL PHOENIX PERIMETER DAEDALIAN

775VMW-23 782VMW-99 775VMW-11 775VMW-25 775VMW-15R1 775MW-2 775VMW-24 775VMW-14 775VMW-4 775VMW-18R SD052-02_IW-01 SD052-02_IW-02 SD052-02_IW-07 SD052-02_IW-08 SD052-02_IW-03 SD052-02_IW-04 775VMW-5 775MW-6 SD052-02_IW-12 SD052-02_IW-05 SD052-02_IW-06 775EW-1 SD052-02_IW-09 775EW-3 775MW-27 775EW-1R 775VMW-9 SD052-02_IW-13 SD052-02_IW-14 775VMW-16 775VMW-8 775VMW-19R 775MW-28 775VMW-10 775-MW20 775-MW20R 775VMW-20R 775-MW20RBR

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Sites SD052-02 and SD052-SVI Buildings 774 and 776

Figure 11

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM
DATE: 3/24/2025
SCALE: As Shown
PROJECT NO: MSC2021.0012

bhate
www.bhate.com


This page intentionally left blank.

Figure 12. Well Locations Associated with Site SD052-04

This page intentionally left blank.

Figure 12

Well Locations Associated with Site SD052-04

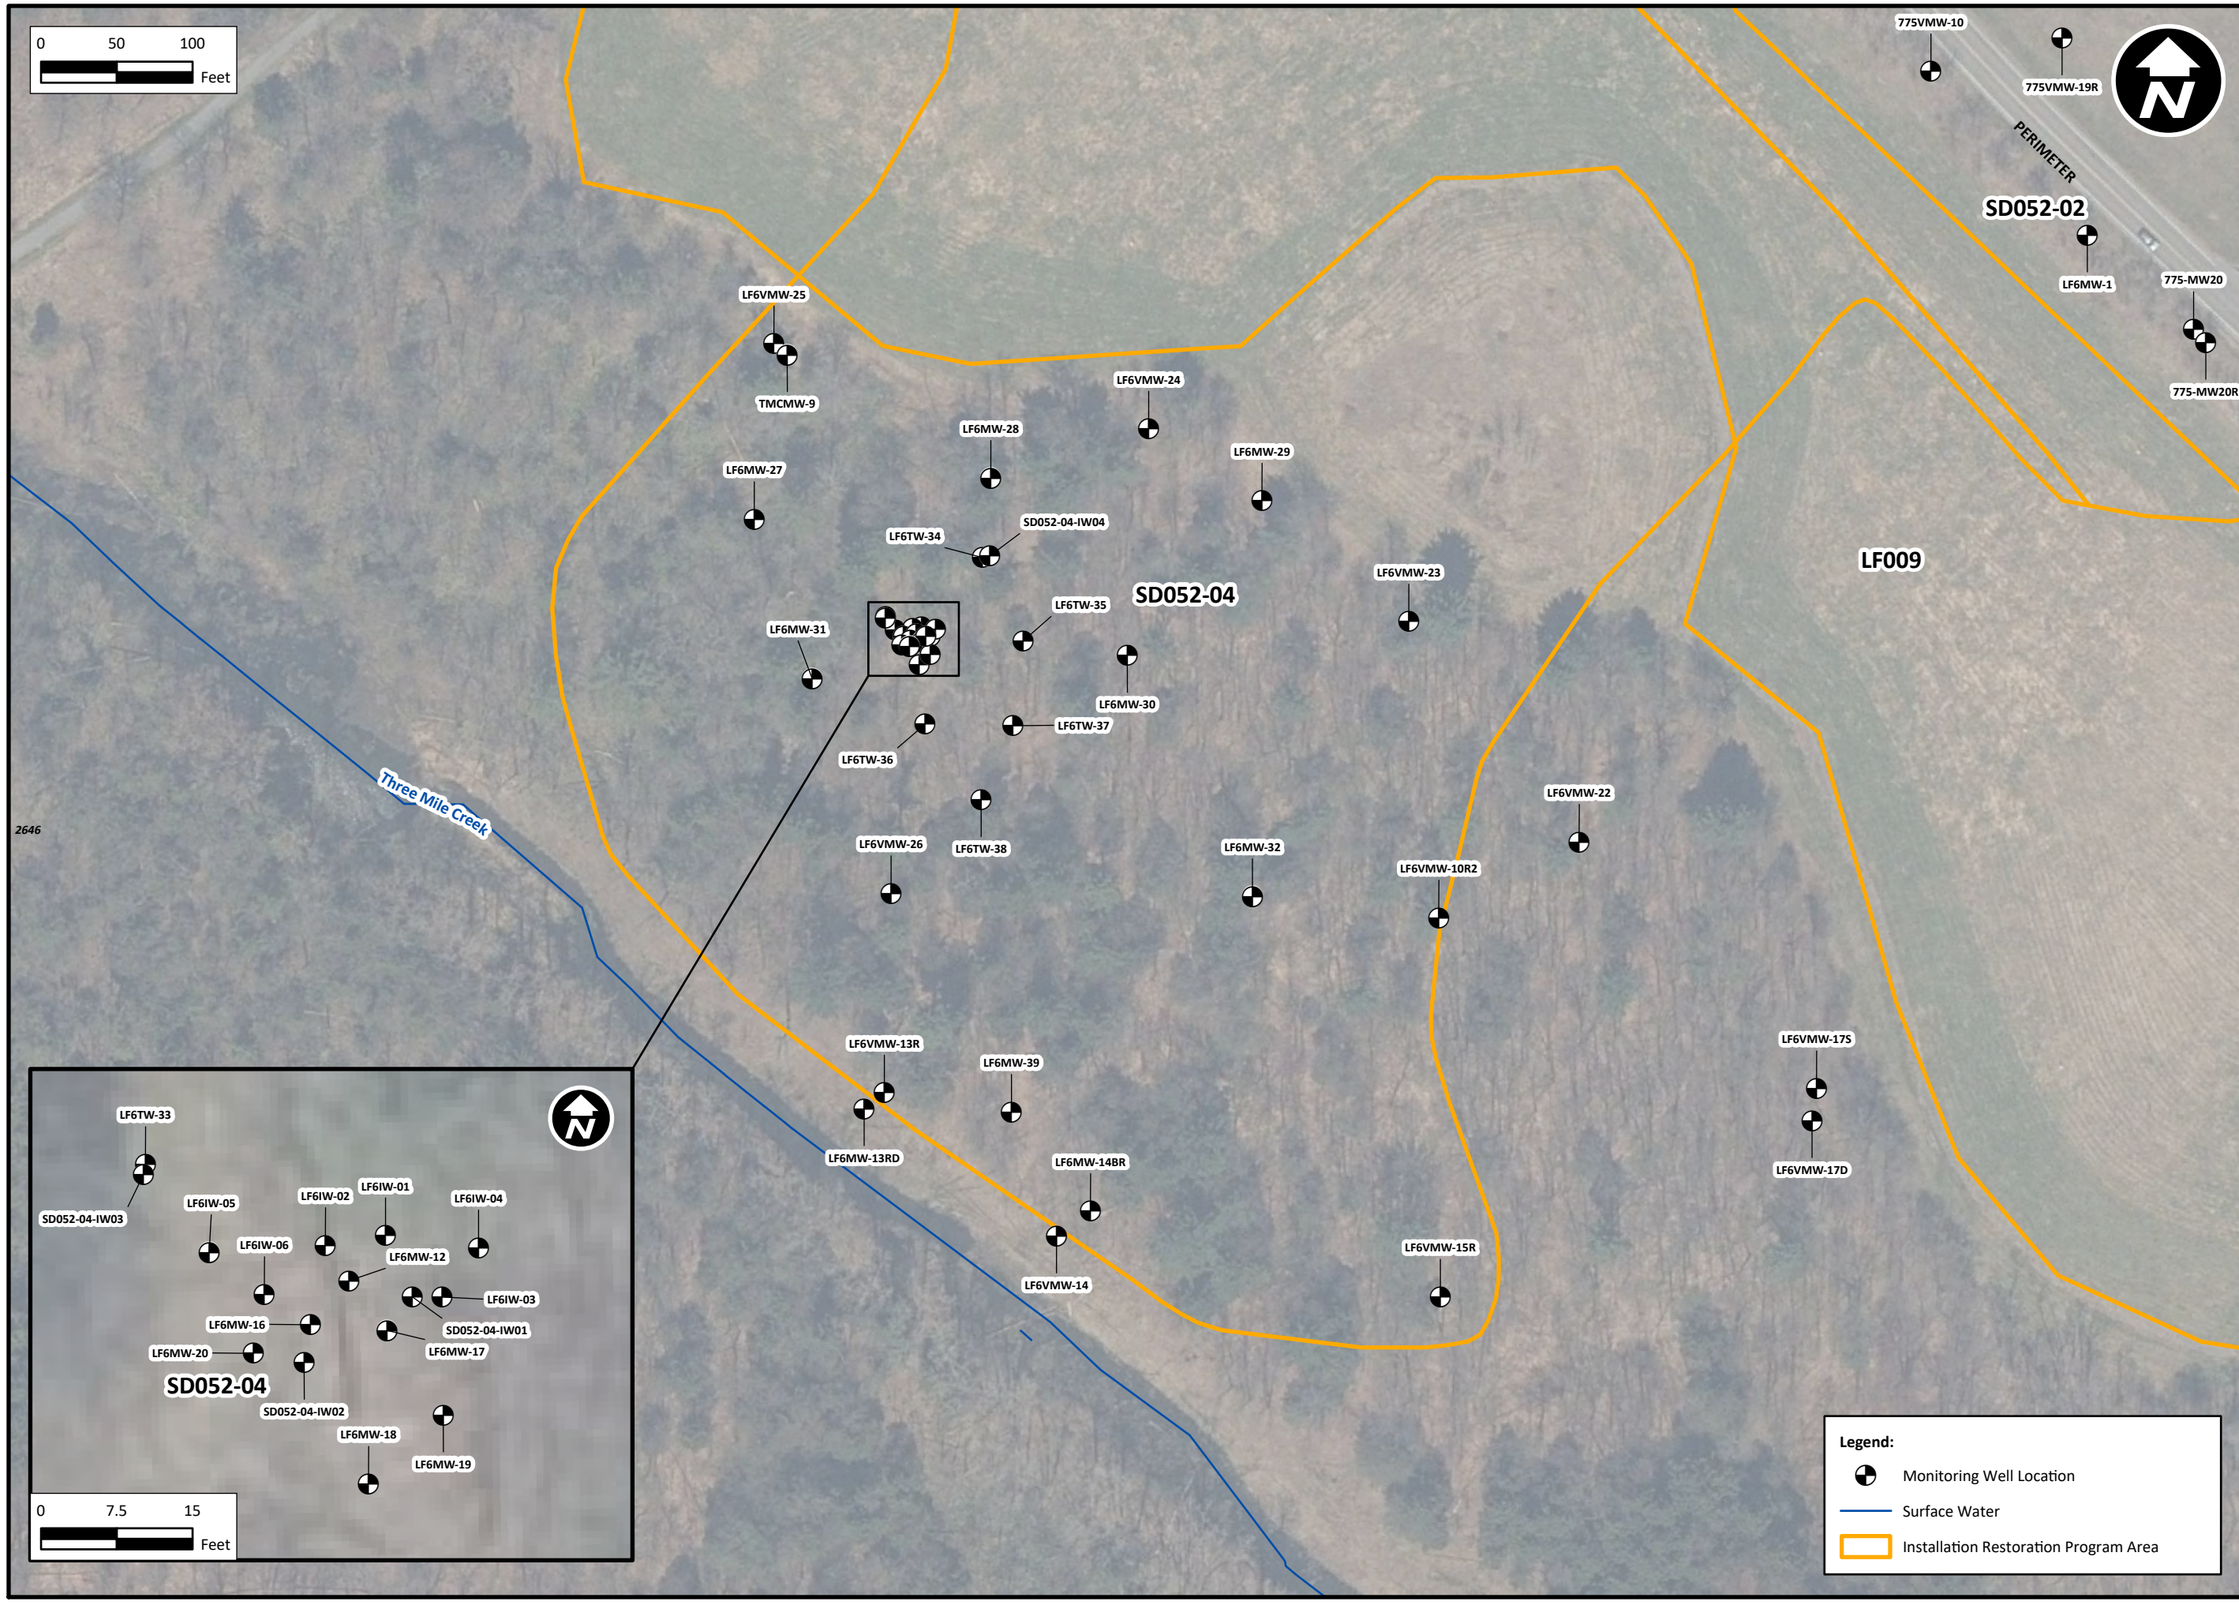

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/28/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

This page intentionally left blank.

Figure 13. Well Locations Associated with Site LF009

This page intentionally left blank.

0 60 120 Feet

LF6MW-32
LF6VMW-22
LF6VMW-10R2
SD052-04
LF6VMW-17S
LF6VMW-17D
LF6VMW-15R
LF009
LF6VMW-21
781MW-20
781MW-21
PERIMETER
781VBS-7
781MW-17
781PPRW-2
781PPRW-1
SS054
781VBS-6
781VBS-5
781MW-18
781MW-19
LF6VMW-18
LF6VMW-19
LF6VMW-20
Three Mile Creek
TMC-USGS-2
TMC-USGS-1
Three Mile Creek

Legend:

- Monitoring Well Location
- Surface Water
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Figure 13

Well Locations Associated with Site LF009

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/25/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figures 14a and 14b. Well Locations Associated with Site SS054

This page intentionally left blank.

0 40 80 Feet

0778

0780

0796

0788

PHOENIX

PATROL

PERIMETER

781MW-2
781MW-1
781MW-3
781PAIW-2
781VBS-11
781MW-9
781MW-11
781MW-10
781PPRW-9
781VBS-12
781MW-8
781VBS-10
781VBS-8
781VBS-9
781PPRW-8
781PAIW-1
781MW-15
781MW-7
781PPRW-7
781MW-4
781MW-5
SS054
781PPRW-6
781MW-6
781PPRW-3
781PPRW-5
781MW-14
781MW-12
781VBS-1
781MW-13R
781PPRW-4
781VBS-2
781VBS-4
781MW-16
781PPRW-2
781MW-13
781PPRW-1
781VBS-3
781VBS-7
781MW-17
781VBS-6
LF6VMW-21
781VBS-5
781MW-19
781MW-18
LF009
781MW-20

Legend:

- Monitoring Well Location
- Installation Restoration Program Area

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Site SS054

Figure 14a

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

0 60 120 Feet

781MW-20

781MW-21

LF009

LF6VMW-20

PERIMETER

PATROL

LAWMW-19

Legend:

- Monitoring Well Location
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services, Westchester County GIS

Well Locations Associated with Site SS054

Figure 14b

2024 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 3/24/2025

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com
