DEPARTMENT OF THE AIR FORCE
AIR FORCE CIVIL ENGINEER CENTER

11 August 2026

MEMORANDUM FOR U.S. Environmental Protection Agency – Region 2
Attn: Mr. Daniel D'Agostino
Federal Facilities Section
290 Broadway, 18th Floor
New York, NY 10007-1866

New York State Department of Environmental Conservation
Attn: Ms. Crystal Wolf
Bureau of Eastern Remedial Action
625 Broadway 12th Floor
Albany, NY 12233-7015

FROM: AFCEC/CZBE-Plattsburgh
8 Colorado Street, Suite 121
Plattsburgh NY 12903

SUBJECT: Final 2025 Well Inspection Survey and Well Maintenance Report
Former Griffiss Air Force Base, Rome, New York

Accompanying this letter, please find the following document for the former Griffiss Air Force Base for your information.

- Final 2025 Well Inspection Survey and Well Maintenance Report
  Former Griffiss Air Force Base, Rome, New York


The following recommendations are presented within the report and will be completed by the Air Force.

- Maintenance and repair of wells as detailed above in "Well Maintenance Planned for 2026". Priority should be given to any maintenance tasks that were not addressed in 2025, such as the wells that need to have their vaults or surface completions cleaned out, repaired, or replaced.
- Collect coordinates and confirm construction of the three unknown wells identified at LF001 (LF1MW-UNK-01, -02, and -03) and one unknown well identified at LF002 (LF2MW-UNK-1). While the linear spatial orientation of the wells will provided clues as to their identity, potential precision issues due to tree canopy may interfere with confirming the coordinates. If no definitive correlation to known wells can be made, decommissioning will be recommended; however, if the well ID is determined, the well will be inspected under the original well ID.
- Collect coordinates and confirm construction of the unknown well identified at LF002 (LF2MW-UNK-01). Compare the information to LF2MW2-2 to determine whether it is the

well found in 2025. If no definitive correlation to a known well can be made, decommissioning will be recommended; however, if the well ID is determined, the well will be inspected under the original well ID.

- Two wells, 789MW-64 and 789MW-103 have sustained severe damage are not repairable, and should be properly abandoned and replaced. Although associated with petroleum site SS067, they are not currently part of the quarterly groundwater monitoring program. Well 789MW-103 is considered beneficial to confirm the extent of free product observed near Six Mile Creek at an upgradient location. A replacement of this well has been recommended in greater detail in the site SS067 DGI Report. Abandonment of well 789MW-64 would not negatively impact the site groundwater monitoring program. The Air Force will address the abandonment and replacement of these wells under a separate task order, with a timeline still to be determined. No other well in the 2025 well inventory is recommended for decommissioning or decommissioning and replacement.

Should you have any questions or concerns please contact me at 518-563-2871 or david.farnsworth@us.af.mil.



DAVID S. FARNSWORTH, DAF
Program Manager/BRAC Environmental Coordinator
BRAC Program Management Division

Attachment: Final 2025 Well Inspection Survey and Well Maintenance Report, Former Griffiss Air Force Base, Rome, New York (July2026)

cc: Mr. John Swartwout, NYSDEC
Mr. Mark Sergott, NYSDOH
Ms. Christina Villanueva, CO, 772 ESS/PKS
Ms. DeAngel Hardison, CO, AFCEC
Mr. Jose Flores, COR, AFCEC/CZBE
Mr. Richard Dugoh, CS, 772 ESS/PKS
Mr. Chance Pircher, AFIMSC/DST
Ms. Debra MacDonald, ECC
Ms. Catherine Guido, ECC
Mr. Joe Tellez, Cherokee Federal
Mr. John Carr, Cherokee Federal
Mr. Allen Tevyaw, Cherokee Federal
Mr. Ted Volskay, Cherokee Federal

FINAL
2025 ANNUAL WELL INSPECTION SURVEY AND WELL MAINTENANCE
FORMER GRIFFISS AIR FORCE BASE
ROME, NEW YORK

Document Control No. NEBECOS-0600-GRI

PREPARED FOR: Mr. David Farnsworth/Former Griffiss Air Force Base, Base Realignment and Closure Environmental Coordinator and Contracting Officer's Representative

PREPARED BY: Bhate Environmental Associates, Inc.

COPIES: Mr. Daniel D'Agostino, United States Environmental Protection Agency
Ms. Heather Bishop, New York State Department of Environmental Conservation

DATE: 11 August 2026

INTRODUCTION AND OBJECTIVES

Bhate Environmental Associates, Inc. (Bhate), in association with Environmental Chemical Corporation (ECC), was retained by the Air Force Civil Engineer Center (AFCEC), under Contract Number FA8903-20-D-0001, to conduct environmental remediation activities at the former Griffiss Air Force Base (AFB). Under this contract, Bhate has prepared this document for the inspection and maintenance of existing groundwater monitoring and groundwater remediation wells at the former Griffiss AFB located in the City of Rome in Oneida County, New York (**Figure 1**). Site locations are presented on **Figure 2**. Well locations are shown on **Figures 3** through **14b.**

The purpose of this annual inspection is to note the presence or absence of groundwater monitoring wells, evaluate the condition of wells that are included in the current groundwater sampling program, identify deficiencies, make repairs, and ensure there has been no unauthorized usage, encroachment upon, or interference with the wells. The inventoried wells include permanent monitoring wells, temporary monitoring wells, and remedial system process wells installed as part of the Air Force's Installation Restoration Program (IRP). However, this report does not include vapor monitoring wells or vapor probes. In addition to documenting results of the well inspection, this document presents the details of any well maintenance and repair activities performed in 2025 along with providing recommendations for future maintenance, repairs, and other activities.

WELL INVENTORY

A comprehensive list from the Final Technical Memorandum 2024 Annual Well Inspection Survey and Maintenance Report (Bhate, June 2025) containing 351 well locations formed the initial basis

of this report. One well, MW10002, was removed during the 2024 Annual Well Inspection (Bhate, June 2025) for a total of 350 wells for the 2025 Well Inventory. Two wells that were recommended for removal in the 2024 report, SD052-02_IW-14 and AOC9TW-95, were retained as they were located and/or repaired. The 2025 Well Inventory is the eleventh comprehensive inventory or inspection reported for the former Griffiss AFB since the 2010 inspection (FPM Group Ltd. [FPM], January 2010).

Field activities associated with the well inventory were conducted throughout the year in conjunction with other activities, including a mobilization in October 2025. Field personnel examined and noted the condition of each inspected well. Efforts were also made to locate some wells that were not found during the 2024 Well Inventory. The 2025 Well Inventory information is summarized in **Table 1**, the static well details (i.e., coordinates, elevations, construction details) are provided in **Table 2**.

The details recorded during the well inspections and repairs included the presence/absence (where applicable) of the well itself; identification markings; a lock; a well cap; the type of surface completion; condition of concrete pad; and any maintenance issues completed or noted. Findings of the 2025 Well Inventory are presented in **Table 1** and summarized below.

Out of a possible 350 wells, inspection and/or repairs were completed at 339 wells at the former Griffiss AFB in 2025. The remaining 11 wells were not located during 2025 field activities. Reasons for not locating wells included: unavailability of an airfield escort, time constraints, dense/overgrown vegetation, other access issues, and the inability to locate a well in the vicinity of the given coordinates. The previously reported locations of wells not found or visited during the 2025 Well Inventory are included on **Figures 3** through **14b**. Efforts to locate and inspect these wells shall continue throughout the ensuing years of this contract and the well inventory will be updated accordingly. As noted in the 2023 Well Inspection Technical Memorandum (Bhate, October 2024), wells that are not located for three consecutive years will be removed from the well inventory. The 2025 Well Inventory for the former Griffiss AFB includes all 350 wells as presented in **Table 1**.

WELL MAINTENANCE PERFORMED IN 2025

Overgrown vegetation was removed from the well pads or surrounding areas at five wells as detailed in **Table 1**. Identification (ID) tags were refreshed on 26 wells.

WELL MAINTENANCE PLANNED FOR 2026

The 2025 well inventory inspections identified 133 wells that require maintenance or repairs. The details are provided in **Table 1**. The following issues with wells at the former Griffiss AFB remain outstanding in 2025:

- Renew fading or indistinct ID markings or add new ID markings (69 locations)
- Locating the well should be prioritized (11 locations)
- Clean, repair, or replace vault / surface completion (26 locations)
- Add a new lock or remove and replace a lock (16 locations)
- Remove extensive vegetation to access the well (22 locations)

- Repair or replace a protective bollard(s) (16 locations)
- Add or replace a well plug or cap (8 locations)
- Repair concrete well pad (12 locations)
- Redevelop the well (3 locations)
- Add visibility marking for the well (1 location)
- Replace cap (8 locations)
- Abandon and replace wells (2 locations)

Some well locations have more than one of the issues listed above.

WELL DISCREPANCIES

In 2025, no new well discrepancies were identified.

Previously observed (Bhate, June 2025) well discrepancies that are pending resolution are provided below.

- Three stickup wells not listed in the current well inventory were identified at LF001, one with an Air Force-issued lock keyed consistently with others in the Griffiss AFB well inventory. No ID markings or tags were observed on or near the unidentified wells; photographs were not taken. Investigation of these wells occurred in 2025 and included measurement of total depth and casing stick up heights, and notation of approximate GPS coordinates. No wells in the GIS database issued in 2016 are definitively similar in location or construction to the three unidentified wells. A review of available historical document figures did not yield potential identification of these wells. These wells have been temporarily identified as locations LF1MW-UNK-01, LF1MW-UNK-02, and LF1MW-UNK-03 on **Figure 3**, in **Table 1** and **Table 2,** and will be further investigated during the 2026 well inventory**.**
- One well at LF002 was found with the same label as a known nearby well (LF2MW2-1). Investigation of this well occurred in 2025 and included: total depth, stick up height, and approximate GPS coordinates. No wells in the GIS database issued in 2016 were definitive matches although additional records indicate location LF2MW2-2 was installed approximately 29 feet south of LF2MW2-1. No identification markings or tags were observed on or near the well; photographs were not taken. Based on the location, the found well was compared to LF2MW2-2. The listed depth for LF2MW2-2 is 95.69 feet (no reference point) which does not align with the 2025 measured depth of 33.16 feet bTOC. This well has been tentatively identified as location LF2MW2-2 on **Figure 6** and in **Table 2** and will be reinvestigated during the 2026 well inventory.

WELL INSTALLATIONS

No wells were installed during 2025 under the former Griffiss AFB IRP.

WELL DECOMMISSIONING

The following former Griffiss AFB IRP wells were decommissioned and abandoned during 2025 as part of the No Further Action closure of Site SS054 (AFCEC, July 2025) and will be removed from the inventory (**Table 3**):

- 781MW-1
- 781MW-4
- 781MW-5
- 781MW-6
- 781MW-9
- 781MW-10
- 781MW-12
- 781MW-13
- 781MW-14
- 781MW-16
- 781MW-17
- 781MW-18
- 781MW-19
- 781PAIW-1
- 781PAIW-2
- 781PPRW-1
- 781PPRW-2
- 781PPRW-3
- 781PPRW-4
- 781PPRW-5
- 781PPRW-6
- 781PPRW-7
- 781PPRW-8
- 781PPRW-9
- 781VBS-1
- 781VBS-2
- 781VBS-3
- 781VBS-4
- 781VBS-5
- 781VBS-6
- 781VBS-7
- 781VBS-8
- 781VBS-9
- 781VBS-10
- 781VBS-11
- 781VBS-12

WELLS RECOMMENDED FOR REPLACEMENT

Two wells are recommended for proper abandonment and replacement from the 2025 Well Inventory (**Table 1**):

- Monitoring well 789MW-64, a 2-inch PVC LTM well at SS067, was discovered heavily damaged by mowing activity. The casing and bollards are severely bent.
- Monitoring well 789MW-103, a 2-inch PVC LTM well at SS067, was badly damaged by mowing activity. The pad and bollards were destroyed.

RECOMMENDATIONS

Well inventory activities for 2026 will focus on:

- Maintenance and repair of wells as detailed above in “Well Maintenance Planned for 2026”. Priority should be given to any maintenance tasks that were not addressed in 2025, such as the wells that need to have their vaults or surface completions cleaned out, repaired, or replaced.
- Collect coordinates and confirm construction of the three unknown wells identified at LF001 (LF1MW-UNK-01, -02, and -03) and one unknown well identified at LF002 (LF2MW-UNK-1). While the linear spatial orientation of the wells will provided clues as to their identity, potential precision issues due to tree canopy may interfere with confirming the coordinates. If no definitive correlation to known wells can be made, decommissioning will be

recommended; however, if the well ID is determined, the well will be inspected under the original well ID.

- Collect coordinates and confirm construction of the unknown well identified at LF002 (LF2MW-UNK-01). Compare the information to LF2MW2-2 to determine whether it is the well found in 2025. If no definitive correlation to a known well can be made, decommissioning will be recommended; however, if the well ID is determined, the well will be inspected under the original well ID.
- Two wells, 789MW-64 and 789MW-103 have sustained severe damage are not repairable, and should be properly abandoned and replaced. Although associated with petroleum site SS067, they are not currently part of the quarterly groundwater monitoring program. Well 789MW-103 is considered beneficial to confirm the extent of free product observed near Six Mile Creek at an upgradient location. A replacement of this well has been recommended in greater detail in the site SS067 DGI Report. Abandonment of well 789MW-64 would not negatively impact the site groundwater monitoring program. The Air Force will address the abandonment and replacement of these wells under a separate task order, with a timeline still to be determined. No other well in the 2025 well inventory is recommended for decommissioning or decommissioning and replacement.

Following the 2026 Well Inventory, Bhate will compile a list of wells that are recommended for decommissioning or decommissioning and replacement. These proposals, if made, will be presented with the 2026 well inventory reporting.

ATTACHMENTS

Table 1 – 2025 Well Inventory
Table 2 – Static Well Details
Table 3 – Wells Removed from Well Inventory in 2025

Figure 1 – Former Griffis Air Force Base Location Map
Figure 2 – Site Locations
Figure 3 – Well Locations Associated with Site LF001
Figure 4 – Well Locations Associated with Site SS062
Figure 5 – Well Locations Associated with Site SD052-05
Figure 6 – Well Locations Associated with Sites LF002 and LF003
Figure 7 – Well Locations Associated with Sites SS008, SS025, and ST006,
Figure 8 – Well Locations Associated with Sites SD052-01, SD052-SVI Buildings 785 and 786, CSS681 – Apron 1 Area LCP-E9, and CSS682 – Building 785 Pipeline
Figures 9a and 9b– Well Locations Associated with Site SS067
Figure 10 – Well Locations Associated with Sites AOI66, LF007, SS060, and SS017
Figure 11 – Well Locations Associated with Sites SD052-02 and SD052-SVI Buildings 774 and 776
Figure 12 – Well Locations Associated with Site SD052-04
Figure 13 – Well Locations Associated with Site LF009
Figures 14a and 14b – Well Locations Associated with Site SS054

REFERENCES

AFCEC. July 2025. *NYSDEC Spill No. 9202658 Technical Memorandum, Decommissioning and Completion, Site SS054 (Building 781).* Former Griffiss Air Force Base Rome, New York.

Bhate. October 2024. *Final 2023 Well Inspection Survey and Well Maintenance.* Former Griffiss Air Force Base, Rome, New York.

Bhate. June 2025. *Final 2024 Well Inspection Survey and Well Maintenance Report.* Former Griffiss Air Force Base, Rome, New York

FPM. January 2010, Revision 1.0. *Well Decommissioning Report Round 4 and Round 5 Long Term Monitoring Program.* Former Griffiss Air Force Base Rome, New York. (AR 2091).

TABLES

This page intentionally left blank.

Table 1. 2025 Well Inventory

This page intentionally left blank.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
1	ANGMW-1	3	10/23/2025	Yes	No	No	-	No	-	-	Buried under grass	Clear vegetation, add lock and ID	-	-
2	LF1MW-UNK-01	3	10/23/2025	Yes	No	No	N/A	Yes	Yes	No	-	Identify and add ID	-	-
3	LF1MW-UNK-02	3	10/23/2025	Yes	No	No	N/A	No	Yes	No	Missing lock	Add lock, identify, and add ID	-	-
4	LF1MW-UNK-03	3	10/23/2025	Yes	No	No	N/A	No	Yes	No	Missing lock	Add lock, identify, and add ID	-	-
5	LF1P-2	3	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	Missing bollards. Refreshed ID.	Install bollards	-	-
6	LF1P-3	3	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Missing bollards	Install bollards	-	-
7	LF1P-5	3	10/23/2025	No	No	-	-	-	-	Yes	DNL; In beaver pond	Locate and inspect	Access	Access is difficult.
8	LF1MW-5	3	10/23/2025	No	No	-	-	Yes	-	-	DNL; In beaver pond	Locate and inspect	Access	Access is difficult.
9	LF1MW-6	3	10/23/2025	No	No	-	-	-	-	-	DNL; In beaver pond	Locate and inspect	Access	Beaver pond prevents access during most of the year.
10	LF1MW-10	3	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
11	LF1MW-11	3	10/23/2025	Yes	No	-	-	-	-	-	J-plug stops well from closing; PVC riser too high.	-	-	Access is difficult. Riser too high for lid to close.
12	LF1MW-12	3	10/23/2025	Yes	No	-	-	-	-	Yes	-	-	-	Access is difficult.
13	LF1MW-13	3	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Refresh ID	-	-
14	LF1MW-14	3	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Riser is too high for lid to close properly.
15	LF1MW-103	3	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
16	MWSAR03	3	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
17	LF2MW-4	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
18	LF2MW-12	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
19	LF2MW-13	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
20	LF2MW-14	6	10/23/2025	Yes	No	Yes	Good	Yes	-	-	-	-	-	-
21	LF2MW2-1	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
22	LF2MW-UNK-01	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	-	Missing bollards	Install bollards and identify, Add ID	-	-
23	LF2MW-100	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
24	LF7MW-22	6, 7	10/23/2025	Yes	No	-	Good	N/A	Yes	-	Overgrown, marker visible	Clear vegetation	-	Vault prevents lock placement but well is inside airport fence line.
25	LF7MW-23	6	10/23/2025	Yes	No	-	Good	N/A	Yes	-	Cap/PVC is damaged. Cap was slightly open when visited.	Replace cap	-	Red plastic pipe at location. Vault prevents lock placement but well is inside airport fence line.
26	LF7MW-26	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
27	LF7MW-27	6, 7	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
28	LF7MW-28	6, 7	Not visited	No	No	-	-	-	-	-	Overgrown at surface. No Marker. Some vegetation removed.	Clear vegetation and locate and inspect well. Add marker.	Overgrown at surface. No marker.	-
29	LF7MW-29	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
30	LF7MW-30	6	10/23/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
31	LF7MW-100	6	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	No bollards	Install bollards	-	No bollards present.
32	LF5MW-1A	10	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	No bollards	Install bollards	-	-
33	LF5MW-3	10	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Overgrown vegetation	Remove vegetation	-	-
34	LF5MW-4	10	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
35	LF5MW-5	10	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
36	MW49D07	10	10/22/2025	Yes	No	Yes	Undercut	Yes	Yes	No	-	-	-	-
37	LF5MW-100R	10	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
38	SD052-04-IW01	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	TOC is female cam, cap is male cam plug.
39	SD052-04-IW02	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	TOC is female cam, cap is male cam plug.
40	SD052-04-IW03	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	TOC is female cam, cap is male cam plug.
41	SD052-04-IW04	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	TOC is female cam, cap is male cam plug.
42	LF6IW-01	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
43	LF6IW-02	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
44	LF6IW-03	12	10/22/2025	Yes	No	Yes	Good	No	No	No	No well cap or J-plug. Refreshed ID.	Replace cap and J-plug. Add lock.	-	-
45	LF6IW-04	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
46	LF6IW-05	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
47	LF6IW-06	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
48	LF6MW-1	12	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
49	LF6MW-12	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
50	LF6MW-13RD	12	10/22/2025	Yes	No	-	-	Yes	Yes	-	-	-	-	-
51	LF6MW-14BR	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
52	LF6MW-16	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
53	LF6MW-17	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
54	LF6MW-18	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
55	LF6MW-19	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
56	LF6MW-20	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
57	LF6MW-27	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
58	LF6MW-28	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
59	LF6MW-29	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
60	LF6MW-30	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
61	LF6MW-31	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
62	LF6MW-32	12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
63	LF6MW-39	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	No bollards. Refreshed ID.	Replace bollards	-	-
64	LF6TW-33	12	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Bolted cap does not lock.
65	LF6TW-34	12	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Painted red. Bolted cap does not lock.
66	LF6TW-35	12	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Red marking tape. Bolted cap does not lock.
67	LF6TW-36	12	10/22/2025	Yes	No	No	Good	N/A	Yes	No	-	Add ID	-	Red marking tape. Bolted cap does not lock.
68	LF6TW-37	12	10/22/2025	Yes	No	No	Good	N/A	Yes	No	-	Add ID	-	Red marking tape. Bolted cap does not lock.
69	LF6TW-38	12	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Red marking tape. Bolted cap does not lock.
70	LF6VMW-10R2	12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
71	LF6VMW-13R	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
72	LF6VMW-14	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
73	LF6VMW-15R	10, 11, 12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
74	LF6VMW-17D	12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
75	LF6VMW-17S	12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	SS riser is crushed inward ~1 ft down.
76	LF6VMW-18	13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
77	LF6VMW-19	13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
78	LF6VMW-20	13, 14b	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
79	LF6VMW-21	13, 14a	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
80	LF6VMW-22	12, 13	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
81	LF6VMW-23	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
82	LF6VMW-24	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
83	LF6VMW-25	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
84	LF6VMW-26	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
85	TMCMW-9	12	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
86	TMC-USGS-2	13	10/22/2025	No	-	-	-	-	-	-	Well may have been run over with mower (not located).	Locate	See remarks.	PVC stick up only. No outer casing or bollards.
87	LAWMW-19	14b	10/23/2025	Yes	No	-	-	-	-	-	-	-	-	USGS monitoring equipment on well. No access to well head.
88	TMC-USGS-1	13		Yes	No	Yes	Good	Yes	Yes	No	-	-	-	No protective casing.
89	782MW-1	8	10/23/2025	Yes	No	No	Good	N/A	Yes	No	-	Add ID	-	Well listed in historical report as being "previously decommissioned" (AECOM/Cape, May 2016) but well was identified during 2016, 2017, 2018, 2020, 2021, 2023, and 2025 field inspections.
90	782MW-1R	8	10/23/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	-
91	782MW-3	8	10/23/2025	Yes	No	No	Good	-	-	-	-	Add ID	-	Well listed in historical report as being "previously decommissioned" (AECOM/Cape, May 2016) but well was identified during 2018, 2019, 2021, and 2025 field inspections.
92	782MW-3R	8	10/23/2025	Yes	No	No	Good	-	-	-	-	Add ID	-	-
93	782MW-5	8	10/23/2025	Yes	No	No	Good	-	Yes	-	-	Add ID	-	-
94	782MW-6D	8	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
95	782MW-6R2	8	10/22/2025	Yes	No	No	Good	No	Yes	No	Broken lid lock; no bollards.	Add ID, replace lock, and add bollards	-	-
96	782MW-9	8	10/23/2025	Yes	No	No	Good	-	-	-	Sealed with tar	Add ID. Repair surface completion.	-	-
97	782MW-10	8	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	Missing 2 bolts	Add ID and replace bolts.	-	-
98	782MW-11	8	10/23/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-
99	782MW-12	8	10/23/2025	Yes	No	Yes	Good	-	-	-	-	-	-	-
100	782-MW184	8	10/22/2025	Yes	No	Yes	Good	-	Yes	-	Missing 1 bolt	Replace bolt	-	84, 84D, 184 all located very close together.
101	782VMW-76	8	10/22/2025	Yes	No	Yes	Good	N/A	Yes	Yes	Refreshed ID	-	-	Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
102	782VMW-78	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
103	782VMW-81	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Cap does not close all the way.	Fix well cap	-	-
104	782VMW-82	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
105	782VMW-83	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
106	782VMW-84	8	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	Missing 3 bolts	Replace bolts	-	84, 84D, 184 all located very close together. Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
107	782VMW-84D	8	10/22/2025	Yes	No	-	-	-	Yes	-	Located. Vegetation removed.	-	-	84, 84D, 184 all located very close together.
108	782VMW-85	8	10/23/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
109	782VMW-86	8	10/23/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
110	782VMW-87	8	10/22/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-
111	782VMW-88	8	10/22/2025	Yes	No	No	Good	N/A	-	-	Located	Add ID	-	Center bolt lid. Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
112	782VMW-89	8	10/23/2025	Yes	No	No	Poor	Yes	Yes	No	Eroded pad, lifted off ground	Add ID, repair or replace pad	-	-
113	782VMW-90	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
114	782VMW-92	8	10/22/2025	Yes	No	No	Good	-	-	-	Well lid destroyed; vault filled with dirt.	Add ID, replace lid, and clear vault	-	Need 5 point socket to open.
115	782VMW-93	8	10/22/2025	Yes	No	No	Good	N/A	Yes	No	Missing 3 bolts	Replace bolts and add ID	-	Well completion prevents addition of a lock.
116	782VMW-94	8	10/22/2025	Yes	No	-	Good	-	Yes	-	Located under pallets	-	-	-
117	782VMW-95	8	10/22/2025	Yes	No	No	Good	N/A	No	No	No well lid; vault filled with dirt	Add ID, replace cap and well lid, and clear vault	-	Well completion prevents addition of a lock.
118	782VMW-96	8	10/22/2025	Yes	No	No	Good	N/A	-	-	-	Add ID	-	Vault lid is small, center bolt type. Vault is too small for a lock to be placed, however, well is located within secured airfield fence line.
119	782VMW-97	8	10/22/2025	Yes	No	Yes	Poor	Yes	Yes	Yes	Concrete pad broken up	Repair or replace pad	-	-
120	782VMW-98	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
121	782VMW-99	8, 11	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
122	782VMW-100	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
123	782VMW-101	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
124	782VMW-102	8	10/22/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
125	782VMW-104	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
126	782VMW-105B	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	One leaning bollard	Repair bollard	-	PVC is blistered ~6 ft btoc, preventing use of sub-pump. Peristaltic is needed to sample.
127	782VMW-121	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
128	782VMW-121D	8	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
129	AP2MW-3	8	10/22/2025	Yes	No	Yes	Good	N/A	-	-	Missing 1 bolt. Vault can filled with sediment.	Replace bolt and clear vault	-	Well completion prevents addition of a lock, however, the well is located within the airport's secured area.
130	775EW-1	11	10/20/2025	Yes	No	No	Good	N/A	-	-	-	Add ID	-	Well head completion does not allow for lock installation.
131	775EW-1R	11	10/20/2025	Yes	No	No	Good	N/A	-	-	No bolts	Add ID, replace bolts.	-	Well head completion does not allow for lock installation.
132	775EW-3	11	10/20/2025	Yes	No	No	Good	N/A	Yes	No	No bolts	Add ID, replace bolts.	-	Well head completion does not allow for lock installation.
133	775MW-2	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
134	775MW-6	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
135	775-MW20	11, 12	10/20/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
136	775-MW20R	11, 12	10/20/2025	Yes	No	No	Good	Yes	No	No	-	Add ID and replace cap	-	-
137	775-MW20RBR	11	10/20/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-
138	775MW-27	11	10/20/2025	Yes	No	No	Good	-	-	Yes	No bolts	Replace bolts. Add ID.	-	Dedicated bladder pump has been lost in well and the associated tubing blocks deployment of pumps and water level measurement.
139	775MW-28	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
140	775VMW-4	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
141	775VMW-5	11	10/20/2025	Yes	No	Yes	Good	Yes	-	-	-	-	-	-
142	775VMW-8	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Labeled incorrectly on KMZ file	-	-	-
143	775VMW-9	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Well cap does not close fully	Fix well cap.	-	-
144	775VMW-10	11	10/20/2025	Yes	No	Yes	Good	Yes	No	-	-	Replace cap	-	-
145	775VMW-11	11	10/20/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Remove tree and add ID	-	Large tree growing within bollard area.
146	775VMW-14	11	10/20/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Add ID	-	-
147	775VMW-15R1	11	10/20/2025	Yes	No	No	Good	Yes	-	-	-	Add ID	-	-
148	775VMW-16	11	10/20/2025	Yes	No	No	Bad	Yes	Yes	Yes	Concrete pad damaged; half missing.	Repair or replace concrete pad. Add ID.	-	-
149	775VMW-18R	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
150	775VMW-19R	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
151	775VMW-20R	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
152	775VMW-23	11	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
153	775VMW-24	11	10/20/2025	Yes	No	No	Good	Yes	Yes	Yes	-	Remove tree and add ID	-	Large tree growing within bollard area.
154	775VMW-25	11	10/20/2025	Yes	No	No	Good	No	Yes	No	Bolt is bent, bolts are missing	Replace bolts, replace lock, and redevelop. Add ID.	-	Redevelop prior to any sampling.
155	SD052-02_IW-01	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
156	SD052-02_IW-02	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
157	SD052-02_IW-03	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
158	SD052-02_IW-04	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
159	SD052-02_IW-05	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
160	SD052-02_IW-06	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
161	SD052-02_IW-07	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
162	SD052-02_IW-08	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
163	SD052-02_IW-09	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
164	SD052-02_IW-12	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	Well is not on KMZ file	Add ID	-	Well head completion does not allow for lock installation.
165	SD052-02_IW-13	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	Well is not on KMZ file	Add ID	-	Well head completion does not allow for lock installation.
166	SD052-02_IW-14	11	10/20/2025	Yes	No	No	Good	N/A	-	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
167	817IW-1	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
168	817IW-2	5	10/22/2025	No	No	-	-	N/A	-	-	Possibly destroyed by mower	Locate	See remarks.	Well head completion does not allow for lock installation.
169	817IW-3	5	10/22/2025	No	No	-	-	N/A	-	-	Possibly destroyed by mower	Locate	See remarks.	Well head completion does not allow for lock installation.
170	817IW-4	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
171	817IW-5	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
172	817IW-6	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
173	817IW-7	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
174	817IW-8	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	N/A	-	Add ID	-	Well head completion does not allow for lock installation.
175	817MW-1	5	10/22/2025	Yes	No	No	N/A	N/A	Yes	No	-	Add ID	-	-
176	817MW-3	5	10/22/2025	Yes	No	No	N/A	Yes	Yes	No	-	Add ID	-	-
177	LAWMW-9	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
178	WSA-IW01	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation overgrown	Remove vegetation	-	3/4" threaded male cap
179	WSA-IW02	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Vegetation overgrown	Remove vegetation	-	3/4" threaded male cap
180	WSA-IW03	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Vegetation overgrown	Remove vegetation	-	3/4" threaded male cap. TOC is too high for lid to easily close and lock.
181	WSA-IW04	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Vegetation overgrown	Remove vegetation	-	3/4" threaded male cap
182	WSAMW-2	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
183	WSAMW-3	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
184	WSAMW-8	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	One knocked over bollard	Repair bollard	-	-
185	WSAMW-9	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	One leaning bollard - others missing	Repair/replace bollards	-	-
186	WSAMW-11	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation overgrown	Remove vegetation	-	-
187	WSAMW-12BR	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
188	WSAMW-13BR	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
189	WSAMW-14BR	5	10/22/2025	Yes	No	N/A	Good	Yes	N/A	N/A	-	-	-	USGS observation well. No access to well head.
190	WSA-MW-15	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Vegetation overgrown. Refreshed ID.	Remove vegetation	-	Formerly mislabeled external ID as WSAMW-11BR.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
191	WSAMW-16	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation overgrown	Remove vegetation	-	-
192	WSAMW-18	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation overgrown	Remove vegetation	-	-
193	WSAMW-19	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
194	WSAMW-21	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
195	WSAMW-23	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
196	WSAVMW-17	5	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	SS casing is bent ~6 ft bgs and prevents use of submersible pumps. Must be sampled with peristaltic pump.
197	781MW-1	11, 14a	10/20/2025	Yes	Yes	No	Good	No	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
198	781MW-2	14a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
199	781MW-3	14a	10/20/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-
200	781MW-4	11, 14a	10/20/2025	Yes	Yes	Yes	Good	Yes	-	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
201	781MW-5	11, 14a	10/20/2025	Yes	Yes	No	Good	No	No	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
202	781MW-6	11, 14a	10/20/2025	Yes	Yes	Yes	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
203	781MW-7	14a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
204	781MW-8	14a	10/20/2025	Yes	No	Yes	Good	No	Yes	No	No bolts.	Replace bolts and lock	-	-
205	781MW-9	11, 14a	10/20/2025	Yes	Yes	No	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
206	781MW-10	11, 14a	10/20/2025	Yes	Yes	No	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
207	781MW-11	14a	10/20/2025	Yes	No	No	Poor	No	Yes	No	Pad is damaged; no bolts; vault is damaged.	Repair or replace pad and vault. Add ID and lock	-	-
208	781MW-12	11, 14a	10/20/2025	Yes	Yes	Yes	Good	No	Yes	No	DECOMMISSIONED (no longer present)	Add lock	-	Abandoned 2025
209	781MW-13	14a	10/20/2025	Yes	Yes	No	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
210	781MW-13R	13, 14a	10/20/2025	Yes	No	No	Good	Yes	Yes	No	-	Add ID	-	-
211	781MW-14	11, 14a	10/20/2025	Yes	Yes	Yes	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
212	781MW-15	14a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
213	781MW-16	14a	10/20/2025	Yes	Yes	Yes	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
214	781MW-17	13, 14a	10/20/2025	Yes	Yes	Yes	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
215	781MW-18	13, 14a	10/20/2025	Yes	Yes	Yes	Good	N/A	No	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
216	781MW-19	13, 14a	10/20/2025	Yes	Yes	Yes	Good	Yes	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
217	781MW-20	13, 14a, 14b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
218	781MW-21	13, 14b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
219	781PAIW-1	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
220	781PAIW-2	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	No	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
221	781PPRW-1	14a	10/20/2025	Yes	Yes	No	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
222	781PPRW-2	13, 14a	10/20/2025	Yes	Yes	No	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
223	781PPRW-3	11, 14a	10/20/2025	Yes	Yes	Yes	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
224	781PPRW-4	14a	10/20/2025	Yes	Yes	Yes	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
225	781PPRW-5	11, 14a	10/20/2025	Yes	Yes	Yes	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
226	781PPRW-6	11, 14a	10/20/2025	Yes	Yes	Yes	Good	N/A	No	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
227	781PPRW-7	11, 14a	10/20/2025	Yes	Yes	No	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
228	781PPRW-8	11, 14a	10/20/2025	Yes	Yes	No	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
229	781PPRW-9	11, 14a	10/20/2025	Yes	No	No	Good	N/A	-	No	DECOMMISSIONED (no longer present)	-	-	Lid asphalt sealed shut
230	781VBS-1	11, 14a	10/20/2025	Yes	Yes	Yes	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
231	781VBS-2	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
232	781VBS-3	14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
233	781VBS-4	11, 14a	10/20/2025	Yes	Yes	Yes	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
234	781VBS-5	13, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
235	781VBS-6	13, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
236	781VBS-7	13, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
237	781VBS-8	11, 14a	10/20/2025	Yes	Yes	No	Good	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
238	781VBS-9	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
239	781VBS-10	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
240	781VBS-11	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present)	-	-	Abandoned 2025
241	781VBS-12	11, 14a	10/20/2025	Yes	Yes	No	N/A	N/A	Yes	No	DECOMMISSIONED (no longer present).	-	-	Abandoned 2025
242	AOC9MW-05	4	10/23/2025	Yes	No	-	-	-	-	-	Missing bolt	Replace bolt	-	-
243	AOC9MW-06	4	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
244	AOC9MW-07	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation is overgrown - no access. Some vegetation removed.	Clear vegetation	-	-
245	AOC9MW-08	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation overgrown; leaning bollard.	Repair bollard and clear vegetation	-	-

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
246	AOC9MW-9BR	4	10/23/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
247	AOC9MW-11BR	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Located - vegetation overgrown. Some vegetation removed.	Clear vegetation	-	-
248	AOC9MW-12	4	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Vault does not allow for installation of a lock, however, well is located within secured airfield fence line.
249	AOC9MW-13	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
250	AOC9MW-14	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
251	AOC9MW-15	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
252	AOC9MW-16	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
253	AOC9MW-17	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	Vegetation is overgrown - no access. Some vegetation removed.	Clear vegetation	-	-
254	AOC9MW-18	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	In deployed resources area, need to call number on gate to access.
255	AOC9MW-19	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Missing 2 bolts	Replace bolts	-	-
256	AOC9MW-20	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Installed 2022
257	AOC9MW-21	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Installed 2022
258	AOC9MW-22	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Installed 2022
259	AOC9MW-23	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Installed 2022
260	AOC9MW-24	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	Installed 2022
261	AOC9TW-95	4	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	Located	-	-	-
262	G009-MW01	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
263	G009-MW02	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
264	G009-MW03	4	10/22/2025	Yes	No	Yes	Bad	No	Yes	Yes	Located; 2 bollards knocked over; no lock	Repair bollards and lock and replace concrete pad	-	-
265	G009-MW04	4	10/23/2025	Yes	No	Yes	Poor	Yes	Yes	Yes	Bollard knocked over	Repair bollards, repair pad	-	-
266	WSAMW-4	4	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
267	789MW-46R	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
268	789MW-63R	9a, 9b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
269	789MW-64	9a	10/20/2025	Yes	No	Yes	Poor	No	Yes	No	Casing and bollards are severely bent	Repair pad, repair or replace casing and bollards, and replace lock	-	Heavily damaged by mower - recommend complete abandonment and replacement of well
270	789MW-83	9a, 9b	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	Replace vault, redevelop, and re-survey prior to any groundwater elevation measurement and sampling	Replace vault and redevelop, and resurvey well	-	Well head completion does not allow for lock installation.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
271	789MW-95	9a	10/20/2025	Yes	No	Yes	Bad	Yes	Yes	No	-	Repair or replace pad	-	-
272	789MW-96	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
273	789MW-97	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	Yes	-	-	-	-
274	789MW-98	9a	10/20/2025	Yes	No	Yes	Good	No	Yes	No	-	Add lock	-	-
275	789MW-99	9a	10/20/2025	Yes	No	Yes	Good	No	Yes	No	-	Add lock	-	-
276	789MW-100	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
277	789MW-101	9b	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	Bollards leaning (all 3)	Upright bollards.	-	-
278	789MW-102	9b	10/22/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
279	789MW-103	9b	10/22/2025	Yes	No	Yes	Bad	No	No	No	Cap missing; 1 bollard destroyed; concrete pad lifted.	Repair or replace pad, bollard, cap, and lock	-	Heavily damaged - recommend complete abandonment and replacement of well
280	789MW-134	9a, 9b	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	Missing 1 bolt	Replace bolt and repair vault	-	Well head completion does not allow for lock installation. Vault threads damaged, could not bolt.
281	789MW-135	9a, 9b	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	Missing 1 bolt	Replace bolt	-	Well head completion does not allow for lock installation.
282	789MW-214	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
283	789MW-215	9a, 9b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
284	789MW-216	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
285	789MW-222	9a, 9b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
286	789MW-223	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
287	789MW-250	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
288	789MW-251	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
289	789MW-252	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
290	789MW-253	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
291	789MW-254	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
292	789MW-255	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
293	789MW-256	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
294	789MW-257	9b	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
295	789RW-200	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
296	789RW-201	9a, 9b	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
297	789RW-202	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
298	789RW-203	9a	Not visited	Yes	No	Yes	Good	N/A	Yes	No	Buried underneath grass	Remove dirt and vegetation	Buried.	Well head completion does not allow for lock installation.
299	789RW-204	9a	10/20/2025	Yes	No	No	Good	N/A	Yes	No	-	Add ID	-	Well head completion does not allow for lock installation.
300	789RW-205	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
301	789RW-206	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
302	789RW-207	9a	10/20/2025	Yes	No	No	Good	N/A	Yes	No	-	Add ID	-	Well head completion does not allow for lock installation.
303	789RW-208	9a, 9b	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
304	789RW-209	9a	10/20/2025	Yes	No	No	Good	N/A	Yes	No	Casing is damaged	Repair casing and add ID	-	Well head completion does not allow for lock installation.
305	789RW-210	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
306	789RW-211	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
307	789RW-212	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
308	789RW-213	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
309	789RW-217	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
310	789RW-218	9a	10/20/2025	Yes	No	Yes	N/A	N/A	Yes	No	-	Repair surface completion and redevelop	-	Well head completion does not allow for lock installation. Soils and unknown debris have likely fallen into the well while the surface completion was damaged. The well must be cleared of potential debris and redeveloped prior to any use.
311	789RW-219	9a	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
312	789RW-220	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
313	789RW-221	9a	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	Well head completion does not allow for lock installation.
314	MW01001	10	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	Refreshed ID	-	-	-
315	MW01003	10	10/20/2025	Yes	No	Yes	Good	N/A	Yes	No	Refreshed ID	-	-	Vault does not allow for installation of a lock.
316	MW02001	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary	-	-	Vault does not allow for installation of a lock.
317	MW02002	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary	-	-	Vault does not allow for installation of a lock.
318	MW02003	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary; buried under grass.	Remove dirt and vegetation	-	Vault does not allow for installation of a lock.
319	MW02004	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary	-	-	Vault does not allow for installation of a lock.
320	MW03001	7	10/23/2025	Yes	No	No	Good	N/A	-	-	Escort necessary	Add ID	-	Vault does not allow for installation of a lock.
321	MW03002	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	-	-	-	Vault does not allow for installation of a lock.
322	MW03003	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Pad slightly eroded	Repair pad	-	Vault does not allow for installation of a lock.
323	MW05001	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary; needs bolts.	Replace bolts	-	Vault does not allow for installation of a lock.
324	MW05002	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary	-	-	Vault does not allow for installation of a lock.

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
325	MW05003	7	10/23/2025	Yes	No	-	-	N/A	-	-	Escort necessary	-	-	Vault does not allow for installation of a lock.
326	MW06001	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
327	MW06002	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
328	MW07002	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
329	MW07003	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
330	MW07004	7	10/20/2025	Yes	No	Yes	Good	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
331	MW08001	7	10/20/2025	Yes	No	-	Good	-	-	-	-	-	-	-
332	MW08002	7	10/20/2025	Yes	No	-	Poor	-	-	-	Pad is lifted off ground	Replace pad and vault	-	Repair/replace vault and resurvey prior to water elevation measurement.
333	MW08003	7	10/20/2025	Yes	No	-	Poor	-	-	-	Pad is lifted off ground	Replace pad and vault	-	Repair/replace vault and resurvey prior to water elevation measurement.
334	MW09001	4	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	In Deployed Resources area, call number on gate to access.	-	-	Vault does not allow for installation of a lock.
335	MW09004	4	10/22/2025	No	-	-	-	N/A	-	-	Deployed Resources employee said DEC could have abandoned the MW.	Locate	See remarks.	Vault does not allow for installation of a lock.
336	MW10001	5	10/20/2025	Yes	No	Yes	-	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
337	MW10003	5	10/20/2025	Yes	No	Yes	-	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
338	MW11001	7	10/23/2025	Yes	No	Yes	-	N/A	-	-	Missing bolt. Refreshed ID.	Replace bolt	-	Vault does not allow for installation of a lock.
339	MW11002	7	10/23/2025	Yes	No	Yes	-	N/A	-	-	Refreshed ID	-	-	Vault does not allow for installation of a lock.
340	MW11003	7	10/23/2025	No	No	-	-	N/A	-	-	Did not locate	Locate	-	Vault does not allow for installation of a lock.
341	MW14001	8	10/22/2025	Yes	No	Yes	N/A	N/A	Yes	No	-	-	-	1" PVC stick-up marker with 1" stick-up well
342	MW14002	8	10/22/2025	No	No	-	-	-	-	-	Could not locate (dense vegetation)	Locate and remove vegetation	-	1" PVC stick-up marker with 1" stick-up well

Table 1
2025 Well Inventory
Former Griffiss Air Force Base

Count	Well ID	Figure	Inspection Date	Well Located (Yes/No)	Well Abandoned (Yes/No)	Well ID (Yes/No)	Concrete Pad Condition	Lock Present (Yes, No, N/A)	Well Cap Present (Yes/No)	Pump Present (Yes/No)	2025 Field Remarks	Future Actions & Repairs Needed	Justification for not Identifying Well in 2025	General Comments and Comments Carried Over From Previous Well Inventories
343	MW14003	8	10/22/2025	No	No	-	-	-	-	-	Could not locate (dense vegetation)	Locate and remove vegetation	-	1" PVC stick-up marker with 1" stick-up well
344	MW14004	8	10/22/2025	Yes	No	Yes	Good	N/A	Yes	No	-	-	-	1" PVC stick-up marker with flush mount vault. Vault does not allow for installation of a lock.
345	MW14005	8	10/22/2025	Yes	No	Yes	N/A	N/A	Yes	No	-	-	-	1" PVC stick-up marker with 1" stick-up well
346	AP1MW-1	8	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
347	AP1MW-2	8	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-
348	AP1MW-3	8	10/20/2025	Yes	No	Yes	Good	-	-	-	Located only (inside fence)	-	-	-
349	AP1MW-4	8	10/20/2025	Yes	No	Yes	Good	-	-	-	Located only (inside fence)	-	-	-
350	AP1MW-5	8	10/20/2025	Yes	No	Yes	Good	Yes	Yes	No	-	-	-	-

Total wells sampled in 2025:	0
Total wells not sampled in 2025:	315
AFFF wells inspected in 2025:	33
Total wells located in 2025:	339
Total wells not located in 2025:	11
Wells requiring maintenance in 2026:	136

Notes:

" = inch
AFFF = Aqueous film forming foam
bgs = below ground surface
DNL = Did not locate
ft btoc = feet below top of casing
ID = Identification
KMZ = A compressed file that stores map locations viewable in various geographic information systems (GIS) applications, most notably Google Earth.
N/A = Not applicable
PVC = Polyvinyl chloride
SS = Stainless steel
TOC = Top of casing
USGS - United States Geological Survey

Table 2. Static Well Details

This page intentionally left blank.

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
1	ANGMW-1	Monitoring Well	FT030 - Not Used	1182056.00	1130500.00	2" PVC	Flush mount	18.0	-	-	-	8.0 - 18.0	10.0
2	LF1MW-UNK-01	Monitoring Well	LF001 - Not Used	approx: 1183428.66	approx: 1132850.73	2" PVC	Stick-up	-	-	-	4.00	- - -	-
3	LF1MW-UNK-02	Monitoring Well	LF001 - Not Used	approx: 1183385.25	approx: 1132819.48	2" PVC	Stick-up	-	-	-	4.00	- - -	-
4	LF1MW-UNK-03	Monitoring Well	LF001 - Not Used	approx: 1183334.91	approx: 1132776.07	2" PVC	Stick-up	-	-	-	4.20	- - -	-
5	LF1P-2	Monitoring Well	LF001 - LTM	1183682.00	1132543.00	4" PVC	Stick-up	13.0	502.31	504.18	1.87	8.0 - 13.0	5.0
6	LF1P-3	Monitoring Well	LF001 - LTM	1183270.00	1132922.00	4" PVC	Stick-up	17.0	506.13	512.5	6.37	12.0 - 17.0	5.0
7	LF1P-5	Monitoring Well	LF001 - LTM	1183482.00	1132160.00	4" PVC	Stick-up	20.0	494.91	496.94	2.03	15.0 - 20.0	5.0
8	LF1MW-5	Monitoring Well	LF001 - LTM	1183506.00	1132374.00	4" PVC	Stick-up	20.0	494.74	496.51	1.77	10.0 - 20.0	10.0
9	LF1MW-6	Monitoring Well	LF001 - LTM	1183754.00	1132441.00	4" PVC	Stick-up	15.0	497.36	499.15	1.79	5.0 - 15.0	10.0
10	LF1MW-10	Monitoring Well	LF001 - LTM	1183544.31	1132764.36	2" SS	Stick-up	30.0	528.08	530.65	2.57	20.0 - 30.0	10.0
11	LF1MW-11	Monitoring Well	LF001 - LTM	1184166.39	1132207.50	2" SS	Stick-up	12.5	499.38	502.08	2.70	2.5 - 12.5	10.0
12	LF1MW-12	Monitoring Well	LF001 - LTM	1184381.05	1132127.83	2" SS	Stick-up	13.0	501.82	504.38	2.56	3.0 - 13.0	10.0
13	LF1MW-13	Monitoring Well	LF001 - LTM	1183192.36	1132127.04	2" SS	Stick-up	20.0	492.91	495.33	2.42	10.0 - 20.0	10.0
14	LF1MW-14	Monitoring Well	LF001 - LTM	1184033.70	1131755.80	2" SS	Stick-up	12.5	501.44	504.34	2.90	2.5 - 12.5	10.0
15	LF1MW-103	Monitoring Well	LF001 - LTM	1183707.24	1132550.91	2" SS	Stick-up	32.8	505.27	507.93	2.66	22.8 - 32.8	10.0
16	MWSAR03	Monitoring Well	LF001 - LTM	1183824.00	1133585.00	2" PVC	Stick-up	22.0	533.28	535.09	1.81	12.0 - 22.0	10.0
17	LF2MW-4	Monitoring Well	LF002 - LTM	1177293.00	1139871.00	2" PVC	Stick-up	38.8	553.54	555.02	1.48	28.9 - 38.8	10.0
18	LF2MW-12	Monitoring Well	LF002 - LTM	1176923.27	1139287.75	2" SS	Stick-up	18.0	527.14	529.50	2.36	8.0 - 18.0	10.0
19	LF2MW-13	Monitoring Well	LF002 - LTM	1177362.29	1139036.66	2" Steel	Stick-up	14.5	522.50	524.48	1.98	4.5 - 14.5	10.0
20	LF2MW-14	Monitoring Well	LF002 - LTM	1177793.86	1140216.73	2" SS	Stick-up	15.5	536.85	539.57	2.72	5.5 - 15.5	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
21	LF2MW2-1	Monitoring Well	LF002 - LTM	1177656.00	1139216.00	4" PVC	Stick-up	32.0	-	-	-	22.0 - 32.0	10.0
22	LF2MW-UNK-01	Monitoring Well	LF002 - Not Used	Approx: 1177719.73	Approx: 1139190.63	2"	Stick-up	-	-	-	3.10	- - -	-
23	LF2MW-100	Monitoring Well	LF002 - LTM	1176912.42	1139303.67	2" SS	Stick-up	64.0	526.58	529.20	2.62	54.0 - 64.0	10.0
24	LF7MW-22	Monitoring Well	LF003 - LTM	1178159.21	1136704.00	2" SS	Flush mount	10.9	485.10	486.63	1.53	6.0 - 10.9	4.9
25	LF7MW-23	Monitoring Well	LF003 - LTM	1177765.45	1137119.19	2" PVC	Flush mount	14.0	486.04	487.83	1.79	4.0 - 14.0	10.0
26	LF7MW-26	Monitoring Well	LF003 - LTM	1178060.22	1137047.43	2" SS	Stick-up	16.5	499.77	502.03	2.26	6.5 - 16.5	10.0
27	LF7MW-27	Monitoring Well	LF003 - LTM	1178508.55	1136580.51	2" SS	Stick-up	12.5	500.96	502.93	1.97	2.5 - 12.5	10.0
28	LF7MW-28	Monitoring Well	LF003 - LTM	1177972.90	1136790.61	2" SS	Flush mount	11.5	485.81	487.83	2.02	1.5 - 11.5	10.0
29	LF7MW-29	Monitoring Well	LF003 - LTM	1178541.35	1137510.34	2" Steel	Stick-up	21.0	522.46	525.56	3.10	11.0 - 21.0	10.0
30	LF7MW-30	Monitoring Well	LF003 - LTM	1177806.46	1137473.59	2" SS	Stick-up	11.5	494.39	496.17	1.78	1.5 - 11.5	10.0
31	LF7MW-100	Monitoring Well	LF003 - LTM	1178139.99	1136973.28	4" PVC	Stick-up	43.0	500.99	503.57	2.58	33.0 - 43.0	10.0
32	LF5MW-1A	Monitoring Well	LF007 - LTM	1173976.70	1133819.84	2" PVC	Stick-up	22.9	476.15	478.50	2.35	12.9 - 22.9	10.0
33	LF5MW-3	Monitoring Well	LF007 - LTM	1173953.00	1133260.00	2" PVC	Stick-up	13.2	460.31	462.45	2.14	3.2 - 13.2	10.0
34	LF5MW-4	Monitoring Well	LF007- Not Used	1173569.42	1133541.14	2" SS	Stick-up	14.8	457.43	459.66	2.23	2.0 - 12.0	10.0
35	LF5MW-5	Monitoring Well	LF007 - LTM	1173619.07	1133630.64	2" SS	Stick-up	12.0	459.58	461.49	1.91	2.0 - 12.0	10.0
36	MW49D07	Monitoring Well	LF007 - LTM	1173539.00	1133247.00	2" PVC	Stick-up	14.0	457.07	459.51	2.44	4.0 - 14.0	10.0
37	LF5MW-100R	Monitoring Well	LF007 - LTM	1173686.99	1133338.49	2" SS	Stick-up	67.4	447.63	450.76	3.13	57.4 - 67.4	10.0
38	SD052-04-IW01	Injection Well	SD052-04 - Injections Only	1172408.40	1134923.80	2" PVC	Stick-up	53.9	455.60	458.79	3.19	33.7 - 53.7	20.0
39	SD052-04-IW02	Injection Well	SD052-04 - Injections Only	1172389.80	1134939.70	2" PVC	Stick-up	55.3	455.00	457.13	2.13	35.1 - 55.1	20.0
40	SD052-04-IW03	Injection Well	SD052-04 - Injections Only	1172393.30	1134950.40	2" PVC	Stick-up	53.5	457.68	455.40	-2.28	33.3 - 53.3	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
41	SD052-04-IW04	Injection Well	SD052-04 - Injections Only	1172449.40	1134992.70	2" PVC	Stick-up	54.8	457.40	459.15	1.75	34.6 - 54.6	20.0
42	LF6IW-01	Injection Well	SD052-04 - Injections Only	1172402.36	1134947.75	2" PVC	Stick-up	47.0	455.70	457.69	1.99	37.0 - 47.0	10.0
43	LF6IW-02	Injection Well	SD052-04 - Injections Only	1172401.39	1134941.80	2" PVC	Stick-up	55.0	455.45	457.41	1.96	45.0 - 55.0	10.0
44	LF6IW-03	Injection Well	SD052-04 - Injections Only	1172396.27	1134953.35	2" PVC	Stick-up	55.0	455.80	457.62	1.82	45.0 - 55.0	10.0
45	LF6IW-04	Injection Well	SD052-04 - Injections Only	1172401.15	1134956.96	2" PVC	Stick-up	55.0	456.43	458.77	2.34	45.0 - 55.0	10.0
46	LF6IW-05	Injection Well	SD052-04 - Injections Only	1172400.69	1134930.30	2" PVC	Stick-up	47.0	455.26	456.97	1.71	37.0 - 47.0	10.0
47	LF6IW-06	Injection Well	SD052-04 - Injections Only	1172396.53	1134935.76	2" PVC	Stick-up	55.0	455.50	457.67	2.17	45.0 - 55.0	10.0
48	LF6MW-1	Monitoring Well	LF009 - LTM	1172661.00	1135717.00	2" PVC	Stick-up	67.3	518.12	519.33	1.21	57.3 - 67.3	10.0
49	LF6MW-12	Monitoring Well	LF009 - LTM	1172397.87	1134944.13	2" PVC	Stick-up	51.0	455.61	457.59	1.98	41.0 - 51.0	10.0
50	LF6MW-13RD	Monitoring Well	SD052-04 - LTM	1172084.49	1134909.71	2" PVC	Stick-up	40.0	451.51	453.41	1.90	20.0 - 40.0	20.0
51	LF6MW-14BR	Monitoring Well	LF009 - Not Used	1172017.01	1135059.12	2" PVC	Stick-up	112.5	454.17	456.61	2.44	102.5 - 112.5	10.0
52	LF6MW-16	Monitoring Well	SD052-04 - LTM	1172393.53	1134940.32	2" PVC	Stick-up	47.0	455.41	457.39	1.98	37.0 - 47.0	10.0
53	LF6MW-17	Monitoring Well	SD052-04 - LTM	1172392.96	1134947.91	2" PVC	Stick-up	55.0	456.04	457.96	1.92	45.0 - 55.0	10.0
54	LF6MW-18	Monitoring Well	SD052-04 - Not Used	1172377.76	1134946.07	2" PVC	Stick-up	47.0	455.59	457.47	1.88	37.0 - 47.0	10.0
55	LF6MW-19	Monitoring Well	SD052-04 - Not Used	1172384.58	1134953.47	2" PVC	Stick-up	55.0	455.83	457.70	1.87	45.0 - 55.0	10.0
56	LF6MW-20	Monitoring Well	SD052-04 - LTM	1172390.70	1134934.67	2" PVC	Stick-up	51.0	455.35	457.31	1.96	41.0 - 51.0	10.0
57	LF6MW-27	Monitoring Well	SD052-04 - Not Used	1172473.54	1134837.28	2" PVC	Stick-up	55.0	453.46	455.48	2.02	35.0 - 55.0	20.0
58	LF6MW-28	Monitoring Well	SD052-04 - Not Used	1172500.73	1134993.37	2" PVC	Stick-up	45.0	455.78	457.03	1.25	25.0 - 45.0	20.0
59	LF6MW-29	Monitoring Well	SD052-04 - Not Used	1172485.75	1135172.31	2" PVC	Stick-up	37.0	466.62	468.54	1.92	17.0 - 37.0	20.0
60	LF6MW-30	Monitoring Well	SD052-04 - Not Used	1172383.69	1135083.41	2" PVC	Stick-up	45.0	459.13	461.04	1.91	25.0 - 45.0	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
61	LF6MW-31	Monitoring Well	SD052-04 - LTM	1172368.48	1134875.43	2" PVC	Stick-up	55.0	453.20	455.17	1.97	35.0 - 55.0	20.0
62	LF6MW-32	Monitoring Well	SD052-04 - Not Used	1172224.69	1135166.03	2" PVC	Stick-up	44.5	462.67	464.56	1.89	34.5 - 44.5	10.0
63	LF6MW-39	Monitoring Well	SD052-04 - LTM	1172082.35	1135006.96	2" PVC	Stick-up	32.0	456.70	458.50	1.80	22.0 - 32.0	10.0
64	LF6TW-33	Temporary Monitoring Well	SD052-04 - LTM	1172409.41	1134923.99	1" PVC	Stick-up	39.0	456.17	459.74	3.57	19.0 - 39.0	20.0
65	LF6TW-34	Temporary Monitoring Well	SD052-04 - LTM	1172448.34	1134987.84	1" PVC	Stick-up	55.0	457.60	460.00	2.40	35.0 - 55.0	20.0
66	LF6TW-35	Temporary Monitoring Well	SD052-04 - LTM	1172393.30	1135014.77	1" PVC	Stick-up	55.0	457.39	459.27	1.88	35.0 - 55.0	20.0
67	LF6TW-36	Temporary Monitoring Well	SD052-04 - LTM	1172338.33	1134950.04	1" PVC	Stick-up	55.0	455.08	459.08	4.00	35.0 - 55.0	20.0
68	LF6TW-37	Temporary Monitoring Well	SD052-04 - Not Used	1172337.31	1135007.88	1" PVC	Stick-up	55.0	455.98	459.35	3.37	35.0 - 55.0	20.0
69	LF6TW-38	Temporary Monitoring Well	SD052-04 - LTM	1172288.45	1134986.99	1" PVC	Stick-up	55.0	457.35	460.53	3.18	35.0 - 55.0	20.0
70	LF6VMW-10R2	Monitoring Well	LF009 - LTM	1172210.55	1135288.97	2" PVC	Stick-up	35.0	464.20	466.14	1.94	25.0 - 35.0	10.0
71	LF6VMW-13R	Monitoring Well	SD052-04 - LTM	1172095.12	1134923.10	2" PVC	Stick-up	37.0	453.12	454.66	1.54	17.0 - 37.0	20.0
72	LF6VMW-14	Monitoring Well	SD052-04 - Not Used	1172000.51	1135036.68	2" PVC	Stick-up	42.0	452.69	454.87	2.18	22.0 - 42.0	20.0
73	LF6VMW-15R	Monitoring Well	SD052-04 - Not Used	1171960.35	1135290.01	2" PVC	Stick-up	40.0	464.42	466.61	2.19	30.0 - 40.0	10.0
74	LF6VMW-17D	Monitoring Well	LF009 - LTM	1172076.60	1135535.30	2" SS	Stick-up	50.0	465.10	467.18	2.08	40.0 - 50.0	10.0
75	LF6VMW-17S	Monitoring Well	LF009 - LTM	1172097.90	1135538.30	2" SS	Stick-up	16.0	464.88	466.69	1.81	6.0 - 16.0	10.0
76	LF6VMW-18	Monitoring Well	LF009 - LTM	1171848.40	1135825.10	2" SS	Stick-up	55.0	460.98	463.15	2.17	45.0 - 55.0	10.0
77	LF6VMW-19	Monitoring Well	LF009 - LTM	1171789.66	1136061.18	2" SS	Stick-up	30.0	459.73	461.34	1.61	20.0 - 30.0	10.0
78	LF6VMW-20	Monitoring Well	LF009 - LTM	1171846.50	1136385.50	2" SS	Stick-up	70.5	461.96	464.79	2.83	60.5 - 70.5	10.0
79	LF6VMW-21	Monitoring Well	LF009 - LTM	1172188.00	1136190.50	2" SS	Stick-up	70.5	495.43	497.74	2.31	60.5 - 70.5	10.0
80	LF6VMW-22	Monitoring Well	LF009 - LTM	1172260.50	1135381.60	2" SS	Stick-up	40.0	465.71	467.64	1.93	30.0 - 40.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
81	LF6VMW-23	Monitoring Well	LF009 - LTM	1172406.00	1135269.20	2" PVC	Stick-up	50.3	467.64	469.65	2.01	40.3 - 50.3	10.0
82	LF6VMW-24	Monitoring Well	LF009 - LTM	1172533.20	1135097.50	2" SS	Stick-up	51.0	463.25	465.76	2.51	41.0 - 51.0	10.0
83	LF6VMW-25	Monitoring Well	LF009 - LTM	1172589.50	1134850.20	2" SS	Stick-up	49.0	455.60	457.69	2.09	39.0 - 49.0	10.0
84	LF6VMW-26	Monitoring Well	SD052-04/LF009 - LTM	1172226.72	1134927.56	2" SS	Stick-up	55.0	455.08	457.90	2.82	45.0 - 55.0	10.0
85	TMCMW-9	Monitoring Well	LF009 - LTM	1172582.00	1134859.00	4" PVC	Stick-up	28.0	455.48	457.16	1.68	18.0 - 28.0	10.0
86	TMC-USGS-2	Monitoring Well	LF009 - LTM	1171618.05	1135664.49	2" PVC	Stick-up	26.5	452.13	454.50	2.37	24.0 - 26.5	2.5
87	LAWMW-19	Monitoring Well	USGS well - Not Used	1171023.00	1137732.00	2" PVC	Stick-up	51.8	489.97	491.76	1.79	41.8 - 51.8	10.0
88	TMC-USGS-1	Monitoring Well	None - Not Used	1171250.00	1135344.00	2" PVC	Stick-up	21.5	454.91	457.81	2.90	19.0 - 21.5	2.5
89	782MW-1	Monitoring Well	SD052-01 - Not Used	1175125.90	1137634.60	2" PVC	Flush mount	32.7	473.76	473.58	-0.18	22.7 - 32.7	10.0
90	782MW-1R	Monitoring Well	SD052-01 - PFC Investigation	1175131.00	1137630.00	2" PVC	Flush mount	28.3	473.62	473.38	-0.24	18.3 - 28.3	10.0
91	782MW-3	Monitoring Well	SD052-01 - Not Used	1175289.30	1137307.59	2" PVC	Flush mount	19.0	473.81	473.49	-0.32	9.0 19.0	10.0
92	782MW-3R	Monitoring Well	SD052-01 - PFC Investigation	1175294.00	1137315.00	2" PVC	Flush mount	31.6	473.67	473.33	-0.34	16.6 - 31.6	15.0
93	782MW-5	Monitoring Well	SD052-01 - Not Used	1174918.45	1136711.77	2" PVC	Flush mount	25.0	477.30	476.63	-0.67	15.0 - 25.0	10.0
94	782MW-6D	Monitoring Well	SD052-01 - Not Used	1174869.57	1137670.31	2" PVC	Stick-up	48.0	478.54	478.55	0.01	38.0 - 48.0	10.0
95	782MW-6R2	Monitoring Well	SD052-01 - Not Used	1174890.35	1137643.75	2" PVC	Stick-up	34.5	476.82	478.42	1.60	19.5 - 34.5	15.0
96	782MW-9	Monitoring Well	SD052-01 - PFC Investigation	1175045.31	1137985.45	2" PVC	Flush mount	30.0	476.51	476.54	0.03	15.0 - 30.0	15.0
97	782MW-10	Monitoring Well	SD052-01 - LTM	1174739.67	1137498.35	2" PVC	Flush mount	34.0	477.79	477.50	-0.29	19.0 - 34.0	15.0
98	782MW-11	Monitoring Well	SD052-01 - PFC Investigation	1175150.04	1137909.34	2" PVC	Stick-up	32.7	475.68	478.21	2.53	22.7 - 32.7	10.0
99	782MW-12	Monitoring Well	SD052-01 - PFC Investigation	1175304.72	1137742.26	2" PVC	Flush mount	33.0	475.81	475.56	-0.25	23.0 - 33.0	10.0
100	782-MW184	Monitoring Well	SD052-01 - Not Used	1174819.11	1138003.00	2" PVC	Flush mount	74.5	476.20	475.86	-0.34	64.5 - 74.5	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
101	782VMW-76	Monitoring Well	SD052-01 - LTM	1174418.22	1137171.89	2" PVC	Flush mount	43.0	477.86	477.59	-0.27	33.0 - 43.0	10.0
102	782VMW-78	Monitoring Well	SD052-01 - LTM	1174578.68	1137025.78	2" PVC	Stick-up	42.0	478.26	481.22	2.96	32.0 - 42.0	10.0
103	782VMW-81	Monitoring Well	SD052-01 - LTM	1174369.98	1136784.76	2" PVC	Stick-up	50.0	477.71	479.57	1.86	40.0 - 50.0	10.0
104	782VMW-82	Monitoring Well	SD052-01 - Not Used	1174499.71	1136644.46	2" PVC	Stick-up	48.0	475.49	478.06	2.57	38.0 - 48.0	10.0
105	782VMW-83	Monitoring Well	SD052-01 - Not Used	1174121.75	1136506.61	2" PVC	Stick-up	35.0	477.72	480.13	2.41	25.0 - 35.0	10.0
106	782VMW-84	Monitoring Well	SD052-01 - LTM	1174821.59	1137992.22	2" PVC	Flush mount	44.5	476.40	476.08	-0.32	34.5 - 44.5	10.0
107	782VMW-84D	Monitoring Well	SD052-01 - LTM	1174796.74	1138001.78	2" PVC	Flush mount	56.5	475.57	475.18	-0.39	41.5 - 56.5	15.0
108	782VMW-85	Monitoring Well	SD052-01 - Not Used	1175001.90	1137788.48	2" PVC	Stick-up	39.0	475.70	478.02	2.32	29.0 - 39.0	10.0
109	782VMW-86	Monitoring Well	SD052-01 - Not Used	1175194.30	1137587.73	2" PVC	Stick-up	37.0	475.65	477.68	2.03	27.0 - 37.0	10.0
110	782VMW-87	Monitoring Well	SD052-01 - Not Used	1174719.49	1138182.13	2" PVC	Flush mount	40.0	476.86	476.27	-0.59	30.0 - 40.0	10.0
111	782VMW-88	Monitoring Well	SD052-01 - Not Used	1174912.33	1138272.99	2" PVC	Flush mount	40.0	478.15	477.75	-0.40	30.0 - 40.0	10.0
112	782VMW-89	Monitoring Well	SD052-01 - Not Used	1175100.54	1137690.09	2" PVC	Stick-up	40.0	475.94	478.85	2.91	25.0 - 40.0	15.0
113	782VMW-90	Monitoring Well	SD052-01 - Not Used	1175018.57	1137506.82	2" PVC	Stick-up	30.0	476.23	478.95	2.72	20.0 - 30.0	10.0
114	782VMW-92	Monitoring Well	SD052-01 - Not Used	1174479.88	1137671.17	2" PVC	Flush mount	40.0	476.99	476.65	-0.34	30.0 - 40.0	10.0
115	782VMW-93	Monitoring Well	SD052-01 - Not Used	1174569.71	1137325.35	2" PVC	Flush mount	40.0	477.87	477.57	-0.30	30.0 - 40.0	10.0
116	782VMW-94	Monitoring Well	SD052-01 - Not Used	1174743.61	1137348.67	2" PVC	Flush mount	44.5	478.3	478.03	-0.27	34.5 - 44.5	10.0
117	782VMW-95	Monitoring Well	SD052-01 - Not Used	1174876.72	1137232.26	2" PVC	Flush mount	35.0	476.49	476.16	-0.33	20.0 - 35.0	15.0
118	782VMW-96	Monitoring Well	SD052-01 - LTM	1174603.52	1137545.52	2" PVC	Flush mount	43.0	477.13	476.73	-0.40	33.0 - 43.0	10.0
119	782VMW-97	Monitoring Well	SD052-01 - Not Used	1174073.12	1136622.81	2" PVC	Stick-up	35.0	478.52	480.76	2.24	25.0 - 35.0	10.0
120	782VMW-98	Monitoring Well	SD052-01 - Not Used	1173953.03	1136359.76	2" PVC	Stick-up	35.0	477.06	479.47	2.41	25.0 - 35.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
121	782VMW-99	Monitoring Well	SD052-01 - Not Used	1173703.09	1136597.73	2" PVC	Stick-up	35.0	477.83	480.89	3.06	20.0 - 35.0	15.0
122	782VMW-100	Monitoring Well	SD052-01 - LTM	1174894.76	1138716.31	2" PVC	Stick-up	25.0	457.10	459.94	2.84	10.0 - 25.0	15.0
123	782VMW-101	Monitoring Well	SD052-01 - LTM	1174658.16	1138910.74	2" PVC	Stick-up	22.0	451.11	453.95	2.84	7.0 - 22.0	15.0
124	782VMW-102	Monitoring Well	SD052-01 - LTM	1174386.72	1139063.60	2" PVC	Stick-up	23.0	448.82	451.84	3.02	8.0 - 23.0	15.0
125	782VMW-104	Monitoring Well	SD052-01 - LTM	1174163.56	1136567.00	2" PVC	Stick-up	33.0	477.04	479.63	2.59	18.0 - 33.0	15.0
126	782VMW-105B	Monitoring Well	SD052-01 - LTM	1174207.49	1136605.09	2" PVC	Stick-up	42.0	477.37	480.25	2.88	27.0 - 42.0	15.0
127	782VMW-121	Monitoring Well	SD052-01 - LTM	1174778.29	1138757.34	2" PVC	Stick-up	25.0	458.06	459.87	1.81	10.0 - 25.0	15.0
128	782VMW-121D	Monitoring Well	SD052-01 - LTM	1174761.65	1138752.45	2" PVC	Stick-up	31.0	458.81	460.71	1.90	21.0 - 31.0	10.0
129	AP2MW-3	Monitoring Well	SD052-01 - LTM	1174551.00	1138744.00	2" PVC	Flush mount	33.6	465.97	465.63	-0.34	19.0 - 33.6	14.6
130	775EW-1	Extraction Well converted to Injection Well	SD052-02 - Injections	1173032.34	1135795.01	4" SS	Flush mount	76.0	516.72	516.56	-0.16	56.0 - 76.0	20.0
131	775EW-1R	Extraction Well converted to Injection Well	SD052-02 - Injections	1172983.69	1135816.60	4" SS	Flush mount	-	516.40	515.55	-0.85	- - -	-
132	775EW-3	Extraction Well converted to Injection Well	SD052-02 - Injections	1172996.82	1135753.37	4" SS	Flush mount	-	516.02	515.16	-0.86	- - -	-
133	775MW-2	Monitoring Well	SD052-02 - Not Used	1173493.00	1135938.00	2" PVC	Stick-up	65.0	514.08	515.65	1.57	50.0 - 65.0	15.0
134	775MW-6	Monitoring Well	SD052-02 - LTM	1173123.00	1135631.00	2" PVC	Stick-up	78.0	517.18	518.02	0.84	68.0 - 78.0	10.0
135	775-MW20	Monitoring Well	SD052-02 - LTM	1172598.94	1135787.11	2" PVC	Stick-up	120.2	518.14	520.35	2.21	110.2 - 120.2	10.0
136	775-MW20R	Monitoring Well	SD052-02 - LTM	1172590.24	1135795.13	2" PVC	Stick-up	138.7	518.62	519.48	0.86	133.7 - 138.7	5.0
137	775-MW20RBR	Monitoring Well	SD052-02 - Not Used	1172492.89	1135900.74	2" PVC	Stick-up	169.7	518.58	519.50	0.92	159.7 - 169.7	10.0
138	775MW-27	Monitoring Well	SD052-02 - LTM	1173004.19	1135837.05	2" PVC	Flush mount	80.8	516.59	515.99	-0.60	60.8 - 80.8	20.0
139	775MW-28	Monitoring Well	SD052-02 - LTM	1172787.53	1135778.13	2" PVC	Stick-up	91.0	515.72	517.68	1.96	71.0 - 91.0	20.0
140	775VMW-4	Monitoring Well	SD052-02 - LTM	1173227.00	1135813.00	2" PVC	Stick-up	70.0	517.64	518.51	0.87	60.0 - 70.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
141	775VMW-5	Monitoring Well	SD052-02 - LTM	1173147.00	1135890.00	2" PVC	Stick-up	75.0	517.94	518.64	0.70	65.0 - 75.0	10.0
142	775VMW-8	Monitoring Well	SD052-02 - LTM	1172910.00	1135803.00	2" PVC	Stick-up	78.0	517.79	518.22	0.43	68.0 - 78.0	10.0
143	775VMW-9	Monitoring Well	SD052-02 - LTM	1172920.34	1135482.28	2" PVC	Stick-up	99.0	511.92	513.63	1.71	84.0 - 99.0	15.0
144	775VMW-10	Monitoring Well	SD052-02 - LTM	1172769.09	1135613.75	2" PVC	Stick-up	103.0	515.14	517.22	2.08	88.0 - 103.0	15.0
145	775VMW-11	Monitoring Well	SD052-02 - Not Used	1173630.84	1136124.93	2" PVC	Stick-up	57.0	484.66	486.60	1.94	47.0 - 57.0	10.0
146	775VMW-14	Monitoring Well	SD052-02 - Not Used	1173337.31	1136103.63	2" PVC	Stick-up	70.0	513.91	515.85	1.94	60.0 - 70.0	10.0
147	775VMW-15R1	Monitoring Well	SD052-02 - Not Used	1173477.86	1135425.48	2" PVC	Stick-up	104.0	516.54	518.82	2.28	94.0 - 104.0	10.0
148	775VMW-16	Monitoring Well	SD052-02 - Not Used	1172880.00	1136036.31	2" PVC	Stick-up	87.0	518.96	520.94	1.98	77.0 - 87.0	10.0
149	775VMW-18R	Monitoring Well	SD052-02/LF009 - LTM	1173166.52	1135300.79	2" PVC	Stick-up	95.0	508.67	510.71	2.04	85.0 - 95.0	10.0
150	775VMW-19R	Monitoring Well	SD052-02 - LTM	1172790.97	1135700.29	2" PVC	Stick-up	75.0	515.58	517.46	1.88	55.0 - 75.0	20.0
151	775VMW-20R	Monitoring Well	SD052-02/LF009 - LTM	1172499.98	1135888.24	2" PVC	Stick-up	115.0	518.85	521.11	2.26	105.0 - 115.0	10.0
152	775VMW-23	Monitoring Well	SD052-02 - Not Used	1173770.00	1135979.80	2" PVC	Stick-up	35.0	484.35	486.77	2.42	25.0 - 35.0	10.0
153	775VMW-24	Monitoring Well	SD052-02 - Not Used	1173495.87	1136265.91	2" PVC	Stick-up	67.0	483.79	485.40	1.61	57.0 - 67.0	10.0
154	775VMW-25	Monitoring Well	SD052-02 - Not Used	1173593.56	1135622.50	2" PVC	Flush mount	75.0	512.10	511.94	-0.16	65.0 - 75.0	10.0
155	SD052-02_IW-01	Injection Well	SD052-02 - Injections	1173188.90	1135887.00	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
156	SD052-02_IW-02	Injection Well	SD052-02 - Injections	1173178.30	1135912.30	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
157	SD052-02_IW-03	Injection Well	SD052-02 - Injections	1173127.90	1135662.50	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
158	SD052-02_IW-04	Injection Well	SD052-02 - Injections	1173108.00	1135698.10	2" PVC	Flush mount	84.0	-	-	-	64.0 - 84.0	20.0
159	SD052-02_IW-05	Injection Well	SD052-02 - Injections	1173108.90	1135819.70	2" PVC	Flush mount	84.0	-	-	-	64.0 - 84.0	20.0
160	SD052-02_IW-06	Injection Well	SD052-02 - Injections	1173056.80	1135873.60	2" PVC	Flush mount	83.0	-	-	-	63.0 - 83.0	20.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
161	SD052-02_IW-07	Injection Well	SD052-02 - Injections	1173147.50	1135624.00	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
162	SD052-02_IW-08	Injection Well	SD052-02 - Injections	1173121.50	1135550.20	2" PVC	Flush mount	92.0	-	-	-	72.0 - 92.0	20.0
163	SD052-02_IW-09	Injection Well	SD052-02 - Injections	1173063.10	1135598.80	2" PVC	Flush mount	92.0	-	-	-	72.0 - 92.0	20.0
164	SD052-02_IW-12	Injection Well	SD052-02 - Injections	1173019.30	1135523.30	2" PVC	Flush mount	100.0	-	-	-	80.0 - 100.0	20.0
165	SD052-02_IW-13	Injection Well	SD052-02 - Injections	1172971.00	1135552.50	2" PVC	Flush mount	100.0	-	-	-	80.0 - 100.0	20.0
166	SD052-02_IW-14	Injection Well	SD052-02 - Injections	1172939.20	1135801.90	2" PVC	Flush mount	78.0	-	-	-	68.0 - 78.0	10.0
167	817IW-1	Injection Well	SD052-05 - Injections	1180082.76	1135879.96	2" PVC	Stick-up	-	518.59	-	-	- - -	-
168	817IW-2	Injection Well	SD052-05 - Injections	1180076.77	1135885.76	2" PVC	Stick-up	-	518.88	-	-	- - -	-
169	817IW-3	Injection Well	SD052-05 - Injections	1180069.76	1135891.10	2" PVC	Stick-up	-	519.05	-	-	- - -	-
170	817IW-4	Injection Well	SD052-05 - Injections	1180064.86	1135898.52	2" PVC	Stick-up	-	519.23	-	-	- - -	-
171	817IW-5	Injection Well	SD052-05 - Injections	1180059.69	1135903.22	2" PVC	Stick-up	-	519.17	-	-	- - -	-
172	817IW-6	Injection Well	SD052-05 - Injections	1180054.25	1135908.66	2" PVC	Stick-up	-	519.12	-	-	- - -	-
173	817IW-7	Injection Well	SD052-05 - Injections	1180049.52	1135913.91	2" PVC	Stick-up	-	519.29	-	-	- - -	-
174	817IW-8	Injection Well	SD052-05 - Injections	1180043.77	1135917.10	2" PVC	Stick-up	-	519.40	-	-	- - -	-
175	817MW-1	Monitoring Well	SD052-05 - LTM	1180068.47	1135910.04	1" PVC	Stick-up	20.0	519.93	522.10	2.17	10.0 - 20.0	10.0
176	817MW-3	Monitoring Well	SD052-05 - LTM	1180034.09	1135874.52	1" PVC	Stick-up	20.0	517.72	519.80	2.08	10.0 - 20.0	10.0
177	LAWMW-9	Monitoring Well	SD052-05 - LTM	1179884.00	1135570.00	2" PVC	Stick-up	17.0	505.83	507.84	2.01	7.0 - 17.0	10.0
178	WSA-IW01	Injection Well	SD052-05 - Not Used	1179950.44	1135783.51	2" PVC	Stick-up	19.0	512.69	514.77	2.08	9.0 - 19.0	10.0
179	WSA-IW02	Injection Well	SD052-05 - Not Used	1179957.83	1135790.28	2" PVC	Stick-up	20.0	512.39	514.61	2.22	10.0 - 20.0	10.0
180	WSA-IW03	Injection Well	SD052-05 - Not Used	1179958.91	1135800.50	2" PVC	Stick-up	20.0	512.71	515.10	2.39	10.0 - 20.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
181	WSA-IW04	Injection Well	SD052-05 - Not Used	1179949.01	1135811.54	2" PVC	Stick-up	19.5	512.18	514.33	2.15	9.5 - 19.5	10.0
182	WSAMW-2	Monitoring Well	SD052-05 - Not Used	1180469.00	1136049.00	2" PVC	Stick-up	15.2	531.99	533.95	1.96	5.2 - 15.2	10.0
183	WSAMW-3	Monitoring Well	SD052-05 - Not Used	1180971.00	1134913.00	2" PVC	Stick-up	16.3	527.48	530.34	2.86	6.3 - 16.3	10.0
184	WSAMW-8	Monitoring Well	SD052-05 - LTM	1180198.23	1135971.00	2" PVC	Stick-up	14.0	520.37	521.88	1.51	4.0 - 14.0	10.0
185	WSAMW-9	Monitoring Well	SD052-05 - LTM	1179468.66	1135387.24	2" PVC	Stick-up	8.0	482.60	484.19	1.59	3.0 - 8.0	5.0
186	WSAMW-11	Monitoring Well	SD052-05 - Not Used	1179950.70	1135795.44	2" PVC	Stick-up	12.5	512.14	513.89	1.75	7.2 - 12.2	5.0
187	WSAMW-12BR	Monitoring Well	SD052-05 - Not Used	1179451.23	1135646.55	2" PVC	Stick-up	42.0	500.01	502.13	2.12	32.0 - 42.0	10.0
188	WSAMW-13BR	Monitoring Well	SD052-05 - Not Used	1179597.57	1135249.32	2" PVC	Stick-up	43.0	483.08	485.17	2.09	23.0 - 43.0	20.0
189	WSAMW-14BR	Monitoring Well	SD052-05 - Not Used	1180205.21	1135964.95	2" PVC	Stick-up	35.0	518.50	522.01	3.51	24.7 - 34.7	10.0
190	WSA-MW-15	Monitoring Well	SD052-05 - Not Used	1179944.44	1135792.40	2" PVC	Stick-up	21.0	512.04	514.40	2.36	10.0 - 20.0	10.0
191	WSAMW-16	Monitoring Well	SD052-05 - LTM	1179943.17	1135804.76	2" PVC	Stick-up	20.0	511.86	514.18	2.32	10.0 - 20.0	10.0
192	WSAMW-18	Monitoring Well	SD052-05 - LTM	1179990.61	1135831.91	2" PVC	Stick-up	16.0	515.23	516.89	1.66	11.0 - 16.0	5.0
193	WSAMW-19	Monitoring Well	SD052-05 - LTM	1179856.58	1135748.98	2" PVC	Stick-up	18.0	511.79	513.07	1.28	13.0 - 18.0	5.0
194	WSAMW-21	Monitoring Well	SD052-05 - LTM	1179643.16	1135642.04	2" PVC	Stick-up	25.0	509.72	511.68	1.96	15.0 - 25.0	10.0
195	WSAMW-23	Monitoring Well	SD052-05 - LTM	1179679.21	1135866.52	2" PVC	Stick-up	25.0	518.16	519.92	1.76	15.0 - 25.0	10.0
196	WSAVMW-17	Monitoring Well	SD052-05 - LTM	1179785.39	1135658.66	2" SS	Stick-up	25.0	508.83	511.39	2.56	15.0 - 25.0	10.0
197	781MW-1	Monitoring Well	SS054 - LTM	1172759.69	1136628.86	2" PVC	Stick-up	64.5	516.2	515.71	-0.49	49.5 - 64.5	15.0
198	781MW-2	Monitoring Well	SS054 - LTM	1172828.68	1136642.29	2" PVC	Stick-up	65.0	513.3	514.66	1.36	50.0 - 65.0	15.0
199	781MW-3	Monitoring Well	SS054 - LTM	1172754.51	1136721.46	2" PVC	Stick-up	69.0	513.5	514.30	0.80	54.0 - 69.0	15.0
200	781MW-4	Monitoring Well	SS054 - LTM	1172565.01	1136720.25	2" PVC	Stick-up	64.0	513.5	515.89	2.39	54.0 - 64.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
201	781MW-5	Monitoring Well	SS054 - LTM	1172499.44	1136657.45	2" PVC	Stick-up	65.0	515.5	517.04	1.54	55.0 - 65.0	10.0
202	781MW-6	Monitoring Well	SS054 - LTM	1172461.56	1136622.83	2" PVC	Stick-up	64.0	515.9	517.26	1.36	54.0 - 64.0	10.0
203	781MW-7	Monitoring Well	SS054 - LTM	1172555.49	1136524.14	2" PVC	Stick-up	68.0	515.7	517.79	2.09	58.0 - 68.0	10.0
204	781MW-8	Monitoring Well	SS054 - LTM	1172670.37	1136612.59	2" PVC	Flush mount	63.0	514.5	514.26	-0.24	53.0 - 63.0	10.0
205	781MW-9	Monitoring Well	SS054 - LTM	1172729.68	1136670.72	2" PVC	Stick-up	64.0	515.6	516.90	1.30	54.0 - 64.0	10.0
206	781MW-10	Monitoring Well	SS054 - LTM	1172684.63	1136737.68	2" PVC	Stick-up	63.0	513.77	515.26	1.49	53.0 - 63.0	10.0
207	781MW-11	Monitoring Well	SS054 - LTM	1172702.30	1136562.64	2" PVC	Flush mount	65.0	513.8	513.49	-0.31	55.0 - 65.0	10.0
208	781MW-12	Monitoring Well	SS054 - LTM	1172423.31	1136584.90	2" PVC	Stick-up	68.0	515.7	517.16	1.46	58.0 - 68.0	10.0
209	781MW-13	Monitoring Well	SS054 - LTM	1172356.88	1136714.54	2" PVC	Stick-up	65.0	510.5	512.49	1.99	55.0 - 65.0	10.0
210	781MW-13R	Monitoring Well	SS054 - LTM	1172359.00	1136710.40	2" PVC	Stick-up	66.5	512.2	515.22	3.02	55.5 - 65.5	10.0
211	781MW-14	Monitoring Well	SS054 - LTM	1172440.17	1136799.26	2" PVC	Stick-up	62.0	508.8	510.87	2.07	52.0 - 62.0	10.0
212	781MW-15	Monitoring Well	SS054 - LTM	1172570.50	1136859.95	2" PVC	Stick-up	64.0	513.4	515.29	1.89	54.0 - 64.0	10.0
213	781MW-16	Monitoring Well	SS054 - LTM	1172328.65	1136850.64	2" PVC	Stick-up	60.0	505.6	507.65	2.05	50.0 - 60.0	10.0
214	781MW-17	Monitoring Well	SS054 - LTM	1172267.74	1136601.31	2" PVC	Stick-up	67.0	512.6	515.20	2.60	57.0 - 67.0	10.0
215	781MW-18	Monitoring Well	SS054 - LTM	1172164.51	1136652.64	2" PVC	Stick-up	58.0	505.7	507.48	1.78	48.0 - 58.0	10.0
216	781MW-19	Monitoring Well	SS054 - LTM	1172189.84	1136794.56	2" PVC	Stick-up	51.0	495.7	497.41	1.71	41.0 - 51.0	10.0
217	781MW-20	Monitoring Well	SS054 - LTM	1172090.64	1136463.32	2" PVC	Stick-up	44.0	491.4	493.70	2.30	34.0 - 44.0	10.0
218	781MW-21	Monitoring Well	SS054 - LTM	1171993.28	1136578.55	2" PVC	Stick-up	34.0	482.4	484.86	2.46	24.0 - 34.0	10.0
219	781PAIW-1	Injection Well	SS054 - LTM	1172601.22	1136721.02	4" PVC	Stick-up	63.0	515.8	518.57	2.77	48.0 - 63.0	15.0
220	781PAIW-2	Injection Well	SS054 - LTM	1172741.51	1136680.88	4" PVC	Stick-up	-	514.56	-	-	- - -	-

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
221	781PPRW-1	Recovery Well	SS054 - LTM	1172345.47	1136716.56	4" PVC	Stick-up	63.0	510.7	513.44	2.74	48.0 - 63.0	15.0
222	781PPRW-2	Recovery Well	SS054 - LTM	1172357.03	1136702.25	4" PVC	Stick-up	64.0	512.2	514.54	2.34	49.0 - 64.0	15.0
223	781PPRW-3	Recovery Well	SS054 - LTM	1172446.25	1136690.41	4" PVC	Stick-up	64.0	513.6	516.85	3.25	49.0 - 64.0	15.0
224	781PPRW-4	Recovery Well	SS054 - LTM	1172360.83	1136725.48	4" PVC	Stick-up	63.0	510.5	513.51	3.01	48.0 - 63.0	15.0
225	781PPRW-5	Recovery Well	SS054 - LTM	1172476.70	1136729.99	4" PVC	Stick-up	-	512.3	515.80	3.50	- - -	-
226	781PPRW-6	Recovery Well	SS054 - LTM	1172499.30	1136683.81	4" PVC	Stick-up	-	514.3	517.76	3.46	- - -	-
227	781PPRW-7	Recovery Well	SS054 - LTM	1172549.26	1136681.02	4" PVC	Stick-up	-	514.6	517.85	3.25	- - -	-
228	781PPRW-8	Recovery Well	SS054 - LTM	1172578.19	1136634.82	4" PVC	Stick-up	-	515.1	518.58	3.48	- - -	-
229	781PPRW-9	Recovery Well	SS054 - LTM	1172697.50	1136592.62	4" PVC	Flush mount	56.0	513.0	512.77	-0.23	46.0 - 56.0	10.0
230	781VBS-1	Biosparge	SS054 - Biosparge	1172404.54	1136693.69	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
231	781VBS-2	Biosparge	SS054 - Biosparge	1172365.64	1136696.82	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
232	781VBS-3	Biosparge	SS054 - Biosparge	1172337.59	1136724.30	1" PVC	Stick-up	65.0	-	-	-	60.0 - 65.0	5.0
233	781VBS-4	Biosparge	SS054 - Biosparge	1172364.22	1136742.99	1" PVC	Stick-up	62.0	-	-	-	57.0 - 62.0	5.0
234	781VBS-5	Biosparge	SS054 - Biosparge	1172210.87	1136641.48	1" PVC	Stick-up	64.0	-	-	-	59.0 - 64.0	5.0
235	781VBS-6	Biosparge	SS054 - Biosparge	1172241.28	1136626.67	1" PVC	Stick-up	70.0	-	-	-	65.0 - 70.0	5.0
236	781VBS-7	Biosparge	SS054 - Biosparge	1172270.77	1136556.43	1" PVC	Stick-up	70.0	-	-	-	65.0 - 70.0	5.0
237	781VBS-8	Biosparge	SS054 - Biosparge	1172627.12	1136699.84	1" PVC	Stick-up	60.0	-	-	-	55.0 - 60.0	5.0
238	781VBS-9	Biosparge	SS054 - Biosparge	1172640.61	1136608.44	1" PVC	Flush mount	65.0	-	-	-	60.0 - 65.0	5.0
239	781VBS-10	Biosparge	SS054 - Biosparge	1172688.87	1136626.85	1" PVC	Flush mount	64.0	-	-	-	59.0 - 64.0	5.0
240	781VBS-11	Biosparge	SS054 - Biosparge	1172749.46	1136657.95	1" PVC	Stick-up	62.0	-	-	-	60.0 - 62.0	2.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
241	781VBS-12	Biosparge	SS054 - Biosparge	1172707.46	1136697.70	1" PVC	Stick-up	64.5	-	-	-	59.5 - 64.5	5.0
242	AOC9MW-05	Monitoring Well	SS062 - LTM	1181171.85	1133372.26	2" PVC	Flush mount	14.0	484.17	482.72	-1.45	4.0 - 14.0	10.0
243	AOC9MW-06	Monitoring Well	SS062 - LTM	1181035.53	1133815.84	2" PVC	Stick-up	14.2	482.57	484.10	1.53	4.2 - 14.2	10.0
244	AOC9MW-07	Monitoring Well	SS062 - LTM	1181437.34	1133545.46	2" PVC	Stick-up	9.2	482.75	484.83	2.08	4.2 - 9.2	5.0
245	AOC9MW-08	Monitoring Well	SS062 - LTM	1181830.99	1133888.39	2" PVC	Stick-up	20.4	498.47	499.73	1.26	15.4 - 20.4	5.0
246	AOC9MW-9BR	Monitoring Well	SS062 - Not Used	1181037.03	1133735.93	2" PVC	Stick-up	43.2	481.21	482.59	1.38	23.2 - 43.2	20.0
247	AOC9MW-11BR	Monitoring Well	SS062 - Not Used	1182007.19	1134127.47	2" PVC	Stick-up	57.5	524.21	525.85	1.64	37.5 - 57.5	20.0
248	AOC9MW-12	Monitoring Well	SS062 - LTM	1181781.27	1133845.24	2" PVC	Flush mount	19.7	509.09	508.83	-0.26	10.0 - 19.7	9.7
249	AOC9MW-13	Monitoring Well	SS062 - LTM	1181793.24	1133855.65	2" PVC	Stick-up	22.2	508.53	510.76	2.23	12.2 - 22.2	10.0
250	AOC9MW-14	Monitoring Well	SS062 - LTM	1181913.04	1134024.58	2" PVC	Stick-up	24.0	519.05	520.86	1.81	14.0 - 24.0	10.0
251	AOC9MW-15	Monitoring Well	SS062 - LTM	1181701.71	1133799.71	2" PVC	Stick-up	14.0	500.04	501.99	1.95	9.0 - 14.0	5.0
252	AOC9MW-16	Monitoring Well	SS062 - LTM	1181624.12	1133750.28	2" PVC	Stick-up	14.0	497.26	499.19	1.93	9.0 - 14.0	5.0
253	AOC9MW-17	Monitoring Well	SS062 - LTM	1181517.91	1133589.49	2" PVC	Stick-up	14.0	487.51	489.44	1.93	9.0 - 14.0	5.0
254	AOC9MW-18	Monitoring Well	SS062 - LTM	1182102.90	1134592.40	2" PVC	Stick-up	20.5	527.84	529.34	1.50	10.5 - 20.5	10.0
255	AOC9MW-19	Monitoring Well	SS062 - LTM	1182022.06	1134404.34	2" PVC	Flush mount	18.7	523.38	523.05	-0.33	8.7 - 18.7	10.0
256	AOC9MW-20	Monitoring Well	SS062 - LTM	1181976.16	1134253.47	2" PVC	Stick-up	18.0	516.67	519.31	2.64	6.0 - 18.0	12.0
257	AOC9MW-21	Monitoring Well	SS062 - LTM	1181922.73	1134088.13	2" PVC	Stick-up	24.0	520.55	523.22	2.67	9.0 - 24.0	15.0
258	AOC9MW-22	Monitoring Well	SS062 - LTM	1181963.73	1134040.39	2" PVC	Stick-up	24.0	519.60	522.47	2.87	9.0 - 24.0	15.0
259	AOC9MW-23	Monitoring Well	SS062 - LTM	1181969.33	1134158.06	2" PVC	Stick-up	21.0	516.66	519.55	2.89	6.0 - 21.0	15.0
260	AOC9MW-24	Monitoring Well	SS062 - LTM	1181892.44	1134120.57	2" PVC	Stick-up	24.0	520.52	523.20	2.68	9.0 - 24.0	15.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
261	AOC9TW-95	Temporary Monitoring Well	SS062 - Not Used	1182021.16	1134088.07	1" PVC	Flush mount	23.2	522.62	522.35	-0.27	13.2 - 23.2	10.0
262	G009-MW01	Monitoring Well	SS062 - LTM	1181715.74	1133596.78	2" PVC	Stick-up	9.0	492.39	494.42	2.03	4.0 - 9.0	5.0
263	G009-MW02	Monitoring Well	SS062 - LTM	1181543.01	1133716.02	2" PVC	Stick-up	9.0	494.02	495.58	1.56	4.0 - 9.0	5.0
264	G009-MW03	Monitoring Well	SS062 - LTM	1181440.42	1133617.19	2" PVC	Stick-up	9.0	485.10	485.10	0.00	4.0 - 9.0	5.0
265	G009-MW04	Monitoring Well	SS062 - LTM	1181305.07	1133496.60	2" PVC	Stick-up	16.7	483.66	484.87	1.21	6.7 - 16.7	10.0
266	WSAMW-4	Monitoring Well	SS062 - Not Used	1181718.00	1134023.00	2" PVC	Stick-up	17.2	516.86	518.72	1.86	7.2 - 17.2	10.0
267	789MW-46R	Monitoring Well	SS067 - LTM	1173946.46	1138241.59	4" PVC	Stick-up	29.0	476.68	479.09	2.41	14.0 - 29.0	15.0
268	789MW-63R	Monitoring Well	SS067 - LTM	1174345.41	1138378.63	2" PVC	Stick-up	29.0	478.42	480.21	1.79	14.0 - 29.0	15.0
269	789MW-64	Monitoring Well	SS067 - LTM	1174419.27	1138155.83	2" PVC	Stick-up	22.0	476.16	478.53	2.37	12.0 - 22.0	10.0
270	789MW-83	Monitoring Well	SS067 - LTM	1174133.67	1138394.51	2" PVC	Flush mount	31.0	479.29	478.79	-0.50	21.0 - 31.0	10.0
271	789MW-95	Monitoring Well	SS067 - LTM	1174293.54	1138106.77	2" PVC	Stick-up	20.5	477.28	479.39	2.11	10.5 - 20.5	10.0
272	789MW-96	Monitoring Well	SS067 - LTM	1174085.78	1138127.20	4" PVC	Stick-up	24.5	474.71	476.69	1.98	14.5 - 24.5	10.0
273	789MW-97	Monitoring Well	SS067 - LTM	1174144.38	1138027.15	4" PVC	Stick-up	25.0	475.88	478.06	2.18	15.0 - 25.0	10.0
274	789MW-98	Monitoring Well	SS067 - LTM	1174058.90	1137931.05	4" PVC	Flush mount	20.0	476.59	476.32	-0.27	10.0 - 20.0	10.0
275	789MW-99	Monitoring Well	SS067 - LTM	1173966.05	1138022.60	4" PVC	Stick-up	24.5	474.85	475.80	0.95	14.5 - 24.5	10.0
276	789MW-100	Monitoring Well	SS067 - LTM	1173833.09	1137798.88	2" PVC	Stick-up	21.0	476.11	478.08	1.97	11.0 - 21.0	10.0
277	789MW-101	Monitoring Well	SS067 - LTM	1174188.99	1139180.95	2" PVC	Stick-up	15.0	448.58	450.86	2.28	5.0 - 15.0	10.0
278	789MW-102	Monitoring Well	SS067 - LTM	1173999.60	1139292.87	2" PVC	Stick-up	15.0	448.23	451.03	2.80	5.0 - 15.0	10.0
279	789MW-103	Monitoring Well	SS067 - LTM	1173816.99	1139411.93	2" PVC	Stick-up	15.0	447.50	449.99	2.49	5.0 - 15.0	10.0
280	789MW-134	Monitoring Well	SS067 - LTM	1174176.94	1138621.97	2" PVC	Flush mount	33.0	481.26	480.74	-0.52	23.0 - 33.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
281	789MW-135	Monitoring Well	SS067 - LTM	1174061.91	1138663.65	2" PVC	Flush mount	33.0	482.02	481.54	-0.48	23.0 - 33.0	10.0
282	789MW-214	Monitoring Well	SS067 - LTM	1174312.86	1138288.48	2" PVC	Stick-up	28.0	476.42	479.13	2.71	23.0 - 28.0	5.0
283	789MW-215	Monitoring Well	SS067 - LTM	1174240.92	1138369.74	2" PVC	Stick-up	30.0	473.95	481.16	7.21	25.0 - 30.0	5.0
284	789MW-216	Monitoring Well	SS067 - LTM	1174172.52	1138265.59	2" PVC	Stick-up	29.0	476.75	477.98	1.23	19.0 - 29.0	10.0
285	789MW-222	Monitoring Well	SS067 - LTM	1174008.16	1138434.93	2" PVC	Stick-up	28.0	479.52	481.39	1.87	18.0 - 28.0	10.0
286	789MW-223	Monitoring Well	SS067 - LTM	1173858.16	1138102.37	2" PVC	Stick-up	23.0	474.13	475.79	1.66	13.0 - 23.0	10.0
287	789MW-250	Monitoring Well	SS067 - LTM	1174155.20	1138076.20	2" PVC	Stick-up	33.0	475.00	478.46	3.46	5.8 - 30.8	25.0
288	789MW-251	Monitoring Well	SS067 - LTM	1174163.20	1138122.70	2" PVC	Stick-up	30.0	475.60	478.50	2.90	4.8 - 29.8	25.0
289	789MW-252	Monitoring Well	SS067 - LTM	1174098.80	1138144.90	2" PVC	Stick-up	33.0	475.10	478.04	2.94	4.8 - 29.8	25.0
290	789MW-253	Monitoring Well	SS067 - LTM	1173900.06	1138010.67	2" PVC	Stick-up	26.0	474.98	477.92	2.94	11.0 - 26.0	15.0
291	789MW-254	Monitoring Well	SS067 - LTM	1174117.64	1137877.00	2" PVC	Stick-up	26.0	476.68	479.82	3.14	11.0 - 26.0	15.0
292	789MW-255	Monitoring Well	SS067 - LTM	1174170.09	1137948.01	2" PVC	Stick-up	26.0	476.51	478.82	2.31	11.0 - 26.0	15.0
293	789MW-256	Monitoring Well	SS067 - LTM	1174253.20	1138007.83	2" PVC	Stick-up	26.0	477.13	479.90	2.77	6.0 - 26.0	20.0
294	789MW-257	Monitoring Well	SS067 - LTM	1173900.00	1139010.95	2" PVC	Stick-up	48.0	481.21	483.72	2.51	33.0 - 48.0	15.0
295	789RW-200	Recovery Well	SS067 - LTM	1174168.62	1138106.95	6" PVC	Vault	-	476.18	475.34	-0.84	- - -	-
296	789RW-201	Recovery Well	SS067 - LTM	1174106.11	1138357.27	6" PVC	Vault	-	478.82	477.97	-0.85	- - -	-
297	789RW-202	Recovery Well	SS067 - LTM	1174069.02	1138199.55	6" PVC	Vault	-	476.68	475.37	-1.31	- - -	-
298	789RW-203	Recovery Well	SS067 - LTM	1174206.70	1138180.24	6" PVC	Vault	-	476.88	476.05	-0.83	- - -	-
299	789RW-204	Recovery Well	SS067 - LTM	1174066.47	1138283.07	6" PVC	Vault	-	477.82	477.10	-0.72	- - -	-
300	789RW-205	Recovery Well	SS067 - LTM	1174127.69	1138149.89	6" PVC	Vault	-	475.97	475.06	-0.91	- - -	-

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
301	789RW-206	Recovery Well	SS067 - LTM	1174118.30	1138222.76	6" PVC	Vault	-	476.83	475.57	-1.26	- - -	-
302	789RW-207	Recovery Well	SS067 - LTM	1174118.01	1138292.73	6" PVC	Vault	-	477.99	477.30	-0.69	- - -	-
303	789RW-208	Recovery Well	SS067 - LTM	1174121.19	1138404.09	6" PVC	Vault	-	479.35	478.69	-0.66	- - -	-
304	789RW-209	Recovery Well	SS067 - LTM	1174251.53	1138093.26	6" PVC	Vault	-	476.68	475.93	-0.75	- - -	-
305	789RW-210	Recovery Well	SS067 - LTM	1174086.89	1138320.61	6" PVC	Vault	-	478.45	478.42	-0.03	- - -	-
306	789RW-211	Recovery Well	SS067 - LTM	1174147.96	1138128.05	6" PVC	Vault	-	475.92	476.00	0.08	- - -	-
307	789RW-212	Recovery Well	SS067 - LTM	1174016.63	1138218.43	6" PVC	Stick-up	28.5	476.34	478.28	1.94	13.5 - 28.5	15.0
308	789RW-213	Recovery Well	SS067 - LTM	1174103.69	1138014.20	6" PVC	Stick-up	32.0	475.39	477.19	1.80	17.0 - 32.0	15.0
309	789RW-217	Recovery Well	SS067 - LTM	1174211.77	1138107.42	4" PVC	Vault	30.0	-	-	-	15.0 - 30.0	15.0
310	789RW-218	Recovery Well	SS067 - LTM	1174167.83	1138138.14	4" PVC	Stick-up	30.0	-	-	-	15.0 - 30.0	15.0
311	789RW-219	Recovery Well	SS067 - LTM	1174077.05	1138160.11	4" PVC	Stick-up	30.0	-	-	-	15.0 - 30.0	15.0
312	789RW-220	Recovery Well	SS067 - LTM	1174086.92	1138239.42	4" PVC	Stick-up	20.0	-	-	-	10.0 - 20.0	10.0
313	789RW-221	Recovery Well	SS067 - LTM	1174045.73	1138255.60	4" PVC	Stick-up	25.0	-	-	-	10.0 - 25.0	15.0
314	MW01001	Monitoring Well	PFC - Site Investigation	1175072.67	1134318.06	1" PVC	Flush mount	16.5	456.07	455.85	-0.22	6.5 - 16.5	10.0
315	MW01003	Monitoring Well	PFC - Site Investigation	1174983.47	1134397.45	1" PVC	Flush mount	16.0	455.94	455.80	-0.14	6.0 - 16.0	10.0
316	MW02001	Monitoring Well	PFC - Site Investigation	1175926.29	1136638.39	1" PVC	Flush mount	20.0	472.26	471.81	-0.45	10.0 - 20.0	10.0
317	MW02002	Monitoring Well	PFC - Site Investigation	1176095.48	1136689.17	1" PVC	Flush mount	20.0	472.50	472.17	-0.33	10.0 - 20.0	10.0
318	MW02003	Monitoring Well	PFC - Site Investigation	1176202.52	1136575.81	1" PVC	Flush mount	20.0	470.58	470.33	-0.25	10.0 - 20.0	10.0
319	MW02004	Monitoring Well	PFC - Site Investigation	1176073.02	1136489.55	1" PVC	Flush mount	20.0	466.89	466.61	-0.28	10.0 - 20.0	10.0
320	MW03001	Monitoring Well	PFC - Site Investigation	1177005.99	1135764.11	1" PVC	Flush mount	20.0	471.05	470.58	-0.47	10.0 - 20.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
321	MW03002	Monitoring Well	PFC - Site Investigation	1176752.10	1135663.95	1" PVC	Flush mount	20.0	468.56	468.45	-0.11	10.0 - 20.0	10.0
322	MW03003	Monitoring Well	PFC - Site Investigation	1176959.03	1135434.55	1" PVC	Flush mount	21.0	469.94	469.62	-0.32	11.0 - 21.0	10.0
323	MW05001	Monitoring Well	PFC - Site Investigation	1176007.32	1135862.16	1" PVC	Flush mount	20.0	466.90	466.30	-0.60	10.0 - 20.0	10.0
324	MW05002	Monitoring Well	PFC - Site Investigation	1176043.91	1135844.12	1" PVC	Flush mount	20.0	467.05	466.52	-0.53	10.0 - 20.0	10.0
325	MW05003	Monitoring Well	PFC - Site Investigation	1176026.77	1135832.21	1" PVC	Flush mount	20.0	467.22	466.81	-0.41	10.0 - 20.0	10.0
326	MW06001	Monitoring Well	PFC - Site Investigation	1177547.09	1133557.81	1" PVC	Flush mount	20.0	470.12	469.67	-0.45	10.0 - 20.0	10.0
327	MW06002	Monitoring Well	PFC - Site Investigation	1177523.66	1133815.65	1" PVC	Flush mount	20.0	469.71	469.26	-0.45	10.0 - 20.0	10.0
328	MW07002	Monitoring Well	PFC - Site Investigation	1177382.89	1132151.87	1" PVC	Flush mount	22.0	472.24	472.10	-0.14	12.0 - 22.0	10.0
329	MW07003	Monitoring Well	PFC - Site Investigation	1177399.09	1132847.80	1" PVC	Flush mount	22.0	472.46	472.37	-0.09	12.0 - 22.0	10.0
330	MW07004	Monitoring Well	PFC - Site Investigation	1177317.06	1133055.72	1" PVC	Flush mount	21.2	471.62	471.36	-0.26	11.2 - 21.2	10.0
331	MW08001	Monitoring Well	PFC - Site Investigation	1177252.69	1134675.31	1" PVC	Flush mount	20.0	471.09	470.98	-0.11	10.0 - 20.0	10.0
332	MW08002	Monitoring Well	PFC - Site Investigation	1177097.65	1134841.76	1" PVC	Flush mount	22.0	471.41	471.04	-0.37	12.0 - 22.0	10.0
333	MW08003	Monitoring Well	PFC - Site Investigation	1176971.29	1134977.32	1" PVC	Flush mount	20.0	471.55	471.15	-0.40	10.0 - 20.0	10.0
334	MW09001	Monitoring Well	PFC - Site Investigation	1182233.23	1134426.53	1" PVC	Flush mount	23.0	525.45	525.25	-0.20	13.0 - 23.0	10.0
335	MW09004	Monitoring Well	PFC - Site Investigation	1182184.89	1134490.51	1" PVC	Flush mount	20.0	524.94	524.72	-0.22	10.0 - 20.0	10.0
336	MW10001	Monitoring Well	PFC - Site Investigation	1179435.11	1136687.19	1" PVC	Flush mount	20.0	527.06	526.78	-0.28	10.0 - 20.0	10.0
337	MW10003	Monitoring Well	PFC - Site Investigation	1179342.08	1136862.82	1" PVC	Flush mount	20.0	528.81	528.45	-0.36	10.0 - 20.0	10.0
338	MW11001	Monitoring Well	PFC - Site Investigation	1178745.23	1132360.90	1" PVC	Flush mount	25.0	478.81	478.30	-0.51	15.0 - 25.0	10.0
339	MW11002	Monitoring Well	PFC - Site Investigation	1178745.12	1132883.53	1" PVC	Flush mount	25.0	477.33	476.90	-0.43	15.0 - 25.0	10.0
340	MW11003	Monitoring Well	PFC - Site Investigation	1178773.92	1133625.95	1" PVC	Flush mount	25.0	475.76	475.38	-0.38	15.0 - 25.0	10.0

Table 2
Static Well Details
Former Griffiss Air Force Base

Count	Well ID	Well Type	IRP Site - Well Use	Northing	Easting	Casing Type	Surface Completion Type	As-Built Depth (ft bgs)	Ground Elevation (ft amsl)	TOC Elevation (ft amsl)	Offset from TOC (ft)	Screened Interval (ft bgs)	Screen Length
341	MW14001	Monitoring Well	PFC - Site Investigation	1175487.10	1138754.80	1" PVC	Stick-up	10.0	472.90	476.10	3.20	2.0 - 10.0	8.0
342	MW14002	Monitoring Well	PFC - Site Investigation	1175278.33	1138787.28	1" PVC	Stick-up	11.0	462.00	464.45	2.45	1.0 - 11.0	10.0
343	MW14003	Monitoring Well	PFC - Site Investigation	1175112.37	1138987.54	1" PVC	Stick-up	11.0	461.77	464.27	2.50	1.0 - 11.0	10.0
344	MW14004	Monitoring Well	PFC - Site Investigation	1174798.73	1138957.44	1" PVC	Flush mount	18.0	455.00	454.70	-0.30	8.0 - 18.0	10.0
345	MW14005	Monitoring Well	PFC - Site Investigation	1174591.33	1139070.07	1" PVC	Stick-up	12.0	447.16	449.83	2.67	2.0 - 12.0	10.0
346	AP1MW-1	Monitoring Well	CSS681 - LTM	1174225.00	1136299.00	2" PVC	Flush mount	20.0	476.73	476.46	-0.27	10.0 - 20.0	10.0
347	AP1MW-2	Monitoring Well	CSS681 - LTM	1174221.40	1136338.90	2" PVC	Flush mount	23.0	476.14	475.91	-0.23	13.0 - 23.0	10.0
348	AP1MW-3	Monitoring Well	CSS681 - LTM	1174226.00	1136253.40	2" PVC	Flush mount	21.0	478.12	477.88	-0.24	11.0 - 21.0	10.0
349	AP1MW-4	Monitoring Well	CSS681 - LTM	1174275.80	1136282.20	2" PVC	Flush mount	21.0	477.93	477.51	-0.42	11.0 - 21.0	10.0
350	AP1MW-5	Monitoring Well	CSS681 - LTM	1174194.20	1136295.50	2" PVC	Flush mount	20.0	476.57	476.27	-0.30	10.0 - 20.0	10.0

Notes:

amsl = above mean sea level
approx. = approximately
ft bgs = feet below ground surface
ID = Identification
IRP = Installation Restoration Program
LTM = Long Term Monitoring
PFC = Perfluorinated compound
PVC = Polyvinyl chloride
SS = Stainless steel
TOC = top of casing
USGS = United States Geological Survey

Table 3. Wells Removed from Well Inventory in 2025

This page intentionally left blank.

Table 3
Wells Removed from Well Inventory in 2025
Former Griffiss Air Force Base

Well ID	Reason For Removal
781MW-1	Decommissioned and no longer present
781MW-4	Decommissioned and no longer present
781MW-5	Decommissioned and no longer present
781MW-6	Decommissioned and no longer present
781MW-9	Decommissioned and no longer present
781MW-10	Decommissioned and no longer present
781MW-12	Decommissioned and no longer present
781MW-13	Decommissioned and no longer present
781MW-14	Decommissioned and no longer present
781MW-16	Decommissioned and no longer present
781MW-17	Decommissioned and no longer present
781MW-18	Decommissioned and no longer present
781MW-19	Decommissioned and no longer present
781PAIW-1	Decommissioned and no longer present
781PAIW-2	Decommissioned and no longer present
781PPRW-1	Decommissioned and no longer present
781PPRW-2	Decommissioned and no longer present
781PPRW-3	Decommissioned and no longer present
781PPRW-4	Decommissioned and no longer present
781PPRW-5	Decommissioned and no longer present
781PPRW-6	Decommissioned and no longer present
781PPRW-7	Decommissioned and no longer present
781PPRW-8	Decommissioned and no longer present
781PPRW-9	Decommissioned and no longer present
781VBS-1	Decommissioned and no longer present
781VBS-2	Decommissioned and no longer present
781VBS-3	Decommissioned and no longer present
781VBS-4	Decommissioned and no longer present
781VBS-5	Decommissioned and no longer present
781VBS-6	Decommissioned and no longer present
781VBS-7	Decommissioned and no longer present
781VBS-8	Decommissioned and no longer present
781VBS-9	Decommissioned and no longer present
781VBS-10	Decommissioned and no longer present
781VBS-11	Decommissioned and no longer present
781VBS-12	Decommissioned and no longer present

Notes:


ID = Identification


This page intentionally left blank.

FIGURES

This page intentionally left blank.



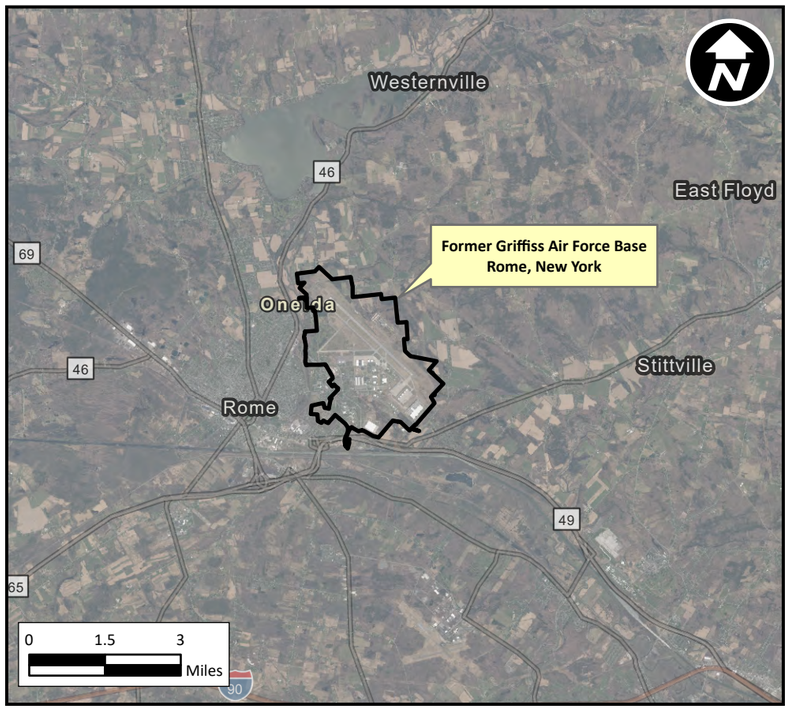

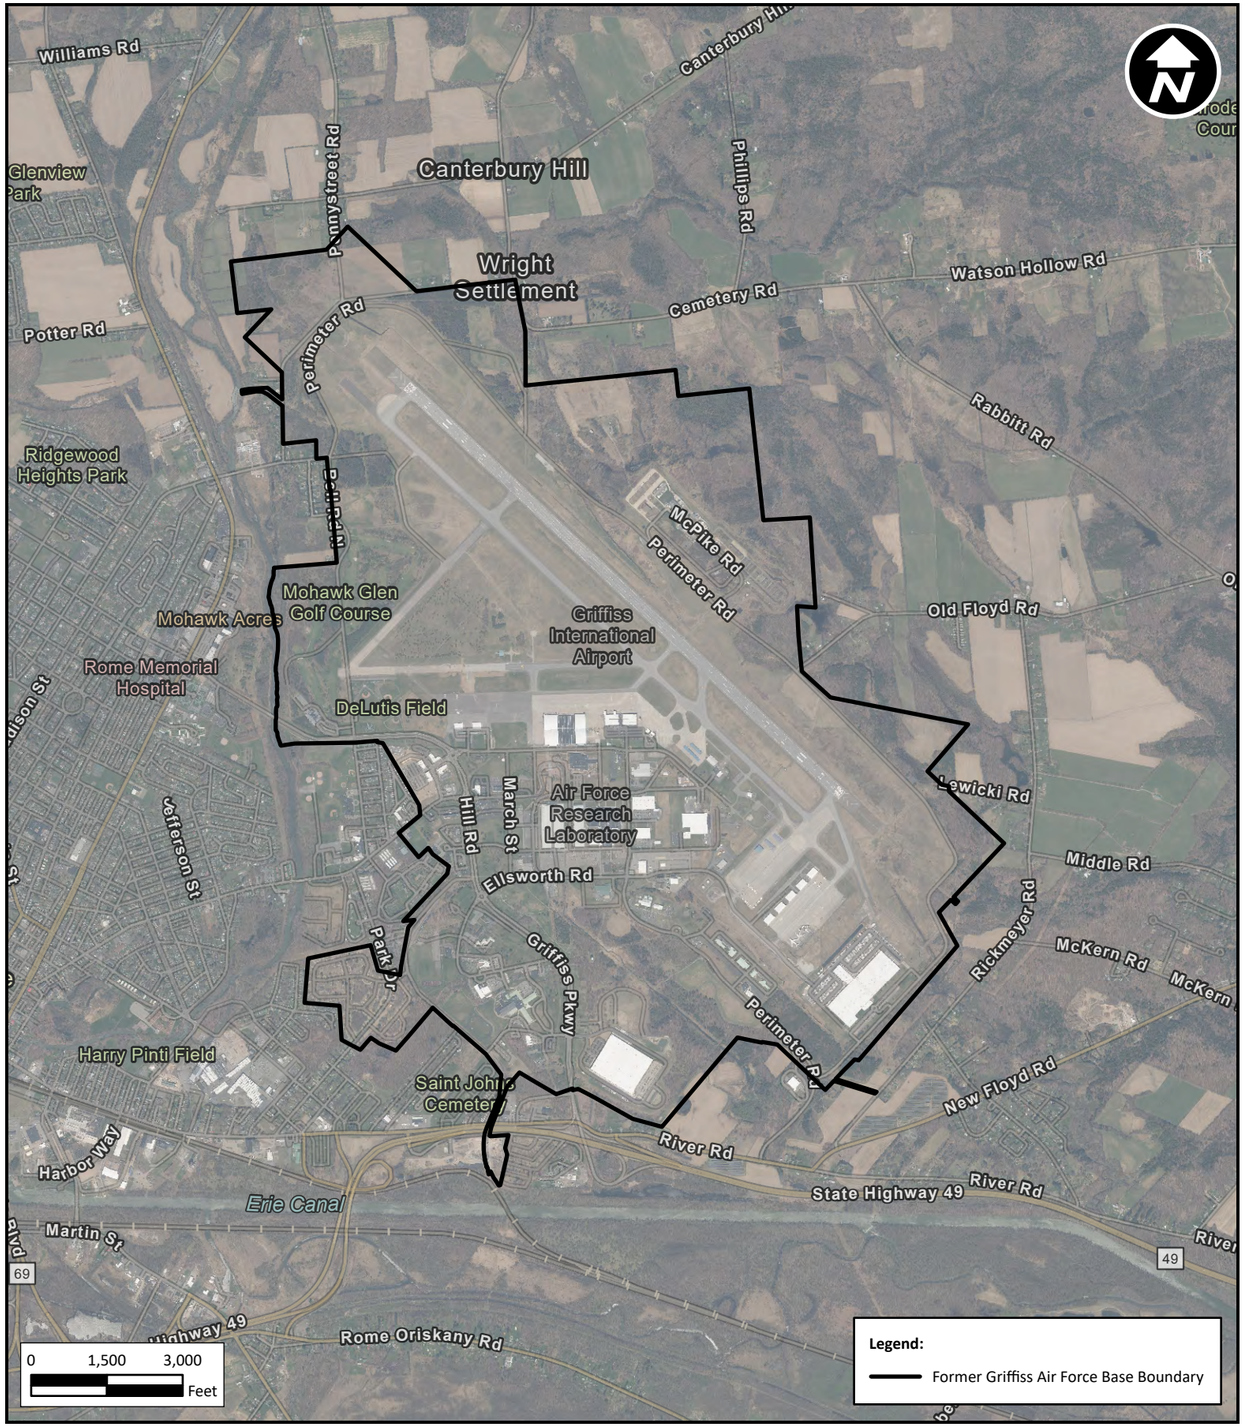

Service Layer Credits: Hybrid Reference Layer: Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS, (c) OpenStreetMap contributors, and the GIS User Community
NYS_Orthoimagery_Latest: NYS ITS Geospatial Services
World Imagery: Earthstar Geographics

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Former Griffiss Air Force Base Location Map

Figure 1

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

PROJECT NO:	SCALE:	DATE:	DRAWN BY:
MSC2021.0012	As Shown	1/30/2026	MRM

bhate
www.bhate.com

This page intentionally left blank.

Figure 2

Site Locations

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

0 1,000 2,000 Feet

LF001
SS062
SD052-05
LF003
LF002
ST006
DP022
SS008
SS025
SS060
SS017
AOI66
CSS681 - Apron 1 Area LCP-E9
CSS682 - Building 785 Pipeline
SD052-01
SS044
SD052-02
SS067
LF007
SD052-SVI Buildings 785 & 786
SD052-04
SS054
LF009
SD052-SVI Buildings 774 & 776

Wright Settlement
Griffiss International Airport
Mohawk Glen Golf Course
DeLutis Field
Air Force Research Laboratory
Ridgewood Heights Park
Rome Dog Park
Mohawk Acres
Rome Memorial Hospital
Freedom Plaza
Harry Pinti Field
Saint Johns Cemetery
Rome
Erie Canal

Wilson Rd
Bishop Rd
Potter Rd
Turin Rd
Rome Westernville Rd
Perimeter Rd
Cemetery Rd
Watson Hollow Rd
Rabbitt Rd
Old Floyd Rd
McPike Rd
Hangar Rd
Lewicki Rd
Ellsworth Rd
Middle Rd
McKern Rd
Rickmeyer Rd
Floyd Ave
Roosevelt Ave
E Bloomfield St
Railroad St
E Dominick St
State Highway 49
River Rd
New Floyd Rd
Taft Ave
Maybery Rd
Merrick Rd
W Cedar St
W Oak St
N Madison St
N James St
N George St
Union St
Elm St
Thomas St
Court St
Black River Blvd N
Jefferson St
Broadway
Bell Rd S
Hill Rd
March St
Harbor Way
Martin St

Notes:
This information is depicted to provide visual aid within the context of this document and should not be used as a sole reference in precise dimensioning of features indicated. Please verify the location of all features including underground and aboveground utilities prior to conducting any subsurface exploration or site assessment.

Legend:
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

This page intentionally left blank.

0 125 250
Feet

Legend:

- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

LF1MW-12
LF1MW-11
LF1MW-14
LF001
MWSAR03
LF1MW-6
LF1MW-103
LF1P-2
LF1MW-10
LF1P-5
LF1MW-5
Six Mile Creek
LF1MW-UNK-02
LF1P-3
LF1MW-UNK-03
LF1MW-UNK-01
LF1MW-13
PERIMETER
Intermittent Stream
Pond
Six Mile Creek
ANGMW-1
SS062

5950
5525
5985
6028
0854
6025
0738

Figure 3

Well Locations Associated with Site LF001

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 5/11/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 5/11/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

This page intentionally left blank.

0 75 150
Feet

Legend:

- Monitoring Well Location
- Surface Water
- Installation Restoration Program Area

MW09001
MW09004
AOC9MW-18
AOC9TW-95
AOC9MW-11BR
AOC9MW-19
AOC9MW-22
AOC9MW-21
AOC9MW-20
AOC9MW-23
AOC9MW-14
AOC9MW-24
AOC9MW-08
AOC9MW-12
AOC9MW-13
G009-MW01
WSAMW-4
AOC9MW-15
SS062
AOC9MW-16
AOC9MW-17
G009-MW02
AOC9MW-07
G009-MW03
G009-MW04
AOC9MW-05
AOC9MW-9BR
AOC9MW-06
WSAMW-3

0906
0907
0930
0912
0913
0917
0915
0832
0829
CONNEX
6364
0916
0846
0838

PERIMETER
Intermittent Stream
Six Mile Creek
Pond
McPike

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Figure 4

Well Locations Associated with Site SS062

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM
DATE: 1/30/2026
SCALE: As Shown
PROJECT NO: MSC2021.0012

bhate
www.bhate.com

This page intentionally left blank.

0 60 120
Feet

Legend:

- Monitoring Well Location
- Drainage Path
- Installation Restoration Program Area

WSAMW-2
0825
0826
6328
0810
WSAMW-14BR
WSAMW-8
817IW-2
817MW-1
817IW-3
817IW-1
0817
817IW-6
817IW-4
817IW-7
0818
817MW-3
817IW-5
817IW-8
WSAMW-11
WSAMW-18
0816
WSA-IW02
WSA-IW04
WSA-IW01
WSA-IW03
WSAMW-16
WSA-MW15
LAWMW-9
WSAMW-19
SD052-05
WSAVMW-17
WSAMW-23
0830
WSAMW-21
0819
WSAMW-13BR
PERIMETER
WSAMW-9
WSAMW-12BR
MW10001
MW10003

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Figure 5

Well Locations Associated with Site SD052-05

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

0 150 300 Feet

MW10003

Pond

LF7MW-27

LF7MW-29

5960

0802

LF003

LF7MW-22

LF7MW-100

5945

LF7MW-26

LF7MW-28

LF7MW-30

LF7MW-23

6235

5986

6242

5985

5525

PERIMETER

LF2MW-14

LF2MW2-1

LF002

LF2MW2-2

LF2MW-UNK-01

LF2MW-13

LF2MW-4

5982

5326

Six Mile Creek

6204

33

LF2MW-12

LF2MW-100

N0797

0041

5887

Legend:

- Monitoring Well Location
- LF2MW2-2 is included on this figure for reference purposes; although the well was previously removed from the well inventory, the date of removal is unknown.
- Surface Water
- Drainage Path
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 5/11/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Well Locations Associated with Sites LF002 and LF003

Figure 6

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 5/11/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

0 175 350
Feet

MW11001
MW11002
MW11003
6020
LF7MW-27
5960
LF003
LF7MW-22
LF7MW-28
Six Mile Creek
6203
6389B
0100
0504
ST006
0101
MW06001
MW06002
0135
5893
MW07002
MW07003
0108
6385
6390
6376
N0731
0131
MW08001
MW08002
MW08003
Hangar
PAINE
SELFRIDGE
MW03001
MW03003
MW03002
0045
5982
5326
0133
0123
0143
MW07004
6336
0128
0104
0106
BURHANNA
0105
6346
6052
6338
Moody
0109
SS008
CHAPPIE JAMES
Electronic
0118
0119
0037
BROOKS
Turner
5892
SS025
0041
5887
GOODRIC
0043
0040
MW02003
MW02002
MW05002
0042
0047
0044
MW02004
MW05003
MW05001
6335
0132
Olive Grove
MW02001
0004
5657
OTIS
0003
6349
MGS

Legend:
- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Well Locations Associated with Sites SS008, SS025, and ST006

Figure 7

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM
DATE: 1/30/2026
SCALE: As Shown
PROJECT NO: MSC2021.0012

bhate
www.bhate.com

This page intentionally left blank.

0 120 240 Feet

Legend:

- Monitoring Well Location recommended for replacement in 2025
- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

782MW-3R
782MW-3
782VMW-86
782MW-12
782MW-11
782VMW-89
782MW-1R
782VMW-90
782MW-1
782MW-5
782VMW-95
782MW-6R2
6389C
782VMW-85
782MW-9
782VMW-88
782VMW-94
782MW-10
782MW-6D
782MW-184
782VMW-84
782VMW-84D
782VMW-87
782VMW-78
0783
782VMW-93
782VMW-96
782VMW-82
782VMW-76
782VMW-81
0784
782VMW-92
SD052-01
8004
CSS681 - Apron 1 Area LCP-E9
BOMBER
AP1MW-4
AP1MW-1
AP1MW-3
AP1MW-2
AP1MW-5
782VMW-83
782VMW-105B
0785
782VMW-104
782VMW-98
782VMW-97
0786
SD052-SVI Buildings 785 & 786
CSS682 - Building 785 Pipeline
782VMW-99
775VMW-11
775VMW-24
SD052-02
SS067
N0763
782VMW-100
782VMW-121
782VMW-121D
AP2MW-3
782VMW-101
MW14001
MW14002
MW14003
MW14004
MW14005
782VMW-102
Six Mile Creek
5989
5340
0782
PATROL

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Z:\Projects\WSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Well Locations Associated with Sites SD052-01, SD052-SVI Buildings 785 and 786, CSS681 – Apron 1 Area LCP-E9, and CSS682 – Building 785 Pipeline

Figure 8

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012


bhate

www.bhate.com

This page intentionally left blank.

Figure 9a

Well Locations Associated with Site SS067

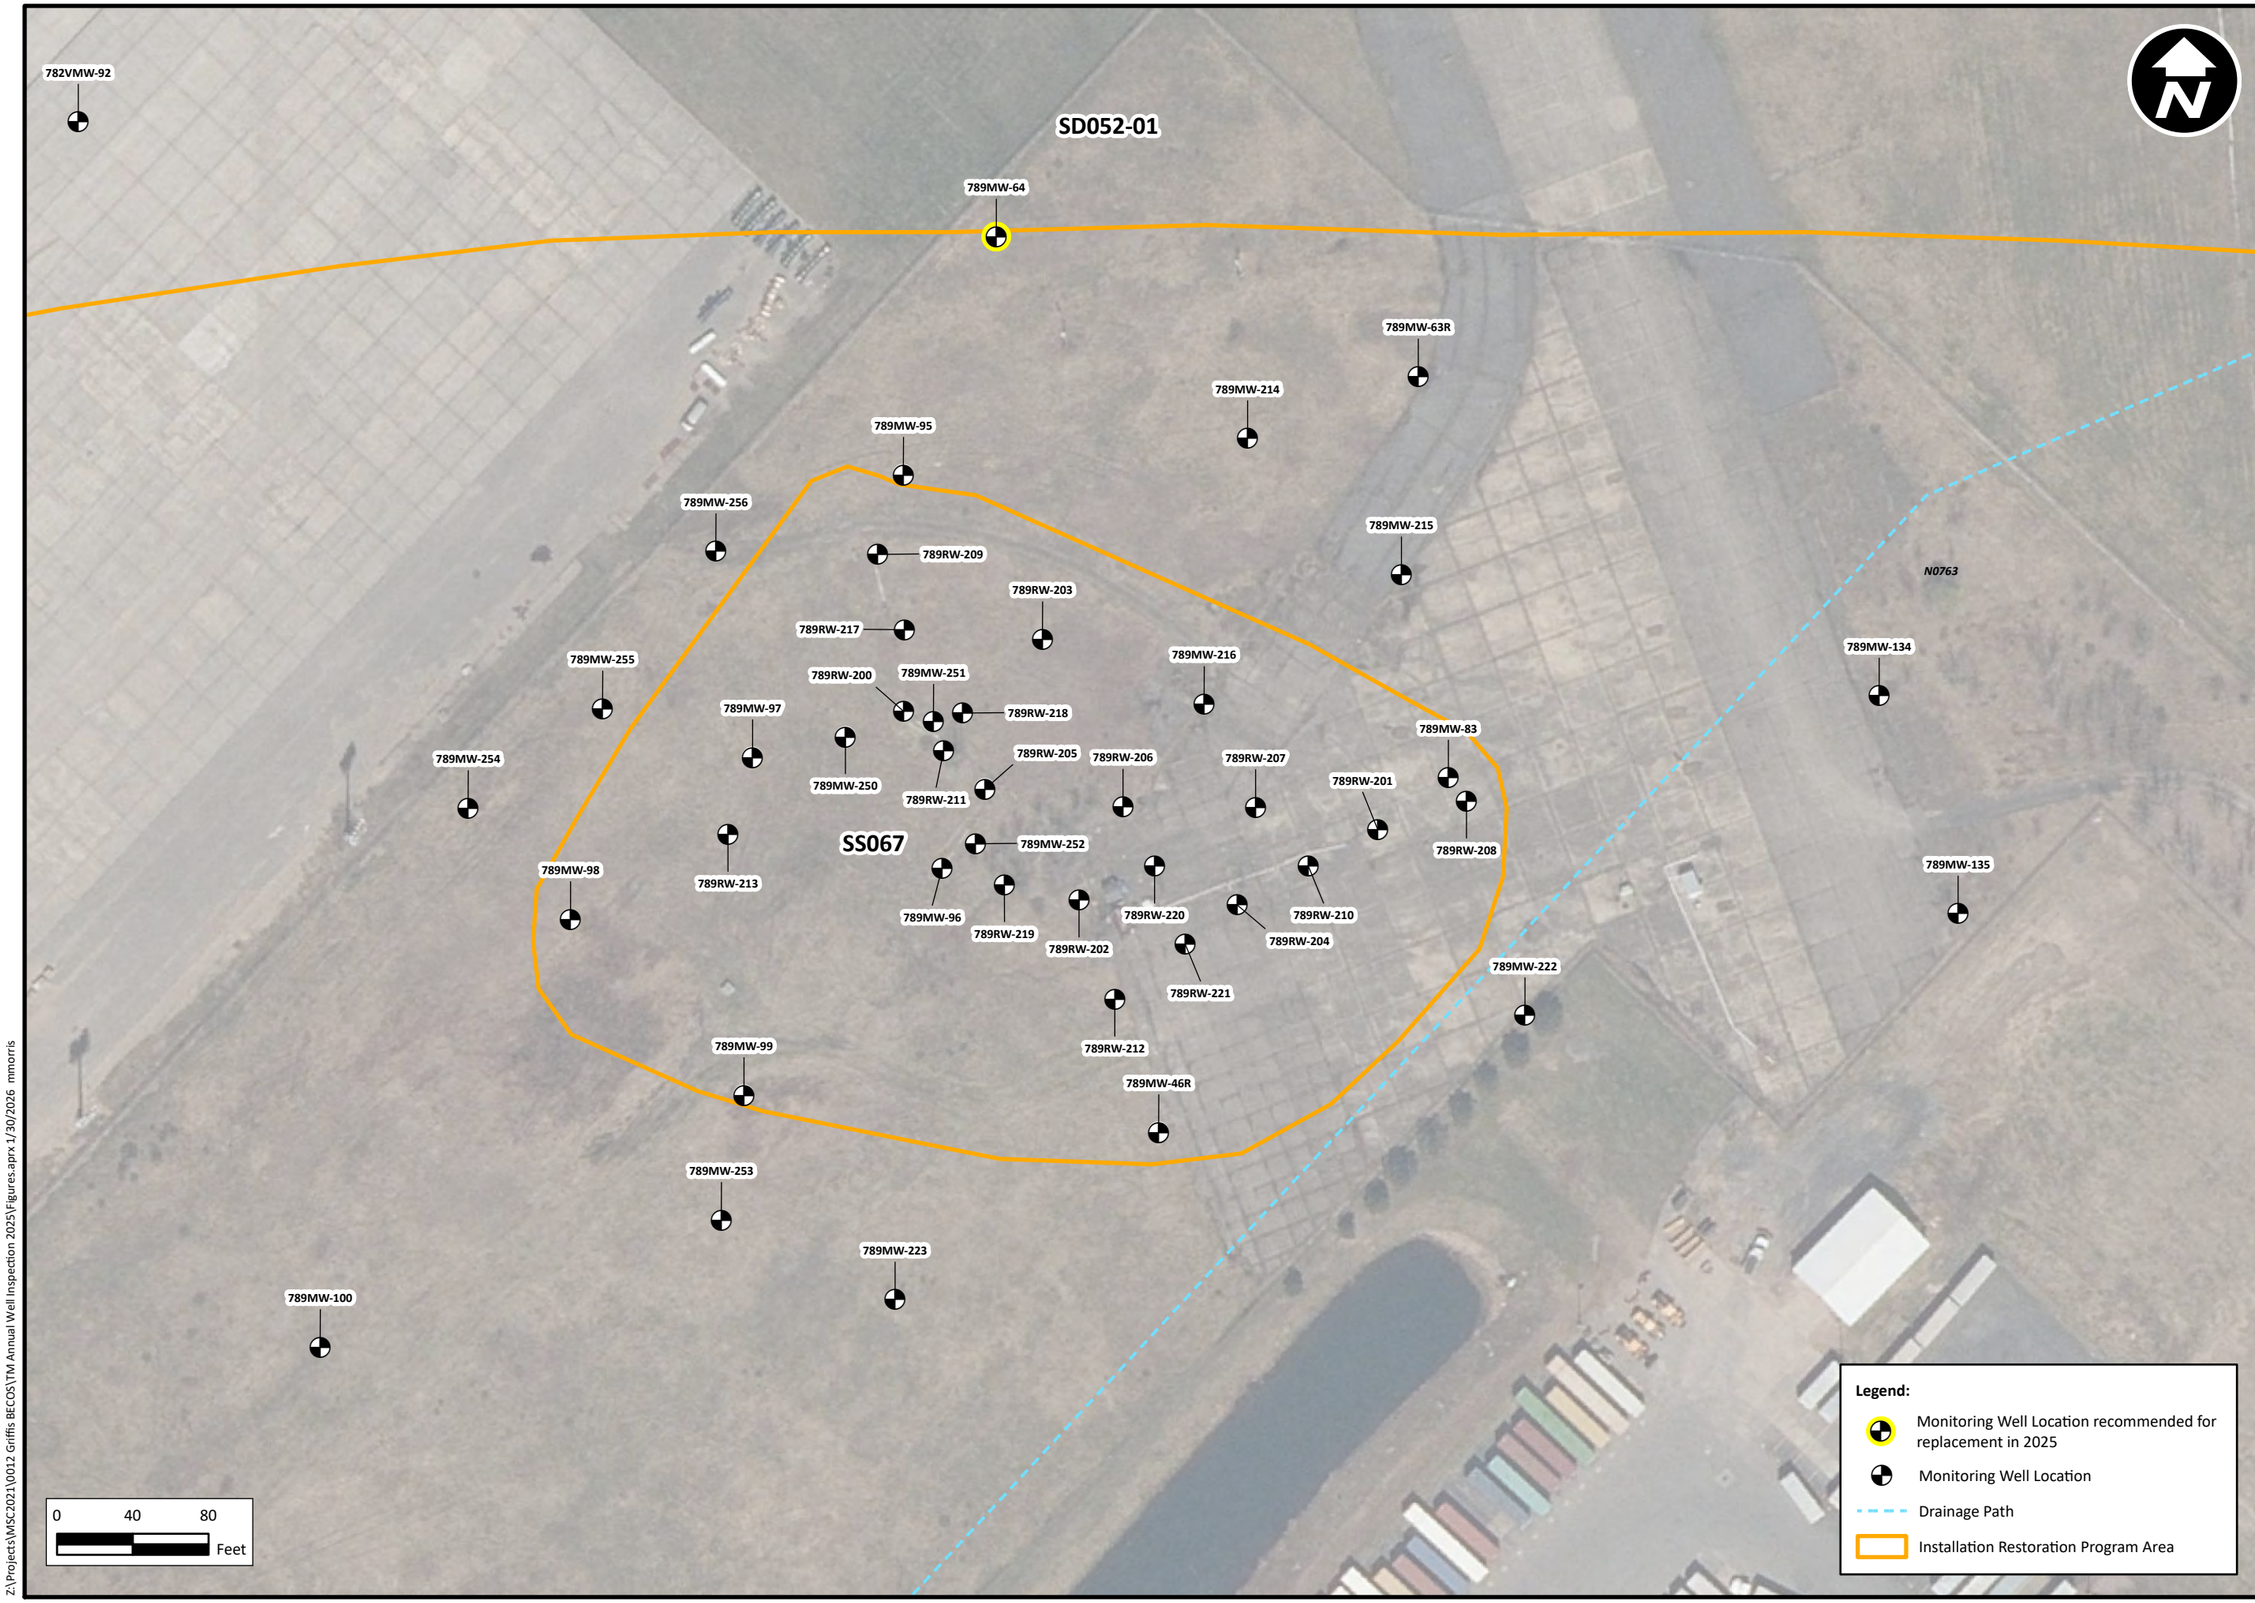

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY:	MRM
DATE:	1/30/2026
SCALE:	As Shown
PROJECT NO:	MSC2021.0012

bhate

www.bhate.com

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

This page intentionally left blank.

0 40 80 Feet

SD052-01

N0763

789MW-63R

789MW-215

789MW-134

789MW-83

789RW-201

789RW-208

SS067

789MW-135

789MW-222

782VMW-102

789MW-101

Six Mile Creek

SS067

789MW-102

789MW-257

789MW-103

Legend:

- Monitoring Well Location recommended for replacement in 2025
- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Well Locations Associated with Site SS067

Figure 9b

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

0 100 200 Feet

Legend:

- Monitoring Well Location
- Surface Water
- Drainage Path
- Installation Restoration Program Area

MARKET
DONALDSON
Parking
Olive Grove
Otis
OTIS
Ellsworth
PERIMETER
RECREATION
PHOENIX
READY
CE ACCESS
SHELL
Three Mile Creek

SS017
SS060
AOI66
LF007
MW01001
MW01003
LF5MW-1A
LF5MW-3
LF5MW-4
LF5MW-5
LF5MW-100R
MW49D07
775VMW-15R1
SD052-02

0003 0011 0015 0019 0020 1300 0030 0035 0029 0036 0016 0024 8001 8000 8002 0702 0701 0700 0772 5470 0770 0750

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Figure 10

Well Locations Associated with Sites AOI66, LF007, SS060, and SS017

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY:	SCALE:	DATE:	PROJECT NO:
MRM	As Shown	1/30/2026	MSC2021.0012

bhate
www.bhate.com

This page intentionally left blank.

0 75 150
Feet

Legend:

- Monitoring Well Location Decommissioned in 2025
- Monitoring Well Location
- Installation Restoration Program Area

SD052-SVI Buildings 785 & 786

SD052-SVI Buildings 774 & 776

SD052-02

SD052-04

LF009

775VMW-23
782VMW-99
775VMW-11
775VMW-25
775VMW-15R1
775MW-2
775VMW-24
775VMW-14
775VMW-4
SD052-02_IW-01
SD052-02_IW-02
775VMW-5
775VMW-18R
SD052-02_IW-07
SD052-02_IW-08
SD052-02_IW-03
775MW-6
SD052-02_IW-04
SD052-02_IW-05
775EW-1
SD052-02_IW-06
SD052-02_IW-12
SD052-02_IW-09
775EW-3
775MW-27
775EW-1R
775VMW-9
SD052-02_IW-13
SD052-02_IW-14
775VMW-16
775VMW-8
775VMW-19R
775MW-28
775VMW-10
775-MW20
775-MW20R
775VMW-20R
775-MW20RBR

781MW-1
781VBS-11
781PAIW-2
781VBS-12
781MW-9
781PPRW-9
781MW-10
781VBS-10
781VBS-9
781VBS-8
781PAIW-1
781PPRW-8
781MW-4
781PPRW-7
SS054
781PPRW-6
781MW-5
781PPRW-5
781MW-6
781MW-14
781VBS-1
781PPRW-3
781VBS-2
781MW-12
781VBS-4

PERIMETER
READY
PATROL
PHOENIX
DAEDALIAN

0750 0770 0769 0774 0776 0786 0777 5660 0778 0796 0780 0788

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Well Locations Associated with Sites SD052-02 and SD052-SVI Buildings 774 and 776

Figure 11

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

Figure 12

Well Locations Associated with Site SD052-04

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

www.bhate.com

0 50 100 Feet

775VMW-10
775VMW-19R
PERIMETER
SD052-02
LF6MW-1
775-MW20
775-MW20R
LF009
LF6VMW-25
TMCMW-9
LF6VMW-24
LF6MW-28
LF6MW-29
LF6MW-27
LF6TW-34
SD052-04-IW04
SD052-04
LF6VMW-23
LF6TW-35
LF6MW-31
LF6MW-30
LF6TW-37
LF6TW-36
LF6VMW-22
LF6TW-38
LF6VMW-26
LF6MW-32
LF6VMW-10R2
Three Mile Creek
2646
LF6VMW-13R
LF6MW-39
LF6VMW-17S
LF6VMW-17D
LF6MW-13RD
LF6MW-14BR
LF6VMW-14
LF6VMW-15R

LF6TW-33
SD052-04-IW03
LF6IW-05
LF6IW-02
LF6IW-01
LF6IW-04
LF6IW-06
LF6MW-12
LF6IW-03
LF6MW-16
SD052-04-IW01
LF6MW-17
LF6MW-20
SD052-04
SD052-04-IW02
LF6MW-18
LF6MW-19
0 7.5 15 Feet

Legend:

- Monitoring Well Location
- Surface Water
- Installation Restoration Program Area

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

This page intentionally left blank.

0 60 120 Feet

LF6MW-32
LF6VMW-10R2
LF6VMW-22
SD052-04
LF6VMW-15R
LF6VMW-17S
LF6VMW-17D
LF009
LF6VMW-21
781MW-20
781MW-21
PERIMETER
781PPRW-2
781MW-13R
781MW-13
781VBS-7
781MW-17
SS054
781VBS-6
781VBS-5
781MW-19
781MW-18
LF6VMW-18
LF6VMW-19
LF6VMW-20
Three Mile Creek
TMC-USGS-2
TMC-USGS-1
Three Mile Creek

Legend:

- Monitoring Well Location Decommissioned in 2025
- Monitoring Well Location
- Surface Water
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Figure 13

Well Locations Associated with Site LF009

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

0 40 80 Feet

781MW-2
781MW-1
781VBS-11
781MW-3
781PAIW-2
781MW-11
781VBS-10
781MW-9
781MW-10
781VBS-12
781PPRW-9
781MW-8
781VBS-8
781VBS-9
781PPRW-8
781PAIW-1
781MW-15
781MW-7
781PPRW-7
781MW-4
SS054
781MW-5
781PPRW-5
781PPRW-6
781MW-14
781MW-12
781MW-6
781PPRW-3
781VBS-1
781MW-13R
781MW-13
781VBS-2
781VBS-4
781MW-16
781PPRW-4
781PPRW-2
781PPRW-1
781VBS-3
781VBS-7
781MW-17
781VBS-6
781VBS-5
781MW-19
LF6VMW-21
781MW-18
781MW-20
LF009

0778
0780
0796
0788
PHOENIX
PERIMETER
PATROL

Legend:

- Monitoring Well Location Decommissioned in 2025
- Monitoring Well Location
- Installation Restoration Program Area

Z:\Projects\WSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Well Locations Associated with Site SS054

Figure 14a

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.

0 60 120
Feet

781MW-20

781MW-21

LF009

LF6VMW-20

PERIMETER

PATROL

LAWMW-19

Legend:

- Monitoring Well Location
- Installation Restoration Program Area
- Former Griffiss Air Force Base Boundary

Z:\Projects\MSC2021\0012 Griffis BECOS\TM Annual Well Inspection 2025\Figures.aprx 1/30/2026 mmorris

Service Layer Credits: NYS_Orthoimagery_Latest: NYS ITS Geospatial Services

Well Locations Associated with Site SS054

Figure 14b

2025 Annual Well-Inspection Survey and Well Maintenance
Former Griffiss Air Force Base Rome, New York

DRAWN BY: MRM

DATE: 1/30/2026

SCALE: As Shown

PROJECT NO: MSC2021.0012

bhate

www.bhate.com

This page intentionally left blank.
