Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

United Refining
Location #A0075

7188 Route 96
Victor, NY 14564
+1 585-924-2919

Leak Detector

Equipment #	Grade	Pump Type	Result
006	Regular	Mechanical (MLLD)	Pass
007	Premium	Mechanical (MLLD)	Pass

Precision Line Tightness Test

Equipment #	Grade	Result
006	Regular	Pass
007	Premium	Pass

Shear Valve

Form Name	Result
Shear Valve	Pass



Tyzay McClinton



Thomas Grinder

MECHANICAL AND ELECTRONIC LINE LEAK DETECTORS
PERFORMANCE TESTS

Facility Name: Kwik Fill			Owner: United Refining			
Address: 7188 Route 96			Address:			
City, State, Zip Code: Victor NY 14564			City, State, Zip Code:			
Facility I.D. #: 8-027081			Phone #: 5859242919			
Testing Company: Owl Services USA			Phone #: 800-646-3161		Date: 6/16/2026	
This data sheet can be used to test mechanical line leak detectors (MLLD) and electronic line leak detectors (ELLD) with submersible turbine pump (STP) systems. See PEI/RP1200 Sections 9.1 and 9.2 for test procedures.						
Line Number	006	007				
Product Stored	Regular	Premium				
Leak Detector Manufacturer	FE Petro	FE Petro				
Leak Detector Model	STP-MLD	STP-MLD				
Type of Leak Detector	☑ MLLD ☐ ELLD	☑ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD	☐ MLLD ☐ ELLD
MLLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)						
STP Full Operating Pressure	28	25				
Check Valve Holding Pressure	28	25				
Line Resiliency (ml) (line bleed back volume as measured from check valve holding pressure to 0 psig)	283.91	302.83				
Step Through Time in Seconds (time the MLLD hesitates at metering pressure before going to full operating pressure as measured from 0 psig with no leak induced on the line)	20	8				
Metering Pressure (STP pressure when simulated leak rate 3 gph at 10 psig)	10	10				
Opening Time in Seconds (the time the MLLD opens to allow full pressure after simulated leak is stopped)	20	8				
Does the STP pressure remain at or below the metering pressure for at least 60 seconds when the simulated leak is induced?	☑ Yes ☐ No	☑ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Does the leak detector reset (trip) when the line pressure is bled off to zero psig?	☑ Yes ☐ No	☑ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
Does the STP properly cycle on/off under normal fuel system operation conditions?	☑ Yes ☐ No	☑ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
A "No" answer to either of the above questions indicates the MLLD fails the test.						
ELLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)						
STP Full Operating Pressure						
How many test cycles are observed before alarm/shutdown occurs?						
Does the simulated leak cause an alarm?	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No
A "No" answer to the above question indicates the ELLD fails the test.						
Does the simulated leak cause an STP shutdown?	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA	☐ Yes ☐ No ☐ NA
Test Results	☒ Pass ☐ Fail	☒ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail	☐ Pass ☐ Fail

Comments: Testing was conducted in accordance with PEI/RP1200

Tester Signature: Thomas Grinder

Tester Name: Thomas Grinder

Kwik Fill
7188 Route 96
Victor
NY 14564

Purpora Engineering
Petro-Tite Line Tightness Test Form

Work Visit # 186275
UST Registration #
8-027081

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE PSI BEFORE	PRESSURE PSI AFTER	VOLUME READING BEFORE	VOLUME READING AFTER	VOLUME NET CHANGE	REMARKS SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS
006	12:48	Connected line tester to: Shear						
Regular	12:50	Started line test		60		.015		
	13:00	Line Test Continued	60	60	.015	.015	0	
	13:10	Line Test Continued	60	60	.015	.015	0	
	13:20	Line Test Continued	60	60	.015	.015	0	
	13:20	Bleed Back	60	0	.015	.1	0.085	

Material APT Polytech (light

Wall Type Double

Line Length (feet) 100

Diameter (inches) 2

Pressure/Suction Pressure

Allowable Bleedback

(PL x Ba) + (FC x Bb(.006)) + B(.05) = N

(100 * 0.0012)
+ (2 * 0.006) + 0.05 = 0.182

Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows:

Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested
006 Regular	Yes	0	6/16/2026

CONTRACTOR CERTIFICATION

Technician:
Thomas Grinder

f5b88a3d

Certification # _____

Notes:

Kwik Fill
7188 Route 96
Victor
NY 14564

Purpora Engineering
Petro-Tite Line Tightness Test Form

Work Visit # 186275
UST Registration #
8-027081

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE PSI BEFORE	PRESSURE PSI AFTER	VOLUME READING BEFORE	VOLUME READING AFTER	VOLUME NET CHANGE	REMARKS SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS
007	12:53	Connected line tester to: Shear						
Premium	12:55	Started line test		60		.010		
	13:05	Line Test Continued	60	60	.010	.010	0	
	13:15	Line Test Continued	60	60	.010	.010	0	
	13:25	Line Test Continued	60	60	.010	.010	0	
	13:25	Bleed Back	60	0	.010	.1	0.09	

Material APT Polytech (light

Wall Type Double

Line Length (feet) 75

Diameter (inches) 2

Pressure/Suction Pressure

Allowable Bleedback

(PL x Ba) + (FC x Bb(.006)) + B(.05) = N

(75 * 0.0012)
+ (2 * 0.006) + 0.05 = 0.152

Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows:

Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested
007 Premium	Yes	0	6/16/2026

CONTRACTOR CERTIFICATION

Technician:
Thomas Grinder

f5b88a3d
Certification # _____

Notes:

SHEAR VALVE OPERATION INSPECTION

Facility Name: Kwik Fill	Owner United Refining
Address: 7188 Route 96	Address
City, State, Zip Code: Victor NY 14564	City, State, Zip Code:
Facility I.D. #: 8-027081	Phone #: 5859242919
Testing Company: Owl Services USA	Phone #: 610-278-7203

This data sheet is for inspecting shear valves located inside dispensers. See PEI/RP1200 Section 10 for the inspection procedure.

Product Grade	Regular	Premium	Regular	Premium					
Dispenser ID#	1-2	1-2	1-2	3-4					
Shear ValveType (Product/Vapor)	Product	Product	Product	Product					
1. Is the shear valve rigidly anchored to the dispenser box frame or dispenser island?	☑Yes ☐No	☑Yes ☐No	☑Yes ☐No	☑Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No
2. Is the shear section positioned between ½ inch above or below the top surface of the dispenser island?	☑Yes ☐No	☑Yes ☐No	☑Yes ☐No	☑Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No	☐Yes ☐No
3. Is the lever arm free to move?	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA
4. Does the lever arm snap shut the poppet valve?	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☑Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA
5. Can any product be dispensed when the product shear valve is closed?	☐Yes ☑No ☐NA	☐Yes ☑No ☐NA	☐Yes ☑No ☐NA	☐Yes ☑No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA	☐Yes ☐No ☐NA
A "No" to Lines 1-4 or a "Yes" for Line 5 indicates a test failure.									
Test Results	☑Pass ☐Fail	☑Pass ☐Fail	☑Pass ☐Fail	☑Pass ☐Fail	☐Pass ☐Fail	☐Pass ☐Fail	☐Pass ☐Fail	☐Pass ☐Fail	☐Pass ☐Fail

Comments:

Tester's Name (print) Thomas Grinder Tester's Signature _____ 6/16/2026

Testing was conducted in accordance with PEI/RP1200

Images



20260616_124714.jpg



20260616_124706.jpg



20260616_124701.jpg



20260616_124647.jpg



20260616_124638.jpg


Crompco LLC
1815 Gallagher Rd
Plymouth Meeting, PA 19462

United Refining
Location #A0075

7188 Route 96
Victor, NY 14564
+1 585-924-2919

Diagram - KWIK FILL (v1)



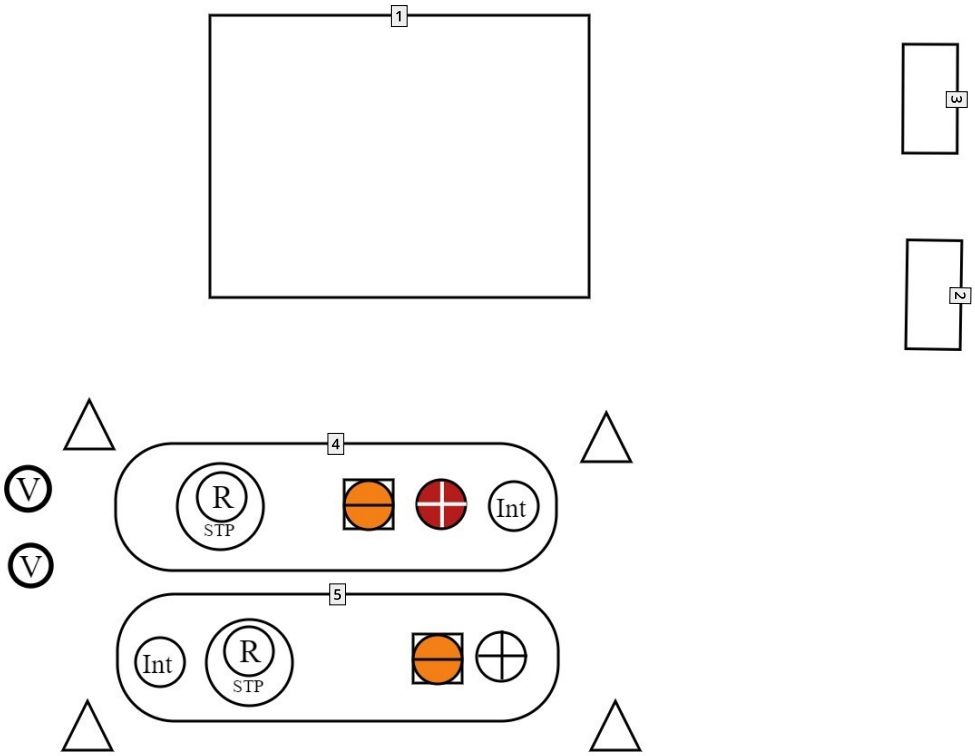

1: Store / Kiosk - Kwik fill
2: Dispenser - 3-4
3: Dispenser - 1-2
4: Fiberglass Tank - Premium
5: Fiberglass Tank - Regular

Visit Verification

CUSTOMER
United Refining

LOCATION
#A0075
7188 Route 96
Victor, NY 14564

CONTACT
United Refining Company of PA

SCHEDULED
06/16/2026 12:00am (EDT)

ASSIGNED TO
Tyzay McClinton, Thomas Grinder

SERVICE REASON
Compliance

PRODUCTS & SERVICES

Item	Qty
Combos	
All Lines, LDs, Shear Valves	2.00
Expenses	
MINIMUM SITE CHARGE	1.00

CONFIRMATION
By signing this verification you are agreeing that we have performed and/or provided services and parts listed above.

Approver's Name
Andy Sickles

Email

Signature Status
Nobody available to sign
