DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/25/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 63-79°F, Sunny, RH: 80%, Pres: 30.00 in Hg, Wind: W @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
NRP (Construction Manager) **Platinum Scaffolding** - Hand tools	Roux D.P.C. - Christopher Farrington NRP - Ed Pierce Platinum Scaffolding - ~10 workers

SCOPE OF WORK:

Roux D.P.C. (Roux) was onsite to complete environmental monitoring during remedial activities in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated August 6, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all outdoor intrusive activities.

Description of work activities performed and general observations/comments:

- Platinum Scaffolding set up construction fencing across the adjoining parking lot/staging area and southeastern perimeter of the Site.

CAMP data evaluation: CAMP was implemented from 08:00-15:00 which consisted of one upwind and one downwind station, each containing a photoionization detector (PID) and particulate meter. No exceedances of downwind particulates greater than 150 µg/m3 were recorded. No exceedances of volatile organic compounds (VOCs) were recorded.

Offsite Disposal: None

Import: None.

Sampling Performed: None

Upcoming work activities anticipated:

- Continuation of construction fencing installation around perimeter of Site.

Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/25/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 63-79°F, Sunny, RH: 80%, Pres: 30.00 in Hg, Wind: W @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00



Legend

CAMP Station

SITE BOUNDARY


Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/25/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 63-79°F, Sunny, RH: 80%, Pres: 30.00 in Hg, Wind: W @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

Soil Disposal Grids and Facilities

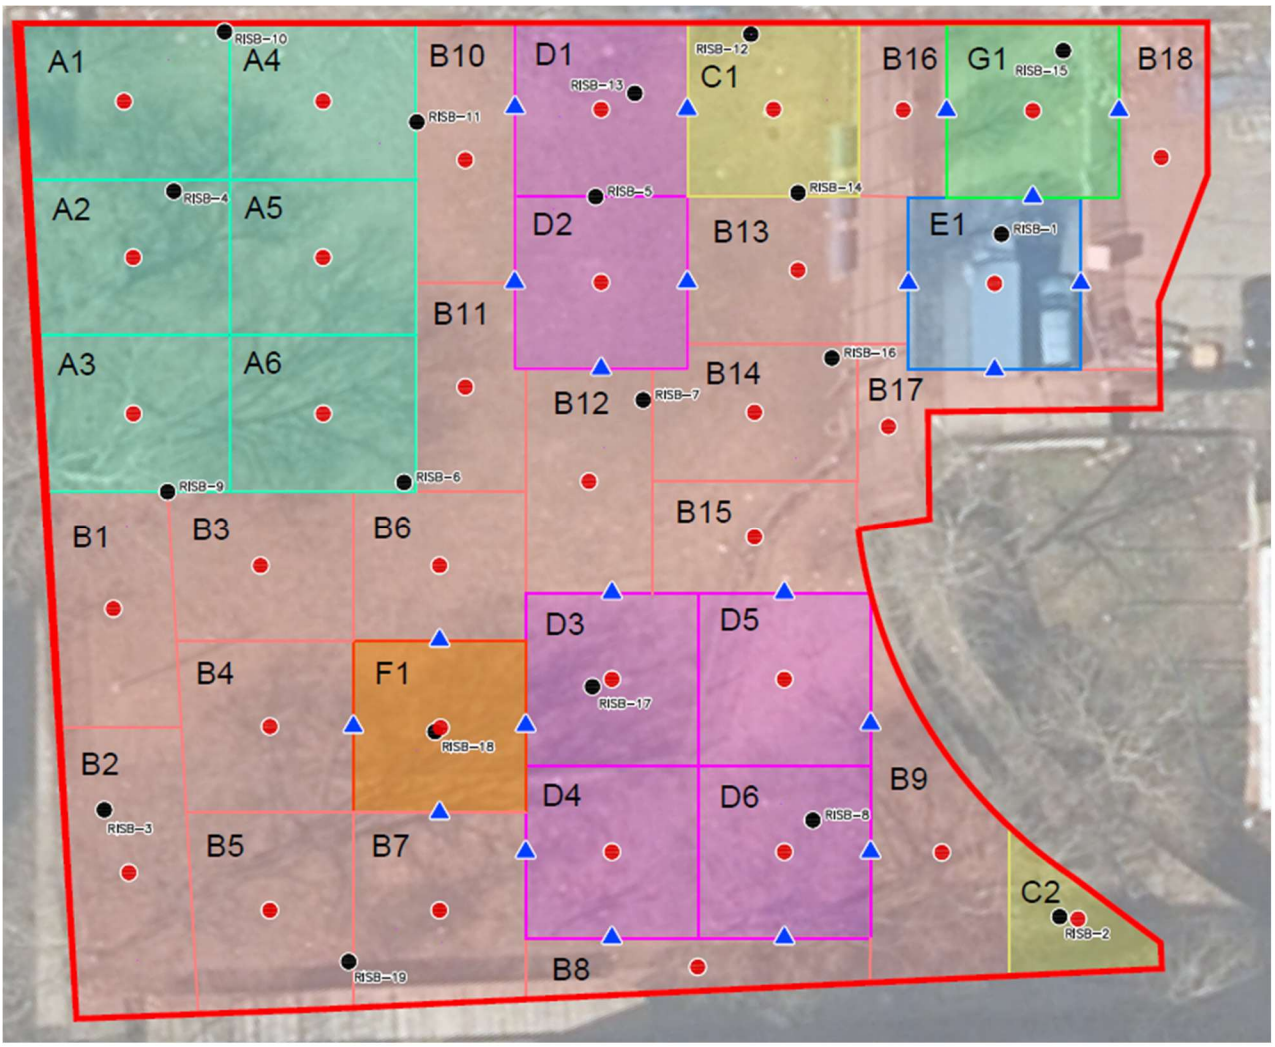

LEGEND

- RISB-1 ● LOCATION OF RI/SRI SOIL BORING
- ▲ PROPOSED SIDEWALL ENDPOINT SAMPLE
- ● PROPOSED BOTTOM ENDPOINT SAMPLE
- BCP SITE BOUNDARY
- PARCEL BOUNDARY
- EXCAVATION TO 2 FEET BELOW GRADE
- EXCAVATION TO 3 FEET BELOW GRADE
- EXCAVATION TO 4 FEET BELOW GRADE
- EXCAVATION TO 6 FEET BELOW GRADE
- EXCAVATION TO 7 FEET BELOW GRADE
- EXCAVATION TO 8 FEET BELOW GRADE
- EXCAVATION TO 11 FEET BELOW GRADE

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/25/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 63-79°F, Sunny, RH: 80%, Pres: 30.00 in Hg, Wind: W @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

PHOTOGRAPHS TAKEN TODAY: Sol On Park



Photo 1: Facing East, Platinum Scaffolding getting scaffolding delivered.



Photo 2: Facing South, Platinum constructing scaffolding across adjoining parking lot.

Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/25/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 63-79°F, Sunny, RH: 80%, Pres: 30.00 in Hg, Wind: W @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

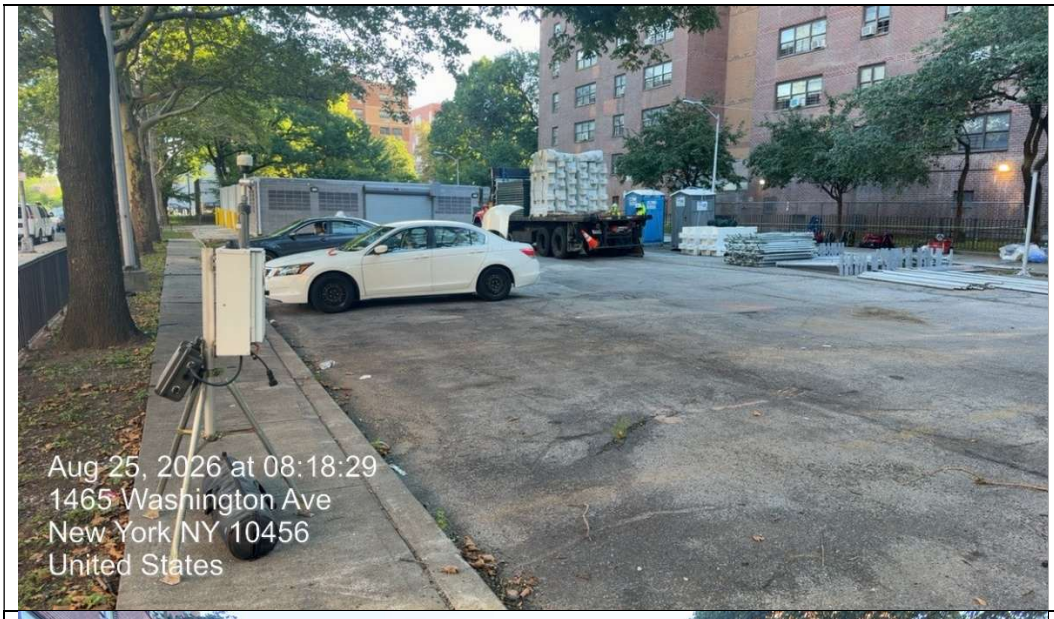


Photo 3: Facing North, Upwind CAMP station location.

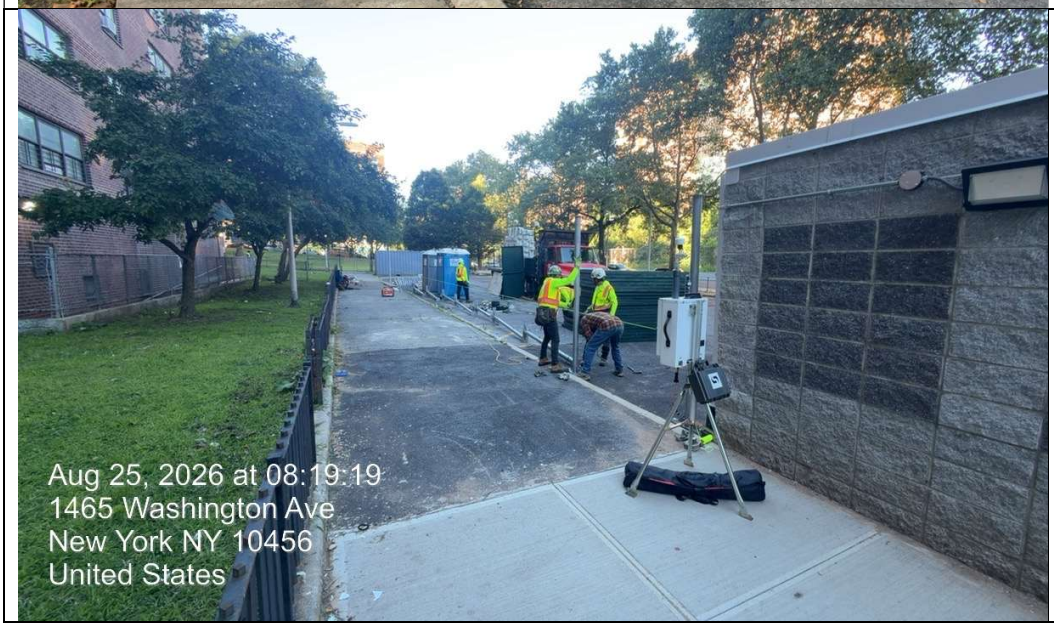


Photo 4: Facing West, Platinum constructing scaffolding across adjoining parking lot, plus downwind CAMP station.

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - Meter Locations

Project:	NRP Sol on Park
Project Number:	2908.0011Y
Project Manager:	Dana Hignell
Location:	3728 Park Avenue, Bronx, New York
Date:	8/25/2026
Times:	8:00 AM-15:00 PM



MEAN WIND DIRECTION
W @ 0-10 MPH
08:00-15:00 PM

Notes: CAMP - Community Air Monitoring Program
UW - Upwind CAMP Station
DW - Downwind CAMP Station

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - Dust

Project: NRP Sol on Park
Project Number: 2908.0011Y
Project Manager: Dana Hignell
Location Bronx, NY
Date: 8/25/2026

Upwind Station #1 Serial Number DS 27032023-2259		Downwind Station #1 Serial Number DS 20052024-2653		15-min Average (Corrected for Background)	Comments
Time	15-min Avg. (ug/m^3)	Time	15-min Avg. (ug/m^3)		
8:15:00 AM	7.66	8:15:00 AM	8.19	0.53	
8:30:00 AM	5.14	8:30:00 AM	7.03	1.89	
8:45:00 AM	3.75	8:45:00 AM	5.10	1.35	
9:00:00 AM	3.63	9:00:00 AM	3.79	0.16	
9:15:00 AM	5.53	9:15:00 AM	6.41	0.88	
9:30:00 AM	2.82	9:30:00 AM	4.42	1.60	
9:45:00 AM	2.39	9:45:00 AM	3.78	1.39	
10:00:00 AM	2.38	10:00:00 AM	3.79	1.41	
10:15:00 AM	2.46	10:15:00 AM	3.79	1.33	
10:30:00 AM	2.52	10:30:00 AM	3.41	0.89	
10:45:00 AM	2.24	10:45:00 AM	3.05	0.81	
11:00:00 AM	2.30	11:00:00 AM	2.93	0.63	
11:15:00 AM	2.03	11:15:00 AM	2.61	0.58	
11:30:00 AM	1.94	11:30:00 AM	2.21	0.27	
11:45:00 AM	1.70	11:45:00 AM	2.03	0.33	
12:00:00 PM	1.73	12:00:00 PM	1.88	0.15	
12:15:00 PM	2.33	12:15:00 PM	1.66	-0.67	
12:30:00 PM	2.77	12:30:00 PM	1.48	-1.29	
12:45:00 PM	1.85	12:45:00 PM	1.40	-0.45	
1:00:00 PM	1.78	1:00:00 PM	1.56	-0.22	
1:15:00 PM	1.94	1:15:00 PM	1.55	-0.39	
1:30:00 PM	2.65	1:30:00 PM	1.55	-1.10	
1:45:00 PM	2.69	1:45:00 PM	1.52	-1.17	
2:00:00 PM	1.83	2:00:00 PM	1.44	-0.39	
2:15:00 PM	1.90	2:15:00 PM	1.79	-0.11	
2:30:00 PM	2.02	2:30:00 PM	1.93	-0.09	
2:45:00 PM	2.07	2:45:00 PM	1.43	-0.64	
3:00:00 PM	1.81	3:00:00 PM	3.78	1.97	

NR - Not recorded
µg/m3 - micrograms per meters cubed

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - VOC

Project: NRP Sol on Park
Project Number: 2908.0011Y
Project Manager: Dana Hignell
Location Bronx, NY
Date: 8/25/2026

Upwind Station #1 Serial Number DS 27032023-2259		Downwind Station #1 Serial Number DS 20052024-2653		15-min Average (Corrected for Background)	Comments
Time	15-min Avg. (ppm)	Time	15-min Avg. (ppm)		
8:15:00 AM	0.00	8:15:00 AM	0.00	0.00	
8:30:00 AM	0.06	8:30:00 AM	0.02	-0.04	
8:45:00 AM	0.07	8:45:00 AM	0.02	-0.05	
9:00:00 AM	0.04	9:00:00 AM	0.00	-0.04	
9:15:00 AM	0.04	9:15:00 AM	0.00	-0.04	
9:30:00 AM	0.01	9:30:00 AM	0.00	-0.01	
9:45:00 AM	0.01	9:45:00 AM	0.00	-0.01	
10:00:00 AM	0.01	10:00:00 AM	0.00	-0.01	
10:15:00 AM	0.01	10:15:00 AM	0.00	-0.01	
10:30:00 AM	0.01	10:30:00 AM	0.00	-0.01	
10:45:00 AM	0.01	10:45:00 AM	0.00	-0.01	
11:00:00 AM	0.01	11:00:00 AM	0.00	-0.01	
11:15:00 AM	0.01	11:15:00 AM	0.00	-0.01	
11:30:00 AM	0.01	11:30:00 AM	0.00	-0.01	
11:45:00 AM	0.01	11:45:00 AM	0.01	0.00	
12:00:00 PM	0.01	12:00:00 PM	0.00	-0.01	
12:15:00 PM	0.01	12:15:00 PM	0.00	-0.01	
12:30:00 PM	0.01	12:30:00 PM	0.00	-0.01	
12:45:00 PM	0.01	12:45:00 PM	0.00	-0.01	
1:00:00 PM	0.01	1:00:00 PM	0.00	-0.01	
1:15:00 PM	0.01	1:15:00 PM	0.00	-0.01	
1:30:00 PM	0.01	1:30:00 PM	0.00	-0.01	
1:45:00 PM	0.01	1:45:00 PM	0.00	-0.01	
2:00:00 PM	0.01	2:00:00 PM	0.00	-0.01	
2:15:00 PM	0.01	2:15:00 PM	0.00	-0.01	
2:30:00 PM	0.01	2:30:00 PM	0.00	-0.01	
2:45:00 PM	0.01	2:45:00 PM	0.00	-0.01	
3:00:00 PM	0.01	3:00:00 PM	0.00	-0.01	

ppm - Parts Per Million
NR - Not recorded

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/26/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 64-82°F, Sunny, RH: 87%, Pres: 30.06 in Hg, Wind: N @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
NRP (Construction Manager) **Platinum Scaffolding** - Hand tools	Roux D.P.C. - Christopher Farrington NRP - Ed Pierce Platinum Scaffolding - ~10 workers

SCOPE OF WORK:

Roux D.P.C. (Roux) was onsite to complete environmental monitoring during remedial activities in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated August 6, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all outdoor intrusive activities.

Description of work activities performed and general observations/comments:

- Platinum Scaffolding continued setting up construction fencing across the adjoining parking lot/staging area and along the southeastern perimeter of the Site.
- Adjacent to the Site, an exit slab was poured for NYCHA Morris Building 17, because the original exit path will be obstructed due to construction fencing.

CAMP data evaluation: CAMP was implemented from 07:00-15:00 which consisted of one upwind and one downwind station, each containing a photoionization detector (PID) and particulate meter. No exceedances of downwind particulates greater than 150 µg/m3 were recorded. No exceedances of volatile organic compounds (VOCs) were recorded.

Offsite Disposal: None

Import: None.

Sampling Performed: None

Upcoming work activities anticipated:

- Continuation of building up construction fencing around perimeter of Site.

Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/26/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 64-82°F, Sunny, RH: 87%, Pres: 30.06 in Hg, Wind: N @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00



Legend

CAMP Station

SITE BOUNDARY


Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/26/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 64-82°F, Sunny, RH: 87%, Pres: 30.06 in Hg, Wind: N @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

Soil Disposal Grids and Facilities

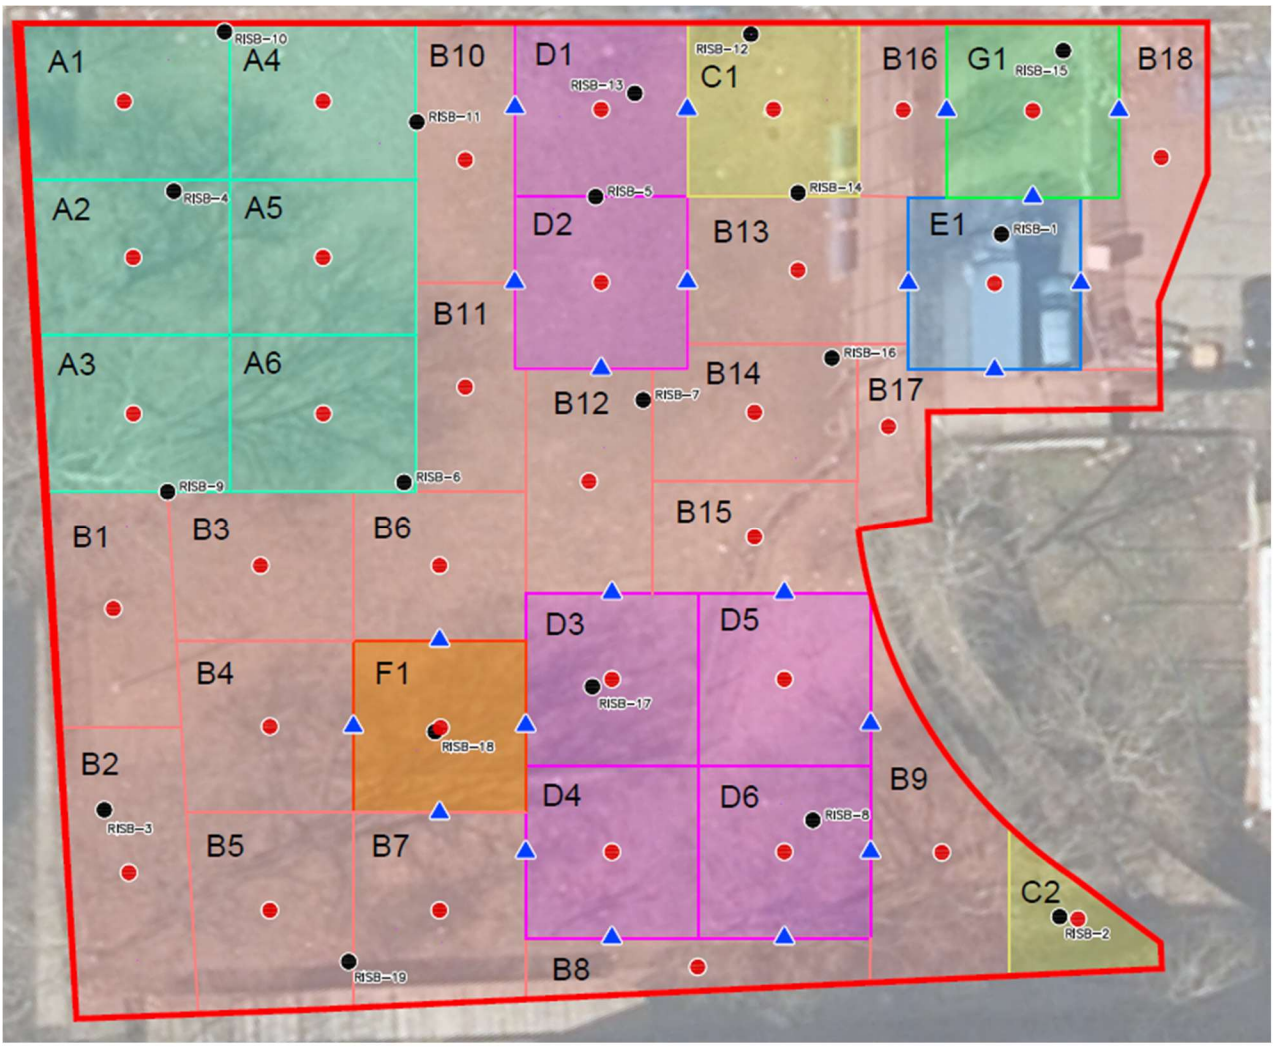

LEGEND

- RISB-1 ● LOCATION OF RI/SRI SOIL BORING
- ▲ PROPOSED SIDEWALL ENDPOINT SAMPLE
- ● PROPOSED BOTTOM ENDPOINT SAMPLE
- BCP SITE BOUNDARY
- PARCEL BOUNDARY
- EXCAVATION TO 2 FEET BELOW GRADE
- EXCAVATION TO 3 FEET BELOW GRADE
- EXCAVATION TO 4 FEET BELOW GRADE
- EXCAVATION TO 6 FEET BELOW GRADE
- EXCAVATION TO 7 FEET BELOW GRADE
- EXCAVATION TO 8 FEET BELOW GRADE
- EXCAVATION TO 11 FEET BELOW GRADE

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/26/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 64-82°F, Sunny, RH: 87%, Pres: 30.06 in Hg, Wind: N @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

PHOTOGRAPHS TAKEN TODAY: Soil On Park



Photo 1: Facing South, construction perimeter continuing to be constructed.



Photo 2: Facing East, Platinum continuing to construct fencing along stairs around Site perimeter.

Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/26/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 64-82°F, Sunny, RH: 87%, Pres: 30.06 in Hg, Wind: N @ 0-10 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-15:00

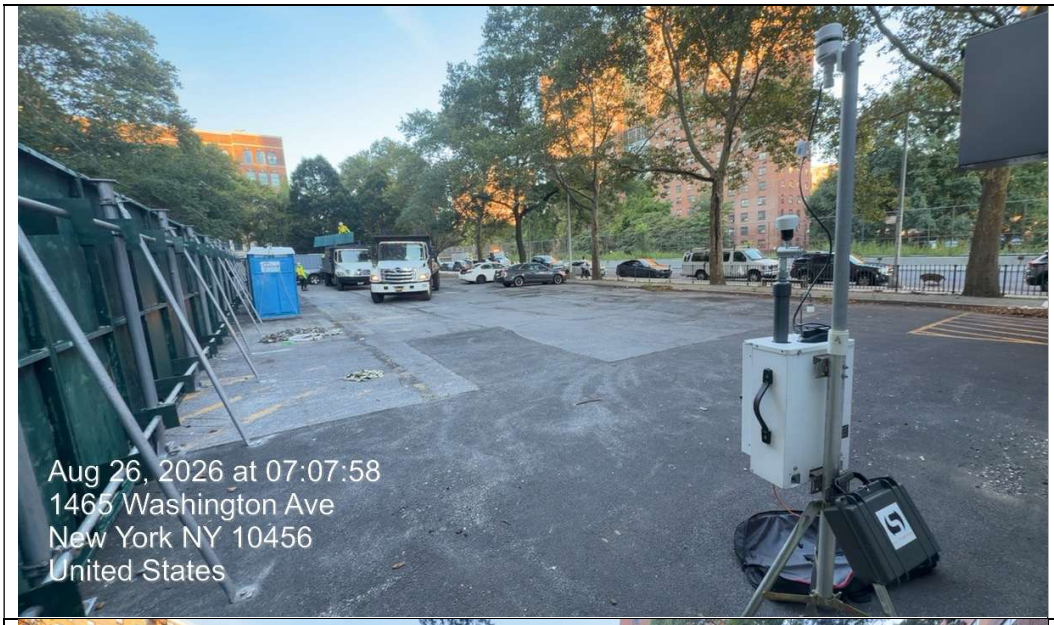


Photo 3: Facing West, Upwind CAMP station location.

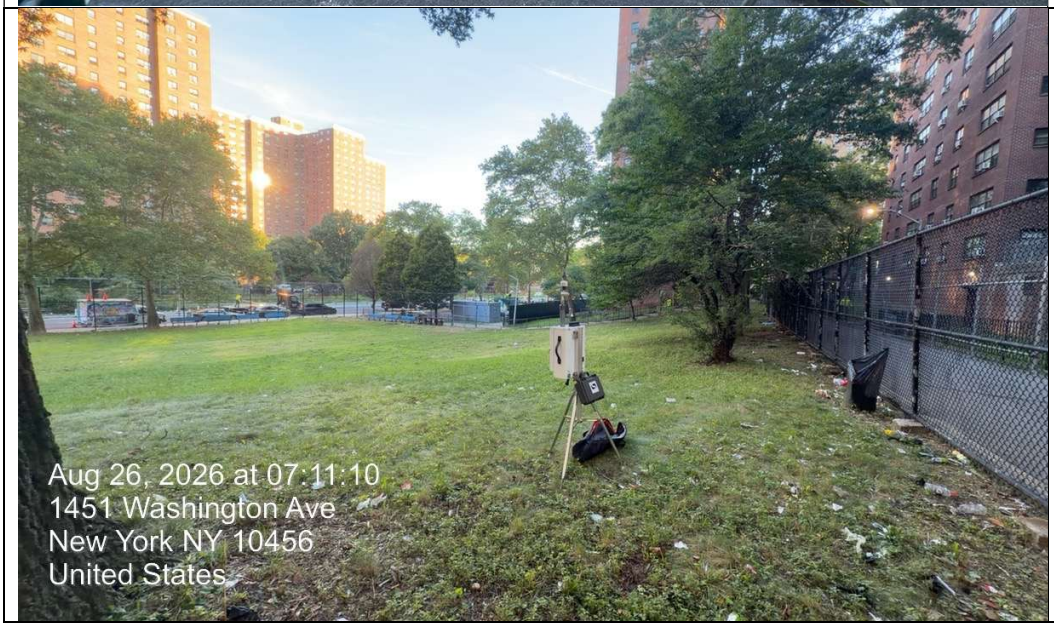


Photo 4: Facing North, downwind CAMP station.

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - Meter Locations

Project:	NRP Sol on Park
Project Number:	2908.0011Y
Project Manager:	Dana Hignell
Location:	3728 Park Avenue, Bronx, New York
Date:	8/26/2026
Times:	7:00 AM-15:00 PM



MEAN WIND DIRECTION
N @ 0-10 MPH
07:00-15:20 PM

Notes: CAMP - Community Air Monitoring Program
UW - Upwind CAMP Station
DW - Downwind CAMP Station

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - DUST

Project: NRP Sol on Park
Project Number: 2908.0011Y
Project Manager: Dana Hignell
Location Bronx, NY
Date: 8/26/2026

Upwind Station #1 Serial Number DS 20052024-2653		Downwind Station #1 Serial Number DS 27032023-2259		15-min Average (Corrected for Background)	Comments
Time	15-min Avg. (ug/m^3)	Time	15-min Avg. (ug/m^3)		
7:00:00 AM	2.09	7:00:00 AM	2.70	0.61	
7:15:00 AM	1.76	7:15:00 AM	2.44	0.68	
7:30:00 AM	1.67	7:30:00 AM	2.06	0.39	
7:45:00 AM	1.71	7:45:00 AM	1.94	0.23	
8:00:00 AM	1.81	8:00:00 AM	2.03	0.22	
8:15:00 AM	1.73	8:15:00 AM	2.08	0.35	
8:30:00 AM	1.85	8:30:00 AM	2.21	0.36	
8:45:00 AM	1.93	8:45:00 AM	2.36	0.43	
9:00:00 AM	1.91	9:00:00 AM	2.21	0.30	
9:15:00 AM	2.19	9:15:00 AM	2.26	0.07	
9:30:00 AM	1.90	9:30:00 AM	2.50	0.60	
9:45:00 AM	2.06	9:45:00 AM	2.48	0.42	
10:00:00 AM	2.51	10:00:00 AM	2.94	0.43	
10:15:00 AM	2.53	10:15:00 AM	2.97	0.44	
10:30:00 AM	3.08	10:30:00 AM	3.65	0.57	
10:45:00 AM	2.22	10:45:00 AM	2.78	0.56	
11:00:00 AM	2.26	11:00:00 AM	2.69	0.43	
11:15:00 AM	2.29	11:15:00 AM	2.57	0.28	
11:30:00 AM	2.19	11:30:00 AM	2.42	0.23	
11:45:00 AM	2.04	11:45:00 AM	2.34	0.30	
12:00:00 PM	2.08	12:00:00 PM	2.32	0.24	
12:15:00 PM	2.03	12:15:00 PM	2.21	0.18	
12:30:00 PM	2.13	12:30:00 PM	2.38	0.25	
12:45:00 PM	2.03	12:45:00 PM	2.31	0.28	
1:00:00 PM	2.04	1:00:00 PM	2.24	0.20	
1:15:00 PM	2.00	1:15:00 PM	2.34	0.34	
1:30:00 PM	2.58	1:30:00 PM	2.49	-0.09	
1:45:00 PM	2.42	1:45:00 PM	2.48	0.06	
2:00:00 PM	2.60	2:00:00 PM	2.60	0.00	
2:15:00 PM	2.88	2:15:00 PM	2.85	-0.03	
2:30:00 PM	2.73	2:30:00 PM	2.85	0.12	
2:45:00 PM	2.62	2:45:00 PM	2.73	0.11	
3:00:00 PM	2.75	3:00:00 PM	2.77	0.02	

NR - Not recorded
µg/m3 - micrograms per meters cubed

Roux Environmental Engineering and Geology, D.P.C.
Community Air Monitoring Program - VOC

Project: NRP Sol on Park
Project Number: 2908.0011Y
Project Manager: Dana Hignell
Location Bronx, NY
Date: 8/26/2026

Upwind Station #1 Serial Number DS 20052024-2653		Downwind Station #1 Serial Number DS 27032023-2259		15-min Average (Corrected for Background)	Comments
Time	15-min Avg. (ppm)	Time	15-min Avg. (ppm)		
7:00:00 AM	0.00	7:00:00 AM	0.00	0.00	
7:15:00 AM	0.00	7:15:00 AM	0.01	0.01	
7:30:00 AM	0.00	7:30:00 AM	0.01	0.01	
7:45:00 AM	0.00	7:45:00 AM	0.01	0.01	
8:00:00 AM	0.00	8:00:00 AM	0.01	0.01	
8:15:00 AM	0.00	8:15:00 AM	0.01	0.01	
8:30:00 AM	0.00	8:30:00 AM	0.01	0.01	
8:45:00 AM	0.00	8:45:00 AM	0.01	0.01	
9:00:00 AM	0.00	9:00:00 AM	0.01	0.01	
9:15:00 AM	0.00	9:15:00 AM	0.01	0.01	
9:30:00 AM	0.00	9:30:00 AM	0.01	0.01	
9:45:00 AM	0.00	9:45:00 AM	0.01	0.01	
10:00:00 AM	0.00	10:00:00 AM	0.01	0.01	
10:15:00 AM	0.00	10:15:00 AM	0.01	0.01	
10:30:00 AM	0.00	10:30:00 AM	0.01	0.01	
10:45:00 AM	0.00	10:45:00 AM	0.01	0.01	
11:00:00 AM	0.00	11:00:00 AM	0.01	0.01	
11:15:00 AM	0.00	11:15:00 AM	0.01	0.01	
11:30:00 AM	0.00	11:30:00 AM	0.01	0.01	
11:45:00 AM	0.00	11:45:00 AM	0.01	0.01	
12:00:00 PM	0.00	12:00:00 PM	0.01	0.01	
12:15:00 PM	0.00	12:15:00 PM	0.01	0.01	
12:30:00 PM	0.00	12:30:00 PM	0.01	0.01	
12:45:00 PM	0.00	12:45:00 PM	0.01	0.01	
1:00:00 PM	0.00	1:00:00 PM	0.01	0.01	
1:15:00 PM	0.00	1:15:00 PM	0.01	0.01	
1:30:00 PM	0.00	1:30:00 PM	0.01	0.01	
1:45:00 PM	0.00	1:45:00 PM	0.01	0.01	
2:00:00 PM	0.00	2:00:00 PM	0.01	0.01	
2:15:00 PM	0.00	2:15:00 PM	0.01	0.01	
2:30:00 PM	0.00	2:30:00 PM	0.01	0.01	
2:45:00 PM	0.00	2:45:00 PM	0.01	0.01	
3:00:00 PM	0.00	3:00:00 PM	0.01	0.01	

ppm - Parts Per Million
NR - Not recorded

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/31/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 69-80ºF, Overcast, RH: 87%, Pres: 30.10 in Hg, Wind: Variable @ 0-5 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-11:00

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
NRP (Construction Manager) **Bauer Structures** - Survey equipment	Roux D.P.C. - Christopher Farrington NRP - Ed Pierce Bauer - 1 Surveyor

SCOPE OF WORK:

Roux D.P.C. (Roux) was onsite to complete environmental monitoring during remedial activities in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated August 6, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all outdoor intrusive activities.

Description of work activities performed and general observations/comments:

- Surveying occurred onsite. No other work occurred.

CAMP data evaluation: CAMP was not implemented due to the lack of soil disturbing work activities.

Offsite Disposal: None

Import: None.

Sampling Performed: None

Upcoming work activities anticipated:

- Continuation of building up construction fencing around perimeter of Site.

Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/31/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 69-80ºF, Overcast, RH: 87%, Pres: 30.10 in Hg, Wind: Variable @ 0-5 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-11:00



Legend

CAMP Station

SITE BOUNDARY

DW

UW


Approved:	**Dana Hignell**	By:	**Christopher Farrington** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/31/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 69-80°F, Overcast, RH: 87%, Pres: 30.10 in Hg, Wind: Variable @ 0-5 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-11:00

Soil Disposal Grids and Facilities

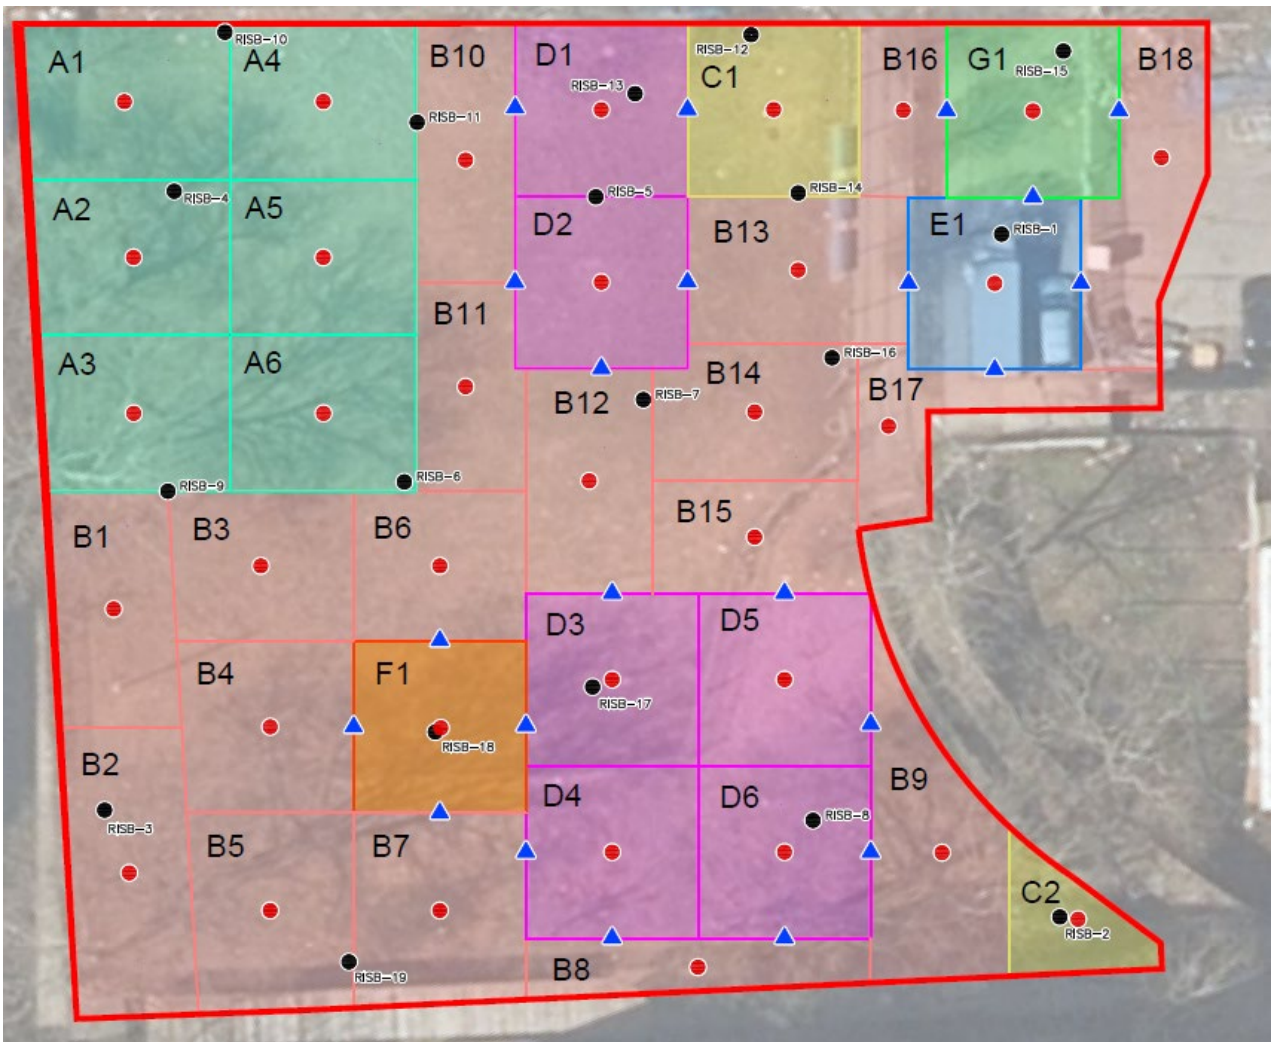

LEGEND

RISB-1 ● LOCATION OF RI/SRI SOIL BORING

▲ PROPOSED SIDEWALL ENDPOINT SAMPLE

● PROPOSED BOTTOM ENDPOINT SAMPLE

BCP SITE BOUNDARY

PARCEL BOUNDARY

EXCAVATION TO 2 FEET BELOW GRADE

EXCAVATION TO 3 FEET BELOW GRADE

EXCAVATION TO 4 FEET BELOW GRADE

EXCAVATION TO 6 FEET BELOW GRADE

EXCAVATION TO 7 FEET BELOW GRADE

EXCAVATION TO 8 FEET BELOW GRADE

EXCAVATION TO 11 FEET BELOW GRADE

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	2908.0011Y	**CLIENT:**	**DATE:**	8/31/2026
PROJECT:	Sol on Park Site (C203169)	Sol on Park LLC	**WEATHER:**	Temp: 69-80ºF, Overcast, RH: 87%, Pres: 30.10 in Hg, Wind: Variable @ 0-5 mph
LOCATION:	3728 Park Avenue, Bronx, New York		**TIME:**	07:00-11:00

PHOTOGRAPHS TAKEN TODAY: Soil On Park



Photo 1: Facing Northeast, view of Site conditions.



Photo 2: Facing Southwest, view of adjoining parking lot conditions.

Approved:	**Dana Hignell**	By:	**Christopher Farrington**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.
