ACTION LIMIT REPORT

Project Location: Lafayette Site A
1920 Turnbull Avenue, NY
NYSDEC BCP Site No. C203178

Date: October 21, 2026 Time: 1:30 pm and 1:45 pm

Name: Lafayette Site A

Contaminant: PM-10: X VOC:

Wind Speed: 0.6-5.7 mph Wind Direction: East Northeast

Temperature: 44.8-76.6 F Barometric Pressure: 30.1 & 30.4" Hg

DOWNWIND DATA

Monitor ID #: 18032022-1990 Location: Northwest perimeter Level Reported: 248.9 ug/m3

Monitor ID#: 18032022-1990 Location: Northwest perimeter Level Reported: 545.3 ug/m3

UPWIND DATA

Monitor ID #: 15072022-2115 Location: Southeast perimeter Level Reported: 12.1 ug/m3

Monitor ID#: 15072022-2115 Location: Southeast perimeter Level Reported: 20.1 ug/m3

BACKGROUND CORRECTED LEVELS

Monitor ID #: - Location: - Level Reported: 236.8 ug/m3

Monitor ID#: - Location: - Level Reported: 525.2 ug/m3

ACTIVITY DESCRIPTION

Contractors were conducting hot work to the SOE piles within the northwestern site corner. The CAMP station was positioned directly adjacent to the SOE and rising welding fumes were captured by the air intake. The exceedance was not caused by dust generated from ground intrusive work.

CORRECTIVE ACTION TAKEN

The exceedance was investigated and attributed to the welding activities as there was no visible airborne dust, but visible welding fumes. Site activities were paused and the CAMP station was moved several feet from the SOE to avoid drawing in welding fumes.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/06/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-64°F, Sunny RH: 72% Pres: 30.13” Wind: NW @ 6-18 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator Tony Casale Inc. -Takeuchi TS70V Skid Steer	Asa Tuke – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco excavated in waste characterization (WC) grid A1 (4-8) and stockpiled section of Bayshore material in WC grid A2 and stockpiled Keystone material in WC grid A1. Stockpiles were covered with plastic sheeting overnight.
- Glenco welded T-bars in the southwestern corner of grid A3/A4.
- Glenco installed inlet protection at catch basin on Turnbull Ave near the northwestern corner of the Site.
- Capstone drilled and installed steel casing for one SOE pile along White Plains Rd in grid A2.

CAMP data evaluation: CAMP was implemented from 07:00-15:15. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	53
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/06/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-64°F, Sunny RH: 72% Pres: 30.13” Wind: NW @ 6-18 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Sampling Performed:

None.

Upcoming work activities anticipated:


- Glenco will export asphalt and concrete debris from the site.
- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/06/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-64°F, Sunny RH: 72% Pres: 30.13” Wind: NW @ 6-18 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

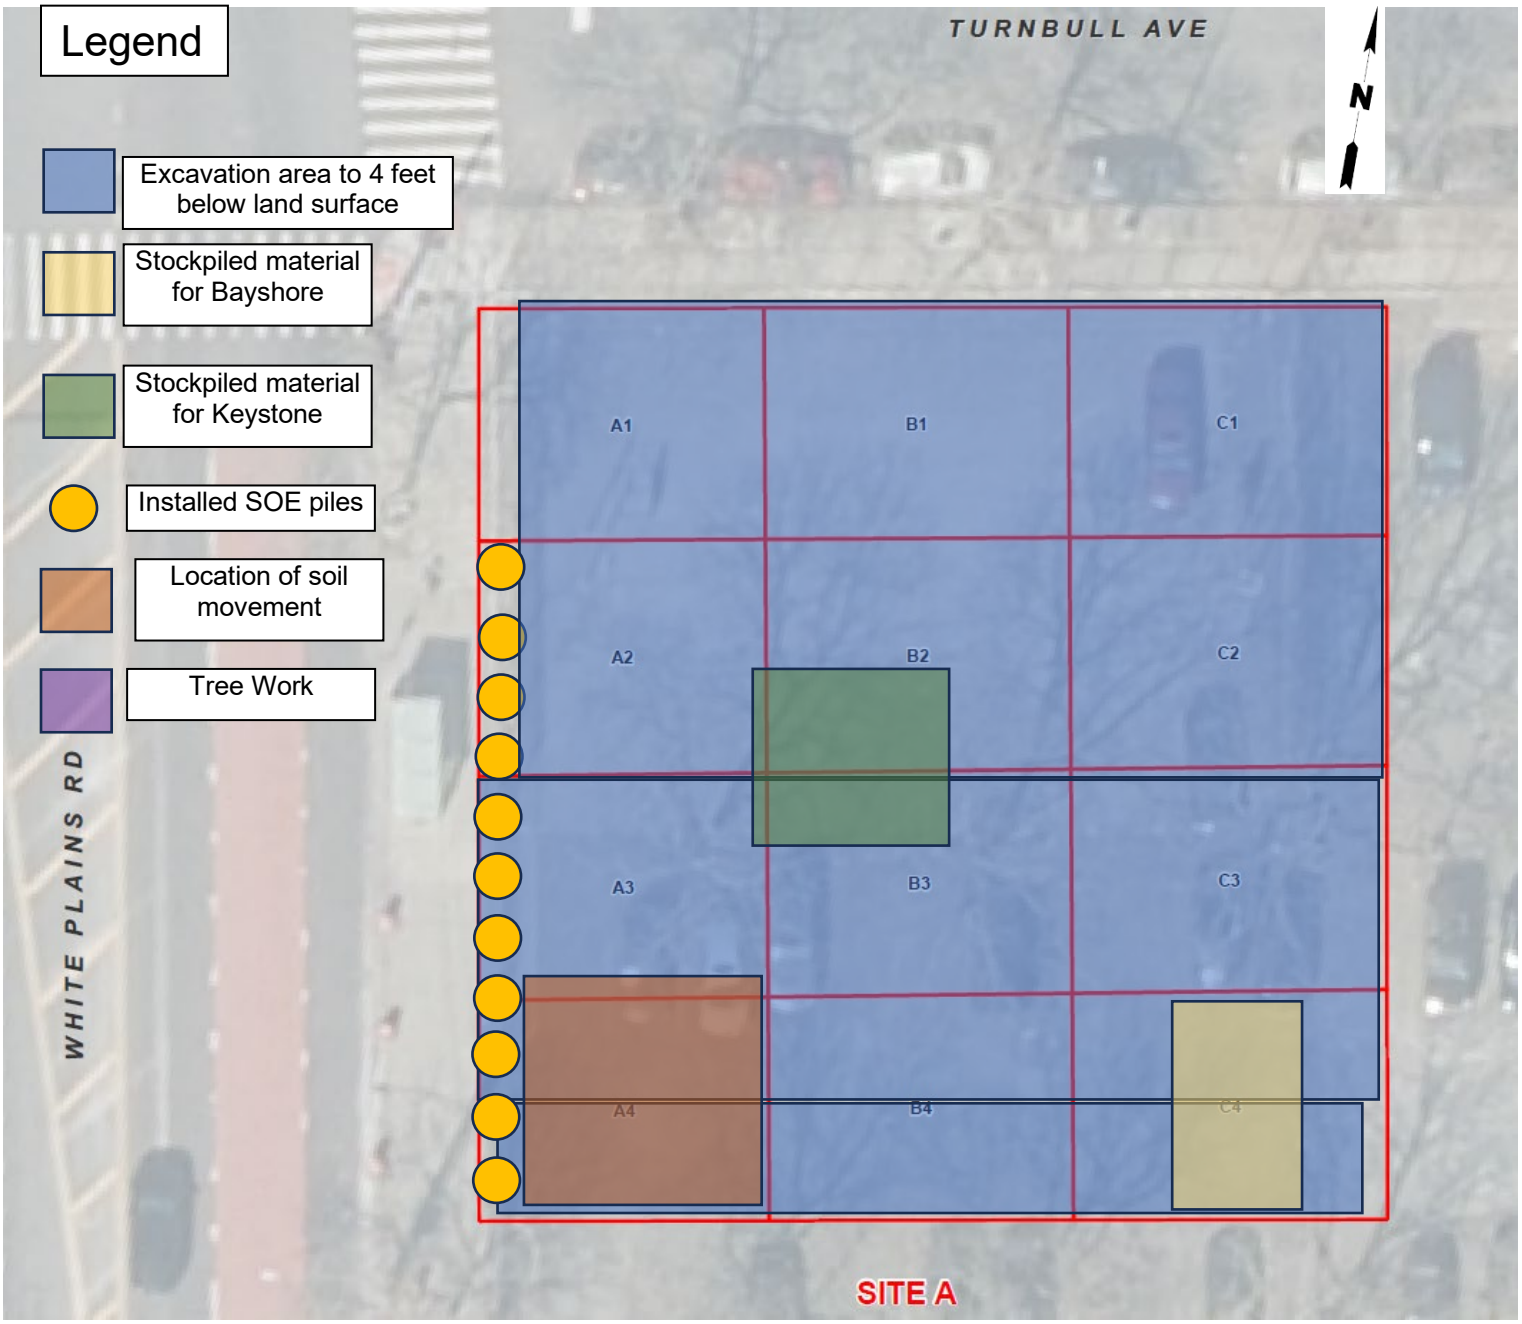

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/06/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-64°F, Sunny RH: 72% Pres: 30.13” Wind: NW @ 6-18 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A

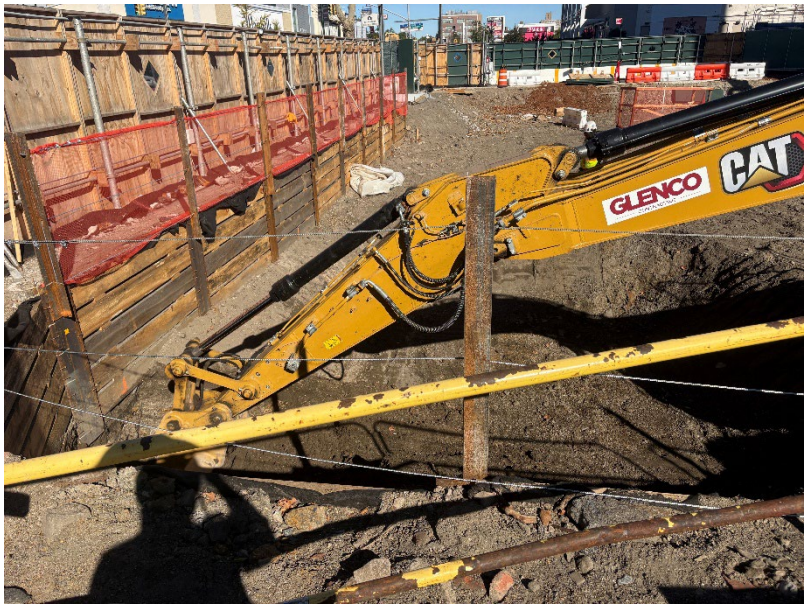


Photo 1:
Facing north, view of Glenco excavating in WC grid A1 in the southwest area of the excavated area onsite.



Photo 2:
Facing northwest, view of Capstone drilling to install steel casing for SOE piles in the northwestern corner of the Site.

Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/06/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-64°F, Sunny RH: 72% Pres: 30.13” Wind: NW @ 6-18 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing west, view of Glenco installing inlet protection to the catch basin on Turnbull Ave by the northwest corner of the Site.


Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/06/2026 07:00
		To: 10/06/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/06/2026	45.5 - 64.8	35.9 - 60.0	30.0 - 30.4	0.9 - 5.5	ENE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/6/2026	0.0	07:00	0.0000	07:00
Max Contribution (15 min avg.) - 10/6/2026	26.0	07:30	0.0040	07:15
Daily Avg. Contribution (15 min avg.) - 10/6/2026	1.1	-	0.0001	-

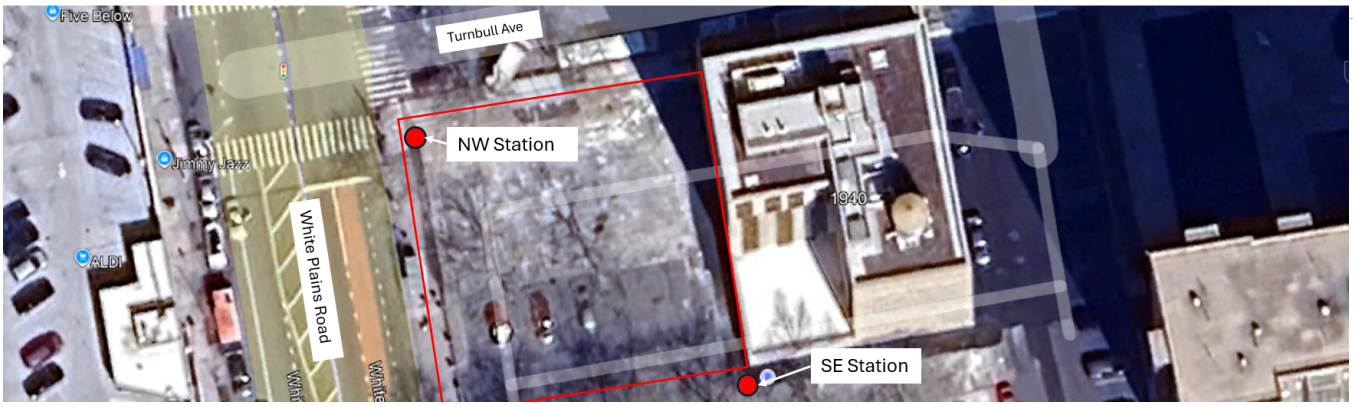


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

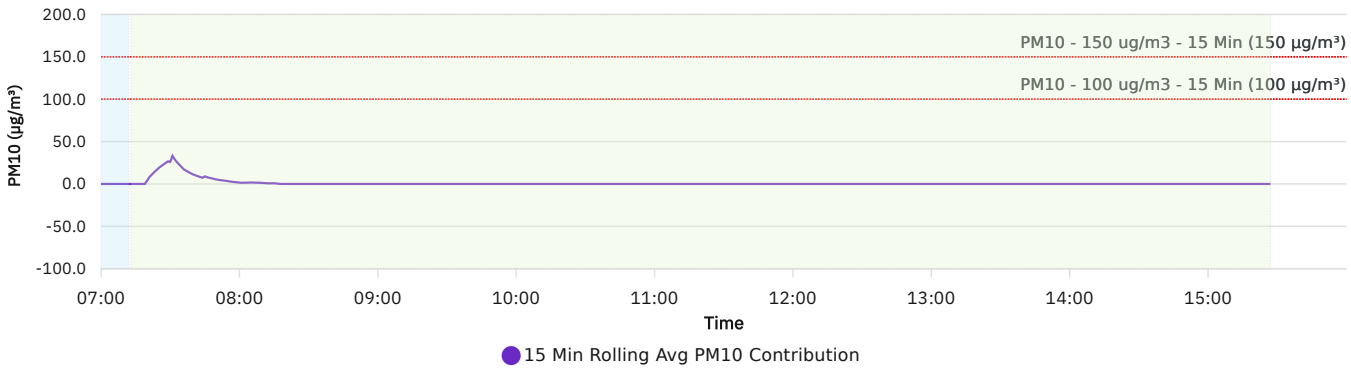

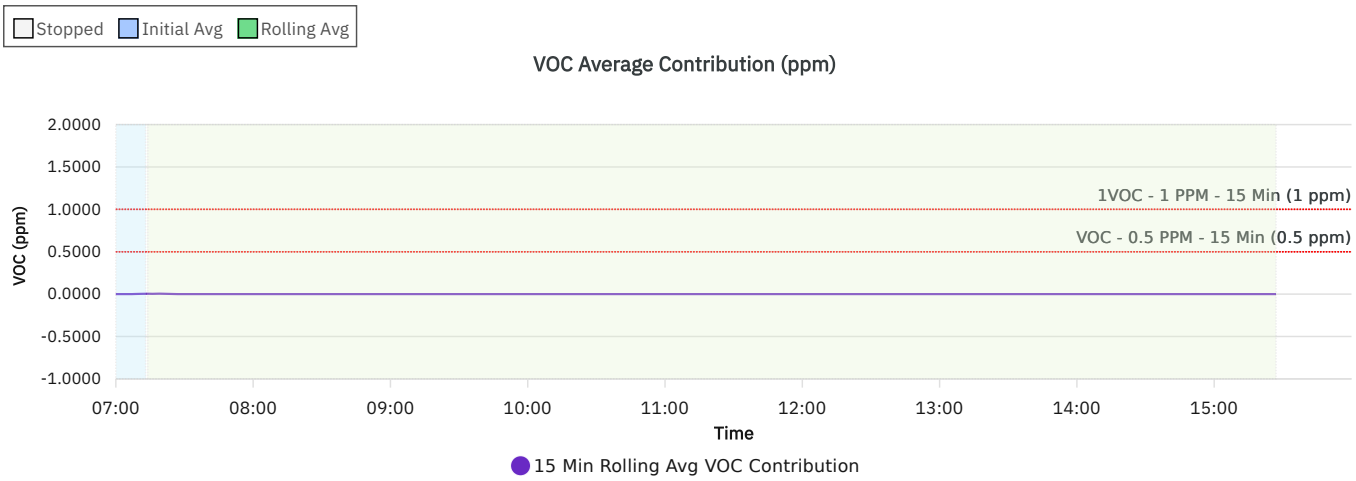

Wind rose (mph)

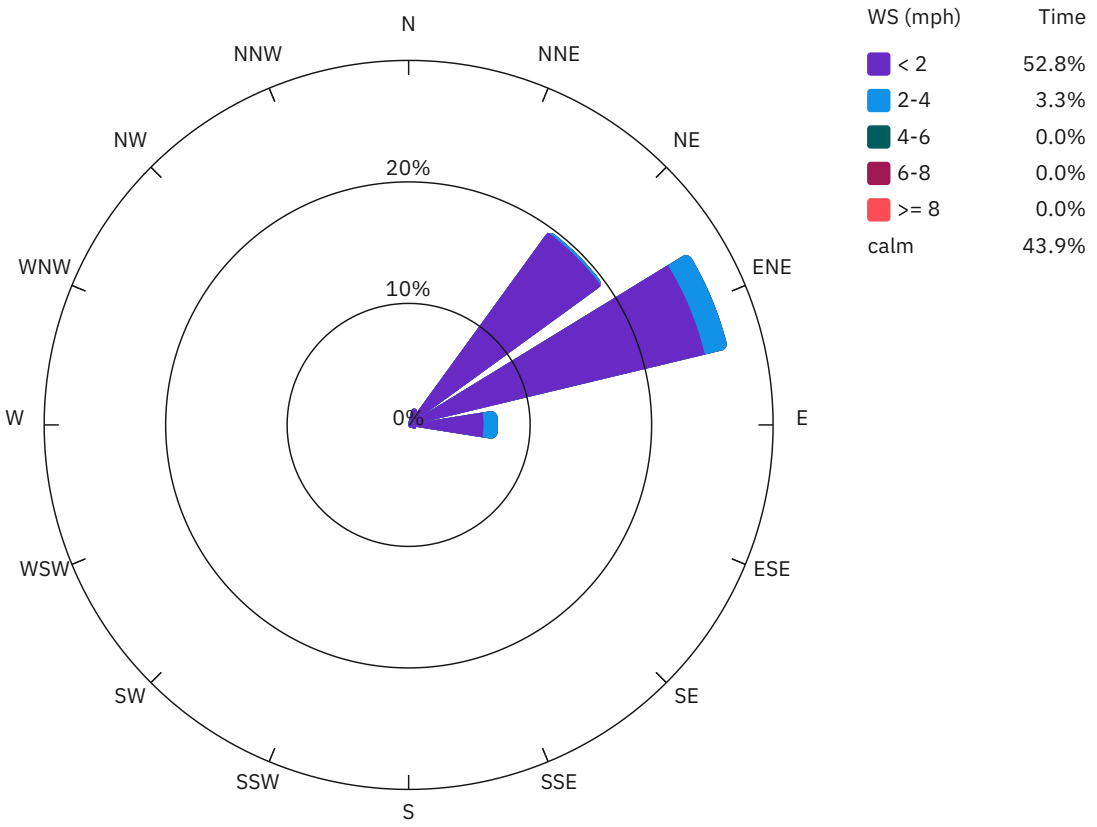

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/6/2026 07:00	5.8	3.7	0.0	0.0000	0.0000	0.0000	0.5	N
10/6/2026 07:15	12.2	2.0	0.0	0.0100	0.0140	0.0040	0.6	NE
10/6/2026 07:30	15.6	41.6	26.0	0.0100	0.0080	0.0000	0.7	ENE
10/6/2026 07:45	7.1	16.0	8.9	0.0113	0.0027	0.0000	1.0	NE
10/6/2026 08:00	7.3	8.9	1.6	0.0113	0.0000	0.0000	0.9	NE
10/6/2026 08:15	7.5	8.3	0.8	0.0133	0.0000	0.0000	1.0	NE
10/6/2026 08:30	7.6	5.7	0.0	0.0093	0.0007	0.0000	0.9	NE
10/6/2026 08:45	7.8	4.7	0.0	0.0093	0.0007	0.0000	0.9	NE
10/6/2026 09:00	43.1	3.4	0.0	0.0100	0.0000	0.0000	1.1	ENE
10/6/2026 09:15	14.3	5.7	0.0	0.0100	0.0000	0.0000	1.1	NE
10/6/2026 09:30	10.7	4.5	0.0	0.0093	0.0007	0.0000	1.2	NE
10/6/2026 09:45	9.9	3.5	0.0	0.0113	0.0007	0.0000	1.2	ENE
10/6/2026 10:00	10.5	3.2	0.0	0.0120	0.0000	0.0000	1.1	NE
10/6/2026 10:15	12.5	1.9	0.0	0.0100	0.0000	0.0000	1.3	ENE
10/6/2026 10:30	13.2	2.0	0.0	0.0100	0.0000	0.0000	1.2	ENE
10/6/2026 10:45	11.6	1.8	0.0	0.0133	0.0000	0.0000	1.2	ENE
10/6/2026 11:00	10.1	2.4	0.0	0.0093	0.0007	0.0000	1.0	NE
10/6/2026 11:15	11.1	2.0	0.0	0.0100	0.0000	0.0000	1.1	ENE
10/6/2026 11:30	11.1	2.0	0.0	0.0100	0.0000	0.0000	1.3	ENE
10/6/2026 11:45	8.1	1.0	0.0	0.0100	0.0000	0.0000	1.0	ENE
10/6/2026 12:00	9.9	2.4	0.0	0.0100	0.0000	0.0000	1.5	ENE
10/6/2026 12:15	9.6	2.1	0.0	0.0100	0.0000	0.0000	0.9	NE
10/6/2026 12:30	9.5	2.0	0.0	0.0100	0.0000	0.0000	1.1	ENE
10/6/2026 12:45	7.9	1.4	0.0	0.0100	0.0000	0.0000	0.7	ENE
10/6/2026 13:00	8.4	1.7	0.0	0.0100	0.0000	0.0000	0.9	ENE
10/6/2026 13:15	8.0	1.5	0.0	0.0100	0.0000	0.0000	0.9	ENE
10/6/2026 13:30	8.6	2.1	0.0	0.0107	0.0000	0.0000	0.9	ENE
10/6/2026 13:45	8.4	1.7	0.0	0.0107	0.0000	0.0000	1.1	ENE
10/6/2026 14:00	9.0	1.8	0.0	0.0100	0.0000	0.0000	1.0	ENE
10/6/2026 14:15	6.7	2.0	0.0	0.0100	0.0000	0.0000	1.1	ENE
10/6/2026 14:30	7.0	1.3	0.0	0.0100	0.0000	0.0000	0.9	ENE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/6/2026 14:45	7.4	2.3	0.0	0.0093	0.0007	0.0000	0.9	ENE
10/6/2026 15:00	7.5	2.1	0.0	0.0100	0.0000	0.0000	1.1	ENE
10/6/2026 15:15	8.0	1.5	0.0	0.0113	0.0000	0.0000	1.0	ENE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/7/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 44-67°F, Sunny RH: 83% Pres: 30.07” Wind: NW @ 3 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator Tony Casale Inc. -Takeuchi TS70V Skid Steer	Asa Tuke – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp. Tony Casale

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco exported 8 trucks of soil from grids A3 and A4 from 4-8 feet below land surface (ft bls) to Keystone Trade Center, PA Permit # PAD090088 located at 1 Ben Fairless Drive, Morrisville, PA 19067.
- Glenco ensured all trucks entering the site were washed on the truck pad prior to exiting.
- Glenco excavated and stockpiled soil from grids A3 and A4 from 4-8 ft bls.
- Glenco welded T-bars in the southwestern corner of grid A3/A4.
- Capstone drilled and installed steel casings for three SOE piles along White Plains Rd in grid A1.
- Tony Casale moved the Site’s western construction fence in line with sidewalk following tree work on White Plains Rd are now outside of the fence. Tony Casale ensured both trees are protected with tree wrap and protective fencing.

CAMP data evaluation: CAMP was implemented from 07:00-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	8	61
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/7/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 44-67°F, Sunny RH: 83% Pres: 30.07” Wind: NW @ 3 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will export concrete debris from the site.
- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/7/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 44-67°F, Sunny RH: 83% Pres: 30.07” Wind: NW @ 3 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

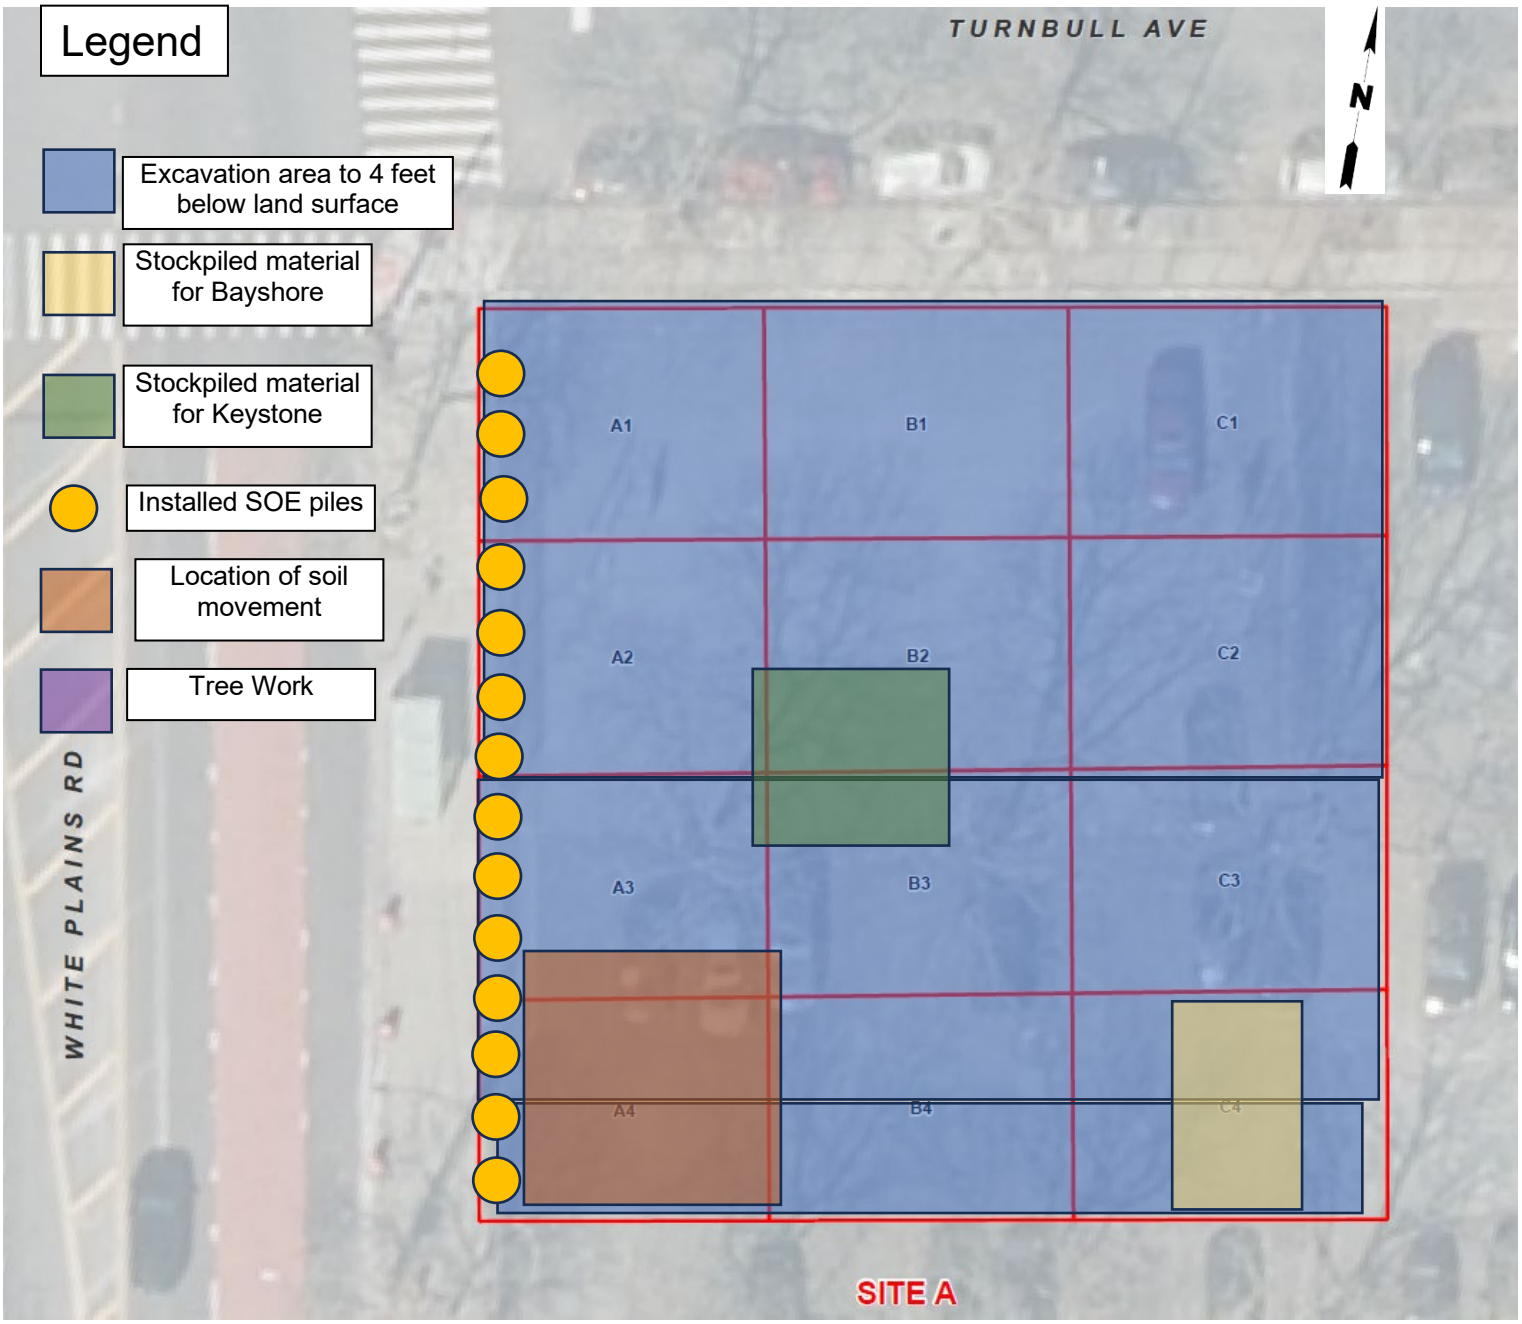

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/7/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 44-67°F, Sunny RH: 83% Pres: 30.07” Wind: NW @ 3 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing southwest, view of Glenco loading truck with soil from grids A3 and A4 from 4-8 ft bls to be exported to the Keystone Trade Center facility in Morrisville, PA.



Photo 2:
Facing northwest, view of Capstone drilling to install steel casing for SOE piles in the northwestern corner of the Site.

Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/7/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 44-67°F, Sunny RH: 83% Pres: 30.07” Wind: NW @ 3 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing northwest, view of Glenco welding T-bars along the western boundary of the Site.


Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.


ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/07/2026 07:00
		To: 10/07/2026 16:00


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/07/2026	43.2 - 69.8	36.3 - 72.9	29.9 - 30.3	0.2 - 9.3	S


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/7/2026	0.0	07:00	0.0000	09:15
Max Contribution (15 min avg.) - 10/7/2026	42.4	14:00	0.0713	07:15
Daily Avg. Contribution (15 min avg.) - 10/7/2026	6.7	-	0.0159	-

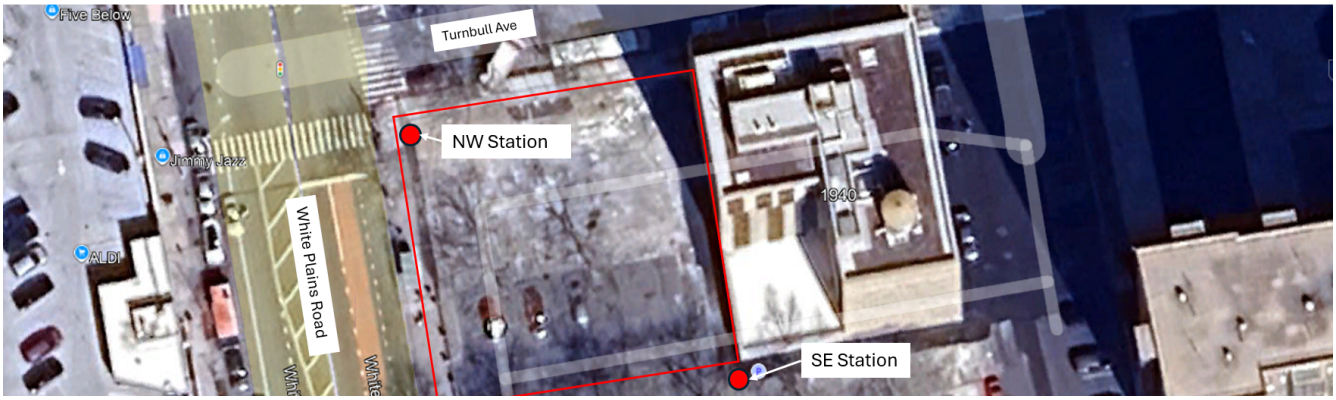

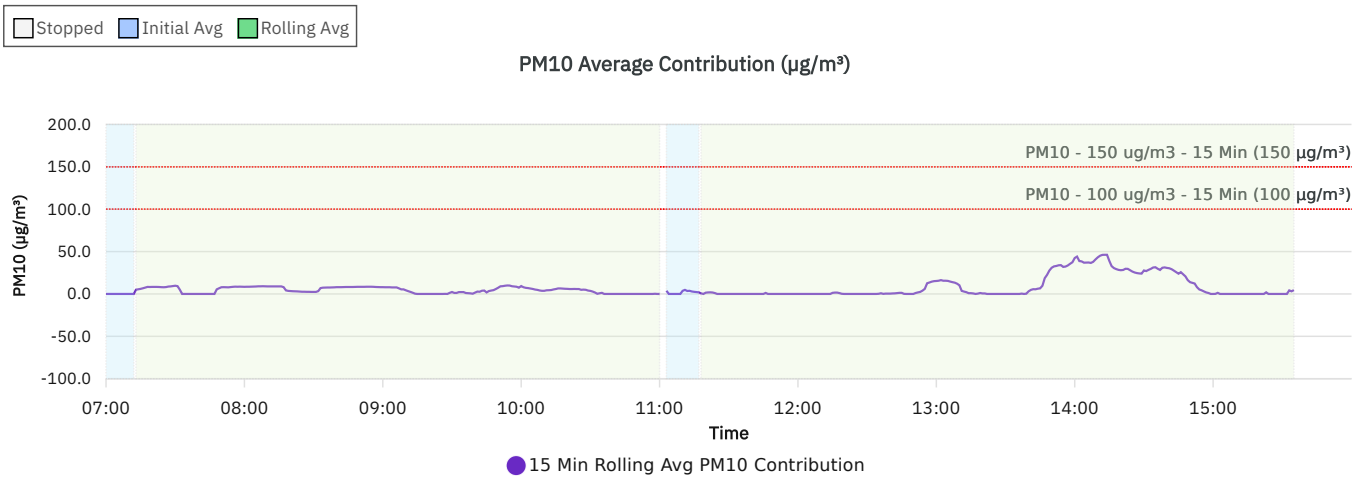

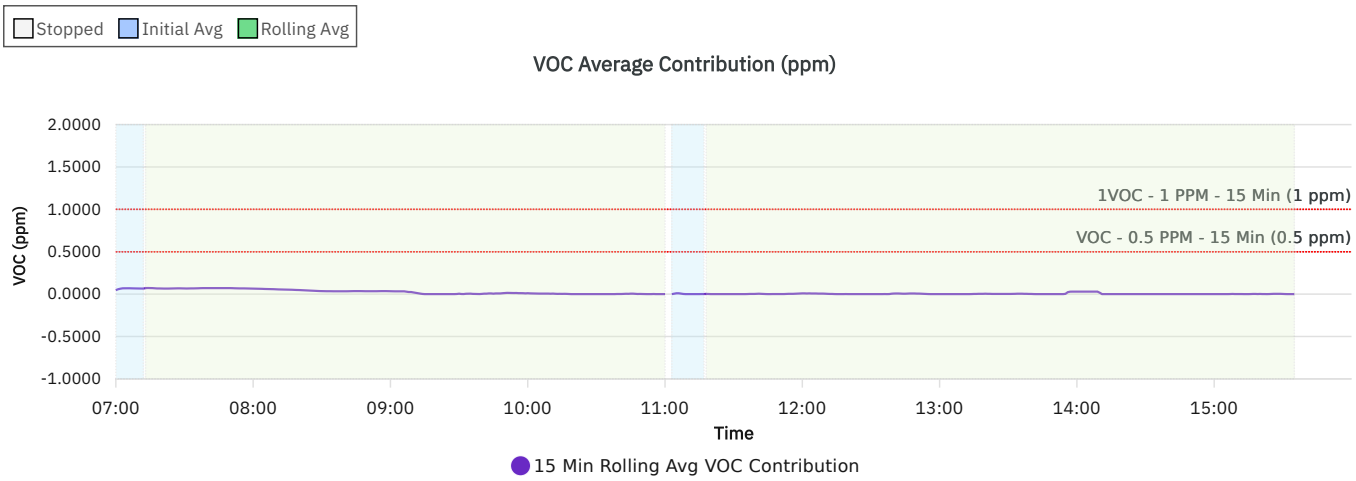

Wind rose (mph)

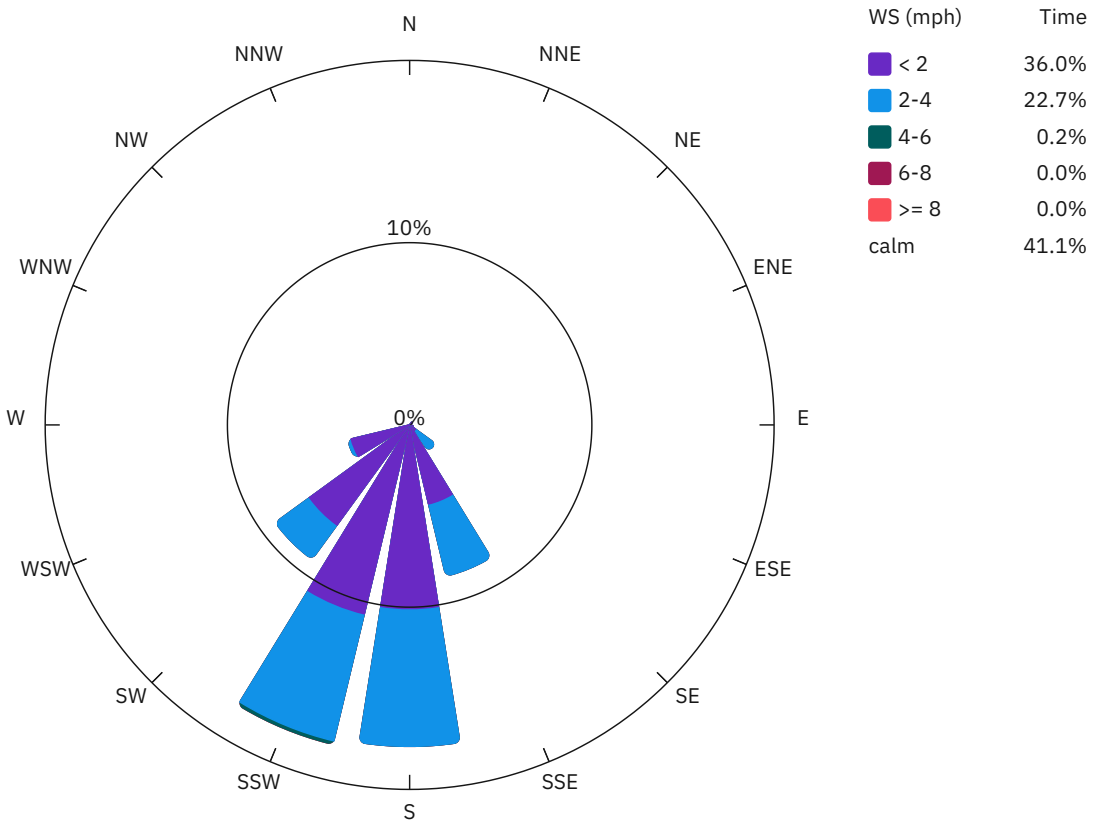

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/7/2026 07:00	41.5	11.5	0.0	0.0100	0.0567	0.0467	0.3	NE
10/7/2026 07:15	5.8	11.8	6.0	0.0180	0.0893	0.0713	0.3	ENE
10/7/2026 07:30	3.2	12.9	9.7	0.0287	0.0953	0.0667	0.4	ENE
10/7/2026 07:45	18.0	11.8	0.0	0.0240	0.0947	0.0707	0.3	ENE
10/7/2026 08:00	1.3	9.7	8.4	0.0200	0.0847	0.0647	0.4	ENE
10/7/2026 08:15	0.0	8.9	8.9	0.0200	0.0727	0.0527	0.4	E
10/7/2026 08:30	5.5	7.8	2.4	0.0200	0.0553	0.0353	0.3	ENE
10/7/2026 08:45	0.1	8.3	8.2	0.0200	0.0553	0.0353	0.4	ENE
10/7/2026 09:00	0.5	8.5	8.0	0.0200	0.0540	0.0340	0.4	ENE
10/7/2026 09:15	4.5	3.7	0.0	0.0360	0.0340	0.0000	0.1	SSW
10/7/2026 09:30	3.6	5.9	2.3	0.0307	0.0353	0.0047	0.5	S
10/7/2026 09:45	3.7	5.5	1.8	0.0267	0.0320	0.0053	0.6	S
10/7/2026 10:00	3.5	12.8	9.3	0.0220	0.0327	0.0107	0.4	SSE
10/7/2026 10:15	0.7	6.5	5.8	0.0207	0.0233	0.0027	0.5	SSE
10/7/2026 10:30	1.1	4.8	3.6	0.0180	0.0120	0.0000	1.2	S
10/7/2026 10:45	10.3	2.3	0.0	0.0080	0.0133	0.0053	1.2	SW
10/7/2026 11:00	5.6	5.1	0.0	0.0120	0.0100	0.0000	0.8	S
10/7/2026 11:15	8.4	10.9	2.5	0.0077	0.0077	0.0000	1.1	SSW
10/7/2026 11:30	12.0	6.1	0.0	0.0053	0.0053	0.0000	1.3	SSW
10/7/2026 11:45	9.4	8.9	0.0	0.0053	0.0047	0.0000	1.4	SSW
10/7/2026 12:00	11.6	3.3	0.0	0.0007	0.0093	0.0087	1.5	SW
10/7/2026 12:15	4.8	6.1	1.3	0.0053	0.0047	0.0000	1.1	SSW
10/7/2026 12:30	7.2	4.2	0.0	0.0227	0.0153	0.0000	1.2	SW
10/7/2026 12:45	4.9	6.2	1.3	0.0027	0.0073	0.0047	1.4	SSW
10/7/2026 13:00	3.0	18.3	15.3	0.0067	0.0033	0.0000	1.5	S
10/7/2026 13:15	3.9	4.8	0.9	0.0040	0.0060	0.0020	1.8	SSW
10/7/2026 13:30	7.8	5.8	0.0	0.0040	0.0060	0.0020	2.3	SSW
10/7/2026 13:45	5.1	11.7	6.6	0.0073	0.0040	0.0000	2.1	S
10/7/2026 14:00	4.7	47.1	42.4	0.0100	0.0393	0.0293	2.2	SSE
10/7/2026 14:15	6.5	45.5	39.0	0.0093	0.0007	0.0000	2.2	SSE
10/7/2026 14:30	5.8	33.5	27.7	0.0093	0.0007	0.0000	2.2	SSE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/7/2026 14:45	6.5	30.4	23.9	0.0093	0.0007	0.0000	1.9	S
10/7/2026 15:00	7.7	7.3	0.0	0.0053	0.0047	0.0000	2.0	SSW
10/7/2026 15:15	15.8	13.2	0.0	0.0053	0.0047	0.0000	1.9	SSW
10/7/2026 15:30	15.9	11.0	0.0	0.0040	0.0060	0.0020	2.3	SSW

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/8/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 56-75°F, Sunny RH: 88% Pres: 29.81” Wind: SW @ 5-13 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Asa Tuke – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp. Tony Casale Josh Remer – MRCE Verizon

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco excavated and stockpiled soil from grids A1, A2, A3 and A4.
- Glenco welded T bars and installed lagging along the western boundary of the Site.
- Capstone drilled and installed steel casings for four SOE piles in the northeastern corner of the Site in grid C1.
- Verizon repaired an underground fiber optic line that was hit during Capstone’s drilling yesterday (10/7/26) in the northwest corner of the Site in grid A1.

CAMP data evaluation: CAMP was implemented from 07:00-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	61
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/8/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 56-75°F, Sunny RH: 88% Pres: 29.81” Wind: SW @ 5-13 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Upcoming work activities anticipated:


- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/8/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 56-75°F, Sunny RH: 88% Pres: 29.81” Wind: SW @ 5-13 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

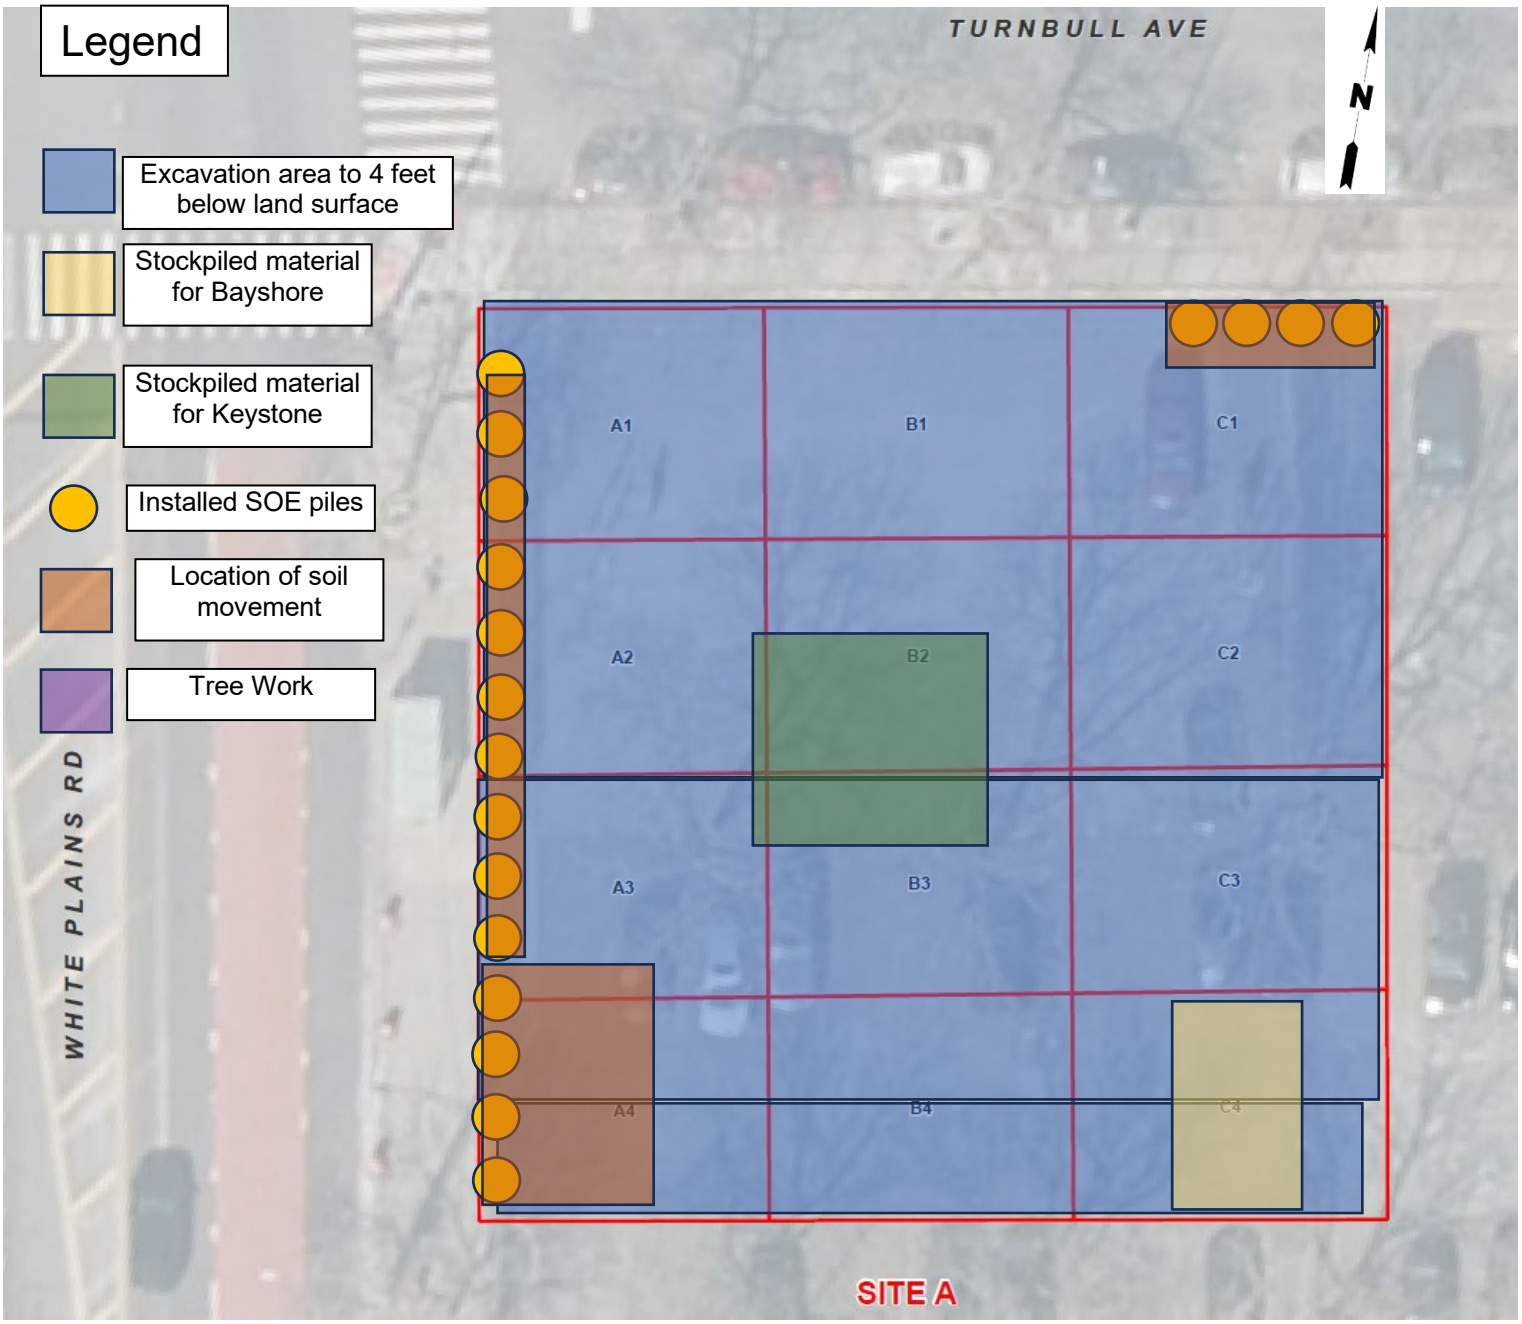

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/8/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 56-75°F, Sunny RH: 88% Pres: 29.81” Wind: SW @ 5-13 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing southwest, view of Glenco excavating in grid A3 from 4 to 8 feet below land surface along the western boundary of the Site.



Photo 2:
Facing east, view of Capstone drilling to install steel casing for SOE piles in the northeastern corner of the Site.

Approved:	Patrick Perry	By:	**Asa Tuke**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/8/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 56-75°F, Sunny RH: 88% Pres: 29.81” Wind: SW @ 5-13 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing west, view of Verizon repairing broken fiber optic cable in the northwestern corner of the Site.

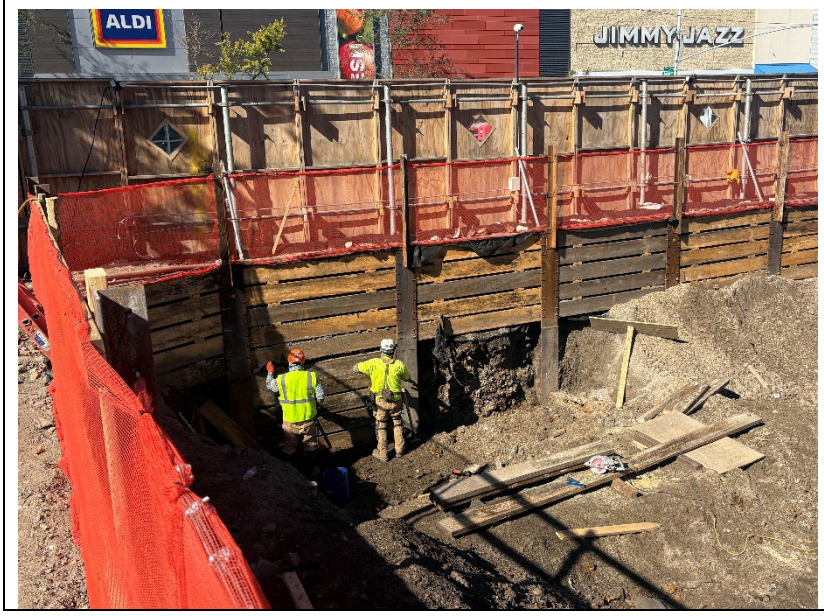


Photo 4: Facing west, view of Glenco installing lagging along the western boundary of the Site.


Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/08/2026 07:00
		To: 10/08/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/08/2026	55.6 - 77.5	33.3 - 76.6	29.8 - 30.0	0.8 - 5.5	ENE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/8/2026	0.0	07:00	0.0000	07:00
Max Contribution (15 min avg.) - 10/8/2026	30.5	13:15	0.0420	11:30
Daily Avg. Contribution (15 min avg.) - 10/8/2026	5.4	-	0.0024	-

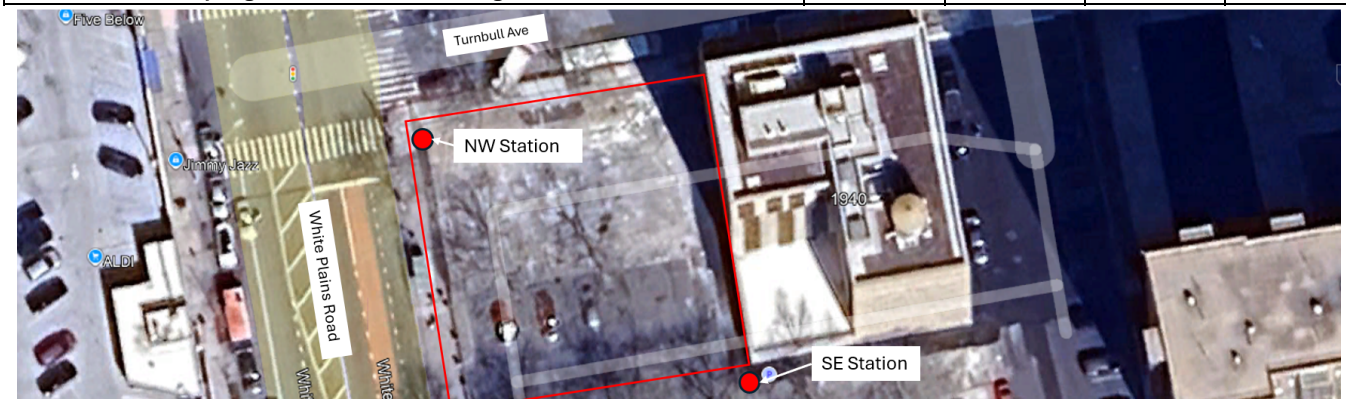


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

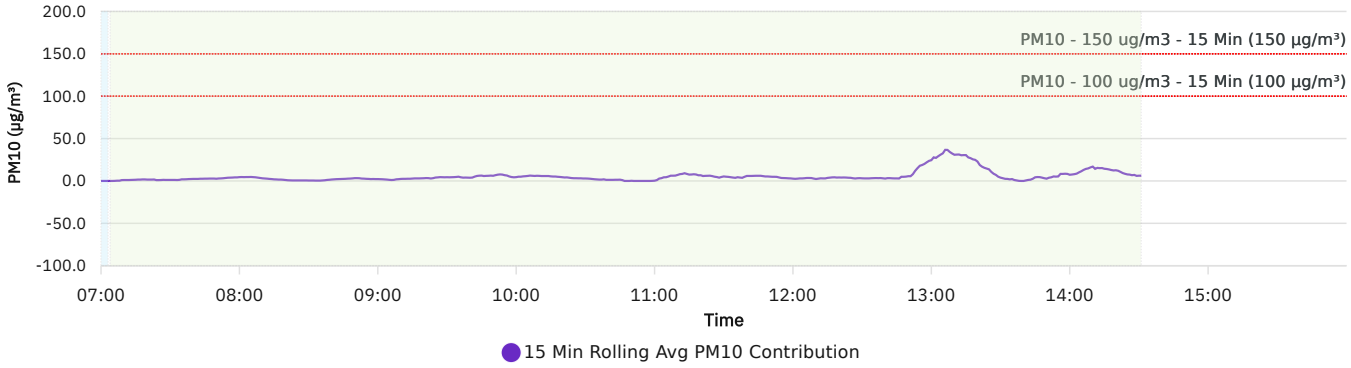

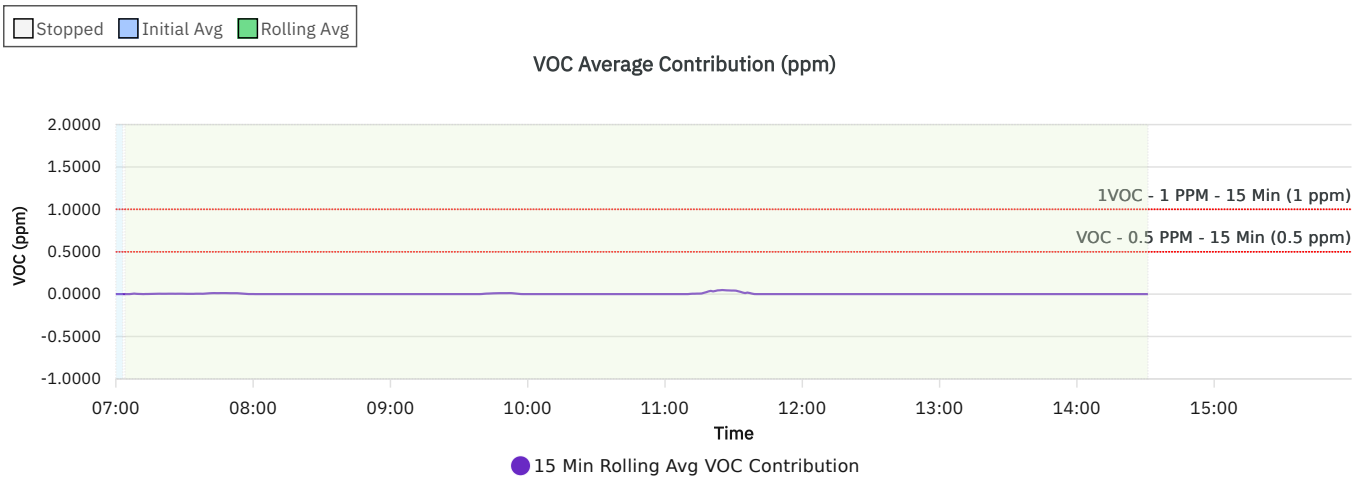

Wind rose (mph)

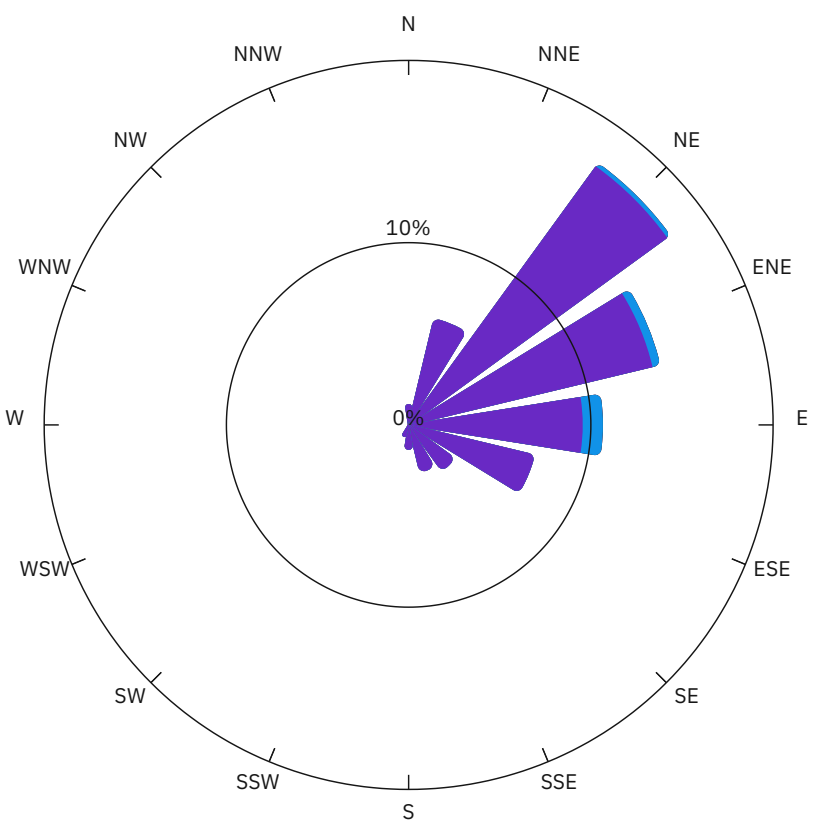

WS (mph)	Time
< 2	62.6%
2-4	1.8%
4-6	0.0%
6-8	0.0%
>= 8	0.0%
calm	35.6%

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/8/2026 07:00	5.2	4.9	0.0	0.0217	0.0200	0.0000	0.3	S
10/8/2026 07:15	4.2	5.6	1.4	0.0207	0.0227	0.0020	0.5	ESE
10/8/2026 07:30	4.1	5.3	1.2	0.0207	0.0247	0.0040	0.8	E
10/8/2026 07:45	3.6	6.3	2.7	0.0200	0.0313	0.0113	1.1	E
10/8/2026 08:00	4.4	8.9	4.5	0.0180	0.0187	0.0007	0.9	ESE
10/8/2026 08:15	4.8	6.7	1.9	0.0193	0.0107	0.0000	1.0	E
10/8/2026 08:30	5.3	5.9	0.5	0.0193	0.0107	0.0000	0.7	ESE
10/8/2026 08:45	5.6	8.0	2.4	0.0173	0.0100	0.0000	1.0	E
10/8/2026 09:00	6.0	8.2	2.2	0.0193	0.0080	0.0000	1.4	ESE
10/8/2026 09:15	6.5	9.2	2.8	0.0120	0.0100	0.0000	1.1	E
10/8/2026 09:30	6.7	11.1	4.4	0.0173	0.0100	0.0000	1.0	ESE
10/8/2026 09:45	8.2	14.5	6.3	0.0153	0.0247	0.0093	0.9	SSE
10/8/2026 10:00	7.0	11.5	4.5	0.0187	0.0173	0.0000	0.8	SE
10/8/2026 10:15	7.6	13.1	5.4	0.0187	0.0140	0.0000	0.6	E
10/8/2026 10:30	7.5	10.4	2.9	0.0180	0.0100	0.0000	0.9	ENE
10/8/2026 10:45	7.0	8.5	1.5	0.0113	0.0093	0.0000	0.8	NE
10/8/2026 11:00	9.2	9.6	0.3	0.0100	0.0053	0.0000	1.0	NE
10/8/2026 11:15	6.2	13.6	7.5	0.0120	0.0180	0.0060	1.1	NNE
10/8/2026 11:30	5.2	10.5	5.3	0.0167	0.0587	0.0420	1.1	NE
10/8/2026 11:45	5.8	11.9	6.1	0.0100	0.0000	0.0000	0.9	NE
10/8/2026 12:00	6.6	9.3	2.7	0.0087	0.0013	0.0000	1.1	NE
10/8/2026 12:15	6.4	10.0	3.6	0.0100	0.0000	0.0000	0.8	ENE
10/8/2026 12:30	4.7	7.7	3.1	0.0093	0.0007	0.0000	1.1	NE
10/8/2026 12:45	4.8	7.8	3.0	0.0100	0.0000	0.0000	0.9	NE
10/8/2026 13:00	4.7	29.2	24.5	0.0100	0.0000	0.0000	1.3	NE
10/8/2026 13:15	4.0	34.6	30.5	0.0100	0.0000	0.0000	1.3	ENE
10/8/2026 13:30	7.7	11.7	3.9	0.0093	0.0007	0.0000	1.2	NE
10/8/2026 13:45	7.5	11.8	4.3	0.0100	0.0000	0.0000	1.4	NE
10/8/2026 14:00	5.1	12.4	7.3	0.0100	0.0000	0.0000	1.2	NE
10/8/2026 14:15	5.5	19.9	14.4	0.0100	0.0000	0.0000	1.3	ENE
10/8/2026 14:30	4.6	10.8	6.2	0.0100	0.0000	0.0000	0.9	NE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/9/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 50-72°F, Sunny RH: 79% Pres: 30.10” Wind: W @ 4-7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Asa Tuke – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco exported 16 trucks of soil from grids A3 and A4 from 4-8 feet below land surface (ft bls) to Keystone Trade Center, PA Permit # PAD090088 located at 1 Ben Fairless Drive, Morrisville, PA 19067.
- Glenco excavated and stockpiled soil from grids A2 and A3 from 4-8 feet ft bls.
- Glenco welded T bars and installed lagging along the western boundary of the Site.
- Capstone drilled and installed steel casings for four SOE piles in the northeastern corner of the Site in grids C1 and B1.

CAMP data evaluation: CAMP was implemented from 07:00-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	16	77
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Sampling Performed:

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/9/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 50-72°F, Sunny RH: 79% Pres: 30.10” Wind: W @ 4-7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/9/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 50-72°F, Sunny RH: 79% Pres: 30.10” Wind: W @ 4-7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

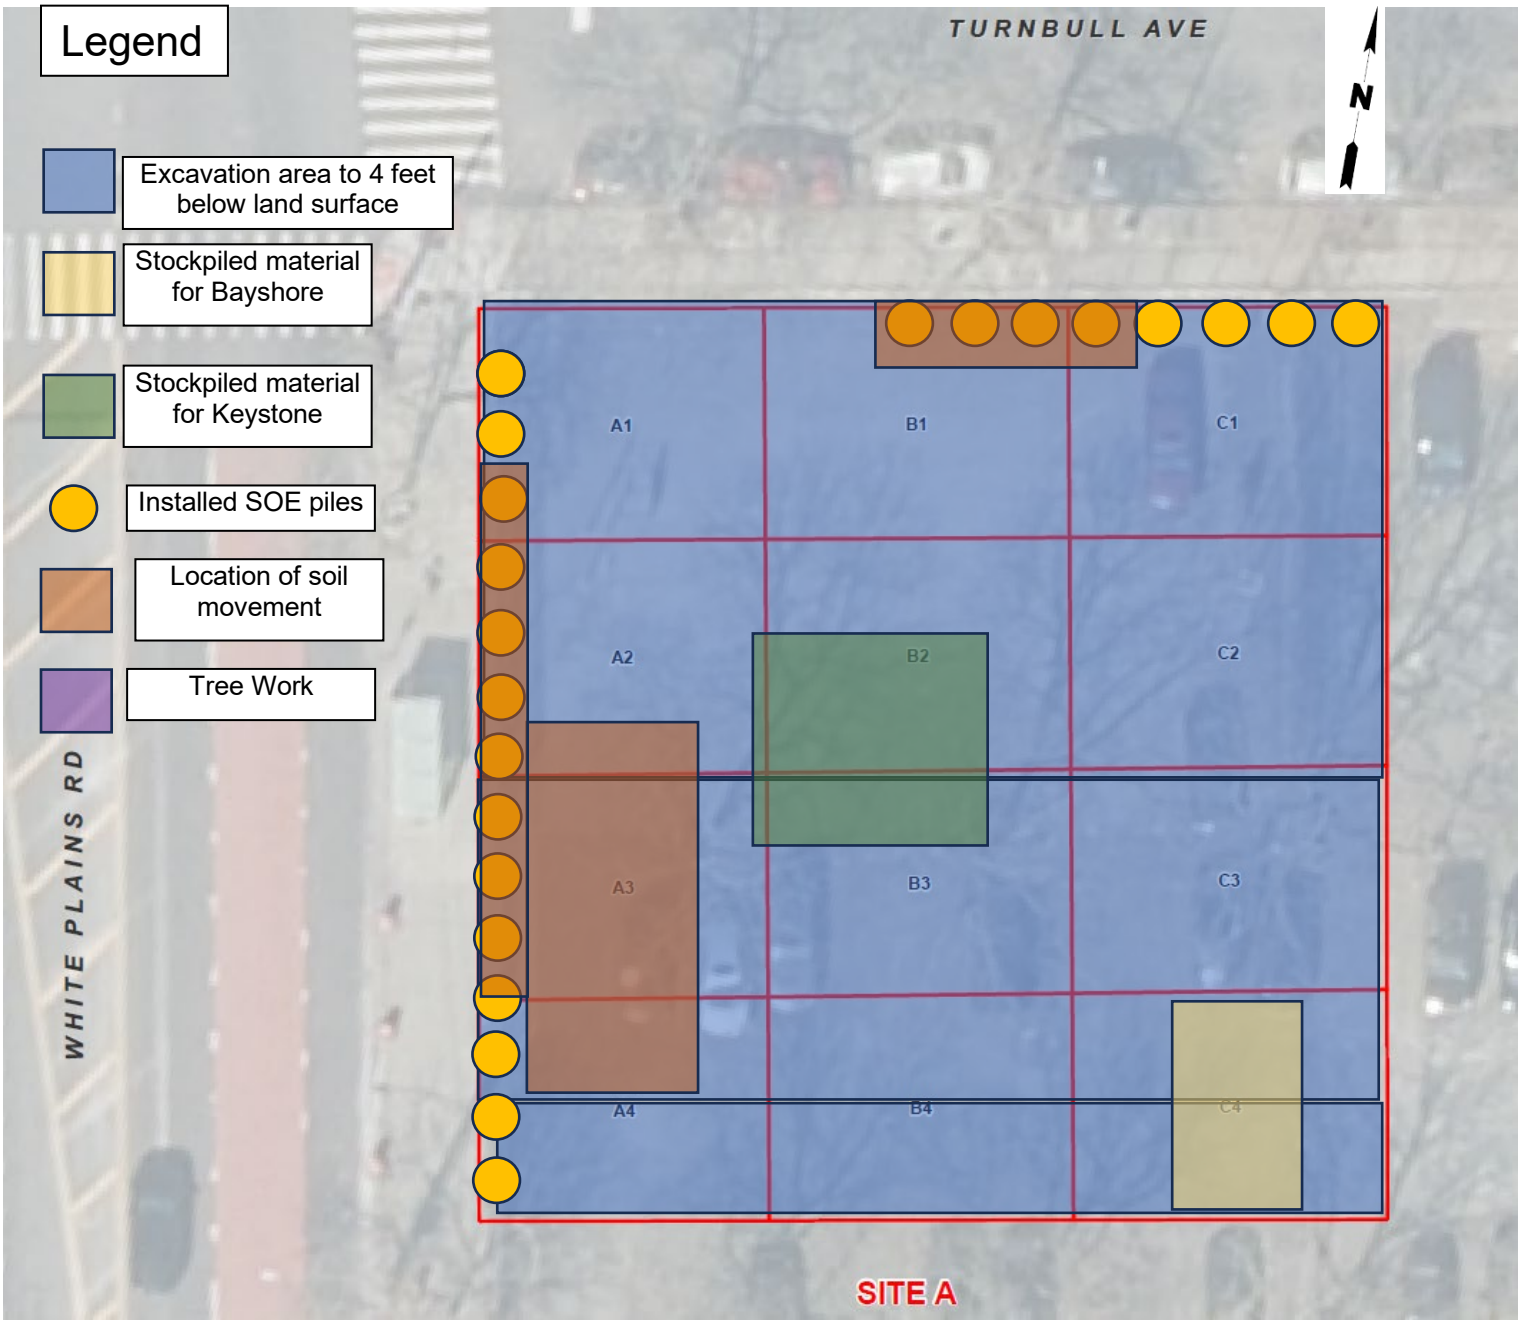

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/9/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 50-72°F, Sunny RH: 79% Pres: 30.10” Wind: W @ 4-7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, view of Glenco loading truck with soil to be exported to Keystone Trade Center in Morrisville, PA .



Photo 2:
Facing west, view of Capstone drilling to install steel casing for SOE piles in the northern area of the Site.

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/9/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 50-72°F, Sunny RH: 79% Pres: 30.10” Wind: W @ 4-7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing east, view of southeast CAMP station near the Site’s office trailers.

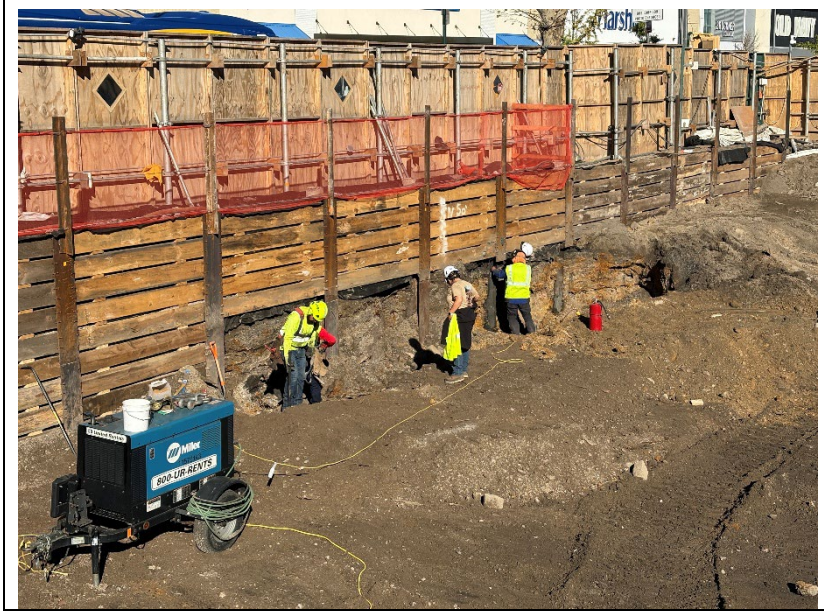


Photo 4: Facing northwest, view of Glenco installing lagging along the western boundary of the Site.

Approved:	Patrick Perry	By:	**Asa Tuke** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/09/2026 07:00
		To: 10/09/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/09/2026	52.5 - 75.2	32.8 - 60.1	30.1 - 30.3	0.2 - 5.5	NE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/9/2026	0.0	07:00	0.0000	07:15
Max Contribution (15 min avg.) - 10/9/2026	27.4	14:00	0.0060	07:00
Daily Avg. Contribution (15 min avg.) - 10/9/2026	2.0	-	0.0005	-




Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

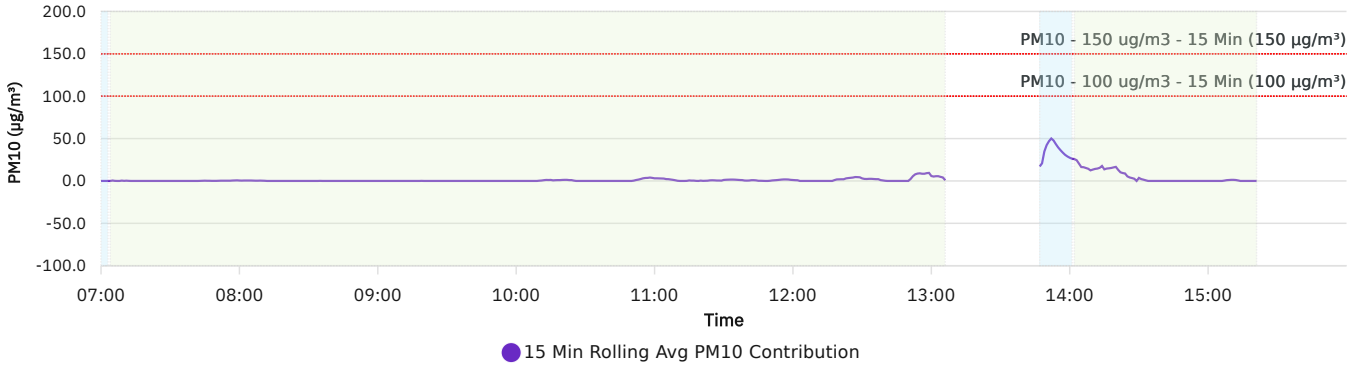

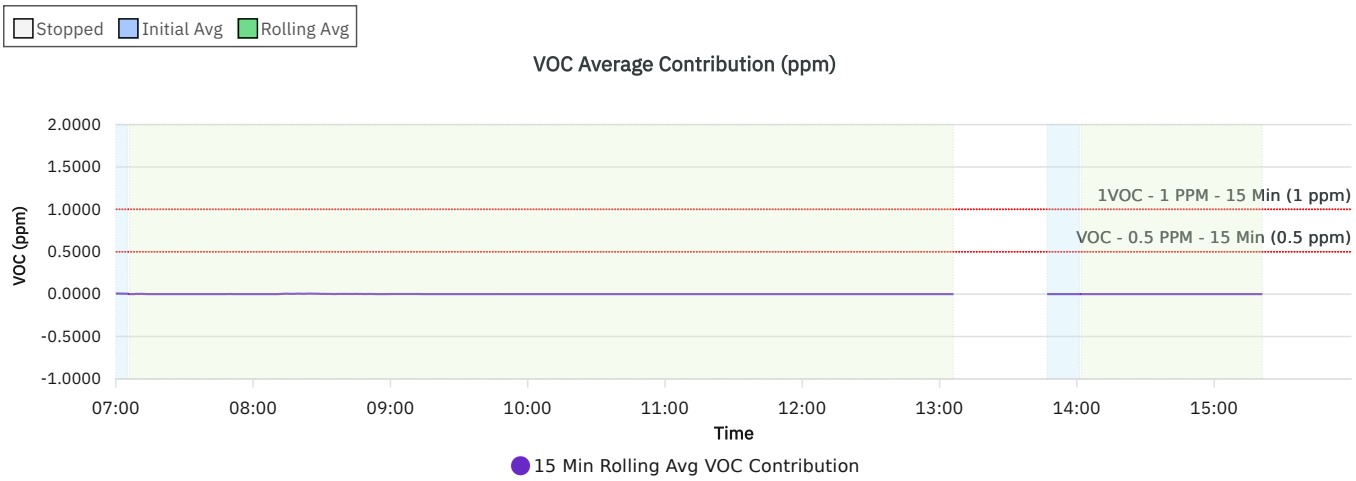

Wind rose (mph)

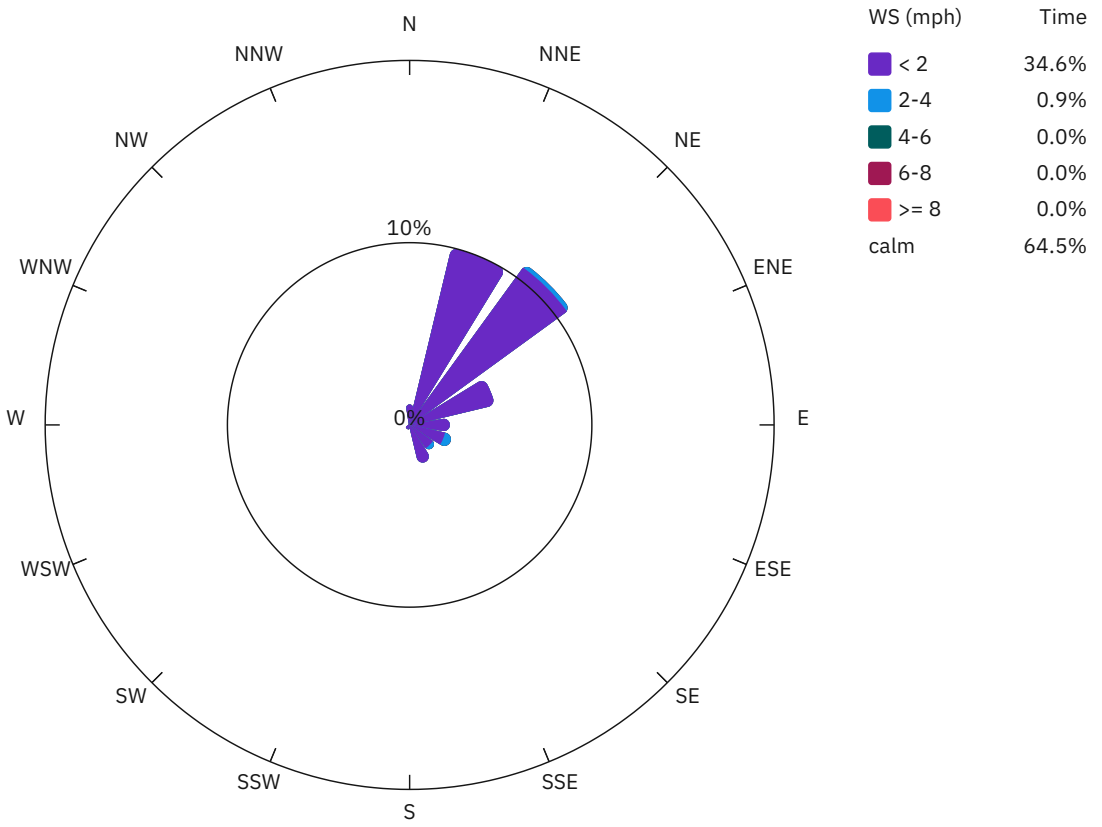

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/9/2026 07:00	6.2	5.1	0.0	0.0220	0.0280	0.0060	0.1	NE
10/9/2026 07:15	3.7	3.4	0.0	0.0207	0.0193	0.0000	0.3	SW
10/9/2026 07:30	4.0	3.7	0.0	0.0293	0.0207	0.0000	0.8	SW
10/9/2026 07:45	5.1	5.3	0.3	0.0313	0.0253	0.0000	0.1	NNW
10/9/2026 08:00	5.0	5.5	0.5	0.0307	0.0227	0.0000	0.1	NNW
10/9/2026 08:15	5.2	4.7	0.0	0.0227	0.0273	0.0047	0.3	NE
10/9/2026 08:30	4.3	4.1	0.0	0.0240	0.0260	0.0020	0.3	NNE
10/9/2026 08:45	5.3	4.8	0.0	0.0227	0.0253	0.0027	0.3	NE
10/9/2026 09:00	5.6	3.9	0.0	0.0187	0.0193	0.0007	0.6	NNE
10/9/2026 09:15	4.7	4.4	0.0	0.0200	0.0200	0.0000	0.5	NNE
10/9/2026 09:30	5.2	3.5	0.0	0.0187	0.0147	0.0000	0.5	NE
10/9/2026 09:45	4.5	3.8	0.0	0.0153	0.0127	0.0000	0.6	NNE
10/9/2026 10:00	4.7	4.0	0.0	0.0100	0.0073	0.0000	0.8	NNE
10/9/2026 10:15	5.7	6.9	1.2	0.0113	0.0033	0.0000	0.4	NE
10/9/2026 10:30	6.2	5.0	0.0	0.0087	0.0080	0.0000	0.8	NNE
10/9/2026 10:45	6.0	3.9	0.0	0.0187	0.0000	0.0000	0.7	NE
10/9/2026 11:00	5.9	9.0	3.1	0.0127	0.0027	0.0000	0.5	ESE
10/9/2026 11:15	4.8	5.4	0.6	0.0093	0.0020	0.0000	0.5	NE
10/9/2026 11:30	4.0	5.3	1.2	0.0093	0.0040	0.0000	0.5	NE
10/9/2026 11:45	3.1	3.3	0.2	0.0087	0.0013	0.0000	1.0	NE
10/9/2026 12:00	4.2	5.3	1.1	0.0093	0.0007	0.0000	1.0	NE
10/9/2026 12:15	5.8	4.3	0.0	0.0093	0.0007	0.0000	1.0	NE
10/9/2026 12:30	4.5	7.5	3.0	0.0093	0.0007	0.0000	1.0	E
10/9/2026 12:45	5.7	5.5	0.0	0.0093	0.0007	0.0000	1.2	NE
10/9/2026 13:00	9.6	15.4	5.8	0.0080	0.0020	0.0000	1.0	NE
10/9/2026 13:15							1.5	NE
10/9/2026 14:00	4.6	32.1	27.4	0.0100	0.0000	0.0000	0.9	E
10/9/2026 14:15	8.1	21.8	13.7	0.0087	0.0013	0.0000	0.9	E
10/9/2026 14:30	9.1	12.7	3.6	0.0100	0.0000	0.0000	1.0	NE
10/9/2026 14:45	15.0	6.8	0.0	0.0100	0.0000	0.0000	1.2	NE
10/9/2026 15:00	8.3	6.1	0.0	0.0087	0.0013	0.0000	1.0	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/9/2026 15:15	5.8	5.6	0.0	0.0087	0.0013	0.0000	0.9	NE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/12/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 60-72°F, Partly Cloudy RH: 66% Pres: 29.81” Wind: NNW @ 10-20 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco exported 5 trucks of soil from grids A3 and A4 from 4-8 feet below land surface (ft bls) to Keystone Trade Center, PA Permit # PAD090088 located at 1 Ben Fairless Drive, Morrisville, PA 19067.
- Glenco welded T bars and installed lagging along the northern boundary of the Site.
- Capstone drilled and installed steel casings for four SOE piles in the northwestern corner of the Site in grid A1.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Keystone Trade Center	5	82
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Allocco Recycling Corp.	0	17

Imported Material:

Facility	**Material Imported**	**CY Imported Today**	**Cumulative CY Imported**
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/12/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 60-72°F, Partly Cloudy RH: 66% Pres: 29.81” Wind: NNW @ 10-20 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Upcoming work activities anticipated:


- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/12/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 60-72°F, Partly Cloudy RH: 66% Pres: 29.81” Wind: NNW @ 10-20 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

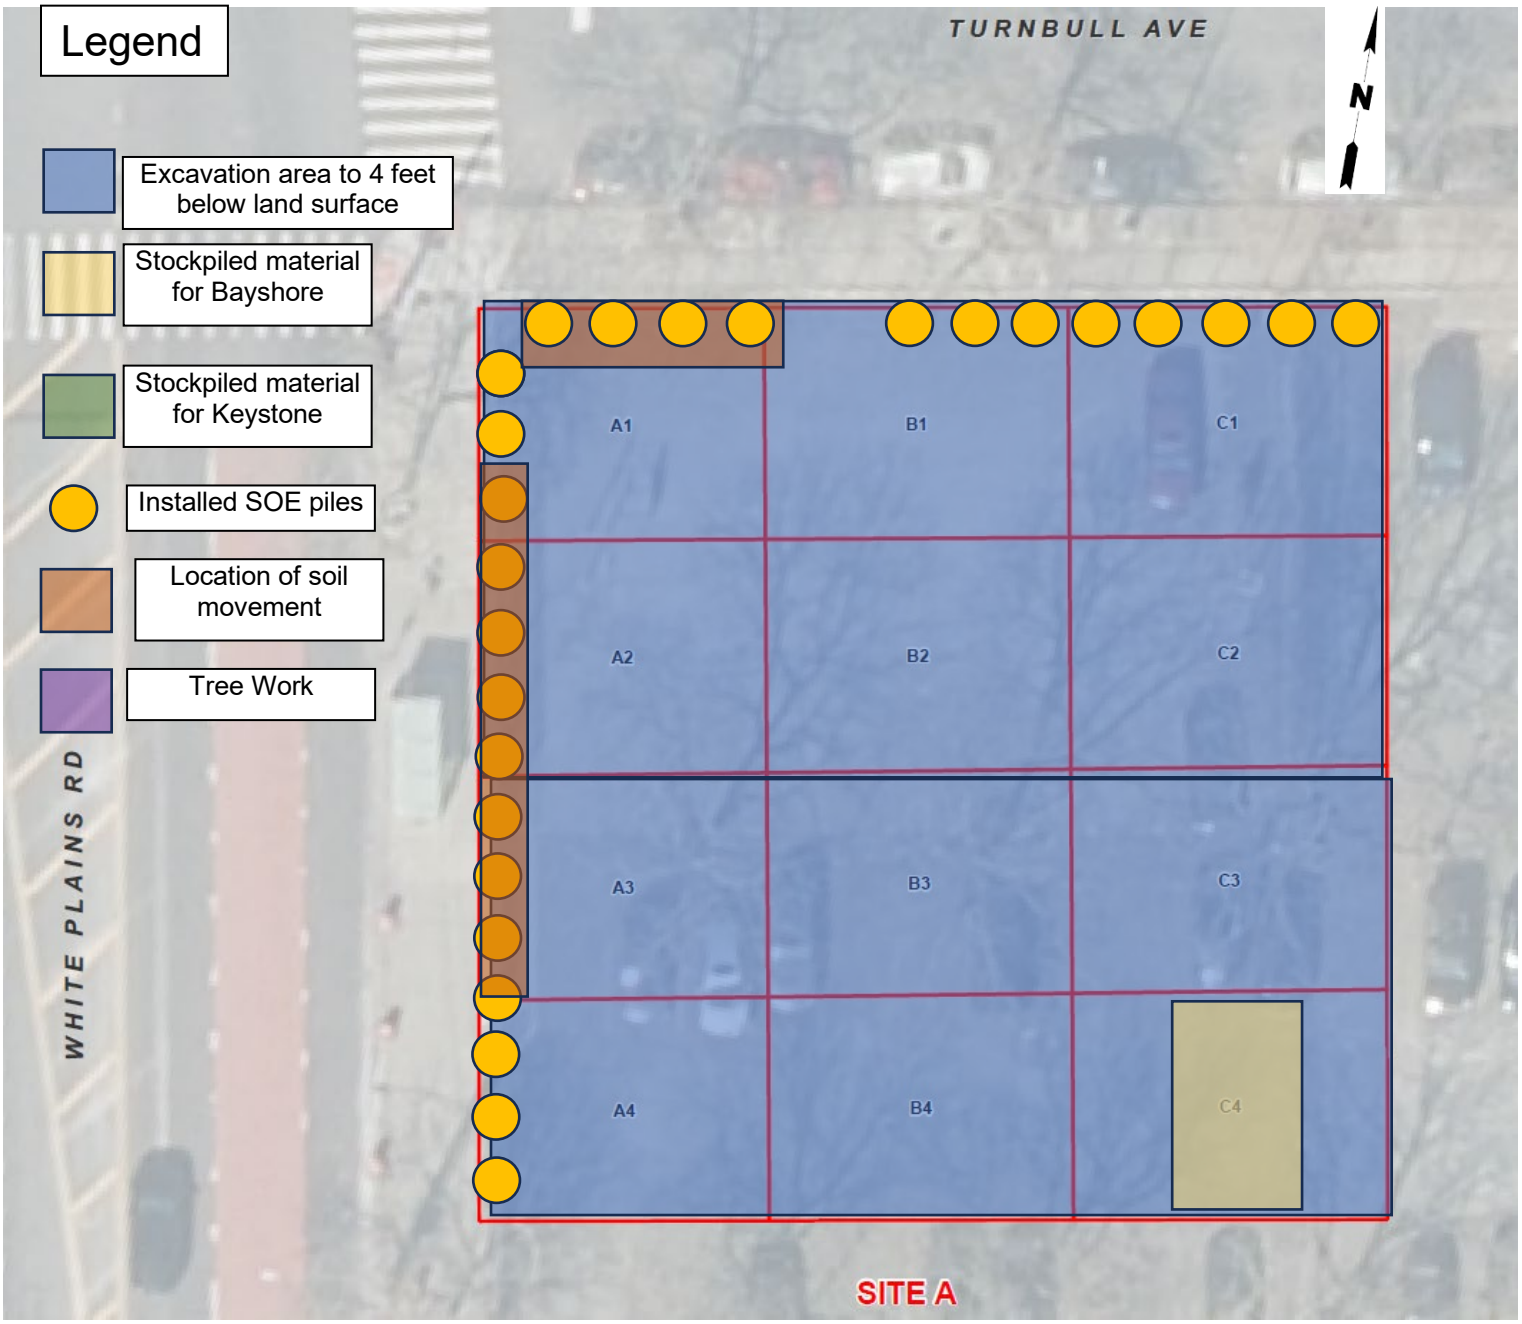

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/12/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 60-72°F, Partly Cloudy RH: 66% Pres: 29.81” Wind: NNW @ 10-20 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, view of Glenco loading truck with soil to be exported to Keystone Trade Center in Morrisville, PA .




Photo 2:
Facing west, view of Glenco washing truck tires prior to exiting the site.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/12/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 60-72°F, Partly Cloudy RH: 66% Pres: 29.81” Wind: NNW @ 10-20 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

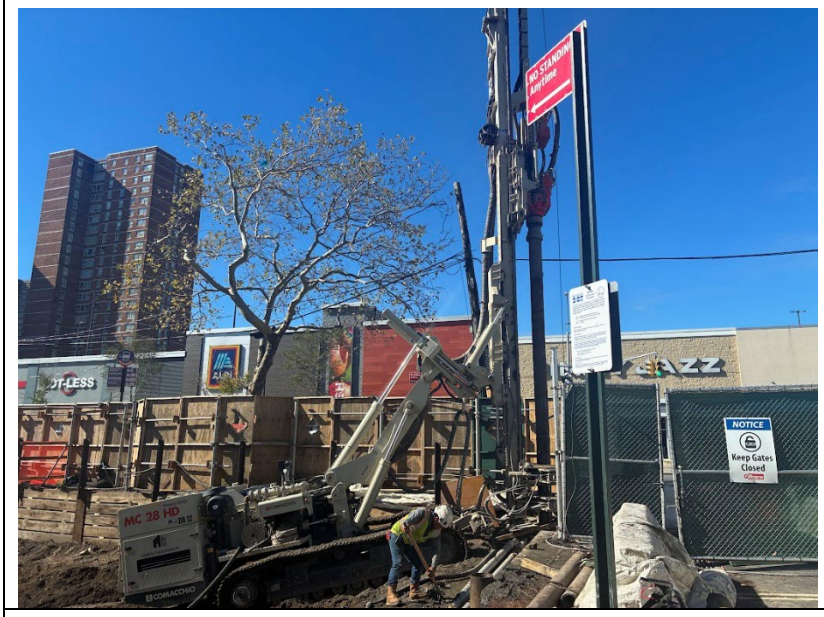	**Photo 3**: Facing west, view of Capstone drilling to install steel casing for SOE piles in the northern area of the Site
	**Photo 4:** Facing southeast, view of southeast CAMP station located within the southeast site corner.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/12/2026 07:00
		To: 10/12/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/12/2026	52.9 - 83.1	49.6 - 89.6	29.7 - 29.9	0.5 - 5.4	ENE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/12/2026	0.0	07:30	0.0000	07:30
Max Contribution (15 min avg.) - 10/12/2026	10.4	14:45	0.0027	07:15
Daily Avg. Contribution (15 min avg.) - 10/12/2026	1.1	-	0.0001	-

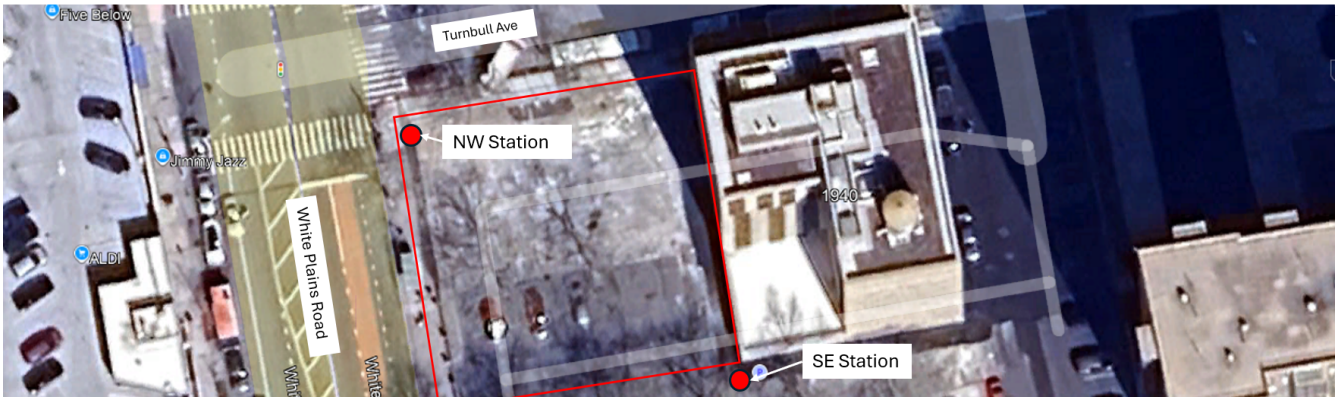


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

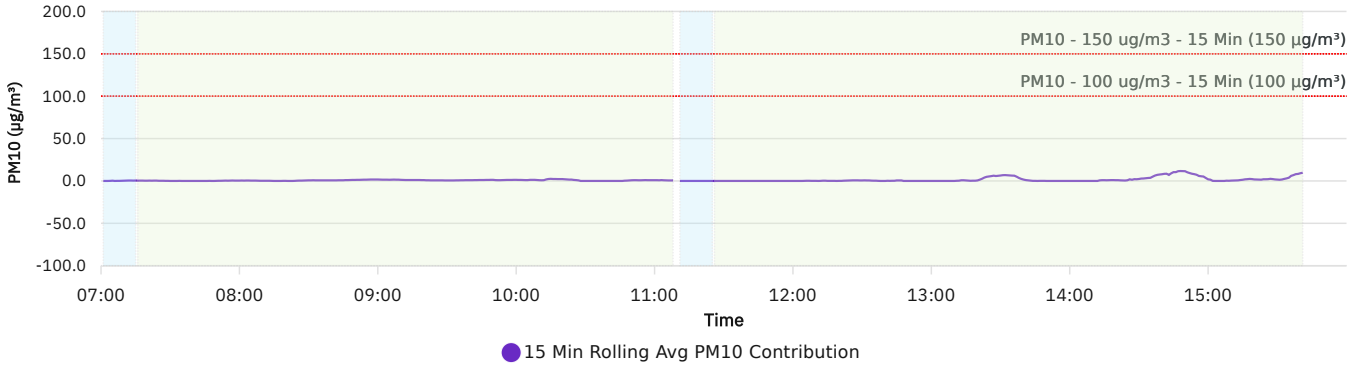

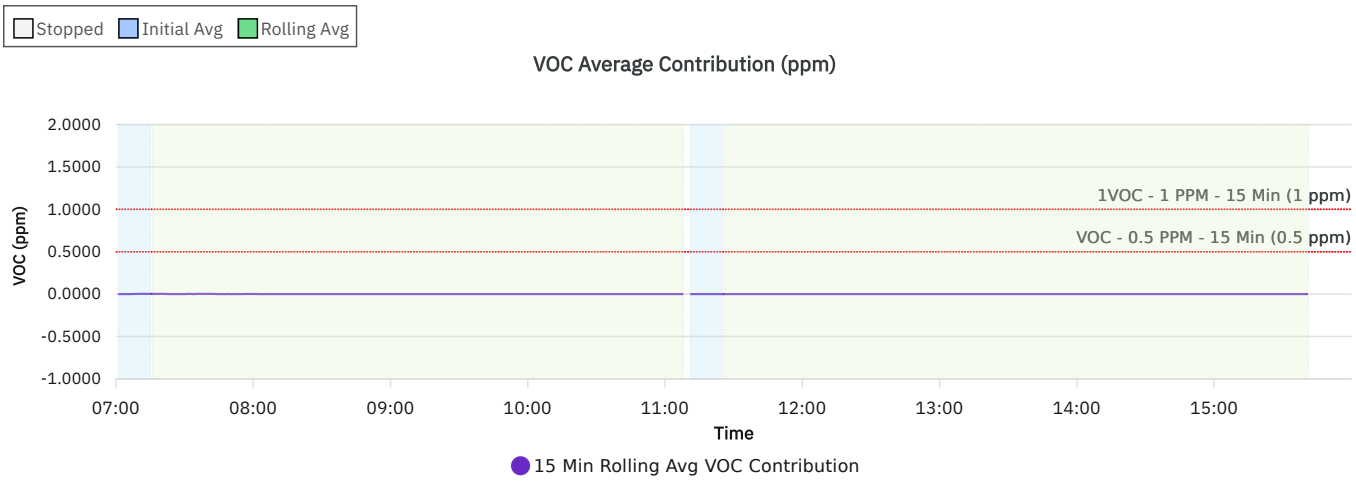

Wind rose (mph)

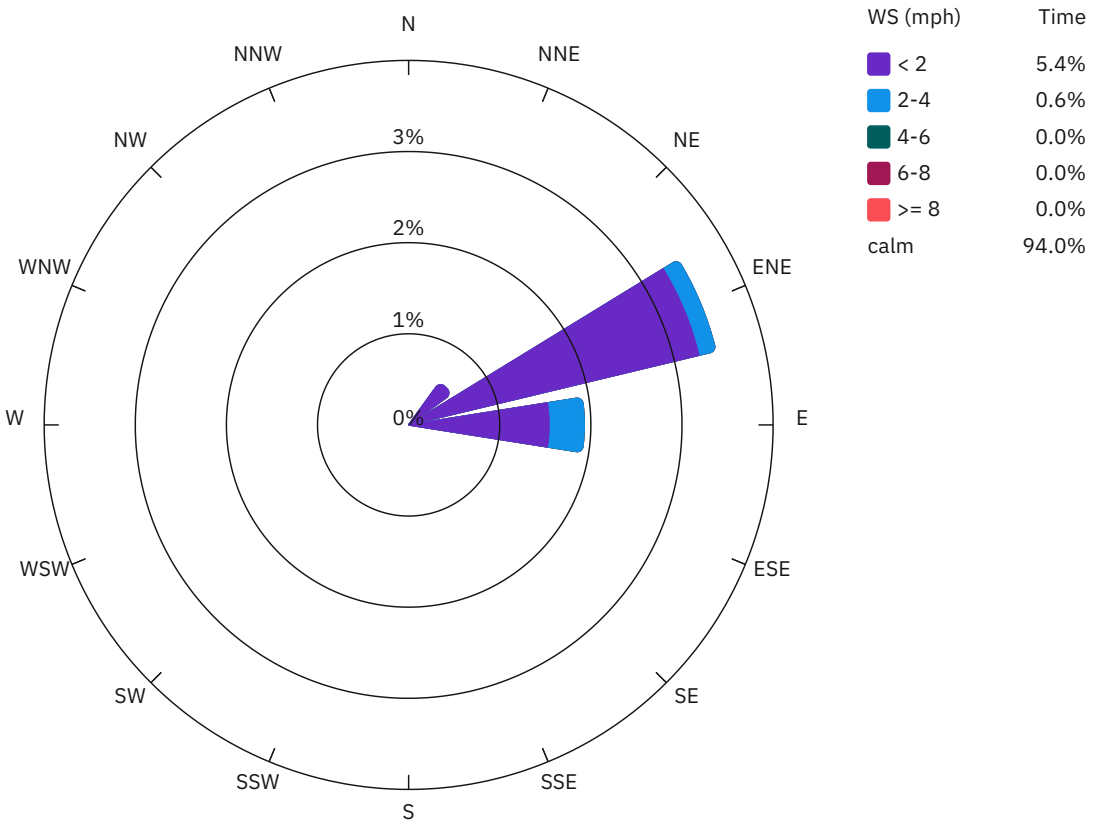

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/12/2026 07:15	1.1	1.5	0.5	0.0073	0.0100	0.0027	0.7	NE
10/12/2026 07:30	0.6	0.5	0.0	0.0107	0.0107	0.0000	0.5	NNE
10/12/2026 07:45	0.4	0.3	0.0	0.0160	0.0160	0.0000	0.5	NNE
10/12/2026 08:00	0.2	0.6	0.4	0.0100	0.0113	0.0013	0.5	NE
10/12/2026 08:15	0.3	0.3	0.0	0.0100	0.0100	0.0000	0.5	NNE
10/12/2026 08:30	0.2	0.9	0.7	0.0100	0.0060	0.0000	0.6	NE
10/12/2026 08:45	0.1	0.8	0.8	0.0093	0.0007	0.0000	0.7	ENE
10/12/2026 09:00	0.0	1.7	1.7	0.0100	0.0027	0.0000	0.6	ENE
10/12/2026 09:15	0.0	1.1	1.1	0.0100	0.0000	0.0000	0.7	ENE
10/12/2026 09:30	0.1	0.6	0.6	0.0107	0.0000	0.0000	0.9	ENE
10/12/2026 09:45	0.1	1.1	1.1	0.0113	0.0000	0.0000	0.5	ENE
10/12/2026 10:00	0.7	2.0	1.3	0.0100	0.0000	0.0000	0.7	ENE
10/12/2026 10:15	1.3	3.9	2.5	0.0100	0.0000	0.0000	0.7	ENE
10/12/2026 10:30	3.9	2.4	0.0	0.0093	0.0007	0.0000	0.4	ENE
10/12/2026 10:45	2.8	2.5	0.0	0.0167	0.0000	0.0000	0.5	ENE
10/12/2026 11:00	1.2	2.0	0.9	0.0100	0.0007	0.0000	0.5	ENE
10/12/2026 11:15	3.0	1.5	0.0	0.0100	0.0000	0.0000	0.6	NE
10/12/2026 11:30	4.3	2.5	0.0	0.0100	0.0000	0.0000	0.7	ENE
10/12/2026 11:45	2.2	2.2	0.0	0.0073	0.0027	0.0000	0.3	NNE
10/12/2026 12:00	3.6	3.3	0.0	0.0100	0.0053	0.0000	0.6	ENE
10/12/2026 12:15	2.8	2.9	0.1	0.0100	0.0000	0.0000	0.6	ENE
10/12/2026 12:30	2.7	3.2	0.6	0.0093	0.0007	0.0000	0.4	E
10/12/2026 12:45	2.9	3.5	0.6	0.0100	0.0000	0.0000	0.5	ENE
10/12/2026 13:00	4.6	3.5	0.0	0.0100	0.0000	0.0000	0.5	ENE
10/12/2026 13:15	3.9	4.5	0.6	0.0087	0.0013	0.0000	0.4	ENE
10/12/2026 13:30	4.0	10.4	6.4	0.0100	0.0000	0.0000	0.6	ENE
10/12/2026 13:45	4.2	4.3	0.1	0.0100	0.0027	0.0000	0.6	ENE
10/12/2026 14:00	2.9	2.2	0.0	0.0100	0.0000	0.0000	0.6	ENE
10/12/2026 14:15	3.8	4.7	0.9	0.0200	0.0000	0.0000	0.4	ENE
10/12/2026 14:30	5.5	7.8	2.3	0.0140	0.0000	0.0000	0.5	E
10/12/2026 14:45	4.6	15.1	10.4	0.0107	0.0000	0.0000	0.5	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/12/2026 15:00	3.8	5.7	1.9	0.0107	0.0000	0.0000	0.5	E
10/12/2026 15:15	3.5	4.9	1.4	0.0127	0.0000	0.0000	0.5	ENE
10/12/2026 15:30	3.6	5.2	1.6	0.0100	0.0007	0.0000	0.5	E

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/13/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 62-73°F, Partly Cloudy RH: 79% Pres: 29.89” Wind: SSE @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern boundary of the Site.
- Capstone drilled and installed steel casings for two SOE piles in the northwestern corner of the Site in grid A1.
- Glenco stockpiled concrete sidewalk debris from the northern portion of the site for future export offsite.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:45. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	82
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/13/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 62-73°F, Partly Cloudy RH: 79% Pres: 29.89” Wind: SSE @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Upcoming work activities anticipated:


- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing SOE piles.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/13/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 62-73°F, Partly Cloudy RH: 79% Pres: 29.89” Wind: SSE @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

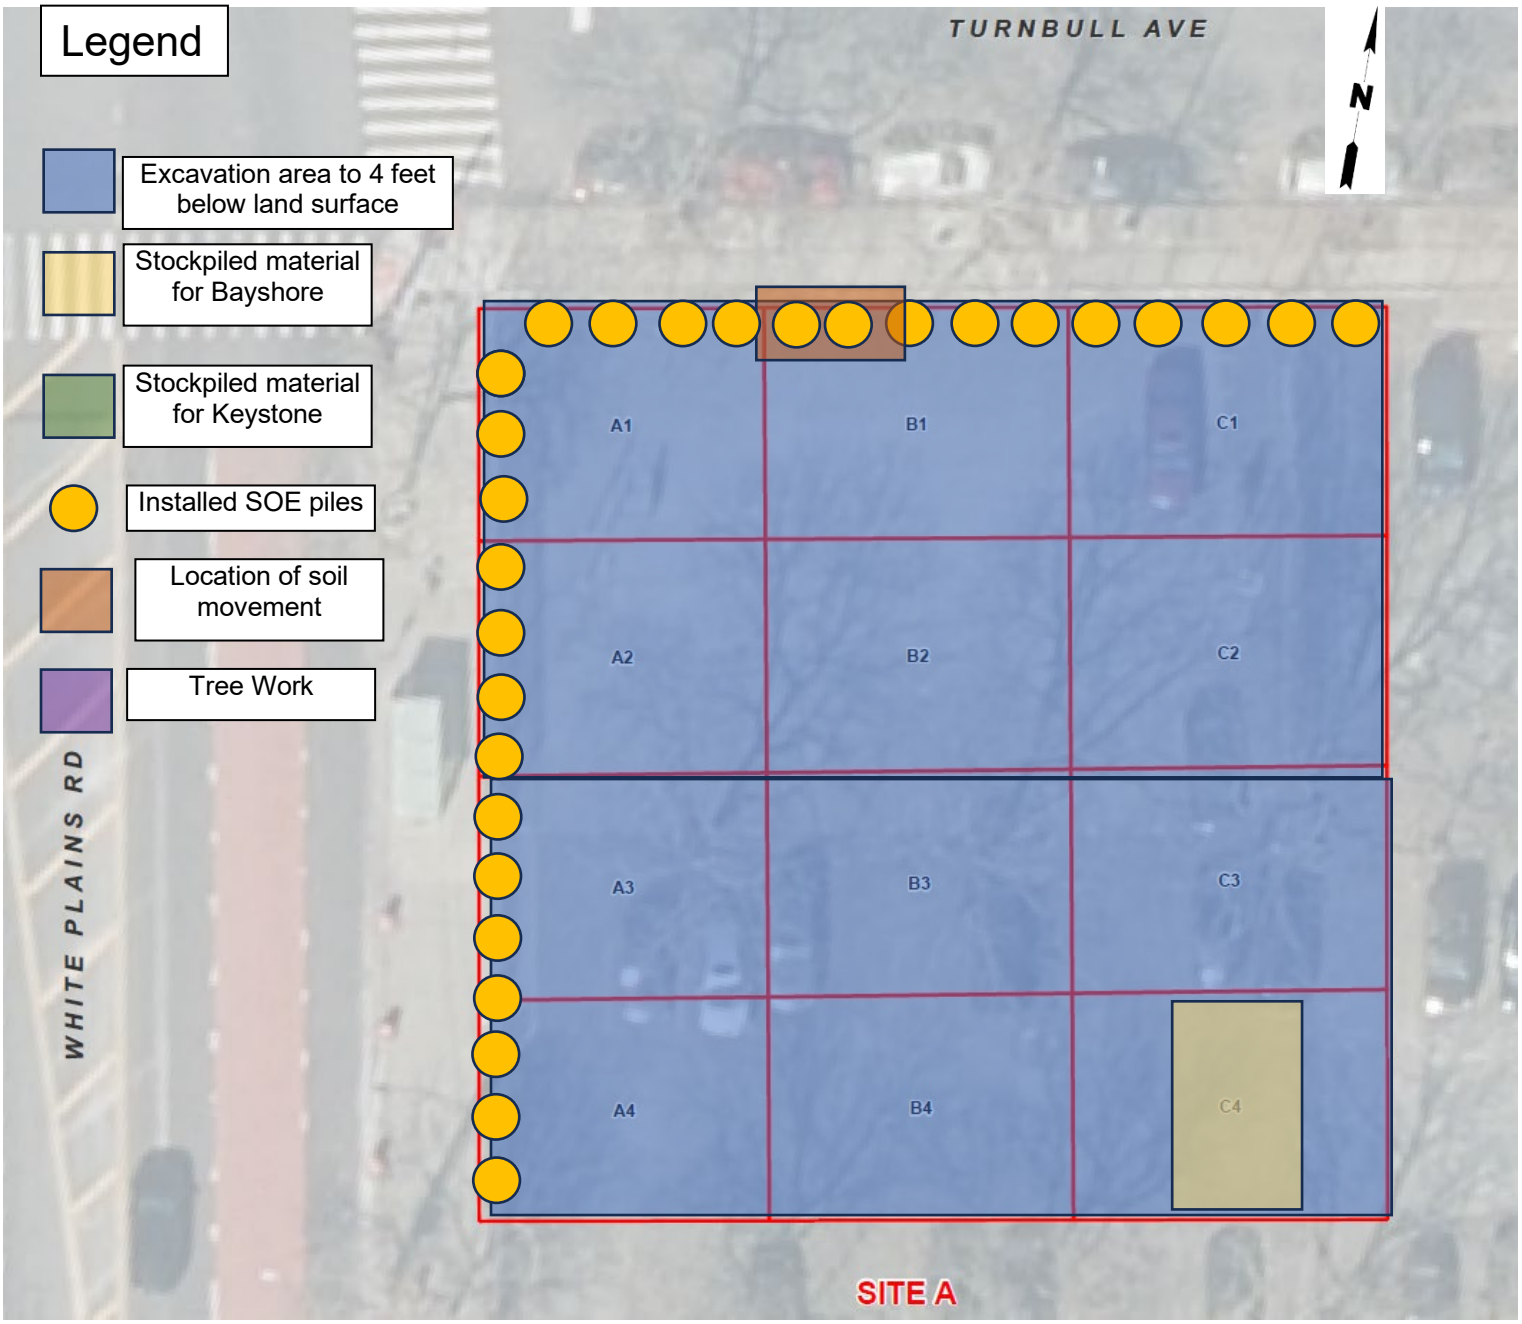

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/13/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 62-73°F, Partly Cloudy RH: 79% Pres: 29.89” Wind: SSE @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing northwest, view of Capstone drilling to install steel casing for SOE piles in the northern area of the Site



Photo 2:
Facing west, view of Glenco conducting general housekeeping.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/13/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 62-73°F, Partly Cloudy RH: 79% Pres: 29.89” Wind: SSE @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing north, Glenco installs lagging along SOE piles within the northern portion of the Site.

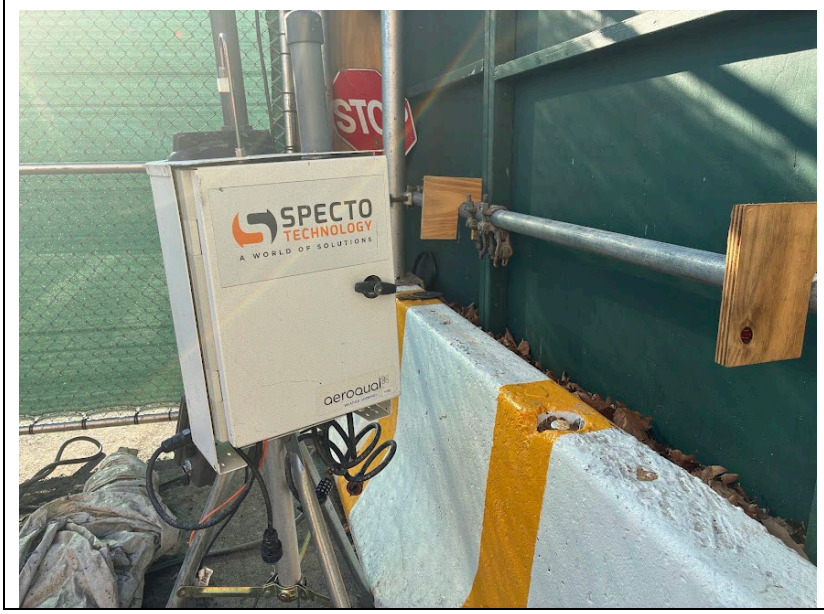


Photo 4: Facing west, view of northwest CAMP station located within the northwest site corner.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/13/2026 07:00
		To: 10/13/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/13/2026	54.7 - 77.7	52.9 - 85.1	29.9 - 30.0	0.3 - 7.0	SE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/13/2026	0.0	08:15	0.0000	09:45
Max Contribution (15 min avg.) - 10/13/2026	32.5	13:30	0.0733	08:00
Daily Avg. Contribution (15 min avg.) - 10/13/2026	6.0	-	0.0119	-

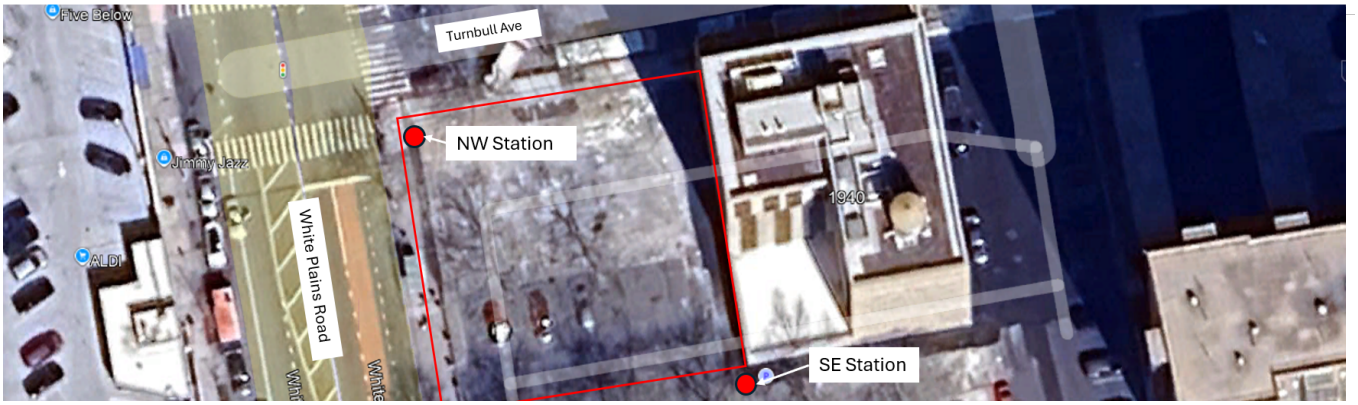


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

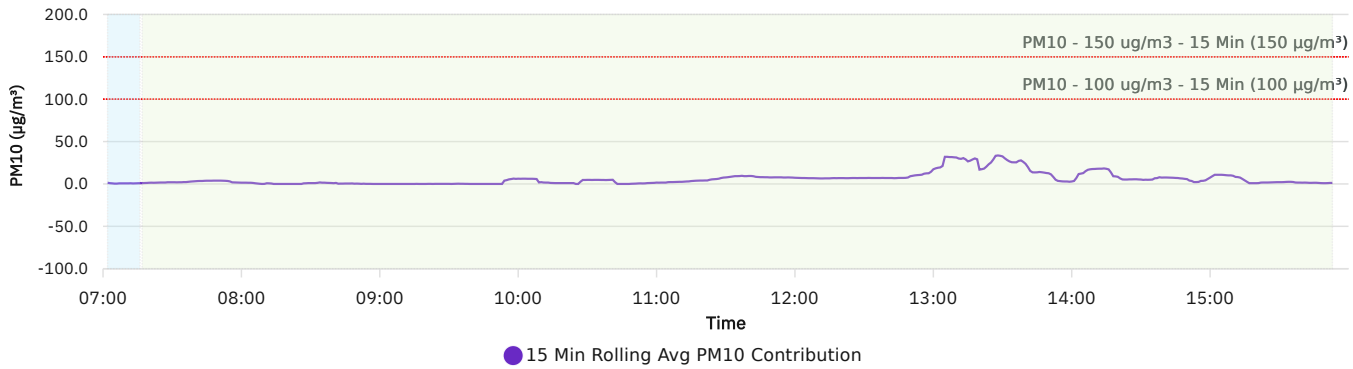

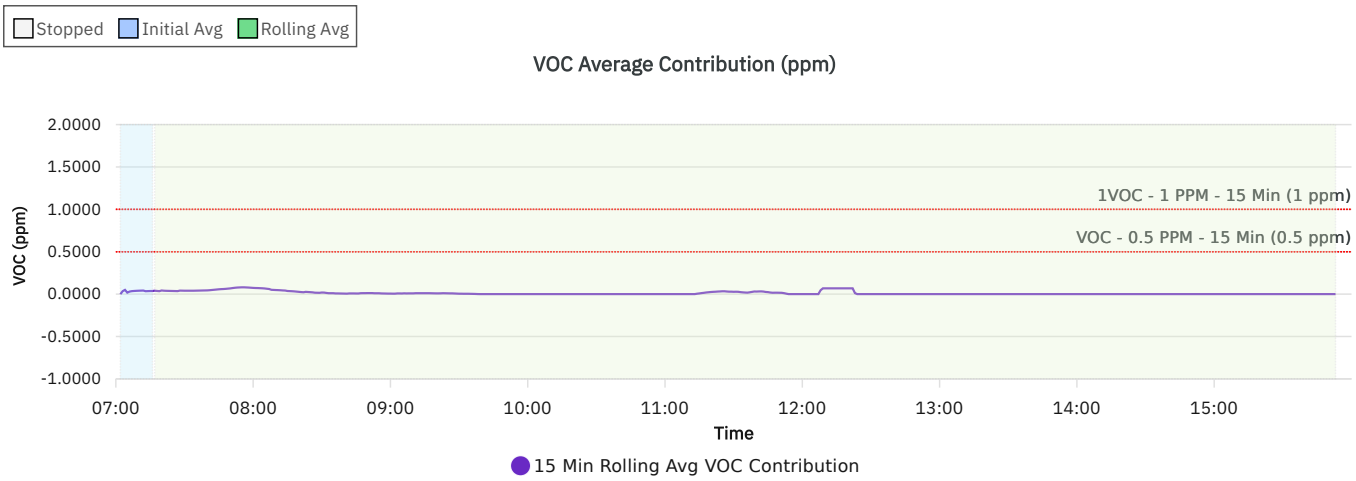

Wind rose (mph)

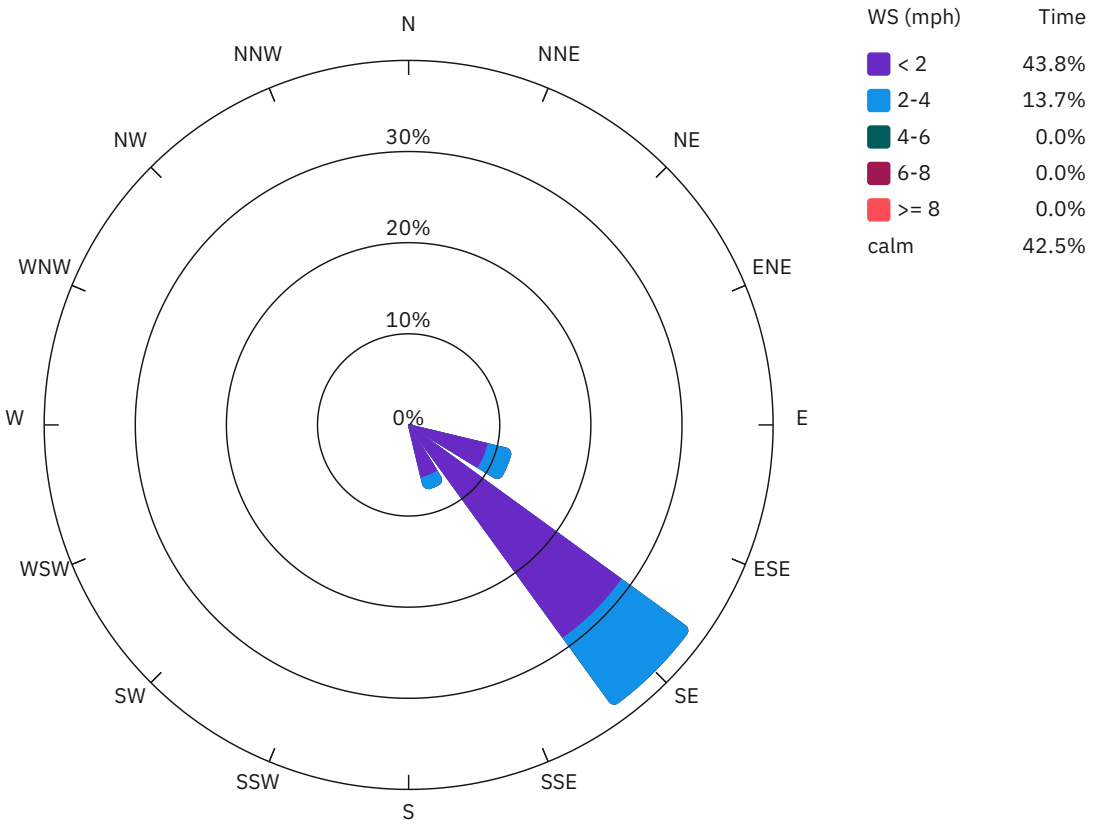

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/13/2026 07:15	8.8	9.6	0.8	0.0321	0.0686	0.0364	0.2	NE
10/13/2026 07:30	6.6	8.5	2.0	0.0300	0.0700	0.0400	0.2	NE
10/13/2026 07:45	6.6	10.4	3.8	0.0300	0.0867	0.0567	0.3	NE
10/13/2026 08:00	7.9	9.4	1.5	0.0313	0.1047	0.0733	0.2	NE
10/13/2026 08:15	9.0	8.9	0.0	0.0353	0.0720	0.0367	0.2	NNE
10/13/2026 08:30	7.4	8.4	1.0	0.0313	0.0500	0.0187	0.3	NE
10/13/2026 08:45	7.8	8.3	0.5	0.0353	0.0427	0.0073	0.2	NE
10/13/2026 09:00	9.8	9.4	0.0	0.0307	0.0367	0.0060	0.2	NE
10/13/2026 09:15	7.9	7.8	0.0	0.0227	0.0333	0.0107	0.3	NE
10/13/2026 09:30	6.8	6.9	0.1	0.0220	0.0267	0.0047	0.3	NE
10/13/2026 09:45	6.9	6.4	0.0	0.0220	0.0207	0.0000	0.3	ENE
10/13/2026 10:00	4.8	11.0	6.2	0.0207	0.0087	0.0000	0.5	ENE
10/13/2026 10:15	3.9	4.9	1.1	0.0180	0.0000	0.0000	0.5	ESE
10/13/2026 10:30	4.5	9.3	4.8	0.0160	0.0000	0.0000	0.4	ESE
10/13/2026 10:45	4.7	4.5	0.0	0.0173	0.0027	0.0000	0.7	SE
10/13/2026 11:00	4.4	6.0	1.6	0.0147	0.0013	0.0000	1.1	SE
10/13/2026 11:15	2.5	6.0	3.4	0.0100	0.0180	0.0080	1.7	SE
10/13/2026 11:30	1.8	9.5	7.7	0.0100	0.0373	0.0273	1.7	SE
10/13/2026 11:45	1.7	9.7	8.0	0.0100	0.0333	0.0233	1.6	SE
10/13/2026 12:00	1.5	8.9	7.3	0.0100	0.0027	0.0000	1.8	SE
10/13/2026 12:15	1.6	8.2	6.6	0.0100	0.0780	0.0680	1.7	SE
10/13/2026 12:30	1.3	8.4	7.0	0.0100	0.0000	0.0000	1.6	SE
10/13/2026 12:45	1.2	8.3	7.1	0.0100	0.0000	0.0000	1.5	SE
10/13/2026 13:00	1.1	18.4	17.3	0.0100	0.0000	0.0000	1.5	SE
10/13/2026 13:15	1.1	27.8	26.6	0.0100	0.0000	0.0000	2.0	SE
10/13/2026 13:30	1.1	33.6	32.5	0.0100	0.0000	0.0000	2.0	SE
10/13/2026 13:45	0.7	14.5	13.7	0.0100	0.0000	0.0000	2.1	SE
10/13/2026 14:00	0.9	3.7	2.9	0.0100	0.0000	0.0000	2.0	SE
10/13/2026 14:15	1.1	19.0	17.9	0.0100	0.0000	0.0000	1.6	SE
10/13/2026 14:30	1.0	6.2	5.2	0.0100	0.0000	0.0000	1.7	SE
10/13/2026 14:45	1.1	8.2	7.1	0.0100	0.0000	0.0000	1.7	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/13/2026 15:00	1.2	8.8	7.5	0.0100	0.0000	0.0000	1.6	SE
10/13/2026 15:15	1.9	6.0	4.2	0.0100	0.0000	0.0000	1.6	SE
10/13/2026 15:30	2.4	4.5	2.1	0.0100	0.0027	0.0000	1.6	SE
10/13/2026 15:45	2.3	3.7	1.4	0.0100	0.0000	0.0000	1.8	ESE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/15/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-65°F, Partly Cloudy RH: 59% Pres: 30.17” Wind: NNE @ 8-16 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern and western boundaries of the Site.
- Capstone grouted piles within southeastern and northern portion of the site
- Capstone prepared Hutte HBR 504 tieback rig for future tieback installation.
- Glenco excavated and stockpiled soil from grids A1, B1, A2, and B2 from 4-8 ft below sidewalk grade for future export to Keystone Trade Center.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Keystone Trade Center	0	82
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Allocco Recycling Corp.	0	17

Imported Material:

Facility	**Material Imported**	**CY Imported Today**	**Cumulative CY Imported**
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	0

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/15/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-65°F, Partly Cloudy RH: 59% Pres: 30.17” Wind: NNE @ 8-16 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will begin installing tiebacks along SOE.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/15/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-65°F, Partly Cloudy RH: 59% Pres: 30.17” Wind: NNE @ 8-16 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

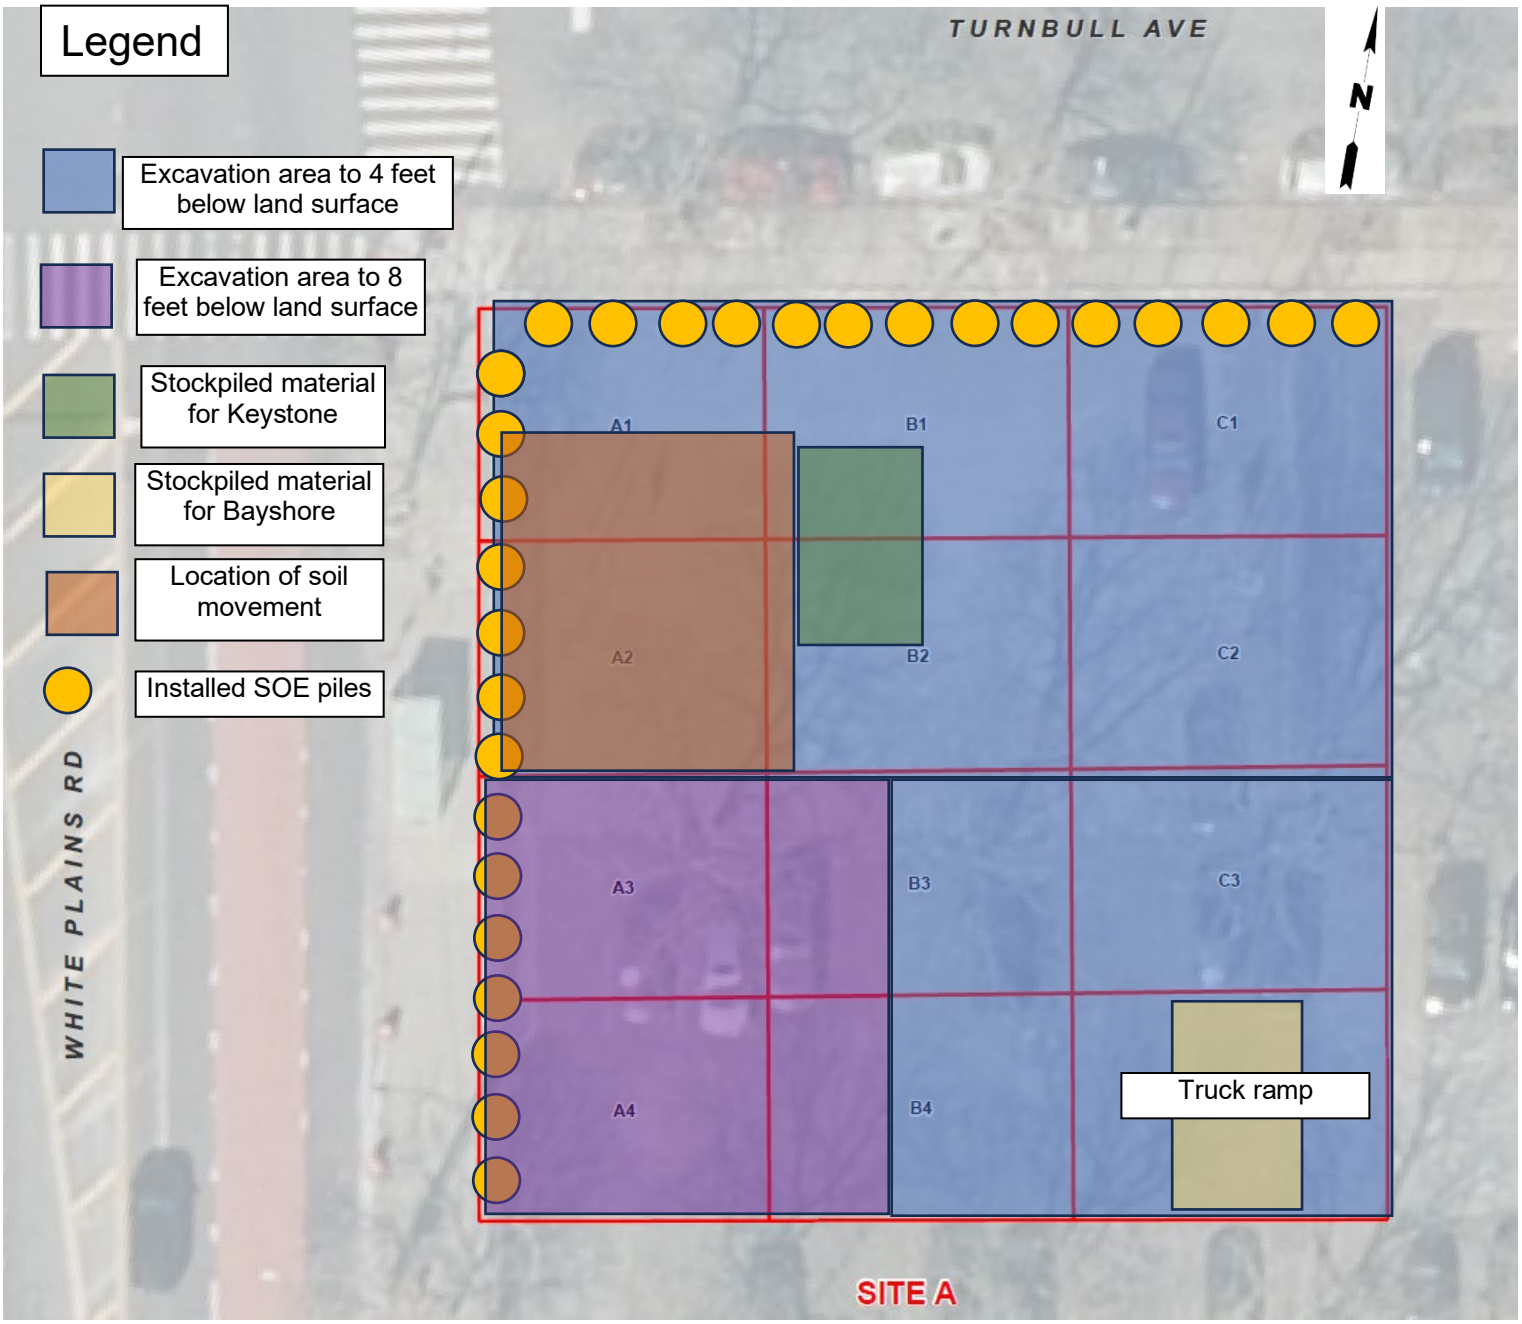

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/15/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-65°F, Partly Cloudy RH: 59% Pres: 30.17” Wind: NNE @ 8-16 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing northwest, view of Capstone grouting SOE piles in the northwestern portion of the Site



Photo 2:
Facing west, view of Glenco welding along SOE piles and installing lagging within the northwestern portion of the site.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/15/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-65°F, Partly Cloudy RH: 59% Pres: 30.17” Wind: NNE @ 8-16 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

	**Photo 3**: Facing northwest, Glenco ensures all stockpiles are covered with polyethylene sheeting at the conclusion of work activities.
	**Photo 4:** Facing north, view of southeast CAMP station located within the southeastern site corner.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/15/2026 07:00
		To: 10/15/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/15/2026	52.2 - 79.3	40.7 - 67.6	30.1 - 30.3	0.2 - 4.3	NE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/15/2026	0.0	07:15	0.0000	07:15
Max Contribution (15 min avg.) - 10/15/2026	15.5	15:15	0.0167	08:00
Daily Avg. Contribution (15 min avg.) - 10/15/2026	1.8	-	0.0030	-

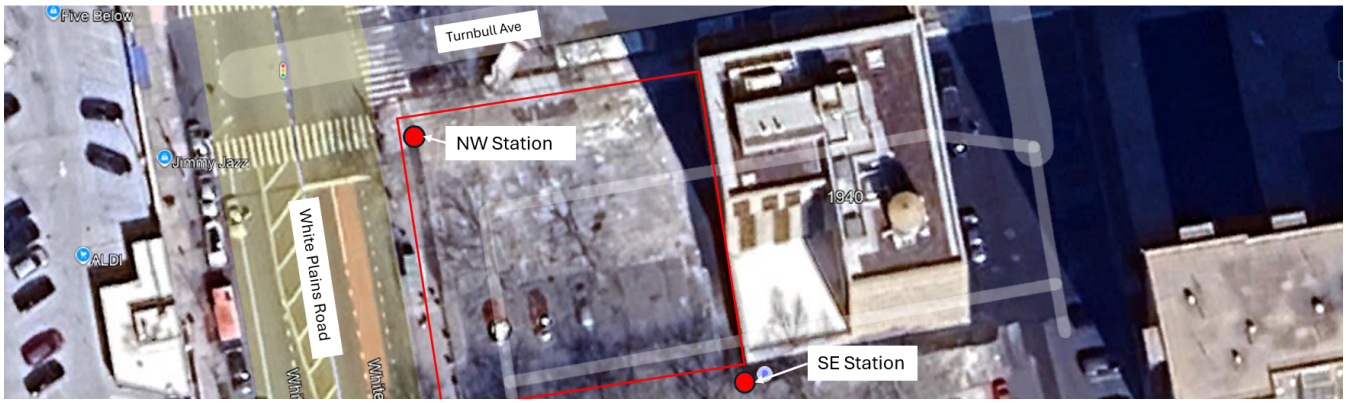


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

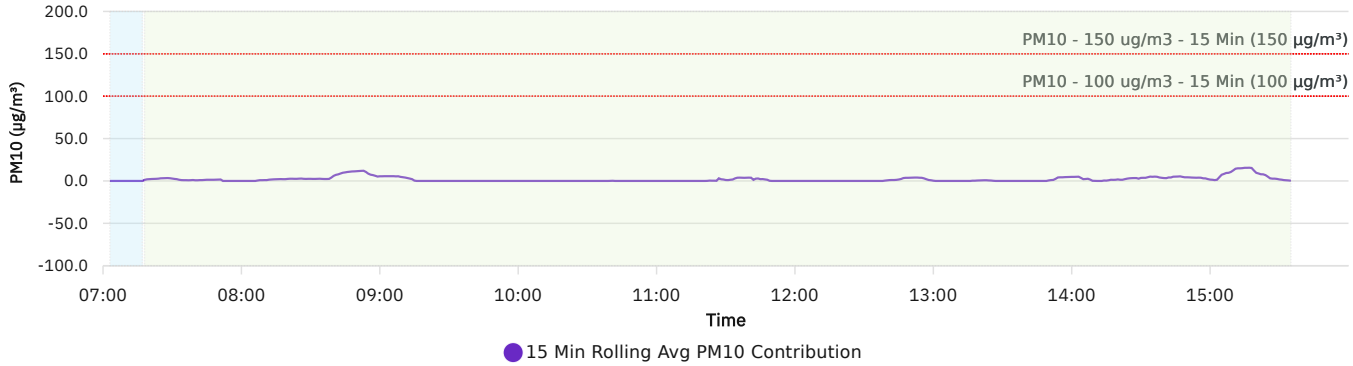

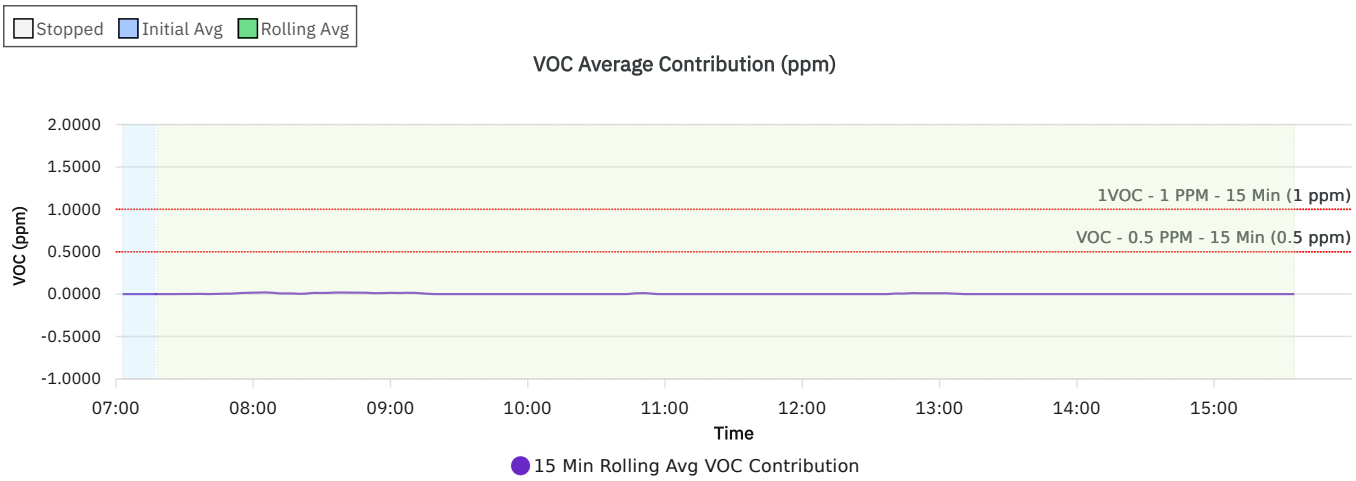

Wind rose (mph)

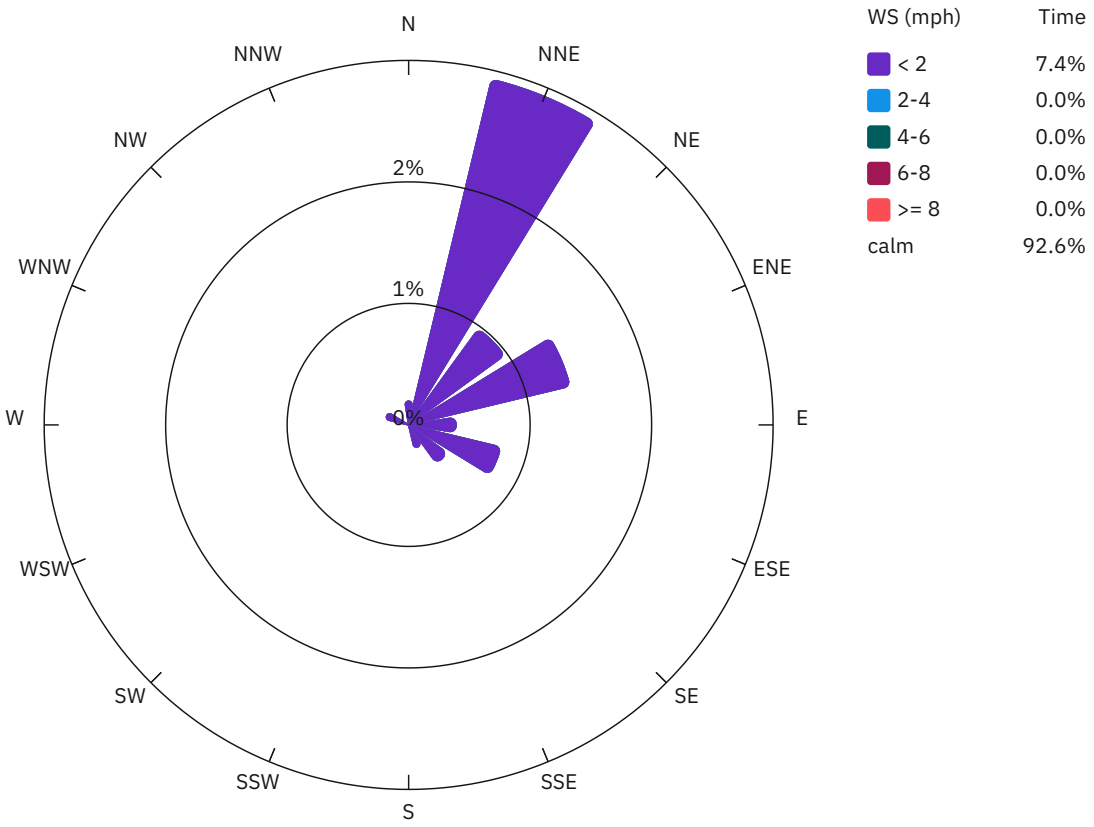

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/15/2026 07:15	2.7	1.9	0.0	0.0231	0.0085	0.0000	0.1	N
10/15/2026 07:30	1.1	3.8	2.8	0.0153	0.0167	0.0013	0.1	N
10/15/2026 07:45	0.9	2.2	1.4	0.0113	0.0147	0.0033	0.1	N
10/15/2026 08:00	3.3	1.9	0.0	0.0033	0.0200	0.0167	0.1	N
10/15/2026 08:15	1.3	3.3	2.0	0.0107	0.0187	0.0080	0.1	N
10/15/2026 08:30	1.3	3.8	2.5	0.0067	0.0200	0.0133	0.1	N
10/15/2026 08:45	2.0	12.1	10.1	0.0033	0.0200	0.0167	0.1	N
10/15/2026 09:00	1.8	7.3	5.5	0.0033	0.0180	0.0147	0.1	N
10/15/2026 09:15	3.6	4.0	0.4	0.0067	0.0127	0.0060	0.1	ENE
10/15/2026 09:30	8.0	2.4	0.0	0.0173	0.0027	0.0000	0.4	E
10/15/2026 09:45	4.3	2.9	0.0	0.0200	0.0000	0.0000	0.5	E
10/15/2026 10:00	5.3	1.6	0.0	0.0160	0.0053	0.0000	0.4	NE
10/15/2026 10:15	5.6	3.2	0.0	0.0140	0.0020	0.0000	0.9	NE
10/15/2026 10:30	7.2	5.0	0.0	0.0167	0.0020	0.0000	0.7	NE
10/15/2026 10:45	5.8	4.9	0.0	0.0080	0.0120	0.0040	1.4	NNE
10/15/2026 11:00	8.0	3.9	0.0	0.0113	0.0027	0.0000	0.2	ENE
10/15/2026 11:15	5.9	6.0	0.0	0.0073	0.0047	0.0000	0.3	NNE
10/15/2026 11:30	4.6	5.8	1.1	0.0080	0.0033	0.0000	0.4	NE
10/15/2026 11:45	4.2	6.2	2.1	0.0100	0.0007	0.0000	0.5	ENE
10/15/2026 12:00	4.0	2.6	0.0	0.0100	0.0000	0.0000	0.5	ENE
10/15/2026 12:15	2.9	2.2	0.0	0.0087	0.0040	0.0000	0.5	NNE
10/15/2026 12:30	2.8	1.6	0.0	0.0147	0.0033	0.0000	0.5	NE
10/15/2026 12:45	1.6	3.3	1.7	0.0027	0.0100	0.0073	0.5	N
10/15/2026 13:00	4.5	4.8	0.3	0.0000	0.0100	0.0100	0.6	NNW
10/15/2026 13:15	3.5	2.9	0.0	0.0073	0.0040	0.0000	0.3	NNE
10/15/2026 13:30	3.1	2.1	0.0	0.0087	0.0020	0.0000	0.6	ENE
10/15/2026 13:45	4.0	1.1	0.0	0.0107	0.0000	0.0000	0.9	ENE
10/15/2026 14:00	2.4	7.2	4.8	0.0113	0.0000	0.0000	0.9	ENE
10/15/2026 14:15	3.3	3.7	0.4	0.0120	0.0000	0.0000	0.9	ENE
10/15/2026 14:30	3.2	6.8	3.6	0.0113	0.0000	0.0000	0.9	ENE
10/15/2026 14:45	3.0	8.1	5.1	0.0100	0.0000	0.0000	0.9	ENE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/15/2026 15:00	3.2	4.8	1.6	0.0100	0.0000	0.0000	0.9	ENE
10/15/2026 15:15	1.4	16.9	15.5	0.0140	0.0000	0.0000	0.9	ENE
10/15/2026 15:30	1.2	2.9	1.8	0.0107	0.0000	0.0000	0.9	ESE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/16/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 51-75°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern and western boundaries of the Site.
- Capstone began tieback installation along the SOE piles.
- Glenco excavated and stockpiled soil from grids A1, B1, A2, and B2 from 4-8 ft below sidewalk grade for future export to Keystone Trade Center.
- Glenco excavated and stockpiled soil from grids B1 and C1 from 4-8 ft below sidewalk grade for future export to Bayshore Soil Management, LLC.
- Glenco received one truckload of 2 ½” crushed stone from Haledon Quarry, mine registration # 004864 to replenish truck pad for washing.
- Glenco exported 13 trucks of soil from grids A1, B1, A2, B2, and B3 from 4-8 feet below land surface (ft bls) to Keystone Trade Center, PA Permit # PAD090088 located at 1 Ben Fairless Drive, Morrisville, PA 19067.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:15. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	13	95
Bayshore Soil Management, LLC	0	46
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/16/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 51-75°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	20	20

Sampling Performed:

None.

Upcoming work activities anticipated:


- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks along SOE.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/16/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 51-75°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

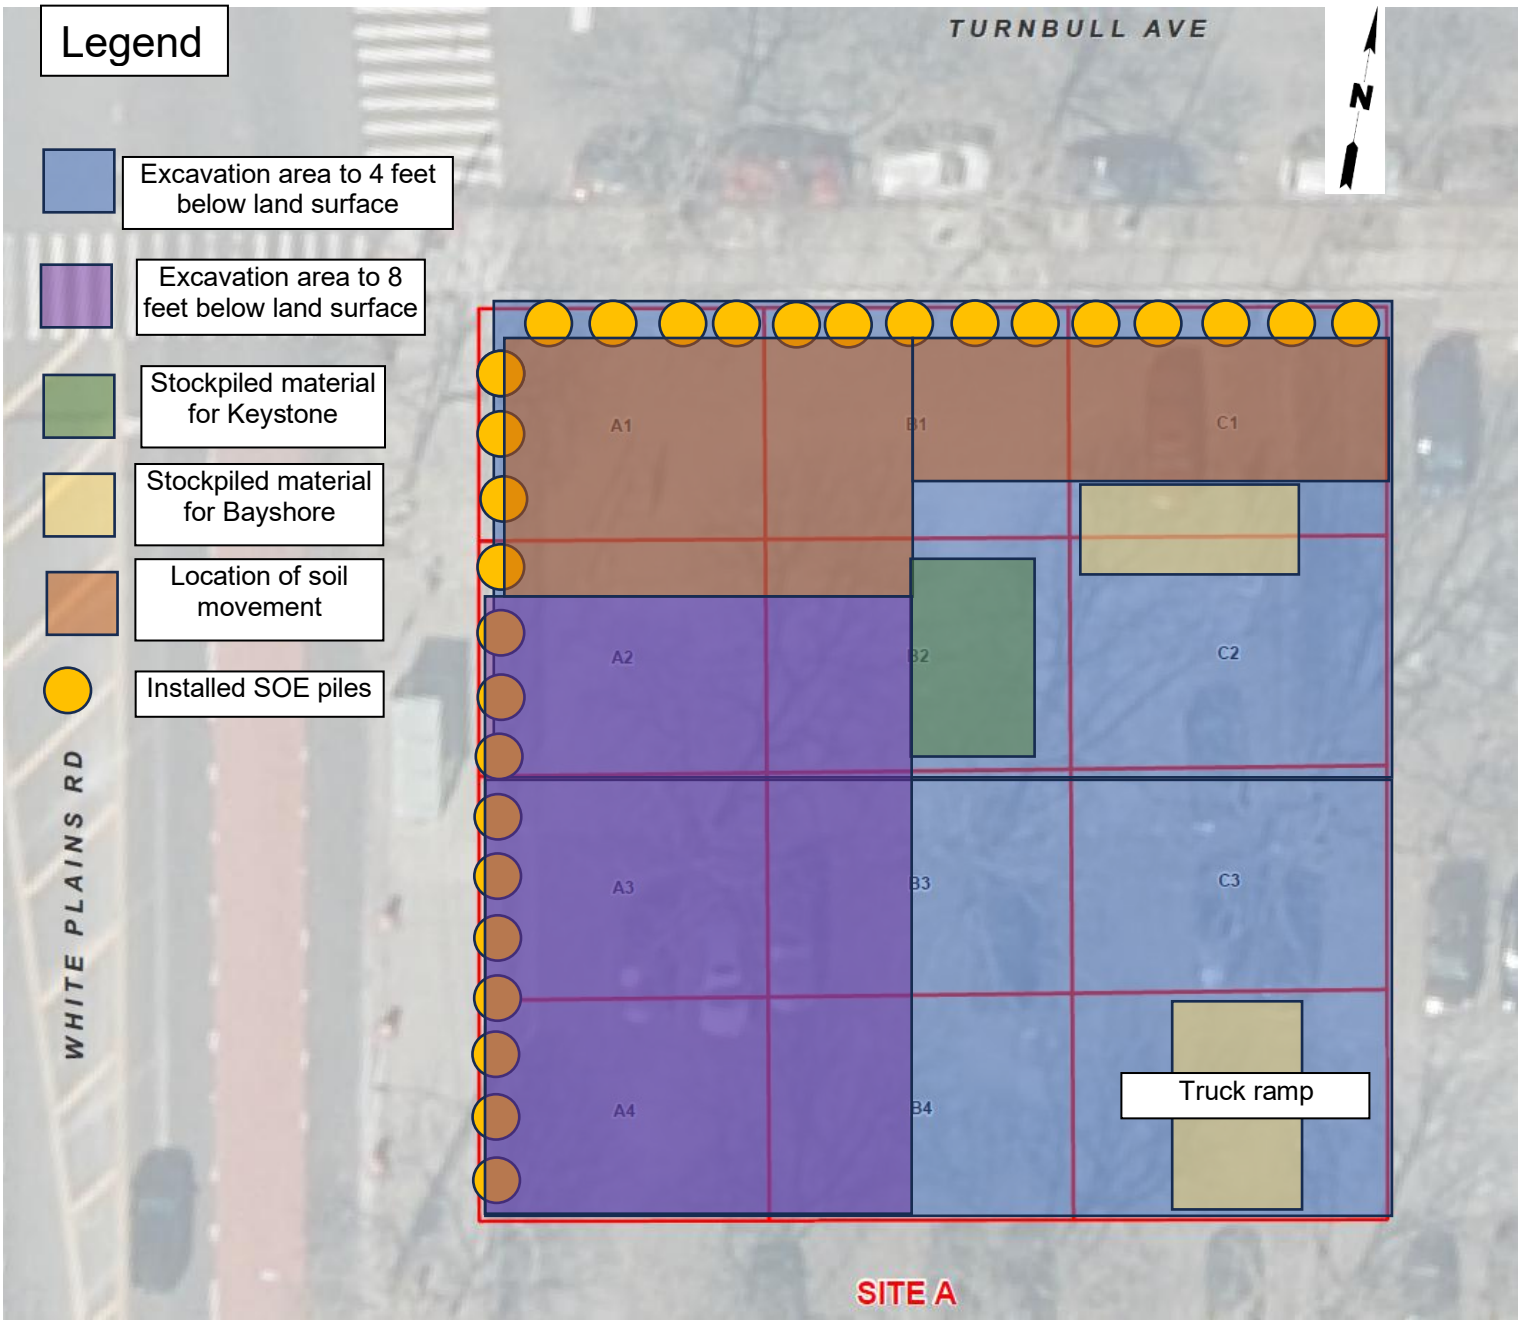

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/16/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 51-75°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Glenco loads truck with material to be exported to Keystone Trade Center.



Photo 2:
Facing west, Glenco ensures all trucks are properly washed prior to exiting the site.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/16/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 51-75°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

	**Photo 3**: Facing northwest, Capstone begins installing tiebacks along the SOE on the western portion of the site.
	**Photo 4:** Facing northwest, Glenco ensures all stockpiles are covered with polyethylene sheeting at the conclusion of work activities.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**


ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/16/2026 07:00
		To: 10/16/2026 16:00


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/16/2026	59.7 - 72.5	68.0 - 81.6	29.6 - 30.0	1.0 - 5.1	ESE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/16/2026	0.2	10:30	0.0000	07:30
Max Contribution (15 min avg.) - 10/16/2026	12.2	14:30	0.0133	07:15
Daily Avg. Contribution (15 min avg.) - 10/16/2026	3.4	-	0.0004	-

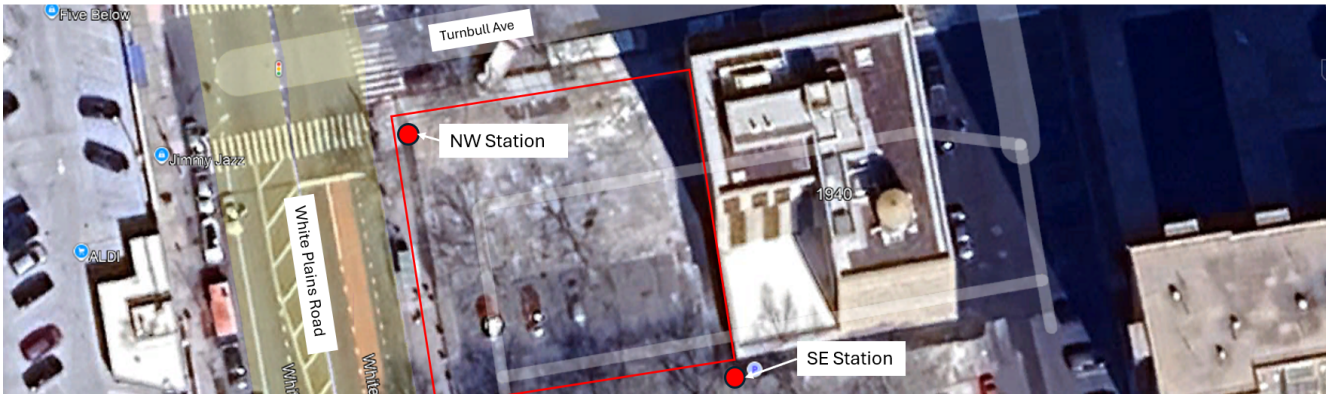

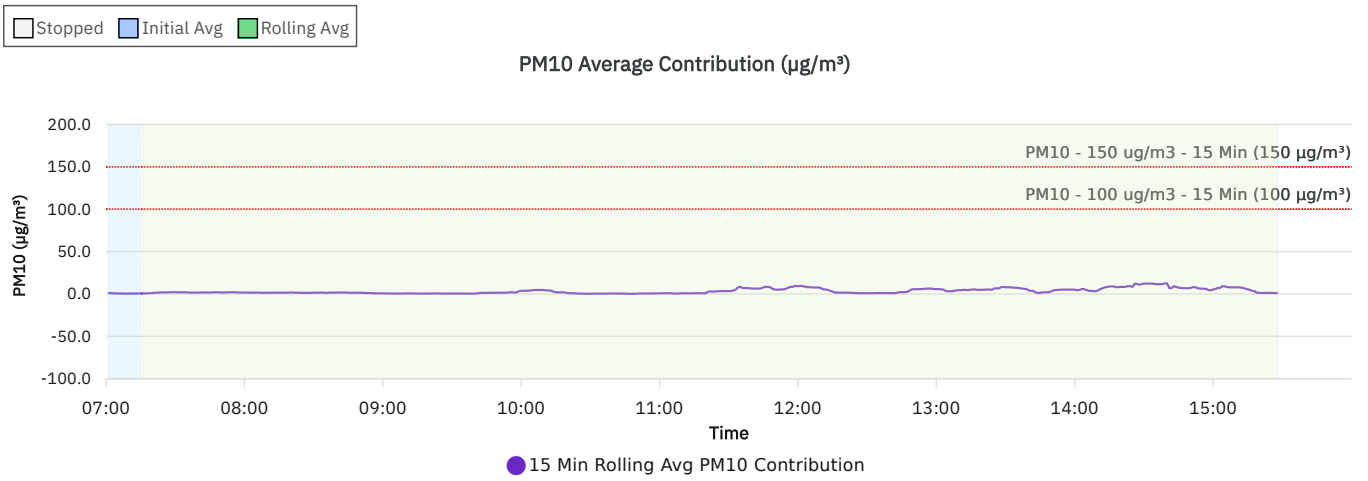

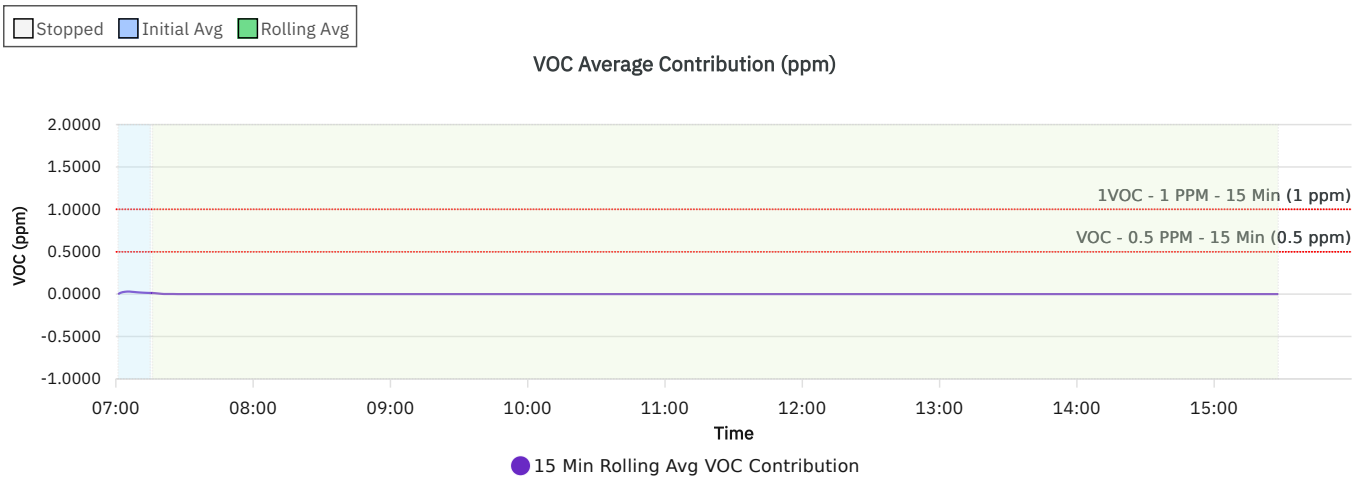

Wind rose (mph)

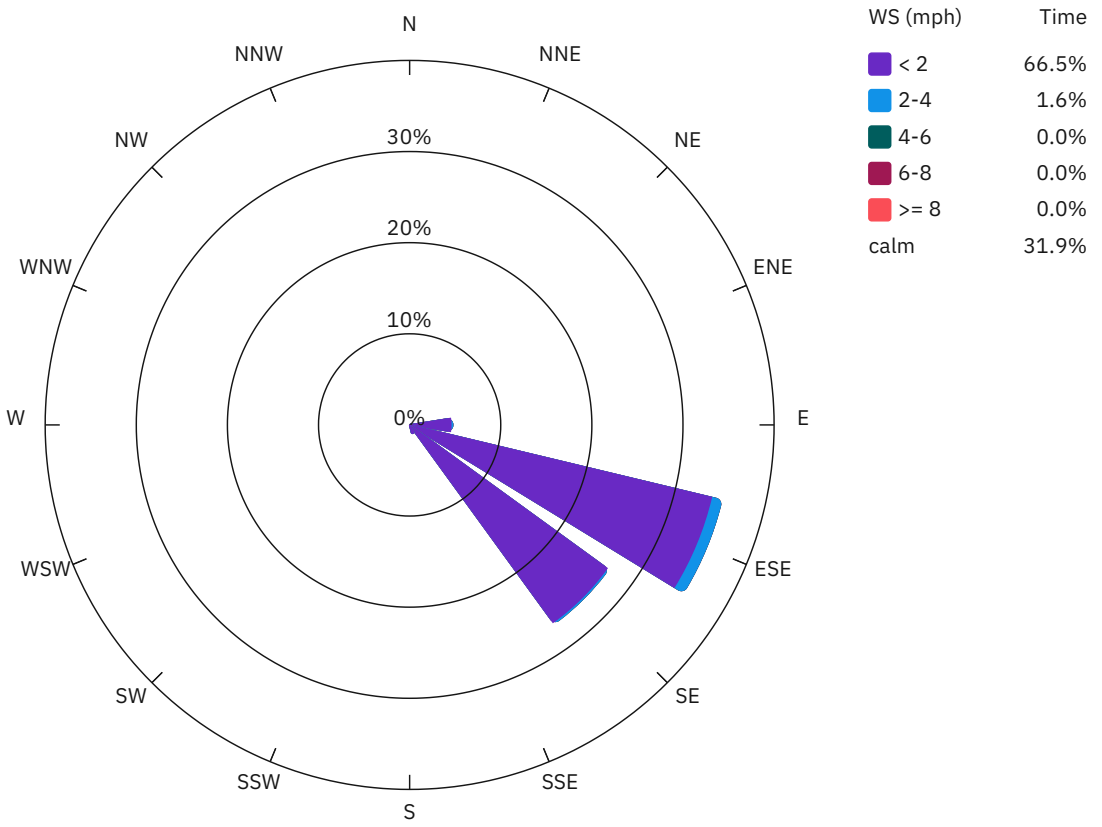

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/16/2026 07:15	3.6	4.2	0.6	0.0067	0.0200	0.0133	1.3	ESE
10/16/2026 07:30	2.6	4.7	2.1	0.0127	0.0113	0.0000	1.2	ESE
10/16/2026 07:45	2.5	4.2	1.7	0.0140	0.0100	0.0000	1.2	SE
10/16/2026 08:00	2.9	4.5	1.6	0.0113	0.0093	0.0000	1.2	SE
10/16/2026 08:15	2.9	4.5	1.5	0.0100	0.0000	0.0000	1.3	SE
10/16/2026 08:30	3.9	5.4	1.5	0.0120	0.0000	0.0000	1.0	ESE
10/16/2026 08:45	3.2	4.7	1.5	0.0100	0.0000	0.0000	1.0	ESE
10/16/2026 09:00	3.1	3.8	0.7	0.0100	0.0000	0.0000	1.1	ESE
10/16/2026 09:15	2.9	3.4	0.4	0.0100	0.0000	0.0000	1.1	SE
10/16/2026 09:30	3.0	3.5	0.5	0.0100	0.0000	0.0000	1.1	ESE
10/16/2026 09:45	3.3	4.6	1.3	0.0100	0.0000	0.0000	1.2	ESE
10/16/2026 10:00	3.5	7.3	3.7	0.0107	0.0000	0.0000	1.2	SE
10/16/2026 10:15	3.7	5.7	2.0	0.0100	0.0000	0.0000	1.2	ESE
10/16/2026 10:30	4.2	4.4	0.2	0.0100	0.0000	0.0000	1.3	ESE
10/16/2026 10:45	4.7	5.2	0.4	0.0100	0.0000	0.0000	1.4	ESE
10/16/2026 11:00	5.1	5.8	0.7	0.0107	0.0000	0.0000	1.1	ESE
10/16/2026 11:15	4.6	5.5	0.8	0.0100	0.0000	0.0000	1.5	ESE
10/16/2026 11:30	4.6	8.0	3.4	0.0100	0.0013	0.0000	1.1	ESE
10/16/2026 11:45	4.7	12.4	7.7	0.0100	0.0013	0.0000	0.9	SE
10/16/2026 12:00	5.0	14.2	9.2	0.0100	0.0047	0.0000	0.9	SE
10/16/2026 12:15	5.1	7.9	2.8	0.0107	0.0060	0.0000	0.8	ESE
10/16/2026 12:30	5.0	5.8	0.9	0.0133	0.0000	0.0000	1.1	ESE
10/16/2026 12:45	5.5	7.6	2.1	0.0147	0.0013	0.0000	0.9	ESE
10/16/2026 13:00	6.1	11.9	5.7	0.0200	0.0000	0.0000	1.0	ESE
10/16/2026 13:15	6.6	11.7	5.1	0.0200	0.0000	0.0000	1.1	ESE
10/16/2026 13:30	7.3	15.2	7.9	0.0200	0.0093	0.0000	0.8	ESE
10/16/2026 13:45	8.1	9.4	1.3	0.0200	0.0027	0.0000	1.5	SE
10/16/2026 14:00	9.0	13.9	5.0	0.0200	0.0000	0.0000	1.1	SE
10/16/2026 14:15	9.7	18.5	8.7	0.0200	0.0000	0.0000	1.0	ESE
10/16/2026 14:30	10.6	22.7	12.2	0.0200	0.0053	0.0000	0.9	ESE
10/16/2026 14:45	11.7	19.1	7.4	0.0200	0.0020	0.0000	1.1	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/16/2026 15:00	12.9	18.1	5.2	0.0200	0.0000	0.0000	0.9	ESE
10/16/2026 15:15	12.8	18.3	5.5	0.0200	0.0000	0.0000	0.9	E

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/19/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 41-64°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern boundary of the Site.
- Capstone continued tieback installation along the SOE piles.
- Glenco excavated and stockpiled soil from grids A1, B1, A2, and B2 from 4-8 ft below sidewalk grade for future export to Keystone Trade Center.
- Glenco exported 5 trucks of soil from grids A1, B1, A2, B2, and B3 from 4-8 feet below land surface (ft bls) to Keystone Trade Center, PA Permit # PAD090088 located at 1 Ben Fairless Drive, Morrisville, PA 19067.
- Glenco exported 15 trucks of soil from grids B1, C1, B2, and C2 to Bayshore Soil Management, LLC Class B registration No. CBG210002 located at 75 Crow Mill Rd., Keasbey, NJ 08832.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:30. No exceedances of volatile organic compound (VOC) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	5	100
Bayshore Soil Management, LLC	15	61
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/19/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 41-64°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks along SOE.
- Glenco will continue to install lagging and T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/19/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 41-64°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

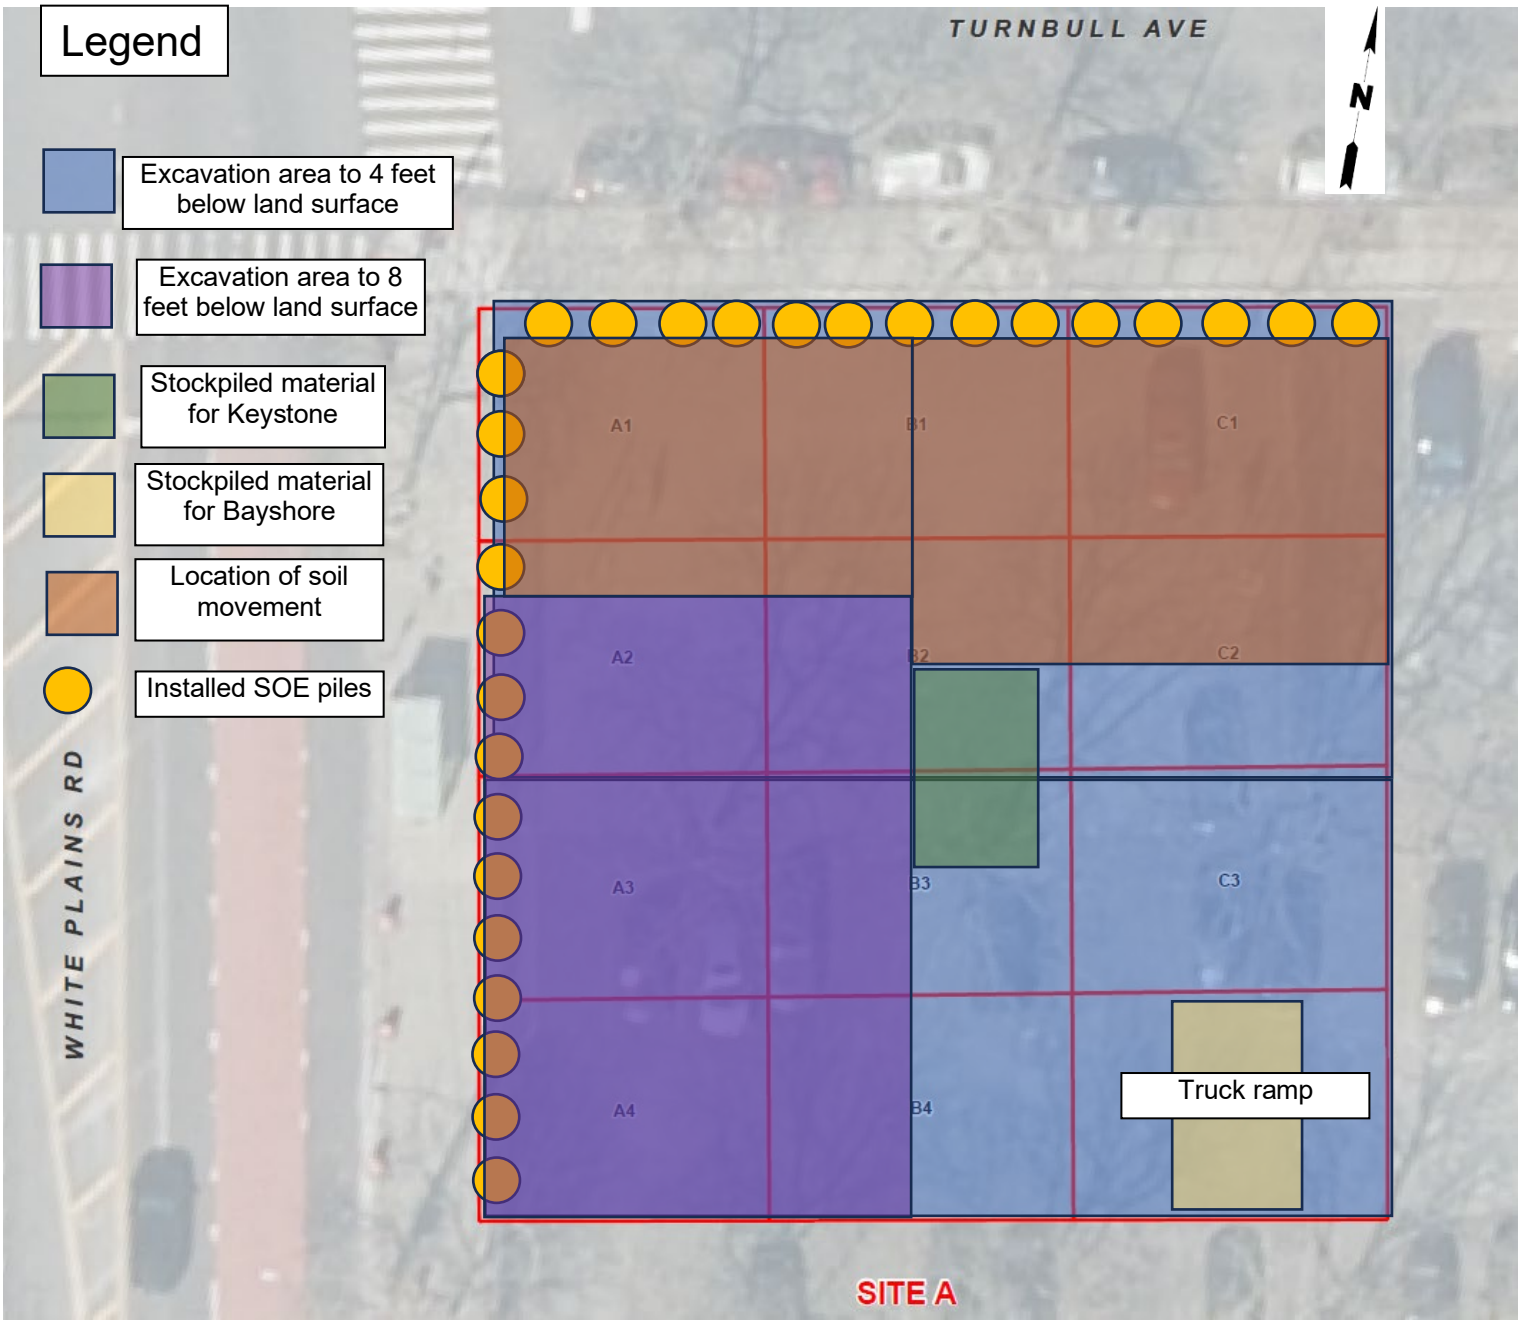

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/19/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 41-64°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Glenco loads truck with material to be exported to Bayshore Soil Management, LLC.




Photo 2:
Facing west, Glenco ensures all trucks are properly washed prior to exiting the site.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/19/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 41-64°F, Cloudy RH: 83% Pres: 29.94” Wind: SSE @ 9-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

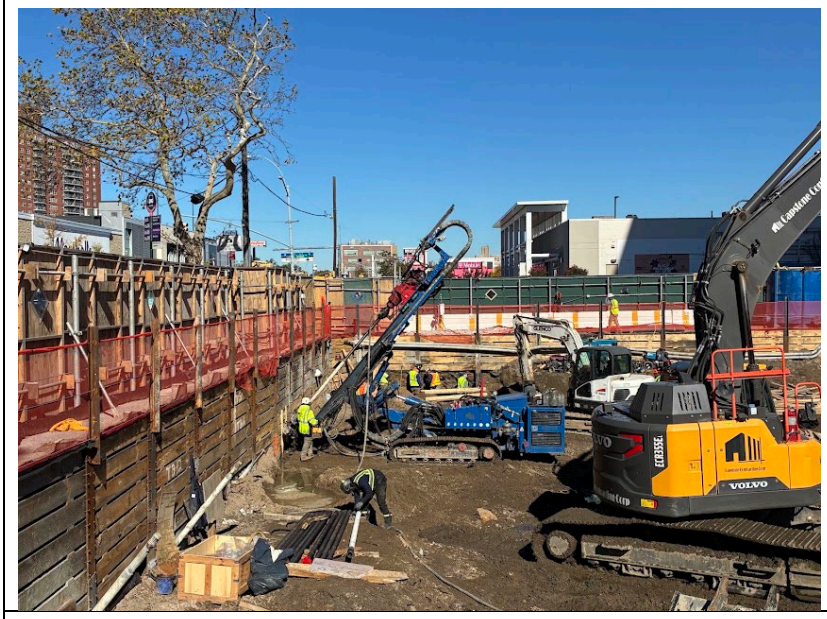	**Photo 3**: Facing north, Capstone continues installing tiebacks along the SOE on the western portion of the site.
	**Photo 4:** Facing west, view of north CAMP station located within the northwest site corner near the intersection of White Plains Rd. and Turnbull Ave.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/19/2026 07:00
		To: 10/19/2026 16:00

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/19/2026	40.6 - 76.3	37.8 - 80.8	30.3 - 30.5	0.2 - 2.6	NNE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/19/2026	0.0	07:15	0.0000	08:45
Max Contribution (15 min avg.) - 10/19/2026	17.3	10:45	0.0260	07:30
Daily Avg. Contribution (15 min avg.) - 10/19/2026	1.8	-	0.0026	-

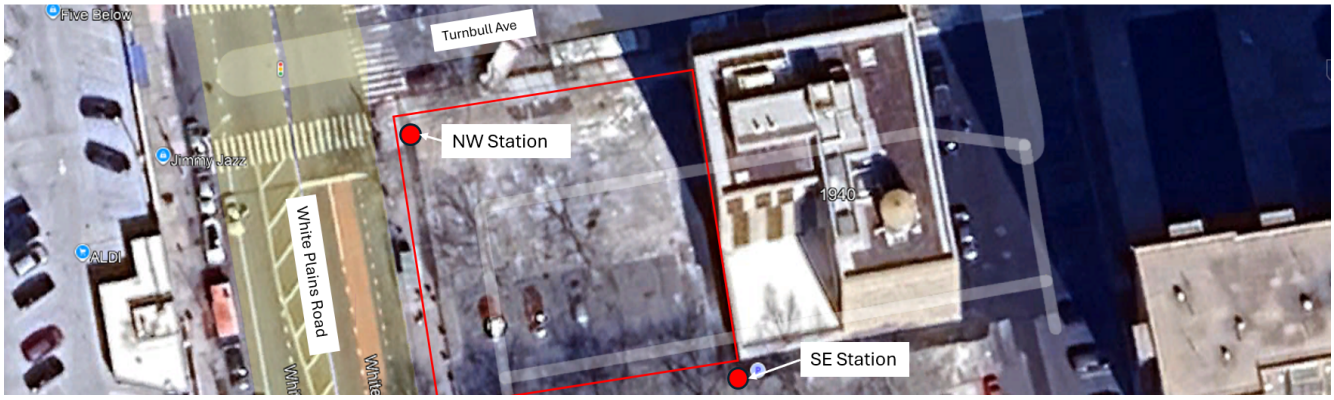


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

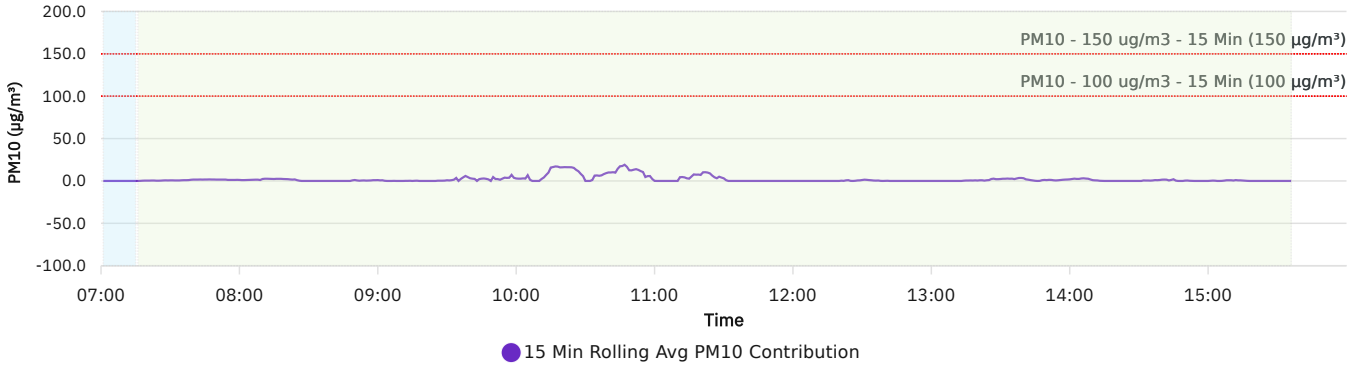

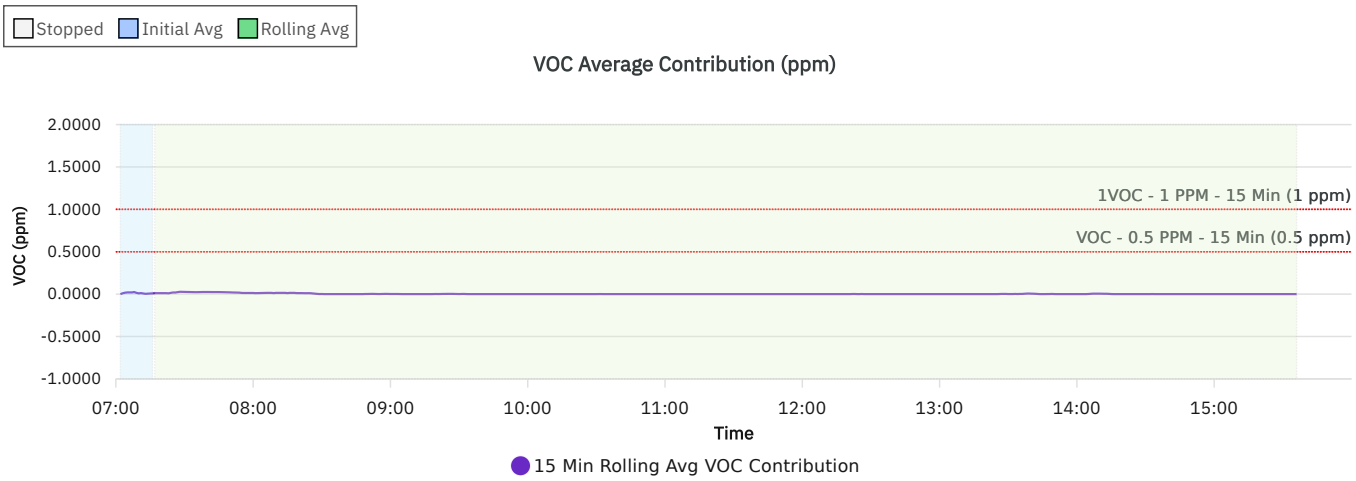

Wind rose (mph)

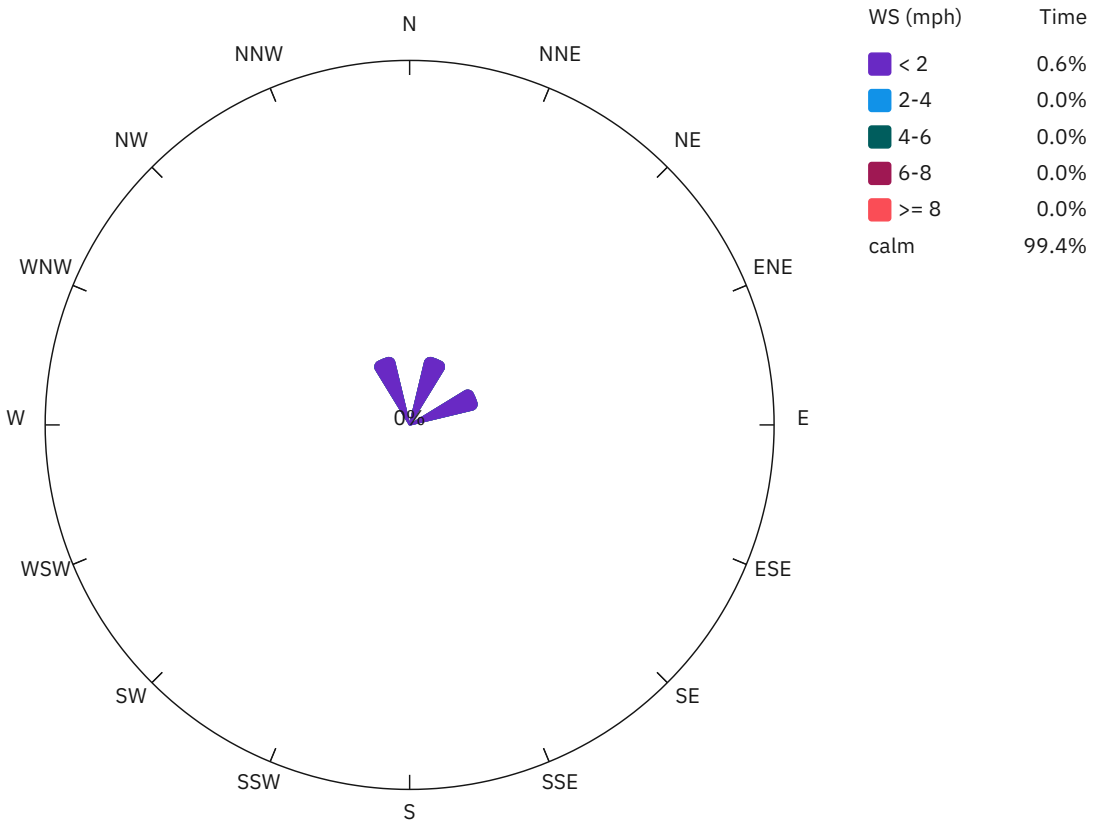

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/19/2026 07:15	9.4	9.2	0.0	0.0300	0.0371	0.0071	0.2	NNE
10/19/2026 07:30	9.2	9.8	0.7	0.0200	0.0460	0.0260	0.2	NE
10/19/2026 07:45	7.4	9.1	1.7	0.0200	0.0440	0.0240	0.2	NE
10/19/2026 08:00	6.8	8.0	1.2	0.0213	0.0347	0.0133	0.2	NE
10/19/2026 08:15	7.6	10.0	2.3	0.0240	0.0360	0.0120	0.2	NE
10/19/2026 08:30	8.2	7.7	0.0	0.0273	0.0287	0.0013	0.2	N
10/19/2026 08:45	8.6	7.1	0.0	0.0260	0.0240	0.0000	0.2	N
10/19/2026 09:00	9.5	10.4	1.0	0.0200	0.0213	0.0013	0.2	N
10/19/2026 09:15	9.2	9.2	0.0	0.0207	0.0200	0.0000	0.3	N
10/19/2026 09:30	10.5	11.3	0.8	0.0167	0.0173	0.0007	0.3	NNE
10/19/2026 09:45	23.7	26.4	2.7	0.0153	0.0140	0.0000	0.2	NNE
10/19/2026 10:00	9.3	12.1	2.9	0.0133	0.0100	0.0000	0.4	NNE
10/19/2026 10:15	3.8	19.6	15.8	0.0187	0.0027	0.0000	0.3	NE
10/19/2026 10:30	6.0	5.8	0.0	0.0113	0.0093	0.0000	0.4	NNE
10/19/2026 10:45	6.7	24.0	17.3	0.0160	0.0040	0.0000	0.3	NE
10/19/2026 11:00	10.8	11.0	0.1	0.0133	0.0067	0.0000	0.3	NNE
10/19/2026 11:15	8.2	11.0	2.7	0.0140	0.0040	0.0000	0.4	NNE
10/19/2026 11:30	6.8	10.0	3.1	0.0100	0.0053	0.0000	0.4	NNE
10/19/2026 11:45	4.2	3.6	0.0	0.0127	0.0047	0.0000	0.4	NNE
10/19/2026 12:00	3.7	3.2	0.0	0.0133	0.0040	0.0000	0.5	NNE
10/19/2026 12:15	3.7	2.0	0.0	0.0140	0.0047	0.0000	0.4	NE
10/19/2026 12:30	3.8	4.9	1.1	0.0073	0.0060	0.0000	0.4	NNE
10/19/2026 12:45	3.1	2.0	0.0	0.0127	0.0020	0.0000	0.4	NE
10/19/2026 13:00	2.9	1.9	0.0	0.0107	0.0033	0.0000	0.4	NE
10/19/2026 13:15	2.7	3.2	0.5	0.0067	0.0033	0.0000	0.4	NE
10/19/2026 13:30	2.5	4.8	2.3	0.0047	0.0053	0.0007	0.5	N
10/19/2026 13:45	3.2	3.4	0.2	0.0080	0.0073	0.0000	0.4	NNE
10/19/2026 14:00	2.8	4.7	1.9	0.0067	0.0033	0.0000	0.4	NE
10/19/2026 14:15	7.4	7.0	0.0	0.0073	0.0080	0.0007	0.3	NNE
10/19/2026 14:30	6.7	4.1	0.0	0.0080	0.0033	0.0000	0.3	NE
10/19/2026 14:45	4.1	6.0	2.0	0.0120	0.0040	0.0000	0.4	NNE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/19/2026 15:00	3.6	3.5	0.0	0.0087	0.0033	0.0000	0.2	NE
10/19/2026 15:15	3.3	3.8	0.5	0.0087	0.0033	0.0000	0.4	NNE
10/19/2026 15:30	2.3	1.9	0.0	0.0113	0.0040	0.0000	0.4	NE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/21/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-65°F, Fair RH: 47% Pres: 30.24” Wind: N @ 14-28 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern boundary of the Site.
- Capstone continued tieback installation along the SOE piles.
- Glenco excavated soil from grids B1 and C1 to facilitate lagging work and stockpiled soil for future export to Bayshore Soil Management, LLC.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-16:00. An exceedance of dust action levels was encountered at 13:30 and 13:45 with downwind contribution levels peaking at 525.2 µg/m³. The exceedance was not caused by dust generated from ground intrusive work, and instead was caused by welding fumes from hot work conducted directly adjacent to the CAMP station. At the onset of the exceedance, the hot work was paused, and the CAMP station was moved several feet to avoid drawing in welding fumes. No exceedances of volatile organic compound (VOC) were encountered. An exceedance report was submitted to the NYSDEC.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/21/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-65°F, Fair RH: 47% Pres: 30.24” Wind: N @ 14-28 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/21/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-65°F, Fair RH: 47% Pres: 30.24” Wind: N @ 14-28 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

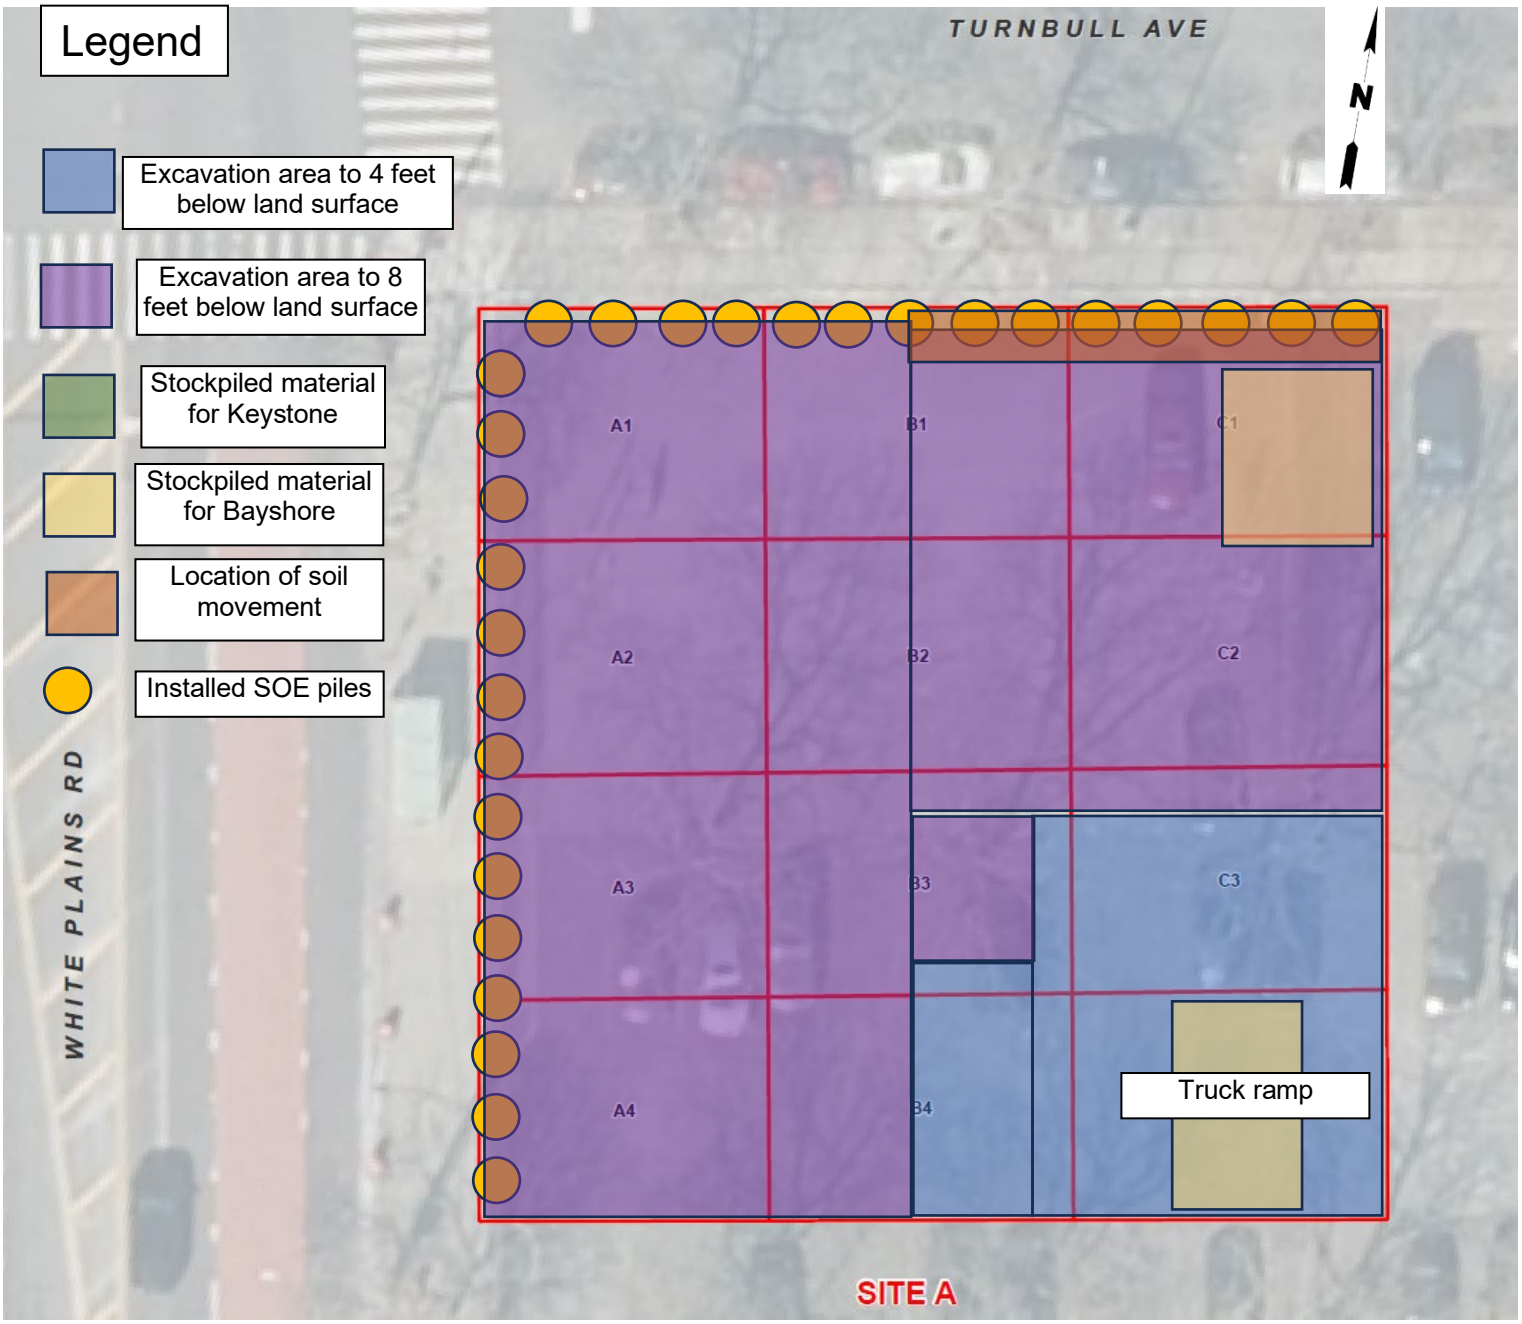

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/21/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-65°F, Fair RH: 47% Pres: 30.24” Wind: N @ 14-28 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A

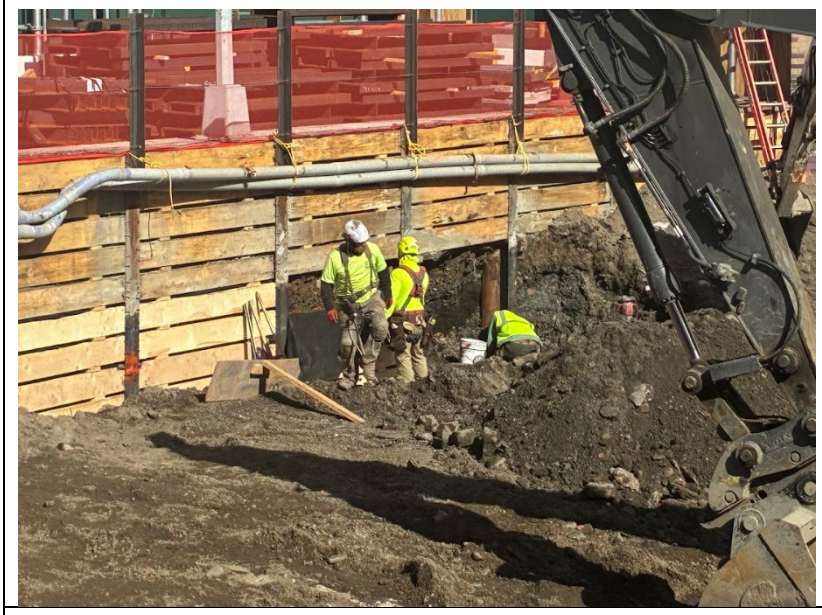


Photo 1:
Facing northeast, Glenco installs lagging along SOE piles within the northern portion of the site.

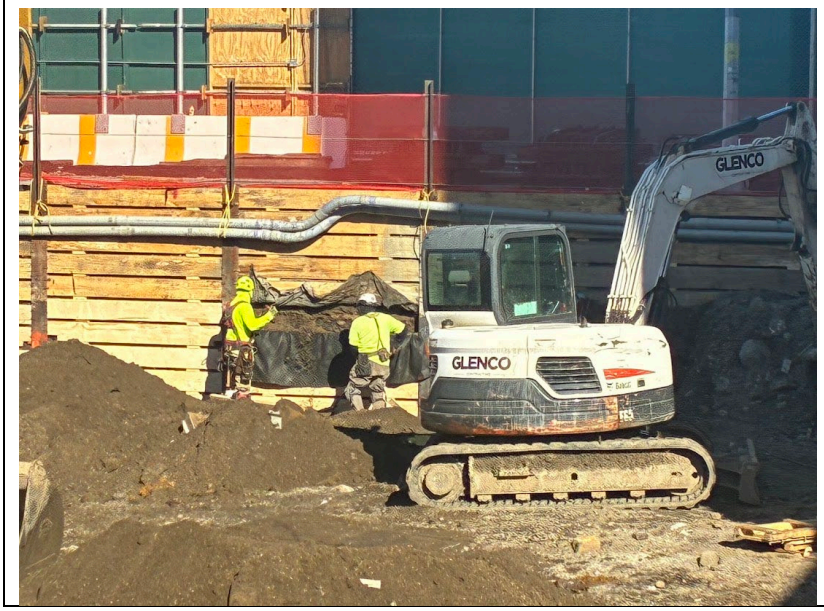


Photo 2:
Facing north, Glenco installs geotextile inside of the SOE.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/21/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-65°F, Fair RH: 47% Pres: 30.24” Wind: N @ 14-28 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

	**Photo 3**: Facing west, view of CAMP station located within the northwestern site corner.
	**Photo 4:** Facing north, view of lagging installed along northern site perimeter.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**


ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A	
		DER-10 contribution	
		Report Period	
		From:	10/21/2026 07:00
		To:	10/21/2026 16:00


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/21/2026	44.8 - 76.6	35.2 - 57.8	30.1 - 30.4	0.6 - 5.7	ENE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/21/2026	0.0	07:15	0.0000	07:30
Max Contribution (15 min avg.) - 10/21/2026	525.2	13:45	0.0653	13:45
Daily Avg. Contribution (15 min avg.) - 10/21/2026	27.2	-	0.0029	-

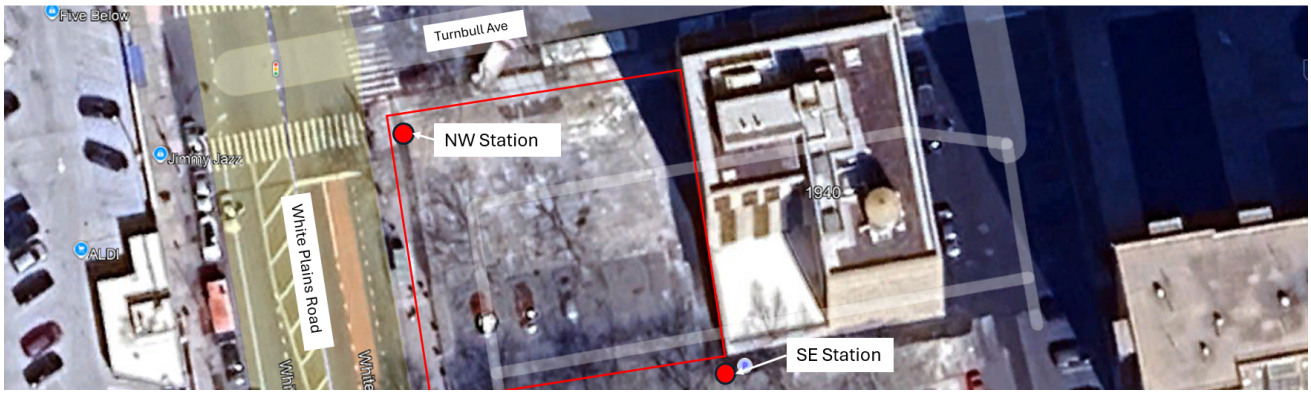

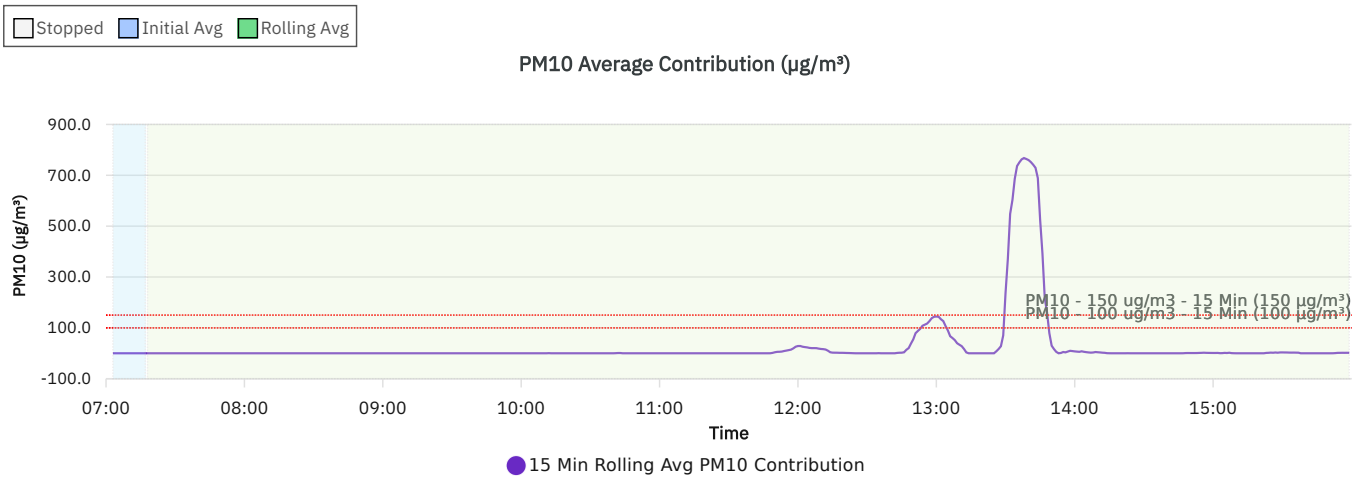

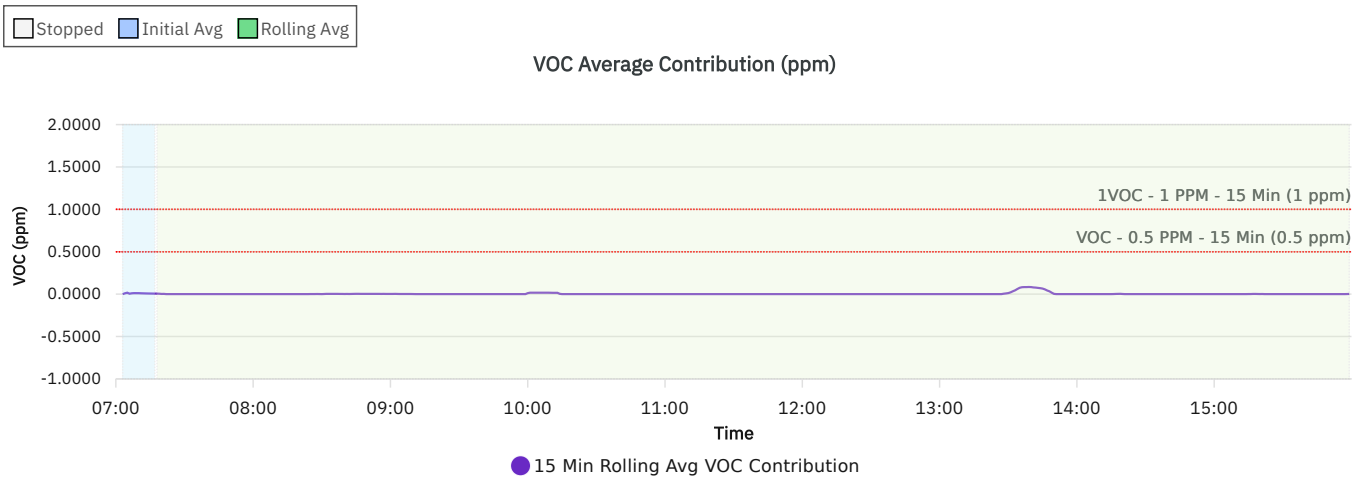

Wind rose (mph)

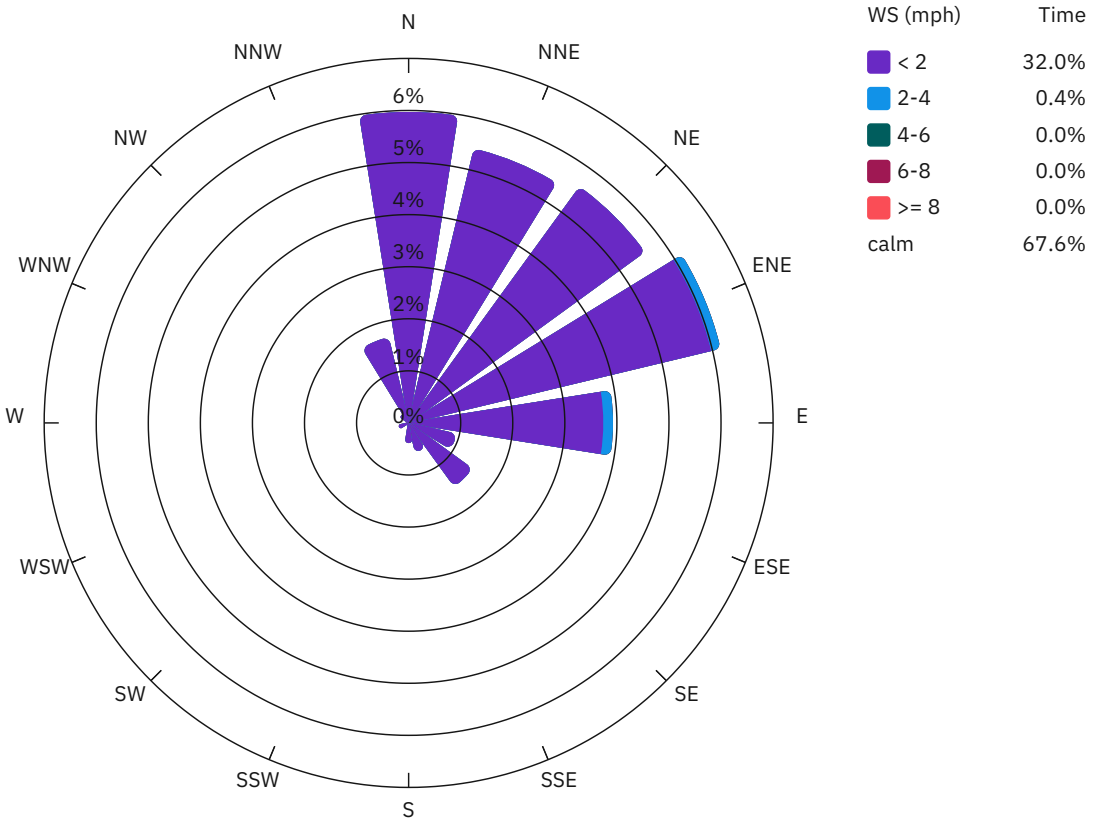

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/21/2026 07:15	62.7	20.3	0.0	0.0085	0.0154	0.0069	0.6	NE
10/21/2026 07:30	36.1	3.8	0.0	0.0227	0.0113	0.0000	0.7	ENE
10/21/2026 07:45	24.0	4.5	0.0	0.0200	0.0053	0.0000	0.7	NE
10/21/2026 08:00	23.7	6.3	0.0	0.0180	0.0107	0.0000	0.7	ENE
10/21/2026 08:15	19.0	7.3	0.0	0.0180	0.0153	0.0000	0.5	NE
10/21/2026 08:30	17.5	5.3	0.0	0.0187	0.0187	0.0000	0.5	ENE
10/21/2026 08:45	15.4	10.5	0.0	0.0160	0.0193	0.0033	0.5	ENE
10/21/2026 09:00	14.7	8.0	0.0	0.0180	0.0200	0.0020	0.7	ENE
10/21/2026 09:15	15.7	5.7	0.0	0.0187	0.0153	0.0000	0.8	ENE
10/21/2026 09:30	17.1	16.5	0.0	0.0160	0.0100	0.0000	0.8	ENE
10/21/2026 09:45	14.0	9.5	0.0	0.0200	0.0080	0.0000	0.7	ENE
10/21/2026 10:00	14.4	9.2	0.0	0.0200	0.0313	0.0113	0.5	ENE
10/21/2026 10:15	12.7	8.3	0.0	0.0200	0.0060	0.0000	0.6	ENE
10/21/2026 10:30	13.1	9.0	0.0	0.0180	0.0000	0.0000	0.6	ENE
10/21/2026 10:45	15.0	14.4	0.0	0.0173	0.0000	0.0000	0.7	E
10/21/2026 11:00	13.4	8.7	0.0	0.0187	0.0027	0.0000	0.7	ESE
10/21/2026 11:15	10.2	9.2	0.0	0.0173	0.0027	0.0000	0.4	ENE
10/21/2026 11:30	9.3	8.7	0.0	0.0193	0.0000	0.0000	0.6	ENE
10/21/2026 11:45	10.7	5.9	0.0	0.0180	0.0000	0.0000	0.5	E
10/21/2026 12:00	11.0	39.5	28.5	0.0180	0.0000	0.0000	0.5	E
10/21/2026 12:15	8.5	11.0	2.5	0.0113	0.0000	0.0000	0.6	E
10/21/2026 12:30	6.1	3.5	0.0	0.0173	0.0000	0.0000	0.5	E
10/21/2026 12:45	13.1	15.4	2.3	0.0140	0.0000	0.0000	0.7	E
10/21/2026 13:00	11.2	155.7	144.5	0.0113	0.0040	0.0000	0.7	E
10/21/2026 13:15	11.7	7.0	0.0	0.0100	0.0007	0.0000	0.7	ENE
10/21/2026 13:30	12.1	248.9	236.8	0.0100	0.0220	0.0120	0.6	E
10/21/2026 13:45	20.1	545.3	525.2	0.0080	0.0733	0.0653	0.8	NE
10/21/2026 14:00	13.1	20.5	7.4	0.0100	0.0027	0.0000	1.0	NE
10/21/2026 14:15	10.0	10.1	0.1	0.0053	0.0047	0.0000	1.0	NNE
10/21/2026 14:30	7.4	5.9	0.0	0.0080	0.0067	0.0000	1.0	NNE
10/21/2026 14:45	6.7	6.6	0.0	0.0087	0.0027	0.0000	1.0	NNE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/21/2026 15:00	7.4	8.5	1.2	0.0080	0.0027	0.0000	1.1	NE
10/21/2026 15:15	12.0	11.0	0.0	0.0073	0.0080	0.0007	1.0	NNE
10/21/2026 15:30	5.5	8.9	3.4	0.0100	0.0027	0.0000	1.1	NE
10/21/2026 15:45	9.7	7.9	0.0	0.0080	0.0020	0.0000	1.0	NE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/22/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 48-67°F, Fair RH: 55% Pres: 30.01” Wind: NNW @ 12-24 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Glenco welded T bars and installed lagging along the northern boundary of the Site.
- Glenco excavated soil from grid C1 to facilitate lagging work and stockpiled soil for future export to Bayshore Soil Management, LLC.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-16:00. No exceedances of dust action levels or volatile organic compounds (VOCs) were encountered.

Offsite Disposal:

Soil Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Allocco Recycling Corp.	0	17

Imported Material:

Facility	**Material Imported**	**CY Imported Today**	**Cumulative CY Imported**
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/22/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 48-67°F, Fair RH: 55% Pres: 30.01” Wind: NNW @ 12-24 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/22/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 48-67°F, Fair RH: 55% Pres: 30.01” Wind: NNW @ 12-24 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

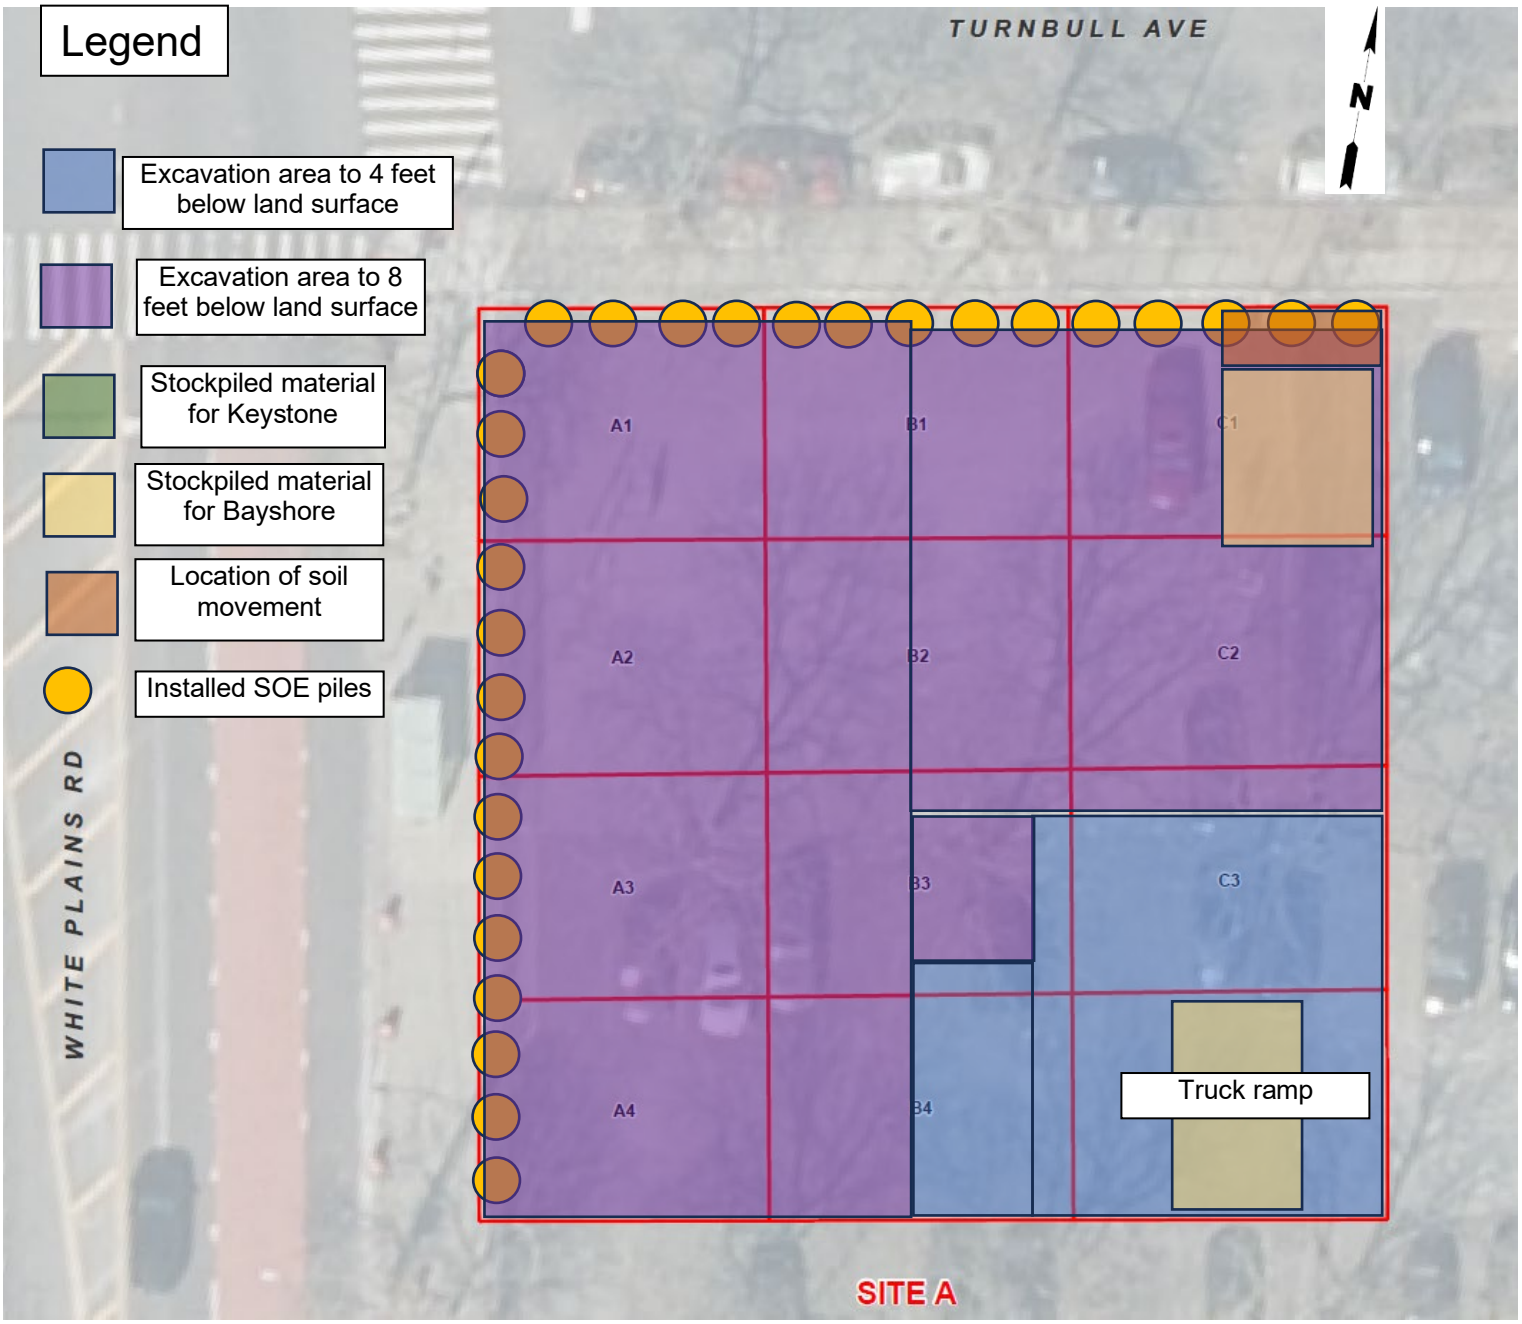

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/22/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 48-67°F, Fair RH: 55% Pres: 30.01” Wind: NNW @ 12-24 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing northeast, Glenco excavates soil within grid C1 to facilitate lagging work along SOE piles within the northern portion of the site.



Photo 2:
Facing northeast, view of lagging completed within the northeast corner of the site.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/22/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 48-67°F, Fair RH: 55% Pres: 30.01” Wind: NNW @ 12-24 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:30

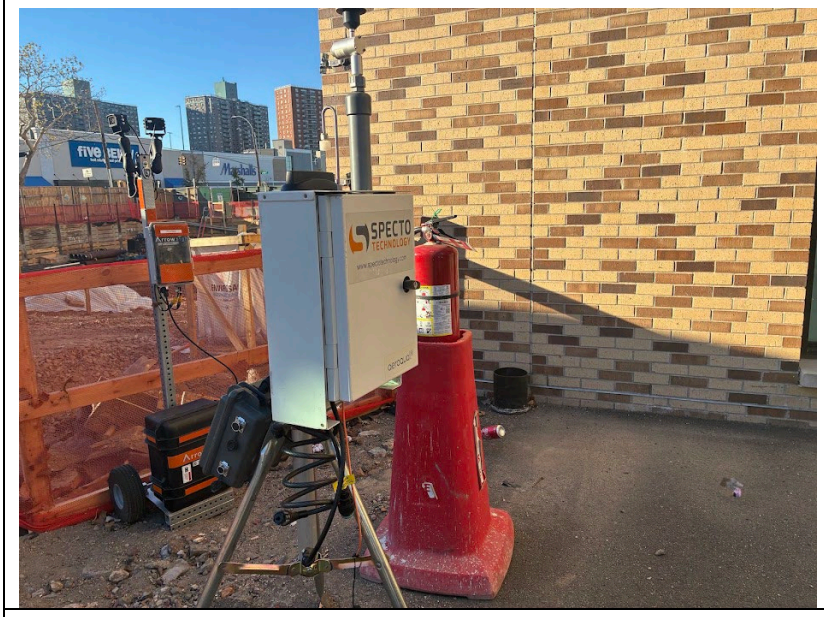


Photo 3:
Facing northwest, view of south CAMP station located within the southeastern site corner.



Photo 4: Facing east, Glenco ensures stockpiled soil is covered in polyethylene sheeting at the conclusion of work activities.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/22/2026 07:00
		To: 10/22/2026 16:30


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/22/2026	46.0 - 72.9	26.4 - 58.5	29.9 - 30.1	0.8 - 7.3	NE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/22/2026	0.0	07:01	0.0000	07:37
Max Contribution (15 min avg.) - 10/22/2026	25.6	07:30	0.0180	07:06
Daily Avg. Contribution (15 min avg.) - 10/22/2026	1.5	-	0.0023	-

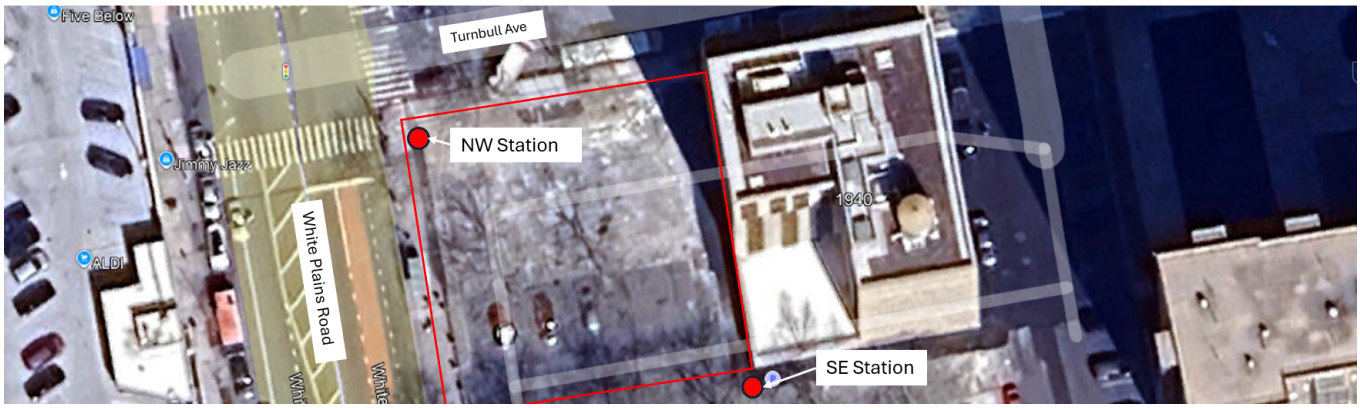


PM10 Average Contribution (µg/m³)

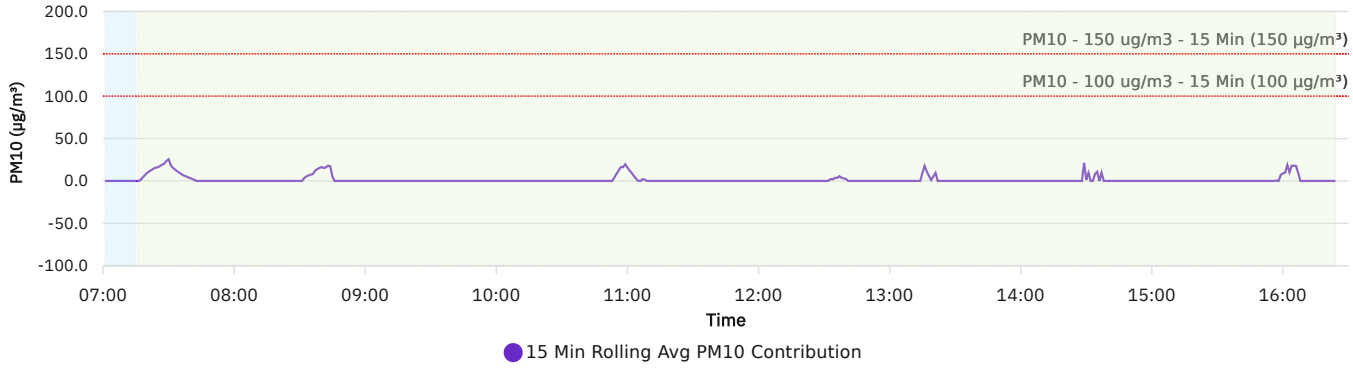

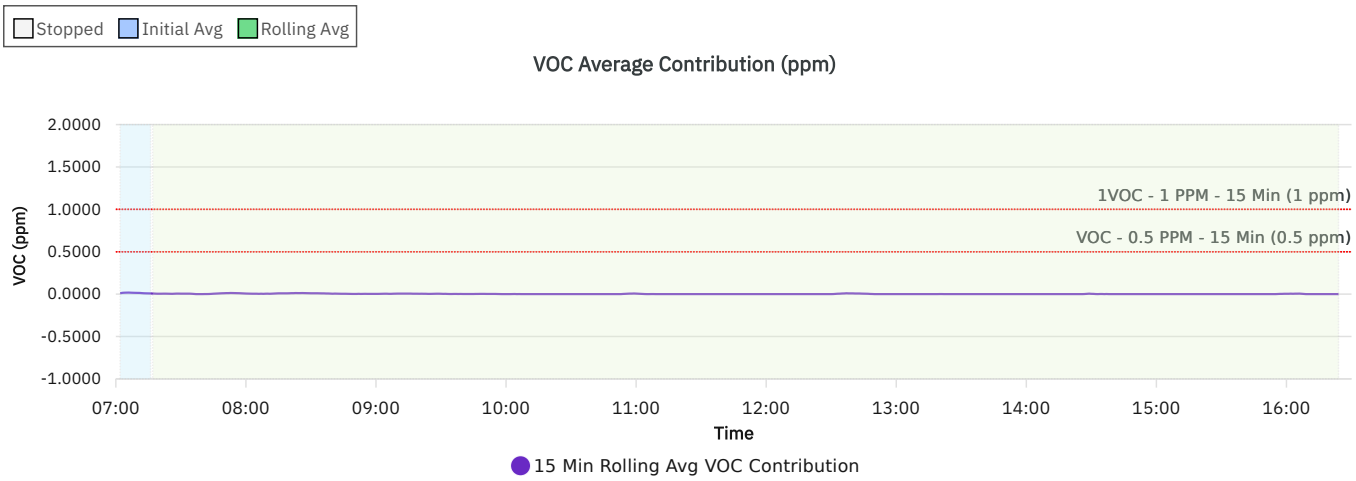

Wind rose (mph)

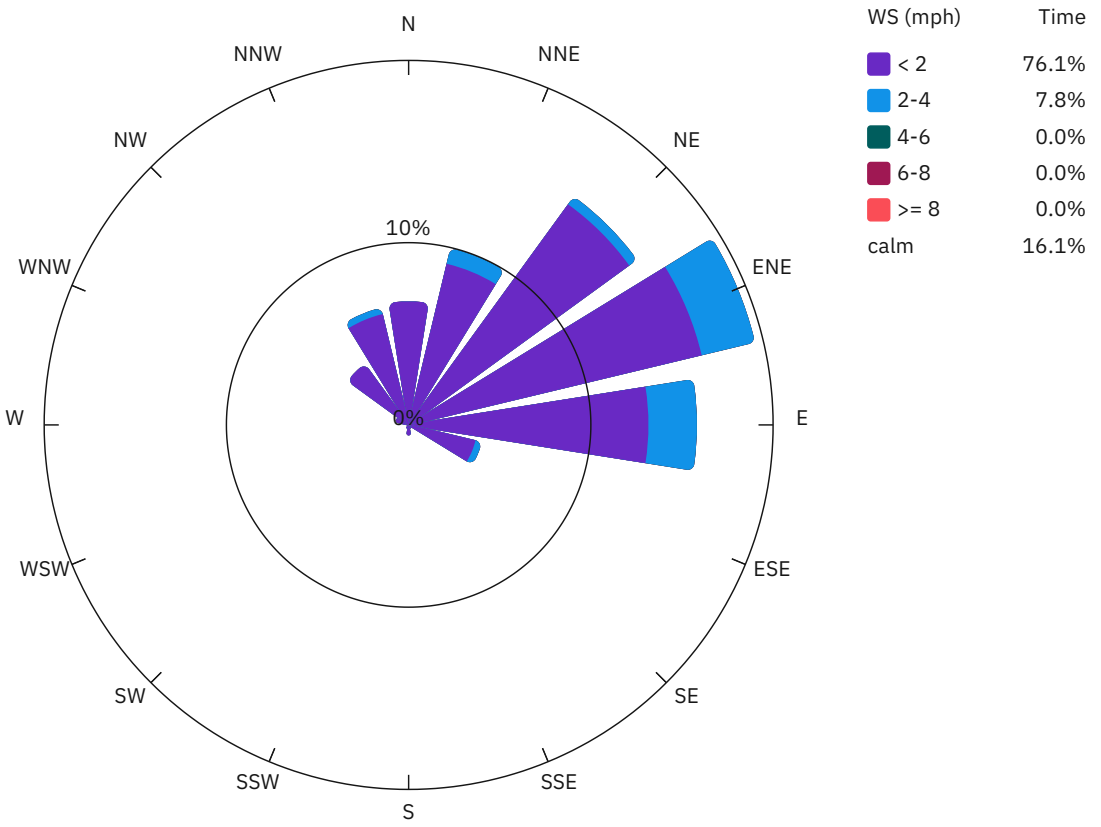

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 07:01	26.0	16.9	0.0				0.5	NE
10/22/2026 07:02	23.0	13.7	0.0	0.0100	0.0200	0.0100	0.8	NE
10/22/2026 07:03	22.0	12.8	0.0	0.0100	0.0250	0.0150	1.0	NE
10/22/2026 07:04	21.5	12.3	0.0	0.0100	0.0267	0.0167	1.0	ENE
10/22/2026 07:05	21.2	12.0	0.0	0.0100	0.0275	0.0175	1.0	ENE
10/22/2026 07:06	20.1	11.8	0.0	0.0100	0.0280	0.0180	1.0	NE
10/22/2026 07:07	19.3	11.0	0.0	0.0100	0.0267	0.0167	1.0	NE
10/22/2026 07:08	19.4	10.3	0.0	0.0100	0.0257	0.0157	1.1	NE
10/22/2026 07:09	19.1	9.9	0.0	0.0100	0.0250	0.0150	1.1	NE
10/22/2026 07:10	18.6	9.7	0.0	0.0100	0.0244	0.0144	1.1	NE
10/22/2026 07:11	18.4	9.2	0.0	0.0100	0.0240	0.0140	1.1	ENE
10/22/2026 07:12	18.4	9.0	0.0	0.0109	0.0227	0.0118	1.1	NE
10/22/2026 07:13	18.2	8.9	0.0	0.0117	0.0217	0.0100	1.1	NE
10/22/2026 07:14	20.3	8.9	0.0	0.0115	0.0208	0.0092	1.1	NE
10/22/2026 07:15	21.4	9.2	0.0	0.0114	0.0200	0.0086	1.1	E
10/22/2026 07:16	21.3	17.2	0.0	0.0113	0.0193	0.0080	1.1	ENE
10/22/2026 07:17	21.5	22.3	0.7	0.0113	0.0187	0.0073	1.0	ENE
10/22/2026 07:18	21.7	25.4	3.8	0.0113	0.0173	0.0060	0.9	SSE
10/22/2026 07:19	21.7	28.1	6.4	0.0120	0.0167	0.0047	0.9	SSE
10/22/2026 07:20	21.6	30.7	9.1	0.0120	0.0167	0.0047	0.8	E
10/22/2026 07:21	22.0	33.0	11.0	0.0120	0.0167	0.0047	0.8	E
10/22/2026 07:22	22.4	35.0	12.7	0.0120	0.0173	0.0053	0.8	ENE
10/22/2026 07:23	22.4	36.8	14.3	0.0120	0.0173	0.0053	0.8	ESE
10/22/2026 07:24	22.4	38.0	15.6	0.0120	0.0167	0.0047	0.7	SSE
10/22/2026 07:25	23.0	39.1	16.1	0.0120	0.0160	0.0040	0.7	NE
10/22/2026 07:26	23.2	40.6	17.5	0.0127	0.0160	0.0033	0.7	ENE
10/22/2026 07:27	23.1	42.2	19.1	0.0127	0.0173	0.0047	0.7	NE
10/22/2026 07:28	23.2	43.6	20.4	0.0127	0.0187	0.0060	0.7	ENE
10/22/2026 07:29	21.1	44.8	23.6	0.0133	0.0193	0.0060	0.7	ENE
10/22/2026 07:30	19.9	45.5	25.6	0.0140	0.0193	0.0053	0.7	NE
10/22/2026 07:31	19.3	38.1	18.8	0.0140	0.0193	0.0053	0.8	ENE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 07:32	18.8	34.1	15.3	0.0140	0.0193	0.0053	0.8	E
10/22/2026 07:33	18.9	32.3	13.4	0.0140	0.0193	0.0053	0.9	E
10/22/2026 07:34	20.0	31.3	11.3	0.0133	0.0187	0.0053	1.0	NE
10/22/2026 07:35	21.1	30.5	9.5	0.0133	0.0173	0.0040	0.9	NNW
10/22/2026 07:36	21.5	29.4	7.8	0.0140	0.0160	0.0020	1.0	NE
10/22/2026 07:37	22.4	28.7	6.3	0.0147	0.0147	0.0000	1.0	NE
10/22/2026 07:38	22.7	28.2	5.5	0.0153	0.0140	0.0000	1.1	NE
10/22/2026 07:39	23.6	27.7	4.2	0.0153	0.0147	0.0000	1.2	NNE
10/22/2026 07:40	23.9	27.2	3.3	0.0160	0.0160	0.0000	1.2	E
10/22/2026 07:41	24.3	26.5	2.1	0.0160	0.0167	0.0007	1.2	NE
10/22/2026 07:42	24.7	25.6	0.9	0.0153	0.0160	0.0007	1.1	S
10/22/2026 07:43	24.6	24.6	0.0	0.0147	0.0160	0.0013	1.1	ENE
10/22/2026 07:44	24.6	23.6	0.0	0.0147	0.0173	0.0027	1.0	SE
10/22/2026 07:45	24.6	22.7	0.0	0.0147	0.0193	0.0047	1.0	NNE
10/22/2026 07:46	24.8	21.8	0.0	0.0153	0.0213	0.0060	1.0	NE
10/22/2026 07:47	24.9	20.9	0.0	0.0153	0.0227	0.0073	1.0	ENE
10/22/2026 07:48	25.2	20.0	0.0	0.0153	0.0240	0.0087	1.0	E
10/22/2026 07:49	25.7	19.3	0.0	0.0153	0.0253	0.0100	1.1	ENE
10/22/2026 07:50	26.5	18.7	0.0	0.0153	0.0260	0.0107	1.2	ENE
10/22/2026 07:51	26.5	18.5	0.0	0.0147	0.0267	0.0120	1.2	NE
10/22/2026 07:52	26.0	18.2	0.0	0.0147	0.0267	0.0120	1.1	N
10/22/2026 07:53	25.6	18.2	0.0	0.0140	0.0273	0.0133	1.1	NNE
10/22/2026 07:54	25.0	18.4	0.0	0.0147	0.0273	0.0127	1.2	ENE
10/22/2026 07:55	24.5	18.5	0.0	0.0147	0.0267	0.0120	1.1	NE
10/22/2026 07:56	24.0	18.5	0.0	0.0147	0.0260	0.0113	1.1	NE
10/22/2026 07:57	24.0	18.8	0.0	0.0153	0.0260	0.0107	1.2	NE
10/22/2026 07:58	25.0	19.4	0.0	0.0160	0.0253	0.0093	1.1	SE
10/22/2026 07:59	25.2	19.7	0.0	0.0160	0.0240	0.0080	1.2	NNE
10/22/2026 08:00	25.3	20.2	0.0	0.0160	0.0227	0.0067	1.2	ENE
10/22/2026 08:01	25.2	20.8	0.0	0.0153	0.0213	0.0060	1.2	ENE
10/22/2026 08:02	25.1	21.2	0.0	0.0153	0.0207	0.0053	1.2	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 08:03	24.4	21.0	0.0	0.0153	0.0200	0.0047	1.2	NNE
10/22/2026 08:04	23.5	20.3	0.0	0.0153	0.0200	0.0047	1.1	NNE
10/22/2026 08:05	25.3	19.7	0.0	0.0160	0.0207	0.0047	1.1	ENE
10/22/2026 08:06	26.5	21.9	0.0	0.0173	0.0207	0.0033	1.0	N
10/22/2026 08:07	27.2	22.6	0.0	0.0173	0.0220	0.0047	1.0	S
10/22/2026 08:08	27.9	23.2	0.0	0.0187	0.0220	0.0033	0.9	NNW
10/22/2026 08:09	28.1	23.5	0.0	0.0180	0.0227	0.0047	0.8	E
10/22/2026 08:10	28.5	24.0	0.0	0.0180	0.0233	0.0053	0.9	NE
10/22/2026 08:11	28.8	26.4	0.0	0.0187	0.0227	0.0040	0.7	SSW
10/22/2026 08:12	30.7	26.3	0.0	0.0180	0.0233	0.0053	0.7	ENE
10/22/2026 08:13	32.0	26.3	0.0	0.0173	0.0240	0.0067	0.7	S
10/22/2026 08:14	33.5	26.3	0.0	0.0167	0.0247	0.0080	0.7	NE
10/22/2026 08:15	34.9	26.2	0.0	0.0160	0.0253	0.0093	0.7	NE
10/22/2026 08:16	36.7	26.3	0.0	0.0160	0.0253	0.0093	0.7	ENE
10/22/2026 08:17	40.5	28.0	0.0	0.0160	0.0253	0.0093	0.8	NE
10/22/2026 08:18	42.8	28.7	0.0	0.0160	0.0253	0.0093	0.8	NNE
10/22/2026 08:19	43.4	29.1	0.0	0.0160	0.0253	0.0093	0.8	NE
10/22/2026 08:20	41.4	29.4	0.0	0.0153	0.0253	0.0100	0.8	ENE
10/22/2026 08:21	42.1	27.3	0.0	0.0147	0.0260	0.0113	0.9	ENE
10/22/2026 08:22	44.3	26.4	0.0	0.0147	0.0260	0.0113	0.9	ESE
10/22/2026 08:23	46.0	25.3	0.0	0.0140	0.0267	0.0127	1.0	NE
10/22/2026 08:24	47.5	26.3	0.0	0.0147	0.0267	0.0120	1.0	NE
10/22/2026 08:25	49.0	27.3	0.0	0.0147	0.0267	0.0120	1.0	ESE
10/22/2026 08:26	49.4	26.5	0.0	0.0147	0.0273	0.0127	1.1	NW
10/22/2026 08:27	48.5	26.6	0.0	0.0153	0.0273	0.0120	1.1	NE
10/22/2026 08:28	48.5	26.4	0.0	0.0160	0.0273	0.0113	1.2	NE
10/22/2026 08:29	48.1	28.2	0.0	0.0167	0.0273	0.0107	1.2	E
10/22/2026 08:30	47.6	40.4	0.0	0.0173	0.0273	0.0100	1.2	E
10/22/2026 08:31	46.9	45.6	0.0	0.0173	0.0273	0.0100	1.1	E
10/22/2026 08:32	44.0	47.0	3.1	0.0173	0.0273	0.0100	1.1	NE
10/22/2026 08:33	43.2	48.4	5.3	0.0173	0.0273	0.0100	1.1	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 08:34	43.5	49.8	6.4	0.0173	0.0267	0.0093	1.1	NNE
10/22/2026 08:35	43.3	50.7	7.4	0.0173	0.0260	0.0087	1.1	E
10/22/2026 08:36	43.1	51.2	8.1	0.0167	0.0253	0.0087	1.1	ENE
10/22/2026 08:37	40.6	52.5	11.8	0.0167	0.0240	0.0073	1.1	NNW
10/22/2026 08:38	39.5	53.4	13.9	0.0167	0.0240	0.0073	1.1	ENE
10/22/2026 08:39	38.3	53.5	15.2	0.0173	0.0233	0.0060	0.9	NW
10/22/2026 08:40	36.9	53.3	16.4	0.0180	0.0227	0.0047	0.9	NNW
10/22/2026 08:41	37.1	52.3	15.3	0.0173	0.0233	0.0060	1.0	NNE
10/22/2026 08:42	36.6	52.6	16.0	0.0173	0.0227	0.0053	0.9	E
10/22/2026 08:43	35.0	53.1	18.1	0.0173	0.0220	0.0047	0.9	ENE
10/22/2026 08:44	34.6	51.8	17.2	0.0173	0.0213	0.0040	0.9	ENE
10/22/2026 08:45	34.9	39.8	4.9	0.0167	0.0207	0.0040	1.0	ENE
10/22/2026 08:46	37.3	34.8	0.0	0.0167	0.0207	0.0040	1.0	ENE
10/22/2026 08:47	38.5	31.8	0.0	0.0173	0.0207	0.0033	1.0	NNE
10/22/2026 08:48	39.0	30.0	0.0	0.0180	0.0207	0.0027	1.1	ENE
10/22/2026 08:49	42.0	28.5	0.0	0.0187	0.0207	0.0020	1.1	ENE
10/22/2026 08:50	43.5	27.2	0.0	0.0187	0.0207	0.0020	1.1	NE
10/22/2026 08:51	43.9	26.0	0.0	0.0187	0.0207	0.0020	1.1	ENE
10/22/2026 08:52	49.5	24.7	0.0	0.0180	0.0213	0.0033	1.2	NE
10/22/2026 08:53	48.1	29.8	0.0	0.0180	0.0200	0.0020	1.2	N
10/22/2026 08:54	51.2	28.0	0.0	0.0173	0.0200	0.0027	1.3	ENE
10/22/2026 08:55	53.4	26.6	0.0	0.0167	0.0200	0.0033	1.4	E
10/22/2026 08:56	55.0	26.1	0.0	0.0167	0.0193	0.0027	1.4	NNE
10/22/2026 08:57	54.7	27.9	0.0	0.0167	0.0193	0.0027	1.5	NNE
10/22/2026 08:58	56.8	29.4	0.0	0.0167	0.0193	0.0027	1.5	ENE
10/22/2026 08:59	56.5	32.8	0.0	0.0167	0.0193	0.0027	1.5	NNW
10/22/2026 09:00	58.2	32.9	0.0	0.0167	0.0193	0.0027	1.4	ESE
10/22/2026 09:01	60.0	33.4	0.0	0.0167	0.0193	0.0027	1.4	ENE
10/22/2026 09:02	62.7	33.5	0.0	0.0160	0.0193	0.0033	1.4	ENE
10/22/2026 09:03	65.0	33.5	0.0	0.0153	0.0193	0.0040	1.3	NE
10/22/2026 09:04	63.6	33.1	0.0	0.0147	0.0193	0.0047	1.3	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 09:05	63.3	33.2	0.0	0.0147	0.0193	0.0047	1.3	NE
10/22/2026 09:06	60.6	35.5	0.0	0.0153	0.0187	0.0033	1.3	NNE
10/22/2026 09:07	55.9	35.0	0.0	0.0153	0.0187	0.0033	1.3	E
10/22/2026 09:08	58.4	28.4	0.0	0.0147	0.0193	0.0047	1.3	SE
10/22/2026 09:09	58.0	28.3	0.0	0.0140	0.0193	0.0053	1.3	ENE
10/22/2026 09:10	60.7	28.9	0.0	0.0133	0.0193	0.0060	1.3	ENE
10/22/2026 09:11	62.2	28.7	0.0	0.0127	0.0187	0.0060	1.4	E
10/22/2026 09:12	65.3	26.4	0.0	0.0120	0.0180	0.0060	1.4	ESE
10/22/2026 09:13	62.2	27.3	0.0	0.0113	0.0173	0.0060	1.3	NNE
10/22/2026 09:14	64.0	22.9	0.0	0.0107	0.0167	0.0060	1.4	NE
10/22/2026 09:15	63.0	22.2	0.0	0.0107	0.0167	0.0060	1.4	ENE
10/22/2026 09:16	59.3	21.0	0.0	0.0107	0.0167	0.0060	1.4	NE
10/22/2026 09:17	54.0	22.1	0.0	0.0113	0.0160	0.0047	1.3	NNE
10/22/2026 09:18	51.4	21.2	0.0	0.0113	0.0160	0.0047	1.3	NNE
10/22/2026 09:19	49.6	20.7	0.0	0.0113	0.0160	0.0047	1.3	E
10/22/2026 09:20	45.9	22.3	0.0	0.0120	0.0160	0.0040	1.2	NW
10/22/2026 09:21	47.3	19.2	0.0	0.0120	0.0167	0.0047	1.2	ENE
10/22/2026 09:22	46.6	18.7	0.0	0.0127	0.0167	0.0040	1.2	ENE
10/22/2026 09:23	45.3	18.3	0.0	0.0127	0.0167	0.0040	1.2	NE
10/22/2026 09:24	40.8	19.9	0.0	0.0133	0.0160	0.0027	1.1	NNW
10/22/2026 09:25	36.1	18.5	0.0	0.0133	0.0160	0.0027	1.0	ENE
10/22/2026 09:26	33.3	17.9	0.0	0.0133	0.0167	0.0033	1.0	NNE
10/22/2026 09:27	30.9	17.5	0.0	0.0133	0.0173	0.0040	1.0	E
10/22/2026 09:28	33.4	14.2	0.0	0.0133	0.0180	0.0047	1.0	E
10/22/2026 09:29	32.7	13.9	0.0	0.0133	0.0180	0.0047	1.0	NE
10/22/2026 09:30	32.3	13.4	0.0	0.0133	0.0173	0.0040	1.0	NE
10/22/2026 09:31	32.4	12.9	0.0	0.0140	0.0167	0.0027	1.0	NNE
10/22/2026 09:32	34.5	10.5	0.0	0.0140	0.0173	0.0033	1.1	NE
10/22/2026 09:33	34.5	10.4	0.0	0.0147	0.0167	0.0020	1.0	E
10/22/2026 09:34	33.9	10.0	0.0	0.0147	0.0160	0.0013	1.0	ENE
10/22/2026 09:35	36.3	7.7	0.0	0.0140	0.0153	0.0013	1.1	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 09:36	36.8	8.0	0.0	0.0133	0.0153	0.0020	1.0	S
10/22/2026 09:37	36.8	8.3	0.0	0.0127	0.0147	0.0020	1.0	NE
10/22/2026 09:38	36.7	8.7	0.0	0.0127	0.0140	0.0013	1.1	ENE
10/22/2026 09:39	37.1	8.4	0.0	0.0120	0.0140	0.0020	1.1	N
10/22/2026 09:40	35.4	10.3	0.0	0.0120	0.0133	0.0013	1.0	NW
10/22/2026 09:41	35.0	10.2	0.0	0.0120	0.0133	0.0013	1.0	NE
10/22/2026 09:42	34.8	10.3	0.0	0.0120	0.0133	0.0013	1.0	ENE
10/22/2026 09:43	35.3	11.6	0.0	0.0120	0.0133	0.0013	1.0	ESE
10/22/2026 09:44	35.5	17.4	0.0	0.0120	0.0133	0.0013	1.0	E
10/22/2026 09:45	35.5	21.1	0.0	0.0120	0.0133	0.0013	1.0	ENE
10/22/2026 09:46	35.0	23.5	0.0	0.0113	0.0133	0.0020	1.0	NE
10/22/2026 09:47	34.5	25.4	0.0	0.0107	0.0127	0.0020	1.0	ENE
10/22/2026 09:48	34.5	27.0	0.0	0.0100	0.0127	0.0027	1.1	NE
10/22/2026 09:49	34.4	28.4	0.0	0.0100	0.0127	0.0027	1.1	NE
10/22/2026 09:50	33.7	30.3	0.0	0.0100	0.0127	0.0027	1.1	ENE
10/22/2026 09:51	32.7	30.9	0.0	0.0100	0.0120	0.0020	1.2	E
10/22/2026 09:52	32.4	31.4	0.0	0.0100	0.0120	0.0020	1.2	NNE
10/22/2026 09:53	32.6	32.1	0.0	0.0100	0.0120	0.0020	1.2	E
10/22/2026 09:54	34.5	31.1	0.0	0.0100	0.0120	0.0020	1.2	ESE
10/22/2026 09:55	35.1	31.1	0.0	0.0100	0.0120	0.0020	1.2	N
10/22/2026 09:56	35.3	31.7	0.0	0.0100	0.0113	0.0013	1.2	ENE
10/22/2026 09:57	35.2	31.9	0.0	0.0100	0.0107	0.0007	1.2	ENE
10/22/2026 09:58	33.1	30.7	0.0	0.0100	0.0100	0.0000	1.2	E
10/22/2026 09:59	32.2	25.1	0.0	0.0100	0.0100	0.0000	1.3	NE
10/22/2026 10:00	32.0	22.6	0.0	0.0100	0.0100	0.0000	1.3	NE
10/22/2026 10:01	31.8	20.7	0.0	0.0100	0.0100	0.0000	1.3	ENE
10/22/2026 10:02	31.9	19.5	0.0	0.0100	0.0100	0.0000	1.3	NE
10/22/2026 10:03	30.4	20.0	0.0	0.0100	0.0107	0.0007	1.1	NW
10/22/2026 10:04	29.0	20.4	0.0	0.0100	0.0113	0.0013	1.1	N
10/22/2026 10:05	29.2	19.0	0.0	0.0107	0.0107	0.0000	1.1	E
10/22/2026 10:06	28.1	20.1	0.0	0.0100	0.0107	0.0007	1.1	N

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 10:07	28.2	20.0	0.0	0.0100	0.0100	0.0000	1.1	NNE
10/22/2026 10:08	27.6	19.5	0.0	0.0100	0.0100	0.0000	1.1	NNE
10/22/2026 10:09	26.9	19.1	0.0	0.0100	0.0100	0.0000	1.2	NE
10/22/2026 10:10	28.2	17.4	0.0	0.0100	0.0100	0.0000	1.2	NNE
10/22/2026 10:11	28.0	16.9	0.0	0.0100	0.0093	0.0000	1.1	SE
10/22/2026 10:12	27.7	16.4	0.0	0.0100	0.0087	0.0000	1.1	NNE
10/22/2026 10:13	27.5	16.0	0.0	0.0100	0.0080	0.0000	1.1	ENE
10/22/2026 10:14	28.1	15.7	0.0	0.0100	0.0080	0.0000	1.0	ESE
10/22/2026 10:15	28.4	14.9	0.0	0.0100	0.0073	0.0000	1.1	NNE
10/22/2026 10:16	29.4	14.8	0.0	0.0100	0.0067	0.0000	1.1	E
10/22/2026 10:17	30.3	14.5	0.0	0.0100	0.0060	0.0000	1.1	NE
10/22/2026 10:18	29.9	16.2	0.0	0.0093	0.0053	0.0000	1.1	NNE
10/22/2026 10:19	32.4	14.7	0.0	0.0093	0.0040	0.0000	1.1	E
10/22/2026 10:20	33.2	14.3	0.0	0.0087	0.0040	0.0000	1.1	ESE
10/22/2026 10:21	35.4	12.6	0.0	0.0093	0.0033	0.0000	1.1	ENE
10/22/2026 10:22	33.8	14.1	0.0	0.0087	0.0040	0.0000	1.1	NNW
10/22/2026 10:23	34.9	14.0	0.0	0.0087	0.0033	0.0000	1.1	ENE
10/22/2026 10:24	33.8	17.0	0.0	0.0080	0.0033	0.0000	1.1	N
10/22/2026 10:25	35.0	17.2	0.0	0.0080	0.0027	0.0000	1.2	E
10/22/2026 10:26	49.9	19.5	0.0	0.0080	0.0027	0.0000	1.3	ENE
10/22/2026 10:27	63.5	20.9	0.0	0.0080	0.0027	0.0000	1.4	ENE
10/22/2026 10:28	74.2	22.2	0.0	0.0080	0.0027	0.0000	1.4	ENE
10/22/2026 10:29	80.6	23.4	0.0	0.0080	0.0020	0.0000	1.4	NE
10/22/2026 10:30	85.2	24.8	0.0	0.0080	0.0020	0.0000	1.4	ENE
10/22/2026 10:31	83.3	30.2	0.0	0.0073	0.0027	0.0000	1.3	N
10/22/2026 10:32	85.6	30.6	0.0	0.0080	0.0027	0.0000	1.3	E
10/22/2026 10:33	92.7	27.5	0.0	0.0093	0.0020	0.0000	1.4	ENE
10/22/2026 10:34	96.5	29.0	0.0	0.0093	0.0020	0.0000	1.5	ENE
10/22/2026 10:35	101.0	30.7	0.0	0.0093	0.0020	0.0000	1.4	E
10/22/2026 10:36	103.3	31.6	0.0	0.0093	0.0020	0.0000	1.4	NE
10/22/2026 10:37	107.5	30.1	0.0	0.0100	0.0013	0.0000	1.5	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 10:38	108.6	30.5	0.0	0.0107	0.0013	0.0000	1.5	ENE
10/22/2026 10:39	111.7	27.7	0.0	0.0120	0.0007	0.0000	1.5	ENE
10/22/2026 10:40	112.1	27.8	0.0	0.0120	0.0007	0.0000	1.4	NE
10/22/2026 10:41	98.8	26.3	0.0	0.0120	0.0007	0.0000	1.3	NNE
10/22/2026 10:42	86.9	25.6	0.0	0.0120	0.0007	0.0000	1.3	E
10/22/2026 10:43	76.1	27.0	0.0	0.0113	0.0013	0.0000	1.2	N
10/22/2026 10:44	70.1	26.6	0.0	0.0113	0.0013	0.0000	1.2	NE
10/22/2026 10:45	63.6	27.7	0.0	0.0107	0.0020	0.0000	1.1	NNW
10/22/2026 10:46	63.3	24.5	0.0	0.0107	0.0020	0.0000	1.0	NW
10/22/2026 10:47	59.2	26.5	0.0	0.0093	0.0027	0.0000	1.0	NNE
10/22/2026 10:48	52.8	28.6	0.0	0.0080	0.0033	0.0000	0.9	N
10/22/2026 10:49	46.7	29.4	0.0	0.0073	0.0040	0.0000	0.8	N
10/22/2026 10:50	40.6	30.0	0.0	0.0067	0.0047	0.0000	0.9	NNE
10/22/2026 10:51	37.9	29.9	0.0	0.0067	0.0047	0.0000	0.9	NE
10/22/2026 10:52	35.6	29.8	0.0	0.0067	0.0047	0.0000	0.9	ENE
10/22/2026 10:53	32.1	31.4	0.0	0.0053	0.0053	0.0000	0.9	NW
10/22/2026 10:54	28.9	32.9	3.9	0.0040	0.0060	0.0020	1.0	N
10/22/2026 10:55	25.9	34.3	8.4	0.0033	0.0067	0.0033	1.0	N
10/22/2026 10:56	22.9	35.3	12.4	0.0027	0.0073	0.0047	0.9	NW
10/22/2026 10:57	20.0	36.3	16.4	0.0020	0.0080	0.0060	0.9	NW
10/22/2026 10:58	19.0	35.4	16.3	0.0020	0.0080	0.0060	0.9	NNW
10/22/2026 10:59	16.5	36.1	19.7	0.0013	0.0087	0.0073	0.9	NNW
10/22/2026 11:00	17.7	33.6	15.8	0.0020	0.0080	0.0060	0.9	NE
10/22/2026 11:01	18.8	31.2	12.3	0.0027	0.0073	0.0047	0.9	ENE
10/22/2026 11:02	19.5	28.7	9.2	0.0033	0.0067	0.0033	0.9	NE
10/22/2026 11:03	20.4	26.2	5.8	0.0040	0.0060	0.0020	0.9	E
10/22/2026 11:04	21.4	23.9	2.5	0.0047	0.0053	0.0007	0.9	E
10/22/2026 11:05	21.9	21.3	0.0	0.0053	0.0047	0.0000	0.8	NE
10/22/2026 11:06	20.9	20.3	0.0	0.0060	0.0047	0.0000	0.8	NNE
10/22/2026 11:07	18.8	21.0	2.2	0.0053	0.0060	0.0007	0.9	N
10/22/2026 11:08	18.4	19.9	1.5	0.0053	0.0060	0.0007	0.9	NW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 11:09	19.3	17.7	0.0	0.0060	0.0053	0.0000	0.9	NNE
10/22/2026 11:10	18.9	17.0	0.0	0.0060	0.0053	0.0000	0.9	N
10/22/2026 11:11	18.5	16.2	0.0	0.0060	0.0053	0.0000	0.9	N
10/22/2026 11:12	19.6	14.3	0.0	0.0073	0.0047	0.0000	0.9	E
10/22/2026 11:13	20.5	12.4	0.0	0.0087	0.0040	0.0000	1.0	ENE
10/22/2026 11:14	21.9	10.7	0.0	0.0100	0.0033	0.0000	1.1	ENE
10/22/2026 11:15	21.4	10.6	0.0	0.0100	0.0033	0.0000	1.0	ESE
10/22/2026 11:16	21.0	10.8	0.0	0.0100	0.0033	0.0000	1.0	ENE
10/22/2026 11:17	20.5	11.0	0.0	0.0100	0.0033	0.0000	1.0	E
10/22/2026 11:18	19.9	10.8	0.0	0.0100	0.0033	0.0000	1.0	ENE
10/22/2026 11:19	18.2	11.7	0.0	0.0093	0.0040	0.0000	0.9	NNW
10/22/2026 11:20	17.8	11.7	0.0	0.0093	0.0040	0.0000	1.0	E
10/22/2026 11:21	17.7	11.7	0.0	0.0093	0.0040	0.0000	0.9	ENE
10/22/2026 11:22	19.3	10.3	0.0	0.0107	0.0027	0.0000	1.0	ENE
10/22/2026 11:23	19.3	10.6	0.0	0.0107	0.0033	0.0000	1.0	NNE
10/22/2026 11:24	18.1	12.1	0.0	0.0100	0.0040	0.0000	1.0	NNW
10/22/2026 11:25	19.5	10.8	0.0	0.0107	0.0033	0.0000	1.0	NNE
10/22/2026 11:26	20.5	9.7	0.0	0.0113	0.0027	0.0000	1.1	NE
10/22/2026 11:27	20.3	9.7	0.0	0.0107	0.0027	0.0000	1.1	E
10/22/2026 11:28	20.3	9.8	0.0	0.0100	0.0027	0.0000	1.1	E
10/22/2026 11:29	19.7	9.6	0.0	0.0100	0.0027	0.0000	1.1	NE
10/22/2026 11:30	19.5	9.6	0.0	0.0100	0.0027	0.0000	1.1	ENE
10/22/2026 11:31	19.1	9.3	0.0	0.0100	0.0027	0.0000	1.1	NE
10/22/2026 11:32	18.7	8.9	0.0	0.0100	0.0027	0.0000	1.1	E
10/22/2026 11:33	18.4	9.2	0.0	0.0100	0.0027	0.0000	1.0	E
10/22/2026 11:34	19.3	8.5	0.0	0.0107	0.0020	0.0000	1.0	S
10/22/2026 11:35	18.2	9.4	0.0	0.0100	0.0027	0.0000	0.9	NNW
10/22/2026 11:36	16.9	10.5	0.0	0.0087	0.0040	0.0000	0.9	NW
10/22/2026 11:37	15.3	11.8	0.0	0.0073	0.0053	0.0000	0.8	NW
10/22/2026 11:38	16.8	10.4	0.0	0.0080	0.0040	0.0000	0.8	ESE
10/22/2026 11:39	17.9	9.3	0.0	0.0087	0.0033	0.0000	0.8	ENE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 11:40	16.9	10.2	0.0	0.0080	0.0040	0.0000	0.7	N
10/22/2026 11:41	16.1	11.1	0.0	0.0073	0.0047	0.0000	0.7	NNW
10/22/2026 11:42	15.1	12.3	0.0	0.0067	0.0053	0.0000	0.7	N
10/22/2026 11:43	14.9	12.3	0.0	0.0067	0.0053	0.0000	0.6	NE
10/22/2026 11:44	15.0	12.3	0.0	0.0060	0.0053	0.0000	0.6	NNE
10/22/2026 11:45	15.1	12.3	0.0	0.0067	0.0053	0.0000	0.6	ENE
10/22/2026 11:46	14.9	12.2	0.0	0.0073	0.0053	0.0000	0.6	ENE
10/22/2026 11:47	13.9	13.3	0.0	0.0067	0.0067	0.0000	0.6	N
10/22/2026 11:48	15.0	12.9	0.0	0.0073	0.0067	0.0000	0.6	E
10/22/2026 11:49	18.3	12.4	0.0	0.0080	0.0067	0.0000	0.7	E
10/22/2026 11:50	18.2	14.2	0.0	0.0080	0.0073	0.0000	0.7	NW
10/22/2026 11:51	19.8	13.2	0.0	0.0093	0.0060	0.0000	0.7	ENE
10/22/2026 11:52	21.3	12.0	0.0	0.0107	0.0047	0.0000	0.8	NE
10/22/2026 11:53	21.8	12.0	0.0	0.0107	0.0047	0.0000	0.8	E
10/22/2026 11:54	22.6	12.1	0.0	0.0107	0.0047	0.0000	0.8	NE
10/22/2026 11:55	24.8	11.2	0.0	0.0113	0.0040	0.0000	0.9	E
10/22/2026 11:56	27.1	10.2	0.0	0.0120	0.0033	0.0000	0.9	NNE
10/22/2026 11:57	29.1	9.0	0.0	0.0127	0.0027	0.0000	0.9	NE
10/22/2026 11:58	29.7	8.9	0.0	0.0127	0.0027	0.0000	0.9	NNE
10/22/2026 11:59	28.5	10.3	0.0	0.0120	0.0033	0.0000	0.9	NNW
10/22/2026 12:00	27.3	11.6	0.0	0.0107	0.0047	0.0000	0.9	N
10/22/2026 12:01	28.6	11.6	0.0	0.0107	0.0047	0.0000	1.0	E
10/22/2026 12:02	33.7	10.6	0.0	0.0113	0.0033	0.0000	1.0	ESE
10/22/2026 12:03	34.2	10.7	0.0	0.0107	0.0033	0.0000	0.9	E
10/22/2026 12:04	32.0	10.7	0.0	0.0100	0.0033	0.0000	0.9	E
10/22/2026 12:05	33.9	7.9	0.0	0.0107	0.0020	0.0000	1.0	ENE
10/22/2026 12:06	33.7	7.8	0.0	0.0100	0.0020	0.0000	1.0	ENE
10/22/2026 12:07	33.4	7.8	0.0	0.0093	0.0020	0.0000	1.0	ESE
10/22/2026 12:08	32.9	7.6	0.0	0.0093	0.0020	0.0000	1.0	NE
10/22/2026 12:09	31.0	8.4	0.0	0.0087	0.0027	0.0000	0.9	WNW
10/22/2026 12:10	29.7	8.3	0.0	0.0087	0.0027	0.0000	0.8	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 12:11	28.1	8.4	0.0	0.0087	0.0027	0.0000	0.9	ENE
10/22/2026 12:12	27.2	8.5	0.0	0.0087	0.0027	0.0000	0.9	ENE
10/22/2026 12:13	26.6	8.6	0.0	0.0087	0.0027	0.0000	0.9	NE
10/22/2026 12:14	27.9	7.1	0.0	0.0093	0.0020	0.0000	0.9	ESE
10/22/2026 12:15	27.9	6.7	0.0	0.0093	0.0013	0.0000	0.8	WSW
10/22/2026 12:16	26.7	6.8	0.0	0.0087	0.0013	0.0000	0.8	NE
10/22/2026 12:17	23.3	6.7	0.0	0.0087	0.0013	0.0000	0.8	E
10/22/2026 12:18	22.1	6.6	0.0	0.0087	0.0013	0.0000	0.8	ENE
10/22/2026 12:19	20.0	7.7	0.0	0.0080	0.0020	0.0000	0.8	NNW
10/22/2026 12:20	19.1	7.7	0.0	0.0080	0.0020	0.0000	0.7	NE
10/22/2026 12:21	17.6	8.5	0.0	0.0073	0.0027	0.0000	0.7	N
10/22/2026 12:22	17.1	8.5	0.0	0.0073	0.0027	0.0000	0.7	NNE
10/22/2026 12:23	15.7	9.4	0.0	0.0067	0.0033	0.0000	0.7	N
10/22/2026 12:24	16.6	8.2	0.0	0.0073	0.0027	0.0000	0.8	NNE
10/22/2026 12:25	16.1	8.1	0.0	0.0073	0.0027	0.0000	0.8	ENE
10/22/2026 12:26	15.0	8.7	0.0	0.0067	0.0033	0.0000	0.8	NNW
10/22/2026 12:27	14.6	8.8	0.0	0.0067	0.0033	0.0000	0.8	E
10/22/2026 12:28	14.3	8.9	0.0	0.0067	0.0033	0.0000	0.8	E
10/22/2026 12:29	13.2	9.7	0.0	0.0060	0.0040	0.0000	0.8	NW
10/22/2026 12:30	13.4	9.6	0.0	0.0060	0.0047	0.0000	0.8	NW
10/22/2026 12:31	12.3	10.3	0.0	0.0053	0.0060	0.0007	0.8	NNW
10/22/2026 12:32	10.7	10.9	0.2	0.0047	0.0073	0.0027	0.8	N
10/22/2026 12:33	9.4	11.6	2.3	0.0040	0.0087	0.0047	0.8	NW
10/22/2026 12:34	9.3	11.2	1.9	0.0040	0.0093	0.0053	0.8	NW
10/22/2026 12:35	8.4	12.0	3.6	0.0033	0.0107	0.0073	0.9	NNW
10/22/2026 12:36	8.4	12.0	3.7	0.0033	0.0113	0.0080	0.9	NNW
10/22/2026 12:37	7.4	13.0	5.6	0.0027	0.0127	0.0100	0.9	NW
10/22/2026 12:38	8.3	12.0	3.7	0.0033	0.0120	0.0087	0.8	E
10/22/2026 12:39	9.1	12.1	3.0	0.0033	0.0120	0.0087	0.7	E
10/22/2026 12:40	9.9	12.3	2.4	0.0033	0.0120	0.0087	0.7	E
10/22/2026 12:41	12.0	11.9	0.0	0.0040	0.0113	0.0073	0.7	ENE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 12:42	12.8	12.1	0.0	0.0040	0.0113	0.0073	0.7	NNE
10/22/2026 12:43	13.4	11.9	0.0	0.0040	0.0113	0.0073	0.7	ESE
10/22/2026 12:44	14.9	11.2	0.0	0.0047	0.0107	0.0060	0.7	ENE
10/22/2026 12:45	14.8	12.3	0.0	0.0047	0.0100	0.0053	0.7	NNE
10/22/2026 12:46	14.8	13.0	0.0	0.0047	0.0093	0.0047	0.8	NNW
10/22/2026 12:47	15.2	13.6	0.0	0.0047	0.0087	0.0040	0.8	NNE
10/22/2026 12:48	16.5	13.0	0.0	0.0053	0.0073	0.0020	0.8	NNE
10/22/2026 12:49	16.5	13.9	0.0	0.0053	0.0067	0.0013	0.8	N
10/22/2026 12:50	18.7	13.2	0.0	0.0060	0.0053	0.0000	0.9	NE
10/22/2026 12:51	21.3	12.4	0.0	0.0067	0.0040	0.0000	0.9	NE
10/22/2026 12:52	24.0	11.5	0.0	0.0073	0.0027	0.0000	1.0	ENE
10/22/2026 12:53	23.0	14.4	0.0	0.0067	0.0033	0.0000	0.9	NNW
10/22/2026 12:54	21.2	17.0	0.0	0.0060	0.0040	0.0000	0.9	NW
10/22/2026 12:55	19.6	19.5	0.0	0.0053	0.0047	0.0000	0.9	N
10/22/2026 12:56	20.2	19.2	0.0	0.0053	0.0047	0.0000	0.9	E
10/22/2026 12:57	22.5	19.0	0.0	0.0053	0.0047	0.0000	0.9	NE
10/22/2026 12:58	24.8	19.1	0.0	0.0053	0.0047	0.0000	0.9	ENE
10/22/2026 12:59	52.1	19.0	0.0	0.0053	0.0047	0.0000	0.9	ESE
10/22/2026 13:00	76.4	16.9	0.0	0.0060	0.0040	0.0000	0.9	NE
10/22/2026 13:01	92.9	15.4	0.0	0.0067	0.0033	0.0000	0.9	E
10/22/2026 13:02	92.4	26.9	0.0	0.0067	0.0033	0.0000	0.8	NNW
10/22/2026 13:03	91.1	37.4	0.0	0.0060	0.0040	0.0000	0.8	NNW
10/22/2026 13:04	91.0	45.3	0.0	0.0060	0.0040	0.0000	0.7	NW
10/22/2026 13:05	99.3	45.3	0.0	0.0067	0.0040	0.0000	0.8	NE
10/22/2026 13:06	108.2	45.2	0.0	0.0067	0.0040	0.0000	0.7	ENE
10/22/2026 13:07	105.6	54.5	0.0	0.0060	0.0047	0.0000	0.7	NNW
10/22/2026 13:08	105.7	58.3	0.0	0.0060	0.0047	0.0000	0.7	NNW
10/22/2026 13:09	105.9	61.9	0.0	0.0060	0.0047	0.0000	0.8	NNW
10/22/2026 13:10	112.9	59.5	0.0	0.0067	0.0040	0.0000	0.7	ENE
10/22/2026 13:11	110.5	69.8	0.0	0.0060	0.0047	0.0000	0.8	N
10/22/2026 13:12	106.7	76.3	0.0	0.0053	0.0053	0.0000	0.8	N

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 13:13	108.8	76.4	0.0	0.0053	0.0053	0.0000	0.8	ENE
10/22/2026 13:14	86.3	76.5	0.0	0.0053	0.0053	0.0000	0.9	ENE
10/22/2026 13:15	68.3	77.8	9.4	0.0053	0.0053	0.0000	0.9	E
10/22/2026 13:16	60.9	78.5	17.7	0.0053	0.0053	0.0000	1.0	ENE
10/22/2026 13:17	61.4	72.5	11.1	0.0053	0.0053	0.0000	1.0	NNW
10/22/2026 13:18	61.7	67.5	5.8	0.0053	0.0053	0.0000	1.1	NNW
10/22/2026 13:19	62.1	63.3	1.2	0.0053	0.0053	0.0000	1.1	N
10/22/2026 13:20	58.7	64.1	5.3	0.0047	0.0053	0.0007	1.1	ENE
10/22/2026 13:21	55.3	64.8	9.5	0.0047	0.0053	0.0007	1.2	NNE
10/22/2026 13:22	64.9	56.4	0.0	0.0053	0.0047	0.0000	1.2	ENE
10/22/2026 13:23	78.3	50.1	0.0	0.0060	0.0040	0.0000	1.3	NE
10/22/2026 13:24	87.3	44.7	0.0	0.0067	0.0033	0.0000	1.4	NE
10/22/2026 13:25	80.7	52.8	0.0	0.0060	0.0040	0.0000	1.3	NNW
10/22/2026 13:26	90.1	42.9	0.0	0.0067	0.0033	0.0000	1.3	ESE
10/22/2026 13:27	96.8	36.5	0.0	0.0073	0.0027	0.0000	1.4	NE
10/22/2026 13:28	91.3	42.4	0.0	0.0067	0.0033	0.0000	1.3	NNW
10/22/2026 13:29	85.2	47.7	0.0	0.0060	0.0040	0.0000	1.2	NW
10/22/2026 13:30	83.5	47.4	0.0	0.0060	0.0040	0.0000	1.2	NNE
10/22/2026 13:31	81.1	47.2	0.0	0.0060	0.0040	0.0000	1.2	ENE
10/22/2026 13:32	89.2	40.8	0.0	0.0067	0.0033	0.0000	1.2	E
10/22/2026 13:33	106.4	36.1	0.0	0.0073	0.0027	0.0000	1.2	ESE
10/22/2026 13:34	106.5	41.3	0.0	0.0073	0.0027	0.0000	1.2	N
10/22/2026 13:35	99.9	48.4	0.0	0.0067	0.0033	0.0000	1.1	NNW
10/22/2026 13:36	92.2	54.3	0.0	0.0060	0.0040	0.0000	1.0	NNW
10/22/2026 13:37	88.8	53.9	0.0	0.0060	0.0040	0.0000	1.0	E
10/22/2026 13:38	81.6	53.6	0.0	0.0060	0.0053	0.0000	1.0	NNE
10/22/2026 13:39	73.0	61.3	0.0	0.0073	0.0060	0.0000	1.0	N
10/22/2026 13:40	72.6	60.9	0.0	0.0080	0.0060	0.0000	1.0	N
10/22/2026 13:41	72.4	60.8	0.0	0.0080	0.0060	0.0000	1.1	NE
10/22/2026 13:42	73.3	61.1	0.0	0.0080	0.0060	0.0000	1.1	E
10/22/2026 13:43	79.6	55.3	0.0	0.0087	0.0053	0.0000	1.0	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 13:44	79.4	55.8	0.0	0.0087	0.0053	0.0000	1.0	NNW
10/22/2026 13:45	80.3	55.2	0.0	0.0087	0.0053	0.0000	1.0	NE
10/22/2026 13:46	78.7	55.4	0.0	0.0093	0.0053	0.0000	1.0	NE
10/22/2026 13:47	74.7	55.4	0.0	0.0100	0.0053	0.0000	1.1	NNE
10/22/2026 13:48	61.7	54.9	0.0	0.0100	0.0053	0.0000	1.1	NNE
10/22/2026 13:49	65.6	44.7	0.0	0.0107	0.0047	0.0000	1.1	NNE
10/22/2026 13:50	71.2	37.4	0.0	0.0113	0.0040	0.0000	1.1	E
10/22/2026 13:51	77.2	31.8	0.0	0.0120	0.0033	0.0000	1.1	ENE
10/22/2026 13:52	71.5	37.1	0.0	0.0113	0.0040	0.0000	1.1	NW
10/22/2026 13:53	70.2	37.3	0.0	0.0113	0.0027	0.0000	1.0	E
10/22/2026 13:54	70.0	33.6	0.0	0.0093	0.0027	0.0000	1.0	NNW
10/22/2026 13:55	70.1	30.3	0.0	0.0087	0.0027	0.0000	1.0	NNE
10/22/2026 13:56	65.9	30.5	0.0	0.0087	0.0027	0.0000	1.0	ENE
10/22/2026 13:57	75.5	34.0	0.0	0.0087	0.0027	0.0000	1.1	ENE
10/22/2026 13:58	83.6	37.0	0.0	0.0093	0.0027	0.0000	1.1	E
10/22/2026 13:59	98.1	33.0	0.0	0.0107	0.0020	0.0000	1.2	E
10/22/2026 14:00	103.1	33.8	0.0	0.0107	0.0020	0.0000	1.2	E
10/22/2026 14:01	107.1	33.6	0.0	0.0100	0.0020	0.0000	1.1	NE
10/22/2026 14:02	102.7	41.0	0.0	0.0087	0.0027	0.0000	1.0	WNW
10/22/2026 14:03	104.5	40.9	0.0	0.0087	0.0027	0.0000	1.1	NE
10/22/2026 14:04	106.3	41.1	0.0	0.0087	0.0027	0.0000	1.1	ENE
10/22/2026 14:05	107.1	41.9	0.0	0.0087	0.0027	0.0000	1.1	E
10/22/2026 14:06	109.7	42.0	0.0	0.0093	0.0027	0.0000	1.0	NE
10/22/2026 14:07	116.8	36.8	0.0	0.0100	0.0020	0.0000	1.2	NE
10/22/2026 14:08	119.7	37.8	0.0	0.0100	0.0020	0.0000	1.3	E
10/22/2026 14:09	127.9	35.0	0.0	0.0107	0.0013	0.0000	1.4	ESE
10/22/2026 14:10	135.3	31.4	0.0	0.0113	0.0007	0.0000	1.4	NE
10/22/2026 14:11	142.2	31.8	0.0	0.0113	0.0007	0.0000	1.5	ENE
10/22/2026 14:12	136.1	28.4	0.0	0.0113	0.0007	0.0000	1.4	NE
10/22/2026 14:13	135.0	26.3	0.0	0.0107	0.0007	0.0000	1.4	ENE
10/22/2026 14:14	140.1	25.3	0.0	0.0100	0.0007	0.0000	1.4	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 14:15	130.2	40.2	0.0	0.0093	0.0013	0.0000	1.5	NNE
10/22/2026 14:16	138.0	40.7	0.0	0.0093	0.0013	0.0000	1.4	E
10/22/2026 14:17	138.3	44.8	0.0	0.0093	0.0013	0.0000	1.5	N
10/22/2026 14:18	142.1	44.7	0.0	0.0093	0.0013	0.0000	1.5	ENE
10/22/2026 14:19	144.8	44.7	0.0	0.0093	0.0013	0.0000	1.5	ENE
10/22/2026 14:20	147.1	43.8	0.0	0.0093	0.0013	0.0000	1.5	NE
10/22/2026 14:21	138.7	50.9	0.0	0.0080	0.0020	0.0000	1.5	N
10/22/2026 14:22	138.8	50.8	0.0	0.0080	0.0020	0.0000	1.5	NNE
10/22/2026 14:23	131.4	56.3	0.0	0.0073	0.0027	0.0000	1.3	N
10/22/2026 14:24	123.4	60.7	0.0	0.0067	0.0033	0.0000	1.3	NNW
10/22/2026 14:25	116.4	65.7	0.0	0.0060	0.0040	0.0000	1.2	N
10/22/2026 14:26	105.2	70.7	0.0	0.0053	0.0047	0.0000	1.1	N
10/22/2026 14:27	94.7	75.5	0.0	0.0047	0.0060	0.0013	1.0	WNW
10/22/2026 14:28	81.5	79.7	0.0	0.0040	0.0073	0.0033	0.9	WNW
10/22/2026 14:29	62.2	83.6	21.3	0.0033	0.0087	0.0053	0.9	N
10/22/2026 14:30	66.7	68.0	1.3	0.0047	0.0080	0.0033	0.8	E
10/22/2026 14:31	58.2	67.7	9.5	0.0053	0.0080	0.0027	0.8	E
10/22/2026 14:32	66.4	56.5	0.0	0.0067	0.0073	0.0007	0.8	E
10/22/2026 14:33	64.1	57.3	0.0	0.0073	0.0073	0.0000	0.7	S
10/22/2026 14:34	56.0	64.1	8.1	0.0067	0.0080	0.0013	0.7	N
10/22/2026 14:35	53.1	64.0	10.9	0.0067	0.0080	0.0013	0.7	E
10/22/2026 14:36	59.0	56.6	0.0	0.0073	0.0073	0.0000	0.7	ENE
10/22/2026 14:37	52.3	62.1	9.7	0.0067	0.0080	0.0013	0.7	N
10/22/2026 14:38	57.9	56.5	0.0	0.0073	0.0073	0.0000	0.7	ESE
10/22/2026 14:39	63.2	51.0	0.0	0.0080	0.0067	0.0000	0.8	NNE
10/22/2026 14:40	63.3	50.2	0.0	0.0080	0.0067	0.0000	0.7	NW
10/22/2026 14:41	68.9	45.0	0.0	0.0087	0.0060	0.0000	0.8	ENE
10/22/2026 14:42	69.0	49.5	0.0	0.0087	0.0053	0.0000	0.9	N
10/22/2026 14:43	75.5	44.8	0.0	0.0093	0.0040	0.0000	1.1	NE
10/22/2026 14:44	82.1	40.8	0.0	0.0100	0.0027	0.0000	1.2	ENE
10/22/2026 14:45	84.2	41.1	0.0	0.0100	0.0027	0.0000	1.2	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 14:46	83.5	41.0	0.0	0.0093	0.0027	0.0000	1.2	ENE
10/22/2026 14:47	75.4	46.8	0.0	0.0080	0.0040	0.0000	1.1	N
10/22/2026 14:48	67.9	51.4	0.0	0.0067	0.0047	0.0000	1.2	NNW
10/22/2026 14:49	67.2	49.3	0.0	0.0067	0.0047	0.0000	1.2	NNW
10/22/2026 14:50	65.8	49.2	0.0	0.0067	0.0047	0.0000	1.2	NNE
10/22/2026 14:51	63.9	49.1	0.0	0.0067	0.0047	0.0000	1.2	NE
10/22/2026 14:52	63.5	47.3	0.0	0.0067	0.0047	0.0000	1.2	NW
10/22/2026 14:53	62.3	47.0	0.0	0.0067	0.0047	0.0000	1.2	ESE
10/22/2026 14:54	61.8	47.0	0.0	0.0067	0.0047	0.0000	1.2	NE
10/22/2026 14:55	66.7	42.7	0.0	0.0073	0.0040	0.0000	1.3	ENE
10/22/2026 14:56	66.4	43.0	0.0	0.0073	0.0040	0.0000	1.2	ENE
10/22/2026 14:57	66.2	38.2	0.0	0.0073	0.0040	0.0000	1.3	NNE
10/22/2026 14:58	64.3	38.5	0.0	0.0073	0.0040	0.0000	1.2	E
10/22/2026 14:59	62.6	38.5	0.0	0.0073	0.0040	0.0000	1.2	ENE
10/22/2026 15:00	60.4	38.7	0.0	0.0067	0.0040	0.0000	1.2	ENE
10/22/2026 15:01	59.1	39.0	0.0	0.0067	0.0040	0.0000	1.3	ENE
10/22/2026 15:02	68.6	33.2	0.0	0.0073	0.0027	0.0000	1.4	E
10/22/2026 15:03	78.3	28.6	0.0	0.0080	0.0020	0.0000	1.4	NNE
10/22/2026 15:04	85.9	24.3	0.0	0.0087	0.0013	0.0000	1.6	ENE
10/22/2026 15:05	88.5	24.5	0.0	0.0087	0.0013	0.0000	1.5	NE
10/22/2026 15:06	94.2	24.3	0.0	0.0087	0.0013	0.0000	1.5	E
10/22/2026 15:07	106.5	20.7	0.0	0.0093	0.0007	0.0000	1.7	E
10/22/2026 15:08	102.2	35.0	0.0	0.0087	0.0013	0.0000	1.6	NNW
10/22/2026 15:09	144.9	34.3	0.0	0.0087	0.0013	0.0000	1.6	ENE
10/22/2026 15:10	169.5	33.6	0.0	0.0087	0.0013	0.0000	1.6	ENE
10/22/2026 15:11	183.9	32.9	0.0	0.0087	0.0013	0.0000	1.6	NE
10/22/2026 15:12	199.6	27.7	0.0	0.0093	0.0007	0.0000	1.5	NE
10/22/2026 15:13	208.2	27.1	0.0	0.0093	0.0007	0.0000	1.5	ENE
10/22/2026 15:14	215.4	26.5	0.0	0.0093	0.0007	0.0000	1.5	E
10/22/2026 15:15	210.6	36.5	0.0	0.0087	0.0013	0.0000	1.3	W
10/22/2026 15:16	204.6	45.5	0.0	0.0080	0.0020	0.0000	1.2	NNE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 15:17	204.2	44.7	0.0	0.0080	0.0020	0.0000	1.2	E
10/22/2026 15:18	203.7	43.7	0.0	0.0080	0.0020	0.0000	1.2	E
10/22/2026 15:19	204.5	42.9	0.0	0.0080	0.0020	0.0000	1.0	SE
10/22/2026 15:20	197.1	50.0	0.0	0.0073	0.0027	0.0000	0.9	NW
10/22/2026 15:21	186.8	57.4	0.0	0.0067	0.0033	0.0000	0.8	NW
10/22/2026 15:22	180.7	56.8	0.0	0.0073	0.0033	0.0000	0.8	E
10/22/2026 15:23	187.4	41.5	0.0	0.0080	0.0027	0.0000	0.9	ESE
10/22/2026 15:24	146.0	41.1	0.0	0.0080	0.0027	0.0000	0.9	ENE
10/22/2026 15:25	124.4	40.8	0.0	0.0080	0.0027	0.0000	0.8	E
10/22/2026 15:26	114.1	40.5	0.0	0.0080	0.0027	0.0000	0.9	E
10/22/2026 15:27	105.7	40.3	0.0	0.0080	0.0027	0.0000	0.9	E
10/22/2026 15:28	99.1	39.9	0.0	0.0080	0.0027	0.0000	0.8	ENE
10/22/2026 15:29	93.4	39.6	0.0	0.0080	0.0027	0.0000	0.8	ENE
10/22/2026 15:30	98.8	28.9	0.0	0.0087	0.0020	0.0000	1.0	ENE
10/22/2026 15:31	103.9	19.0	0.0	0.0093	0.0013	0.0000	1.0	NE
10/22/2026 15:32	100.8	18.9	0.0	0.0093	0.0013	0.0000	1.0	ENE
10/22/2026 15:33	98.1	18.9	0.0	0.0093	0.0013	0.0000	1.0	ENE
10/22/2026 15:34	95.4	18.8	0.0	0.0093	0.0013	0.0000	1.1	NE
10/22/2026 15:35	101.2	11.1	0.0	0.0100	0.0007	0.0000	1.2	NE
10/22/2026 15:36	106.8	3.0	0.0	0.0107	0.0000	0.0000	1.3	E
10/22/2026 15:37	105.3	3.0	0.0	0.0100	0.0000	0.0000	1.3	NNE
10/22/2026 15:38	103.2	3.1	0.0	0.0100	0.0000	0.0000	1.2	NE
10/22/2026 15:39	102.0	3.2	0.0	0.0100	0.0000	0.0000	1.2	ESE
10/22/2026 15:40	99.1	3.2	0.0	0.0100	0.0000	0.0000	1.2	E
10/22/2026 15:41	96.3	3.2	0.0	0.0100	0.0000	0.0000	1.2	ESE
10/22/2026 15:42	94.8	3.4	0.0	0.0100	0.0000	0.0000	1.3	ENE
10/22/2026 15:43	87.6	9.7	0.0	0.0093	0.0007	0.0000	1.1	WSW
10/22/2026 15:44	87.0	9.7	0.0	0.0093	0.0007	0.0000	1.2	E
10/22/2026 15:45	87.0	9.7	0.0	0.0093	0.0007	0.0000	1.2	E
10/22/2026 15:46	86.8	9.8	0.0	0.0093	0.0007	0.0000	1.2	NNE
10/22/2026 15:47	85.2	9.9	0.0	0.0093	0.0007	0.0000	1.1	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 15:48	78.2	14.9	0.0	0.0087	0.0013	0.0000	1.0	WNW
10/22/2026 15:49	76.6	15.1	0.0	0.0087	0.0013	0.0000	1.0	ENE
10/22/2026 15:50	75.1	15.2	0.0	0.0087	0.0013	0.0000	1.0	NE
10/22/2026 15:51	73.8	15.3	0.0	0.0093	0.0013	0.0000	1.0	ESE
10/22/2026 15:52	68.5	19.6	0.0	0.0087	0.0027	0.0000	0.9	NW
10/22/2026 15:53	63.5	24.1	0.0	0.0080	0.0040	0.0000	0.8	WNW
10/22/2026 15:54	58.0	28.6	0.0	0.0073	0.0053	0.0000	0.8	NNW
10/22/2026 15:55	52.4	32.4	0.0	0.0067	0.0067	0.0000	0.6	NW
10/22/2026 15:56	45.3	36.0	0.0	0.0060	0.0073	0.0013	0.6	NW
10/22/2026 15:57	39.2	39.6	0.4	0.0053	0.0080	0.0027	0.6	N
10/22/2026 15:58	39.4	36.9	0.0	0.0053	0.0080	0.0027	0.6	W
10/22/2026 15:59	33.3	40.4	7.1	0.0047	0.0087	0.0040	0.6	WNW
10/22/2026 16:00	31.2	40.3	9.1	0.0047	0.0087	0.0040	0.6	E
10/22/2026 16:01	30.4	40.2	9.8	0.0047	0.0087	0.0040	0.5	NNE
10/22/2026 16:02	25.7	44.5	18.8	0.0040	0.0093	0.0053	0.7	NW
10/22/2026 16:03	29.6	39.7	10.1	0.0047	0.0087	0.0040	0.6	ESE
10/22/2026 16:04	25.4	43.4	17.9	0.0040	0.0093	0.0053	0.6	NW
10/22/2026 16:05	25.5	43.4	18.0	0.0040	0.0093	0.0053	0.6	E
10/22/2026 16:06	25.8	43.5	17.7	0.0033	0.0093	0.0060	0.6	E
10/22/2026 16:07	30.2	39.5	9.3	0.0040	0.0080	0.0040	0.5	E
10/22/2026 16:08	35.5	35.0	0.0	0.0047	0.0067	0.0020	0.6	ENE
10/22/2026 16:09	39.8	30.5	0.0	0.0053	0.0053	0.0000	0.5	E
10/22/2026 16:10	43.6	26.8	0.0	0.0060	0.0040	0.0000	0.6	ENE
10/22/2026 16:11	43.5	26.9	0.0	0.0060	0.0040	0.0000	0.6	NNW
10/22/2026 16:12	48.0	23.3	0.0	0.0067	0.0033	0.0000	0.6	NE
10/22/2026 16:13	55.4	20.2	0.0	0.0073	0.0027	0.0000	0.8	NE
10/22/2026 16:14	61.6	16.8	0.0	0.0080	0.0020	0.0000	0.9	NNE
10/22/2026 16:15	63.9	16.9	0.0	0.0080	0.0020	0.0000	0.9	NE
10/22/2026 16:16	65.7	17.1	0.0	0.0080	0.0020	0.0000	0.9	NE
10/22/2026 16:17	65.9	18.2	0.0	0.0080	0.0020	0.0000	1.0	N
10/22/2026 16:18	67.1	18.3	0.0	0.0080	0.0020	0.0000	1.0	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/22/2026 16:19	72.0	14.7	0.0	0.0087	0.0013	0.0000	1.1	NE
10/22/2026 16:20	78.4	14.7	0.0	0.0087	0.0013	0.0000	1.1	NNE
10/22/2026 16:21	81.2	14.6	0.0	0.0087	0.0013	0.0000	1.1	E
10/22/2026 16:22	85.6	14.6	0.0	0.0087	0.0013	0.0000	1.1	ESE
10/22/2026 16:23	98.7	14.9	0.0	0.0087	0.0013	0.0000	1.1	E
10/22/2026 16:24	107.9	15.3	0.0	0.0087	0.0013	0.0000	1.1	SE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/26/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 53-72°F, Sunny, RH: 54% Pres: 30.31” Wind: W @ 8 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Capstone installed tiebacks along the northern boundary of the site.
- Capstone installed foundation piles within grid A1.
- Glenco received and unloaded deliveries of foundation piles for future installation.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:03-15:23. No exceedances of volatile organic compounds (VOCs) were encountered. An exceedance of dust action levels was encountered between 14:37 and 14:53 caused by the drilling of foundation piles directly adjacent to the SOE, where mist being released by the drill rig was captured by the air intake. The station was moved several feet from the drilling activity.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/26/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 53-72°F, Sunny, RH: 54% Pres: 30.31” Wind: W @ 8 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

Sampling Performed:

None.


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks and foundation piles along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/26/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 53-72°F, Sunny, RH: 54% Pres: 30.31” Wind: W @ 8 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

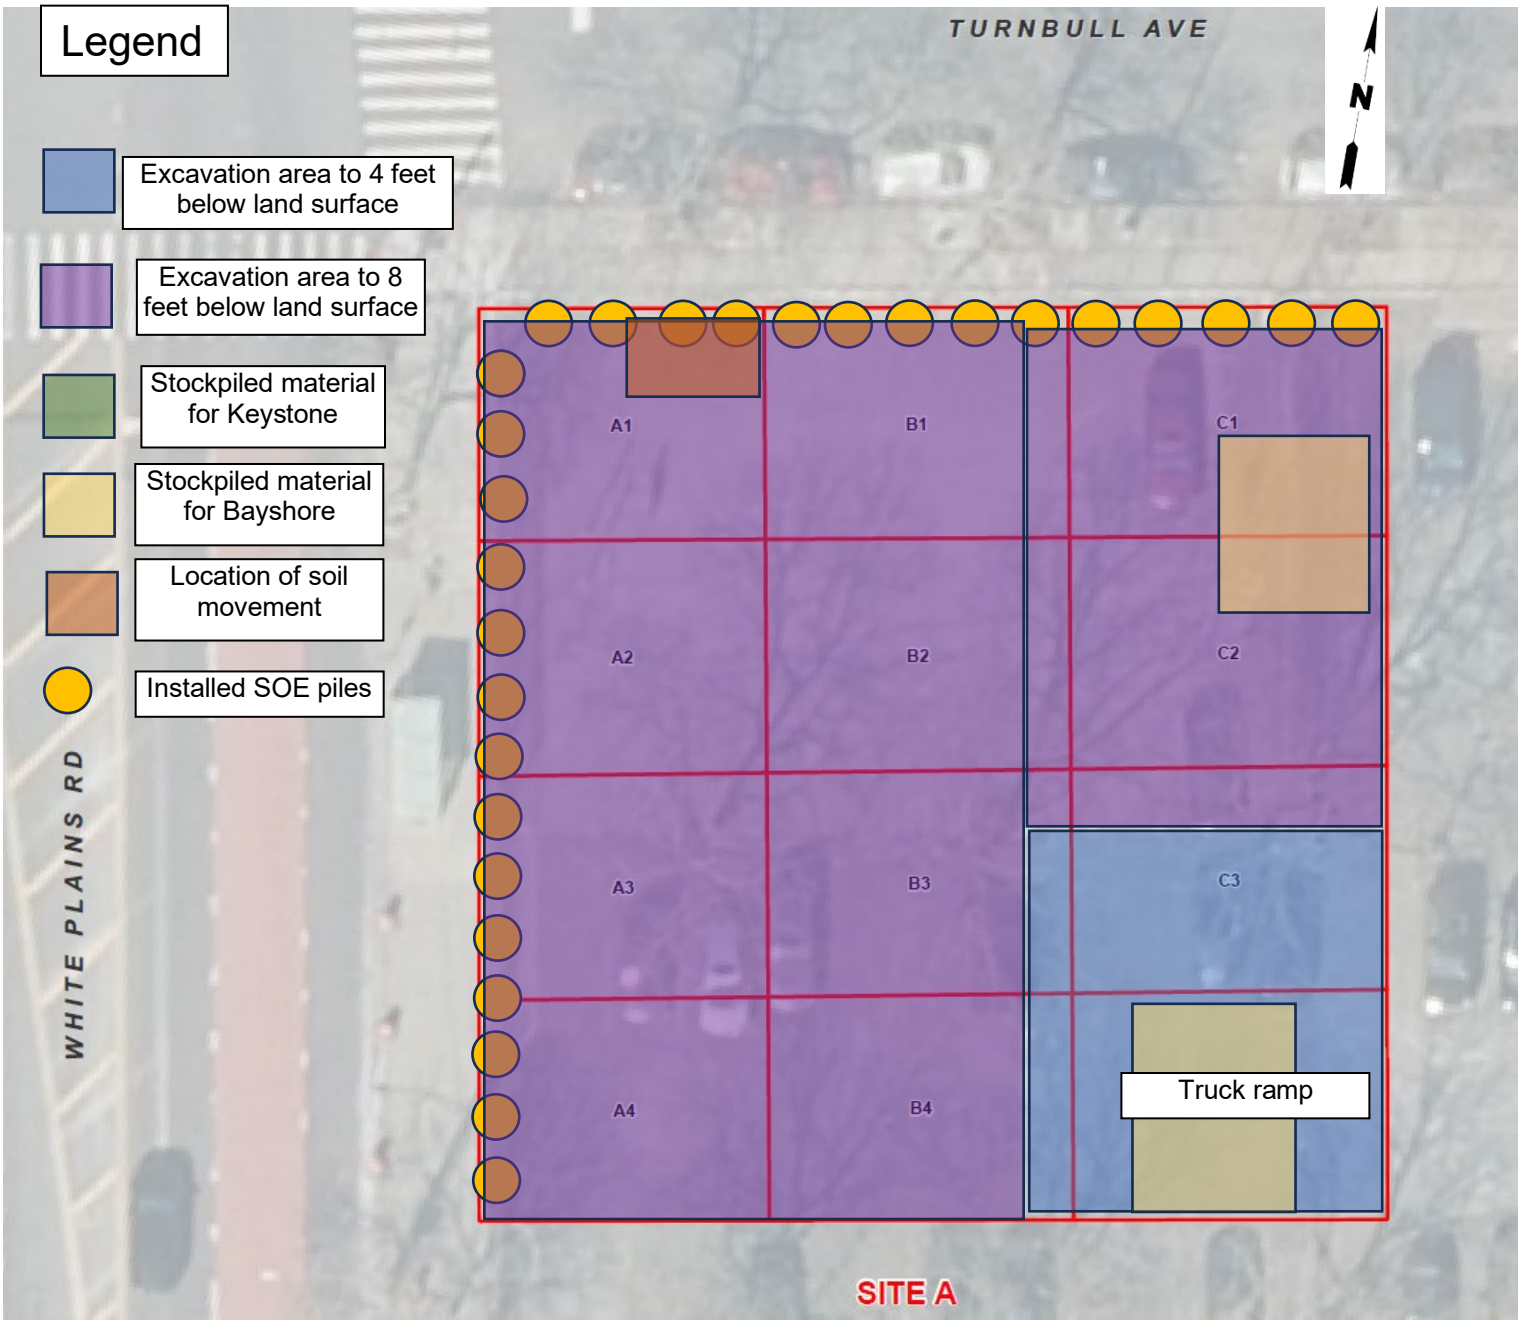

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/26/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 53-72°F, Sunny, RH: 54% Pres: 30.31” Wind: W @ 8 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Capstone installs tiebacks along the northern boundary of the site.



Photo 2:
Facing north, Capstone installing foundation piles within the northern portion of the site in grid A1.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/26/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 53-72°F, Sunny, RH: 54% Pres: 30.31” Wind: W @ 8 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

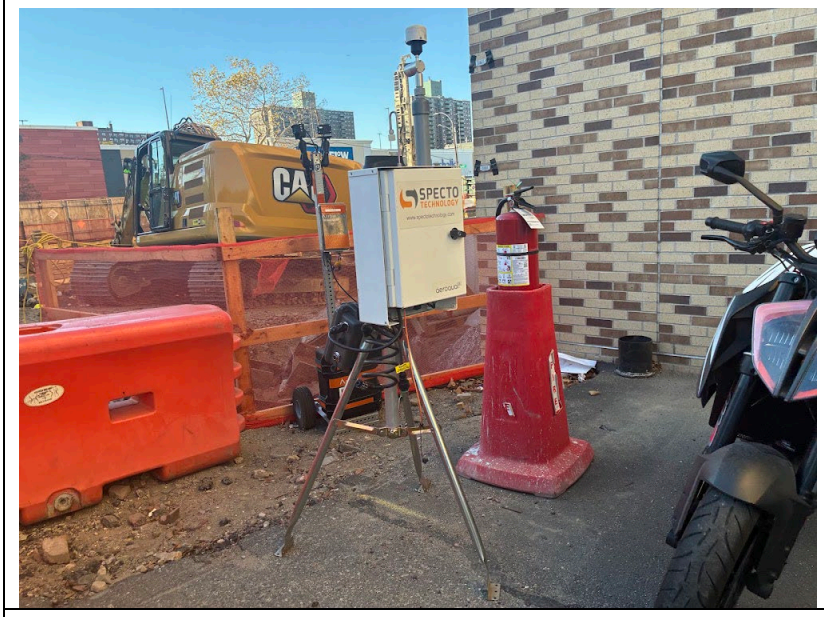


Photo 3:
Facing northwest, view of south CAMP station located within the southeastern site corner.



Photo 4: Facing northeast, Glenco receives truckload of foundation piles for future installation.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/26/2026 07:00
		To: 10/26/2026 16:30


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/26/2026	47.1 - 78.6	29.0 - 64.8	30.1 - 30.4	0.3 - 6.9	ESE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/26/2026	0.0	07:29	0.0000	07:03
Max Contribution (15 min avg.) - 10/26/2026	473.8	14:42	0.0257	07:09
Daily Avg. Contribution (15 min avg.) - 10/26/2026	19.4	-	0.0051	-

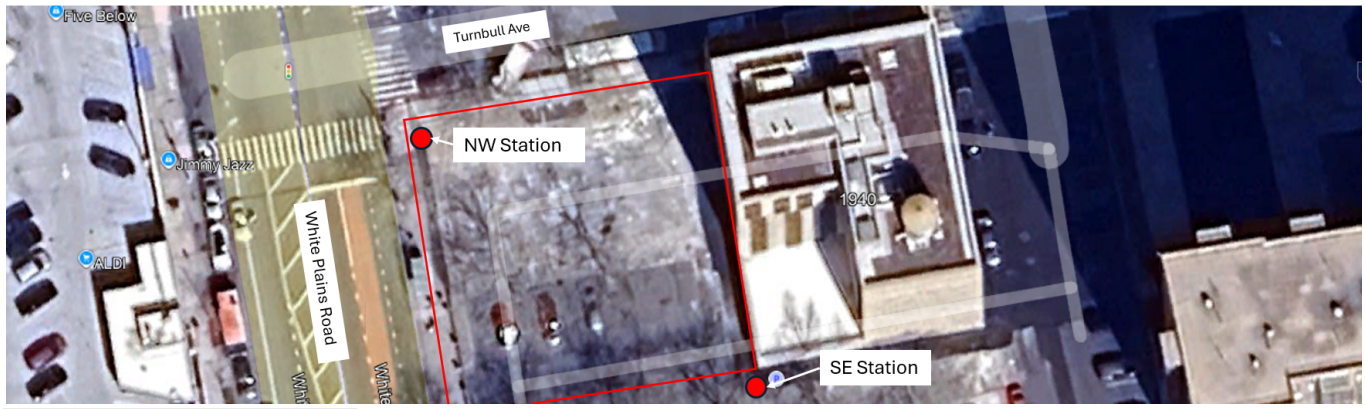


PM10 Average Contribution (µg/m³)

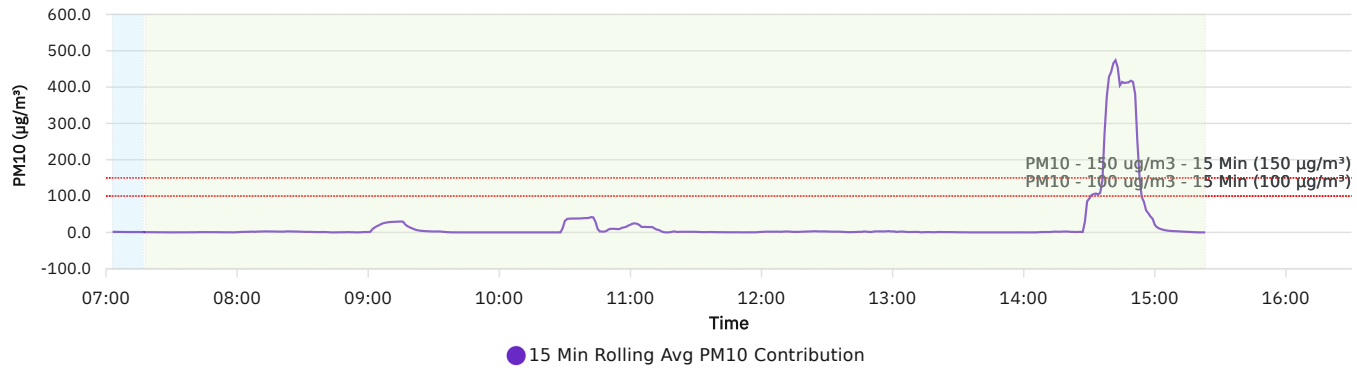

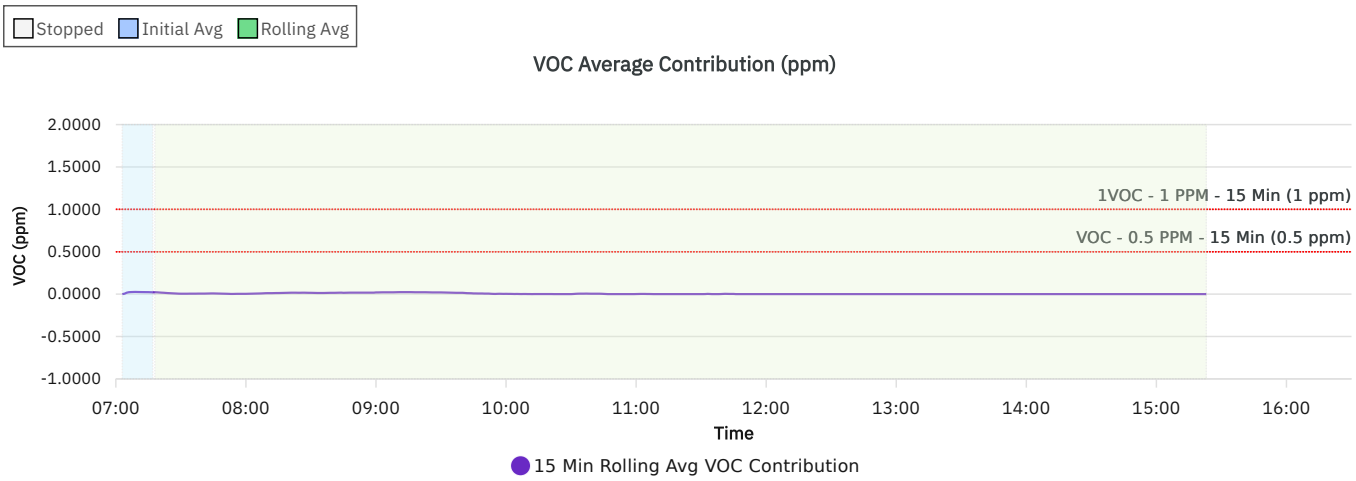

Wind rose (mph)

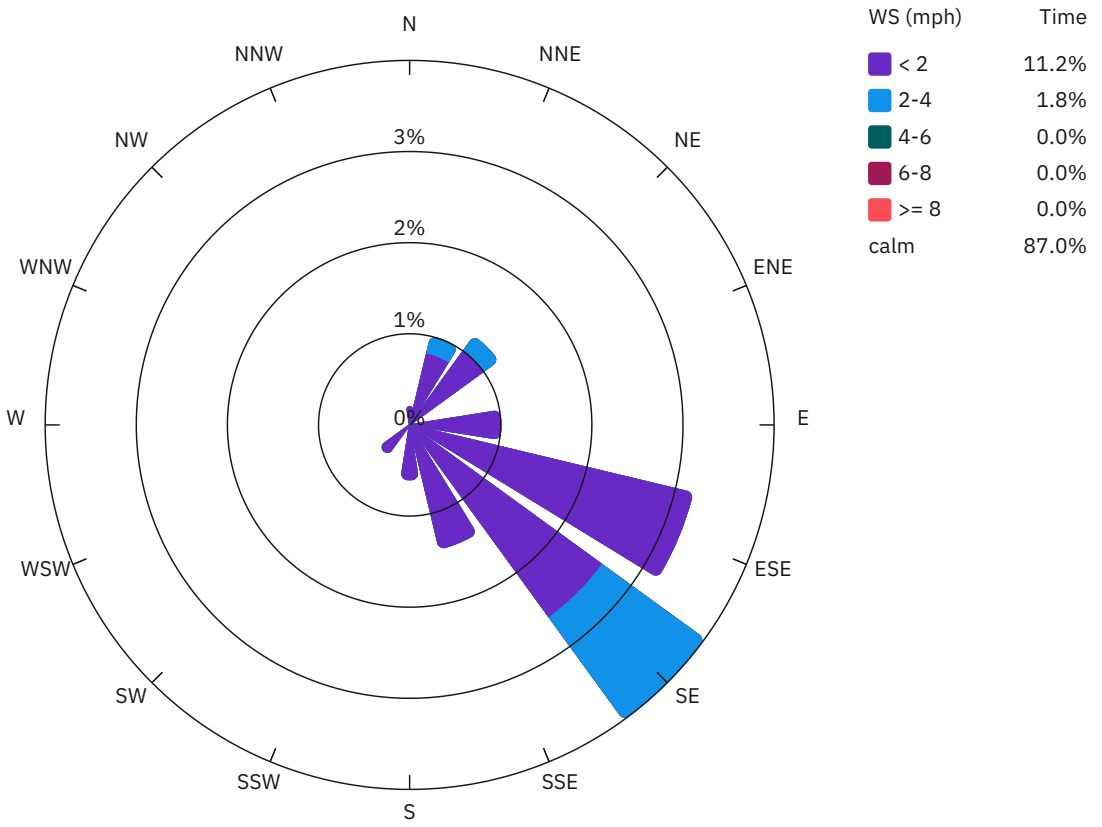

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 07:03	5.7	7.2	1.5	0.0000	0.0000	0.0000	0.7	E
10/26/2026 07:04	5.7	7.1	1.4	0.0000	0.0050	0.0050	0.8	SE
10/26/2026 07:05	5.7	7.0	1.3	0.0000	0.0167	0.0167	0.8	SE
10/26/2026 07:06	5.7	7.0	1.3	0.0000	0.0225	0.0225	0.9	ESE
10/26/2026 07:07	5.8	7.0	1.2	0.0020	0.0260	0.0240	0.7	S
10/26/2026 07:08	5.9	6.9	1.0	0.0033	0.0283	0.0250	0.7	ESE
10/26/2026 07:09	5.9	6.9	1.0	0.0043	0.0300	0.0257	0.7	ESE
10/26/2026 07:10	5.8	6.8	1.0	0.0050	0.0300	0.0250	0.7	SE
10/26/2026 07:11	5.9	6.8	0.9	0.0056	0.0300	0.0244	0.7	ESE
10/26/2026 07:12	5.9	6.8	0.9	0.0060	0.0300	0.0240	0.7	ESE
10/26/2026 07:13	5.8	6.8	1.0	0.0064	0.0300	0.0236	0.7	E
10/26/2026 07:14	5.8	6.7	1.0	0.0067	0.0300	0.0233	0.7	E
10/26/2026 07:15	5.7	6.6	0.9	0.0069	0.0300	0.0231	0.6	NE
10/26/2026 07:16	5.8	6.5	0.8	0.0071	0.0293	0.0221	0.6	E
10/26/2026 07:17	5.8	6.4	0.7	0.0073	0.0287	0.0213	0.6	ENE
10/26/2026 07:18	5.8	6.4	0.6	0.0080	0.0300	0.0220	0.6	SE
10/26/2026 07:19	5.8	6.3	0.6	0.0093	0.0307	0.0213	0.6	E
10/26/2026 07:20	5.8	6.3	0.5	0.0107	0.0300	0.0193	0.6	ESE
10/26/2026 07:21	5.8	6.2	0.5	0.0120	0.0293	0.0173	0.5	ESE
10/26/2026 07:22	5.7	6.2	0.5	0.0127	0.0287	0.0160	0.6	E
10/26/2026 07:23	5.7	6.2	0.4	0.0133	0.0273	0.0140	0.6	E
10/26/2026 07:24	5.8	6.1	0.3	0.0140	0.0260	0.0120	0.6	ESE
10/26/2026 07:25	5.8	6.1	0.3	0.0147	0.0253	0.0107	0.6	E
10/26/2026 07:26	5.8	6.1	0.2	0.0153	0.0247	0.0093	0.6	ESE
10/26/2026 07:27	5.9	6.0	0.2	0.0160	0.0240	0.0080	0.6	SE
10/26/2026 07:28	6.0	6.0	0.1	0.0167	0.0233	0.0067	0.6	ESE
10/26/2026 07:29	6.0	6.0	0.0	0.0173	0.0227	0.0053	0.6	ESE
10/26/2026 07:30	6.1	6.1	0.0	0.0180	0.0227	0.0047	0.6	ESE
10/26/2026 07:31	6.1	6.2	0.1	0.0187	0.0233	0.0047	0.6	ESE
10/26/2026 07:32	6.2	6.3	0.1	0.0193	0.0240	0.0047	0.6	SE
10/26/2026 07:33	6.3	6.5	0.2	0.0200	0.0247	0.0047	0.6	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 07:34	6.3	6.5	0.2	0.0200	0.0253	0.0053	0.7	ESE
10/26/2026 07:35	6.4	6.5	0.1	0.0200	0.0253	0.0053	0.7	ESE
10/26/2026 07:36	6.3	6.5	0.1	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:37	6.3	6.5	0.2	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:38	6.3	6.5	0.2	0.0200	0.0260	0.0060	0.8	SE
10/26/2026 07:39	6.3	6.5	0.3	0.0200	0.0260	0.0060	0.7	ESE
10/26/2026 07:40	6.2	6.6	0.3	0.0200	0.0260	0.0060	0.8	ESE
10/26/2026 07:41	6.3	6.6	0.3	0.0200	0.0260	0.0060	0.8	E
10/26/2026 07:42	6.4	6.8	0.5	0.0200	0.0267	0.0067	0.8	ESE
10/26/2026 07:43	6.4	7.0	0.7	0.0200	0.0273	0.0073	0.8	ESE
10/26/2026 07:44	6.4	7.1	0.7	0.0200	0.0280	0.0080	0.8	ESE
10/26/2026 07:45	6.4	7.1	0.7	0.0200	0.0280	0.0080	0.8	SE
10/26/2026 07:46	6.5	7.1	0.6	0.0200	0.0273	0.0073	0.8	E
10/26/2026 07:47	6.5	7.0	0.6	0.0200	0.0267	0.0067	0.8	ESE
10/26/2026 07:48	6.3	6.9	0.5	0.0200	0.0260	0.0060	0.8	ESE
10/26/2026 07:49	6.3	6.9	0.5	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:50	6.3	6.9	0.6	0.0200	0.0247	0.0047	0.8	SE
10/26/2026 07:51	6.4	6.9	0.5	0.0200	0.0240	0.0040	0.8	E
10/26/2026 07:52	6.6	7.0	0.4	0.0200	0.0233	0.0033	0.8	E
10/26/2026 07:53	6.7	7.1	0.4	0.0207	0.0227	0.0020	0.7	NNW
10/26/2026 07:54	6.8	7.0	0.2	0.0207	0.0227	0.0020	0.7	NE
10/26/2026 07:55	6.9	7.2	0.3	0.0207	0.0233	0.0027	0.6	NE
10/26/2026 07:56	7.0	7.2	0.2	0.0207	0.0240	0.0033	0.6	ENE
10/26/2026 07:57	6.9	7.1	0.2	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 07:58	6.9	7.0	0.1	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 07:59	6.9	7.0	0.1	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 08:00	6.8	7.5	0.6	0.0207	0.0240	0.0033	0.6	SE
10/26/2026 08:01	6.8	7.6	0.8	0.0207	0.0247	0.0040	0.6	ESE
10/26/2026 08:02	6.9	8.0	1.2	0.0207	0.0253	0.0047	0.6	ESE
10/26/2026 08:03	7.0	8.4	1.4	0.0207	0.0260	0.0053	0.6	E
10/26/2026 08:04	7.1	8.6	1.5	0.0207	0.0267	0.0060	0.6	SSE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 08:05	7.1	8.6	1.5	0.0207	0.0273	0.0067	0.6	ESE
10/26/2026 08:06	7.0	8.9	1.9	0.0207	0.0280	0.0073	0.6	E
10/26/2026 08:07	7.0	9.0	2.0	0.0207	0.0287	0.0080	0.6	SE
10/26/2026 08:08	8.0	9.5	1.5	0.0200	0.0293	0.0093	0.6	SE
10/26/2026 08:09	8.1	10.2	2.1	0.0200	0.0307	0.0107	0.6	ESE
10/26/2026 08:10	8.2	10.3	2.1	0.0200	0.0313	0.0113	0.7	E
10/26/2026 08:11	8.1	10.5	2.4	0.0200	0.0313	0.0113	0.7	SSE
10/26/2026 08:12	8.1	10.6	2.5	0.0200	0.0313	0.0113	0.7	SE
10/26/2026 08:13	8.1	10.7	2.7	0.0200	0.0320	0.0120	0.7	SE
10/26/2026 08:14	8.1	10.8	2.7	0.0200	0.0327	0.0127	0.7	ESE
10/26/2026 08:15	8.1	10.5	2.4	0.0200	0.0327	0.0127	0.7	ESE
10/26/2026 08:16	8.1	10.6	2.5	0.0200	0.0333	0.0133	0.7	SE
10/26/2026 08:17	8.0	10.4	2.4	0.0200	0.0340	0.0140	0.7	SE
10/26/2026 08:18	8.0	10.1	2.1	0.0200	0.0347	0.0147	0.7	SE
10/26/2026 08:19	7.9	10.1	2.1	0.0200	0.0353	0.0153	0.7	SE
10/26/2026 08:20	7.9	10.1	2.1	0.0200	0.0360	0.0160	0.7	SE
10/26/2026 08:21	8.0	9.9	2.0	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:22	7.9	10.0	2.2	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:23	7.0	9.8	2.9	0.0200	0.0367	0.0167	0.6	E
10/26/2026 08:24	6.8	9.4	2.6	0.0200	0.0360	0.0160	0.6	SSE
10/26/2026 08:25	6.7	9.2	2.5	0.0200	0.0360	0.0160	0.6	SE
10/26/2026 08:26	6.7	9.2	2.4	0.0200	0.0367	0.0167	0.6	ESE
10/26/2026 08:27	6.7	9.1	2.3	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:28	6.9	9.0	2.1	0.0200	0.0360	0.0160	0.6	ESE
10/26/2026 08:29	7.0	8.9	1.9	0.0200	0.0353	0.0153	0.5	E
10/26/2026 08:30	6.9	8.7	1.7	0.0200	0.0353	0.0153	0.5	ESE
10/26/2026 08:31	7.0	8.4	1.4	0.0200	0.0347	0.0147	0.5	SE
10/26/2026 08:32	7.0	8.4	1.4	0.0200	0.0340	0.0140	0.6	SSE
10/26/2026 08:33	7.0	8.5	1.4	0.0200	0.0333	0.0133	0.6	ESE
10/26/2026 08:34	7.1	8.5	1.3	0.0200	0.0333	0.0133	0.6	ENE
10/26/2026 08:35	7.3	8.4	1.0	0.0200	0.0333	0.0133	0.5	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 08:36	7.4	8.3	0.9	0.0200	0.0333	0.0133	0.5	SE
10/26/2026 08:37	7.4	8.2	0.8	0.0200	0.0340	0.0140	0.5	SSE
10/26/2026 08:38	7.4	8.2	0.8	0.0200	0.0347	0.0147	0.5	SSE
10/26/2026 08:39	7.4	8.4	1.0	0.0200	0.0353	0.0153	0.5	SE
10/26/2026 08:40	7.3	8.3	0.9	0.0200	0.0353	0.0153	0.5	E
10/26/2026 08:41	7.3	8.1	0.8	0.0200	0.0353	0.0153	0.4	ENE
10/26/2026 08:42	7.5	7.9	0.4	0.0200	0.0360	0.0160	0.4	NE
10/26/2026 08:43	7.7	7.7	0.0	0.0200	0.0367	0.0167	0.4	E
10/26/2026 08:44	7.6	7.6	0.0	0.0200	0.0373	0.0173	0.4	SE
10/26/2026 08:45	7.7	7.7	0.0	0.0213	0.0367	0.0153	0.4	NNE
10/26/2026 08:46	7.7	7.8	0.1	0.0213	0.0373	0.0160	0.4	E
10/26/2026 08:47	7.7	8.0	0.3	0.0213	0.0380	0.0167	0.4	ENE
10/26/2026 08:48	7.7	8.0	0.3	0.0213	0.0387	0.0173	0.4	ENE
10/26/2026 08:49	7.6	8.0	0.3	0.0213	0.0387	0.0173	0.4	NE
10/26/2026 08:50	7.5	8.1	0.7	0.0213	0.0387	0.0173	0.4	NE
10/26/2026 08:51	7.4	8.1	0.6	0.0213	0.0387	0.0173	0.4	ESE
10/26/2026 08:52	7.4	7.8	0.4	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:53	7.3	7.6	0.3	0.0213	0.0387	0.0173	0.5	ESE
10/26/2026 08:54	7.3	7.4	0.1	0.0213	0.0387	0.0173	0.5	NE
10/26/2026 08:55	7.4	7.4	0.0	0.0213	0.0387	0.0173	0.5	ESE
10/26/2026 08:56	7.4	7.5	0.1	0.0213	0.0387	0.0173	0.5	SSE
10/26/2026 08:57	7.3	7.7	0.4	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:58	7.0	7.8	0.9	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:59	7.0	7.8	0.9	0.0213	0.0387	0.0173	0.5	E
10/26/2026 09:00	7.1	8.0	0.9	0.0200	0.0400	0.0200	0.6	E
10/26/2026 09:01	7.1	8.9	1.8	0.0200	0.0400	0.0200	0.6	ESE
10/26/2026 09:02	7.1	16.4	9.3	0.0200	0.0407	0.0207	0.6	E
10/26/2026 09:03	7.1	20.7	13.7	0.0200	0.0413	0.0213	0.6	E
10/26/2026 09:04	7.1	24.3	17.2	0.0200	0.0413	0.0213	0.6	SE
10/26/2026 09:05	7.2	27.1	19.9	0.0200	0.0413	0.0213	0.6	SE
10/26/2026 09:06	7.1	30.3	23.2	0.0200	0.0413	0.0213	0.5	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 09:07	7.2	32.7	25.5	0.0200	0.0413	0.0213	0.5	E
10/26/2026 09:08	7.2	34.0	26.7	0.0200	0.0413	0.0213	0.5	E
10/26/2026 09:09	7.3	35.1	27.8	0.0200	0.0420	0.0220	0.5	ESE
10/26/2026 09:10	7.4	35.8	28.5	0.0200	0.0427	0.0227	0.5	ESE
10/26/2026 09:11	7.4	36.2	28.8	0.0200	0.0433	0.0233	0.5	ENE
10/26/2026 09:12	7.4	36.5	29.1	0.0200	0.0433	0.0233	0.5	NE
10/26/2026 09:13	7.4	36.8	29.4	0.0200	0.0433	0.0233	0.5	E
10/26/2026 09:14	7.5	37.2	29.7	0.0200	0.0433	0.0233	0.5	ESE
10/26/2026 09:15	7.3	37.3	30.0	0.0200	0.0433	0.0233	0.4	E
10/26/2026 09:16	7.3	36.4	29.1	0.0200	0.0433	0.0233	0.4	ESE
10/26/2026 09:17	7.4	28.7	21.3	0.0200	0.0427	0.0227	0.4	SE
10/26/2026 09:18	7.4	24.4	17.0	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:19	7.3	21.2	13.8	0.0200	0.0420	0.0220	0.4	ESE
10/26/2026 09:20	7.3	18.7	11.4	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:21	7.3	16.1	8.8	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:22	7.3	13.9	6.6	0.0200	0.0420	0.0220	0.3	ESE
10/26/2026 09:23	7.2	12.6	5.4	0.0200	0.0420	0.0220	0.3	SE
10/26/2026 09:24	7.2	11.7	4.5	0.0200	0.0413	0.0213	0.3	ESE
10/26/2026 09:25	7.1	11.0	3.9	0.0200	0.0407	0.0207	0.3	NNE
10/26/2026 09:26	7.1	10.6	3.5	0.0200	0.0400	0.0200	0.3	ENE
10/26/2026 09:27	7.1	10.2	3.1	0.0200	0.0400	0.0200	0.3	NNE
10/26/2026 09:28	6.9	9.8	2.8	0.0200	0.0400	0.0200	0.3	NE
10/26/2026 09:29	6.8	9.5	2.6	0.0200	0.0400	0.0200	0.3	SE
10/26/2026 09:30	6.8	9.2	2.4	0.0200	0.0400	0.0200	0.3	E
10/26/2026 09:31	6.8	9.2	2.4	0.0200	0.0393	0.0193	0.3	SSE
10/26/2026 09:32	6.8	9.5	2.7	0.0200	0.0387	0.0187	0.3	E
10/26/2026 09:33	7.2	9.5	2.3	0.0200	0.0380	0.0180	0.3	E
10/26/2026 09:34	7.3	9.0	1.7	0.0200	0.0373	0.0173	0.3	ESE
10/26/2026 09:35	7.3	8.6	1.3	0.0200	0.0367	0.0167	0.3	SE
10/26/2026 09:36	7.4	8.1	0.7	0.0200	0.0360	0.0160	0.3	E
10/26/2026 09:37	7.5	7.9	0.4	0.0200	0.0353	0.0153	0.3	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 09:38	7.5	7.8	0.2	0.0200	0.0353	0.0153	0.4	E
10/26/2026 09:39	7.6	7.7	0.0	0.0200	0.0353	0.0153	0.4	ESE
10/26/2026 09:40	7.7	7.8	0.1	0.0200	0.0353	0.0153	0.4	E
10/26/2026 09:41	7.8	7.8	0.0	0.0207	0.0340	0.0133	0.3	NW
10/26/2026 09:42	7.8	7.7	0.0	0.0213	0.0327	0.0113	0.3	NNW
10/26/2026 09:43	7.8	7.8	0.0	0.0213	0.0320	0.0107	0.3	NE
10/26/2026 09:44	7.8	7.7	0.0	0.0213	0.0313	0.0100	0.3	E
10/26/2026 09:45	7.9	7.7	0.0	0.0220	0.0300	0.0080	0.3	N
10/26/2026 09:46	7.9	7.5	0.0	0.0220	0.0300	0.0080	0.3	NNE
10/26/2026 09:47	7.8	7.2	0.0	0.0220	0.0293	0.0073	0.3	ENE
10/26/2026 09:48	7.3	7.1	0.0	0.0220	0.0293	0.0073	0.3	ENE
10/26/2026 09:49	7.2	7.0	0.0	0.0220	0.0293	0.0073	0.3	ESE
10/26/2026 09:50	7.0	7.0	0.0	0.0227	0.0287	0.0060	0.3	NNE
10/26/2026 09:51	7.0	6.9	0.0	0.0227	0.0287	0.0060	0.3	NE
10/26/2026 09:52	6.9	6.8	0.0	0.0227	0.0287	0.0060	0.3	ENE
10/26/2026 09:53	6.8	6.8	0.0	0.0233	0.0273	0.0040	0.3	NE
10/26/2026 09:54	6.7	6.6	0.0	0.0233	0.0260	0.0027	0.3	ESE
10/26/2026 09:55	7.8	6.4	0.0	0.0233	0.0253	0.0020	0.3	SE
10/26/2026 09:56	7.8	6.4	0.0	0.0227	0.0260	0.0033	0.3	NNE
10/26/2026 09:57	7.8	6.4	0.0	0.0220	0.0260	0.0040	0.3	ENE
10/26/2026 09:58	7.8	6.5	0.0	0.0220	0.0253	0.0033	0.3	SE
10/26/2026 09:59	7.8	6.5	0.0	0.0220	0.0247	0.0027	0.3	SE
10/26/2026 10:00	7.8	6.5	0.0	0.0213	0.0247	0.0033	0.3	SSE
10/26/2026 10:01	7.9	6.4	0.0	0.0213	0.0240	0.0027	0.3	ESE
10/26/2026 10:02	8.0	6.4	0.0	0.0213	0.0240	0.0027	0.3	SE
10/26/2026 10:03	8.0	6.3	0.0	0.0213	0.0233	0.0020	0.3	SE
10/26/2026 10:04	8.1	6.3	0.0	0.0213	0.0227	0.0013	0.3	NE
10/26/2026 10:05	8.3	6.2	0.0	0.0207	0.0227	0.0020	0.3	E
10/26/2026 10:06	8.3	6.1	0.0	0.0207	0.0220	0.0013	0.3	SE
10/26/2026 10:07	8.4	6.1	0.0	0.0207	0.0213	0.0007	0.3	ESE
10/26/2026 10:08	8.5	6.1	0.0	0.0200	0.0213	0.0013	0.3	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 10:09	8.6	6.0	0.0	0.0200	0.0213	0.0013	0.3	NNE
10/26/2026 10:10	7.3	5.8	0.0	0.0200	0.0207	0.0007	0.3	SE
10/26/2026 10:11	7.4	5.9	0.0	0.0200	0.0207	0.0007	0.3	SSE
10/26/2026 10:12	7.8	6.2	0.0	0.0207	0.0207	0.0000	0.3	SSW
10/26/2026 10:13	7.9	6.2	0.0	0.0207	0.0213	0.0007	0.3	ESE
10/26/2026 10:14	7.8	6.3	0.0	0.0207	0.0213	0.0007	0.2	N
10/26/2026 10:15	7.8	6.5	0.0	0.0207	0.0213	0.0007	0.2	NW
10/26/2026 10:16	7.8	6.5	0.0	0.0207	0.0213	0.0007	0.2	ENE
10/26/2026 10:17	7.8	6.4	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:18	7.7	6.4	0.0	0.0207	0.0213	0.0007	0.2	ENE
10/26/2026 10:19	7.6	6.3	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:20	7.6	6.4	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:21	7.6	6.4	0.0	0.0207	0.0213	0.0007	0.2	S
10/26/2026 10:22	7.5	6.5	0.0	0.0213	0.0213	0.0000	0.2	NNE
10/26/2026 10:23	7.4	6.7	0.0	0.0220	0.0220	0.0000	0.2	N
10/26/2026 10:24	7.3	6.7	0.0	0.0220	0.0220	0.0000	0.2	S
10/26/2026 10:25	7.4	6.7	0.0	0.0220	0.0220	0.0000	0.2	SE
10/26/2026 10:26	7.2	6.7	0.0	0.0220	0.0213	0.0000	0.2	SSE
10/26/2026 10:27	6.9	6.6	0.0	0.0213	0.0213	0.0000	0.2	SSW
10/26/2026 10:28	6.8	6.9	0.0	0.0213	0.0207	0.0000	0.2	ESE
10/26/2026 10:29	7.0	18.9	11.9	0.0213	0.0207	0.0000	0.2	SE
10/26/2026 10:30	7.4	38.9	31.5	0.0213	0.0213	0.0000	0.3	S
10/26/2026 10:31	7.6	44.6	37.0	0.0213	0.0227	0.0013	0.3	SSE
10/26/2026 10:32	7.7	45.5	37.7	0.0213	0.0247	0.0033	0.3	SE
10/26/2026 10:33	7.8	45.8	38.0	0.0213	0.0260	0.0047	0.3	SE
10/26/2026 10:34	7.8	45.9	38.1	0.0213	0.0267	0.0053	0.3	SSE
10/26/2026 10:35	7.9	46.1	38.1	0.0213	0.0267	0.0053	0.3	SW
10/26/2026 10:36	8.0	46.2	38.2	0.0213	0.0267	0.0053	0.3	ENE
10/26/2026 10:37	8.0	46.3	38.3	0.0207	0.0267	0.0060	0.3	ENE
10/26/2026 10:38	8.1	46.8	38.7	0.0207	0.0260	0.0053	0.4	ESE
10/26/2026 10:39	8.3	47.7	39.4	0.0213	0.0260	0.0047	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 10:40	8.8	48.1	39.3	0.0213	0.0260	0.0047	0.4	ESE
10/26/2026 10:41	9.0	48.9	39.9	0.0213	0.0260	0.0047	0.4	SE
10/26/2026 10:42	9.1	51.0	42.0	0.0213	0.0260	0.0047	0.4	SE
10/26/2026 10:43	9.4	50.7	41.3	0.0213	0.0260	0.0047	0.4	SSW
10/26/2026 10:44	9.6	38.7	29.1	0.0220	0.0260	0.0040	0.3	SW
10/26/2026 10:45	9.3	18.5	9.2	0.0227	0.0253	0.0027	0.3	NW
10/26/2026 10:46	10.4	12.9	2.5	0.0227	0.0240	0.0013	0.2	NE
10/26/2026 10:47	10.6	12.8	2.2	0.0227	0.0220	0.0000	0.2	WSW
10/26/2026 10:48	10.6	12.7	2.1	0.0227	0.0200	0.0000	0.2	SSE
10/26/2026 10:49	10.8	14.6	3.8	0.0227	0.0187	0.0000	0.2	S
10/26/2026 10:50	10.7	19.0	8.3	0.0227	0.0187	0.0000	0.2	S
10/26/2026 10:51	10.8	20.6	9.8	0.0227	0.0193	0.0000	0.2	S
10/26/2026 10:52	11.0	20.7	9.8	0.0227	0.0193	0.0000	0.2	N
10/26/2026 10:53	11.1	20.8	9.7	0.0220	0.0193	0.0000	0.1	ENE
10/26/2026 10:54	11.1	20.1	9.0	0.0213	0.0193	0.0000	0.1	WNW
10/26/2026 10:55	10.6	19.9	9.3	0.0213	0.0193	0.0000	0.1	SE
10/26/2026 10:56	10.5	22.9	12.4	0.0213	0.0193	0.0000	0.1	SSE
10/26/2026 10:57	10.5	24.2	13.7	0.0213	0.0193	0.0000	0.2	SSE
10/26/2026 10:58	10.3	25.5	15.2	0.0213	0.0193	0.0000	0.1	NE
10/26/2026 10:59	10.2	28.9	18.7	0.0207	0.0200	0.0000	0.1	SSE
10/26/2026 11:00	10.2	31.4	21.2	0.0200	0.0207	0.0007	0.2	S
10/26/2026 11:01	8.8	32.9	24.1	0.0200	0.0213	0.0013	0.3	SSE
10/26/2026 11:02	8.6	33.4	24.9	0.0200	0.0220	0.0020	0.3	SSE
10/26/2026 11:03	9.6	33.4	23.7	0.0207	0.0227	0.0020	0.3	SSW
10/26/2026 11:04	10.6	31.3	20.7	0.0213	0.0233	0.0020	0.3	SSW
10/26/2026 11:05	11.6	26.8	15.2	0.0220	0.0233	0.0013	0.3	N
10/26/2026 11:06	11.4	26.3	14.9	0.0220	0.0233	0.0013	0.3	S
10/26/2026 11:07	11.1	26.1	15.0	0.0220	0.0227	0.0007	0.3	SSE
10/26/2026 11:08	10.9	25.4	14.6	0.0220	0.0220	0.0000	0.4	ENE
10/26/2026 11:09	10.6	25.3	14.7	0.0220	0.0213	0.0000	0.4	SSE
10/26/2026 11:10	10.4	25.0	14.6	0.0213	0.0213	0.0000	0.4	SW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 11:11	10.2	21.2	11.0	0.0213	0.0207	0.0000	0.3	NE
10/26/2026 11:12	10.0	17.7	7.7	0.0213	0.0200	0.0000	0.3	S
10/26/2026 11:13	9.7	16.3	6.6	0.0213	0.0193	0.0000	0.3	ENE
10/26/2026 11:14	9.5	12.7	3.3	0.0213	0.0180	0.0000	0.3	E
10/26/2026 11:15	9.3	10.2	0.9	0.0213	0.0167	0.0000	0.3	E
10/26/2026 11:16	9.1	8.9	0.0	0.0213	0.0153	0.0000	0.3	E
10/26/2026 11:17	8.9	8.0	0.0	0.0213	0.0140	0.0000	0.2	ENE
10/26/2026 11:18	7.8	8.0	0.3	0.0207	0.0133	0.0000	0.2	NNE
10/26/2026 11:19	6.6	8.1	1.5	0.0200	0.0133	0.0000	0.2	ENE
10/26/2026 11:20	5.5	8.2	2.8	0.0193	0.0133	0.0000	0.2	ENE
10/26/2026 11:21	5.7	7.1	1.4	0.0193	0.0127	0.0000	0.2	ESE
10/26/2026 11:22	5.8	7.1	1.3	0.0187	0.0133	0.0000	0.2	NW
10/26/2026 11:23	5.8	7.3	1.5	0.0187	0.0133	0.0000	0.2	ESE
10/26/2026 11:24	5.9	7.4	1.6	0.0187	0.0133	0.0000	0.2	SSE
10/26/2026 11:25	5.9	7.6	1.7	0.0193	0.0127	0.0000	0.3	SSE
10/26/2026 11:26	6.0	7.6	1.6	0.0193	0.0127	0.0000	0.3	SSE
10/26/2026 11:27	6.0	7.6	1.5	0.0193	0.0133	0.0000	0.3	SSE
10/26/2026 11:28	6.1	7.7	1.6	0.0193	0.0140	0.0000	0.3	SSE
10/26/2026 11:29	6.1	7.8	1.6	0.0193	0.0147	0.0000	0.3	SSW
10/26/2026 11:30	6.2	7.7	1.5	0.0187	0.0153	0.0000	0.3	W
10/26/2026 11:31	6.2	7.5	1.2	0.0173	0.0160	0.0000	0.2	NNW
10/26/2026 11:32	6.3	7.2	1.0	0.0160	0.0167	0.0007	0.2	NW
10/26/2026 11:33	6.3	7.1	0.8	0.0147	0.0173	0.0027	0.2	SSW
10/26/2026 11:34	6.3	7.0	0.7	0.0147	0.0160	0.0013	0.3	SSE
10/26/2026 11:35	6.3	7.0	0.7	0.0147	0.0147	0.0000	0.3	S
10/26/2026 11:36	6.1	7.0	0.9	0.0147	0.0140	0.0000	0.3	SSE
10/26/2026 11:37	6.1	7.1	1.0	0.0153	0.0133	0.0000	0.3	SE
10/26/2026 11:38	6.1	6.9	0.8	0.0147	0.0140	0.0000	0.3	SW
10/26/2026 11:39	6.1	6.7	0.6	0.0140	0.0147	0.0007	0.3	W
10/26/2026 11:40	6.1	6.7	0.6	0.0133	0.0153	0.0020	0.2	WSW
10/26/2026 11:41	6.1	6.7	0.5	0.0127	0.0160	0.0033	0.2	SSW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 11:42	6.2	6.7	0.5	0.0127	0.0153	0.0027	0.2	S
10/26/2026 11:43	6.2	6.7	0.4	0.0127	0.0147	0.0020	0.2	S
10/26/2026 11:44	6.3	6.6	0.3	0.0127	0.0147	0.0020	0.2	SW
10/26/2026 11:45	6.3	6.7	0.3	0.0127	0.0147	0.0020	0.2	NW
10/26/2026 11:46	6.5	6.7	0.3	0.0140	0.0133	0.0000	0.2	S
10/26/2026 11:47	6.5	6.7	0.2	0.0153	0.0120	0.0000	0.2	SSE
10/26/2026 11:48	6.6	6.8	0.2	0.0167	0.0113	0.0000	0.2	SSE
10/26/2026 11:49	6.7	6.9	0.3	0.0167	0.0120	0.0000	0.2	SSE
10/26/2026 11:50	6.8	7.0	0.2	0.0167	0.0127	0.0000	0.2	SSE
10/26/2026 11:51	6.9	7.0	0.1	0.0167	0.0127	0.0000	0.3	SSE
10/26/2026 11:52	7.0	7.2	0.1	0.0167	0.0127	0.0000	0.3	SE
10/26/2026 11:53	7.1	7.2	0.1	0.0167	0.0127	0.0000	0.2	NNW
10/26/2026 11:54	7.2	7.4	0.2	0.0173	0.0120	0.0000	0.3	SSE
10/26/2026 11:55	7.3	7.5	0.2	0.0180	0.0113	0.0000	0.3	SE
10/26/2026 11:56	7.4	7.6	0.2	0.0187	0.0107	0.0000	0.3	SSE
10/26/2026 11:57	7.4	7.7	0.2	0.0187	0.0107	0.0000	0.3	ENE
10/26/2026 11:58	7.5	7.9	0.4	0.0187	0.0107	0.0000	0.3	S
10/26/2026 11:59	7.5	8.5	1.1	0.0187	0.0100	0.0000	0.4	S
10/26/2026 12:00	7.6	8.9	1.3	0.0193	0.0100	0.0000	0.4	E
10/26/2026 12:01	7.5	9.1	1.6	0.0193	0.0113	0.0000	0.4	SSE
10/26/2026 12:02	7.4	9.3	1.9	0.0193	0.0127	0.0000	0.4	E
10/26/2026 12:03	7.3	9.2	1.9	0.0193	0.0127	0.0000	0.4	E
10/26/2026 12:04	7.2	9.1	1.9	0.0180	0.0133	0.0000	0.4	SW
10/26/2026 12:05	7.2	9.0	1.8	0.0180	0.0127	0.0000	0.4	S
10/26/2026 12:06	7.1	9.0	1.9	0.0180	0.0120	0.0000	0.4	E
10/26/2026 12:07	7.0	8.8	1.8	0.0180	0.0113	0.0000	0.3	S
10/26/2026 12:08	6.9	8.7	1.9	0.0173	0.0113	0.0000	0.3	WNW
10/26/2026 12:09	7.0	8.6	1.6	0.0173	0.0107	0.0000	0.3	S
10/26/2026 12:10	6.9	8.9	2.1	0.0173	0.0107	0.0000	0.4	SSE
10/26/2026 12:11	6.8	9.1	2.4	0.0173	0.0107	0.0000	0.4	ESE
10/26/2026 12:12	6.7	9.0	2.3	0.0173	0.0100	0.0000	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 12:13	6.7	8.7	2.1	0.0173	0.0093	0.0000	0.4	ESE
10/26/2026 12:14	6.6	8.1	1.5	0.0173	0.0087	0.0000	0.4	ESE
10/26/2026 12:15	6.6	8.0	1.4	0.0173	0.0080	0.0000	0.4	SSE
10/26/2026 12:16	6.6	7.9	1.3	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:17	6.6	8.1	1.4	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:18	6.6	8.3	1.7	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:19	6.6	8.6	2.0	0.0187	0.0067	0.0000	0.4	SSE
10/26/2026 12:20	6.6	8.8	2.2	0.0180	0.0073	0.0000	0.4	E
10/26/2026 12:21	6.5	8.8	2.3	0.0173	0.0080	0.0000	0.4	S
10/26/2026 12:22	6.5	9.0	2.5	0.0167	0.0087	0.0000	0.5	SE
10/26/2026 12:23	6.4	9.3	2.8	0.0173	0.0080	0.0000	0.5	ESE
10/26/2026 12:24	6.2	9.4	3.1	0.0167	0.0087	0.0000	0.5	SSE
10/26/2026 12:25	6.2	9.2	3.0	0.0160	0.0087	0.0000	0.5	SE
10/26/2026 12:26	6.3	8.9	2.6	0.0153	0.0087	0.0000	0.4	N
10/26/2026 12:27	6.3	8.8	2.6	0.0147	0.0093	0.0000	0.4	ESE
10/26/2026 12:28	6.3	8.9	2.6	0.0147	0.0100	0.0000	0.4	E
10/26/2026 12:29	6.3	8.9	2.6	0.0133	0.0113	0.0000	0.4	WSW
10/26/2026 12:30	6.3	8.6	2.3	0.0133	0.0107	0.0000	0.4	S
10/26/2026 12:31	6.2	8.5	2.3	0.0133	0.0100	0.0000	0.4	S
10/26/2026 12:32	6.2	8.1	1.9	0.0133	0.0087	0.0000	0.4	S
10/26/2026 12:33	6.2	8.0	1.9	0.0133	0.0080	0.0000	0.4	S
10/26/2026 12:34	6.2	8.0	1.8	0.0133	0.0073	0.0000	0.4	S
10/26/2026 12:35	6.2	8.3	2.1	0.0140	0.0073	0.0000	0.4	SE
10/26/2026 12:36	6.4	8.2	1.8	0.0140	0.0080	0.0000	0.4	SW
10/26/2026 12:37	6.5	7.9	1.5	0.0147	0.0073	0.0000	0.4	SSE
10/26/2026 12:38	6.6	7.6	1.1	0.0153	0.0067	0.0000	0.4	SE
10/26/2026 12:39	6.6	7.4	0.9	0.0160	0.0060	0.0000	0.3	SSW
10/26/2026 12:40	6.5	7.1	0.5	0.0167	0.0053	0.0000	0.3	NE
10/26/2026 12:41	6.3	7.1	0.8	0.0160	0.0060	0.0000	0.3	SSW
10/26/2026 12:42	6.3	7.1	0.8	0.0167	0.0053	0.0000	0.3	S
10/26/2026 12:43	6.3	7.3	1.0	0.0167	0.0047	0.0000	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 12:44	6.3	7.6	1.3	0.0180	0.0033	0.0000	0.4	SE
10/26/2026 12:45	6.2	7.8	1.5	0.0173	0.0040	0.0000	0.4	E
10/26/2026 12:46	6.3	7.8	1.5	0.0167	0.0047	0.0000	0.4	SSE
10/26/2026 12:47	6.2	8.8	2.5	0.0167	0.0053	0.0000	0.4	SSE
10/26/2026 12:48	6.9	8.8	1.8	0.0160	0.0067	0.0000	0.4	NW
10/26/2026 12:49	6.9	8.5	1.5	0.0160	0.0067	0.0000	0.4	E
10/26/2026 12:50	6.9	8.0	1.0	0.0160	0.0060	0.0000	0.3	S
10/26/2026 12:51	6.6	8.5	1.9	0.0160	0.0047	0.0000	0.4	SSE
10/26/2026 12:52	6.5	9.2	2.7	0.0153	0.0053	0.0000	0.4	ESE
10/26/2026 12:53	6.6	9.3	2.7	0.0147	0.0060	0.0000	0.4	SE
10/26/2026 12:54	6.8	9.5	2.8	0.0140	0.0060	0.0000	0.4	SE
10/26/2026 12:55	7.0	9.6	2.6	0.0127	0.0067	0.0000	0.4	W
10/26/2026 12:56	7.0	9.6	2.6	0.0140	0.0053	0.0000	0.4	ENE
10/26/2026 12:57	7.0	9.8	2.8	0.0140	0.0053	0.0000	0.4	ENE
10/26/2026 12:58	6.9	10.5	3.5	0.0140	0.0053	0.0000	0.3	NNE
10/26/2026 12:59	7.2	10.0	2.7	0.0127	0.0067	0.0000	0.2	NNW
10/26/2026 13:00	7.2	9.7	2.5	0.0120	0.0073	0.0000	0.2	NNW
10/26/2026 13:01	7.2	9.6	2.3	0.0113	0.0080	0.0000	0.2	SSW
10/26/2026 13:02	7.2	8.6	1.3	0.0107	0.0073	0.0000	0.2	SE
10/26/2026 13:03	6.5	8.5	2.0	0.0107	0.0060	0.0000	0.2	ESE
10/26/2026 13:04	6.4	8.5	2.1	0.0107	0.0060	0.0000	0.2	SE
10/26/2026 13:05	6.5	8.5	2.0	0.0093	0.0073	0.0000	0.2	N
10/26/2026 13:06	6.5	7.9	1.5	0.0100	0.0073	0.0000	0.2	S
10/26/2026 13:07	6.5	7.4	0.9	0.0107	0.0067	0.0000	0.2	ESE
10/26/2026 13:08	6.2	7.4	1.1	0.0113	0.0060	0.0000	0.2	NE
10/26/2026 13:09	6.0	7.1	1.1	0.0120	0.0060	0.0000	0.2	ESE
10/26/2026 13:10	5.7	7.0	1.3	0.0120	0.0067	0.0000	0.2	NNW
10/26/2026 13:11	5.6	6.8	1.2	0.0107	0.0080	0.0000	0.2	NNW
10/26/2026 13:12	5.5	6.6	1.1	0.0107	0.0080	0.0000	0.2	NE
10/26/2026 13:13	5.5	5.5	0.0	0.0107	0.0080	0.0000	0.2	SE
10/26/2026 13:14	5.1	5.6	0.6	0.0107	0.0073	0.0000	0.2	N

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 13:15	5.1	5.7	0.6	0.0120	0.0060	0.0000	0.2	S
10/26/2026 13:16	5.0	5.8	0.8	0.0133	0.0047	0.0000	0.2	S
10/26/2026 13:17	5.0	5.8	0.7	0.0140	0.0047	0.0000	0.2	NNE
10/26/2026 13:18	5.1	5.5	0.5	0.0147	0.0047	0.0000	0.2	SSE
10/26/2026 13:19	5.2	5.5	0.3	0.0153	0.0047	0.0000	0.2	SSE
10/26/2026 13:20	5.0	5.8	0.8	0.0167	0.0033	0.0000	0.2	ESE
10/26/2026 13:21	5.1	6.0	0.9	0.0160	0.0033	0.0000	0.2	ESE
10/26/2026 13:22	5.1	6.2	1.0	0.0153	0.0033	0.0000	0.3	SE
10/26/2026 13:23	5.3	6.1	0.8	0.0140	0.0040	0.0000	0.2	NW
10/26/2026 13:24	5.4	6.1	0.7	0.0133	0.0040	0.0000	0.2	ESE
10/26/2026 13:25	5.6	6.3	0.7	0.0140	0.0027	0.0000	0.3	SE
10/26/2026 13:26	5.7	6.4	0.8	0.0147	0.0013	0.0000	0.4	SE
10/26/2026 13:27	5.8	6.5	0.7	0.0147	0.0013	0.0000	0.4	SE
10/26/2026 13:28	5.9	6.5	0.6	0.0140	0.0013	0.0000	0.4	E
10/26/2026 13:29	6.0	6.4	0.4	0.0147	0.0007	0.0000	0.5	SSE
10/26/2026 13:30	6.0	6.4	0.4	0.0140	0.0007	0.0000	0.5	ESE
10/26/2026 13:31	6.1	6.3	0.2	0.0133	0.0007	0.0000	0.5	ENE
10/26/2026 13:32	6.1	6.4	0.2	0.0127	0.0007	0.0000	0.5	E
10/26/2026 13:33	6.2	6.4	0.2	0.0120	0.0007	0.0000	0.5	SSE
10/26/2026 13:34	6.2	6.3	0.1	0.0107	0.0007	0.0000	0.5	ESE
10/26/2026 13:35	6.3	5.9	0.0	0.0100	0.0007	0.0000	0.5	NNE
10/26/2026 13:36	6.3	5.6	0.0	0.0107	0.0007	0.0000	0.4	SSE
10/26/2026 13:37	6.3	5.6	0.0	0.0100	0.0020	0.0000	0.4	SW
10/26/2026 13:38	7.0	5.6	0.0	0.0113	0.0013	0.0000	0.4	SSW
10/26/2026 13:39	7.0	5.6	0.0	0.0113	0.0013	0.0000	0.4	SE
10/26/2026 13:40	7.0	5.4	0.0	0.0113	0.0013	0.0000	0.4	E
10/26/2026 13:41	7.1	5.4	0.0	0.0113	0.0013	0.0000	0.4	SE
10/26/2026 13:42	7.0	5.4	0.0	0.0113	0.0013	0.0000	0.4	S
10/26/2026 13:43	7.0	5.8	0.0	0.0120	0.0013	0.0000	0.4	ESE
10/26/2026 13:44	7.0	5.9	0.0	0.0120	0.0013	0.0000	0.4	S
10/26/2026 13:45	7.1	6.0	0.0	0.0120	0.0013	0.0000	0.3	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 13:46	7.0	5.9	0.0	0.0120	0.0013	0.0000	0.4	SE
10/26/2026 13:47	6.9	5.8	0.0	0.0120	0.0013	0.0000	0.4	SE
10/26/2026 13:48	6.9	5.9	0.0	0.0120	0.0013	0.0000	0.4	S
10/26/2026 13:49	6.8	6.0	0.0	0.0120	0.0013	0.0000	0.4	SSE
10/26/2026 13:50	6.7	6.0	0.0	0.0113	0.0020	0.0000	0.5	WSW
10/26/2026 13:51	6.7	6.1	0.0	0.0107	0.0020	0.0000	0.5	ESE
10/26/2026 13:52	6.7	5.7	0.0	0.0113	0.0007	0.0000	0.5	SSE
10/26/2026 13:53	5.8	5.6	0.0	0.0107	0.0007	0.0000	0.5	ESE
10/26/2026 13:54	5.7	5.6	0.0	0.0107	0.0007	0.0000	0.5	SE
10/26/2026 13:55	5.6	5.6	0.0	0.0107	0.0007	0.0000	0.5	SE
10/26/2026 13:56	5.5	5.5	0.0	0.0107	0.0007	0.0000	0.5	SSE
10/26/2026 13:57	5.4	5.5	0.1	0.0093	0.0013	0.0000	0.4	NW
10/26/2026 13:58	5.3	5.0	0.0	0.0087	0.0013	0.0000	0.4	S
10/26/2026 13:59	5.3	5.0	0.0	0.0087	0.0013	0.0000	0.4	SE
10/26/2026 14:00	5.2	4.7	0.0	0.0087	0.0013	0.0000	0.4	S
10/26/2026 14:01	5.1	4.7	0.0	0.0080	0.0020	0.0000	0.4	NW
10/26/2026 14:02	5.1	4.7	0.0	0.0087	0.0020	0.0000	0.3	SSE
10/26/2026 14:03	5.1	4.7	0.0	0.0093	0.0020	0.0000	0.3	S
10/26/2026 14:04	5.2	4.6	0.0	0.0100	0.0020	0.0000	0.3	SSE
10/26/2026 14:05	5.4	4.5	0.0	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:06	5.4	5.5	0.1	0.0113	0.0013	0.0000	0.3	SE
10/26/2026 14:07	5.4	5.8	0.5	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:08	5.4	6.2	0.8	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:09	5.4	6.4	1.0	0.0113	0.0013	0.0000	0.4	SSE
10/26/2026 14:10	5.5	6.4	1.0	0.0113	0.0013	0.0000	0.4	SSE
10/26/2026 14:11	5.4	6.4	1.0	0.0113	0.0013	0.0000	0.4	S
10/26/2026 14:12	5.4	6.4	0.9	0.0113	0.0013	0.0000	0.5	SW
10/26/2026 14:13	5.4	7.0	1.6	0.0113	0.0013	0.0000	0.5	S
10/26/2026 14:14	5.3	7.3	2.0	0.0113	0.0013	0.0000	0.5	S
10/26/2026 14:15	5.4	7.4	1.9	0.0113	0.0013	0.0000	0.6	SE
10/26/2026 14:16	5.5	7.3	1.8	0.0120	0.0007	0.0000	0.7	SSW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 14:17	5.5	7.4	1.9	0.0113	0.0007	0.0000	0.7	SSE
10/26/2026 14:18	5.4	7.6	2.2	0.0107	0.0007	0.0000	0.8	SE
10/26/2026 14:19	5.4	7.7	2.3	0.0093	0.0013	0.0000	0.8	SW
10/26/2026 14:20	5.3	7.7	2.4	0.0080	0.0020	0.0000	0.7	WSW
10/26/2026 14:21	5.3	6.9	1.6	0.0080	0.0020	0.0000	0.7	SE
10/26/2026 14:22	5.3	6.6	1.4	0.0080	0.0020	0.0000	0.7	SSE
10/26/2026 14:23	5.3	6.6	1.3	0.0080	0.0020	0.0000	0.7	SSE
10/26/2026 14:24	5.3	6.4	1.1	0.0073	0.0027	0.0000	0.6	W
10/26/2026 14:25	5.1	6.4	1.3	0.0067	0.0033	0.0000	0.6	SW
10/26/2026 14:26	5.2	6.5	1.4	0.0067	0.0033	0.0000	0.5	NNE
10/26/2026 14:27	5.5	6.5	1.1	0.0067	0.0040	0.0000	0.4	N
10/26/2026 14:28	5.9	35.7	29.8	0.0067	0.0040	0.0000	0.3	ENE
10/26/2026 14:29	6.2	91.6	85.4	0.0073	0.0040	0.0000	0.3	ESE
10/26/2026 14:30	6.2	99.2	93.1	0.0073	0.0040	0.0000	0.3	SE
10/26/2026 14:31	6.3	108.9	102.6	0.0073	0.0040	0.0000	0.3	SSE
10/26/2026 14:32	6.4	111.8	105.5	0.0073	0.0047	0.0000	0.3	SE
10/26/2026 14:33	6.3	113.3	106.9	0.0073	0.0053	0.0000	0.3	S
10/26/2026 14:34	8.9	113.2	104.4	0.0080	0.0053	0.0000	0.3	SW
10/26/2026 14:35	8.8	117.8	109.0	0.0087	0.0053	0.0000	0.4	SE
10/26/2026 14:36	8.8	152.9	144.1	0.0087	0.0060	0.0000	0.4	SSE
10/26/2026 14:37	8.9	283.2	274.3	0.0087	0.0060	0.0000	0.4	ESE
10/26/2026 14:38	9.4	382.6	373.2	0.0087	0.0060	0.0000	0.4	SSE
10/26/2026 14:39	10.2	438.2	428.1	0.0093	0.0060	0.0000	0.4	SE
10/26/2026 14:40	11.0	452.7	441.7	0.0100	0.0067	0.0000	0.5	S
10/26/2026 14:41	11.2	476.6	465.4	0.0100	0.0080	0.0000	0.5	ESE
10/26/2026 14:42	11.0	484.8	473.8	0.0107	0.0073	0.0000	0.6	ESE
10/26/2026 14:43	10.6	464.6	454.0	0.0107	0.0073	0.0000	0.7	ESE
10/26/2026 14:44	10.4	415.3	404.8	0.0100	0.0073	0.0000	0.7	SE
10/26/2026 14:45	10.5	424.7	414.2	0.0100	0.0073	0.0000	0.8	SE
10/26/2026 14:46	10.5	421.8	411.3	0.0100	0.0073	0.0000	1.0	SE
10/26/2026 14:47	10.4	422.6	412.2	0.0100	0.0067	0.0000	1.1	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 14:48	10.6	423.5	413.0	0.0100	0.0060	0.0000	1.1	SE
10/26/2026 14:49	8.0	425.5	417.5	0.0100	0.0053	0.0000	1.3	SE
10/26/2026 14:50	8.0	422.3	414.3	0.0100	0.0047	0.0000	1.3	SE
10/26/2026 14:51	8.0	388.3	380.3	0.0100	0.0040	0.0000	1.3	SE
10/26/2026 14:52	7.9	258.5	250.6	0.0100	0.0040	0.0000	1.3	SE
10/26/2026 14:53	7.3	159.4	152.1	0.0100	0.0040	0.0000	1.3	NNE
10/26/2026 14:54	6.6	104.1	97.5	0.0100	0.0033	0.0000	1.3	SE
10/26/2026 14:55	5.9	89.9	84.0	0.0100	0.0020	0.0000	1.4	SE
10/26/2026 14:56	5.7	66.3	60.6	0.0100	0.0007	0.0000	1.4	ESE
10/26/2026 14:57	5.6	58.5	52.8	0.0100	0.0000	0.0000	1.4	ESE
10/26/2026 14:58	5.5	49.2	43.7	0.0100	0.0000	0.0000	1.5	SE
10/26/2026 14:59	5.4	42.7	37.3	0.0100	0.0000	0.0000	1.5	E
10/26/2026 15:00	5.3	25.9	20.6	0.0100	0.0000	0.0000	1.3	NNE
10/26/2026 15:01	5.2	19.3	14.1	0.0100	0.0000	0.0000	1.1	E
10/26/2026 15:02	5.1	15.8	10.7	0.0100	0.0000	0.0000	1.0	NE
10/26/2026 15:03	4.9	13.5	8.6	0.0100	0.0000	0.0000	1.0	NE
10/26/2026 15:04	4.7	11.6	6.9	0.0100	0.0000	0.0000	0.9	NE
10/26/2026 15:05	4.7	10.3	5.6	0.0100	0.0000	0.0000	0.8	NE
10/26/2026 15:06	4.7	9.4	4.6	0.0100	0.0000	0.0000	0.9	NNE
10/26/2026 15:07	4.7	8.8	4.1	0.0107	0.0000	0.0000	0.9	NNE
10/26/2026 15:08	4.7	8.3	3.6	0.0113	0.0000	0.0000	0.9	E
10/26/2026 15:09	4.6	8.0	3.3	0.0120	0.0000	0.0000	0.9	E
10/26/2026 15:10	4.6	7.8	3.1	0.0127	0.0000	0.0000	0.9	E
10/26/2026 15:11	4.7	7.5	2.8	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:12	4.6	7.0	2.4	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:13	4.6	6.6	2.0	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:14	4.6	6.4	1.7	0.0127	0.0000	0.0000	1.0	NE
10/26/2026 15:15	4.7	6.2	1.5	0.0120	0.0007	0.0000	0.9	N
10/26/2026 15:16	4.7	5.9	1.2	0.0120	0.0007	0.0000	1.0	E
10/26/2026 15:17	4.7	5.6	0.8	0.0120	0.0007	0.0000	0.9	NNE
10/26/2026 15:18	4.7	5.2	0.5	0.0127	0.0007	0.0000	0.8	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 15:19	4.8	5.0	0.2	0.0127	0.0007	0.0000	0.8	E
10/26/2026 15:20	4.8	4.8	0.0	0.0127	0.0007	0.0000	0.9	SE
10/26/2026 15:21	4.7	4.5	0.0	0.0127	0.0007	0.0000	0.9	SE
10/26/2026 15:22	4.7	4.3	0.0	0.0120	0.0007	0.0000	1.0	ESE
10/26/2026 15:23	4.7	4.2	0.0	0.0113	0.0007	0.0000	1.0	E

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/27/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-61°F, Sunny, RH: 50% Pres: 30.34” Wind: N @ 10-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:00

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Capstone installed foundation piles within grid A1.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:30-16:00. No exceedances of volatile organic compounds (VOCs) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/27/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-61°F, Sunny, RH: 50% Pres: 30.34” Wind: N @ 10-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:00


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks and foundation piles along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/27/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-61°F, Sunny, RH: 50% Pres: 30.34” Wind: N @ 10-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:00

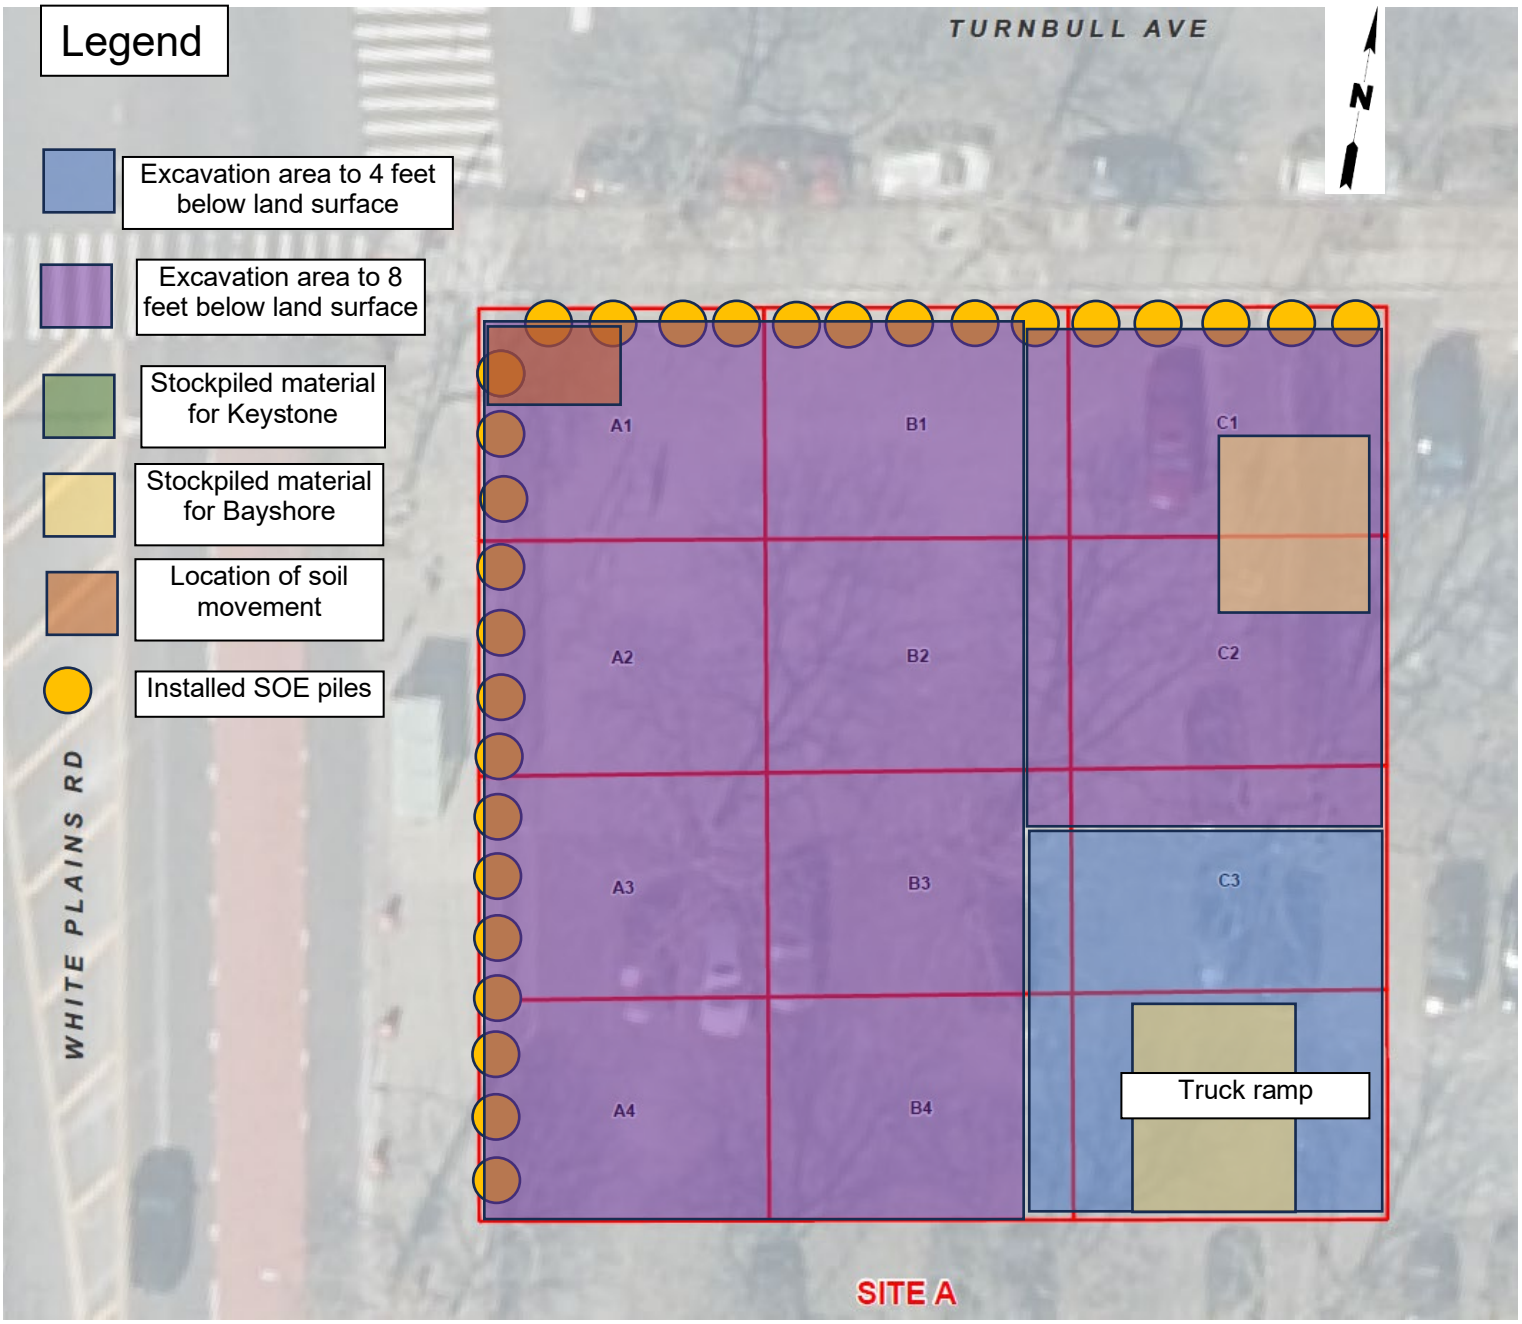

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/27/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-61°F, Sunny, RH: 50% Pres: 30.34” Wind: N @ 10-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:00

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Capstone installs foundation piles in grid A1 along the northern boundary of the site.



Photo 2:
Facing northwest, Capstone continues installing foundation piles within the northern portion of the site in grid A1.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/27/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 47-61°F, Sunny, RH: 50% Pres: 30.34” Wind: N @ 10-19 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 16:00

	**Photo 3**: Facing west, view foundation piles installed along the northern boundary of the site.
	**Photo 4:** Facing northwest, view of south CAMP station located within the southeastern site corner.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/27/2026 07:00
		To: 10/27/2026 16:30

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/27/2026	50.7 - 63.1	27.1 - 58.6	30.3 - 30.4	0.7 - 8.8	NNE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/27/2026	0.0	07:30	0.0000	07:45
Max Contribution (15 min avg.) - 10/27/2026	0.0	07:30	0.0271	07:30
Daily Avg. Contribution (15 min avg.) - 10/27/2026	0.0	-	0.0020	-

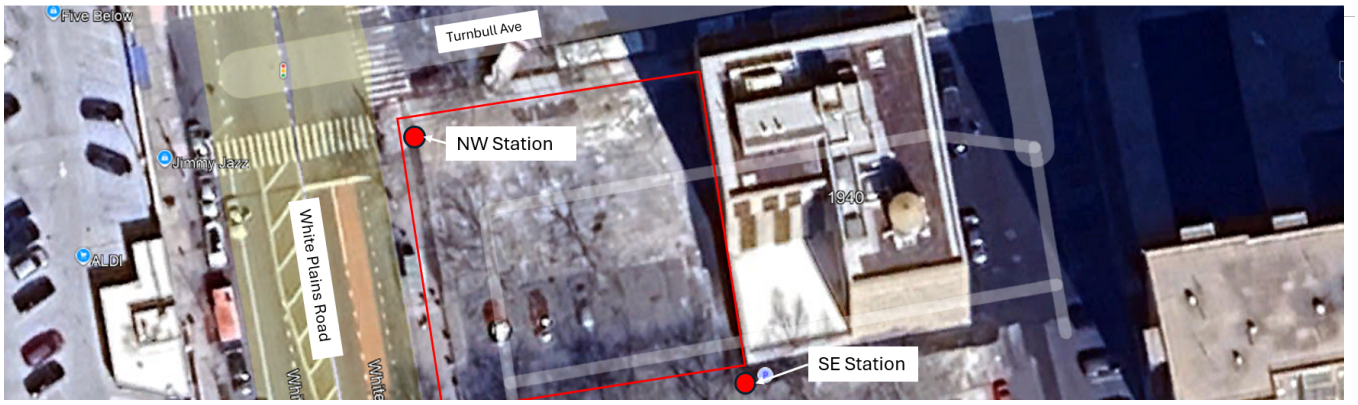


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

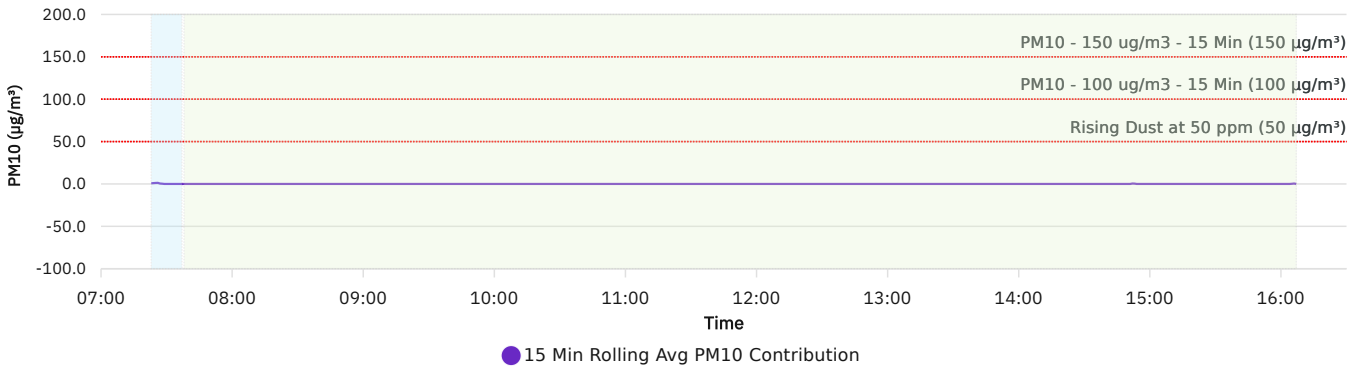

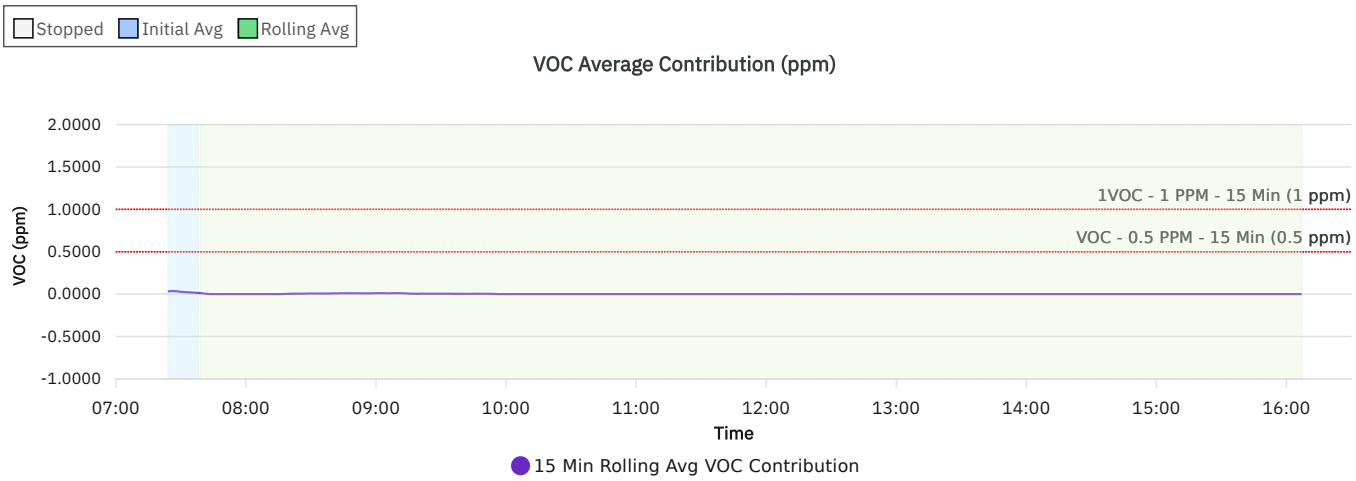

Wind rose (mph)

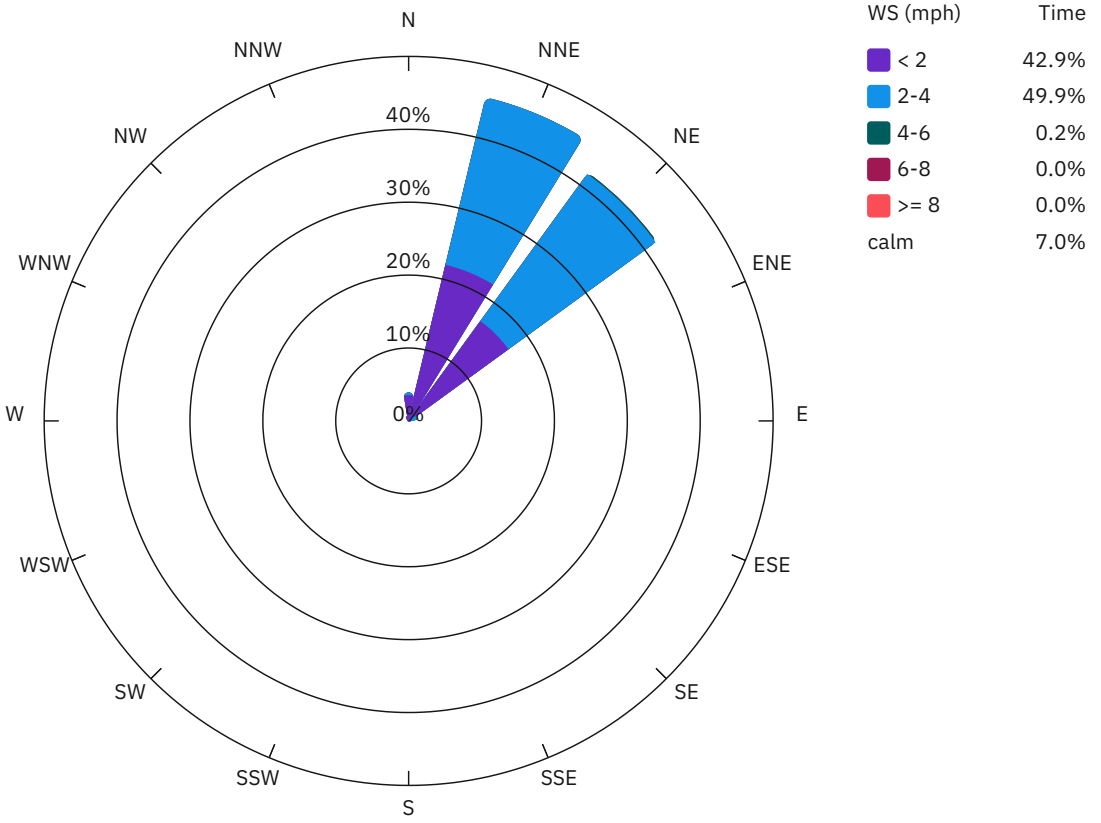

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/27/2026 07:30	4.4	3.7	0.0	0.0057	0.0329	0.0271	2.2	NE
10/27/2026 07:45	7.9	3.2	0.0	0.0133	0.0120	0.0000	2.2	NE
10/27/2026 08:00	6.6	3.2	0.0	0.0200	0.0160	0.0000	1.7	NE
10/27/2026 08:15	6.4	3.8	0.0	0.0213	0.0207	0.0000	1.9	NNE
10/27/2026 08:30	9.6	3.9	0.0	0.0213	0.0287	0.0073	2.2	NE
10/27/2026 08:45	6.8	2.6	0.0	0.0200	0.0300	0.0100	2.1	NNE
10/27/2026 09:00	10.1	3.1	0.0	0.0187	0.0293	0.0107	2.1	NNE
10/27/2026 09:15	6.5	3.2	0.0	0.0187	0.0253	0.0067	2.0	NE
10/27/2026 09:30	8.1	2.8	0.0	0.0173	0.0220	0.0047	1.8	NNE
10/27/2026 09:45	9.6	2.9	0.0	0.0167	0.0200	0.0033	2.1	NE
10/27/2026 10:00	10.4	5.7	0.0	0.0187	0.0173	0.0000	1.6	NNE
10/27/2026 10:15	19.2	3.8	0.0	0.0180	0.0100	0.0000	2.0	NE
10/27/2026 10:30	10.3	6.2	0.0	0.0180	0.0107	0.0000	2.3	NE
10/27/2026 10:45	7.1	4.2	0.0	0.0107	0.0100	0.0000	2.2	NNE
10/27/2026 11:00	9.8	3.7	0.0	0.0133	0.0093	0.0000	2.0	NNE
10/27/2026 11:15	8.0	3.3	0.0	0.0160	0.0053	0.0000	2.1	NNE
10/27/2026 11:30	6.0	1.9	0.0	0.0200	0.0047	0.0000	2.1	NE
10/27/2026 11:45	5.7	2.5	0.0	0.0120	0.0040	0.0000	2.8	NNE
10/27/2026 12:00	5.1	2.5	0.0	0.0100	0.0093	0.0000	2.0	NNE
10/27/2026 12:15	4.6	2.9	0.0	0.0087	0.0080	0.0000	1.7	NNE
10/27/2026 12:30	4.3	2.0	0.0	0.0087	0.0013	0.0000	2.1	NNE
10/27/2026 12:45	11.2	1.9	0.0	0.0100	0.0000	0.0000	2.7	NE
10/27/2026 13:00	10.6	5.9	0.0	0.0120	0.0100	0.0000	1.9	NNE
10/27/2026 13:15	11.6	4.6	0.0	0.0107	0.0040	0.0000	1.4	NNE
10/27/2026 13:30	14.4	2.9	0.0	0.0100	0.0007	0.0000	2.1	NNE
10/27/2026 13:45	8.0	2.5	0.0	0.0093	0.0007	0.0000	1.9	NNE
10/27/2026 14:00	4.8	2.5	0.0	0.0087	0.0013	0.0000	1.7	NNE
10/27/2026 14:15	7.9	2.7	0.0	0.0087	0.0013	0.0000	1.9	NE
10/27/2026 14:30	6.3	2.9	0.0	0.0093	0.0013	0.0000	1.8	NNE
10/27/2026 14:45	7.5	4.9	0.0	0.0073	0.0027	0.0000	1.5	NNE
10/27/2026 15:00	8.2	4.0	0.0	0.0087	0.0040	0.0000	1.4	NNE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/27/2026 15:15	6.9	4.2	0.0	0.0073	0.0027	0.0000	1.6	NNE
10/27/2026 15:30	7.8	2.4	0.0	0.0120	0.0013	0.0000	1.4	NNE
10/27/2026 15:45	5.0	2.2	0.0	0.0073	0.0027	0.0000	1.3	NNE
10/27/2026 16:00	4.7	3.7	0.0	0.0073	0.0033	0.0000	1.2	NNE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/28/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 52-62°F, Partly Cloudy, RH: 49% Pres: 30.48" Wind: NE @ 9 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	PERSONNEL PRESENT AT SITE AND AFFILIATION:
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Capstone installed foundation piles within grid A1.
- Capstone grouted foundation piles within grid B3.
- Glenco conducted hot work along SOE piles within western portion of the site.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:30. No exceedances of volatile organic compounds (VOCs) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	Loads Exported Today	Cumulative Loads Exported
Allocco Recycling Corp.	0	17

Imported Material:

Facility	Material Imported	CY Imported Today	Cumulative CY Imported
Braen Stone, Haledon Quarry	2 ½" Crushed Stone	0	20

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/28/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 52-62°F, Partly Cloudy, RH: 49% Pres: 30.48” Wind: NE @ 9 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks and foundation piles along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/28/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 52-62°F, Partly Cloudy, RH: 49% Pres: 30.48" Wind: NE @ 9 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

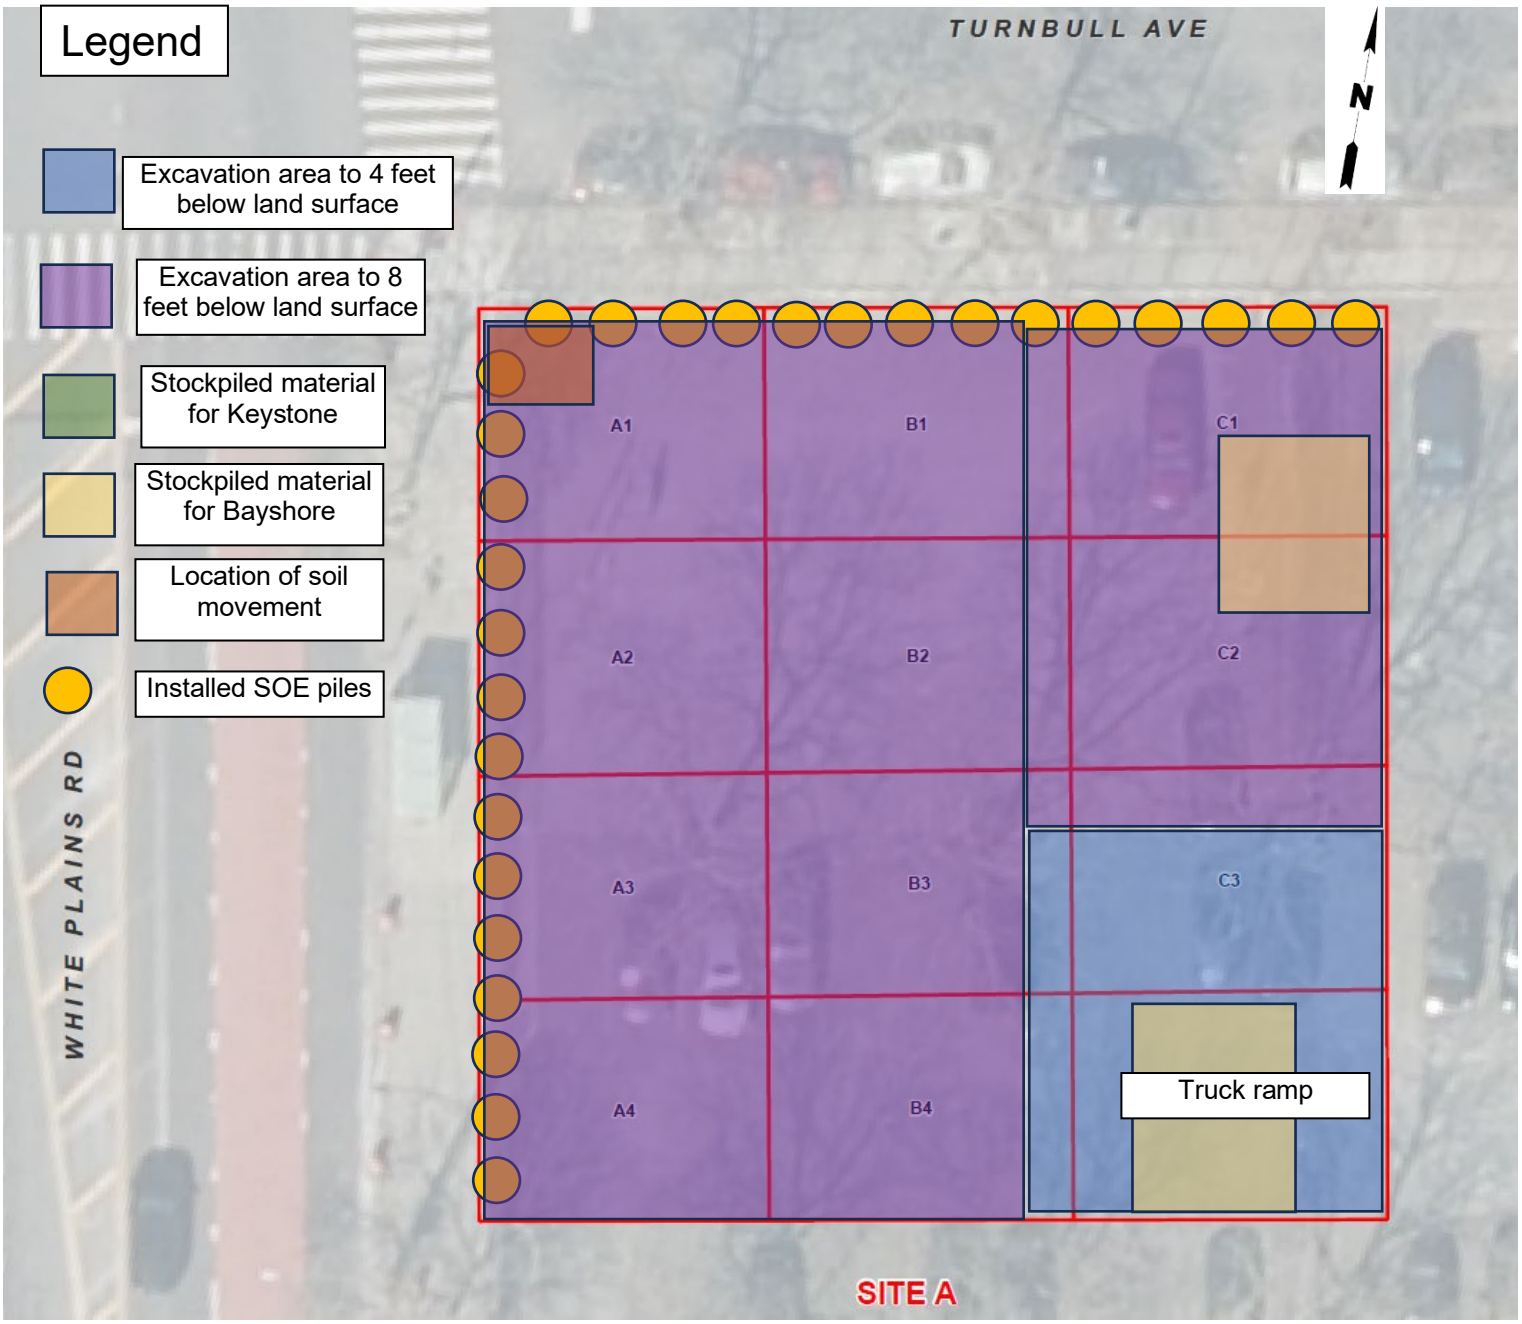

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/28/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 52-62°F, Partly Cloudy, RH: 49% Pres: 30.48” Wind: NE @ 9 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Capstone installs foundation piles in grid A1 along the northern boundary of the site.



Photo 2:
Facing west, Capstone grouts piles installed within grid B3.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/28/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 52-62°F, Partly Cloudy, RH: 49% Pres: 30.48” Wind: NE @ 9 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

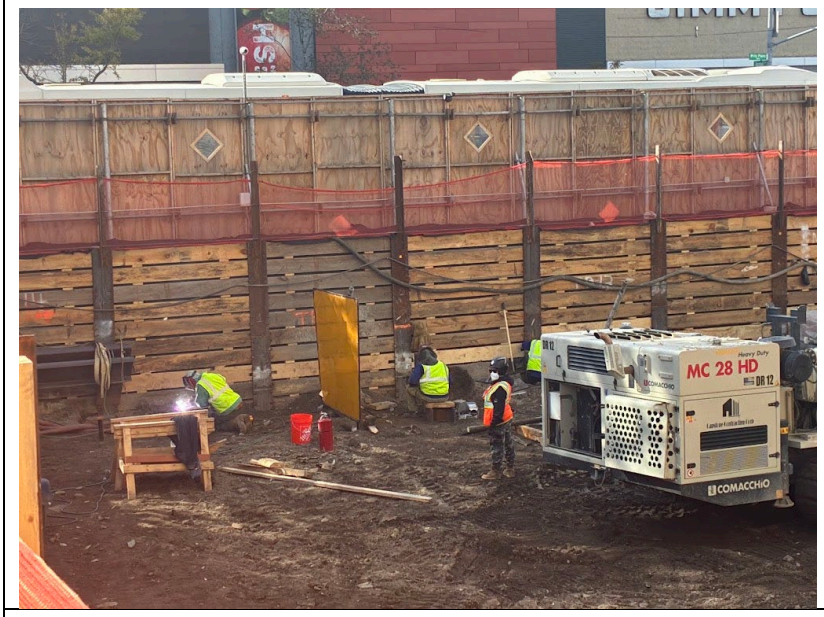


Photo 3:
Facing west, Glenco conducts hot work along the SOE on the western portion of the Site.



Photo 4: south, view of north CAMP station located within northwest site corner.


Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/28/2026 07:00
		To: 10/28/2026 16:30

Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/28/2026	43.9 - 64.8	41.8 - 54.1	30.4 - 30.6	0.6 - 6.6	NNE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/28/2026	0.0	07:30	0.0000	07:45
Max Contribution (15 min avg.) - 10/28/2026	3.4	13:30	0.0300	07:15
Daily Avg. Contribution (15 min avg.) - 10/28/2026	0.2	-	0.0037	-

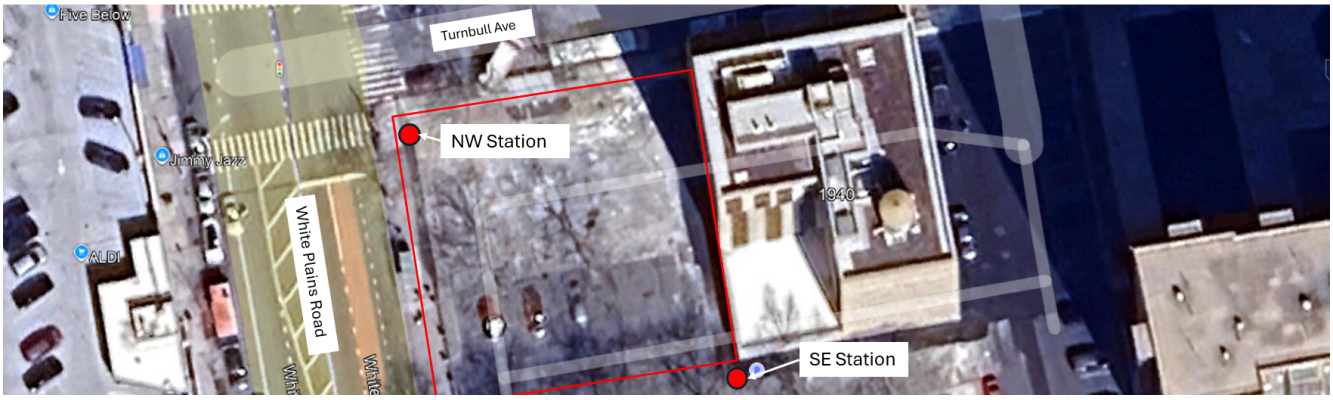


Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

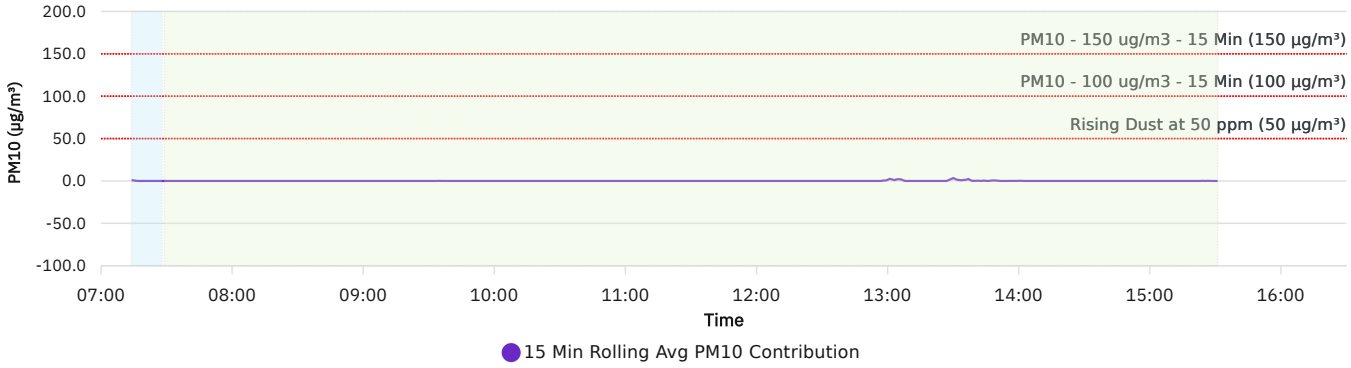

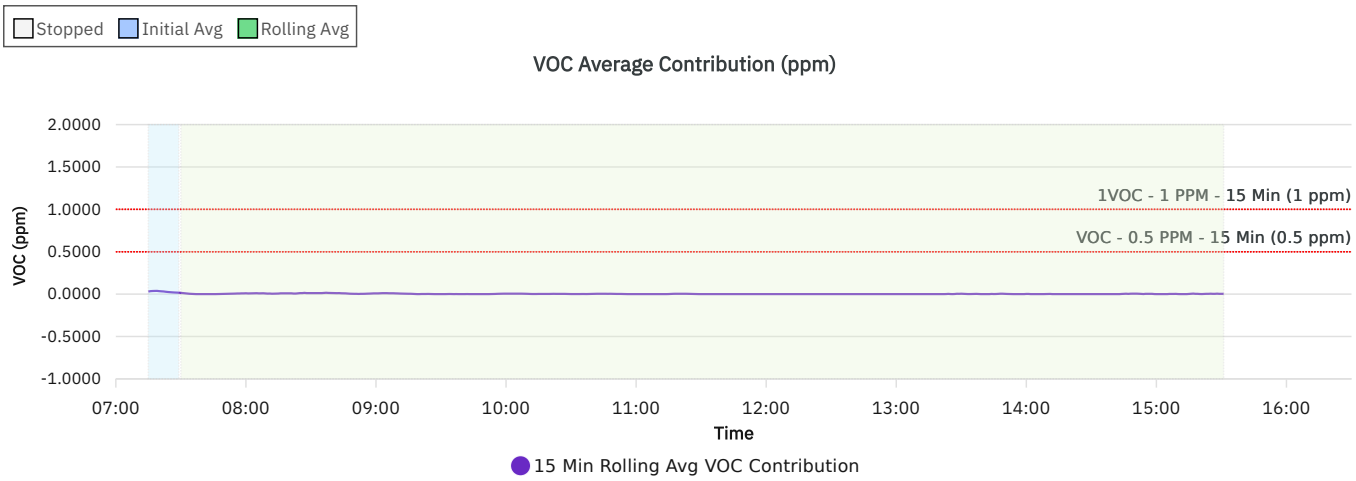

Wind rose (mph)

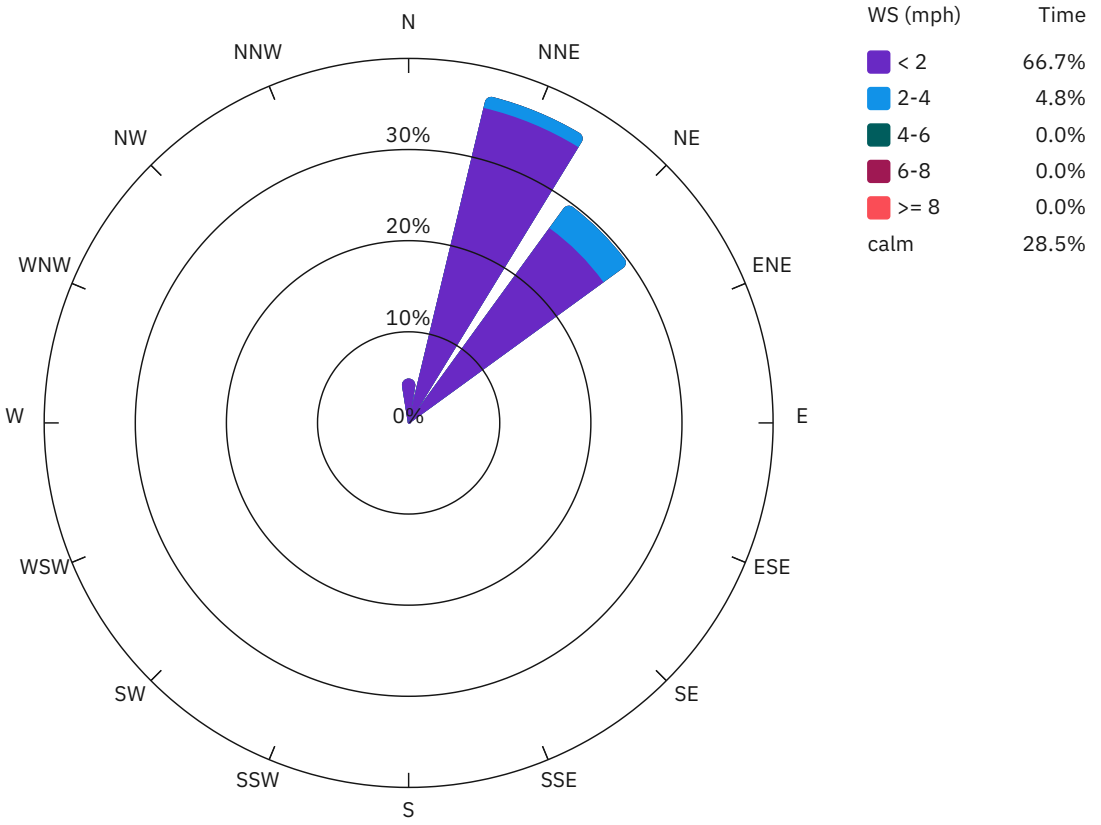

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/28/2026 07:15	2.5	3.0	0.6	0.0100	0.0400	0.0300	1.1	NE
10/28/2026 07:30	5.9	3.9	0.0	0.0153	0.0300	0.0147	1.2	NE
10/28/2026 07:45	8.3	5.4	0.0	0.0220	0.0213	0.0000	1.1	NNE
10/28/2026 08:00	25.3	7.4	0.0	0.0200	0.0300	0.0100	1.3	NNE
10/28/2026 08:15	21.1	12.8	0.0	0.0267	0.0333	0.0067	1.2	NNE
10/28/2026 08:30	16.6	9.0	0.0	0.0240	0.0360	0.0120	1.2	NNE
10/28/2026 08:45	14.0	5.9	0.0	0.0220	0.0313	0.0093	1.3	NNE
10/28/2026 09:00	11.0	4.9	0.0	0.0220	0.0307	0.0087	1.3	NNE
10/28/2026 09:15	5.2	2.9	0.0	0.0220	0.0260	0.0040	1.3	NNE
10/28/2026 09:30	3.9	3.5	0.0	0.0233	0.0233	0.0000	1.2	NNE
10/28/2026 09:45	8.1	4.6	0.0	0.0200	0.0200	0.0000	1.5	NNE
10/28/2026 10:00	13.3	1.9	0.0	0.0193	0.0247	0.0053	1.4	NE
10/28/2026 10:15	11.3	1.5	0.0	0.0180	0.0200	0.0020	1.8	NE
10/28/2026 10:30	7.9	2.5	0.0	0.0187	0.0193	0.0007	1.5	NE
10/28/2026 10:45	12.0	2.2	0.0	0.0187	0.0227	0.0040	1.4	NE
10/28/2026 11:00	9.0	4.6	0.0	0.0193	0.0180	0.0000	1.6	NNE
10/28/2026 11:15	9.3	3.5	0.0	0.0133	0.0140	0.0007	1.3	NNE
10/28/2026 11:30	6.1	3.1	0.0	0.0160	0.0153	0.0000	1.5	NNE
10/28/2026 11:45	10.0	2.3	0.0	0.0193	0.0133	0.0000	1.6	NNE
10/28/2026 12:00	10.9	3.4	0.0	0.0160	0.0113	0.0000	1.4	NE
10/28/2026 12:15	3.7	2.6	0.0	0.0120	0.0120	0.0000	1.0	NNE
10/28/2026 12:30	3.4	1.9	0.0	0.0160	0.0107	0.0000	1.3	NNE
10/28/2026 12:45	8.5	2.6	0.0	0.0167	0.0047	0.0000	1.4	NNE
10/28/2026 13:00	6.3	7.6	1.3	0.0107	0.0067	0.0000	1.2	NNE
10/28/2026 13:15	11.3	3.2	0.0	0.0113	0.0067	0.0000	1.1	NNE
10/28/2026 13:30	3.5	6.9	3.4	0.0080	0.0127	0.0047	1.1	NNE
10/28/2026 13:45	3.0	3.1	0.1	0.0100	0.0107	0.0007	0.9	NNE
10/28/2026 14:00	2.9	3.0	0.2	0.0073	0.0093	0.0020	0.9	NNE
10/28/2026 14:15	3.2	2.8	0.0	0.0080	0.0053	0.0000	0.8	NNE
10/28/2026 14:30	3.7	2.8	0.0	0.0173	0.0047	0.0000	1.0	NNE
10/28/2026 14:45	3.6	2.9	0.0	0.0100	0.0133	0.0033	0.6	N

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/28/2026 15:00	5.1	3.6	0.0	0.0073	0.0067	0.0000	0.8	NNE
10/28/2026 15:15	3.7	3.3	0.0	0.0067	0.0087	0.0020	0.7	NNE
10/28/2026 15:30	3.2	3.1	0.0	0.0113	0.0147	0.0033	0.5	NNW

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/29/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-68°F, Sunny, RH: 69% Pres: 30.28” Wind: SW @ 7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Capstone installed foundation piles within grid A1.
- Glenco conducted hot work along SOE piles within western portion of the site.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:15-15:30. No exceedances of volatile organic compounds (VOCs) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Allocco Recycling Corp.	0	17

Imported Material:

Facility	**Material Imported**	**CY Imported Today**	**Cumulative CY Imported**
Braen Stone, Haledon Quarry	2 ½” Crushed Stone	0	20

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/29/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-68°F, Sunny, RH: 69% Pres: 30.28” Wind: SW @ 7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks and foundation piles along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/29/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-68°F, Sunny, RH: 69% Pres: 30.28” Wind: SW @ 7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

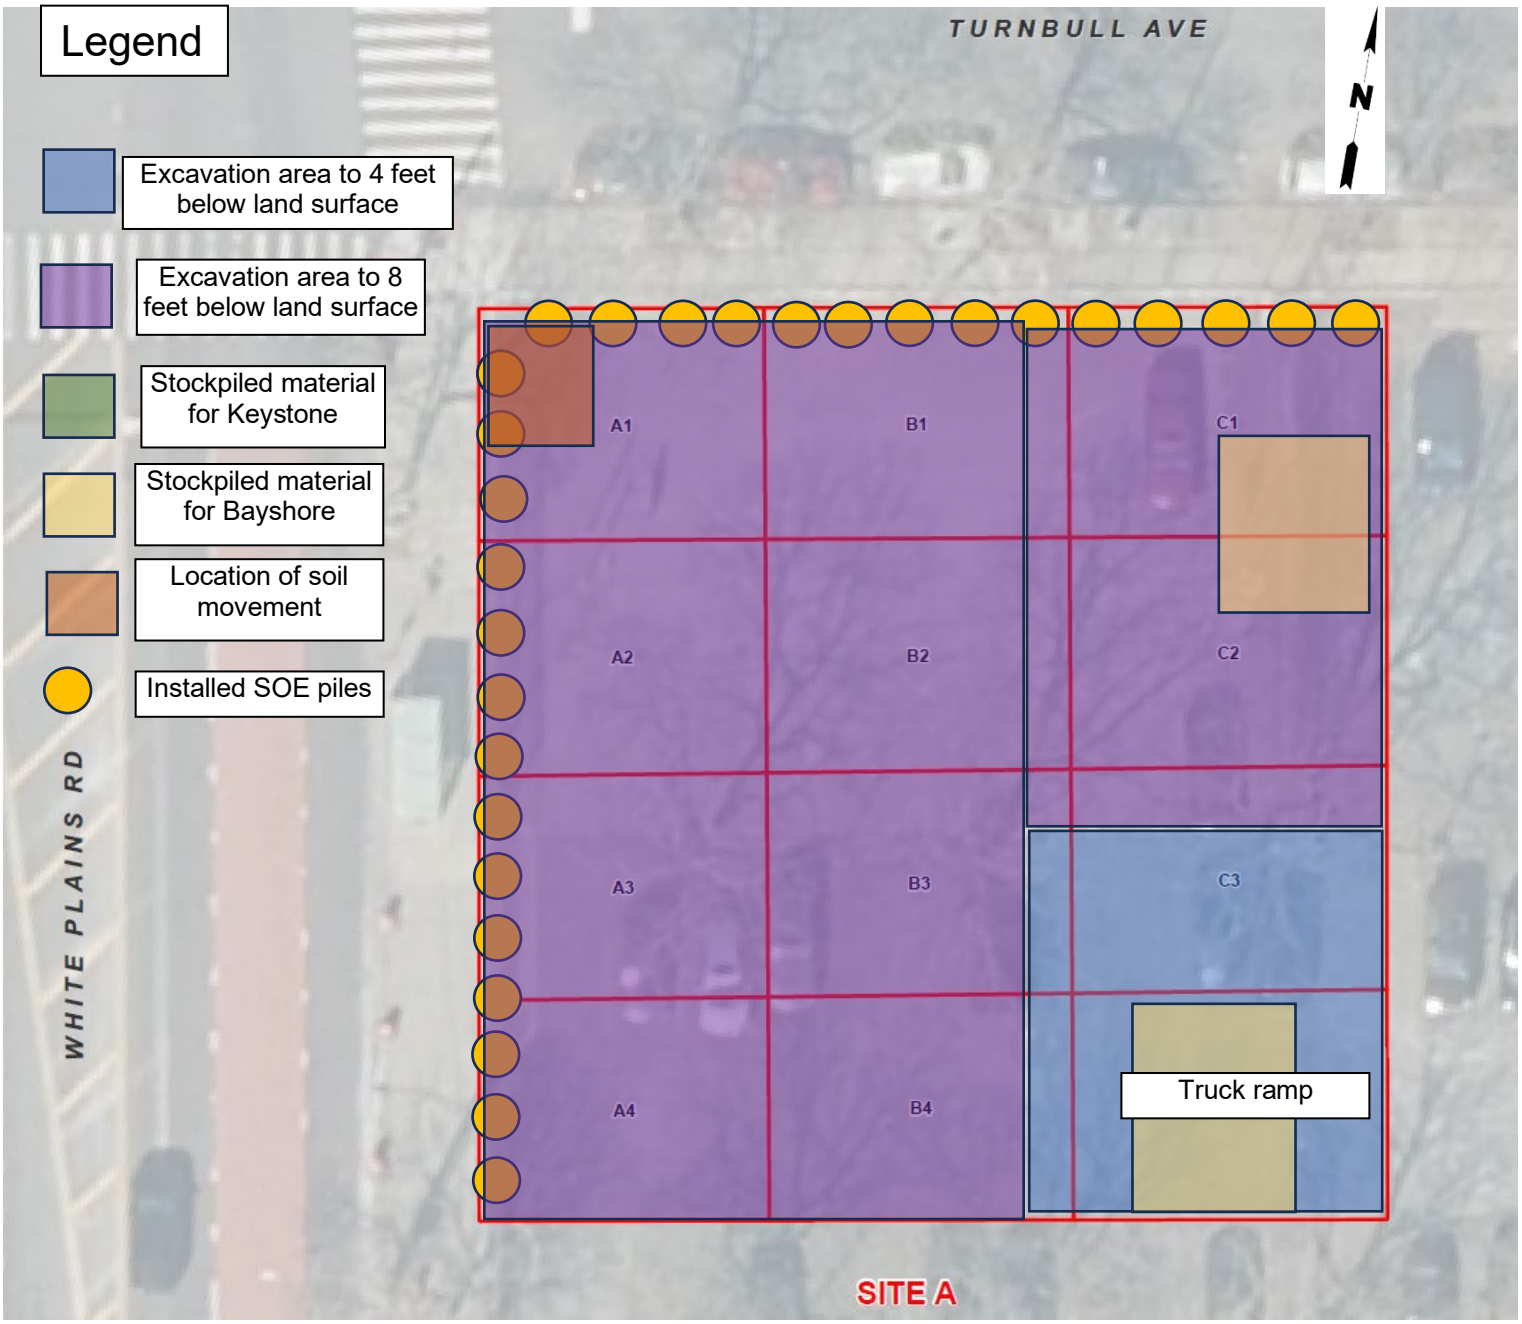

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/29/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-68°F, Sunny, RH: 69% Pres: 30.28” Wind: SW @ 7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Capstone installs foundation piles in grid A1 along the northern boundary of the site.



Photo 2:
Facing west, Glenco conducts hot work along the SOE on the western portion of the Site.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/29/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 58-68°F, Sunny, RH: 69% Pres: 30.28” Wind: SW @ 7 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

	**Photo 3**: Facing southwest, view of foundation piles installed by Capstone in grid A1.
	**Photo 4:** Facing northwest, view of south CAMP station located within southeast site corner.


Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/29/2026 07:00
		To: 10/29/2026 16:30


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/29/2026	46.0 - 68.7	47.3 - 83.3	30.2 - 30.4	0.3 - 7.9	SSE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/29/2026	0.0	07:15	0.0000	07:15
Max Contribution (15 min avg.) - 10/29/2026	3.2	09:30	0.0353	08:30
Daily Avg. Contribution (15 min avg.) - 10/29/2026	0.5	-	0.0021	-

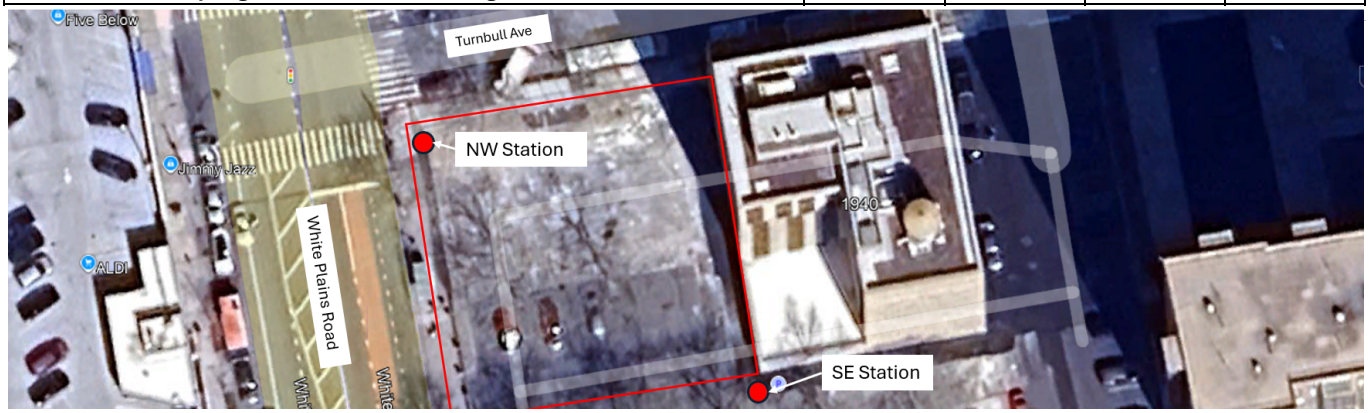


PM10 Average Contribution (µg/m³)

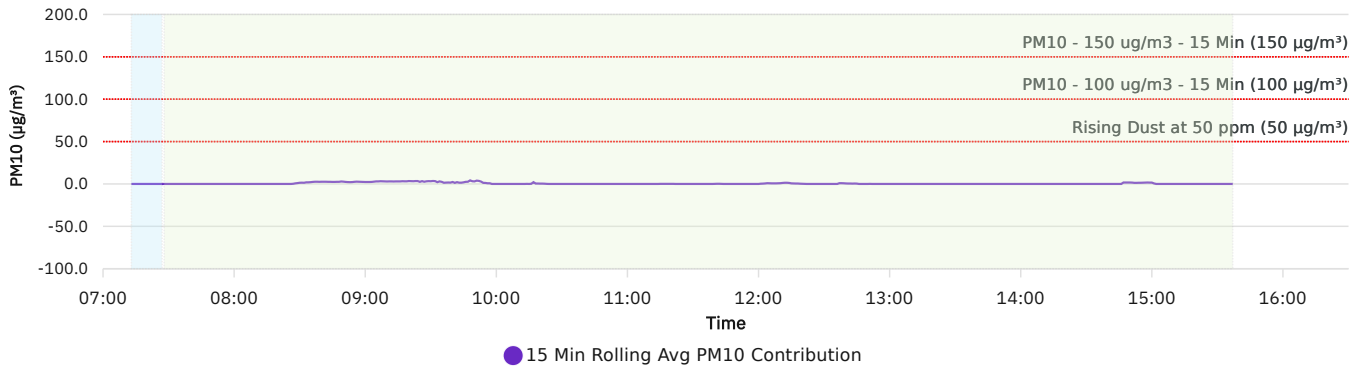

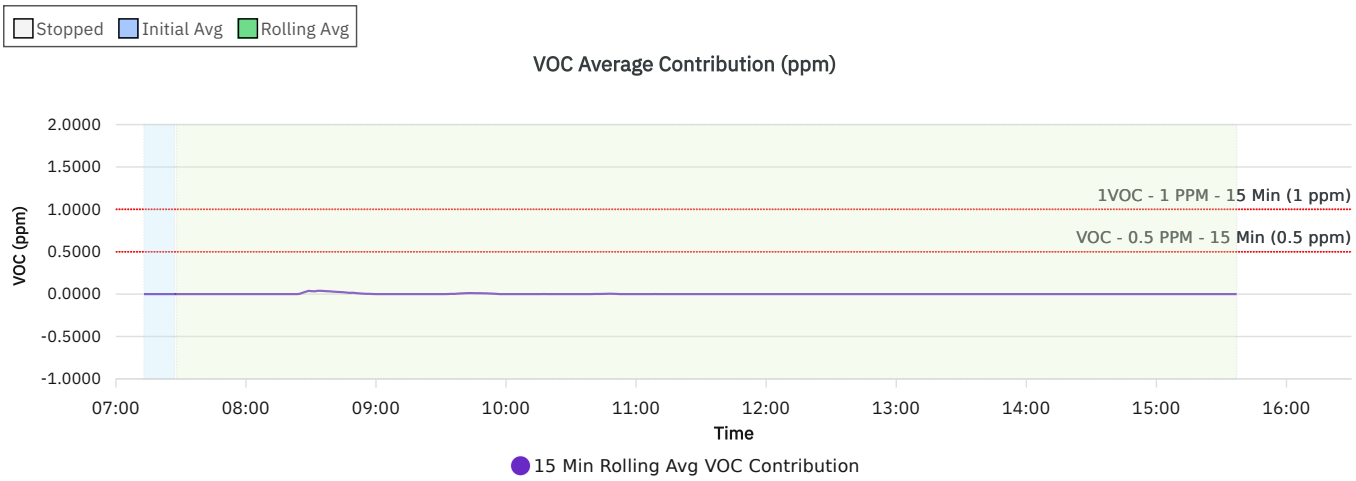

Wind rose (mph)

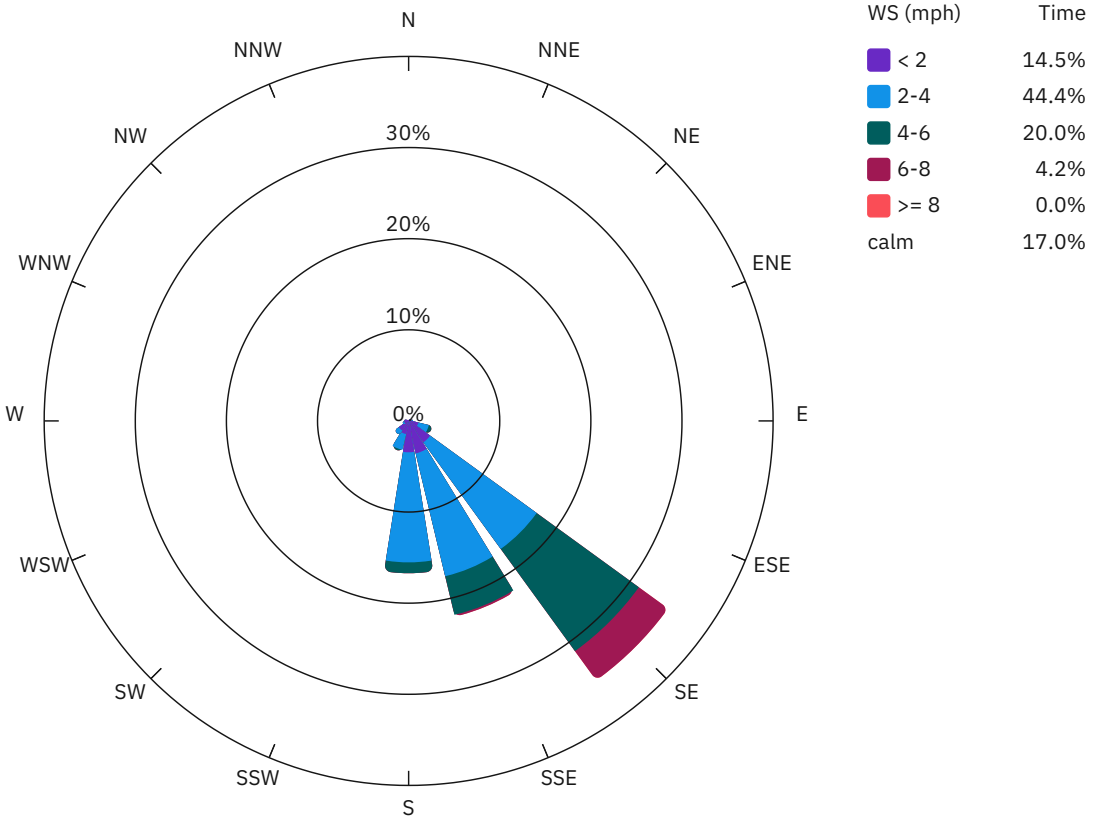

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/29/2026 07:15	18.8	15.6	0.0	0.1300	0.0300	0.0000	0.4	NNW
10/29/2026 07:30	19.0	15.9	0.0	0.1207	0.0307	0.0000	0.5	NNW
10/29/2026 07:45	15.3	13.2	0.0	0.1060	0.0300	0.0000	0.4	NW
10/29/2026 08:00	15.8	12.4	0.0	0.1127	0.0300	0.0000	0.3	W
10/29/2026 08:15	15.5	10.6	0.0	0.1100	0.0353	0.0000	0.3	NW
10/29/2026 08:30	7.9	9.3	1.4	0.0267	0.0620	0.0353	0.8	SE
10/29/2026 08:45	5.4	7.8	2.4	0.0227	0.0447	0.0220	1.3	SE
10/29/2026 09:00	3.1	5.5	2.3	0.0200	0.0187	0.0000	2.0	SE
10/29/2026 09:15	2.3	5.3	3.0	0.0200	0.0033	0.0000	2.2	SSE
10/29/2026 09:30	4.1	7.4	3.2	0.0193	0.0173	0.0000	2.0	SSE
10/29/2026 09:45	6.2	8.1	1.9	0.0213	0.0327	0.0113	1.7	SSE
10/29/2026 10:00	9.0	7.2	0.0	0.0200	0.0180	0.0000	1.9	SSE
10/29/2026 10:15	7.8	7.6	0.0	0.0200	0.0193	0.0000	1.4	S
10/29/2026 10:30	7.1	5.2	0.0	0.0200	0.0193	0.0000	1.6	S
10/29/2026 10:45	5.9	5.2	0.0	0.0133	0.0160	0.0027	2.5	S
10/29/2026 11:00	5.7	5.0	0.0	0.0160	0.0133	0.0000	3.1	SSE
10/29/2026 11:15	5.3	5.4	0.1	0.0147	0.0133	0.0000	3.0	SSE
10/29/2026 11:30	5.7	5.1	0.0	0.0187	0.0127	0.0000	2.9	SE
10/29/2026 11:45	6.0	5.8	0.0	0.0200	0.0107	0.0000	2.9	SSE
10/29/2026 12:00	6.0	5.9	0.0	0.0200	0.0107	0.0000	3.8	SSE
10/29/2026 12:15	5.7	6.4	0.7	0.0187	0.0120	0.0000	4.2	SSE
10/29/2026 12:30	6.6	6.0	0.0	0.0100	0.0013	0.0000	5.3	SE
10/29/2026 12:45	7.4	7.9	0.4	0.0153	0.0020	0.0000	4.5	SE
10/29/2026 13:00	7.3	6.1	0.0	0.0113	0.0013	0.0000	4.9	SE
10/29/2026 13:15	6.4	5.5	0.0	0.0100	0.0020	0.0000	4.9	SE
10/29/2026 13:30	6.1	5.1	0.0	0.0093	0.0007	0.0000	3.7	SSE
10/29/2026 13:45	6.1	5.2	0.0	0.0127	0.0007	0.0000	2.9	SSE
10/29/2026 14:00	6.7	5.8	0.0	0.0113	0.0007	0.0000	3.2	SE
10/29/2026 14:15	6.6	6.0	0.0	0.0087	0.0013	0.0000	2.5	SSE
10/29/2026 14:30	6.7	5.9	0.0	0.0100	0.0000	0.0000	2.7	SSE
10/29/2026 14:45	7.8	6.6	0.0	0.0133	0.0000	0.0000	3.7	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/29/2026 15:00	8.6	10.2	1.6	0.0093	0.0020	0.0000	3.2	SSE
10/29/2026 15:15	6.7	6.4	0.0	0.0100	0.0000	0.0000	4.1	SE
10/29/2026 15:30	6.6	6.5	0.0	0.0113	0.0000	0.0000	3.3	SE

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/30/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-69°F, Mostly Cloudy, RH: 72% Pres: 30.02" Wind: SW @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

CONTRACTOR AND EQUIPMENT	**PERSONNEL PRESENT AT SITE AND AFFILIATION:**
Glenco -Caterpillar 330 Hydraulic Excavator (30-ton class) -Bobcat E85 Excavator -Bobcat T740 Skid Steer -United Rentals Towable 45 kW Diesel Generator -Hutte HBR 504 tieback rig Capstone Contracting Corp. -Comacchio MC 28 HD Drill Rig -Volvo ECR355E Excavator	Margaret Saville – Roux D.P.C. Dan Mancini – Gilbane Building Company Lee Chapman – Glenco Contracting Romulo Simon Portillo – Glenco Contracting Capstone Contracting Corp.

SCOPE OF WORK:

Roux D.P.C. (Roux) will continue to be onsite to complete implementation of the Remedial Action (RA) in accordance with the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP), dated April 24, 2026. Roux implemented the Community Air Monitoring Plan (CAMP) during all intrusive activities.

Description of work activities performed and general observations/comments:

- Capstone installed foundation piles within grid A1.
- Glenco conducted hot work along SOE piles within western portion of the site.
- Glenco conducted general housekeeping throughout the Site.

CAMP data evaluation: CAMP was implemented from 07:30-15:30. No exceedances of volatile organic compounds (VOCs) or dust action levels were encountered.

Offsite Disposal:

Soil Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Keystone Trade Center	0	105
Bayshore Soil Management, LLC	0	76
Conestoga Landfill	0	3

Concrete/Asphalt Disposal Facility	**Loads Exported Today**	**Cumulative Loads Exported**
Allocco Recycling Corp.	0	17

Imported Material:

Facility	**Material Imported**	**CY Imported Today**	**Cumulative CY Imported**
Braen Stone, Haledon Quarry	2 ½" Crushed Stone	0	20

Sampling Performed:

None.

Approved:	Patrick Perry	By:	**Margaret Saville** **ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.**

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/30/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-69°F, Mostly Cloudy, RH: 72% Pres: 30.02” Wind: SW @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30


Upcoming work activities anticipated:

- Glenco will continue exporting soil from site to approved facilities.
- Capstone will continue installing tiebacks and foundation piles along SOE.
- Glenco will continue to install lagging and welding T bars along SOE piles.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/30/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-69°F, Mostly Cloudy, RH: 72% Pres: 30.02" Wind: SW @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

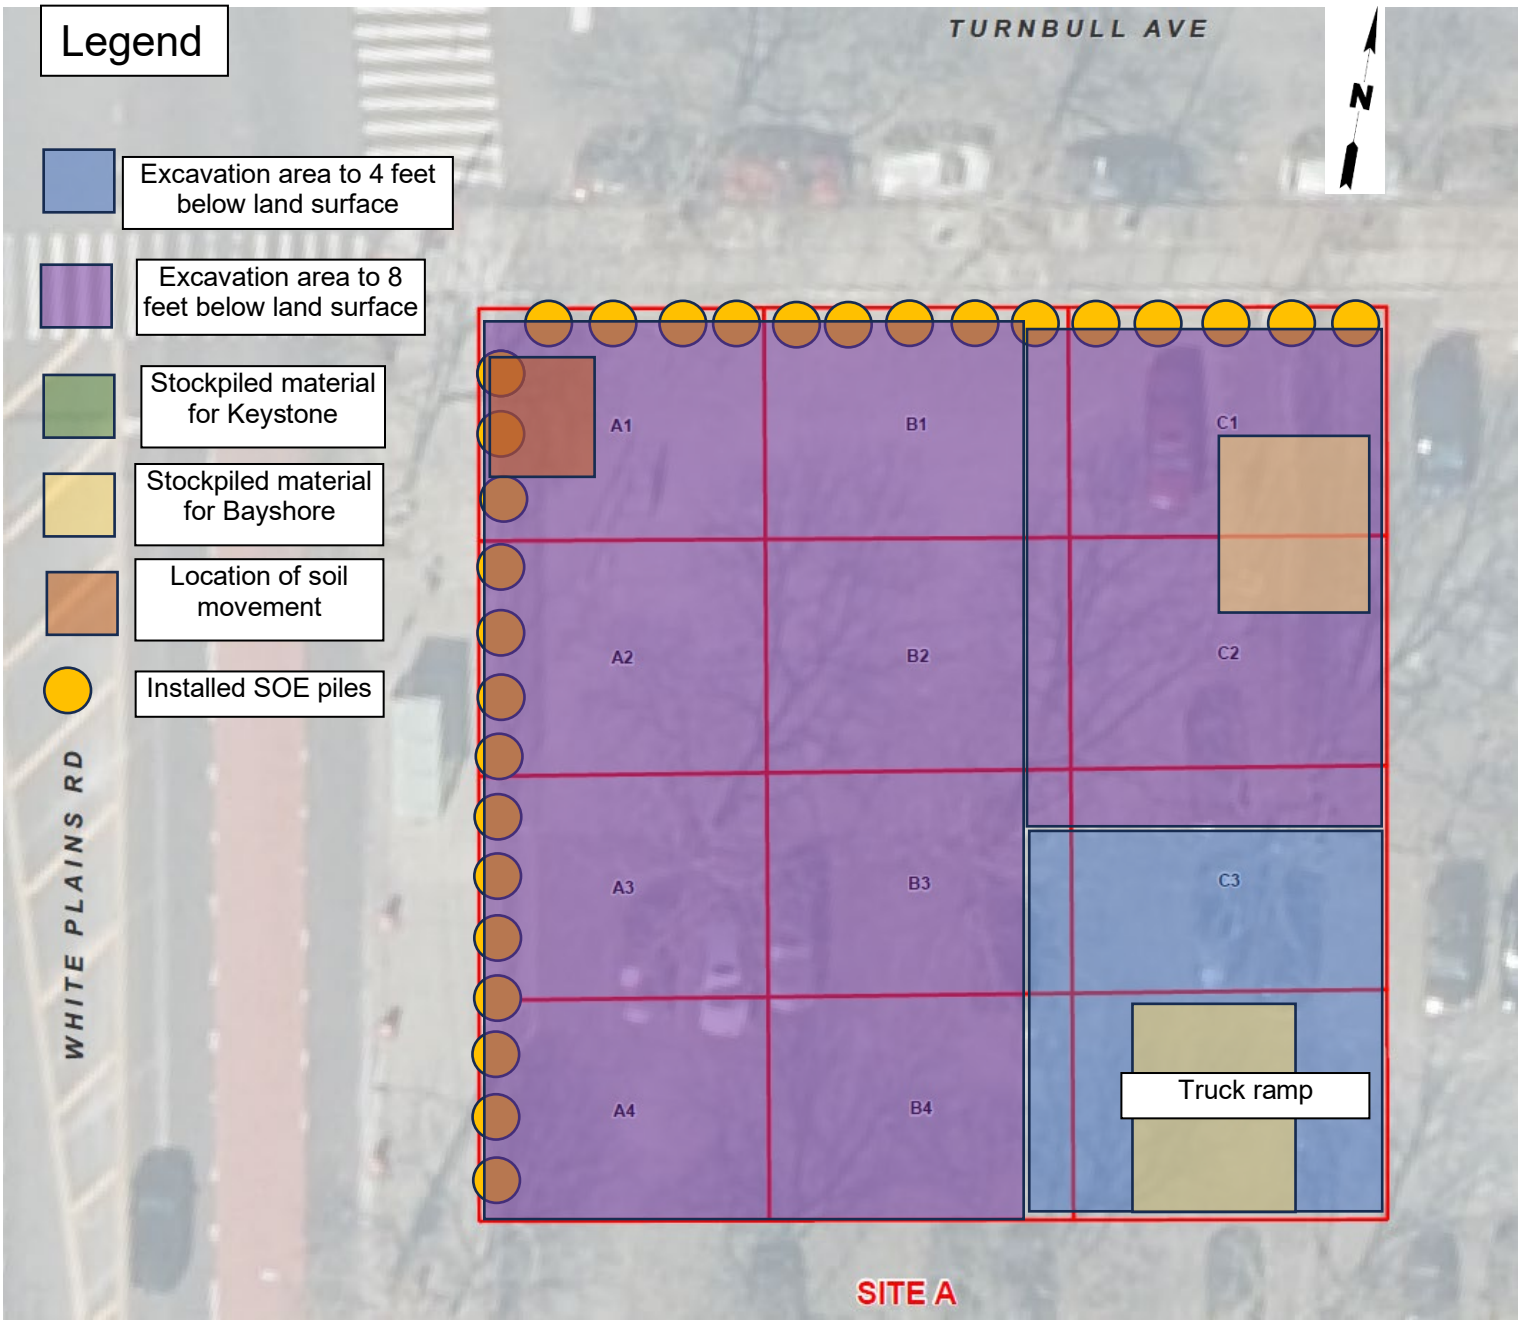

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/30/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-69°F, Mostly Cloudy, RH: 72% Pres: 30.02" Wind: SW @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30

PHOTOGRAPHS TAKEN TODAY: Lafayette Site A



Photo 1:
Facing north, Capstone installs foundation piles in grid A1 along the northern boundary of the site.



Photo 2:
Facing west, Glenco conducts hot work along the SOE on the western portion of the Site.

Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX

DAILY SITE FIELD ACTIVITY REPORT

PROJECT NO.:	3868.0004Y002	**CLIENT:**	**DATE:**	10/30/2026
PROJECT:	Lafayette Site A (C203178)	GDC Strada Castle Hill JV I LLC	**WEATHER:**	Temp: 49-69°F, Mostly Cloudy, RH: 72% Pres: 30.02” Wind: SW @ 6 mph
LOCATION:	1920 Turnbull Avenue, Bronx, NY		**TIME:**	07:00 – 15:30



Photo 3:
Facing southwest, view of foundation piles installed by Capstone in grid A1.



Photo 4: Facing south, view of north CAMP station located within northwest site corner.


Approved:	Patrick Perry	By:	**Margaret Saville**
			ROUX ENVIRONMENTAL ENGINEERING AND GEOLOGY, D.P.C.

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/30/2026 07:00
		To: 10/30/2026 16:30


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/30/2026	57.2 - 71.2	34.3 - 72.9	30.0 - 30.2	0.5 - 14.1	NE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/30/2026	0.0	09:30	0.0000	09:00
Max Contribution (15 min avg.) - 10/30/2026	3.8	07:30	0.0153	07:30
Daily Avg. Contribution (15 min avg.) - 10/30/2026	0.6	-	0.0009	-

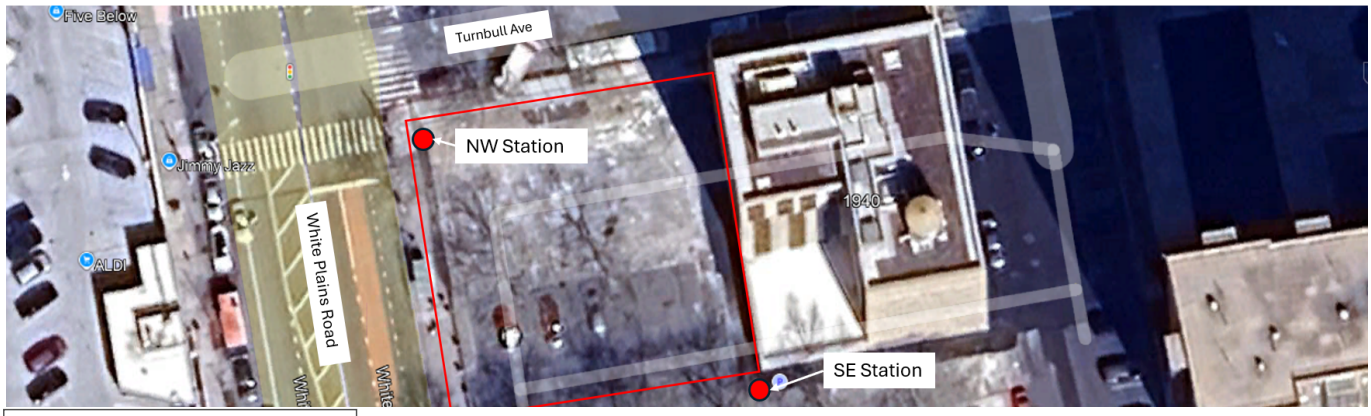


PM10 Average Contribution (µg/m³)

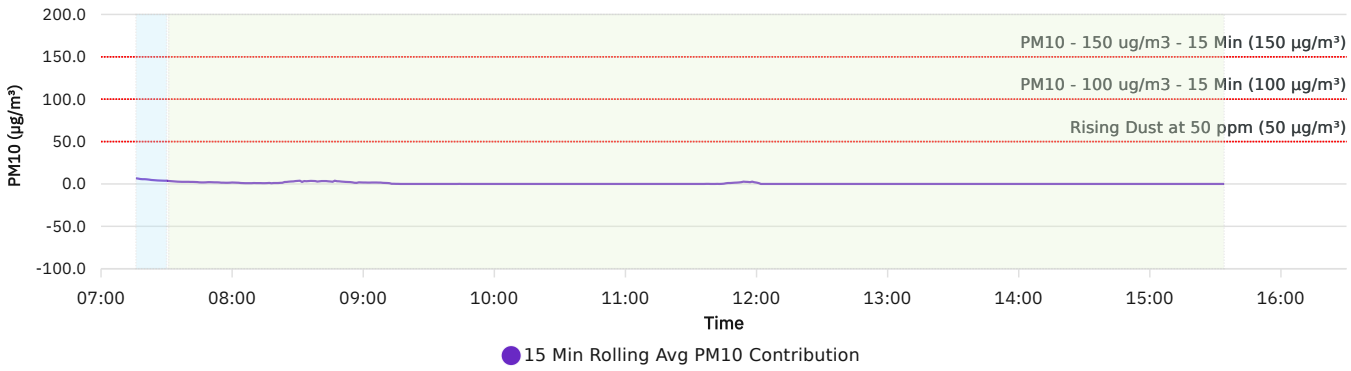

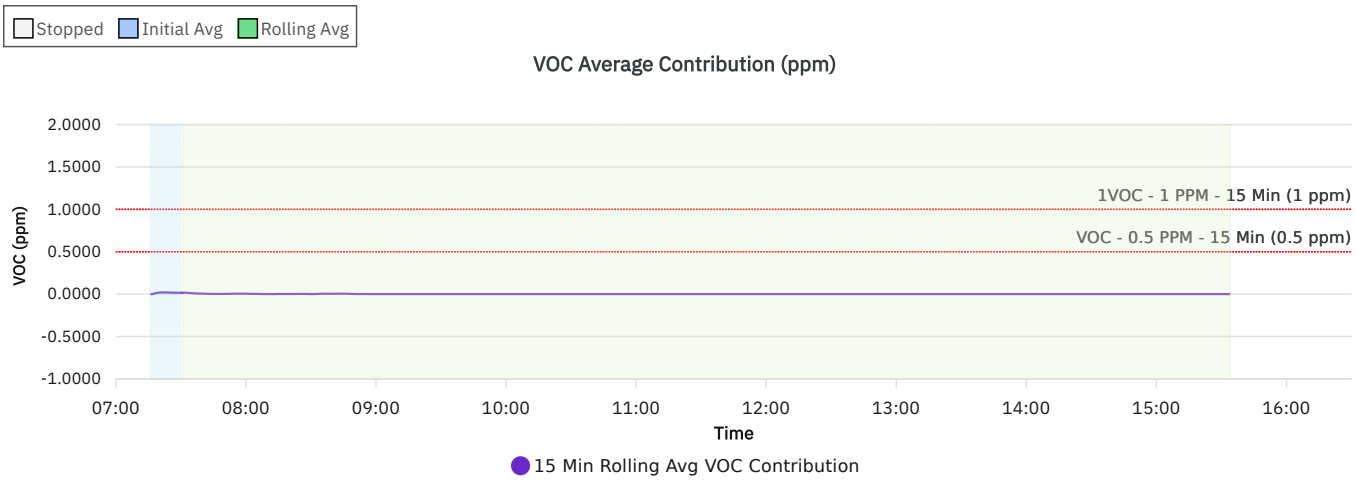

Wind rose (mph)

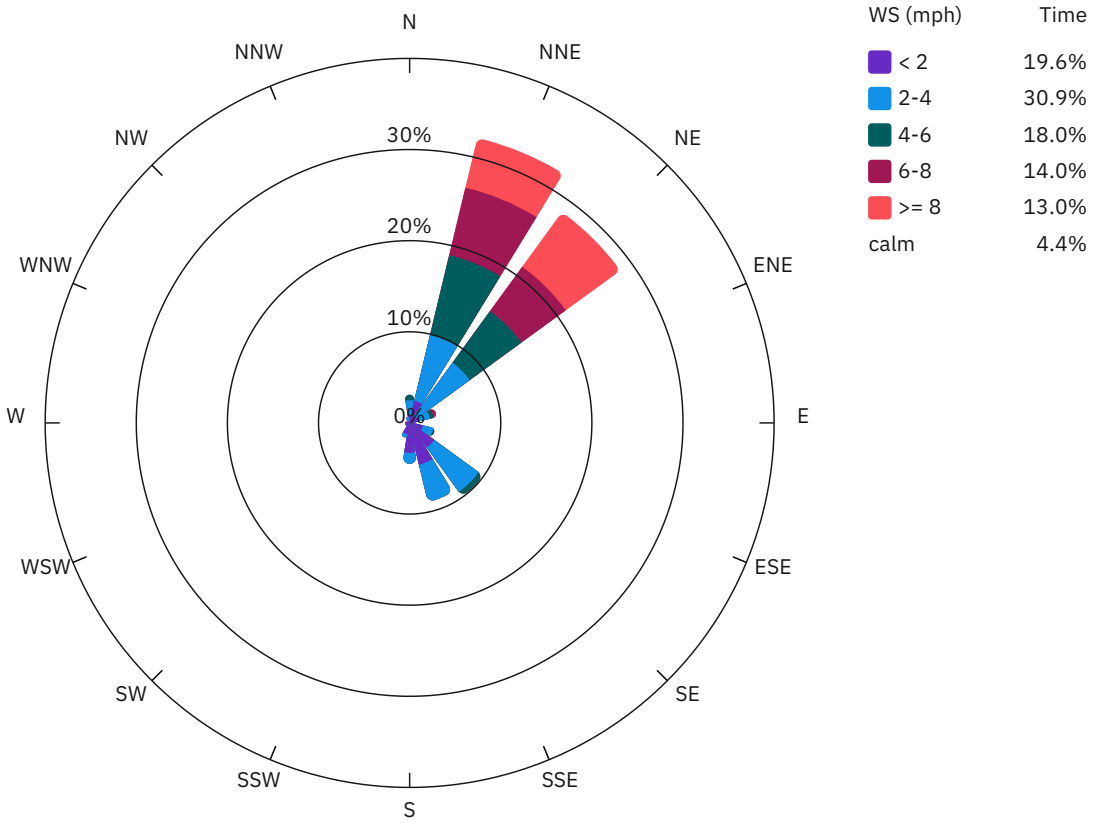

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/30/2026 07:30	10.7	14.5	3.8	0.0200	0.0353	0.0153	1.7	SSE
10/30/2026 07:45	9.7	11.6	1.9	0.0200	0.0220	0.0020	1.3	SSE
10/30/2026 08:00	9.7	11.4	1.7	0.0207	0.0253	0.0047	1.4	SSE
10/30/2026 08:15	9.6	10.5	0.9	0.0200	0.0213	0.0013	2.4	SE
10/30/2026 08:30	10.4	14.0	3.6	0.0200	0.0207	0.0007	1.9	SSE
10/30/2026 08:45	11.6	14.5	2.9	0.0200	0.0247	0.0047	2.1	SSE
10/30/2026 09:00	10.7	12.4	1.7	0.0200	0.0200	0.0000	2.5	SE
10/30/2026 09:15	10.8	10.9	0.1	0.0200	0.0200	0.0000	1.2	SE
10/30/2026 09:30	12.9	10.7	0.0	0.0180	0.0127	0.0000	1.5	ESE
10/30/2026 09:45	9.6	9.6	0.0	0.0180	0.0120	0.0000	0.6	ESE
10/30/2026 10:00	10.2	9.3	0.0	0.0213	0.0153	0.0000	1.1	ESE
10/30/2026 10:15	8.9	8.4	0.0	0.0180	0.0140	0.0000	1.5	NE
10/30/2026 10:30	9.4	8.7	0.0	0.0220	0.0133	0.0000	3.1	NNE
10/30/2026 10:45	9.0	8.5	0.0	0.0187	0.0120	0.0000	3.4	NNE
10/30/2026 11:00	9.7	8.8	0.0	0.0207	0.0107	0.0000	3.1	NNE
10/30/2026 11:15	9.2	8.4	0.0	0.0227	0.0120	0.0000	3.1	NNE
10/30/2026 11:30	8.5	7.9	0.0	0.0227	0.0040	0.0000	3.2	NNE
10/30/2026 11:45	8.6	8.9	0.3	0.0167	0.0060	0.0000	3.0	NNE
10/30/2026 12:00	8.0	9.6	1.6	0.0173	0.0013	0.0000	5.2	NE
10/30/2026 12:15	13.5	7.6	0.0	0.0167	0.0013	0.0000	5.0	NNE
10/30/2026 12:30	18.7	9.4	0.0	0.0120	0.0040	0.0000	5.5	NNE
10/30/2026 12:45	17.4	9.3	0.0	0.0093	0.0007	0.0000	4.8	NNE
10/30/2026 13:00	12.7	8.3	0.0	0.0140	0.0027	0.0000	5.1	NNE
10/30/2026 13:15	16.7	6.5	0.0	0.0100	0.0000	0.0000	9.4	NNE
10/30/2026 13:30	11.7	6.7	0.0	0.0087	0.0013	0.0000	6.3	NE
10/30/2026 13:45	12.3	6.7	0.0	0.0087	0.0013	0.0000	7.0	NNE
10/30/2026 14:00	32.9	7.1	0.0	0.0093	0.0007	0.0000	9.2	NE
10/30/2026 14:15	14.1	6.2	0.0	0.0100	0.0007	0.0000	6.4	NE
10/30/2026 14:30	10.1	5.4	0.0	0.0100	0.0000	0.0000	6.4	NNE
10/30/2026 14:45	8.9	4.1	0.0	0.0113	0.0000	0.0000	8.6	NE
10/30/2026 15:00	7.7	4.5	0.0	0.0093	0.0013	0.0000	5.0	NE


Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/30/2026 15:15	6.9	4.5	0.0	0.0093	0.0007	0.0000	4.5	NE
10/30/2026 15:30	8.9	4.4	0.0	0.0100	0.0000	0.0000	7.2	NNE

ROUX	Site Contribution Lafayette Site A (C203178)	Lafayette Site A
		DER-10 contribution
		Report Period
		From: 10/26/2026 07:00
		To: 10/26/2026 16:30


Sensor	Action Level
PM10	150 µg/m³
VOC	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
10/26/2026	47.1 - 78.6	29.0 - 64.8	30.1 - 30.4	0.3 - 6.9	ESE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 10/26/2026	0.0	07:29	0.0000	07:03
Max Contribution (15 min avg.) - 10/26/2026	473.8	14:42	0.0257	07:09
Daily Avg. Contribution (15 min avg.) - 10/26/2026	19.4	-	0.0051	-

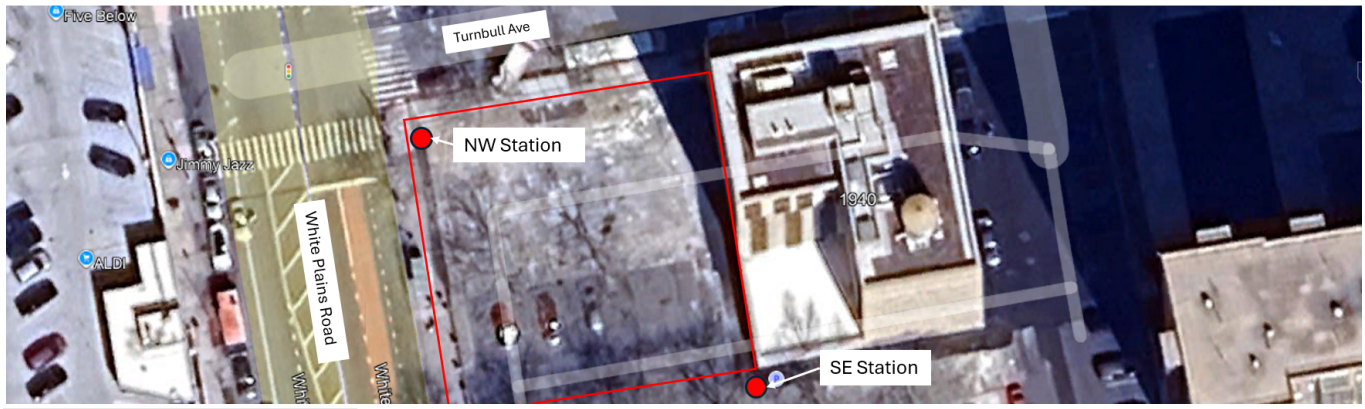


PM10 Average Contribution (µg/m³)

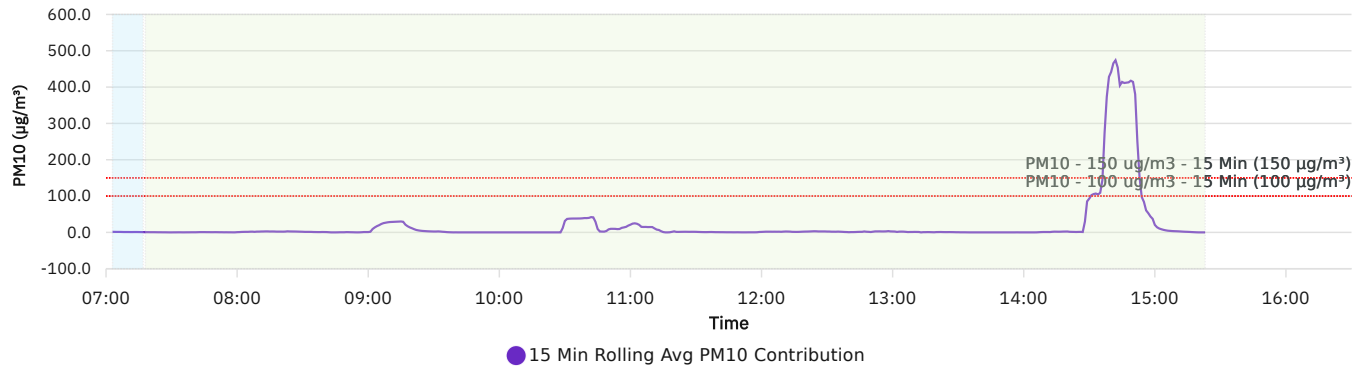

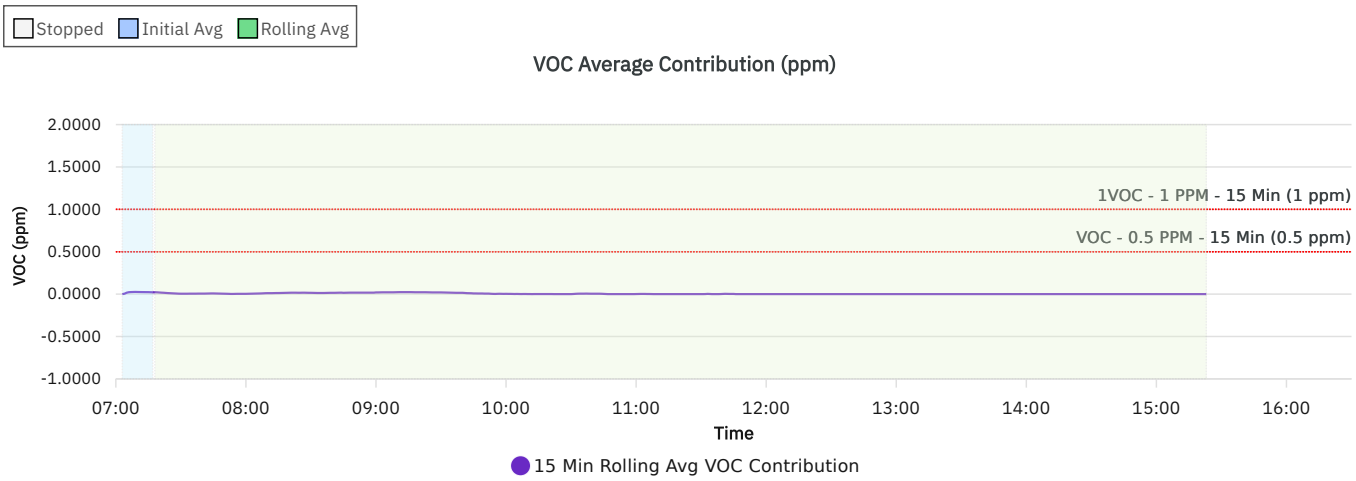

Wind rose (mph)

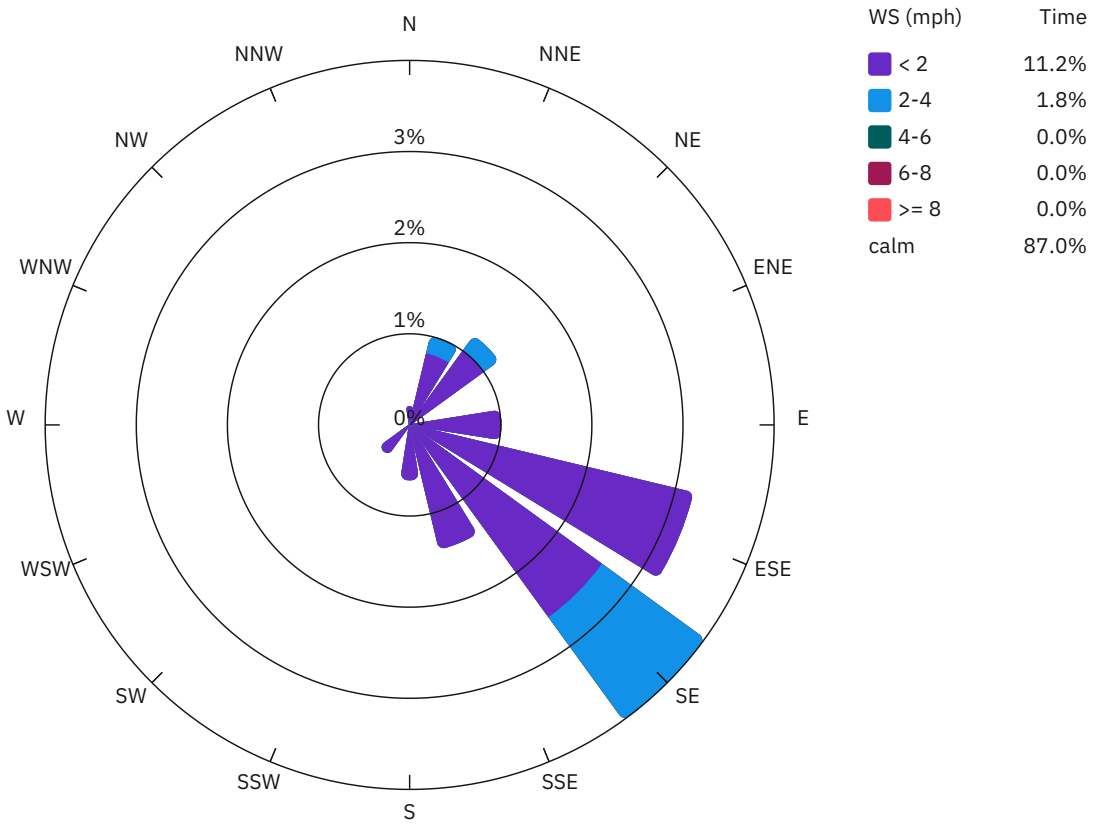

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 07:03	5.7	7.2	1.5	0.0000	0.0000	0.0000	0.7	E
10/26/2026 07:04	5.7	7.1	1.4	0.0000	0.0050	0.0050	0.8	SE
10/26/2026 07:05	5.7	7.0	1.3	0.0000	0.0167	0.0167	0.8	SE
10/26/2026 07:06	5.7	7.0	1.3	0.0000	0.0225	0.0225	0.9	ESE
10/26/2026 07:07	5.8	7.0	1.2	0.0020	0.0260	0.0240	0.7	S
10/26/2026 07:08	5.9	6.9	1.0	0.0033	0.0283	0.0250	0.7	ESE
10/26/2026 07:09	5.9	6.9	1.0	0.0043	0.0300	0.0257	0.7	ESE
10/26/2026 07:10	5.8	6.8	1.0	0.0050	0.0300	0.0250	0.7	SE
10/26/2026 07:11	5.9	6.8	0.9	0.0056	0.0300	0.0244	0.7	ESE
10/26/2026 07:12	5.9	6.8	0.9	0.0060	0.0300	0.0240	0.7	ESE
10/26/2026 07:13	5.8	6.8	1.0	0.0064	0.0300	0.0236	0.7	E
10/26/2026 07:14	5.8	6.7	1.0	0.0067	0.0300	0.0233	0.7	E
10/26/2026 07:15	5.7	6.6	0.9	0.0069	0.0300	0.0231	0.6	NE
10/26/2026 07:16	5.8	6.5	0.8	0.0071	0.0293	0.0221	0.6	E
10/26/2026 07:17	5.8	6.4	0.7	0.0073	0.0287	0.0213	0.6	ENE
10/26/2026 07:18	5.8	6.4	0.6	0.0080	0.0300	0.0220	0.6	SE
10/26/2026 07:19	5.8	6.3	0.6	0.0093	0.0307	0.0213	0.6	E
10/26/2026 07:20	5.8	6.3	0.5	0.0107	0.0300	0.0193	0.6	ESE
10/26/2026 07:21	5.8	6.2	0.5	0.0120	0.0293	0.0173	0.5	ESE
10/26/2026 07:22	5.7	6.2	0.5	0.0127	0.0287	0.0160	0.6	E
10/26/2026 07:23	5.7	6.2	0.4	0.0133	0.0273	0.0140	0.6	E
10/26/2026 07:24	5.8	6.1	0.3	0.0140	0.0260	0.0120	0.6	ESE
10/26/2026 07:25	5.8	6.1	0.3	0.0147	0.0253	0.0107	0.6	E
10/26/2026 07:26	5.8	6.1	0.2	0.0153	0.0247	0.0093	0.6	ESE
10/26/2026 07:27	5.9	6.0	0.2	0.0160	0.0240	0.0080	0.6	SE
10/26/2026 07:28	6.0	6.0	0.1	0.0167	0.0233	0.0067	0.6	ESE
10/26/2026 07:29	6.0	6.0	0.0	0.0173	0.0227	0.0053	0.6	ESE
10/26/2026 07:30	6.1	6.1	0.0	0.0180	0.0227	0.0047	0.6	ESE
10/26/2026 07:31	6.1	6.2	0.1	0.0187	0.0233	0.0047	0.6	ESE
10/26/2026 07:32	6.2	6.3	0.1	0.0193	0.0240	0.0047	0.6	SE
10/26/2026 07:33	6.3	6.5	0.2	0.0200	0.0247	0.0047	0.6	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 07:34	6.3	6.5	0.2	0.0200	0.0253	0.0053	0.7	ESE
10/26/2026 07:35	6.4	6.5	0.1	0.0200	0.0253	0.0053	0.7	ESE
10/26/2026 07:36	6.3	6.5	0.1	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:37	6.3	6.5	0.2	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:38	6.3	6.5	0.2	0.0200	0.0260	0.0060	0.8	SE
10/26/2026 07:39	6.3	6.5	0.3	0.0200	0.0260	0.0060	0.7	ESE
10/26/2026 07:40	6.2	6.6	0.3	0.0200	0.0260	0.0060	0.8	ESE
10/26/2026 07:41	6.3	6.6	0.3	0.0200	0.0260	0.0060	0.8	E
10/26/2026 07:42	6.4	6.8	0.5	0.0200	0.0267	0.0067	0.8	ESE
10/26/2026 07:43	6.4	7.0	0.7	0.0200	0.0273	0.0073	0.8	ESE
10/26/2026 07:44	6.4	7.1	0.7	0.0200	0.0280	0.0080	0.8	ESE
10/26/2026 07:45	6.4	7.1	0.7	0.0200	0.0280	0.0080	0.8	SE
10/26/2026 07:46	6.5	7.1	0.6	0.0200	0.0273	0.0073	0.8	E
10/26/2026 07:47	6.5	7.0	0.6	0.0200	0.0267	0.0067	0.8	ESE
10/26/2026 07:48	6.3	6.9	0.5	0.0200	0.0260	0.0060	0.8	ESE
10/26/2026 07:49	6.3	6.9	0.5	0.0200	0.0253	0.0053	0.8	ESE
10/26/2026 07:50	6.3	6.9	0.6	0.0200	0.0247	0.0047	0.8	SE
10/26/2026 07:51	6.4	6.9	0.5	0.0200	0.0240	0.0040	0.8	E
10/26/2026 07:52	6.6	7.0	0.4	0.0200	0.0233	0.0033	0.8	E
10/26/2026 07:53	6.7	7.1	0.4	0.0207	0.0227	0.0020	0.7	NNW
10/26/2026 07:54	6.8	7.0	0.2	0.0207	0.0227	0.0020	0.7	NE
10/26/2026 07:55	6.9	7.2	0.3	0.0207	0.0233	0.0027	0.6	NE
10/26/2026 07:56	7.0	7.2	0.2	0.0207	0.0240	0.0033	0.6	ENE
10/26/2026 07:57	6.9	7.1	0.2	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 07:58	6.9	7.0	0.1	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 07:59	6.9	7.0	0.1	0.0207	0.0240	0.0033	0.6	ESE
10/26/2026 08:00	6.8	7.5	0.6	0.0207	0.0240	0.0033	0.6	SE
10/26/2026 08:01	6.8	7.6	0.8	0.0207	0.0247	0.0040	0.6	ESE
10/26/2026 08:02	6.9	8.0	1.2	0.0207	0.0253	0.0047	0.6	ESE
10/26/2026 08:03	7.0	8.4	1.4	0.0207	0.0260	0.0053	0.6	E
10/26/2026 08:04	7.1	8.6	1.5	0.0207	0.0267	0.0060	0.6	SSE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 08:05	7.1	8.6	1.5	0.0207	0.0273	0.0067	0.6	ESE
10/26/2026 08:06	7.0	8.9	1.9	0.0207	0.0280	0.0073	0.6	E
10/26/2026 08:07	7.0	9.0	2.0	0.0207	0.0287	0.0080	0.6	SE
10/26/2026 08:08	8.0	9.5	1.5	0.0200	0.0293	0.0093	0.6	SE
10/26/2026 08:09	8.1	10.2	2.1	0.0200	0.0307	0.0107	0.6	ESE
10/26/2026 08:10	8.2	10.3	2.1	0.0200	0.0313	0.0113	0.7	E
10/26/2026 08:11	8.1	10.5	2.4	0.0200	0.0313	0.0113	0.7	SSE
10/26/2026 08:12	8.1	10.6	2.5	0.0200	0.0313	0.0113	0.7	SE
10/26/2026 08:13	8.1	10.7	2.7	0.0200	0.0320	0.0120	0.7	SE
10/26/2026 08:14	8.1	10.8	2.7	0.0200	0.0327	0.0127	0.7	ESE
10/26/2026 08:15	8.1	10.5	2.4	0.0200	0.0327	0.0127	0.7	ESE
10/26/2026 08:16	8.1	10.6	2.5	0.0200	0.0333	0.0133	0.7	SE
10/26/2026 08:17	8.0	10.4	2.4	0.0200	0.0340	0.0140	0.7	SE
10/26/2026 08:18	8.0	10.1	2.1	0.0200	0.0347	0.0147	0.7	SE
10/26/2026 08:19	7.9	10.1	2.1	0.0200	0.0353	0.0153	0.7	SE
10/26/2026 08:20	7.9	10.1	2.1	0.0200	0.0360	0.0160	0.7	SE
10/26/2026 08:21	8.0	9.9	2.0	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:22	7.9	10.0	2.2	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:23	7.0	9.8	2.9	0.0200	0.0367	0.0167	0.6	E
10/26/2026 08:24	6.8	9.4	2.6	0.0200	0.0360	0.0160	0.6	SSE
10/26/2026 08:25	6.7	9.2	2.5	0.0200	0.0360	0.0160	0.6	SE
10/26/2026 08:26	6.7	9.2	2.4	0.0200	0.0367	0.0167	0.6	ESE
10/26/2026 08:27	6.7	9.1	2.3	0.0200	0.0367	0.0167	0.6	SE
10/26/2026 08:28	6.9	9.0	2.1	0.0200	0.0360	0.0160	0.6	ESE
10/26/2026 08:29	7.0	8.9	1.9	0.0200	0.0353	0.0153	0.5	E
10/26/2026 08:30	6.9	8.7	1.7	0.0200	0.0353	0.0153	0.5	ESE
10/26/2026 08:31	7.0	8.4	1.4	0.0200	0.0347	0.0147	0.5	SE
10/26/2026 08:32	7.0	8.4	1.4	0.0200	0.0340	0.0140	0.6	SSE
10/26/2026 08:33	7.0	8.5	1.4	0.0200	0.0333	0.0133	0.6	ESE
10/26/2026 08:34	7.1	8.5	1.3	0.0200	0.0333	0.0133	0.6	ENE
10/26/2026 08:35	7.3	8.4	1.0	0.0200	0.0333	0.0133	0.5	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 08:36	7.4	8.3	0.9	0.0200	0.0333	0.0133	0.5	SE
10/26/2026 08:37	7.4	8.2	0.8	0.0200	0.0340	0.0140	0.5	SSE
10/26/2026 08:38	7.4	8.2	0.8	0.0200	0.0347	0.0147	0.5	SSE
10/26/2026 08:39	7.4	8.4	1.0	0.0200	0.0353	0.0153	0.5	SE
10/26/2026 08:40	7.3	8.3	0.9	0.0200	0.0353	0.0153	0.5	E
10/26/2026 08:41	7.3	8.1	0.8	0.0200	0.0353	0.0153	0.4	ENE
10/26/2026 08:42	7.5	7.9	0.4	0.0200	0.0360	0.0160	0.4	NE
10/26/2026 08:43	7.7	7.7	0.0	0.0200	0.0367	0.0167	0.4	E
10/26/2026 08:44	7.6	7.6	0.0	0.0200	0.0373	0.0173	0.4	SE
10/26/2026 08:45	7.7	7.7	0.0	0.0213	0.0367	0.0153	0.4	NNE
10/26/2026 08:46	7.7	7.8	0.1	0.0213	0.0373	0.0160	0.4	E
10/26/2026 08:47	7.7	8.0	0.3	0.0213	0.0380	0.0167	0.4	ENE
10/26/2026 08:48	7.7	8.0	0.3	0.0213	0.0387	0.0173	0.4	ENE
10/26/2026 08:49	7.6	8.0	0.3	0.0213	0.0387	0.0173	0.4	NE
10/26/2026 08:50	7.5	8.1	0.7	0.0213	0.0387	0.0173	0.4	NE
10/26/2026 08:51	7.4	8.1	0.6	0.0213	0.0387	0.0173	0.4	ESE
10/26/2026 08:52	7.4	7.8	0.4	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:53	7.3	7.6	0.3	0.0213	0.0387	0.0173	0.5	ESE
10/26/2026 08:54	7.3	7.4	0.1	0.0213	0.0387	0.0173	0.5	NE
10/26/2026 08:55	7.4	7.4	0.0	0.0213	0.0387	0.0173	0.5	ESE
10/26/2026 08:56	7.4	7.5	0.1	0.0213	0.0387	0.0173	0.5	SSE
10/26/2026 08:57	7.3	7.7	0.4	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:58	7.0	7.8	0.9	0.0213	0.0387	0.0173	0.5	E
10/26/2026 08:59	7.0	7.8	0.9	0.0213	0.0387	0.0173	0.5	E
10/26/2026 09:00	7.1	8.0	0.9	0.0200	0.0400	0.0200	0.6	E
10/26/2026 09:01	7.1	8.9	1.8	0.0200	0.0400	0.0200	0.6	ESE
10/26/2026 09:02	7.1	16.4	9.3	0.0200	0.0407	0.0207	0.6	E
10/26/2026 09:03	7.1	20.7	13.7	0.0200	0.0413	0.0213	0.6	E
10/26/2026 09:04	7.1	24.3	17.2	0.0200	0.0413	0.0213	0.6	SE
10/26/2026 09:05	7.2	27.1	19.9	0.0200	0.0413	0.0213	0.6	SE
10/26/2026 09:06	7.1	30.3	23.2	0.0200	0.0413	0.0213	0.5	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 09:07	7.2	32.7	25.5	0.0200	0.0413	0.0213	0.5	E
10/26/2026 09:08	7.2	34.0	26.7	0.0200	0.0413	0.0213	0.5	E
10/26/2026 09:09	7.3	35.1	27.8	0.0200	0.0420	0.0220	0.5	ESE
10/26/2026 09:10	7.4	35.8	28.5	0.0200	0.0427	0.0227	0.5	ESE
10/26/2026 09:11	7.4	36.2	28.8	0.0200	0.0433	0.0233	0.5	ENE
10/26/2026 09:12	7.4	36.5	29.1	0.0200	0.0433	0.0233	0.5	NE
10/26/2026 09:13	7.4	36.8	29.4	0.0200	0.0433	0.0233	0.5	E
10/26/2026 09:14	7.5	37.2	29.7	0.0200	0.0433	0.0233	0.5	ESE
10/26/2026 09:15	7.3	37.3	30.0	0.0200	0.0433	0.0233	0.4	E
10/26/2026 09:16	7.3	36.4	29.1	0.0200	0.0433	0.0233	0.4	ESE
10/26/2026 09:17	7.4	28.7	21.3	0.0200	0.0427	0.0227	0.4	SE
10/26/2026 09:18	7.4	24.4	17.0	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:19	7.3	21.2	13.8	0.0200	0.0420	0.0220	0.4	ESE
10/26/2026 09:20	7.3	18.7	11.4	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:21	7.3	16.1	8.8	0.0200	0.0420	0.0220	0.4	SSE
10/26/2026 09:22	7.3	13.9	6.6	0.0200	0.0420	0.0220	0.3	ESE
10/26/2026 09:23	7.2	12.6	5.4	0.0200	0.0420	0.0220	0.3	SE
10/26/2026 09:24	7.2	11.7	4.5	0.0200	0.0413	0.0213	0.3	ESE
10/26/2026 09:25	7.1	11.0	3.9	0.0200	0.0407	0.0207	0.3	NNE
10/26/2026 09:26	7.1	10.6	3.5	0.0200	0.0400	0.0200	0.3	ENE
10/26/2026 09:27	7.1	10.2	3.1	0.0200	0.0400	0.0200	0.3	NNE
10/26/2026 09:28	6.9	9.8	2.8	0.0200	0.0400	0.0200	0.3	NE
10/26/2026 09:29	6.8	9.5	2.6	0.0200	0.0400	0.0200	0.3	SE
10/26/2026 09:30	6.8	9.2	2.4	0.0200	0.0400	0.0200	0.3	E
10/26/2026 09:31	6.8	9.2	2.4	0.0200	0.0393	0.0193	0.3	SSE
10/26/2026 09:32	6.8	9.5	2.7	0.0200	0.0387	0.0187	0.3	E
10/26/2026 09:33	7.2	9.5	2.3	0.0200	0.0380	0.0180	0.3	E
10/26/2026 09:34	7.3	9.0	1.7	0.0200	0.0373	0.0173	0.3	ESE
10/26/2026 09:35	7.3	8.6	1.3	0.0200	0.0367	0.0167	0.3	SE
10/26/2026 09:36	7.4	8.1	0.7	0.0200	0.0360	0.0160	0.3	E
10/26/2026 09:37	7.5	7.9	0.4	0.0200	0.0353	0.0153	0.3	ESE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 09:38	7.5	7.8	0.2	0.0200	0.0353	0.0153	0.4	E
10/26/2026 09:39	7.6	7.7	0.0	0.0200	0.0353	0.0153	0.4	ESE
10/26/2026 09:40	7.7	7.8	0.1	0.0200	0.0353	0.0153	0.4	E
10/26/2026 09:41	7.8	7.8	0.0	0.0207	0.0340	0.0133	0.3	NW
10/26/2026 09:42	7.8	7.7	0.0	0.0213	0.0327	0.0113	0.3	NNW
10/26/2026 09:43	7.8	7.8	0.0	0.0213	0.0320	0.0107	0.3	NE
10/26/2026 09:44	7.8	7.7	0.0	0.0213	0.0313	0.0100	0.3	E
10/26/2026 09:45	7.9	7.7	0.0	0.0220	0.0300	0.0080	0.3	N
10/26/2026 09:46	7.9	7.5	0.0	0.0220	0.0300	0.0080	0.3	NNE
10/26/2026 09:47	7.8	7.2	0.0	0.0220	0.0293	0.0073	0.3	ENE
10/26/2026 09:48	7.3	7.1	0.0	0.0220	0.0293	0.0073	0.3	ENE
10/26/2026 09:49	7.2	7.0	0.0	0.0220	0.0293	0.0073	0.3	ESE
10/26/2026 09:50	7.0	7.0	0.0	0.0227	0.0287	0.0060	0.3	NNE
10/26/2026 09:51	7.0	6.9	0.0	0.0227	0.0287	0.0060	0.3	NE
10/26/2026 09:52	6.9	6.8	0.0	0.0227	0.0287	0.0060	0.3	ENE
10/26/2026 09:53	6.8	6.8	0.0	0.0233	0.0273	0.0040	0.3	NE
10/26/2026 09:54	6.7	6.6	0.0	0.0233	0.0260	0.0027	0.3	ESE
10/26/2026 09:55	7.8	6.4	0.0	0.0233	0.0253	0.0020	0.3	SE
10/26/2026 09:56	7.8	6.4	0.0	0.0227	0.0260	0.0033	0.3	NNE
10/26/2026 09:57	7.8	6.4	0.0	0.0220	0.0260	0.0040	0.3	ENE
10/26/2026 09:58	7.8	6.5	0.0	0.0220	0.0253	0.0033	0.3	SE
10/26/2026 09:59	7.8	6.5	0.0	0.0220	0.0247	0.0027	0.3	SE
10/26/2026 10:00	7.8	6.5	0.0	0.0213	0.0247	0.0033	0.3	SSE
10/26/2026 10:01	7.9	6.4	0.0	0.0213	0.0240	0.0027	0.3	ESE
10/26/2026 10:02	8.0	6.4	0.0	0.0213	0.0240	0.0027	0.3	SE
10/26/2026 10:03	8.0	6.3	0.0	0.0213	0.0233	0.0020	0.3	SE
10/26/2026 10:04	8.1	6.3	0.0	0.0213	0.0227	0.0013	0.3	NE
10/26/2026 10:05	8.3	6.2	0.0	0.0207	0.0227	0.0020	0.3	E
10/26/2026 10:06	8.3	6.1	0.0	0.0207	0.0220	0.0013	0.3	SE
10/26/2026 10:07	8.4	6.1	0.0	0.0207	0.0213	0.0007	0.3	ESE
10/26/2026 10:08	8.5	6.1	0.0	0.0200	0.0213	0.0013	0.3	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 10:09	8.6	6.0	0.0	0.0200	0.0213	0.0013	0.3	NNE
10/26/2026 10:10	7.3	5.8	0.0	0.0200	0.0207	0.0007	0.3	SE
10/26/2026 10:11	7.4	5.9	0.0	0.0200	0.0207	0.0007	0.3	SSE
10/26/2026 10:12	7.8	6.2	0.0	0.0207	0.0207	0.0000	0.3	SSW
10/26/2026 10:13	7.9	6.2	0.0	0.0207	0.0213	0.0007	0.3	ESE
10/26/2026 10:14	7.8	6.3	0.0	0.0207	0.0213	0.0007	0.2	N
10/26/2026 10:15	7.8	6.5	0.0	0.0207	0.0213	0.0007	0.2	NW
10/26/2026 10:16	7.8	6.5	0.0	0.0207	0.0213	0.0007	0.2	ENE
10/26/2026 10:17	7.8	6.4	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:18	7.7	6.4	0.0	0.0207	0.0213	0.0007	0.2	ENE
10/26/2026 10:19	7.6	6.3	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:20	7.6	6.4	0.0	0.0207	0.0213	0.0007	0.2	E
10/26/2026 10:21	7.6	6.4	0.0	0.0207	0.0213	0.0007	0.2	S
10/26/2026 10:22	7.5	6.5	0.0	0.0213	0.0213	0.0000	0.2	NNE
10/26/2026 10:23	7.4	6.7	0.0	0.0220	0.0220	0.0000	0.2	N
10/26/2026 10:24	7.3	6.7	0.0	0.0220	0.0220	0.0000	0.2	S
10/26/2026 10:25	7.4	6.7	0.0	0.0220	0.0220	0.0000	0.2	SE
10/26/2026 10:26	7.2	6.7	0.0	0.0220	0.0213	0.0000	0.2	SSE
10/26/2026 10:27	6.9	6.6	0.0	0.0213	0.0213	0.0000	0.2	SSW
10/26/2026 10:28	6.8	6.9	0.0	0.0213	0.0207	0.0000	0.2	ESE
10/26/2026 10:29	7.0	18.9	11.9	0.0213	0.0207	0.0000	0.2	SE
10/26/2026 10:30	7.4	38.9	31.5	0.0213	0.0213	0.0000	0.3	S
10/26/2026 10:31	7.6	44.6	37.0	0.0213	0.0227	0.0013	0.3	SSE
10/26/2026 10:32	7.7	45.5	37.7	0.0213	0.0247	0.0033	0.3	SE
10/26/2026 10:33	7.8	45.8	38.0	0.0213	0.0260	0.0047	0.3	SE
10/26/2026 10:34	7.8	45.9	38.1	0.0213	0.0267	0.0053	0.3	SSE
10/26/2026 10:35	7.9	46.1	38.1	0.0213	0.0267	0.0053	0.3	SW
10/26/2026 10:36	8.0	46.2	38.2	0.0213	0.0267	0.0053	0.3	ENE
10/26/2026 10:37	8.0	46.3	38.3	0.0207	0.0267	0.0060	0.3	ENE
10/26/2026 10:38	8.1	46.8	38.7	0.0207	0.0260	0.0053	0.4	ESE
10/26/2026 10:39	8.3	47.7	39.4	0.0213	0.0260	0.0047	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 10:40	8.8	48.1	39.3	0.0213	0.0260	0.0047	0.4	ESE
10/26/2026 10:41	9.0	48.9	39.9	0.0213	0.0260	0.0047	0.4	SE
10/26/2026 10:42	9.1	51.0	42.0	0.0213	0.0260	0.0047	0.4	SE
10/26/2026 10:43	9.4	50.7	41.3	0.0213	0.0260	0.0047	0.4	SSW
10/26/2026 10:44	9.6	38.7	29.1	0.0220	0.0260	0.0040	0.3	SW
10/26/2026 10:45	9.3	18.5	9.2	0.0227	0.0253	0.0027	0.3	NW
10/26/2026 10:46	10.4	12.9	2.5	0.0227	0.0240	0.0013	0.2	NE
10/26/2026 10:47	10.6	12.8	2.2	0.0227	0.0220	0.0000	0.2	WSW
10/26/2026 10:48	10.6	12.7	2.1	0.0227	0.0200	0.0000	0.2	SSE
10/26/2026 10:49	10.8	14.6	3.8	0.0227	0.0187	0.0000	0.2	S
10/26/2026 10:50	10.7	19.0	8.3	0.0227	0.0187	0.0000	0.2	S
10/26/2026 10:51	10.8	20.6	9.8	0.0227	0.0193	0.0000	0.2	S
10/26/2026 10:52	11.0	20.7	9.8	0.0227	0.0193	0.0000	0.2	N
10/26/2026 10:53	11.1	20.8	9.7	0.0220	0.0193	0.0000	0.1	ENE
10/26/2026 10:54	11.1	20.1	9.0	0.0213	0.0193	0.0000	0.1	WNW
10/26/2026 10:55	10.6	19.9	9.3	0.0213	0.0193	0.0000	0.1	SE
10/26/2026 10:56	10.5	22.9	12.4	0.0213	0.0193	0.0000	0.1	SSE
10/26/2026 10:57	10.5	24.2	13.7	0.0213	0.0193	0.0000	0.2	SSE
10/26/2026 10:58	10.3	25.5	15.2	0.0213	0.0193	0.0000	0.1	NE
10/26/2026 10:59	10.2	28.9	18.7	0.0207	0.0200	0.0000	0.1	SSE
10/26/2026 11:00	10.2	31.4	21.2	0.0200	0.0207	0.0007	0.2	S
10/26/2026 11:01	8.8	32.9	24.1	0.0200	0.0213	0.0013	0.3	SSE
10/26/2026 11:02	8.6	33.4	24.9	0.0200	0.0220	0.0020	0.3	SSE
10/26/2026 11:03	9.6	33.4	23.7	0.0207	0.0227	0.0020	0.3	SSW
10/26/2026 11:04	10.6	31.3	20.7	0.0213	0.0233	0.0020	0.3	SSW
10/26/2026 11:05	11.6	26.8	15.2	0.0220	0.0233	0.0013	0.3	N
10/26/2026 11:06	11.4	26.3	14.9	0.0220	0.0233	0.0013	0.3	S
10/26/2026 11:07	11.1	26.1	15.0	0.0220	0.0227	0.0007	0.3	SSE
10/26/2026 11:08	10.9	25.4	14.6	0.0220	0.0220	0.0000	0.4	ENE
10/26/2026 11:09	10.6	25.3	14.7	0.0220	0.0213	0.0000	0.4	SSE
10/26/2026 11:10	10.4	25.0	14.6	0.0213	0.0213	0.0000	0.4	SW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 11:11	10.2	21.2	11.0	0.0213	0.0207	0.0000	0.3	NE
10/26/2026 11:12	10.0	17.7	7.7	0.0213	0.0200	0.0000	0.3	S
10/26/2026 11:13	9.7	16.3	6.6	0.0213	0.0193	0.0000	0.3	ENE
10/26/2026 11:14	9.5	12.7	3.3	0.0213	0.0180	0.0000	0.3	E
10/26/2026 11:15	9.3	10.2	0.9	0.0213	0.0167	0.0000	0.3	E
10/26/2026 11:16	9.1	8.9	0.0	0.0213	0.0153	0.0000	0.3	E
10/26/2026 11:17	8.9	8.0	0.0	0.0213	0.0140	0.0000	0.2	ENE
10/26/2026 11:18	7.8	8.0	0.3	0.0207	0.0133	0.0000	0.2	NNE
10/26/2026 11:19	6.6	8.1	1.5	0.0200	0.0133	0.0000	0.2	ENE
10/26/2026 11:20	5.5	8.2	2.8	0.0193	0.0133	0.0000	0.2	ENE
10/26/2026 11:21	5.7	7.1	1.4	0.0193	0.0127	0.0000	0.2	ESE
10/26/2026 11:22	5.8	7.1	1.3	0.0187	0.0133	0.0000	0.2	NW
10/26/2026 11:23	5.8	7.3	1.5	0.0187	0.0133	0.0000	0.2	ESE
10/26/2026 11:24	5.9	7.4	1.6	0.0187	0.0133	0.0000	0.2	SSE
10/26/2026 11:25	5.9	7.6	1.7	0.0193	0.0127	0.0000	0.3	SSE
10/26/2026 11:26	6.0	7.6	1.6	0.0193	0.0127	0.0000	0.3	SSE
10/26/2026 11:27	6.0	7.6	1.5	0.0193	0.0133	0.0000	0.3	SSE
10/26/2026 11:28	6.1	7.7	1.6	0.0193	0.0140	0.0000	0.3	SSE
10/26/2026 11:29	6.1	7.8	1.6	0.0193	0.0147	0.0000	0.3	SSW
10/26/2026 11:30	6.2	7.7	1.5	0.0187	0.0153	0.0000	0.3	W
10/26/2026 11:31	6.2	7.5	1.2	0.0173	0.0160	0.0000	0.2	NNW
10/26/2026 11:32	6.3	7.2	1.0	0.0160	0.0167	0.0007	0.2	NW
10/26/2026 11:33	6.3	7.1	0.8	0.0147	0.0173	0.0027	0.2	SSW
10/26/2026 11:34	6.3	7.0	0.7	0.0147	0.0160	0.0013	0.3	SSE
10/26/2026 11:35	6.3	7.0	0.7	0.0147	0.0147	0.0000	0.3	S
10/26/2026 11:36	6.1	7.0	0.9	0.0147	0.0140	0.0000	0.3	SSE
10/26/2026 11:37	6.1	7.1	1.0	0.0153	0.0133	0.0000	0.3	SE
10/26/2026 11:38	6.1	6.9	0.8	0.0147	0.0140	0.0000	0.3	SW
10/26/2026 11:39	6.1	6.7	0.6	0.0140	0.0147	0.0007	0.3	W
10/26/2026 11:40	6.1	6.7	0.6	0.0133	0.0153	0.0020	0.2	WSW
10/26/2026 11:41	6.1	6.7	0.5	0.0127	0.0160	0.0033	0.2	SSW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 11:42	6.2	6.7	0.5	0.0127	0.0153	0.0027	0.2	S
10/26/2026 11:43	6.2	6.7	0.4	0.0127	0.0147	0.0020	0.2	S
10/26/2026 11:44	6.3	6.6	0.3	0.0127	0.0147	0.0020	0.2	SW
10/26/2026 11:45	6.3	6.7	0.3	0.0127	0.0147	0.0020	0.2	NW
10/26/2026 11:46	6.5	6.7	0.3	0.0140	0.0133	0.0000	0.2	S
10/26/2026 11:47	6.5	6.7	0.2	0.0153	0.0120	0.0000	0.2	SSE
10/26/2026 11:48	6.6	6.8	0.2	0.0167	0.0113	0.0000	0.2	SSE
10/26/2026 11:49	6.7	6.9	0.3	0.0167	0.0120	0.0000	0.2	SSE
10/26/2026 11:50	6.8	7.0	0.2	0.0167	0.0127	0.0000	0.2	SSE
10/26/2026 11:51	6.9	7.0	0.1	0.0167	0.0127	0.0000	0.3	SSE
10/26/2026 11:52	7.0	7.2	0.1	0.0167	0.0127	0.0000	0.3	SE
10/26/2026 11:53	7.1	7.2	0.1	0.0167	0.0127	0.0000	0.2	NNW
10/26/2026 11:54	7.2	7.4	0.2	0.0173	0.0120	0.0000	0.3	SSE
10/26/2026 11:55	7.3	7.5	0.2	0.0180	0.0113	0.0000	0.3	SE
10/26/2026 11:56	7.4	7.6	0.2	0.0187	0.0107	0.0000	0.3	SSE
10/26/2026 11:57	7.4	7.7	0.2	0.0187	0.0107	0.0000	0.3	ENE
10/26/2026 11:58	7.5	7.9	0.4	0.0187	0.0107	0.0000	0.3	S
10/26/2026 11:59	7.5	8.5	1.1	0.0187	0.0100	0.0000	0.4	S
10/26/2026 12:00	7.6	8.9	1.3	0.0193	0.0100	0.0000	0.4	E
10/26/2026 12:01	7.5	9.1	1.6	0.0193	0.0113	0.0000	0.4	SSE
10/26/2026 12:02	7.4	9.3	1.9	0.0193	0.0127	0.0000	0.4	E
10/26/2026 12:03	7.3	9.2	1.9	0.0193	0.0127	0.0000	0.4	E
10/26/2026 12:04	7.2	9.1	1.9	0.0180	0.0133	0.0000	0.4	SW
10/26/2026 12:05	7.2	9.0	1.8	0.0180	0.0127	0.0000	0.4	S
10/26/2026 12:06	7.1	9.0	1.9	0.0180	0.0120	0.0000	0.4	E
10/26/2026 12:07	7.0	8.8	1.8	0.0180	0.0113	0.0000	0.3	S
10/26/2026 12:08	6.9	8.7	1.9	0.0173	0.0113	0.0000	0.3	WNW
10/26/2026 12:09	7.0	8.6	1.6	0.0173	0.0107	0.0000	0.3	S
10/26/2026 12:10	6.9	8.9	2.1	0.0173	0.0107	0.0000	0.4	SSE
10/26/2026 12:11	6.8	9.1	2.4	0.0173	0.0107	0.0000	0.4	ESE
10/26/2026 12:12	6.7	9.0	2.3	0.0173	0.0100	0.0000	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 12:13	6.7	8.7	2.1	0.0173	0.0093	0.0000	0.4	ESE
10/26/2026 12:14	6.6	8.1	1.5	0.0173	0.0087	0.0000	0.4	ESE
10/26/2026 12:15	6.6	8.0	1.4	0.0173	0.0080	0.0000	0.4	SSE
10/26/2026 12:16	6.6	7.9	1.3	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:17	6.6	8.1	1.4	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:18	6.6	8.3	1.7	0.0173	0.0073	0.0000	0.4	SE
10/26/2026 12:19	6.6	8.6	2.0	0.0187	0.0067	0.0000	0.4	SSE
10/26/2026 12:20	6.6	8.8	2.2	0.0180	0.0073	0.0000	0.4	E
10/26/2026 12:21	6.5	8.8	2.3	0.0173	0.0080	0.0000	0.4	S
10/26/2026 12:22	6.5	9.0	2.5	0.0167	0.0087	0.0000	0.5	SE
10/26/2026 12:23	6.4	9.3	2.8	0.0173	0.0080	0.0000	0.5	ESE
10/26/2026 12:24	6.2	9.4	3.1	0.0167	0.0087	0.0000	0.5	SSE
10/26/2026 12:25	6.2	9.2	3.0	0.0160	0.0087	0.0000	0.5	SE
10/26/2026 12:26	6.3	8.9	2.6	0.0153	0.0087	0.0000	0.4	N
10/26/2026 12:27	6.3	8.8	2.6	0.0147	0.0093	0.0000	0.4	ESE
10/26/2026 12:28	6.3	8.9	2.6	0.0147	0.0100	0.0000	0.4	E
10/26/2026 12:29	6.3	8.9	2.6	0.0133	0.0113	0.0000	0.4	WSW
10/26/2026 12:30	6.3	8.6	2.3	0.0133	0.0107	0.0000	0.4	S
10/26/2026 12:31	6.2	8.5	2.3	0.0133	0.0100	0.0000	0.4	S
10/26/2026 12:32	6.2	8.1	1.9	0.0133	0.0087	0.0000	0.4	S
10/26/2026 12:33	6.2	8.0	1.9	0.0133	0.0080	0.0000	0.4	S
10/26/2026 12:34	6.2	8.0	1.8	0.0133	0.0073	0.0000	0.4	S
10/26/2026 12:35	6.2	8.3	2.1	0.0140	0.0073	0.0000	0.4	SE
10/26/2026 12:36	6.4	8.2	1.8	0.0140	0.0080	0.0000	0.4	SW
10/26/2026 12:37	6.5	7.9	1.5	0.0147	0.0073	0.0000	0.4	SSE
10/26/2026 12:38	6.6	7.6	1.1	0.0153	0.0067	0.0000	0.4	SE
10/26/2026 12:39	6.6	7.4	0.9	0.0160	0.0060	0.0000	0.3	SSW
10/26/2026 12:40	6.5	7.1	0.5	0.0167	0.0053	0.0000	0.3	NE
10/26/2026 12:41	6.3	7.1	0.8	0.0160	0.0060	0.0000	0.3	SSW
10/26/2026 12:42	6.3	7.1	0.8	0.0167	0.0053	0.0000	0.3	S
10/26/2026 12:43	6.3	7.3	1.0	0.0167	0.0047	0.0000	0.4	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 12:44	6.3	7.6	1.3	0.0180	0.0033	0.0000	0.4	SE
10/26/2026 12:45	6.2	7.8	1.5	0.0173	0.0040	0.0000	0.4	E
10/26/2026 12:46	6.3	7.8	1.5	0.0167	0.0047	0.0000	0.4	SSE
10/26/2026 12:47	6.2	8.8	2.5	0.0167	0.0053	0.0000	0.4	SSE
10/26/2026 12:48	6.9	8.8	1.8	0.0160	0.0067	0.0000	0.4	NW
10/26/2026 12:49	6.9	8.5	1.5	0.0160	0.0067	0.0000	0.4	E
10/26/2026 12:50	6.9	8.0	1.0	0.0160	0.0060	0.0000	0.3	S
10/26/2026 12:51	6.6	8.5	1.9	0.0160	0.0047	0.0000	0.4	SSE
10/26/2026 12:52	6.5	9.2	2.7	0.0153	0.0053	0.0000	0.4	ESE
10/26/2026 12:53	6.6	9.3	2.7	0.0147	0.0060	0.0000	0.4	SE
10/26/2026 12:54	6.8	9.5	2.8	0.0140	0.0060	0.0000	0.4	SE
10/26/2026 12:55	7.0	9.6	2.6	0.0127	0.0067	0.0000	0.4	W
10/26/2026 12:56	7.0	9.6	2.6	0.0140	0.0053	0.0000	0.4	ENE
10/26/2026 12:57	7.0	9.8	2.8	0.0140	0.0053	0.0000	0.4	ENE
10/26/2026 12:58	6.9	10.5	3.5	0.0140	0.0053	0.0000	0.3	NNE
10/26/2026 12:59	7.2	10.0	2.7	0.0127	0.0067	0.0000	0.2	NNW
10/26/2026 13:00	7.2	9.7	2.5	0.0120	0.0073	0.0000	0.2	NNW
10/26/2026 13:01	7.2	9.6	2.3	0.0113	0.0080	0.0000	0.2	SSW
10/26/2026 13:02	7.2	8.6	1.3	0.0107	0.0073	0.0000	0.2	SE
10/26/2026 13:03	6.5	8.5	2.0	0.0107	0.0060	0.0000	0.2	ESE
10/26/2026 13:04	6.4	8.5	2.1	0.0107	0.0060	0.0000	0.2	SE
10/26/2026 13:05	6.5	8.5	2.0	0.0093	0.0073	0.0000	0.2	N
10/26/2026 13:06	6.5	7.9	1.5	0.0100	0.0073	0.0000	0.2	S
10/26/2026 13:07	6.5	7.4	0.9	0.0107	0.0067	0.0000	0.2	ESE
10/26/2026 13:08	6.2	7.4	1.1	0.0113	0.0060	0.0000	0.2	NE
10/26/2026 13:09	6.0	7.1	1.1	0.0120	0.0060	0.0000	0.2	ESE
10/26/2026 13:10	5.7	7.0	1.3	0.0120	0.0067	0.0000	0.2	NNW
10/26/2026 13:11	5.6	6.8	1.2	0.0107	0.0080	0.0000	0.2	NNW
10/26/2026 13:12	5.5	6.6	1.1	0.0107	0.0080	0.0000	0.2	NE
10/26/2026 13:13	5.5	5.5	0.0	0.0107	0.0080	0.0000	0.2	SE
10/26/2026 13:14	5.1	5.6	0.6	0.0107	0.0073	0.0000	0.2	N

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 13:15	5.1	5.7	0.6	0.0120	0.0060	0.0000	0.2	S
10/26/2026 13:16	5.0	5.8	0.8	0.0133	0.0047	0.0000	0.2	S
10/26/2026 13:17	5.0	5.8	0.7	0.0140	0.0047	0.0000	0.2	NNE
10/26/2026 13:18	5.1	5.5	0.5	0.0147	0.0047	0.0000	0.2	SSE
10/26/2026 13:19	5.2	5.5	0.3	0.0153	0.0047	0.0000	0.2	SSE
10/26/2026 13:20	5.0	5.8	0.8	0.0167	0.0033	0.0000	0.2	ESE
10/26/2026 13:21	5.1	6.0	0.9	0.0160	0.0033	0.0000	0.2	ESE
10/26/2026 13:22	5.1	6.2	1.0	0.0153	0.0033	0.0000	0.3	SE
10/26/2026 13:23	5.3	6.1	0.8	0.0140	0.0040	0.0000	0.2	NW
10/26/2026 13:24	5.4	6.1	0.7	0.0133	0.0040	0.0000	0.2	ESE
10/26/2026 13:25	5.6	6.3	0.7	0.0140	0.0027	0.0000	0.3	SE
10/26/2026 13:26	5.7	6.4	0.8	0.0147	0.0013	0.0000	0.4	SE
10/26/2026 13:27	5.8	6.5	0.7	0.0147	0.0013	0.0000	0.4	SE
10/26/2026 13:28	5.9	6.5	0.6	0.0140	0.0013	0.0000	0.4	E
10/26/2026 13:29	6.0	6.4	0.4	0.0147	0.0007	0.0000	0.5	SSE
10/26/2026 13:30	6.0	6.4	0.4	0.0140	0.0007	0.0000	0.5	ESE
10/26/2026 13:31	6.1	6.3	0.2	0.0133	0.0007	0.0000	0.5	ENE
10/26/2026 13:32	6.1	6.4	0.2	0.0127	0.0007	0.0000	0.5	E
10/26/2026 13:33	6.2	6.4	0.2	0.0120	0.0007	0.0000	0.5	SSE
10/26/2026 13:34	6.2	6.3	0.1	0.0107	0.0007	0.0000	0.5	ESE
10/26/2026 13:35	6.3	5.9	0.0	0.0100	0.0007	0.0000	0.5	NNE
10/26/2026 13:36	6.3	5.6	0.0	0.0107	0.0007	0.0000	0.4	SSE
10/26/2026 13:37	6.3	5.6	0.0	0.0100	0.0020	0.0000	0.4	SW
10/26/2026 13:38	7.0	5.6	0.0	0.0113	0.0013	0.0000	0.4	SSW
10/26/2026 13:39	7.0	5.6	0.0	0.0113	0.0013	0.0000	0.4	SE
10/26/2026 13:40	7.0	5.4	0.0	0.0113	0.0013	0.0000	0.4	E
10/26/2026 13:41	7.1	5.4	0.0	0.0113	0.0013	0.0000	0.4	SE
10/26/2026 13:42	7.0	5.4	0.0	0.0113	0.0013	0.0000	0.4	S
10/26/2026 13:43	7.0	5.8	0.0	0.0120	0.0013	0.0000	0.4	ESE
10/26/2026 13:44	7.0	5.9	0.0	0.0120	0.0013	0.0000	0.4	S
10/26/2026 13:45	7.1	6.0	0.0	0.0120	0.0013	0.0000	0.3	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 13:46	7.0	5.9	0.0	0.0120	0.0013	0.0000	0.4	SE
10/26/2026 13:47	6.9	5.8	0.0	0.0120	0.0013	0.0000	0.4	SE
10/26/2026 13:48	6.9	5.9	0.0	0.0120	0.0013	0.0000	0.4	S
10/26/2026 13:49	6.8	6.0	0.0	0.0120	0.0013	0.0000	0.4	SSE
10/26/2026 13:50	6.7	6.0	0.0	0.0113	0.0020	0.0000	0.5	WSW
10/26/2026 13:51	6.7	6.1	0.0	0.0107	0.0020	0.0000	0.5	ESE
10/26/2026 13:52	6.7	5.7	0.0	0.0113	0.0007	0.0000	0.5	SSE
10/26/2026 13:53	5.8	5.6	0.0	0.0107	0.0007	0.0000	0.5	ESE
10/26/2026 13:54	5.7	5.6	0.0	0.0107	0.0007	0.0000	0.5	SE
10/26/2026 13:55	5.6	5.6	0.0	0.0107	0.0007	0.0000	0.5	SE
10/26/2026 13:56	5.5	5.5	0.0	0.0107	0.0007	0.0000	0.5	SSE
10/26/2026 13:57	5.4	5.5	0.1	0.0093	0.0013	0.0000	0.4	NW
10/26/2026 13:58	5.3	5.0	0.0	0.0087	0.0013	0.0000	0.4	S
10/26/2026 13:59	5.3	5.0	0.0	0.0087	0.0013	0.0000	0.4	SE
10/26/2026 14:00	5.2	4.7	0.0	0.0087	0.0013	0.0000	0.4	S
10/26/2026 14:01	5.1	4.7	0.0	0.0080	0.0020	0.0000	0.4	NW
10/26/2026 14:02	5.1	4.7	0.0	0.0087	0.0020	0.0000	0.3	SSE
10/26/2026 14:03	5.1	4.7	0.0	0.0093	0.0020	0.0000	0.3	S
10/26/2026 14:04	5.2	4.6	0.0	0.0100	0.0020	0.0000	0.3	SSE
10/26/2026 14:05	5.4	4.5	0.0	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:06	5.4	5.5	0.1	0.0113	0.0013	0.0000	0.3	SE
10/26/2026 14:07	5.4	5.8	0.5	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:08	5.4	6.2	0.8	0.0113	0.0013	0.0000	0.3	SSE
10/26/2026 14:09	5.4	6.4	1.0	0.0113	0.0013	0.0000	0.4	SSE
10/26/2026 14:10	5.5	6.4	1.0	0.0113	0.0013	0.0000	0.4	SSE
10/26/2026 14:11	5.4	6.4	1.0	0.0113	0.0013	0.0000	0.4	S
10/26/2026 14:12	5.4	6.4	0.9	0.0113	0.0013	0.0000	0.5	SW
10/26/2026 14:13	5.4	7.0	1.6	0.0113	0.0013	0.0000	0.5	S
10/26/2026 14:14	5.3	7.3	2.0	0.0113	0.0013	0.0000	0.5	S
10/26/2026 14:15	5.4	7.4	1.9	0.0113	0.0013	0.0000	0.6	SE
10/26/2026 14:16	5.5	7.3	1.8	0.0120	0.0007	0.0000	0.7	SSW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 14:17	5.5	7.4	1.9	0.0113	0.0007	0.0000	0.7	SSE
10/26/2026 14:18	5.4	7.6	2.2	0.0107	0.0007	0.0000	0.8	SE
10/26/2026 14:19	5.4	7.7	2.3	0.0093	0.0013	0.0000	0.8	SW
10/26/2026 14:20	5.3	7.7	2.4	0.0080	0.0020	0.0000	0.7	WSW
10/26/2026 14:21	5.3	6.9	1.6	0.0080	0.0020	0.0000	0.7	SE
10/26/2026 14:22	5.3	6.6	1.4	0.0080	0.0020	0.0000	0.7	SSE
10/26/2026 14:23	5.3	6.6	1.3	0.0080	0.0020	0.0000	0.7	SSE
10/26/2026 14:24	5.3	6.4	1.1	0.0073	0.0027	0.0000	0.6	W
10/26/2026 14:25	5.1	6.4	1.3	0.0067	0.0033	0.0000	0.6	SW
10/26/2026 14:26	5.2	6.5	1.4	0.0067	0.0033	0.0000	0.5	NNE
10/26/2026 14:27	5.5	6.5	1.1	0.0067	0.0040	0.0000	0.4	N
10/26/2026 14:28	5.9	35.7	29.8	0.0067	0.0040	0.0000	0.3	ENE
10/26/2026 14:29	6.2	91.6	85.4	0.0073	0.0040	0.0000	0.3	ESE
10/26/2026 14:30	6.2	99.2	93.1	0.0073	0.0040	0.0000	0.3	SE
10/26/2026 14:31	6.3	108.9	102.6	0.0073	0.0040	0.0000	0.3	SSE
10/26/2026 14:32	6.4	111.8	105.5	0.0073	0.0047	0.0000	0.3	SE
10/26/2026 14:33	6.3	113.3	106.9	0.0073	0.0053	0.0000	0.3	S
10/26/2026 14:34	8.9	113.2	104.4	0.0080	0.0053	0.0000	0.3	SW
10/26/2026 14:35	8.8	117.8	109.0	0.0087	0.0053	0.0000	0.4	SE
10/26/2026 14:36	8.8	152.9	144.1	0.0087	0.0060	0.0000	0.4	SSE
10/26/2026 14:37	8.9	283.2	274.3	0.0087	0.0060	0.0000	0.4	ESE
10/26/2026 14:38	9.4	382.6	373.2	0.0087	0.0060	0.0000	0.4	SSE
10/26/2026 14:39	10.2	438.2	428.1	0.0093	0.0060	0.0000	0.4	SE
10/26/2026 14:40	11.0	452.7	441.7	0.0100	0.0067	0.0000	0.5	S
10/26/2026 14:41	11.2	476.6	465.4	0.0100	0.0080	0.0000	0.5	ESE
10/26/2026 14:42	11.0	484.8	473.8	0.0107	0.0073	0.0000	0.6	ESE
10/26/2026 14:43	10.6	464.6	454.0	0.0107	0.0073	0.0000	0.7	ESE
10/26/2026 14:44	10.4	415.3	404.8	0.0100	0.0073	0.0000	0.7	SE
10/26/2026 14:45	10.5	424.7	414.2	0.0100	0.0073	0.0000	0.8	SE
10/26/2026 14:46	10.5	421.8	411.3	0.0100	0.0073	0.0000	1.0	SE
10/26/2026 14:47	10.4	422.6	412.2	0.0100	0.0067	0.0000	1.1	SE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 14:48	10.6	423.5	413.0	0.0100	0.0060	0.0000	1.1	SE
10/26/2026 14:49	8.0	425.5	417.5	0.0100	0.0053	0.0000	1.3	SE
10/26/2026 14:50	8.0	422.3	414.3	0.0100	0.0047	0.0000	1.3	SE
10/26/2026 14:51	8.0	388.3	380.3	0.0100	0.0040	0.0000	1.3	SE
10/26/2026 14:52	7.9	258.5	250.6	0.0100	0.0040	0.0000	1.3	SE
10/26/2026 14:53	7.3	159.4	152.1	0.0100	0.0040	0.0000	1.3	NNE
10/26/2026 14:54	6.6	104.1	97.5	0.0100	0.0033	0.0000	1.3	SE
10/26/2026 14:55	5.9	89.9	84.0	0.0100	0.0020	0.0000	1.4	SE
10/26/2026 14:56	5.7	66.3	60.6	0.0100	0.0007	0.0000	1.4	ESE
10/26/2026 14:57	5.6	58.5	52.8	0.0100	0.0000	0.0000	1.4	ESE
10/26/2026 14:58	5.5	49.2	43.7	0.0100	0.0000	0.0000	1.5	SE
10/26/2026 14:59	5.4	42.7	37.3	0.0100	0.0000	0.0000	1.5	E
10/26/2026 15:00	5.3	25.9	20.6	0.0100	0.0000	0.0000	1.3	NNE
10/26/2026 15:01	5.2	19.3	14.1	0.0100	0.0000	0.0000	1.1	E
10/26/2026 15:02	5.1	15.8	10.7	0.0100	0.0000	0.0000	1.0	NE
10/26/2026 15:03	4.9	13.5	8.6	0.0100	0.0000	0.0000	1.0	NE
10/26/2026 15:04	4.7	11.6	6.9	0.0100	0.0000	0.0000	0.9	NE
10/26/2026 15:05	4.7	10.3	5.6	0.0100	0.0000	0.0000	0.8	NE
10/26/2026 15:06	4.7	9.4	4.6	0.0100	0.0000	0.0000	0.9	NNE
10/26/2026 15:07	4.7	8.8	4.1	0.0107	0.0000	0.0000	0.9	NNE
10/26/2026 15:08	4.7	8.3	3.6	0.0113	0.0000	0.0000	0.9	E
10/26/2026 15:09	4.6	8.0	3.3	0.0120	0.0000	0.0000	0.9	E
10/26/2026 15:10	4.6	7.8	3.1	0.0127	0.0000	0.0000	0.9	E
10/26/2026 15:11	4.7	7.5	2.8	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:12	4.6	7.0	2.4	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:13	4.6	6.6	2.0	0.0127	0.0000	0.0000	0.9	ESE
10/26/2026 15:14	4.6	6.4	1.7	0.0127	0.0000	0.0000	1.0	NE
10/26/2026 15:15	4.7	6.2	1.5	0.0120	0.0007	0.0000	0.9	N
10/26/2026 15:16	4.7	5.9	1.2	0.0120	0.0007	0.0000	1.0	E
10/26/2026 15:17	4.7	5.6	0.8	0.0120	0.0007	0.0000	0.9	NNE
10/26/2026 15:18	4.7	5.2	0.5	0.0127	0.0007	0.0000	0.8	E

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
10/26/2026 15:19	4.8	5.0	0.2	0.0127	0.0007	0.0000	0.8	E
10/26/2026 15:20	4.8	4.8	0.0	0.0127	0.0007	0.0000	0.9	SE
10/26/2026 15:21	4.7	4.5	0.0	0.0127	0.0007	0.0000	0.9	SE
10/26/2026 15:22	4.7	4.3	0.0	0.0120	0.0007	0.0000	1.0	ESE
10/26/2026 15:23	4.7	4.2	0.0	0.0113	0.0007	0.0000	1.0	E
