SITE OBSERVATION REPORT – RAWP Implementation – Day 67

LANGAN

PROJECT No.:	170390001	**CLIENT:**		**DATE:**	Tuesday, May 6, 2025
PROJECT:	141 3rd Street			**WEATHER:**	Rain, 54-63 ^{0}F Wind: SSW @ 0.5 – 3.3 mph
LOCATION:	Brooklyn, New York	Third Street Owner LLC and 155 Third St., LLC		**TIME:**	6:45 a.m. – 3:45 p.m.
BCP SITE ID:	C224336			**MONITOR:**	Gabriella DeGennaro

EQUIPMENT:
Hyundai HX520L Excavator
Komatsu PC490LC Excavator
LB46-410 Drilling Rig
LRB- 355.1 Drilling Rig
CME LC45 Rotary Drill Rig
MiniRae 3000

PRESENT AT SITE:
Langan: Gabriella DeGennaro, Kiki Wallick
Monadnock Construction (Construction Management): John Henry
New Leaf (Development/Drilling Contractor): Joe Sullivan
NYSDEC: Aaron Fischer
WSP: Chris DeSclafani
Roux, Inc.: James Smyth
Aquifer Drilling & Testing, Inc. (ADT): Christopher Peters

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:

Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2024, and Remedial Design Document (RDD) for In-Situ Stabilization/Solidification (ISS) dated 5 April 2024.

Remedial Action Work Summary:

Work Activities Performed Onsite

- NYSDEC conducted a site visit. No adverse conditions were noted as a result of the site visit and no further action was required.

ISS Work Performed Onsite

- ADT used a CME LC45 rotary drill rig to advance core locations ISS-C4-R1 and ISS-C4-R2 (representative of previously mixed cells ISS-19, ISS-23, and ISS-24) to about 15 feet below grade surface (bgs) (el. -8.18±) and 20 feet bgs (el. -13.21±), respectively. Cores and drilling equipment were inspected for visible non-aqueous phase liquid (NAPL), percent of core sample recovered, and NAPL coating on drilling tools.
    - **ISS-C4-R1**: Low recovery (about 5% of the total rock core) was observed from about 0 to 15 feet bgs (el. 6.82± and -8.18±).
    - **ISS-C4-R2**: Low recovery (about 64% of the total core) was observed from about 0 to 15 feet bgs (el. 6.79± and -13.21±).
    - No impacts were observed.
    - The cores demonstrated a homogenous mix in ISS cells.
    - Following completion of cores, each location was tremie-grouted from the base of the core to surface grade.
    - ISS cores were retained on site in wood core boxes and will be maintained on site through the remediation.

  Another core representing the ISS-C4 location will be re-advanced at a later date once the monolith has had additional time to cure.

Sampling

- No samples were collected.

Community Air Monitoring Plan (CAMP) Activities

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on CAMP summary data sheet appended to the end of this Daily Field Report.

Material Tracking

- No material was exported from the site.
- No material was imported to site.

Material Import Summary				
Facility	**NYSDEC Approved Quantity**	**Imported**	**Today**	**Total**
Tilcon - Haverstraw Haverstraw, NY ASTM #3 Virgin Stone (1.5-Inch)	400 CY (560 tons)	**No. Loads**	0	**4**
		Quantity (tons)	0	**89.95**
Impact Materials Jersey City (IMJC) Jersey City, NJ 0.75-inch Stone	2,000 CY (2,800 tons)	**No. Loads**	0	**0**
		Quantity (tons)	0	**0**
IMJC Jersey City, NJ 1.5-inch Stone	400 CY (560 tons)	**No. Loads**	0	**2**
		Quantity (tons)	0	**49.65**

Material Export Summary				
Facility	**Approved Quantity**	**Imported**	**Today**	**Total**
Clean Earth of Carteret (CEC) Carteret, NJ Elevated Soil/Fill	9,857 CY (13,800 tons)	**No. Loads**	0	**62**
		Quantity (CY)	0	**1,240**
Clean Earth of New Castle (CENC) New Castle, DE Non-Hazardous Contaminated Soil/Urban Fill	3,571 CY (5,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Atlantic County Utilities Authority (ACUA) Egg Harbor Township, NJ Non-Hazardous Contaminated Soil/Urban Fill	714 CY (1,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Clean Earth of North Jersey (CENJ) Kearny, NJ Hazardous Lead	107 CY (150 tons)	**No. Loads**	0	**2**
		Quantity (CY)	0	**40**

Drums

- One 55-gallon drum containing purged groundwater and dense non-aqueous phase liquid (DNAPL) is staged in the southern part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- One 55-gallon drum containing purged groundwater is staged in the southern part of the site.

Anticipated Activities

- ADT will advance off-sets of the core locations.

SITE PHOTOGRAPHS:

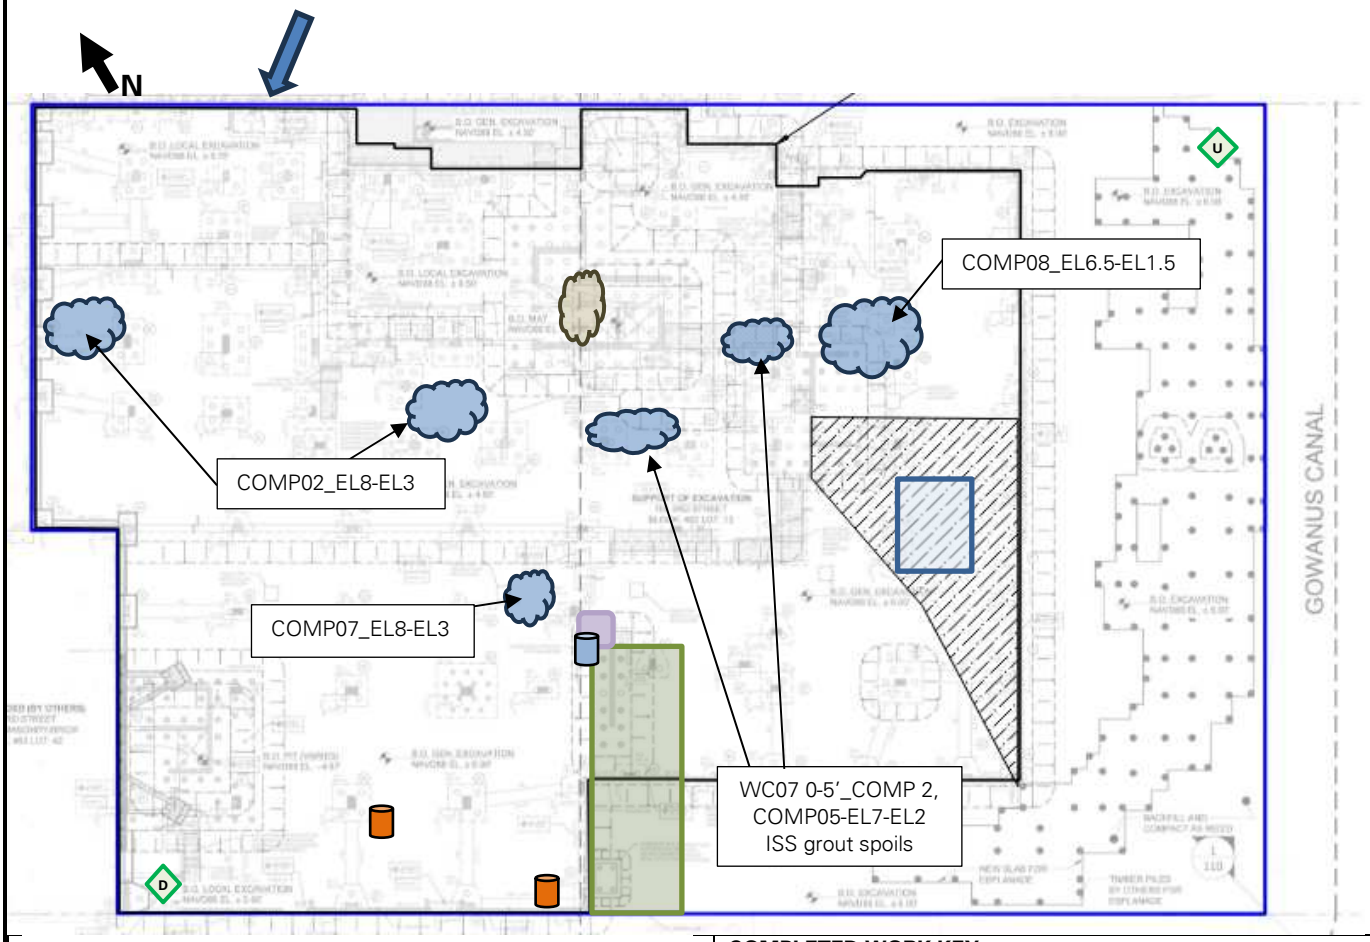


Photo 1: ADT advancing core location ISS-C4-R1 (facing west)



Photo 2: ADT advancing core location ISS-C4-R2 (facing west)

FIGURE 1 - SITE MAP:



LEGEND:

- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)


COMPLETED WORK KEY

- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin

Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024

FIGURE 2 - ISGS PROGRESS MAP

N

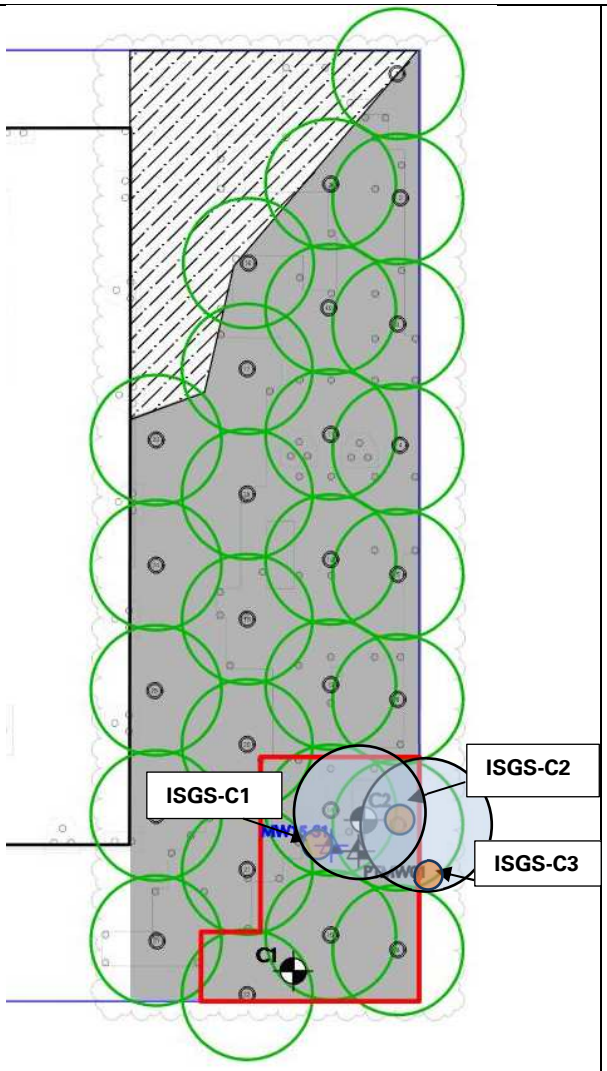

LEGEND:


- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISGS AREA BETWEEN EL. -19± TO EL. -23±
- APPROXIMATE PROPOSED EXTENT OF ISGS SUPPORT/LAYDOWN AREA
- APPROXIMATE PROPOSED TEMPORARY DIRECT-PUSH INJECTION POINT LOCATION
- APPROXIMATE ROI (13-FOOT RADIUS, 25-FOOT SPACING)
- C1 — APPROXIMATE PROPOSED PILOT TEST QA/QC CORE LOCATION
- APPROXIMATE ISGS PILOT TEST AREA
- MW15-S1 — EXISTING MONITORING WELL LOCATION
- PTWM01 — PROPOSED MONITORING WELL LOCATION

COMPLETED WORK KEY

- ISGS injection point completed today
- ISGS injection point previously completed
- Core location completed today
- Core location previously completed

Base map includes Figure 2 – Project Implementation Plan In-Situ Stabilization/Solidification, prepared by Roux Environmental and Geology, D.P.C, dated October 2024

FIGURE 3 - ISS PROGRESS MAP:

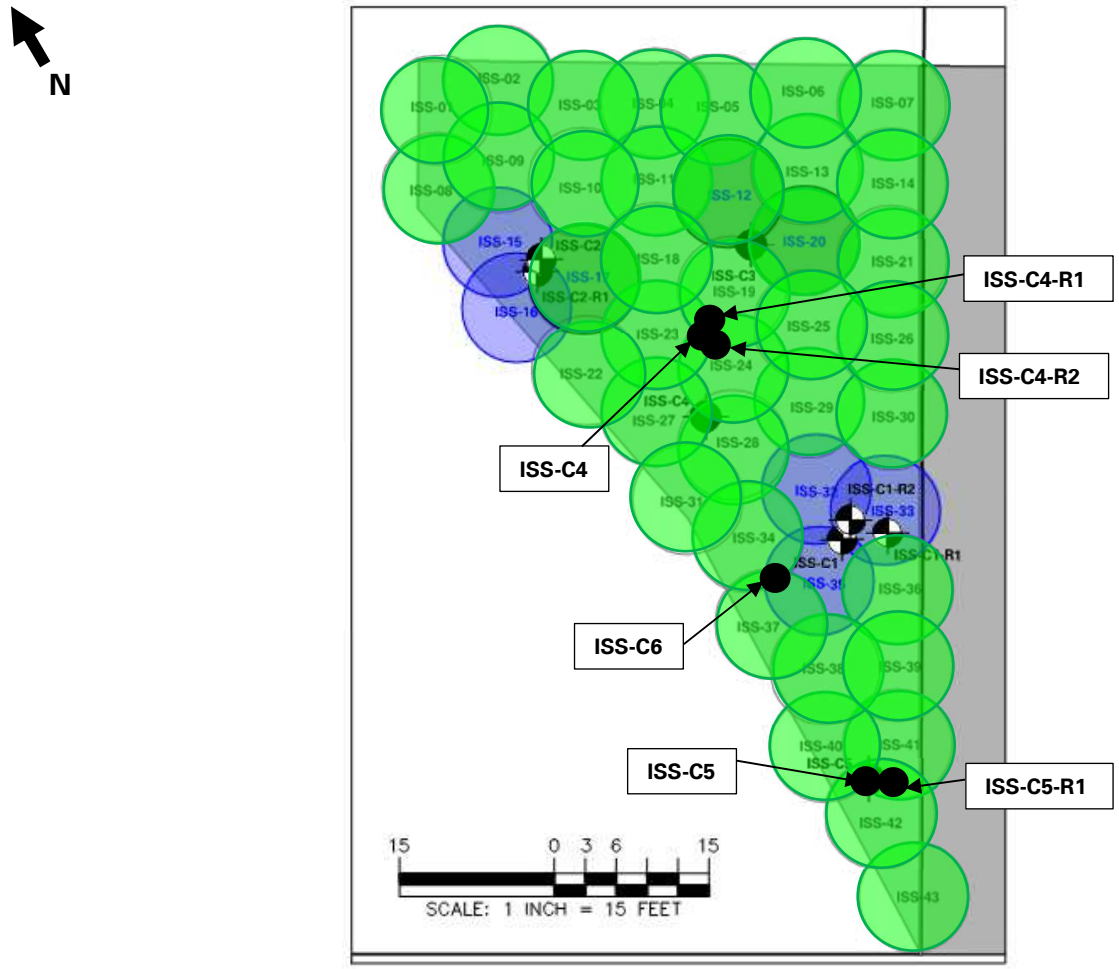

LEGEND:

- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE EXTENT OF ISS SUPPORT/LAYDOWN AREA
- APPROXIMATE EXTENT OF ISS IMPLEMENTATION AREA
- ISS-C1 APPROXIMATE COMPLETED CORE LOCATION
- ISS-C3 APPROXIMATE PROPOSED CORE LOCATION

COMPLETED WORK KEY

- Completed ISS Pilot Test Columns
- Columns to be re-mixed
- Completed Full-Scale ISS Columns
- ISS Columns mixed today
- Columns to be mixed tomorrow
- Collected core today
- Previously collected sample location

Base map includes Figure 2 – ISS Plan from the ISS Pilot Test Results Letter, prepared by Langan, dated March 5, 2025

LANGAN

TABLE 1 - ISS PROGRESS TABLE:

ISS Column ID	Coordinates (N, E)	Column Diameter (ft)	No. of Column Passes	Bottom Elevation of Column	Approximate Volume Treated (CY)	Mixing Time Per Interval (min/ft)	Reagent Additional Per Interval (kg)	Injection Pressure (psi)	Injection Rate (gal/min)	Rotational Speed (rpm)	Advance Rate (ft/min)	Sampled
Pilot Study												
ISS-20	98.87, 221.23	10.6	N/A	-26.5±	N/A	N/A	N/A	50	6.5	30	3.75	Yes
ISS-12	103.418, 213.788	10.6	N/A	-21.5±	N/A	N/A	N/A	N/A	N/A	15	1.4	Yes
ISS-16	92.59, 193.29	10.6	1	-26.5±	93	5	948.78	N/A	N/A	17	0.1	Yes
ISS-17	95.14, 199.81	10.6	1	-26.5±	105	10	841.75	N/A	N/A	18	0.19	Yes
ISS-15	98.75, 191.97	10.6	1	-26.5±	105	5	765.22	N/A	N/A	16	0.28	Yes
ISS-35	65.47, 222.59	10.6	2	-26.5±	101	7	871.43	N/A	N/A	16	0.36	Yes
ISS-32	74.47, 222.33	10.6	2	-26.5±	105	4	841.75	N/A	N/A	16	0.25	Yes
ISS-33	74.47, 229.01	10.6	2	-26.5±	105	11	765.22	N/A	N/A	16	0.17	Yes
Full-Scale Implementation												
ISS-01	110.99, 185.10	10.6	2	-26.5±	100	5.3*	800*	22*	21*	13*	0.2*	No
ISS-02	113.11, 190.95	10.6	2	-26.5±	109	4.3*	809*	24*	34*	14*	0.2*	No
ISS-03	112.32, 199.07	10.6	2	-26.5±	99	7.8*	886*	19*	37*	14*	0.1*	Yes
ISS-04	114.11, 206.99	10.6	2	-26.5±	109	9.1*	956*	21*	24*	13*	0.1*	No
ISS-05	111.93, 214.38	10.6	2	-26.5±	101	8.6*	874*	25*	21*	13*	0.1*	No
ISS-06	113.45, 221.56	10.6	2	-26.5±	102	8.0*	938*	22*	27*	13*	0.1*	Yes
ISS-07	111.72, 229.09	10.6	2	-26.5±	101	9.5*	1,027*	24*	22*	13*	0.1*	Yes
ISS-08	103.02, 187.19	10.6	2	-26.5±	100	5.6*	964*	22*	41*	13*	0.2*	No
ISS-09	107.17, 192.43	10.6	2	-26.5±	100	6.6*	964*	21*	24*	14*	0.2*	No
ISS-10	103.57, 199.17	10.6	2	-26.5±	100	5.8*	803*	21*	29*	14*	0.2*	No
ISS-11	107.82, 206.44	10.6	2	-26.5±	101	6.8*	869*	19*	27*	13*	0.2*	No
ISS-12	103.42, 213.80	10.6	2	-26.5±	100	9.1*	964*	21*	30*	14*	0.1*	No
ISS-13	106.26, 221.37	10.6	2	-26.5±	102	6.0*	861*	20*	28*	14*	0.2*	No
ISS-14	104.02, 228.87	10.6	2	-26.5±	100	9.8*	961*	19*	40*	13*	0.1*	No
ISS-17	95.14, 199.81	10.6	2	-26.5±	109	8.8*	877*	19*	28*	13*	0.1*	No
ISS-18	99.32, 206.56	10.6	2	-26.5±	101	5.9*	790*	25*	35*	13*	0.2*	No
ISS-19	94.57, 213.51	10.6	2	-26.5±	104	9.2*	1081*	20*	31*	13*	0.1*	Yes
ISS-20	98.37, 221.23	10.6	2	-26.5±	98	9.9*	1,221*	17*	28*	13*	0.1*	No
ISS-21	96.47, 229.17	10.6	2	-26.5±	100	6.0*	876*	18*	21*	13*	0.2*	No
ISS-22	86.23, 199.71	10.6	2	-26.5±	109	6.2*	804*	23*	27*	13*	0.2*	No
ISS-23	90.11, 206.59	10.6	2	-26.5±	100	5.7*	882*	23*	35*	14*	0.2*	No
ISS-24	86.32, 213.53	10.6	2	-26.5±	101	5.6*	875*	19*	35*	14*	0.2*	Yes
ISS-25	91.32, 221.3	10.6	2	-26.5±	110	6.6*	799*	17*	21*	12*	0.2*	No
ISS-26	88.63, 229.16	10.6	2	-26.5±	109	7.1*	807*	30*	28*	13*	0.1*	No
ISS-27	81.32, 206.11	10.6	2	-26.5±	109	6.6*	735*	24*	32*	13*	0.2*	Yes
ISS-28	78.50, 215.04	10.6	2	-26.5±	100	5.4*	880*	23*	37*	13*	0.3*	No
ISS-29	83.08, 221.62	10.6	2	-26.5±	100	5.5*	878*	21*	47*	13*	0.2*	No

ISS Column ID	Coordinates (N, E)	Column Diameter (ft)	No. of Column Passes	Bottom Elevation of Column	Approximate Volume Treated (CY)	Mixing Time Per Interval (min/ft)	Reagent Additional Per Interval (kg)	Injection Pressure (psi)	Injection Rate (gal/min)	Rotational Speed (rpm)	Advance Rate (ft/min)	Sampled
ISS-30	80.66, 229.01	10.6	2	-26.5±	101	5.5*	948*	19*	35*	13*	0.3*	No
ISS-31	73.77, 209.56	10.6	2	-26.5±	105	7.3*	842*	23*	30*	13*	0.2*	No
ISS-34	69.19, 215.20	10.6	2	-26.5±	104	5.9*	850*	17*	34*	14*	0.3*	No
ISS-36	64.95, 229.19	10.6	2	-26.5±	102	6.8*	782*	24*	27*	13*	0.3*	No
ISS-37	61.04, 216.20	10.6	2	-26.5±	105	6.2*	837*	25*	33*	13*	0.3*	No
ISS-38	56.31, 222.47	10.6	2	-26.5±	105	6.0*	759*	19.3*	32*	14*	0.3*	No
ISS-39	57.46, 228.81	10.6	2	-26.5±	103	5.7*	853*	16*	33*	13*	0.3*	No
ISS-40	49. 31, 222.87	10.6	2	-26.5±	104	5.5*	848*	28*	33*	13*	0.4*	Yes
ISS-41	49.74, 229.96	10.6	2	-26.5±	99	8.1*	890*	19*	30*	13*	0.2*	Yes
ISS-42	42.22, 228.29	10.6	2	-26.5±	103	5.4*	851*	16.4*	31*	13*	0.3*	No
ISS-43	35.19, 230.66	10.6	2	-26.5±	102	8.1*	781.47*	8*	45*	14*	0.3*	No

1. Coordinates were measured in northing and eastings from the project datum.
2. * = Estimated parameters based on field observations. Exact parameters will be updated (as needed) once received.

LANGAN

TABLE 2 - ISS QC RESULTS TABLE

ISS Cell	Sample Depth (elevation)	7-day		14-day		21-day		28-day		56-day	
		UCS (psi)	HC (cm/sec)	UCS (psi)	HC (cm/sec)	UCS (psi)	HC (cm/sec)	UCS (psi)	HC (cm/sec)	UCS (psi)	HC (cm/sec)
Pilot Study											
ISS-15	-18.5± to -20.5±	40	1.3×10^{-6}	**80**	**8.6×10^{-7}**	**90**	**4.6×10^{-7}**	**90**	**4.7×10^{-7}**	**100**	**4.2×10^{-7}**
ISS-16	-18.5± to -20.5±	30	3.6×10^{-6}	**50**	1.1×10^{-6}	**60**	**9.8×10^{-7}**	**70**	**7.4×10^{-7}**	**70**	**7.2×10^{-7}**
ISS-17	-18.5± to -20.5±	20	1.6×10^{-6}	30	3.0×10^{-6}	40	2.8×10^{-6}	**50**	2.7×10^{-6}	**60**	2.6×10^{-6}
ISS-32	-18.5± to -20.5±	30	**8.8×10^{-7}**	**60**	**7.5×10^{-7}**	**70**	**6.0×10^{-7}**	**90**	**5.5×10^{-7}**	**100**	**5.3×10^{-7}**
ISS-33	-18.5± to -20.5±	**50**	**2.3×10^{-7}**	**80**	**2.0×10^{-7}**	**90**	**2.0×10^{-7}**	**100**	**2.2×10^{-7}**	**100**	**1.9×10^{-7}**
ISS-35	-18.5± to -20.5±	30	1.3×10^{-6}	**60**	**8.1×10^{-7}**	**80**	**5.9×10^{-7}**	**90**	**5.0×10^{-7}**	**100**	**4.9×10^{-7}**
Full-Scale Implementation											
ISS-03	-14± to -15±	**150**	**1.1×10^{-7}**	**150**	**9.9×10^{-8}**	**340**	**8.7×10^{-8}**	*Pending*	*Pending*	*Pending*	*Pending*
ISS-06	-13± to -14±	**170**	**3.8×10^{-7}**	**220**	**2.0×10^{-7}**	*Pending*	*Pending*	*Pending*	*Pending*	*Pending*	*Pending*
ISS-07	-17± to -18±	**130**	**1.2×10^{-7}**	**210**	**1.7×10^{-7}**	**330**	**9.6×10^{-8}**	*Pending*	*Pending*	*Pending*	*Pending*
ISS-19	-16± to -17±	**110**	**2.0×10^{-7}**	**200**	**1.6×10^{-7}**	**220**	**1.9×10^{-7}**	**230**	**1.7×10^{-7}**	*Pending*	*Pending*
ISS-24	-17± to -18±	**100**	**1.1×10^{-7}**	**230**	**1.8×10^{-7}**	**190**	**2.0×10^{-7}**	**420**	**1.3×10^{-7}**	*Pending*	*Pending*
ISS-27	-16± to -17±	**120**	**1.2×10^{-7}**	**230**	**9.9×10^{-8}**	**170**	**1.5×10^{-7}**	**260**	**9.1×10^{-8}**	*Pending*	*Pending*
ISS-40	-19± to -21±	**210**	**3.1×10^{-7}**	**250**	**3.5×10^{-7}**	**400**	**1.0×10^{-7}**	**420**	**2.1×10^{-7}**	*Pending*	*Pending*
ISS-41	-15.3± to -16.3±	**190**	**4.7×10^{-7}**	**150**	**4.4×10^{-7}**	**220**	**3.5×10^{-7}**	**220**	**3.9×10^{-7}**	*Pending*	*Pending*

1. Results meeting or exceeding field performance criterion (50 pounds per square inch [psi] for unconfined compressive strength [UCS] and 1×10^{-6} centimeters per second [cm/s] for hydraulic conductivity [HC]) are shown in bold.
2. Elevation recorded in North American Vertical Datum of 1988

LANGAN	155 3rd St Report	170390002 - 155 3rd St Brooklyn	
		Report Period	
		From:	5/6/2025 06:00
		To:	5/6/2025 22:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Windspeed (mph)	Prevailing wind direction
5/6/2025	-	-	-	0.5-3.3	NNE

Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/6/2025	0.0	07:36	0.0000	07:11
Max Contribution (15 min avg.) - 5/6/2025	39.1	07:09	0.0100	12:34

