SITE OBSERVATION REPORT - RAWP Implementation – Day 94

LANGAN

PROJECT No.:	170390001	**CLIENT:**		**DATE:**	Thursday, November 20, 2025
PROJECT:	141 3rd Street		Third Street Owner LLC and 155 Third St., LLC	**WEATHER:**	Cloudy, 33 – 47^{0}F Wind: W @ 1 – 5 mph
LOCATION:	Brooklyn, New York			**TIME:**	7:00 a.m. – 3:30 p.m.
BCP SITE ID:	C224336				

EQUIPMENT:
(1) Hyundai HX 520L Hydraulic Excavator
(1) Soilmec SR-75 Drill Rig
(2) Aeroqual Air Monitoring Stations
(1) MiniRAE 3000 Photoionization Detector (PID)
Hand Tools

PRESENT AT SITE:
Langan: Jessie Almont
New Leaf: Luis Madina, Juan Ramirez
Monadnock Construction, Inc. (Monadnock): Bob Hempfling, John Henry

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:
Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2023

Site Activities

- New Leaf used a Hyundai HX 520L excavator to demolish and remove concrete in an approximately 40-foot-long by 30-foot-wide area in the northern part of site.
    - Excavated material consisted of concrete and demolition debris (C&D) debris and was screened for odors, staining, and organic vapors using a photoionization detector (PID). Evidence of impacts were not observed. Excavated material was placed on and covered with polyethylene (poly) sheeting at the end of the workday.

Sampling

- No samples were collected.

Community Air Monitoring Plan (CAMP) Activities

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on CAMP summary data sheet appended to the end of this Daily Field Report.

Material Tracking

- No material was exported from the site.
- No material was imported to site.

Material Import Summary				
Facility	**NYSDEC Approved Quantity**	**Imported**	**Today**	**Total**
Tilcon - Haverstraw Haverstraw, NY ASTM #3 Virgin Stone (1.5-Inch)	400 CY (560 tons)	**No. Loads**	0	**4**
		Quantity (tons)	0	**89.95**
Impact Materials Jersey City (IMJC) Jersey City, NJ 0.75-inch Stone	2,000 CY (2,800 tons)	**No. Loads**	0	**0**
		Quantity (tons)	0	**0**
IMJC Jersey City, NJ 1.5-inch Stone	400 CY (560 tons)	**No. Loads**	0	**2**
		Quantity (tons)	0	**49.65**

Material Export Summary				
Facility	**Approved Quantity**	**Imported**	**Today**	**Total**
Clean Earth of Carteret (CEC) Carteret, NJ Elevated Soil/Fill	9,857 CY (13,800 tons)	**No. Loads**	0	**62**
		Quantity (CY)	0	**1,240**
Clean Earth of New Castle (CENC) New Castle, DE Non-Hazardous Contaminated Soil/Urban Fill	3,571 CY (5,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Atlantic County Utilities Authority (ACUA) Egg Harbor Township, NJ Non-Hazardous Contaminated Soil/Urban Fill	714 CY (1,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Clean Earth of North Jersey (CENJ) Kearny, NJ Hazardous Lead	107 CY (150 tons)	**No. Loads**	0	**2**
		Quantity (CY)	0	**40**

Drums

- One 55-gallon drum containing purged groundwater and DNAPL is staged in the southern part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- Two 55-gallon drums containing purged groundwater are staged in the southern part of the site.
- Three 55-gallon drums containing drill cuttings are staged in the eastern part of the site.
- One 55-gallon drum containing spent personal protective equipment (PPE) is staged in the southeastern part of the site.

Anticipated Activities

- New Leaf will continue slab demolition in the northern part of the site.
- New Leaf will begin drilling displacement piles.

SITE PHOTOGRAPHS:

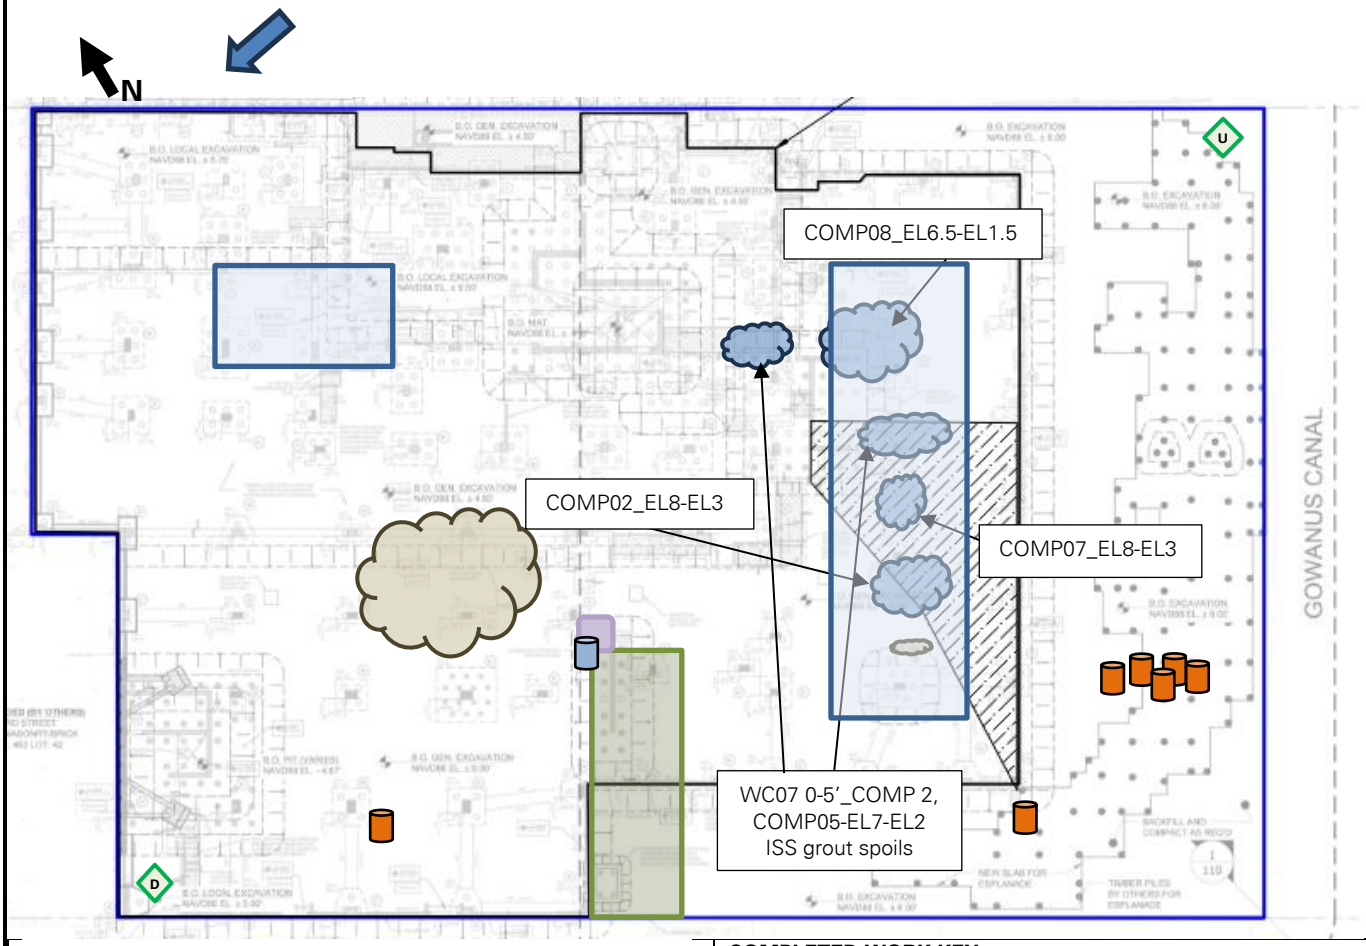


Photo 1: New Leaf demolishing concrete slab in the northern part of site (facing east).



Photo 2: New Leaf stockpiling C&D debris in the central part of site (facing east).

FIGURE 1 - SITE MAP:



LEGEND:

- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)

COMPLETED WORK KEY


- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin


Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024


LANGAN	Site Contribution Report	170390002 - 155 3rd St Brooklyn	
		Report Period	
		From:	11/20/2025 06:00
		To:	11/20/2025 17:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
11/20/2025	36.5 - 53.6	34.1 - 56.2	30.3 - 30.4	0.4 - 4.8	E


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 11/20/2025	0.0	07:30	0.0000	07:15
Max Contribution (15 min avg.) - 11/20/2025	5.1	09:15	0.0020	07:45
Daily Avg. Contribution (15 min avg.) - 11/20/2025	0.4	-	0.0003	-

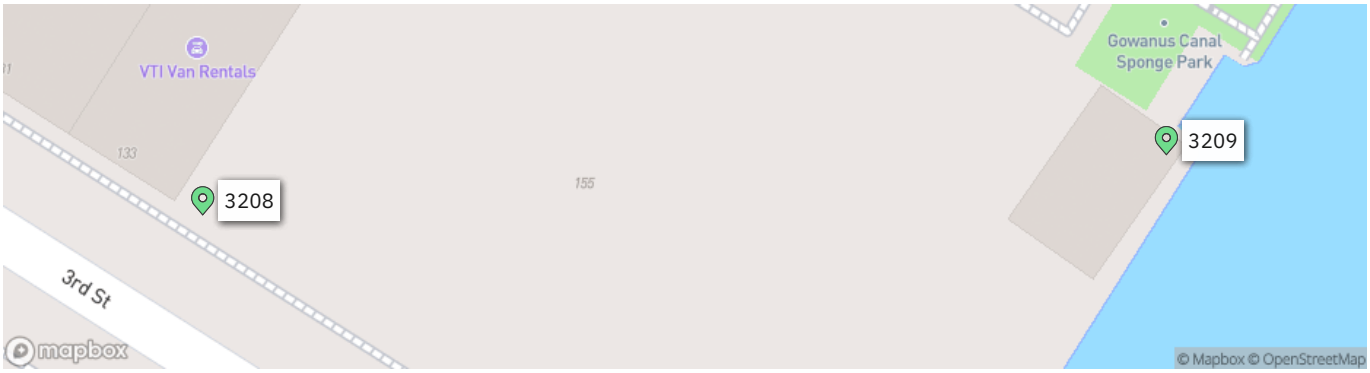

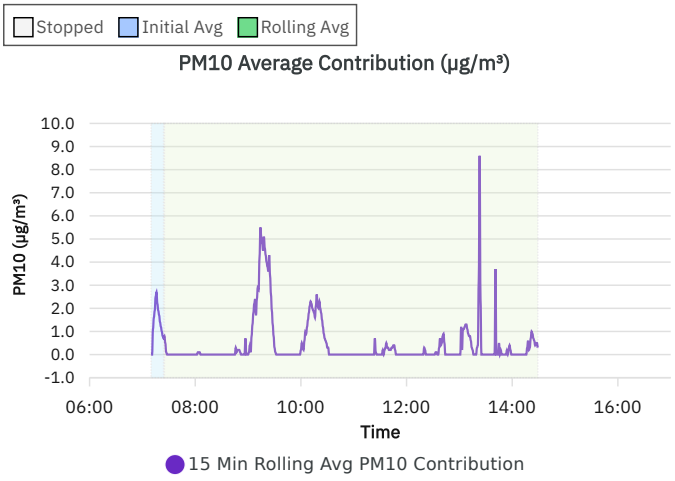


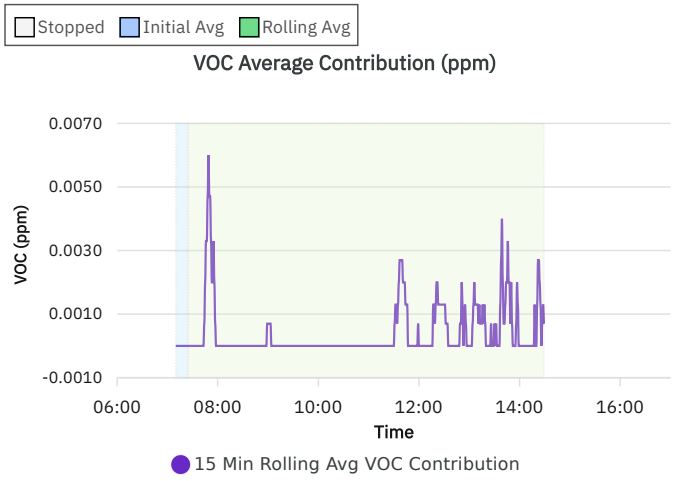


Wind rose (mph)

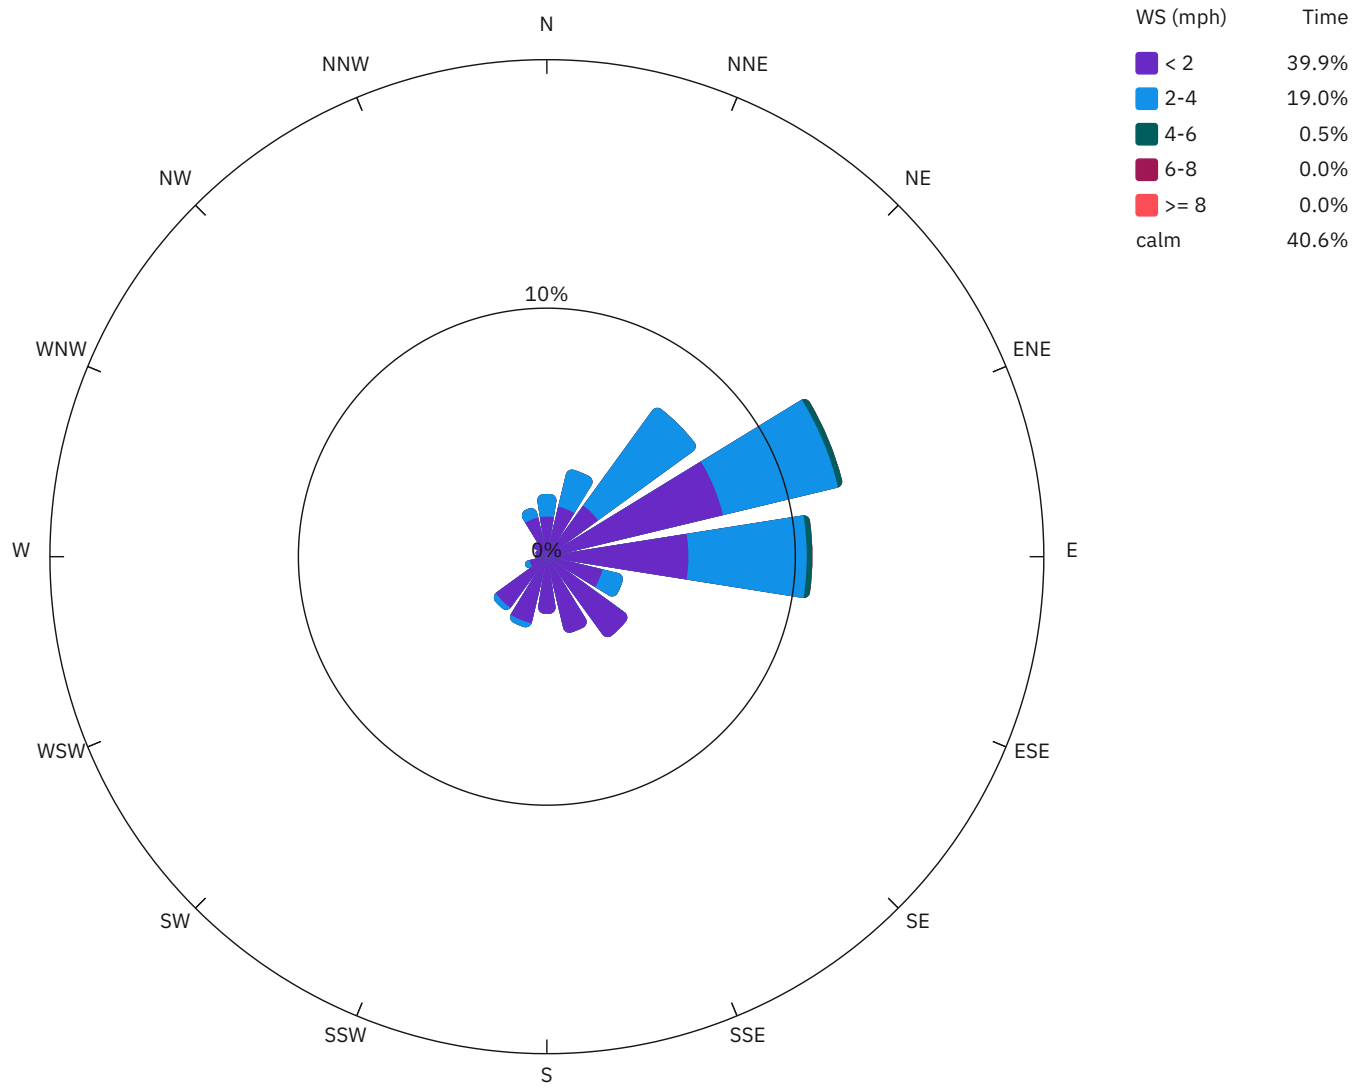

3208

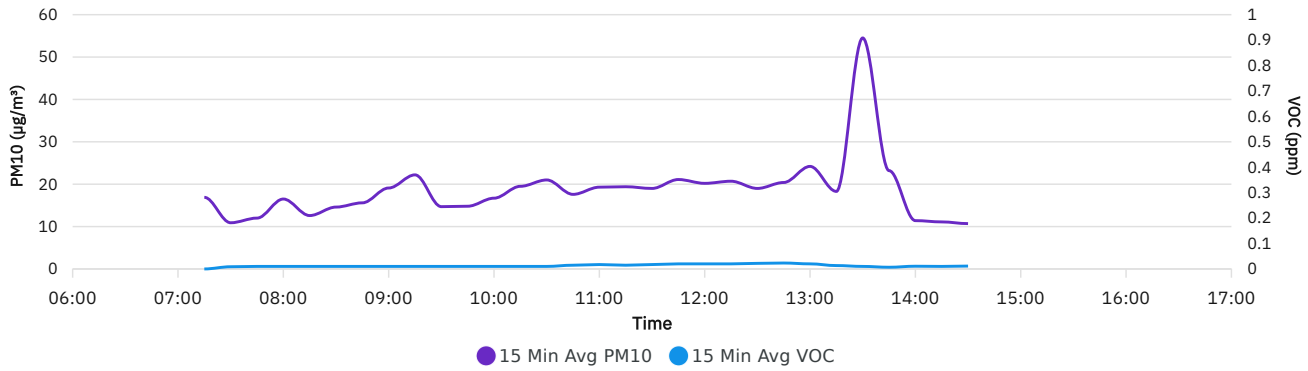

3209

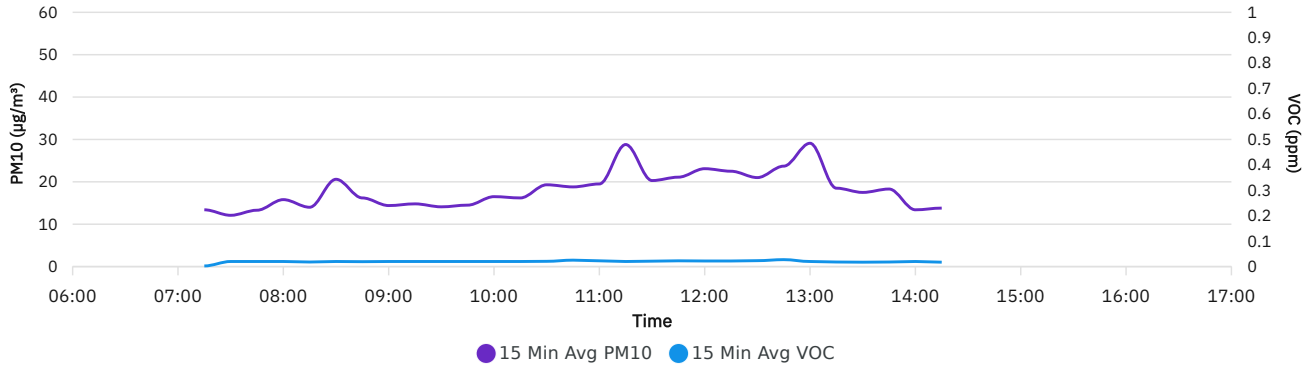
60
50
40
30
20
10
0
PM10 (µg/m³)
1
0.9
0.8
0.7
0.6
0.5
0.4
0.3
0.2
0.1
0
VOC (ppm)
06:00
07:00
08:00
09:00
10:00
11:00
12:00
13:00
14:00
15:00
16:00
17:00
Time
15 Min Avg PM10
15 Min Avg VOC

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
11/20/2025 07:15	13.9	16.4	2.5	0.0033	0.0000	0.0000	1.3	NE
11/20/2025 07:30	12.1	10.9	0.0	0.0200	0.0087	0.0000	1.7	E
11/20/2025 07:45	12.7	12.5	0.0	0.0140	0.0160	0.0020	0.1	SE
11/20/2025 08:00	16.4	15.9	0.0	0.0167	0.0133	0.0000	1.0	ENE
11/20/2025 08:15	14.0	12.6	0.0	0.0173	0.0107	0.0000	2.6	ENE
11/20/2025 08:30	20.3	15.0	0.0	0.0193	0.0107	0.0000	1.6	ENE
11/20/2025 08:45	15.9	15.9	0.0	0.0180	0.0113	0.0000	1.2	ENE
11/20/2025 09:00	17.0	16.5	0.0	0.0147	0.0153	0.0007	0.4	NNE
11/20/2025 09:15	15.9	21.0	5.1	0.0187	0.0113	0.0000	1.0	E
11/20/2025 09:30	14.3	14.6	0.3	0.0193	0.0107	0.0000	1.3	NE
11/20/2025 09:45	14.6	14.7	0.0	0.0193	0.0107	0.0000	1.8	NE
11/20/2025 10:00	16.5	16.7	0.2	0.0200	0.0100	0.0000	1.9	ENE
11/20/2025 10:15	17.0	18.8	1.8	0.0180	0.0120	0.0000	1.1	ENE
11/20/2025 10:30	20.0	20.3	0.3	0.0167	0.0140	0.0000	0.8	ENE
11/20/2025 10:45	18.6	17.7	0.0	0.0233	0.0167	0.0000	1.3	ENE
11/20/2025 11:00	19.5	19.2	0.0	0.0227	0.0173	0.0000	1.7	E
11/20/2025 11:15	26.9	21.3	0.0	0.0193	0.0153	0.0000	1.0	E
11/20/2025 11:30	20.0	19.3	0.0	0.0193	0.0193	0.0000	0.2	ESE
11/20/2025 11:45	21.0	21.3	0.4	0.0207	0.0220	0.0013	0.7	SSW
11/20/2025 12:00	21.9	21.4	0.0	0.0213	0.0207	0.0000	0.8	S
11/20/2025 12:15	22.0	21.2	0.0	0.0213	0.0207	0.0000	0.6	S
11/20/2025 12:30	20.1	19.9	0.0	0.0220	0.0233	0.0013	0.2	S
11/20/2025 12:45	22.5	21.6	0.0	0.0253	0.0253	0.0000	0.5	SSE
11/20/2025 13:00	27.2	26.1	0.0	0.0200	0.0200	0.0000	0.6	SW
11/20/2025 13:15	18.3	18.5	0.2	0.0153	0.0160	0.0007	0.5	S
11/20/2025 13:30	38.5	33.6	0.0	0.0133	0.0140	0.0007	0.5	SSW
11/20/2025 13:45	20.5	21.0	0.5	0.0113	0.0133	0.0020	0.8	S
11/20/2025 14:00	12.6	12.2	0.0	0.0160	0.0147	0.0000	0.9	S
11/20/2025 14:15	12.7	12.3	0.0	0.0140	0.0133	0.0000	0.7	S
11/20/2025 14:30							0.6	S

Air Monitoring Data by Location: 15 Min Avg Data

Date/Time	3208 PM10 (µg/m³)	3208 VOC (ppm)	3209 PM10 (µg/m³)	3209 VOC (ppm)	Wind Direction	Wind Speed
11/20/2025 07:15	16.9	0.0000	13.4	0.0025	NE	1.3
11/20/2025 07:30	10.9	0.0087	12.1	0.0200	E	1.7
11/20/2025 07:45	12.0	0.0100	13.3	0.0200	SE	0.1
11/20/2025 08:00	16.5	0.0100	15.8	0.0200	ENE	1.0
11/20/2025 08:15	12.6	0.0100	14.0	0.0180	ENE	2.6
11/20/2025 08:30	14.6	0.0100	20.6	0.0200	ENE	1.6
11/20/2025 08:45	15.6	0.0100	16.2	0.0193	ENE	1.2
11/20/2025 09:00	19.1	0.0100	14.4	0.0200	NNE	0.4
11/20/2025 09:15	22.2	0.0100	14.8	0.0200	E	1.0
11/20/2025 09:30	14.7	0.0100	14.1	0.0200	NE	1.3
11/20/2025 09:45	14.8	0.0100	14.5	0.0200	NE	1.8
11/20/2025 10:00	16.7	0.0100	16.5	0.0200	ENE	1.9
11/20/2025 10:15	19.5	0.0100	16.2	0.0200	ENE	1.1
11/20/2025 10:30	21.0	0.0100	19.3	0.0207	ENE	0.8
11/20/2025 10:45	17.6	0.0147	18.8	0.0253	ENE	1.3
11/20/2025 11:00	19.3	0.0173	19.5	0.0227	E	1.7
11/20/2025 11:15	19.4	0.0147	28.8	0.0200	E	1.0
11/20/2025 11:30	19.0	0.0173	20.3	0.0213	ESE	0.2
11/20/2025 11:45	21.1	0.0200	21.1	0.0227	SSW	0.7
11/20/2025 12:00	20.2	0.0200	23.1	0.0220	S	0.8
11/20/2025 12:15	20.7	0.0200	22.5	0.0220	S	0.6
11/20/2025 12:30	19.0	0.0220	21.0	0.0233	S	0.2
11/20/2025 12:45	20.4	0.0233	23.7	0.0273	SSE	0.5
11/20/2025 13:00	24.2	0.0200	29.1	0.0200	SW	0.6
11/20/2025 13:15	18.3	0.0133	18.5	0.0180	S	0.5
11/20/2025 13:30	54.5	0.0100	17.5	0.0173	SSW	0.5
11/20/2025 13:45	23.2	0.0067	18.3	0.0180	S	0.8
11/20/2025 14:00	11.4	0.0107	13.4	0.0200	S	0.9
11/20/2025 14:15	11.1	0.0100	13.8	0.0173	S	0.7
11/20/2025 14:30	10.7	0.0113			S	0.6
