SITE OBSERVATION REPORT - RAWP Implementation – Day 113

LANGAN

PROJECT No.:	170390001	**CLIENT:**		**DATE:**	Friday, December 19, 2025
PROJECT:	141 3rd Street	Third Street Owner LLC and 155 Third St., LLC		**WEATHER:**	Rain, 32 – 49°F Wind: ESE @ 1.1 – 25.4 mph
LOCATION:	Brooklyn, New York			**TIME:**	7:00 a.m. – 3:30 p.m.
BCP SITE ID:	C224336				

EQUIPMENT:
(1) Hyundai HX 520L Hydraulic Excavator
(1) Volvo ECR355EL Hydraulic Excavator
(1) Soilmec SR-75 Drill Rig
(1) Leibherr LRB 355.1 Drill Rig
(1) Cammachio MC 22 Drill Rig
(2) Aeroqual Air Monitoring Stations
(1) MiniRAE 3000 Photoionization Detector
Hand Tools

PRESENT AT SITE:
Langan: Jessie Almont
New Leaf: Jose Gomez
Monadnock Construction, Inc. (Monadnock): Bob Hempfling,
Mueser Rutledge Consulting Engineers (MRCE): Joseph Croft, Amani Calderon

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:
Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2023

Site Activities

- New Leaf advanced and installed thirteen displacement piles (pile ID numbers 91, 351, 230, 355, 373, 380, 399, 405, 257, and 253 to about 65 feet below grade surface [bgs] and pile ID numbers 361, 364, and 396 to about 70 feet bgs) in the northern and eastern parts of the site.
    - New Leaf advanced pile ID number 402 to a depth of about 20 feet bgs and abandoned the hole due to inability to drill to full depth. This pile will be reattempted at a later date.
    - Less than one cubic yard of drilling spoils was generated during displacement pile installation and were temporarily staged adjacent to the work area. Langan screened the drilling spoils for odors, staining, and organic vapors using a photoionization detector (PID). No evidence of impacts was observed. The drilling spoils will be removed and stockpiled during future excavation around the piles.
    - New Leaf used a tremie pipe to place grout within the displacement piles. Excess grout will be stockpiled and managed as construction and demolition (C&D) debris at a later date.

Sampling

- No samples were collected.

Community Air Monitoring Plan (CAMP) Activities

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on the CAMP summary data sheet appended to the end of this Daily Field Report.

Material Tracking

- No material was exported from the site.
- No material was imported to the site.

Material Import Summary				
Facility	**NYSDEC Approved Quantity**	**Imported**	**Today**	**Total**
Tilcon - Haverstraw Haverstraw, NY ASTM #3 Virgin Stone (1.5-Inch)	400 CY (560 tons)	**No. Loads**	0	**6**
		Quantity (tons)	0	**130.94**
Impact Materials Jersey City (IMJC) Jersey City, NJ 0.75-inch Stone	2,000 CY (2,800 tons)	**No. Loads**	0	**0**
		Quantity (tons)	0	**0**
IMJC Jersey City, NJ 1.5-inch Stone	400 CY (560 tons)	**No. Loads**	0	**2**
		Quantity (tons)	0	**49.65**

Material Export Summary				
Facility	**Approved Quantity**	**Exported**	**Today**	**Total**
Clean Earth of Carteret (CEC) Carteret, NJ Elevated Soil/Fill	9,857 CY (13,800 tons)	**No. Loads**	0	**72**
		Quantity (CY)	0	**1,440**
Clean Earth of New Castle (CENC) New Castle, DE Non-Hazardous Contaminated Soil/Urban Fill	3,571 CY (5,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Atlantic County Utilities Authority (ACUA) Egg Harbor Township, NJ Non-Hazardous Contaminated Soil/Urban Fill	714 CY (1,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Clean Earth of North Jersey (CENJ) Kearny, NJ Hazardous Lead	107 CY (150 tons)	**No. Loads**	0	**2**
		Quantity (CY)	0	**40**

Drums

- One 55-gallon drum containing purged groundwater and Dense Non-Aqueous Phase Liquid (DNAPL) is staged in the southern part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- Two 55-gallon drums containing purged groundwater are staged in the southern part of the site.
- Three 55-gallon drums containing drill cuttings are staged in the eastern part of the site.
- One 55-gallon drum containing spent personal protective equipment (PPE) is staged in the southeastern part of the site.

Anticipated Activities

- New Leaf will continue drilling displacement piles.

SITE PHOTOGRAPHS:

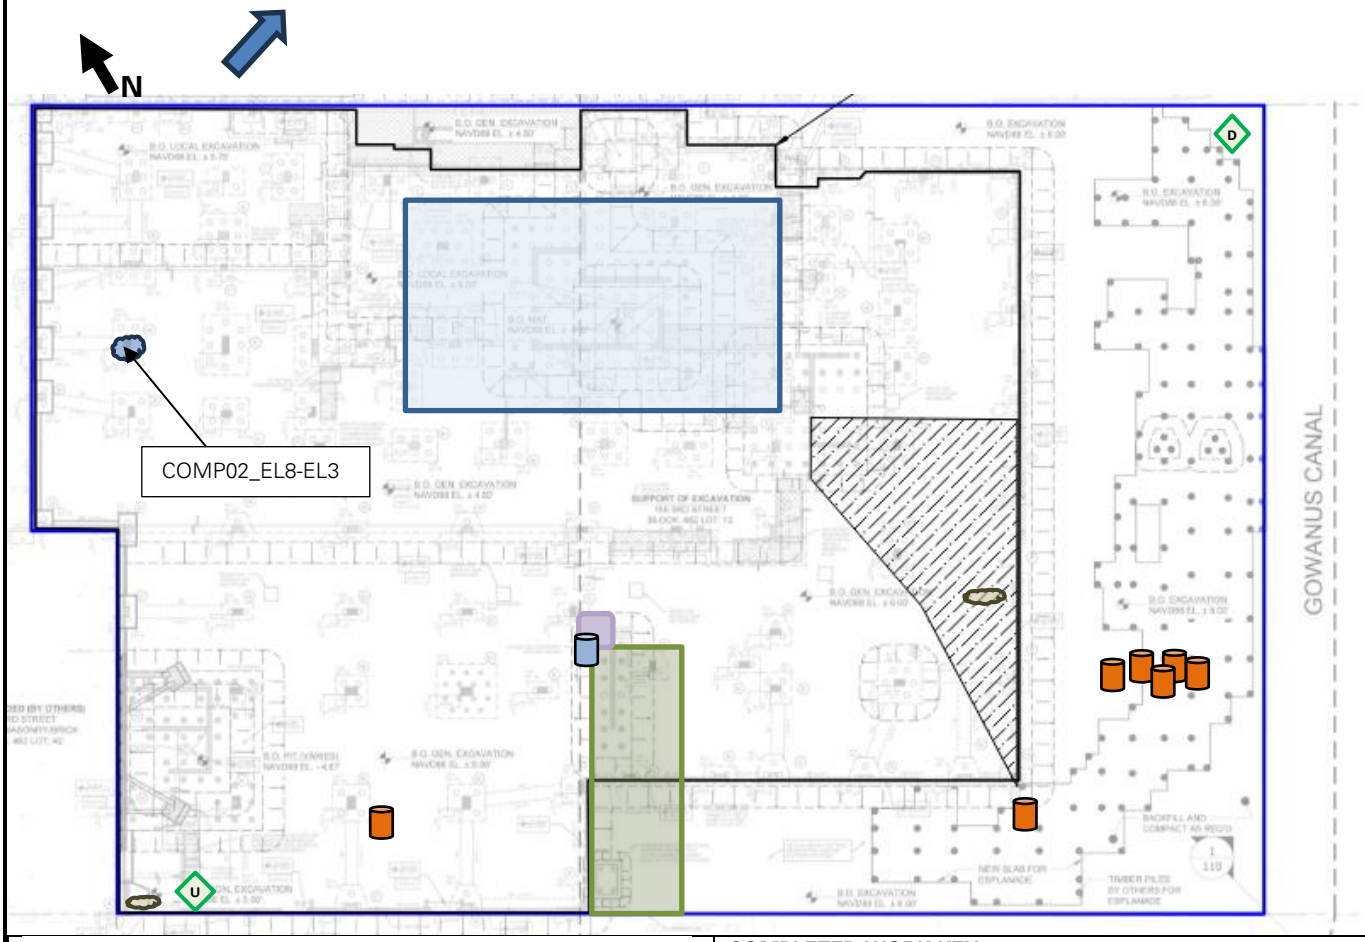


Photo 1: New Leaf drilling displacement piles in the eastern part of site (facing east).



Photo 2: New Leaf performing equipment maintenance (facing north).

FIGURE 1 - SITE MAP:



LEGEND:


- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)

COMPLETED WORK KEY

- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin

Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024

FIGURE 2 – DISPLACEMENT PILE PLAN:

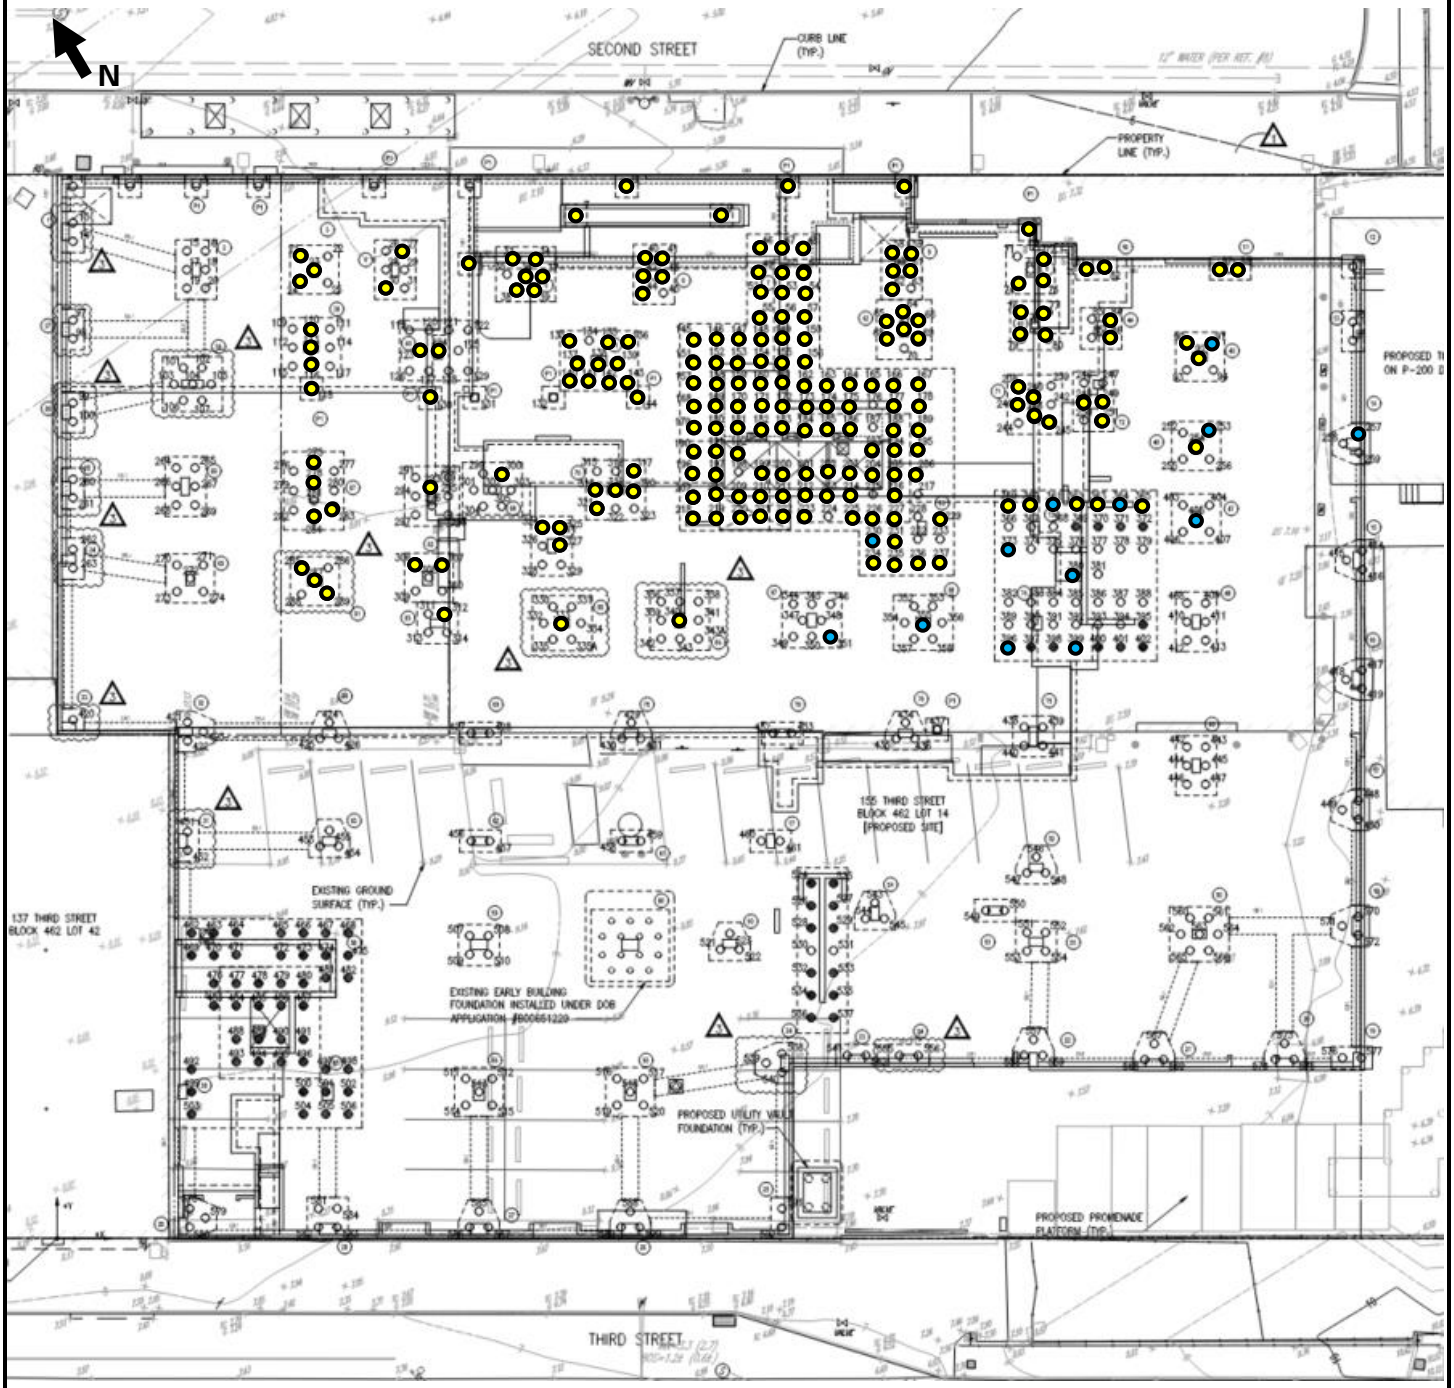

COMPLETED WORK KEY


- Approximate Location of Displacement Pile Advanced Today
- Approximate Location of Displacement Pile Advanced Previously


Base map includes Drawing P100 – Full Displacement Pile (FDP) ID, prepared by Mueser Rutledge Consulting Engineers PLLC, dated 8/18/2025


LANGAN	Site Contribution Report	170390002 - 155 3rd St Brooklyn	
		Report Period	
		From:	12/19/2025 06:00
		To:	12/19/2025 17:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
12/19/2025	49.1 - 54.5	66.1 - 95.8	29.4 - 29.6	1.1 - 25.4	WNW


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 12/19/2025	0.0	07:30	0.0000	08:45
Max Contribution (15 min avg.) - 12/19/2025	6.1	08:00	0.0167	12:30
Daily Avg. Contribution (15 min avg.) - 12/19/2025	1.2	-	0.0045	-

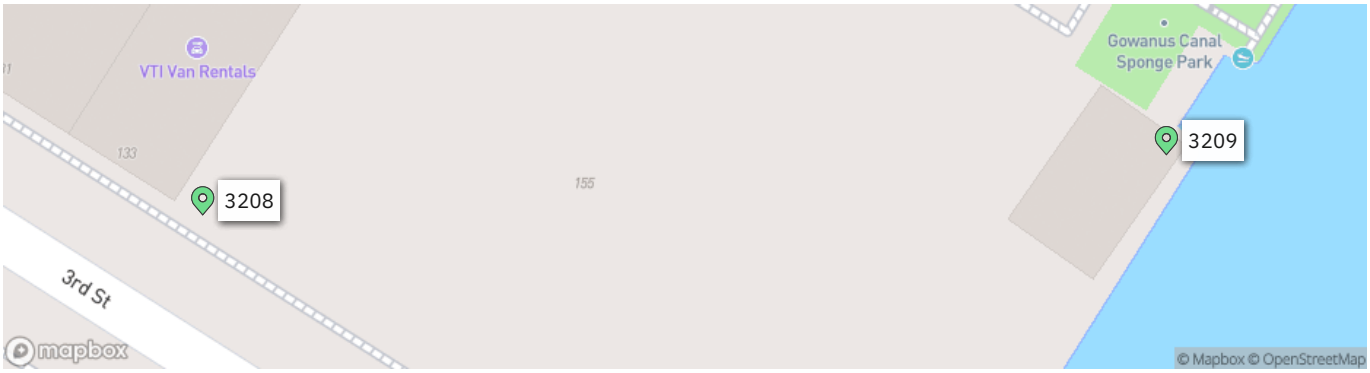

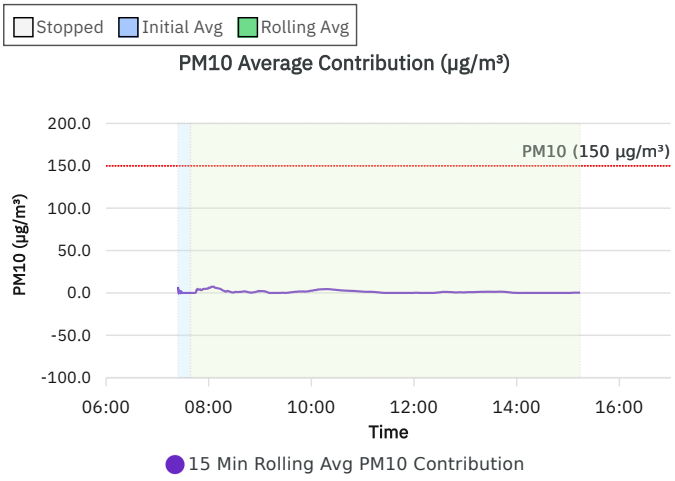


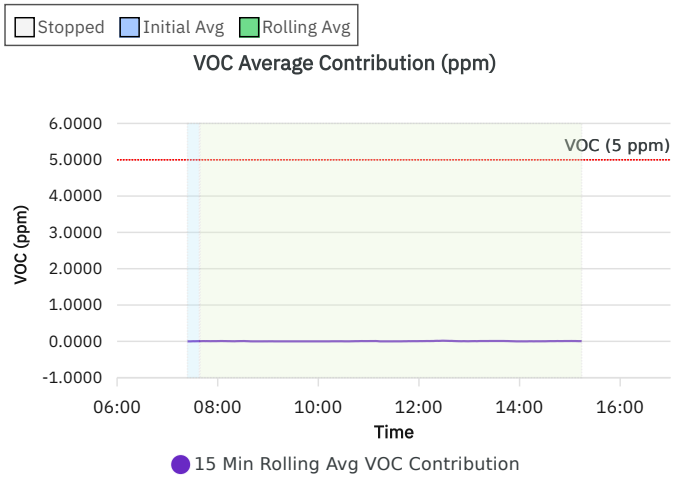


Wind rose (mph)

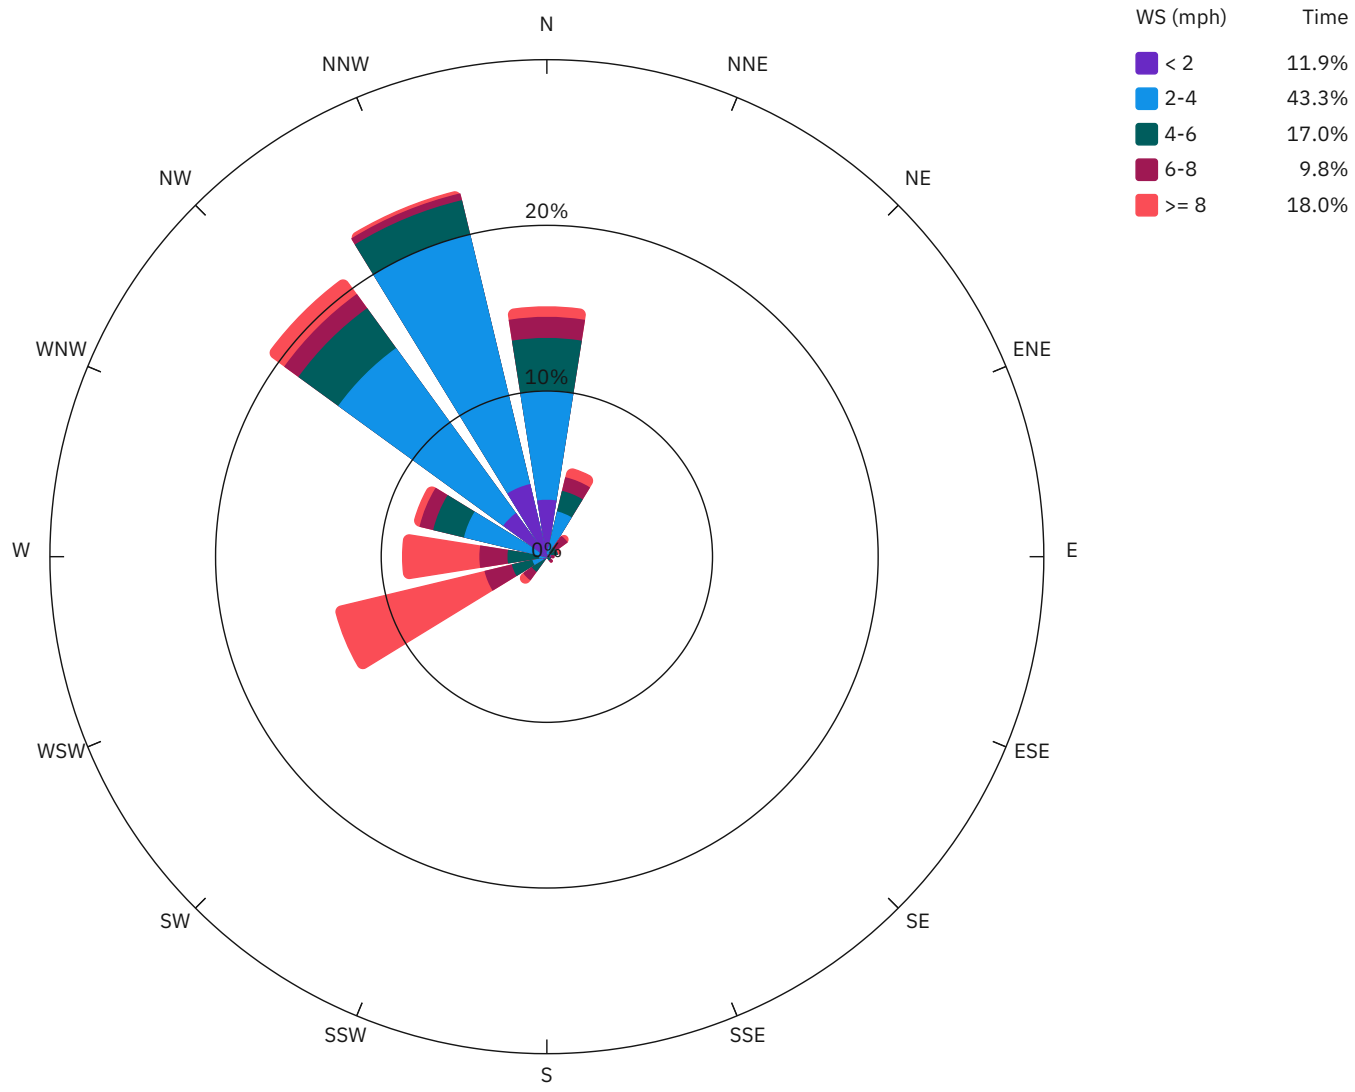

3208

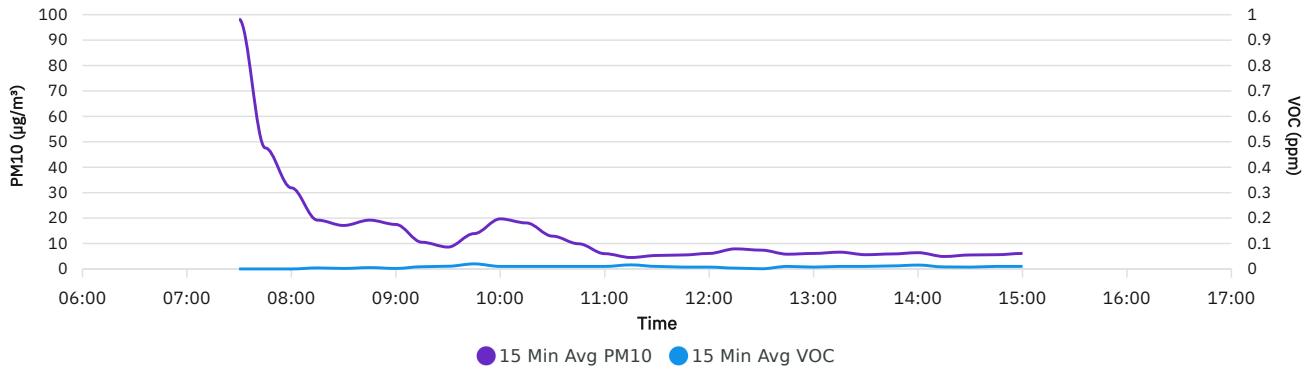

3209

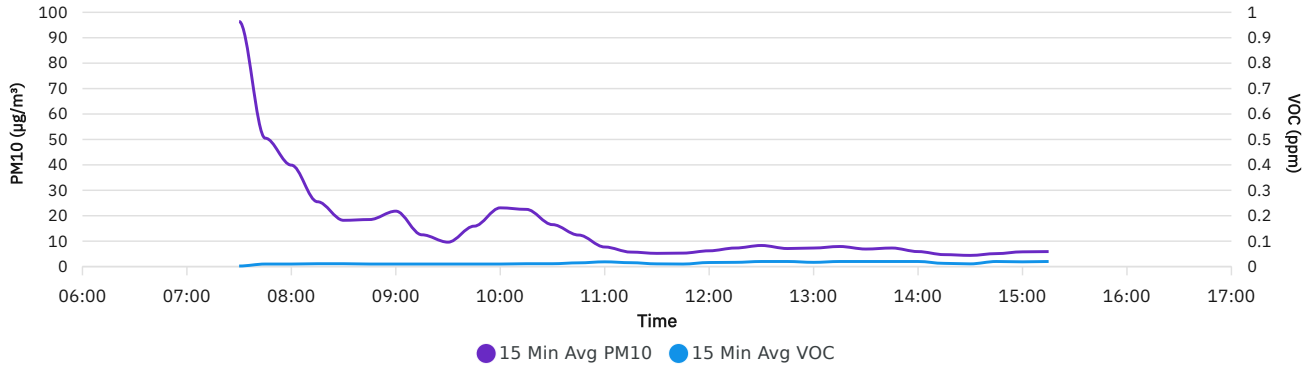
100
90
80
70
60
50
40
30
20
10
0
PM10 (µg/m³)
1
0.9
0.8
0.7
0.6
0.5
0.4
0.3
0.2
0.1
0
VOC (ppm)
06:00
07:00
08:00
09:00
10:00
11:00
12:00
13:00
14:00
15:00
16:00
17:00
Time
15 Min Avg PM10
15 Min Avg VOC

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
12/19/2025 07:30	101.1	90.0	0.0	0.0000	0.0029	0.0029	8.1	W
12/19/2025 07:45	48.8	49.3	0.6	0.0020	0.0080	0.0060	5.3	NW
12/19/2025 08:00	32.8	38.9	6.1	0.0013	0.0087	0.0073	4.5	W
12/19/2025 08:15	20.4	24.3	3.9	0.0053	0.0100	0.0047	5.1	WNW
12/19/2025 08:30	17.2	18.1	0.9	0.0027	0.0107	0.0080	3.6	NW
12/19/2025 08:45	18.3	19.5	1.2	0.0093	0.0060	0.0000	3.3	NE
12/19/2025 09:00	18.5	20.8	2.3	0.0053	0.0067	0.0013	2.5	N
12/19/2025 09:15	11.9	11.1	0.0	0.0113	0.0073	0.0000	3.7	N
12/19/2025 09:30	9.1	9.1	0.1	0.0113	0.0093	0.0000	4.6	NNW
12/19/2025 09:45	14.1	15.7	1.6	0.0193	0.0107	0.0000	6.8	W
12/19/2025 10:00	20.1	22.7	2.6	0.0100	0.0100	0.0000	4.9	W
12/19/2025 10:15	18.1	22.5	4.4	0.0100	0.0113	0.0013	12.1	WSW
12/19/2025 10:30	12.9	16.5	3.5	0.0100	0.0113	0.0013	11.7	WSW
12/19/2025 10:45	9.9	12.4	2.5	0.0100	0.0147	0.0047	14.0	WSW
12/19/2025 11:00	6.1	7.6	1.5	0.0107	0.0180	0.0073	7.0	WNW
12/19/2025 11:15	4.6	5.6	1.0	0.0167	0.0147	0.0000	3.2	NNW
12/19/2025 11:30	5.3	5.2	0.0	0.0100	0.0107	0.0007	2.8	NW
12/19/2025 11:45	5.5	5.3	0.0	0.0073	0.0100	0.0027	2.5	NNW
12/19/2025 12:00	6.1	6.2	0.1	0.0087	0.0147	0.0060	1.9	NNW
12/19/2025 12:15	7.8	7.3	0.0	0.0053	0.0147	0.0093	1.6	NNW
12/19/2025 12:30	7.5	8.2	0.7	0.0020	0.0187	0.0167	2.0	NW
12/19/2025 12:45	6.1	6.8	0.8	0.0120	0.0180	0.0060	1.9	NNW
12/19/2025 13:00	6.3	7.1	0.8	0.0100	0.0140	0.0040	2.7	NW
12/19/2025 13:15	6.7	7.8	1.2	0.0107	0.0193	0.0087	2.6	NW
12/19/2025 13:30	5.6	6.9	1.4	0.0100	0.0200	0.0100	3.2	WNW
12/19/2025 13:45	5.9	7.3	1.3	0.0120	0.0200	0.0080	3.2	NW
12/19/2025 14:00	6.1	6.1	0.0	0.0180	0.0173	0.0000	2.8	NNW
12/19/2025 14:15	4.8	4.8	0.0	0.0093	0.0113	0.0020	3.4	NNW
12/19/2025 14:30	5.3	4.5	0.0	0.0080	0.0100	0.0020	3.4	NNW
12/19/2025 14:45	5.6	5.2	0.0	0.0107	0.0193	0.0087	2.7	NW
12/19/2025 15:00	6.1	5.9	0.0	0.0100	0.0187	0.0087	2.3	NW

Air Monitoring Data by Location: 15 Min Avg Data

Date/Time	3208 PM10 (µg/m³)	3208 VOC (ppm)	3209 PM10 (µg/m³)	3209 VOC (ppm)	Wind Direction	Wind Speed
12/19/2025 07:30	98.2	0.0000	96.4	0.0022	W	8.1
12/19/2025 07:45	47.6	0.0000	50.5	0.0100	NW	5.3
12/19/2025 08:00	31.9	0.0000	39.9	0.0100	W	4.5
12/19/2025 08:15	19.2	0.0040	25.5	0.0113	WNW	5.1
12/19/2025 08:30	17.1	0.0020	18.2	0.0113	NW	3.6
12/19/2025 08:45	19.2	0.0053	18.5	0.0100	NE	3.3
12/19/2025 09:00	17.5	0.0020	21.8	0.0100	N	2.5
12/19/2025 09:15	10.5	0.0087	12.5	0.0100	N	3.7
12/19/2025 09:30	8.6	0.0107	9.6	0.0100	NNW	4.6
12/19/2025 09:45	13.9	0.0200	15.9	0.0100	W	6.8
12/19/2025 10:00	19.7	0.0100	23.1	0.0100	W	4.9
12/19/2025 10:15	18.1	0.0100	22.5	0.0113	WSW	12.1
12/19/2025 10:30	12.9	0.0100	16.5	0.0113	WSW	11.7
12/19/2025 10:45	9.9	0.0100	12.4	0.0147	WSW	14.0
12/19/2025 11:00	6.0	0.0100	7.7	0.0187	WNW	7.0
12/19/2025 11:15	4.5	0.0160	5.7	0.0153	NNW	3.2
12/19/2025 11:30	5.3	0.0100	5.2	0.0107	NW	2.8
12/19/2025 11:45	5.5	0.0073	5.3	0.0100	NNW	2.5
12/19/2025 12:00	6.1	0.0073	6.2	0.0160	NNW	1.9
12/19/2025 12:15	7.9	0.0033	7.3	0.0167	NNW	1.6
12/19/2025 12:30	7.4	0.0007	8.3	0.0200	NW	2.0
12/19/2025 12:45	5.8	0.0100	7.1	0.0200	NNW	1.9
12/19/2025 13:00	6.1	0.0073	7.3	0.0167	NW	2.7
12/19/2025 13:15	6.6	0.0100	7.9	0.0200	NW	2.6
12/19/2025 13:30	5.6	0.0100	6.9	0.0200	WNW	3.2
12/19/2025 13:45	5.9	0.0120	7.3	0.0200	NW	3.2
12/19/2025 14:00	6.4	0.0153	5.9	0.0200	NNW	2.8
12/19/2025 14:15	4.9	0.0080	4.7	0.0127	NNW	3.4
12/19/2025 14:30	5.5	0.0073	4.4	0.0107	NNW	3.4
12/19/2025 14:45	5.6	0.0100	5.1	0.0200	NW	2.7
12/19/2025 15:00	6.1	0.0100	5.8	0.0187	NW	2.3
12/19/2025 15:15			5.9	0.0200		
