# SITE OBSERVATION REPORT - RAWP Implementation – Day 121

LANGAN

| | | | | | |
|---|---|---|---|---|---|
| **PROJECT No.:** | 170390001 | **CLIENT:** | | **DATE:** | Monday, January 5, 2026 |
| **PROJECT:** | 141 3rd Street | | Third Street Owner LLC and 155 Third St., LLC | **WEATHER:** | Cloudy, 28 – 35$^0$F<br>Wind: E @ 1 – 13.6 mph |
| **LOCATION:** | Brooklyn, New York | | | **TIME:** | 7:00 a.m. – 4:45 p.m. |
| **BCP SITE ID:** | C224336 | | | | |

**EQUIPMENT:**
(1) Hyundai HX 520L Hydraulic Excavator
(1) Volvo ECR355EL Hydraulic Excavator
(1) Soilmec SR-75 Drill Rig
(1) Leibherr LRB 355.1 Drill Rig
(1) Cammachio MC 22 Drill Rig
(2) Aeroqual Air Monitoring Stations
(1) MiniRAE 3000 Photoionization Detector
Hand Tools

**PRESENT AT SITE:**
**Langan**: Jessie Almont
**New Leaf:** Jose Gomez
**Monadnock Construction, Inc. (Monadnock):** Bob Hempfling
**Mueser Rutledge Consulting Engineers (MRCE)**: Joseph Croft, Amani Calderon
**WSP:** Christopher DiSclafani

**OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:**
Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2023

**Site Activities**

- New Leaf advanced and installed twenty-four displacement piles (pile ID numbers 125, 102, 271, 265, 18, 114, 375, 379, 403, 574, 569, 566, 558, 553, 546, 441, 391, 328, 431, 338, 433, 435, 346, 353 to about 65 feet below grade surface [bgs]) in the northern, southern and eastern parts of the site.
    - Less than one cubic yard of drilling spoils was generated during displacement pile installation and were temporarily staged adjacent to the work area. Langan screened the drilling spoils for odors, staining, and organic vapors using a photoionization detector (PID). No evidence of impacts was observed. The drilling spoils will be removed and stockpiled during future excavation around the piles.
    - New Leaf used a tremie pipe to place grout within the displacement piles. Excess grout will be stockpiled and managed as construction and demolition (C&D) debris at a later date.
- New Leaf used a Hyundai HX 520L excavator to excavate a former concrete slab in an approximately 5-foot-long by 10-foot-wide area in the northern part of site.
    - Excavated material consisted of C&D debris and was screened for odors, staining, and organic vapors using a PID. Evidence of impacts were not observed. Excavated material was placed on and covered with polyethylene (poly) sheeting at the end of the workday.
- A representative from WSP conducted a site visit on behalf of the NYSDEC. No adverse conditions were noted as a result of the site visit.

**Sampling**

- No samples were collected.

**Community Air Monitoring Plan (CAMP) Activities**

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on the CAMP summary data sheet appended to the end of this Daily Field Report.

**Material Tracking**

- No material was exported from the site.
- No material was imported to the site.

| Material Import Summary | | | | |
|---|---|---|---|---|
| **Facility** | **NYSDEC Approved Quantity** | **Imported** | **Today** | **Total** |
| **Tilcon - Haverstraw<br>Haverstraw, NY<br>ASTM #3 Virgin Stone (1.5-Inch)** | 400 CY (560 tons) | **No. Loads** | 0 | **6** |
| | | **Quantity (tons)** | 0 | **130.94** |
| **Impact Materials Jersey City (IMJC)<br>Jersey City, NJ<br>0.75-inch Stone** | 2,000 CY (2,800 tons) | **No. Loads** | 0 | **0** |
| | | **Quantity (tons)** | 0 | **0** |
| **IMJC<br>Jersey City, NJ<br>1.5-inch Stone** | 400 CY (560 tons) | **No. Loads** | 0 | **2** |
| | | **Quantity (tons)** | 0 | **49.65** |

| Material Export Summary | | | | |
|---|---|---|---|---|
| **Facility** | **Approved Quantity** | **Exported** | **Today** | **Total** |
| **Clean Earth of Carteret (CEC)<br>Carteret, NJ<br>Elevated Soil/Fill** | 9,857 CY (13,800 tons) | **No. Loads** | 0 | **72** |
| | | **Quantity (CY)** | 0 | **1,440** |
| **Clean Earth of New Castle (CENC)<br>New Castle, DE<br>Non-Hazardous Contaminated Soil/Urban Fill** | 3,571 CY (5,000 tons) | **No. Loads** | 0 | **0** |
| | | **Quantity (CY)** | 0 | **0** |
| **Atlantic County Utilities Authority (ACUA)<br>Egg Harbor Township, NJ<br>Non-Hazardous Contaminated Soil/Urban Fill** | 714 CY (1,000 tons) | **No. Loads** | 0 | **0** |
| | | **Quantity (CY)** | 0 | **0** |
| **Clean Earth of North Jersey (CENJ)<br>Kearny, NJ<br>Hazardous Lead** | 107 CY (150 tons) | **No. Loads** | 0 | **2** |
| | | **Quantity (CY)** | 0 | **40** |

## Drums

- One 55-gallon drum containing purged groundwater and Dense Non-Aqueous Phase Liquid (DNAPL) is staged in the southern part of the site.
- One 55-gallon drum containing purged groundwater and DNAPL is staged in the western part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- Two 55-gallon drums containing personal protective equipment (PPE) are staged in the southern part of the site.
- Two 55-gallon drums containing drill cuttings are staged in the southern part of the site.

## Anticipated Activities

- New Leaf will continue drilling displacement piles.

**SITE PHOTOGRAPHS:**

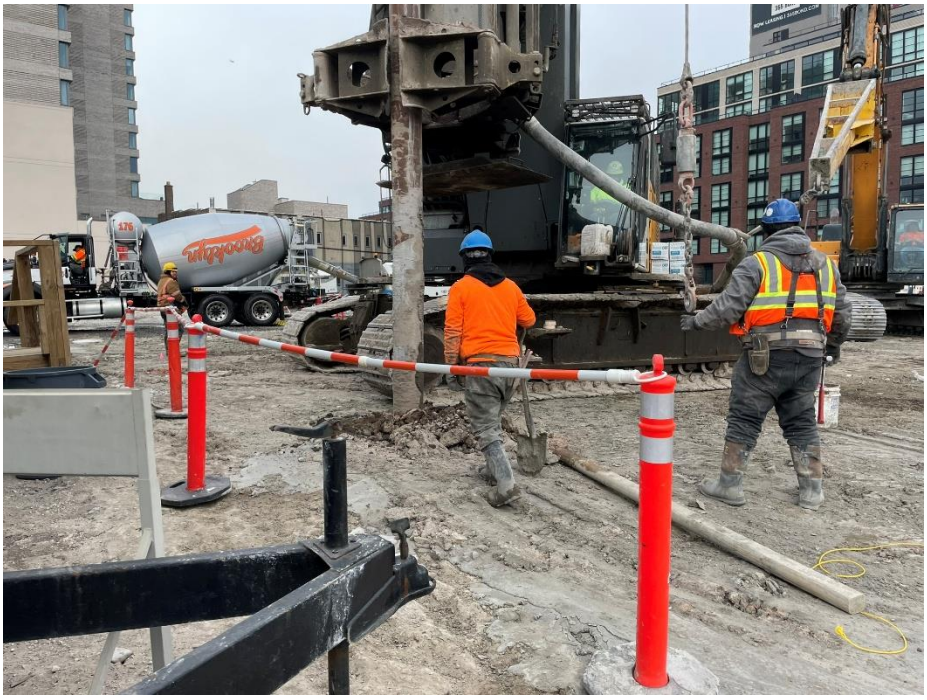


**Photo 1:** New Leaf drilling displacement piles in the southern part of site (facing north).


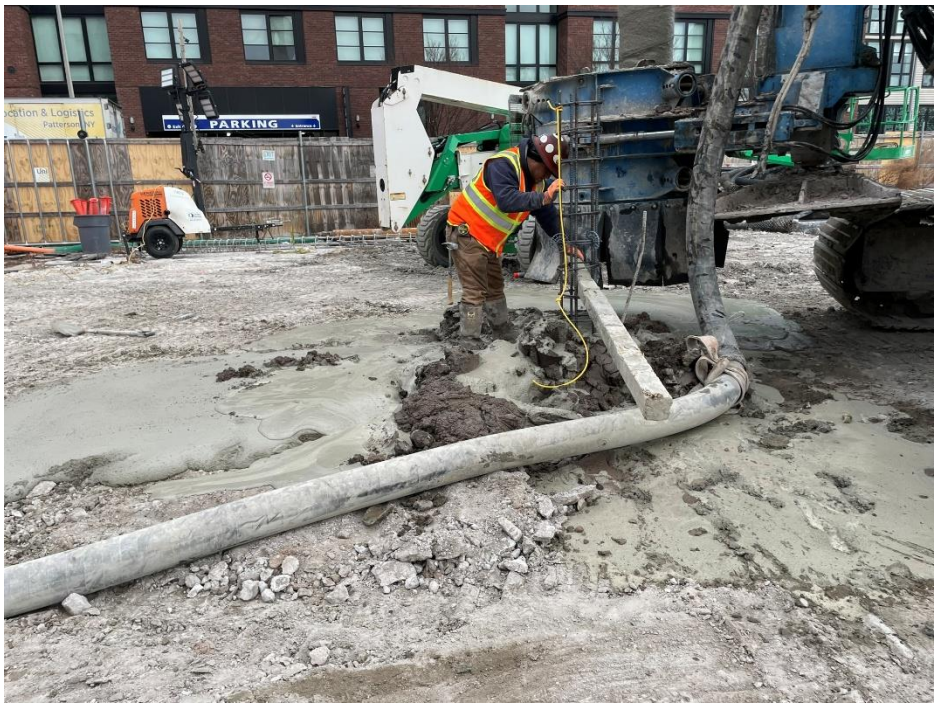



**Photo 2:** New Leaf drilling displacement piles in the northern part of site (facing northeast).

**FIGURE 1 - SITE MAP:**

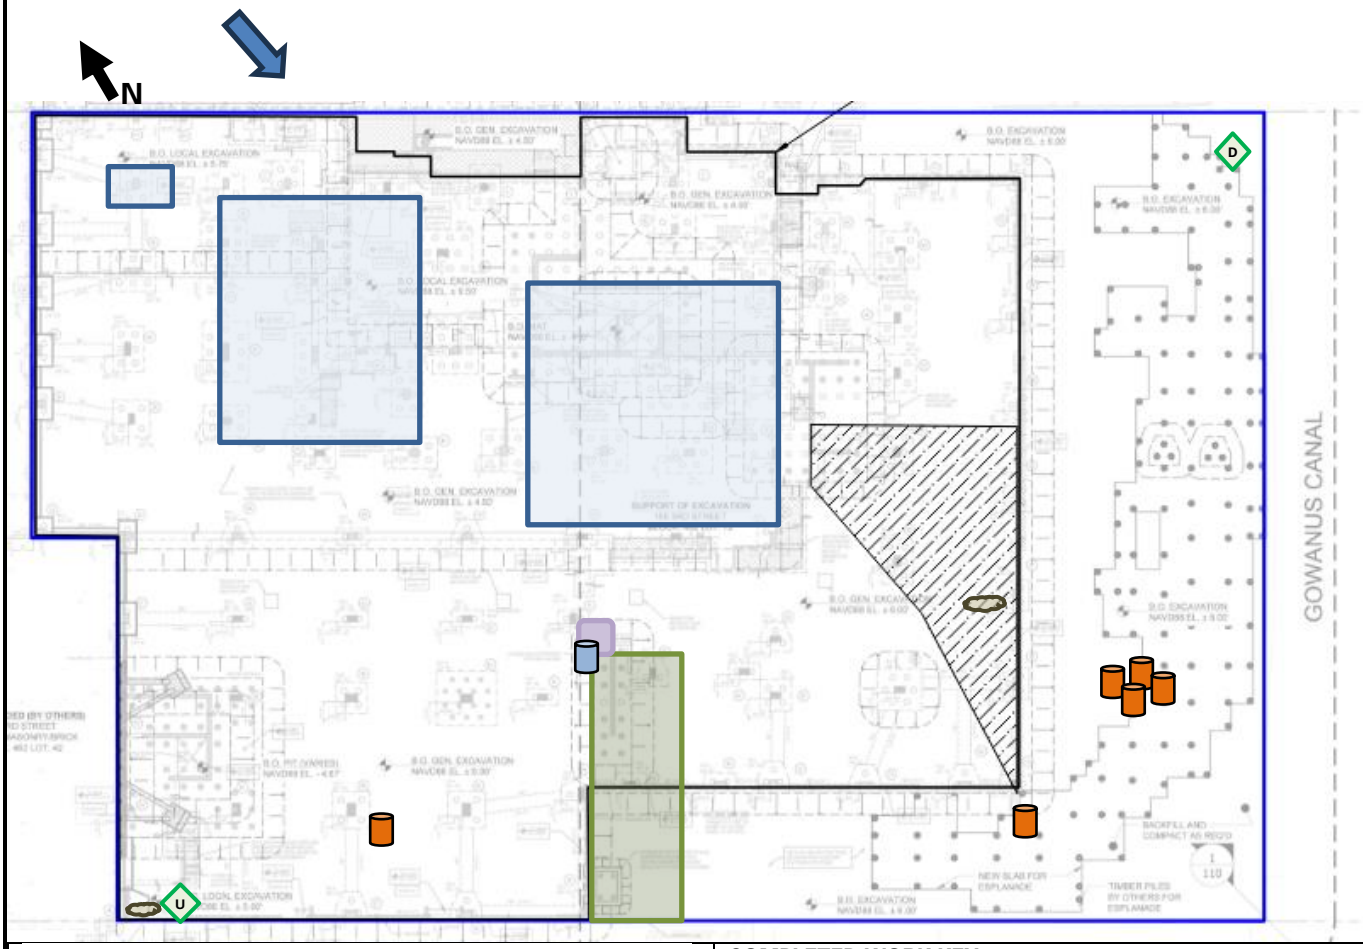


**LEGEND:**


- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)

**COMPLETED WORK KEY**

- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin

Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024

**FIGURE 2 – DISPLACEMENT PILE PLAN:**

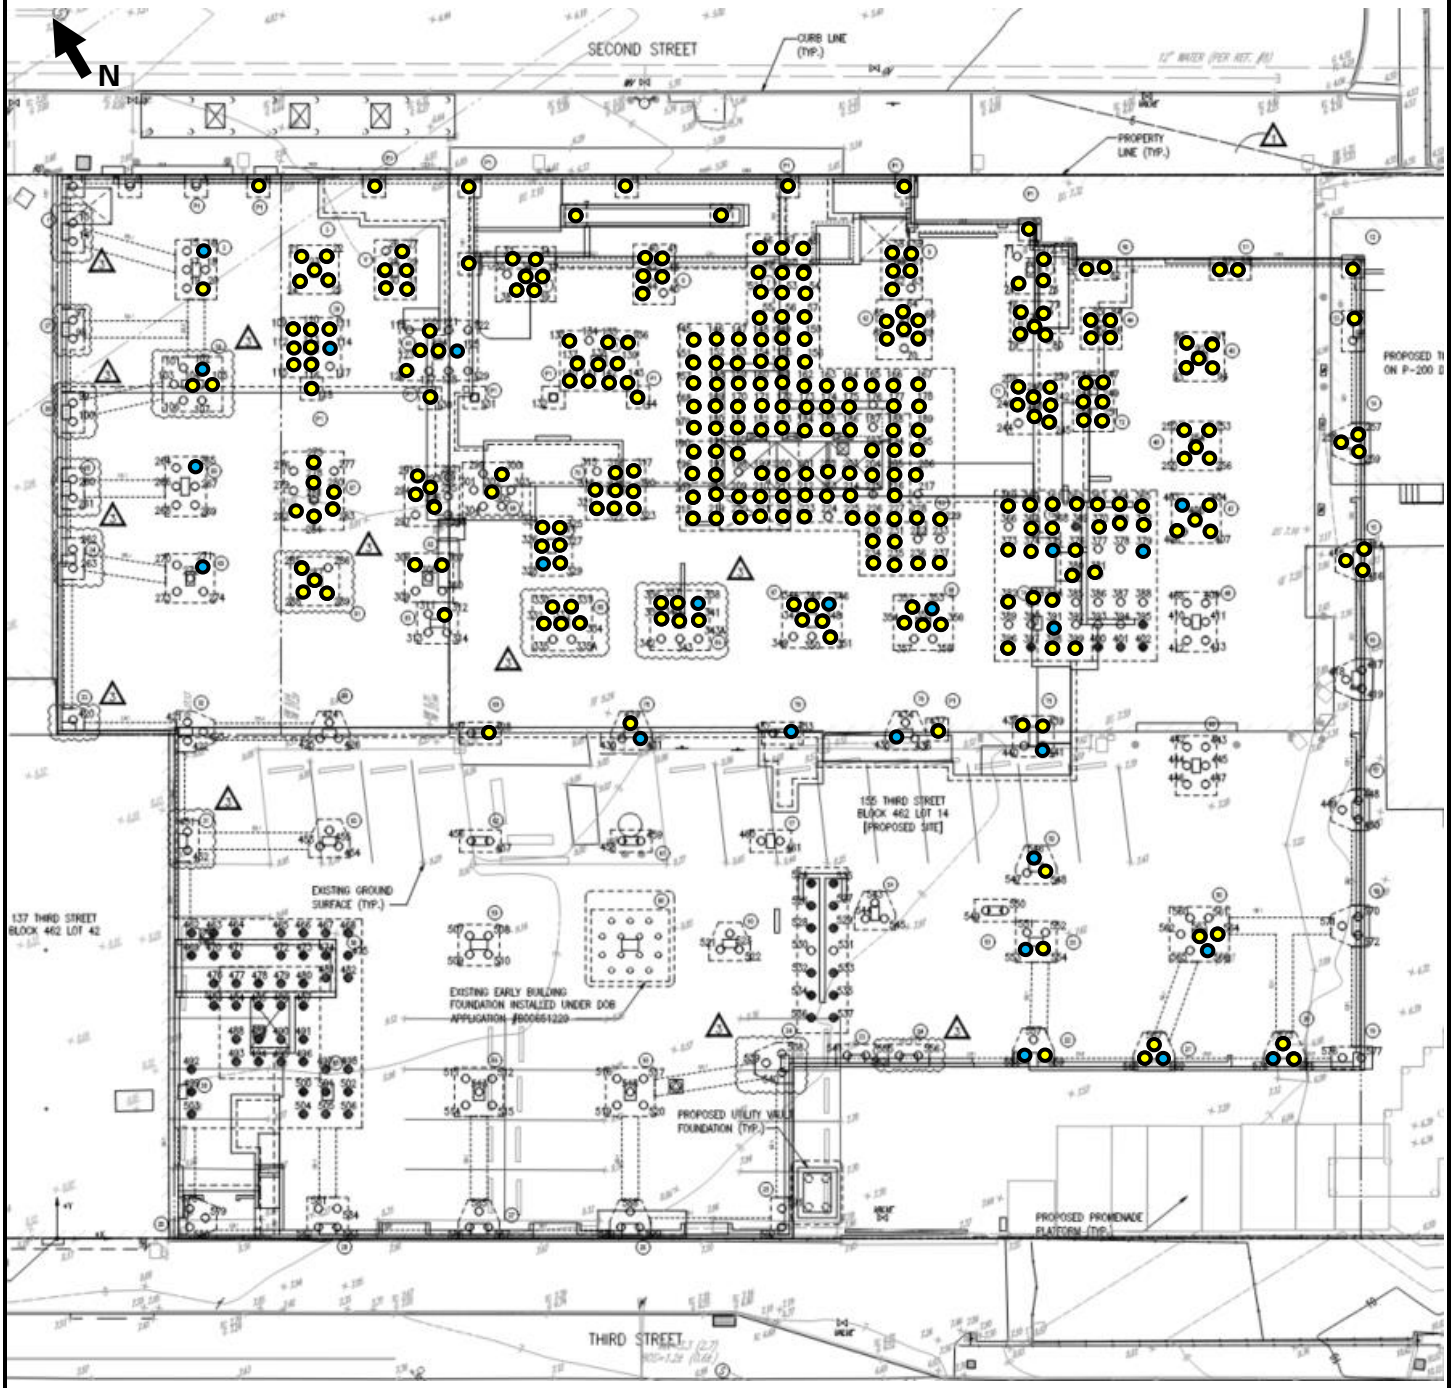


**COMPLETED WORK KEY**


- Approximate Location of Displacement Pile Advanced Today
- Approximate Location of Displacement Pile Advanced Previously


Base map includes Drawing P100 – Full Displacement Pile (FDP) ID, prepared by Mueser Rutledge Consulting Engineers PLLC, dated 8/18/2025


| LANGAN | Site Contribution Report | 170390002 - 155 3rd St Brooklyn | |
|---|---|---|---|
| | | Report Period | |
| | | From: | 01/05/2026 06:00 |
| | | To: | 01/05/2026 17:00 |
| | | PM10 Action Level: | 150 µg/m³ |
| | | VOC Action Level: | 5 ppm |

| Daily Environmental Summary | Temp (°F) | Relative Humidity (%) | Barometer (inHg) | Wind Speed (mph) | Prevailing Wind Direction |
|---|---|---|---|---|---|
| 01/05/2026 | 25.7 - 33.3 | 50.9 - 74.8 | 30.2 - 30.4 | 0.3 - 13.6 | W |


| Daily Monitoring Summary | PM10 (µg/m³) | Time | VOC (ppm) | Time |
|---|---|---|---|---|
| Min Contribution (15 min avg.) - 1/5/2026 | 0.0 | 07:45 | 0.0000 | 07:30 |
| Max Contribution (15 min avg.) - 1/5/2026 | 27.4 | 11:30 | 0.0147 | 10:45 |
| Daily Avg. Contribution (15 min avg.) - 1/5/2026 | 6.3 | - | 0.0058 | - |

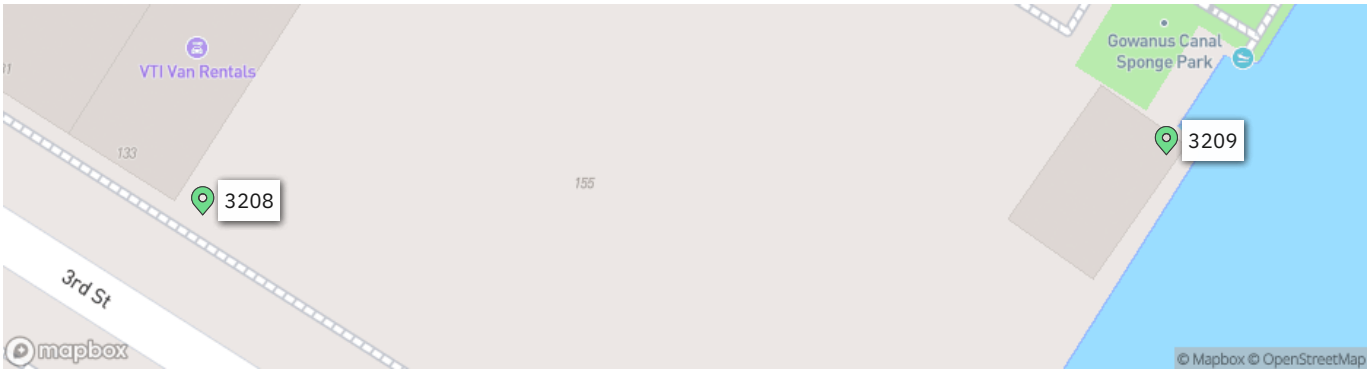

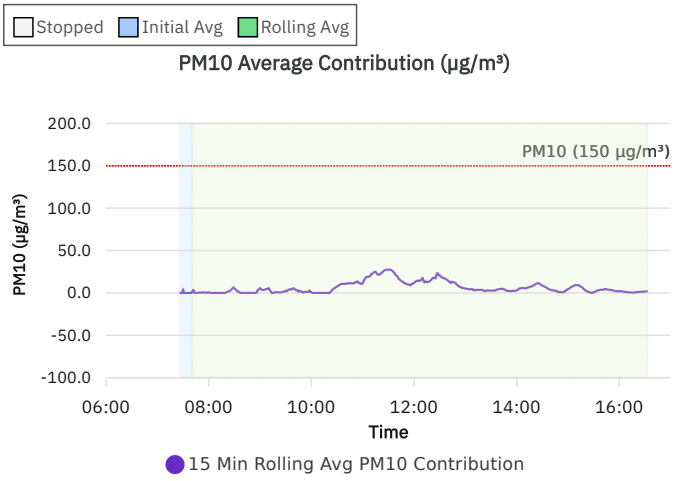


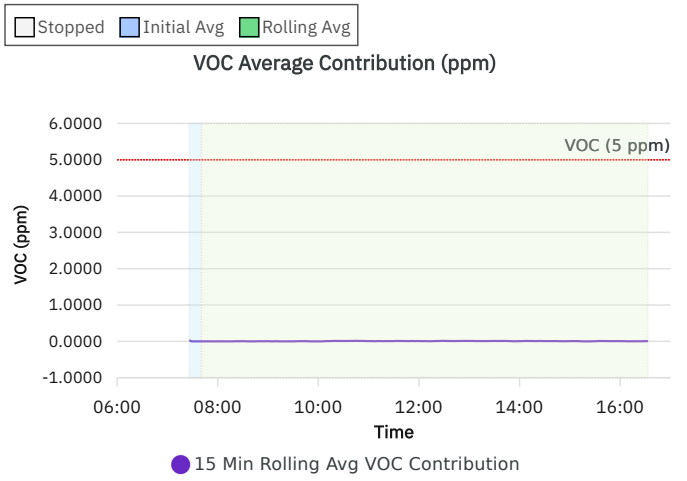
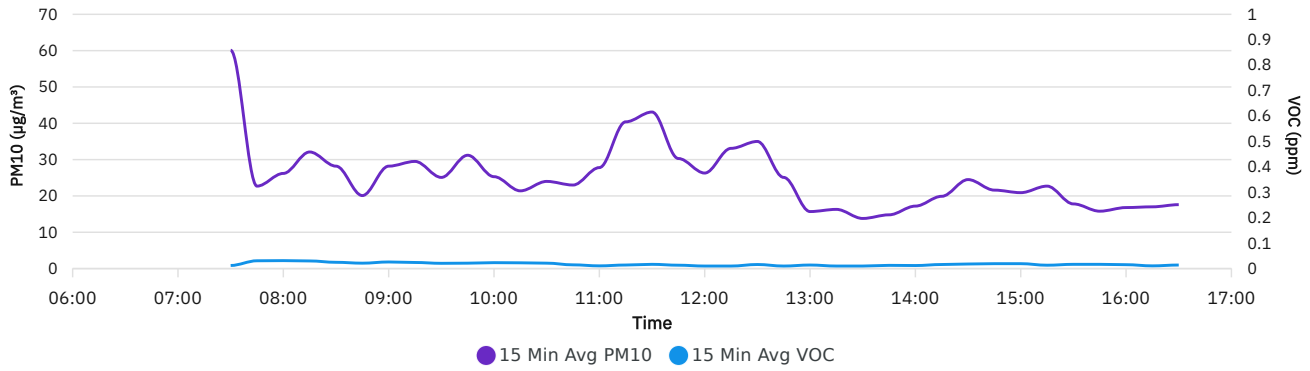
Wind rose (mph)

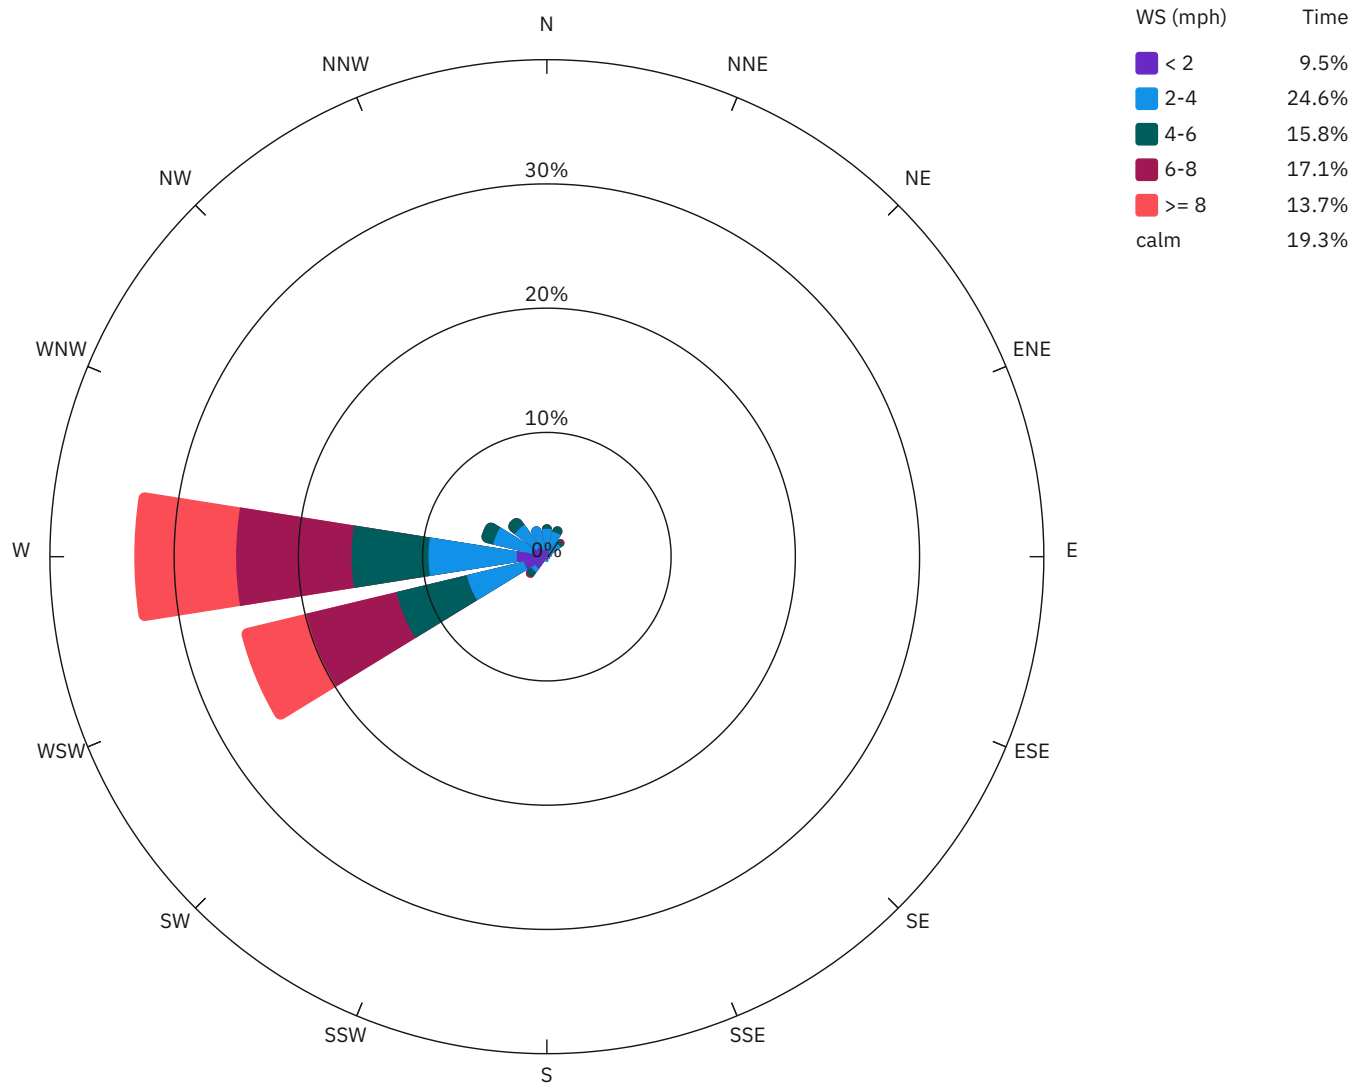


3208

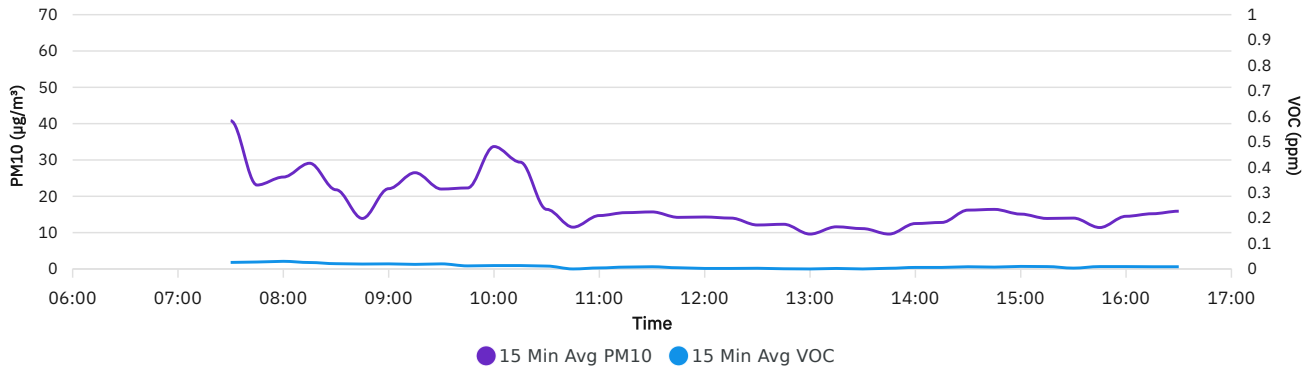

3209


70
60
50
40
30
20
10
0
PM10 (µg/m³)
1
0.9
0.8
0.7
0.6
0.5
0.4
0.3
0.2
0.1
0
VOC (ppm)
06:00
07:00
08:00
09:00
10:00
11:00
12:00
13:00
14:00
15:00
16:00
17:00
Time
15 Min Avg PM10
15 Min Avg VOC

DER-10 Summary: 15 Min Rolling Avg Data

| Date/Time | Average Upwind PM10 (µg/m³) | Average Downwind PM10 (µg/m³) | Average Contribution PM10 (µg/m³) | Average Upwind VOC (ppm) | Average Downwind VOC (ppm) | Average Contribution VOC (ppm) | Wind Speed | Wind Direction |
|---|---|---|---|---|---|---|---|---|
| 1/5/2026 07:30 | 46.4 | 50.1 | 3.7 | 0.0220 | 0.0220 | 0.0000 | 0.6 | N |
| 1/5/2026 07:45 | 23.8 | 22.0 | 0.0 | 0.0293 | 0.0287 | 0.0000 | 0.4 | NW |
| 1/5/2026 08:00 | 25.3 | 26.1 | 0.8 | 0.0300 | 0.0313 | 0.0013 | 1.4 | WSW |
| 1/5/2026 08:15 | 31.4 | 29.7 | 0.0 | 0.0280 | 0.0273 | 0.0000 | 0.2 | WNW |
| 1/5/2026 08:30 | 22.4 | 27.7 | 5.3 | 0.0207 | 0.0247 | 0.0040 | 1.7 | W |
| 1/5/2026 08:45 | 18.9 | 15.0 | 0.0 | 0.0200 | 0.0207 | 0.0007 | 0.3 | NNE |
| 1/5/2026 09:00 | 22.4 | 27.9 | 5.6 | 0.0207 | 0.0253 | 0.0047 | 0.5 | WNW |
| 1/5/2026 09:15 | 28.5 | 27.5 | 0.0 | 0.0220 | 0.0200 | 0.0000 | 0.3 | N |
| 1/5/2026 09:30 | 22.2 | 24.8 | 2.6 | 0.0207 | 0.0200 | 0.0000 | 1.6 | W |
| 1/5/2026 09:45 | 26.0 | 27.5 | 1.5 | 0.0147 | 0.0187 | 0.0040 | 0.4 | W |
| 1/5/2026 10:00 | 29.2 | 29.9 | 0.7 | 0.0180 | 0.0187 | 0.0007 | 0.6 | NNW |
| 1/5/2026 10:15 | 28.5 | 22.3 | 0.0 | 0.0140 | 0.0220 | 0.0080 | 1.6 | W |
| 1/5/2026 10:30 | 16.4 | 24.0 | 7.6 | 0.0113 | 0.0213 | 0.0100 | 5.1 | W |
| 1/5/2026 10:45 | 11.5 | 23.0 | 11.5 | 0.0000 | 0.0147 | 0.0147 | 6.2 | W |
| 1/5/2026 11:00 | 15.4 | 27.1 | 11.7 | 0.0040 | 0.0107 | 0.0067 | 4.8 | WSW |
| 1/5/2026 11:15 | 15.5 | 40.4 | 24.8 | 0.0073 | 0.0140 | 0.0067 | 5.7 | WSW |
| 1/5/2026 11:30 | 15.7 | 43.1 | 27.4 | 0.0087 | 0.0167 | 0.0080 | 6.1 | W |
| 1/5/2026 11:45 | 15.1 | 29.5 | 14.4 | 0.0047 | 0.0133 | 0.0087 | 4.5 | WSW |
| 1/5/2026 12:00 | 14.3 | 26.3 | 11.9 | 0.0020 | 0.0100 | 0.0080 | 4.1 | W |
| 1/5/2026 12:15 | 17.1 | 29.9 | 12.8 | 0.0033 | 0.0087 | 0.0053 | 4.0 | W |
| 1/5/2026 12:30 | 13.3 | 33.9 | 20.6 | 0.0033 | 0.0153 | 0.0120 | 8.4 | W |
| 1/5/2026 12:45 | 12.3 | 25.1 | 12.8 | 0.0007 | 0.0100 | 0.0093 | 7.2 | WSW |
| 1/5/2026 13:00 | 10.1 | 15.3 | 5.2 | 0.0013 | 0.0127 | 0.0113 | 6.6 | W |
| 1/5/2026 13:15 | 12.1 | 15.7 | 3.6 | 0.0020 | 0.0100 | 0.0080 | 5.2 | W |
| 1/5/2026 13:30 | 11.1 | 13.8 | 2.7 | 0.0000 | 0.0100 | 0.0100 | 5.5 | W |
| 1/5/2026 13:45 | 10.0 | 14.4 | 4.4 | 0.0027 | 0.0127 | 0.0100 | 5.5 | W |
| 1/5/2026 14:00 | 13.4 | 16.3 | 2.9 | 0.0067 | 0.0113 | 0.0047 | 3.9 | W |
| 1/5/2026 14:15 | 12.8 | 19.9 | 7.0 | 0.0060 | 0.0160 | 0.0100 | 6.4 | WSW |
| 1/5/2026 14:30 | 16.0 | 24.7 | 8.6 | 0.0100 | 0.0167 | 0.0067 | 6.1 | W |
| 1/5/2026 14:45 | 17.8 | 20.2 | 2.5 | 0.0100 | 0.0167 | 0.0067 | 2.9 | WNW |
| 1/5/2026 15:00 | 15.7 | 20.3 | 4.6 | 0.0113 | 0.0180 | 0.0067 | 4.9 | W |

| Date/Time | Average Upwind PM10 (µg/m³) | Average Downwind PM10 (µg/m³) | Average Contribution PM10 (µg/m³) | Average Upwind VOC (ppm) | Average Downwind VOC (ppm) | Average Contribution VOC (ppm) | Wind Speed | Wind Direction |
|---|---|---|---|---|---|---|---|---|
| 1/5/2026 15:15 | 14.7 | 22.0 | 7.3 | 0.0107 | 0.0120 | 0.0013 | 3.7 | W |
| 1/5/2026 15:30 | 15.4 | 16.4 | 1.0 | 0.0080 | 0.0120 | 0.0040 | 2.4 | NW |
| 1/5/2026 15:45 | 11.4 | 15.8 | 4.4 | 0.0093 | 0.0167 | 0.0073 | 6.2 | W |
| 1/5/2026 16:00 | 14.8 | 16.6 | 1.8 | 0.0093 | 0.0153 | 0.0060 | 4.1 | W |
| 1/5/2026 16:15 | 15.9 | 16.3 | 0.4 | 0.0087 | 0.0107 | 0.0020 | 2.8 | WNW |
| 1/5/2026 16:30 | 15.9 | 17.6 | 1.7 | 0.0087 | 0.0140 | 0.0053 | 5.1 | W |

Air Monitoring Data by Location: 15 Min Avg Data

| Date/Time | 3208 PM10 (µg/m³) | 3208 VOC (ppm) | 3209 PM10 (µg/m³) | 3209 VOC (ppm) | Wind Direction | Wind Speed |
|---|---|---|---|---|---|---|
| 01/05/2026 07:30 | 40.8 | 0.0257 | 60.1 | 0.0122 | N | 0.6 |
| 01/05/2026 07:45 | 23.1 | 0.0273 | 22.7 | 0.0307 | NW | 0.4 |
| 01/05/2026 08:00 | 25.3 | 0.0300 | 26.2 | 0.0313 | WSW | 1.4 |
| 01/05/2026 08:15 | 29.1 | 0.0253 | 32.1 | 0.0300 | WNW | 0.2 |
| 01/05/2026 08:30 | 21.8 | 0.0207 | 28.2 | 0.0247 | W | 1.7 |
| 01/05/2026 08:45 | 13.9 | 0.0193 | 20.1 | 0.0213 | NNE | 0.3 |
| 01/05/2026 09:00 | 22.1 | 0.0200 | 28.2 | 0.0260 | WNW | 0.5 |
| 01/05/2026 09:15 | 26.5 | 0.0180 | 29.5 | 0.0240 | N | 0.3 |
| 01/05/2026 09:30 | 22.0 | 0.0200 | 25.1 | 0.0207 | W | 1.6 |
| 01/05/2026 09:45 | 22.3 | 0.0120 | 31.2 | 0.0213 | W | 0.4 |
| 01/05/2026 10:00 | 33.7 | 0.0133 | 25.3 | 0.0233 | NNW | 0.6 |
| 01/05/2026 10:15 | 29.4 | 0.0133 | 21.4 | 0.0227 | W | 1.6 |
| 01/05/2026 10:30 | 16.4 | 0.0113 | 24.0 | 0.0213 | W | 5.1 |
| 01/05/2026 10:45 | 11.5 | 0.0000 | 23.0 | 0.0147 | W | 6.2 |
| 01/05/2026 11:00 | 14.7 | 0.0040 | 27.8 | 0.0107 | WSW | 4.8 |
| 01/05/2026 11:15 | 15.5 | 0.0073 | 40.4 | 0.0140 | WSW | 5.7 |
| 01/05/2026 11:30 | 15.7 | 0.0087 | 43.1 | 0.0167 | W | 6.1 |
| 01/05/2026 11:45 | 14.2 | 0.0047 | 30.3 | 0.0133 | WSW | 4.5 |
| 01/05/2026 12:00 | 14.3 | 0.0020 | 26.3 | 0.0100 | W | 4.1 |
| 01/05/2026 12:15 | 14.0 | 0.0020 | 33.1 | 0.0100 | W | 4.0 |
| 01/05/2026 12:30 | 12.1 | 0.0027 | 35.0 | 0.0160 | W | 8.4 |
| 01/05/2026 12:45 | 12.3 | 0.0007 | 25.1 | 0.0100 | WSW | 7.2 |
| 01/05/2026 13:00 | 9.6 | 0.0000 | 15.7 | 0.0140 | W | 6.6 |
| 01/05/2026 13:15 | 11.6 | 0.0020 | 16.3 | 0.0100 | W | 5.2 |
| 01/05/2026 13:30 | 11.1 | 0.0000 | 13.8 | 0.0100 | W | 5.5 |
| 01/05/2026 13:45 | 9.6 | 0.0027 | 14.8 | 0.0127 | W | 5.5 |
| 01/05/2026 14:00 | 12.5 | 0.0060 | 17.2 | 0.0120 | W | 3.9 |
| 01/05/2026 14:15 | 12.8 | 0.0060 | 19.9 | 0.0160 | WSW | 6.4 |
| 01/05/2026 14:30 | 16.2 | 0.0087 | 24.5 | 0.0180 | W | 6.1 |
| 01/05/2026 14:45 | 16.4 | 0.0073 | 21.6 | 0.0193 | WNW | 2.9 |
| 01/05/2026 15:00 | 15.1 | 0.0100 | 20.9 | 0.0193 | W | 4.9 |
| 01/05/2026 15:15 | 13.9 | 0.0093 | 22.7 | 0.0133 | W | 3.7 |
| 01/05/2026 15:30 | 14.0 | 0.0033 | 17.8 | 0.0167 | NW | 2.4 |
| 01/05/2026 15:45 | 11.4 | 0.0093 | 15.8 | 0.0167 | W | 6.2 |
| 01/05/2026 16:00 | 14.5 | 0.0093 | 16.8 | 0.0153 | W | 4.1 |
| 01/05/2026 16:15 | 15.2 | 0.0087 | 17.0 | 0.0107 | WNW | 2.8 |
| 01/05/2026 16:30 | 15.9 | 0.0087 | 17.6 | 0.0140 | W | 5.1 |
