SITE OBSERVATION REPORT - RAWP Implementation – Day 123

LANGAN

PROJECT No.:	170390001	**CLIENT:**		**DATE:**	Wednesday, January 7, 2026
PROJECT:	141 3rd Street	Third Street Owner LLC and 155 Third St., LLC		**WEATHER:**	Cloudy, 37 – 48^{0}F Wind: SSE @ 0.5 – 7.1 mph
LOCATION:	Brooklyn, New York			**TIME:**	7:00 a.m. – 4:45 p.m.
BCP SITE ID:	C224336				

EQUIPMENT:
(1) Hyundai HX 520L Hydraulic Excavator
(1) Volvo ECR355EL Hydraulic Excavator
(1) Soilmec SR-75 Drill Rig
(1) Leibherr LRB 355.1 Drill Rig
(1) Cammachio MC 22 Drill Rig
(2) Aeroqual Air Monitoring Stations
(1) MiniRAE 3000 Photoionization Detector
Hand Tools

PRESENT AT SITE:
Langan: Jessie Almont
New Leaf: Jose Gomez
Monadnock Construction, Inc. (Monadnock): Gavin Gawley, Bob Hempfling
Mueser Rutledge Consulting Engineers (MRCE): Joseph Croft, Amani Calderon
WSP: Christopher DiSclafani

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:
Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2023

Site Activities

- New Leaf advanced and installed twenty-four displacement piles (pile ID numbers 2, 17, 127, 101, 270, 545, 555, 551, 565, 378, 440, 390, 427, 295, 309, 303, 335A, 343, 349, and 358 to about 65 feet below grade surface [bgs] and pile ID numbers 525, 528, 536, and 533 to about 70 feet bgs) in the northern, southern and central parts of the site.
    - Less than one cubic yard of drilling spoils was generated during displacement pile installation and were temporarily staged adjacent to the work area. Langan screened the drilling spoils for odors, staining, and organic vapors using a photoionization detector (PID). No evidence of impacts was observed. The drilling spoils will be removed and stockpiled during future excavation around the piles.
    - New Leaf used a tremie pipe to place grout within the displacement piles. Excess grout will be stockpiled and managed as construction and demolition (C&D) debris at a later date.
- A representative from WSP conducted a site visit on behalf of the NYSDEC. No adverse conditions were noted as a result of the site visit.

Sampling

- No samples were collected.

Community Air Monitoring Plan (CAMP) Activities

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on the CAMP summary data sheet appended to the end of this Daily Field Report.

Material Tracking

- No material was exported from the site.
- No material was imported to the site.

Material Import Summary				
Facility	**NYSDEC Approved Quantity**	**Imported**	**Today**	**Total**
Tilcon - Haverstraw Haverstraw, NY ASTM #3 Virgin Stone (1.5-Inch)	400 CY (560 tons)	**No. Loads**	0	**6**
		Quantity (tons)	0	**130.94**
Impact Materials Jersey City (IMJC) Jersey City, NJ 0.75-inch Stone	2,000 CY (2,800 tons)	**No. Loads**	0	**0**
		Quantity (tons)	0	**0**
IMJC Jersey City, NJ 1.5-inch Stone	400 CY (560 tons)	**No. Loads**	0	**2**
		Quantity (tons)	0	**49.65**

Material Export Summary				
Facility	**Approved Quantity**	**Exported**	**Today**	**Total**
Clean Earth of Carteret (CEC) Carteret, NJ Elevated Soil/Fill	9,857 CY (13,800 tons)	**No. Loads**	0	**72**
		Quantity (CY)	0	**1,440**
Clean Earth of New Castle (CENC) New Castle, DE Non-Hazardous Contaminated Soil/Urban Fill	3,571 CY (5,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Atlantic County Utilities Authority (ACUA) Egg Harbor Township, NJ Non-Hazardous Contaminated Soil/Urban Fill	714 CY (1,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Clean Earth of North Jersey (CENJ) Kearny, NJ Hazardous Lead	107 CY (150 tons)	**No. Loads**	0	**2**
		Quantity (CY)	0	**40**

Drums

- One 55-gallon drum containing purged groundwater and Dense Non-Aqueous Phase Liquid (DNAPL) is staged in the southern part of the site.
- One 55-gallon drum containing purged groundwater and DNAPL is staged in the western part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- Two 55-gallon drums containing personal protective equipment (PPE) are staged in the southern part of the site.
- Two 55-gallon drums containing drill cuttings are staged in the southern part of the site.

Anticipated Activities

- New Leaf will continue drilling displacement piles.

SITE PHOTOGRAPHS:



Photo 1: New Leaf drilling displacement piles in the central part of site (facing north).


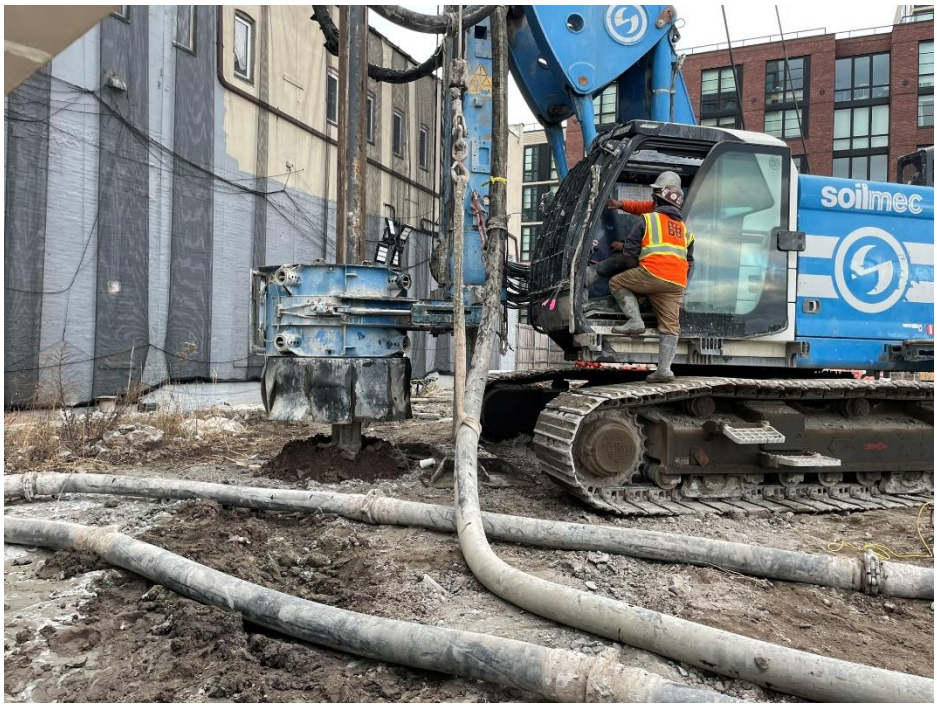


Photo 2: New Leaf drilling displacement piles in the northern part of site (facing north).

FIGURE 1 - SITE MAP:

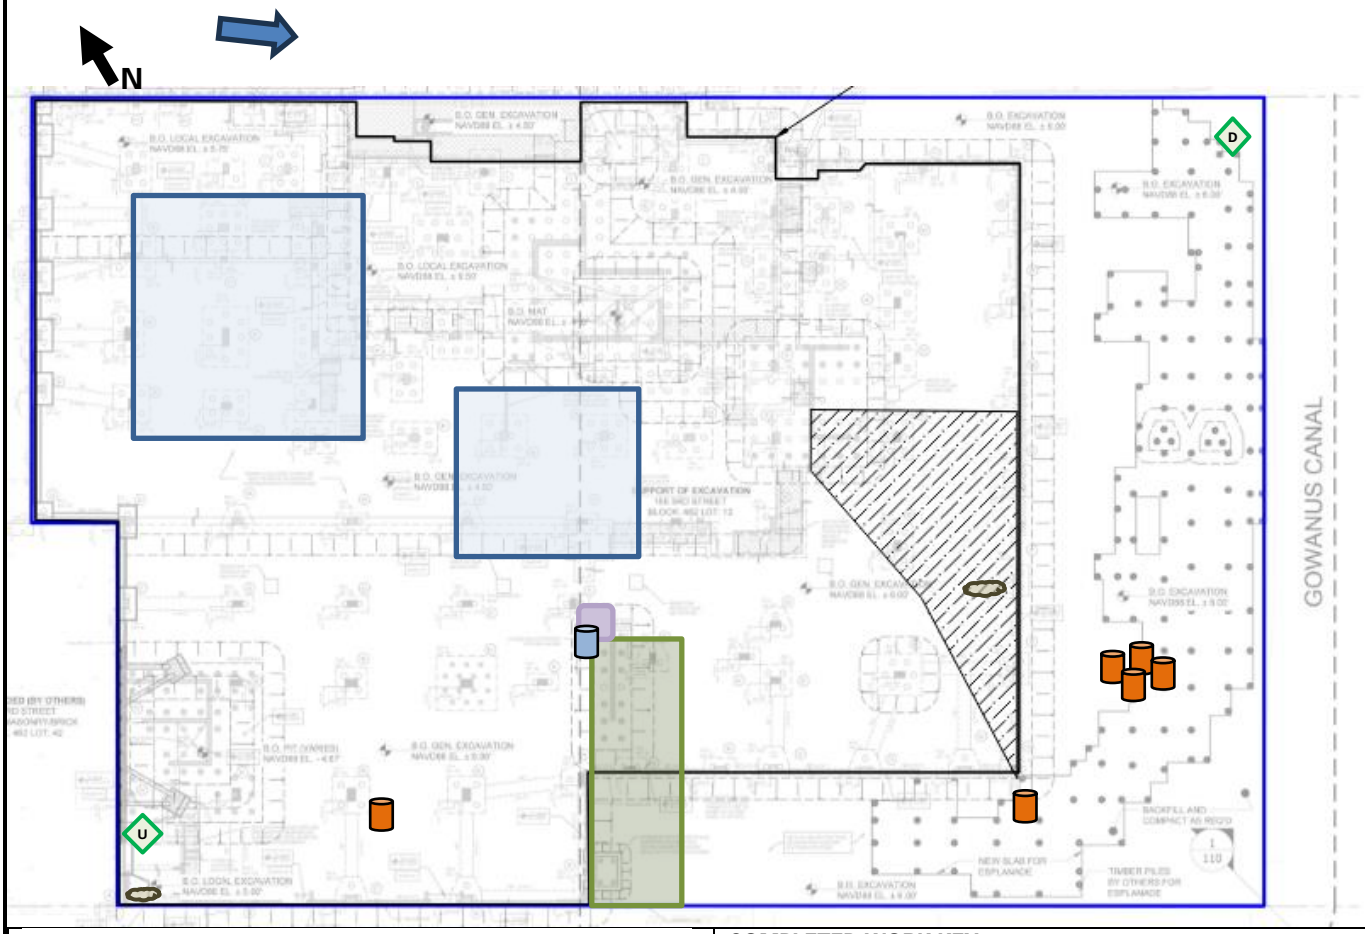

LEGEND:


- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)

COMPLETED WORK KEY

- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin

Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024

FIGURE 2 – DISPLACEMENT PILE PLAN:

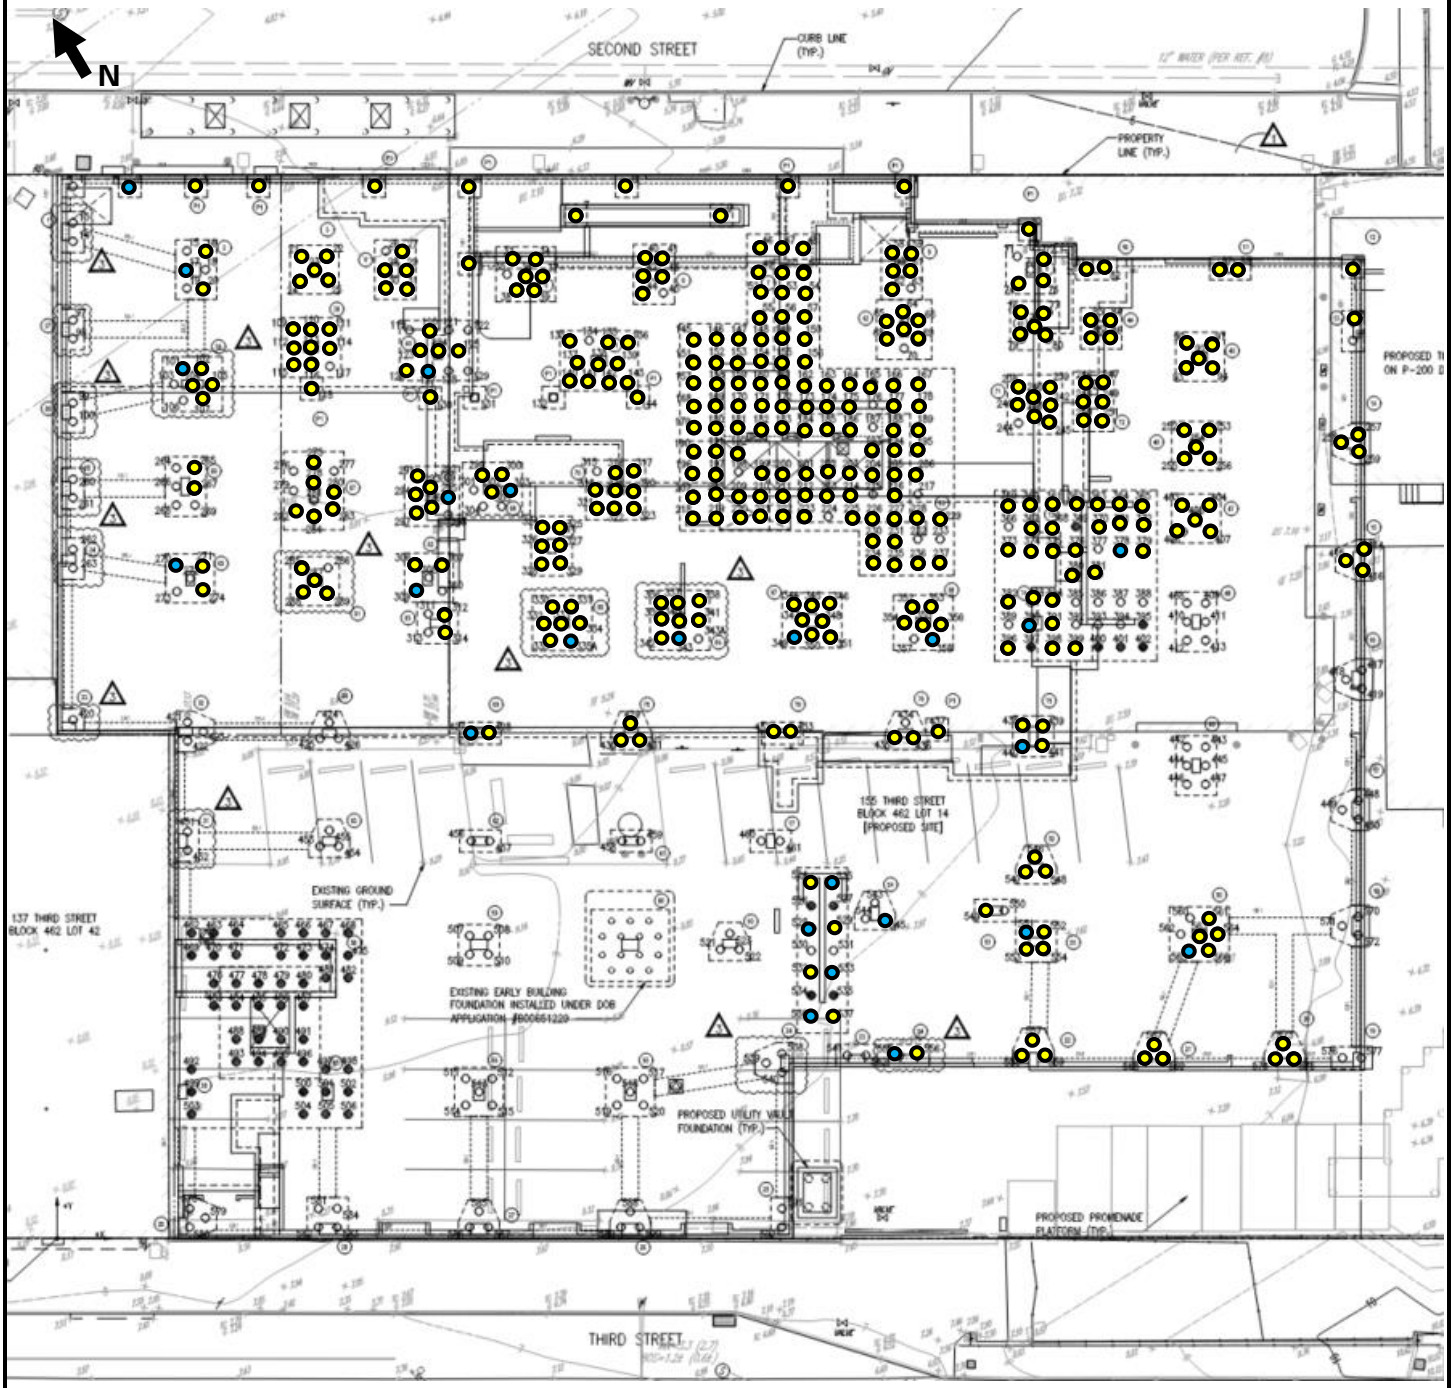

COMPLETED WORK KEY


- Approximate Location of Displacement Pile Advanced Today
- Approximate Location of Displacement Pile Advanced Previously


Base map includes Drawing P100 – Full Displacement Pile (FDP) ID, prepared by Mueser Rutledge Consulting Engineers PLLC, dated 8/18/2025


LANGAN	Site Contribution Report	170390002 - 155 3rd St Brooklyn	
		Report Period	
		From:	01/07/2026 06:00
		To:	01/07/2026 17:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
01/07/2026	35.6 - 54.1	50.6 - 95.9	29.8 - 29.9	0.5 - 7.1	NNW


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 1/7/2026	0.0	08:15	0.0000	09:30
Max Contribution (15 min avg.) - 1/7/2026	7.2	10:15	0.0080	10:00
Daily Avg. Contribution (15 min avg.) - 1/7/2026	0.7	-	0.0022	-

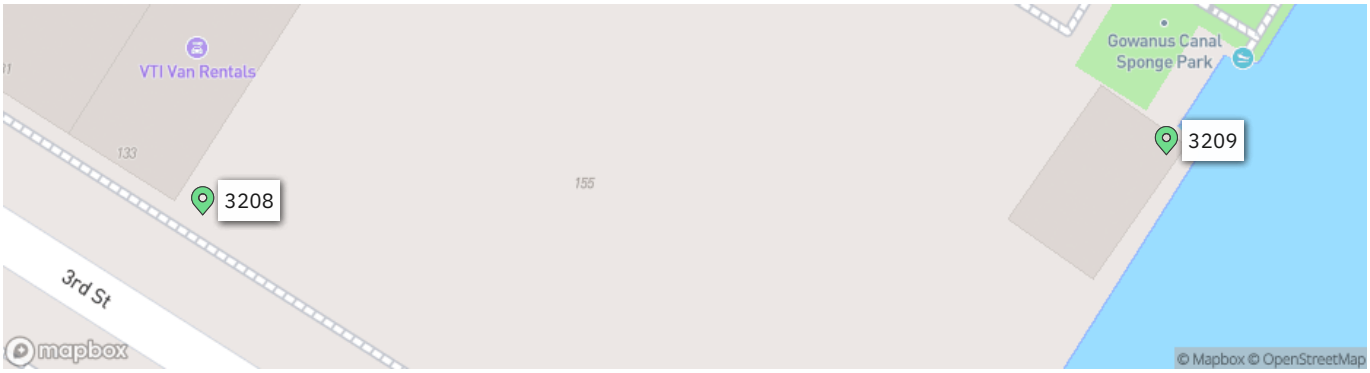

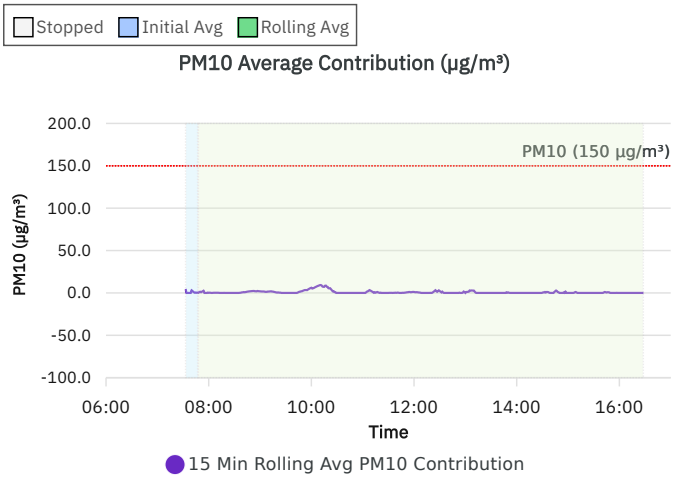


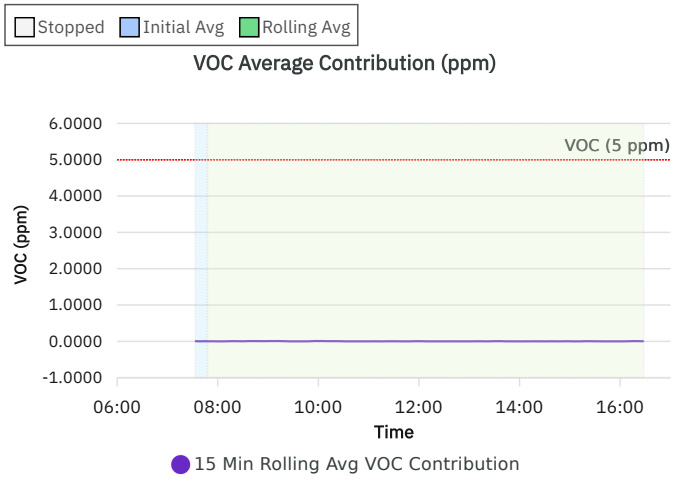


Wind rose (mph)

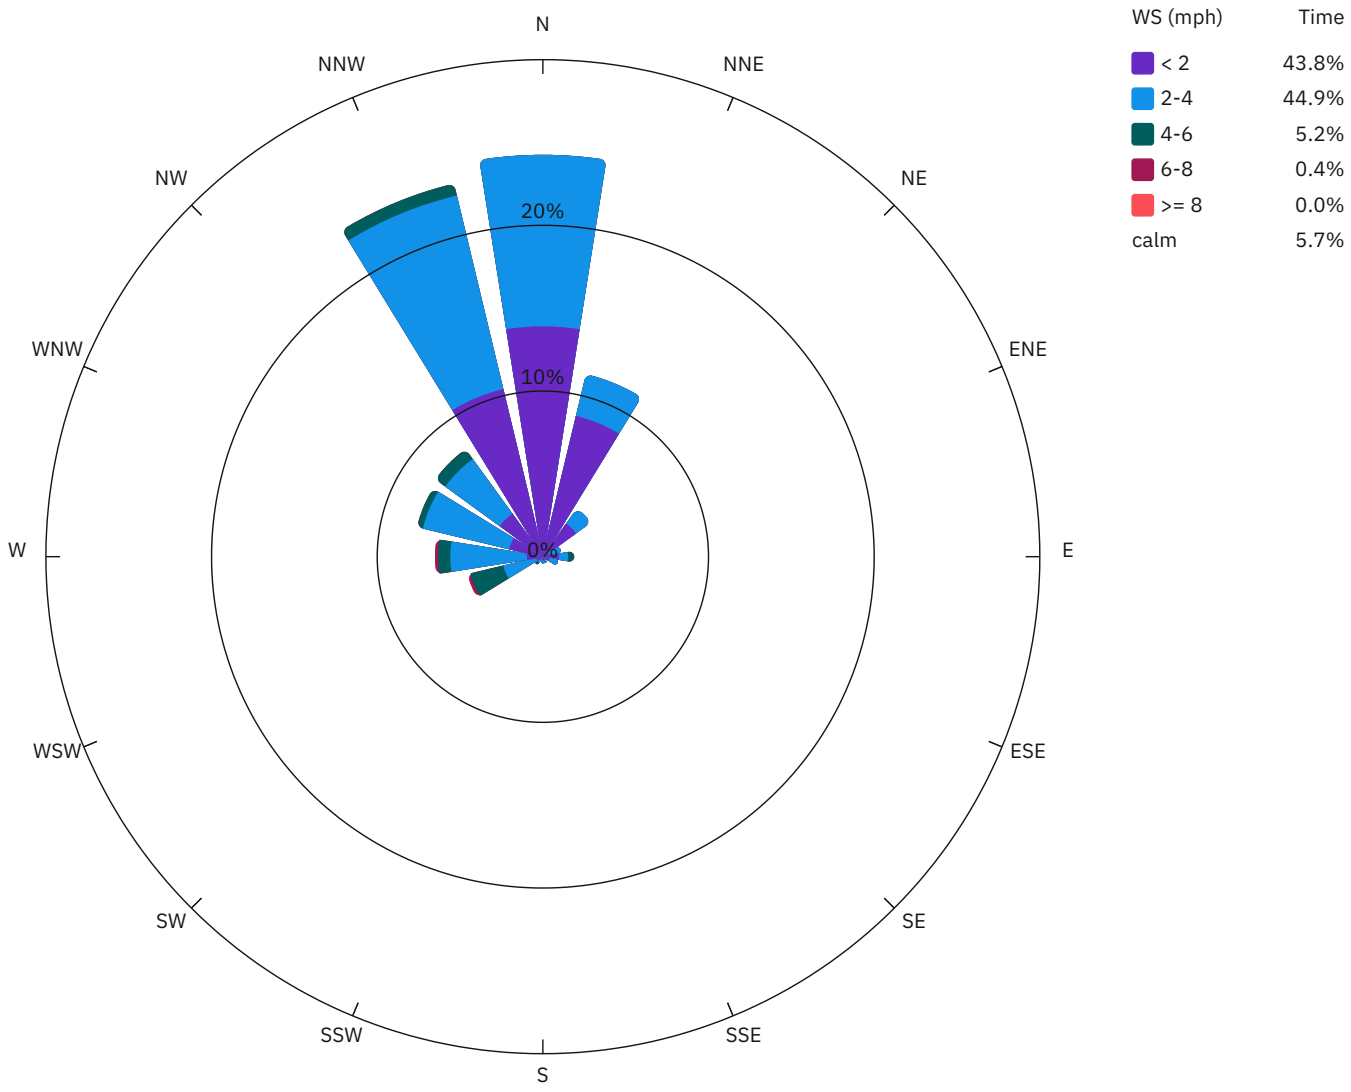

3208

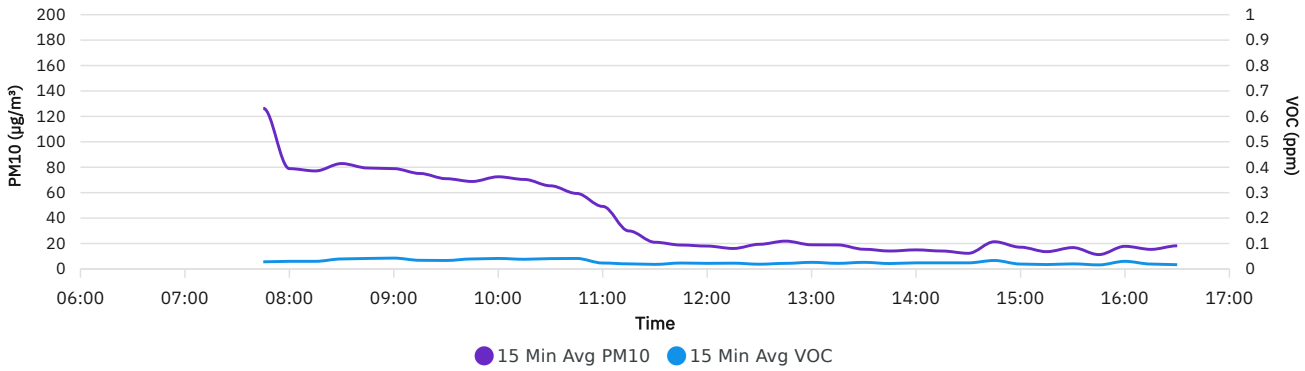

3209

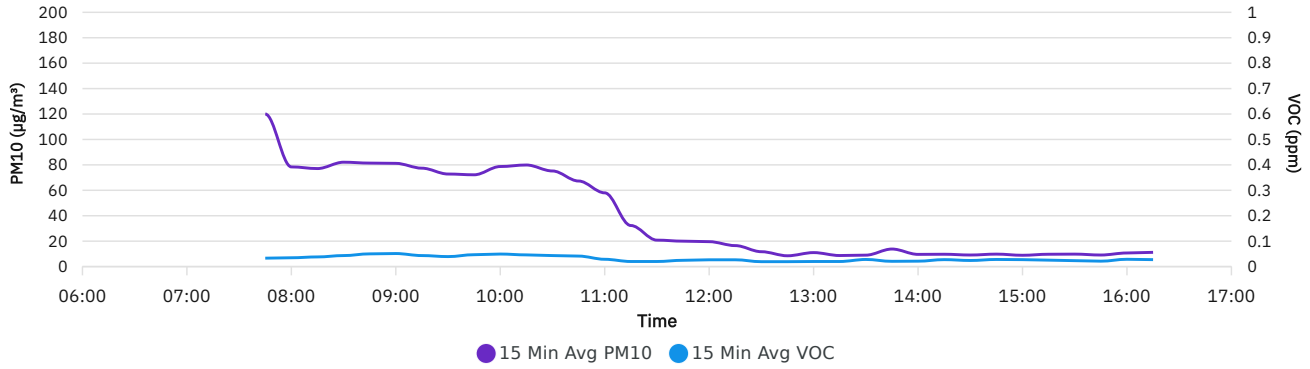
200
180
160
140
120
100
80
60
40
20
0
PM10 (µg/m³)
1
0.9
0.8
0.7
0.6
0.5
0.4
0.3
0.2
0.1
0
VOC (ppm)
06:00
07:00
08:00
09:00
10:00
11:00
12:00
13:00
14:00
15:00
16:00
17:00
Time
15 Min Avg PM10
15 Min Avg VOC

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
1/7/2026 07:45	120.9	121.4	0.5	0.0300	0.0331	0.0031	1.0	NW
1/7/2026 08:00	78.6	78.7	0.1	0.0320	0.0327	0.0007	1.0	NNW
1/7/2026 08:15	77.2	77.1	0.0	0.0313	0.0367	0.0053	1.2	NW
1/7/2026 08:30	82.6	82.4	0.0	0.0407	0.0420	0.0013	1.5	NW
1/7/2026 08:45	79.7	81.1	1.5	0.0420	0.0493	0.0073	1.8	WNW
1/7/2026 09:00	79.1	81.0	1.9	0.0433	0.0507	0.0073	1.8	W
1/7/2026 09:15	75.4	77.1	1.6	0.0353	0.0420	0.0067	1.5	NW
1/7/2026 09:30	72.3	71.5	0.0	0.0367	0.0360	0.0000	1.2	N
1/7/2026 09:45	70.0	70.9	0.9	0.0427	0.0433	0.0007	2.0	WNW
1/7/2026 10:00	72.5	78.7	6.1	0.0413	0.0493	0.0080	3.7	W
1/7/2026 10:15	71.6	78.7	7.2	0.0393	0.0447	0.0053	2.6	W
1/7/2026 10:30	71.2	69.4	0.0	0.0413	0.0427	0.0013	1.4	NNW
1/7/2026 10:45	66.3	60.4	0.0	0.0413	0.0413	0.0000	1.6	NNE
1/7/2026 11:00	54.3	52.9	0.0	0.0267	0.0253	0.0000	1.7	N
1/7/2026 11:15	31.0	31.2	0.3	0.0200	0.0200	0.0000	2.8	NNW
1/7/2026 11:30	20.8	20.9	0.0	0.0180	0.0200	0.0020	2.5	NNW
1/7/2026 11:45	19.5	19.4	0.0	0.0240	0.0240	0.0000	1.9	NNW
1/7/2026 12:00	18.3	19.3	1.1	0.0220	0.0267	0.0047	2.0	N
1/7/2026 12:15	16.3	16.3	0.0	0.0260	0.0233	0.0000	2.0	N
1/7/2026 12:30	14.5	16.7	2.2	0.0200	0.0180	0.0000	1.9	NE
1/7/2026 12:45	16.6	13.7	0.0	0.0207	0.0207	0.0000	2.3	NNW
1/7/2026 13:00	15.0	15.0	0.0	0.0240	0.0220	0.0000	2.1	N
1/7/2026 13:15	14.3	13.3	0.0	0.0200	0.0220	0.0020	2.2	N
1/7/2026 13:30	12.9	11.5	0.0	0.0247	0.0293	0.0047	1.6	NNW
1/7/2026 13:45	14.3	13.6	0.0	0.0207	0.0213	0.0007	2.3	NNW
1/7/2026 14:00	13.4	11.2	0.0	0.0233	0.0220	0.0000	2.0	NNW
1/7/2026 14:15	13.4	10.4	0.0	0.0247	0.0267	0.0020	2.2	NNW
1/7/2026 14:30	10.6	10.8	0.2	0.0240	0.0240	0.0000	1.3	N
1/7/2026 14:45	14.6	16.6	2.0	0.0307	0.0307	0.0000	1.3	N
1/7/2026 15:00	14.5	11.5	0.0	0.0220	0.0247	0.0027	1.8	N
1/7/2026 15:15	12.0	11.3	0.0	0.0207	0.0220	0.0013	0.8	NNW

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
1/7/2026 15:30	15.1	11.4	0.0	0.0207	0.0227	0.0020	1.8	NW
1/7/2026 15:45	9.9	10.4	0.5	0.0200	0.0173	0.0000	0.8	NNE
1/7/2026 16:00	15.2	13.3	0.0	0.0320	0.0267	0.0000	0.4	NW
1/7/2026 16:15	14.2	12.4	0.0	0.0200	0.0267	0.0067	1.5	NNW
1/7/2026 16:30							2.5	NNW

Air Monitoring Data by Location: 15 Min Avg Data

Date/Time	3208 PM10 (µg/m³)	3208 VOC (ppm)	3209 PM10 (µg/m³)	3209 VOC (ppm)	Wind Direction	Wind Speed
01/07/2026 07:45	126.4	0.0280	120.0	0.0331	NW	1.0
01/07/2026 08:00	78.9	0.0300	78.4	0.0347	NNW	1.0
01/07/2026 08:15	77.1	0.0300	77.1	0.0380	NW	1.2
01/07/2026 08:30	82.9	0.0393	82.1	0.0433	NW	1.5
01/07/2026 08:45	79.4	0.0413	81.4	0.0500	WNW	1.8
01/07/2026 09:00	78.9	0.0427	81.2	0.0513	W	1.8
01/07/2026 09:15	75.1	0.0340	77.4	0.0433	NW	1.5
01/07/2026 09:30	71.0	0.0333	72.8	0.0393	N	1.2
01/07/2026 09:45	68.8	0.0393	72.2	0.0467	WNW	2.0
01/07/2026 10:00	72.5	0.0413	78.7	0.0493	W	3.7
01/07/2026 10:15	70.4	0.0380	79.9	0.0460	W	2.6
01/07/2026 10:30	65.4	0.0407	75.2	0.0433	NNW	1.4
01/07/2026 10:45	59.4	0.0413	67.3	0.0413	NNE	1.6
01/07/2026 11:00	49.2	0.0233	58.0	0.0287	N	1.7
01/07/2026 11:15	29.9	0.0200	32.3	0.0200	NNW	2.8
01/07/2026 11:30	21.0	0.0180	20.8	0.0200	NNW	2.5
01/07/2026 11:45	18.8	0.0233	20.0	0.0247	NNW	1.9
01/07/2026 12:00	18.0	0.0220	19.6	0.0267	N	2.0
01/07/2026 12:15	16.1	0.0227	16.5	0.0267	N	2.0
01/07/2026 12:30	19.4	0.0187	11.7	0.0193	NE	1.9
01/07/2026 12:45	21.9	0.0220	8.5	0.0193	NNW	2.3
01/07/2026 13:00	19.0	0.0260	11.0	0.0200	N	2.1
01/07/2026 13:15	18.9	0.0220	8.7	0.0200	N	2.2
01/07/2026 13:30	15.5	0.0260	9.0	0.0280	NNW	1.6
01/07/2026 13:45	14.1	0.0213	13.8	0.0207	NNW	2.3
01/07/2026 14:00	15.0	0.0240	9.6	0.0213	NNW	2.0
01/07/2026 14:15	14.1	0.0240	9.7	0.0273	NNW	2.2
01/07/2026 14:30	12.3	0.0240	9.1	0.0240	N	1.3
01/07/2026 14:45	21.4	0.0333	9.8	0.0280	N	1.3
01/07/2026 15:00	17.1	0.0193	8.9	0.0273	N	1.8
01/07/2026 15:15	13.6	0.0173	9.7	0.0253	NNW	0.8
01/07/2026 15:30	16.8	0.0200	9.8	0.0233	NW	1.8
01/07/2026 15:45	11.3	0.0160	9.1	0.0213	NNE	0.8
01/07/2026 16:00	17.8	0.0300	10.7	0.0287	NW	0.4
01/07/2026 16:15	15.4	0.0193	11.2	0.0273	NNW	1.5
01/07/2026 16:30	18.2	0.0167			NNW	2.5
