SITE OBSERVATION REPORT - RAWP Implementation – Day 129

LANGAN

PROJECT No.:	170390001	**CLIENT:**		**DATE:**	Thursday, January 15, 2026
PROJECT:	141 3rd Street	Third Street Owner LLC and 155 Third St., LLC		**WEATHER:**	Partly Cloudy, 24 – 45^{0}F Wind: SW @ 1.1 – 5.6 mph
LOCATION:	Brooklyn, New York			**TIME:**	7:00 a.m. – 4:45 p.m.
BCP SITE ID:	C224336				

EQUIPMENT:
(1) Hyundai HX 520L Hydraulic Excavator
(1) Volvo ECR355EL Hydraulic Excavator
(1) Soilmec SR-75 Drill Rig
(1) Leibherr LRB 355.1 Drill Rig
(1) Cammachio MC 22 Drill Rig
(1) FES Drill Rig
(2) Aeroqual Air Monitoring Stations
(1) MiniRAE 3000 Photoionization Detector

PRESENT AT SITE:
Langan: Jessie Almont
New Leaf: Joe Sullivan, Jose Gomez
Monadnock Construction, Inc. (Monadnock): Gavin Gawley, Bob Hempfling
Mueser Rutledge Consulting Engineers (MRCE): Joseph Croft, Amani Calderon
WSP: Eddy Nunez

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:
Langan was onsite to document implementation of the New York State Department of Environmental Conservation (NYSDEC)-approved Remedial Action Work Plan (RAWP) dated 12 December 2023

Site Activities

- New Leaf advanced and installed sixteen displacement piles (pile ID numbers 13, 98, 100, 261, 263, 507, 292, 305, 276, 313, 523, 458, 457, 426, and 268 to about 65 feet below grade surface [bgs] and pile ID number 501 to about 70 feet bgs) in the northern and southwestern parts of the site.
    - Less than one cubic yard of drilling spoils was generated during displacement pile installation and were temporarily staged adjacent to the work area. Langan screened the drilling spoils for odors, staining, and organic vapors using a photoionization detector (PID). No evidence of impacts was observed. The drilling spoils will be removed and stockpiled during future excavation around the piles.
    - New Leaf used a tremie pipe to place grout within the displacement piles. Excess grout will be stockpiled and managed as construction and demolition (C&D) debris at a later date.
- A representative from WSP conducted a site visit on behalf of the NYSDEC. No adverse conditions were noted as a result of the site visit.

Sampling

- No samples were collected.

Community Air Monitoring Plan (CAMP) Activities

- Langan performed continuous air monitoring for volatile organic compounds (VOC) and particulate matter smaller than 10 microns in diameter (PM10) using two perimeter air monitoring stations at upwind and downwind locations. The PM10 and VOC action levels were not exceeded during the monitoring period. Recorded air monitoring data is presented on the CAMP summary data sheet appended to the end of this Daily Field Report.

Material Tracking

- No material was exported from the site.
- No material was imported to the site.

Material Import Summary				
Facility	**NYSDEC Approved Quantity**	**Imported**	**Today**	**Total**
Tilcon - Haverstraw Haverstraw, NY ASTM #3 Virgin Stone (1.5-Inch)	400 CY (560 tons)	**No. Loads**	0	**7**
		Quantity (tons)	0	**153.36**
Impact Materials Jersey City (IMJC) Jersey City, NJ 0.75-inch Stone	2,000 CY (2,800 tons)	**No. Loads**	0	**0**
		Quantity (tons)	0	**0**
IMJC Jersey City, NJ	400 CY (560 tons)	**No. Loads**	0	**2**
Material Export Summary				
Facility	**Approved Quantity**	**Exported**	**Today**	**Total**
Clean Earth of Carteret (CEC) Carteret, NJ Elevated Soil/Fill	9,857 CY (13,800 tons)	**No. Loads**	0	**72**
		Quantity (CY)	0	**1,440**
Clean Earth of New Castle (CENC) New Castle, DE Non-Hazardous Contaminated Soil/Urban Fill	3,571 CY (5,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Atlantic County Utilities Authority (ACUA) Egg Harbor Township, NJ Non-Hazardous Contaminated Soil/Urban Fill	714 CY (1,000 tons)	**No. Loads**	0	**0**
		Quantity (CY)	0	**0**
Clean Earth of North Jersey (CENJ) Kearny, NJ Hazardous Lead	107 CY (150 tons)	**No. Loads**	0	**2**
		Quantity (CY)	0	**40**

Drums

- One 55-gallon drum containing purged groundwater and Dense Non-Aqueous Phase Liquid (DNAPL) is staged in the southern part of the site.
- One 55-gallon drum containing purged groundwater and DNAPL is staged in the western part of the site.
- One 55-gallon drum containing truck wash water is staged in the central part of the site.
- Two 55-gallon drums containing personal protective equipment (PPE) are staged in the southern part of the site.
- Two 55-gallon drums containing drill cuttings are staged in the southern part of the site.

Anticipated Activities

- New Leaf will continue drilling displacement piles.

SITE PHOTOGRAPHS:


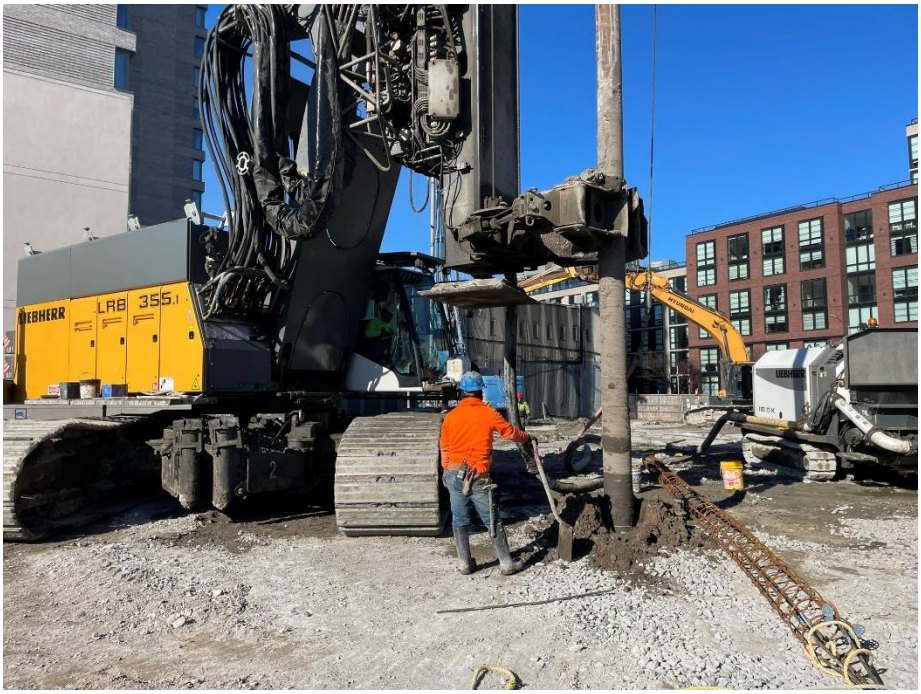


Photo 1: New Leaf drilling displacement piles in the southwestern part of site (facing north).



Photo 2: New Leaf drilling displacement piles in the northern part of site (facing north).

FIGURE 1 - SITE MAP:

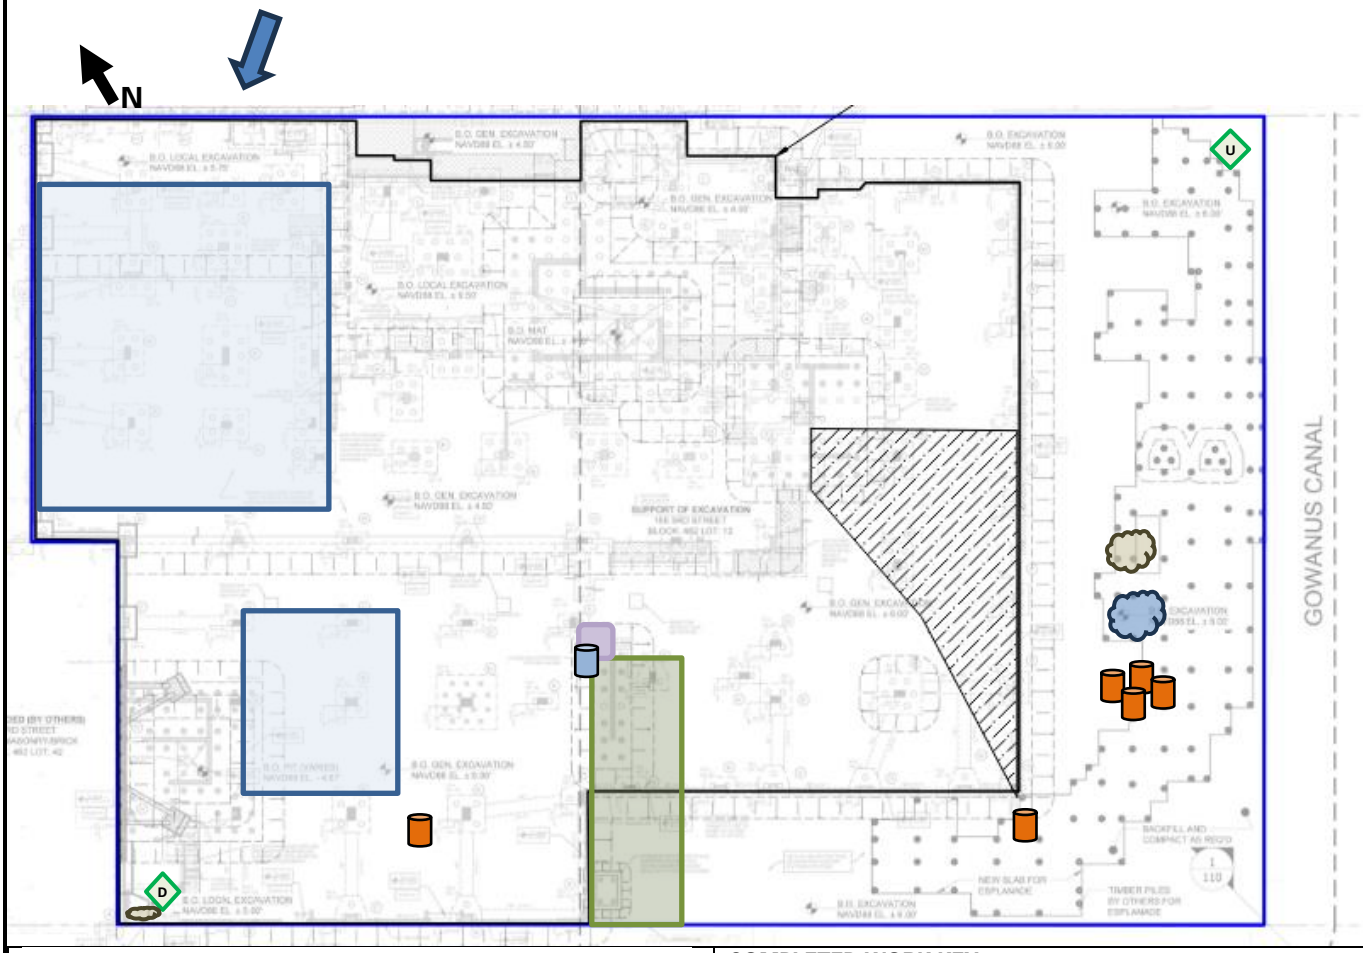

LEGEND:


- APPROXIMATE SITE BOUNDARY
- PROPOSED BUILDING FOOTPRINT
- APPROXIMATE PROPOSED EXTENT OF ISS AREA TO BE EXCAVATED TO 4 FEET BGS (EL. 3.5± FEET NAVD88)

COMPLETED WORK KEY

- Approximate work area
- Approximate location of upwind CAMP station
- Approximate location of downwind CAMP station
- Approximate location of drum
- Approximate location of truck wash drum
- Approximate wind direction
- Stockpiled soil/fill
- Stockpiled C&D debris
- Stockpiled imported stone
- Temporary stabilized construction entrance
- Truck wash catch basin

Base map includes Figure 5 – Pre-ISS Excavation Plan from the NYSDEC-approved RDD for ISS, prepared by Langan Engineering, dated 4/5/2024

FIGURE 2 – DISPLACEMENT PILE PLAN:

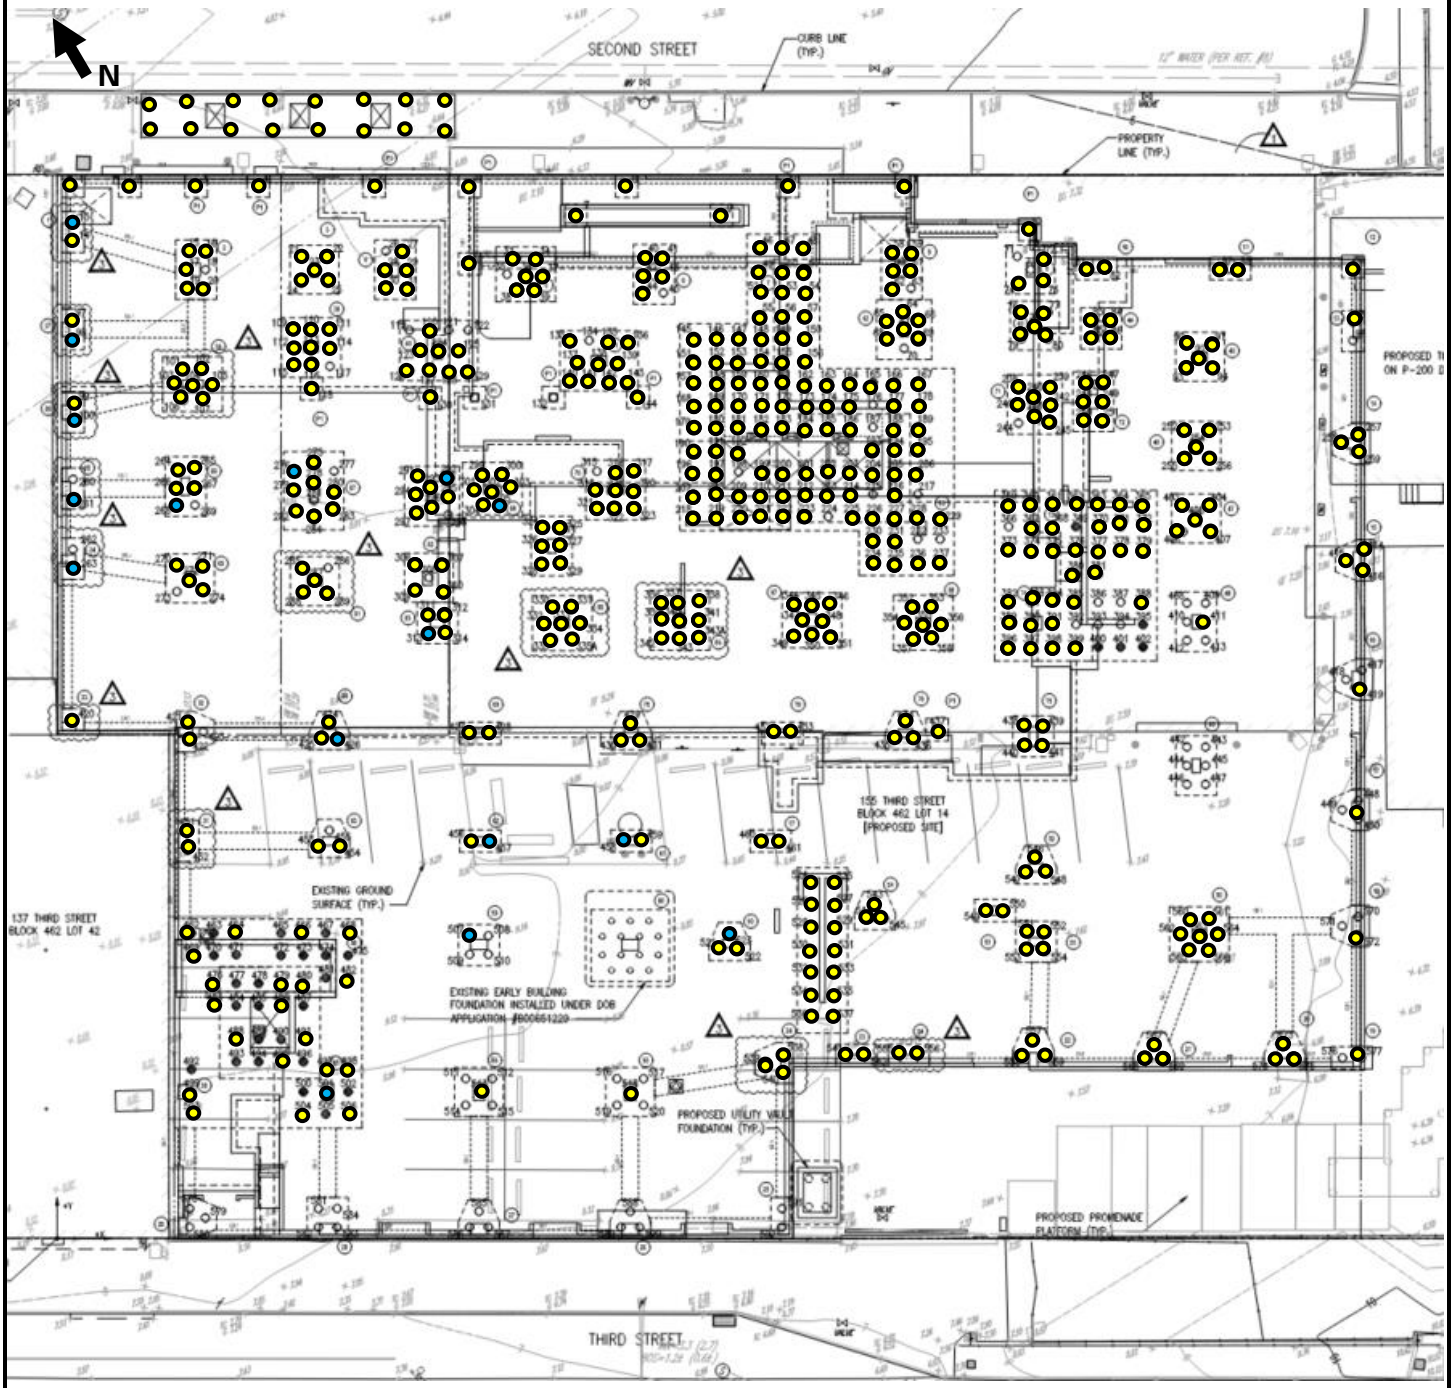

COMPLETED WORK KEY


- Approximate Location of Displacement Pile Advanced Today
- Approximate Location of Displacement Pile Advanced Previously


Base map includes Drawing P100 – Full Displacement Pile (FDP) ID, prepared by Mueser Rutledge Consulting Engineers PLLC, dated 8/18/2025


LANGAN	Site Contribution Report	170390002 - 155 3rd St Brooklyn	
		Report Period	
		From:	01/15/2026 06:00
		To:	01/15/2026 17:00
		PM10 Action Level:	150 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
01/15/2026	32.2 - 45.5	33.5 - 78.7	29.4 - 29.6	1.1 - 5.6	NE


Daily Monitoring Summary	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 1/15/2026	0.0	08:15	0.0000	08:00
Max Contribution (15 min avg.) - 1/15/2026	5.9	07:45	0.0150	07:45
Daily Avg. Contribution (15 min avg.) - 1/15/2026	1.0	-	0.0009	-

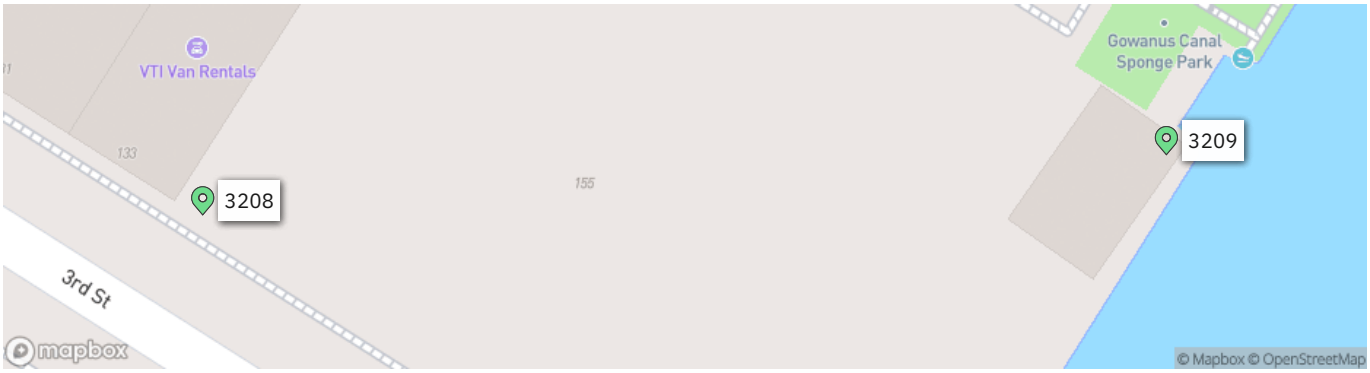

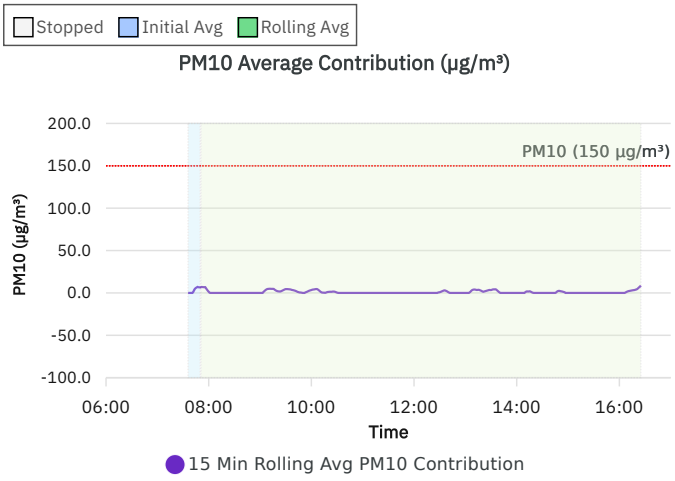


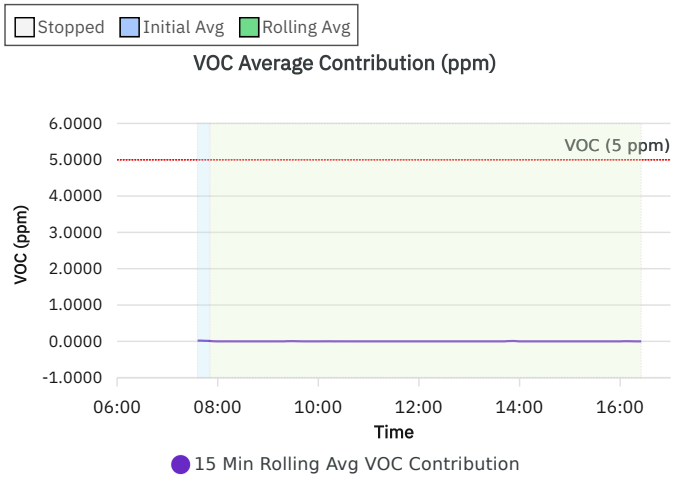


Wind rose (mph)

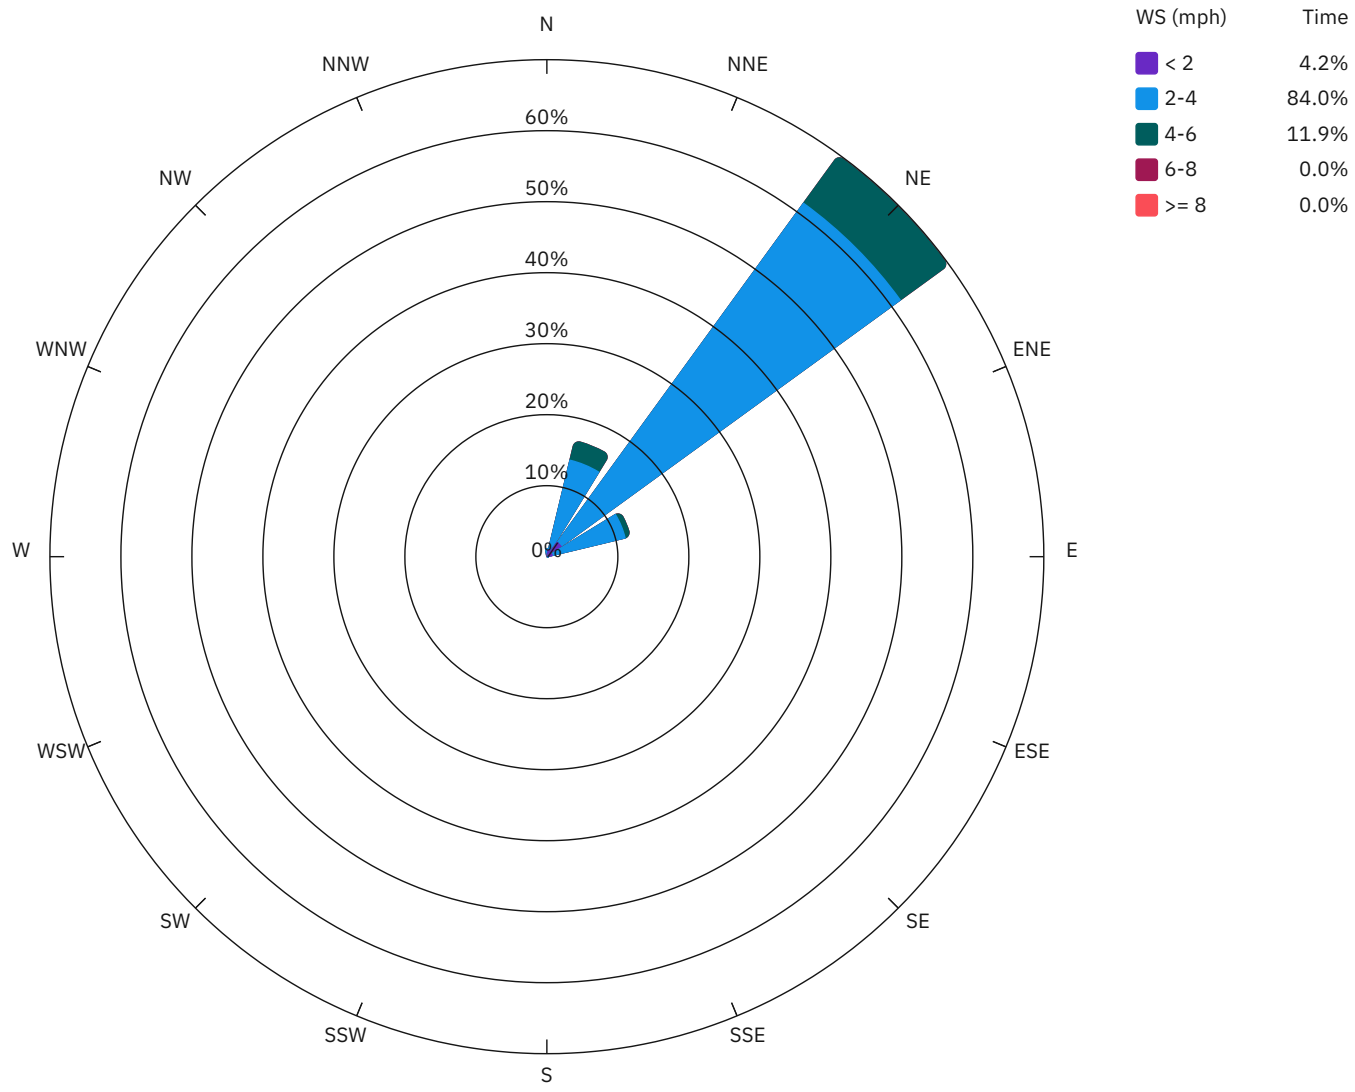

3208

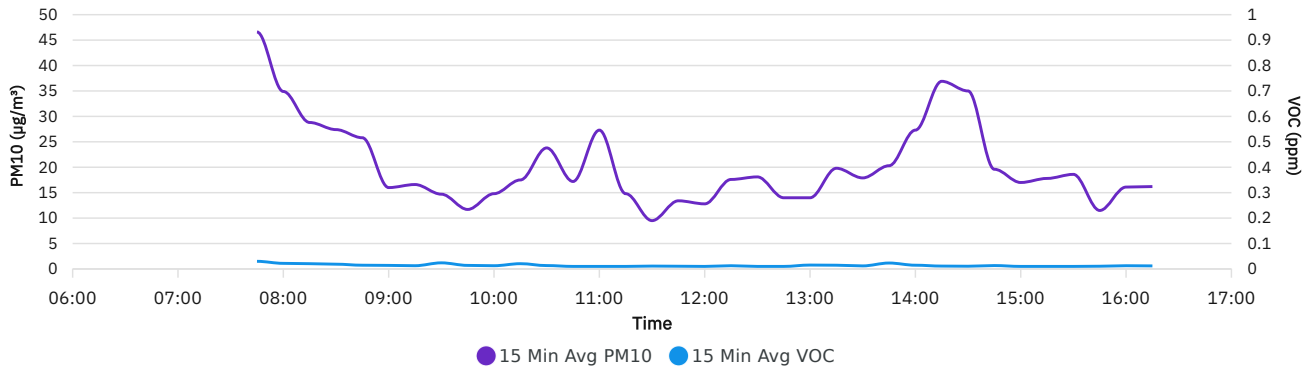

3209

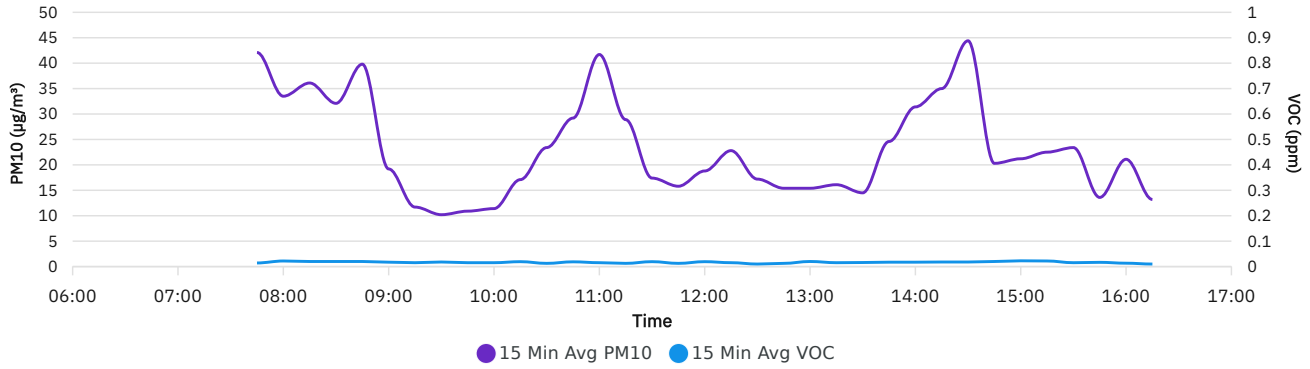
50
45
40
35
30
25
20
15
10
5
0
PM10 (µg/m³)
1
0.9
0.8
0.7
0.6
0.5
0.4
0.3
0.2
0.1
0
VOC (ppm)
06:00
07:00
08:00
09:00
10:00
11:00
12:00
13:00
14:00
15:00
16:00
17:00
Time
15 Min Avg PM10
15 Min Avg VOC

DER-10 Summary: 15 Min Rolling Avg Data

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
1/15/2026 07:45	40.8	46.6	5.9	0.0150	0.0300	0.0150	2.7	NE
1/15/2026 08:00	33.5	34.9	1.4	0.0220	0.0220	0.0000	2.5	NE
1/15/2026 08:15	36.1	28.8	0.0	0.0200	0.0207	0.0007	1.8	NE
1/15/2026 08:30	32.1	27.4	0.0	0.0200	0.0187	0.0000	2.5	NE
1/15/2026 08:45	39.8	25.8	0.0	0.0200	0.0147	0.0000	3.1	NE
1/15/2026 09:00	19.2	16.0	0.0	0.0173	0.0140	0.0000	2.7	NE
1/15/2026 09:15	11.7	16.6	4.8	0.0153	0.0127	0.0000	2.4	NE
1/15/2026 09:30	10.2	14.7	4.5	0.0180	0.0240	0.0060	2.9	NNE
1/15/2026 09:45	10.9	11.7	0.9	0.0153	0.0140	0.0000	2.4	NNE
1/15/2026 10:00	11.4	14.8	3.4	0.0153	0.0127	0.0000	3.2	NE
1/15/2026 10:15	17.1	17.5	0.3	0.0193	0.0207	0.0013	3.2	NE
1/15/2026 10:30	23.4	23.8	0.4	0.0127	0.0133	0.0007	3.1	NE
1/15/2026 10:45	29.2	17.2	0.0	0.0187	0.0100	0.0000	3.4	NE
1/15/2026 11:00	41.7	27.3	0.0	0.0153	0.0100	0.0000	3.8	NE
1/15/2026 11:15	28.9	14.8	0.0	0.0127	0.0100	0.0000	3.1	NE
1/15/2026 11:30	17.4	9.5	0.0	0.0193	0.0113	0.0000	2.8	NE
1/15/2026 11:45	15.8	13.4	0.0	0.0127	0.0107	0.0000	2.7	NE
1/15/2026 12:00	18.8	12.8	0.0	0.0193	0.0100	0.0000	2.9	NE
1/15/2026 12:15	22.8	17.6	0.0	0.0153	0.0127	0.0000	3.6	NE
1/15/2026 12:30	17.2	18.1	0.8	0.0100	0.0100	0.0000	3.2	NE
1/15/2026 12:45	15.4	14.0	0.0	0.0127	0.0100	0.0000	3.4	NE
1/15/2026 13:00	15.4	14.0	0.0	0.0200	0.0153	0.0000	3.4	NE
1/15/2026 13:15	16.1	19.8	3.7	0.0153	0.0147	0.0000	3.5	NE
1/15/2026 13:30	14.5	17.9	3.4	0.0160	0.0120	0.0000	2.8	NE
1/15/2026 13:45	24.6	20.3	0.0	0.0173	0.0233	0.0060	3.4	NE
1/15/2026 14:00	31.4	27.3	0.0	0.0173	0.0147	0.0000	3.2	NE
1/15/2026 14:15	35.0	36.9	1.9	0.0180	0.0113	0.0000	3.7	NE
1/15/2026 14:30	44.4	35.0	0.0	0.0180	0.0107	0.0000	3.9	NE
1/15/2026 14:45	20.3	19.6	0.0	0.0200	0.0133	0.0000	3.5	NE
1/15/2026 15:00	21.2	17.0	0.0	0.0227	0.0100	0.0000	3.5	NE
1/15/2026 15:15	22.5	17.8	0.0	0.0220	0.0100	0.0000	3.2	NE

Date/Time	Average Upwind PM10 (µg/m³)	Average Downwind PM10 (µg/m³)	Average Contribution PM10 (µg/m³)	Average Upwind VOC (ppm)	Average Downwind VOC (ppm)	Average Contribution VOC (ppm)	Wind Speed	Wind Direction
1/15/2026 15:30	23.4	18.6	0.0	0.0153	0.0100	0.0000	3.0	NE
1/15/2026 15:45	13.6	11.5	0.0	0.0167	0.0107	0.0000	2.6	NE
1/15/2026 16:00	21.1	16.1	0.0	0.0133	0.0127	0.0000	3.2	NE
1/15/2026 16:15	13.2	16.2	3.0	0.0100	0.0120	0.0020	3.1	NE

Air Monitoring Data by Location: 15 Min Avg Data

Date/Time	3208 PM10 (µg/m³)	3208 VOC (ppm)	3209 PM10 (µg/m³)	3209 VOC (ppm)	Wind Direction	Wind Speed
01/15/2026 07:45	46.6	0.0300	42.1	0.0142	NE	2.7
01/15/2026 08:00	34.9	0.0220	33.5	0.0220	NE	2.5
01/15/2026 08:15	28.8	0.0207	36.1	0.0200	NE	1.8
01/15/2026 08:30	27.4	0.0187	32.1	0.0200	NE	2.5
01/15/2026 08:45	25.8	0.0147	39.8	0.0200	NE	3.1
01/15/2026 09:00	16.0	0.0140	19.2	0.0173	NE	2.7
01/15/2026 09:15	16.6	0.0127	11.7	0.0153	NE	2.4
01/15/2026 09:30	14.7	0.0240	10.2	0.0180	NNE	2.9
01/15/2026 09:45	11.7	0.0140	10.9	0.0153	NNE	2.4
01/15/2026 10:00	14.8	0.0127	11.4	0.0153	NE	3.2
01/15/2026 10:15	17.5	0.0207	17.1	0.0193	NE	3.2
01/15/2026 10:30	23.8	0.0133	23.4	0.0127	NE	3.1
01/15/2026 10:45	17.2	0.0100	29.2	0.0187	NE	3.4
01/15/2026 11:00	27.3	0.0100	41.7	0.0153	NE	3.8
01/15/2026 11:15	14.8	0.0100	28.9	0.0127	NE	3.1
01/15/2026 11:30	9.5	0.0113	17.4	0.0193	NE	2.8
01/15/2026 11:45	13.4	0.0107	15.8	0.0127	NE	2.7
01/15/2026 12:00	12.8	0.0100	18.8	0.0193	NE	2.9
01/15/2026 12:15	17.6	0.0127	22.8	0.0153	NE	3.6
01/15/2026 12:30	18.1	0.0100	17.2	0.0100	NE	3.2
01/15/2026 12:45	14.0	0.0100	15.4	0.0127	NE	3.4
01/15/2026 13:00	14.0	0.0153	15.4	0.0200	NE	3.4
01/15/2026 13:15	19.8	0.0147	16.1	0.0153	NE	3.5
01/15/2026 13:30	17.9	0.0120	14.5	0.0160	NE	2.8
01/15/2026 13:45	20.3	0.0233	24.6	0.0173	NE	3.4
01/15/2026 14:00	27.3	0.0147	31.4	0.0173	NE	3.2
01/15/2026 14:15	36.9	0.0113	35.0	0.0180	NE	3.7
01/15/2026 14:30	35.0	0.0107	44.4	0.0180	NE	3.9
01/15/2026 14:45	19.6	0.0133	20.3	0.0200	NE	3.5
01/15/2026 15:00	17.0	0.0100	21.2	0.0227	NE	3.5
01/15/2026 15:15	17.8	0.0100	22.5	0.0220	NE	3.2
01/15/2026 15:30	18.6	0.0100	23.4	0.0153	NE	3.0
01/15/2026 15:45	11.5	0.0107	13.6	0.0167	NE	2.6
01/15/2026 16:00	16.1	0.0127	21.1	0.0133	NE	3.2
01/15/2026 16:15	16.2	0.0120	13.2	0.0100	NE	3.1
