vEKtor consultants

WEATHER	Snow		Rain		Overcast	X	Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70		70-85	X	>85	

DAILY STATUS REPORT

Prepared By: Budhiono Riyanto

NYSDEC BCP Site No:	C224392	**Date:**	08/31/2026
Project Name:	601-607 Union Street Site 601-607 Union Street, Brooklyn, NY		

Consultant:	**Personnel On-Site:**
Vektor Consultants- Budhiono Riyanto	RYC Turbos – Piling Subcontractor

Work Activities Performed:

- One upwind and two downwind CAMP stations were set up as described below. No odors or evidence of release were observed during the day's activities.
- RYC Turbos continued piling activities along grids B1, C1, D1, G6 and G7 onsite.
- RYC Turbos excavated and exported 30 truckloads (approximately 600 CY) of non-hazardous material from Grid WC-4A (6'-12') to Clean Earth New Castle in New Castle, DE; and 5 truckloads (approximately 80 CY) of C&D material to Allocco Recycling in Brooklyn, NY.
- RYC Turbos continued lagging activities along grids D1, E1, A6 and A7 onsite.
- As part of the remedial program, to evaluate the remedy with respect to green and sustainable remediation principles, an environmental footprint analysis was completed. The environmental footprint analysis was completed using an accepted environmental footprint analysis calculator, SEFA (Spreadsheets for Environmental Footprint Analysis, USEPA). Water consumption, greenhouse gas emissions, renewable and non-renewable energy use, waste reduction, and material use were estimated, and goals for the project related to these green and sustainable remediation metrics. The following footprint was calculated at the Site. It was estimated that approximately 74,490 tons of greenhouse gas emissions (GHG) emissions (carbon dioxide equivalents of global warming potential), 478 pounds of NOx emissions, 74 pounds of SOx emissions, 259 pounds of particulate matter (PM) emissions, and 3 pounds of hazardous air pollutants (HAPs) were emitted during the reporting period at the Site.

Community Air Monitoring Program (CAMP)

One Upwind and two downwind CAMP stations were placed near the perimeters of the Site during intrusive work. A downwind CAMP was positioned in the northern portion of the Site, and a second downwind CAMP station was in the southeast portion of the Site near the adjoining neighboring building. The upwind CAMP station was positioned in the southern portion of the Site.

Background Levels (Initial Readings at Start of Day):

PID: 0.0 ppm Dust: 41.3 µg/m^3

Highest DW Levels:

PID: 0.0 ppm Dust: 41.3 µg /m^3

No Downwind Respirable Dust concentrations were detected in exceedance of the New York State Department of Health Generic CAMP Response Levels at a work area CAMP station.

No VOC concentrations were detected in exceedance of the New York State Department of Health Generic CAMP Response Levels at a work area CAMP station.

Please note that elevated the upwind readings were caused by the conducting general housekeeping and cleaning around the upwind CAMP station.

Problems Encountered:

None.

Planned Activities for the Next Week/Month:

- Continue soil export, pile installation and SOE activities

DISPOSAL QUANTITIES AND FACILITY DESTINATIONS

Facility # Name/ Location Type of Waste Solid Or Liquid	Clean Earth of North Jersey Kearny, NJ		Clean Earth of New Castle, New Castle, Delaware		Allocco Recycling LTD 540 Kingsland Avenue, Brooklyn, NY	
(Trucks, Cu.Yds. Or Gallons)	Trucks	Cu Yds	Trucks	Cu Yds	Trucks	Cu Yds
Today	0	0	30	~600	5	~100
Total	97	~1,940	194	~3,880	123	~2,460

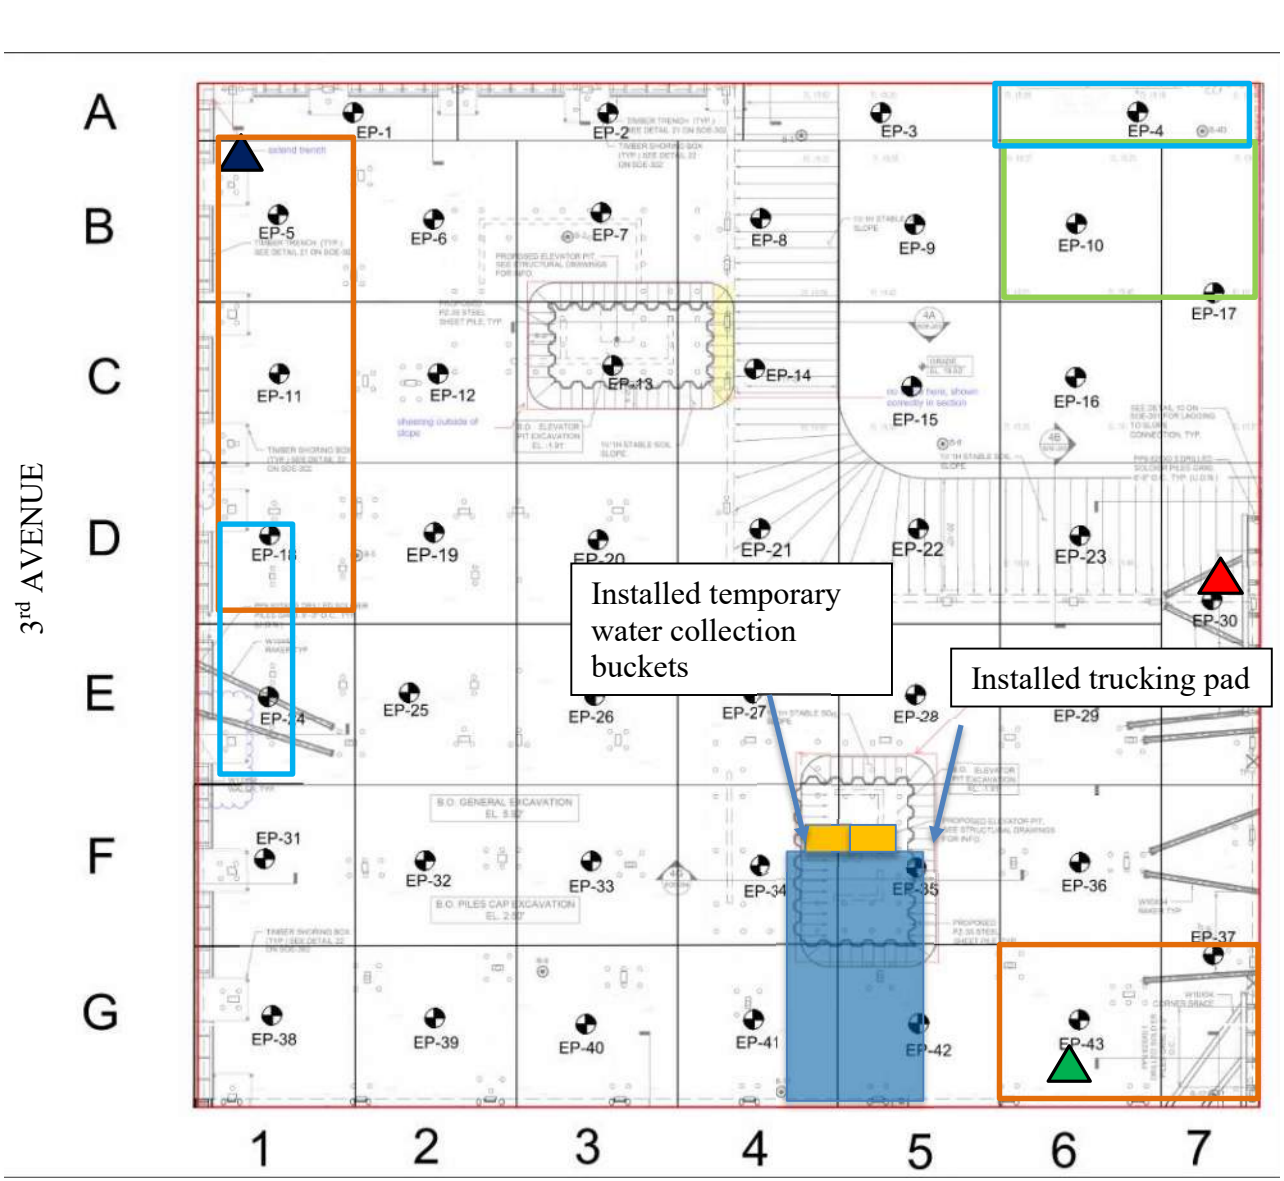
IMPORT QUANTITIES

Facility # Name/ Location Solid Or Liquid	Tilcon Mount Hope, NJ ASTM #57 ¾ Stone	
(Trucks, Cu.Yds.)	Trucks	Cu Yds
Today	0	0
Total	5	~100

vEKtor consultants

SITE PLAN

SACKETT STREET



UNION STREET

N

Legend

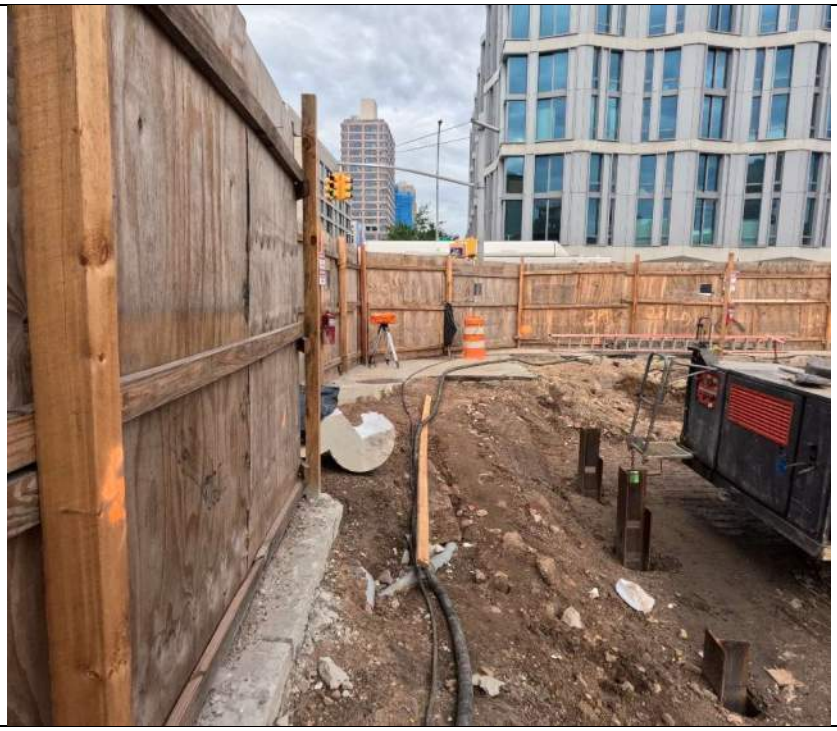
- Upwind CAMP
- Downwind CAMP
- Downwind CAMP 2
- Piling Activities
- Excavation Activities
- Lagging Activities

vEKtor consultants

Photo Log

Photo 1: View of the site looking north.	
Photo 2: View of the lagging activities.	

Photo 3: View of the piling activities.	
Photo 4: View of the trucking activities.	

Photo 5: View of the downwind CAMP station.	

Truck Log

Load	Truck Company	Manifest #	No.	License Plate	Grid/Depth	Facility	Material Type	Volume (Est. CY)
1	D & A Contracting LLC.	3169470	39	AU522N	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
2	D & A Contracting LLC.	3169469	28	AW448Y	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
3	D & A Contracting LLC.	3169468	31	AZ233X	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
4	D & A Contracting LLC.	3169467	75	AY577F	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
5	D & A Contracting LLC.	3169466	15	AW710R	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
6	D & A Contracting LLC.	3169465	343	AW858D	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
7	D & A Contracting LLC.	3169464	30	AX946X	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
8	D & A Contracting LLC.	3169463	40	AU426R	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
9	D & A Contracting LLC.	3169462	20	AT880N	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
10	D & A Contracting LLC.	3169461	36	AU436J	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
11	D & A Contracting LLC.	3169460	25	AU872D	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
12	D & A Contracting LLC.	3169459	33	AZ674W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
13	D & A Contracting LLC.	3169458	51	AZ561R	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
14	D & A Contracting LLC.	3169457	7	AZ680W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
15	D & A Contracting LLC.	3169456	12	AW857D	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
16	D & A Contracting LLC.	3169455	72	AX596U	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
17	D & A Contracting LLC.	3169454	59	AZ676W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
18	D & A Contracting LLC.	3169453	8	AZ222N	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
19	D & A Contracting LLC.	3169452	77	AY760V	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
20	D & A Contracting LLC.	3169451	6	AZ782W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
21	D & A Contracting LLC.	3169450	10	AZ783W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
22	D & A Contracting LLC.	3169449	5	AZ552G	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
23	D & A Contracting LLC.	3169448	28	AW448Y	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
24	D & A Contracting LLC.	3169447	343	AW858W	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
25	D & A Contracting LLC.	3169446	40	AU426R	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
26	D & A Contracting LLC.	3169445	56	A162AA	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
27	D & A Contracting LLC.	3169444	36	AU436J	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
28	D & A Contracting LLC.	3169443	30	AX946X	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
29	D & A Contracting LLC.	3169442	20	AT880N	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20
30	D & A Contracting LLC.	3169441	25	AU872D	WC4A (6'-12')	CE of New Castle	Non-hazardous	~20

31	J & J Urena Inc.	316	4	F650AA	-	Allocco Recycling	C&D	~20
32	Joel Trucking LLC.	3289	9	L410AA	-	Allocco Recycling	C&D	~20
33	E & T Perez LLC.	10068		AY357E	-	Allocco Recycling	C&D	~20
34	Joel Trucking LLC.	3371	8	L409AA	-	Allocco Recycling	C&D	~20
35	Mesa Trucking LLC.	263		AU927B	-	Allocco Recycling	C&D	~20

CAMP

vEKtor consultants

555 8th Ave, Suite 2302 - New York, NY

DAILY AIR MONITORING REPORT
601 Union Street
Brooklyn, New York

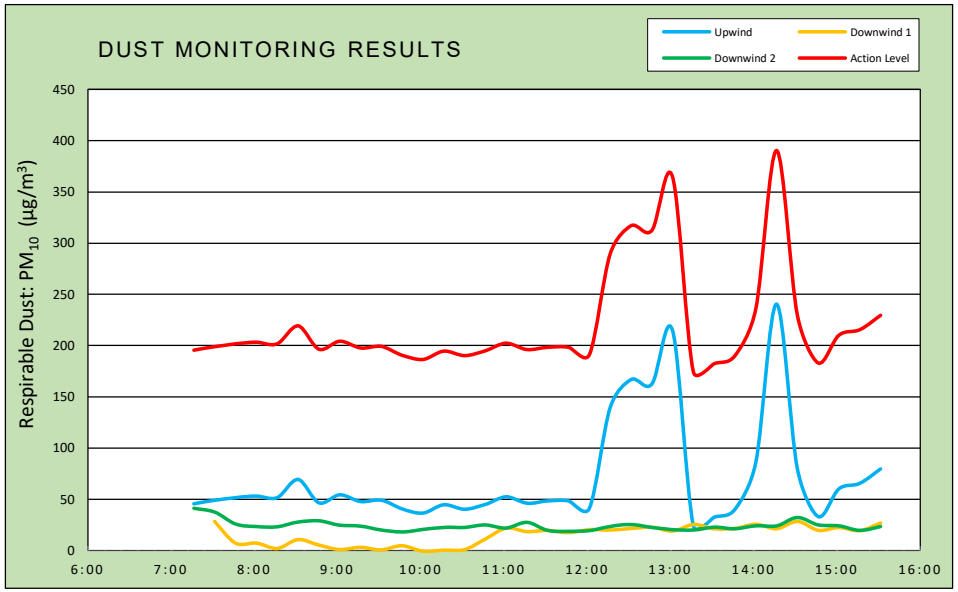
08/31/2026

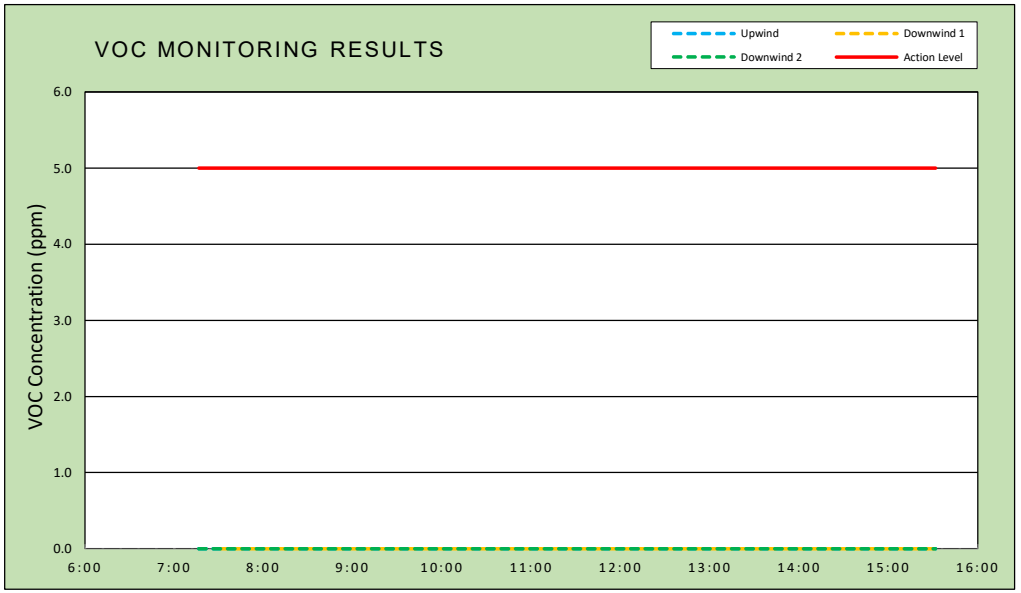
Rev. No. 0	Page 1 of 2
Project Number:	
Dust Action Level	150 µg/m^3
VOC Action Level	5 ppm

Weather Data Range for Work Day		Wind Direction	NNE	Relative Humidity (%)	61.0 - 87.0	Daily Rain Total (in)	0.00
Temperature (°F)	70.0 - 82.0	Wind Speed (MPH)	1.6 - 3.9	Barometer (inHg)	30.10 - 30.10	Avg. Dew Point Temp (°F)	65.5

Readings in the summary table and graphs below are the reported downwind concentrations.

Station Location	Daily Avg. Dust Concentration (µg/m^3)	Max 15-Min Dust Concentration (µg/m^3)	Time of Max Dust Reading	Daily Avg. VOC Concentration (ppm)	Max 15-Min VOC Concentration (ppm)	Time of Max VOC Reading
Upwind	70.1	240.4	14:17	0.0	0.0	7:17
Downwind 1	15.0	28.3	7:32	0.0	0.0	7:32
Downwind 2	24.1	41.3	7:17	0.0	0.0	7:17



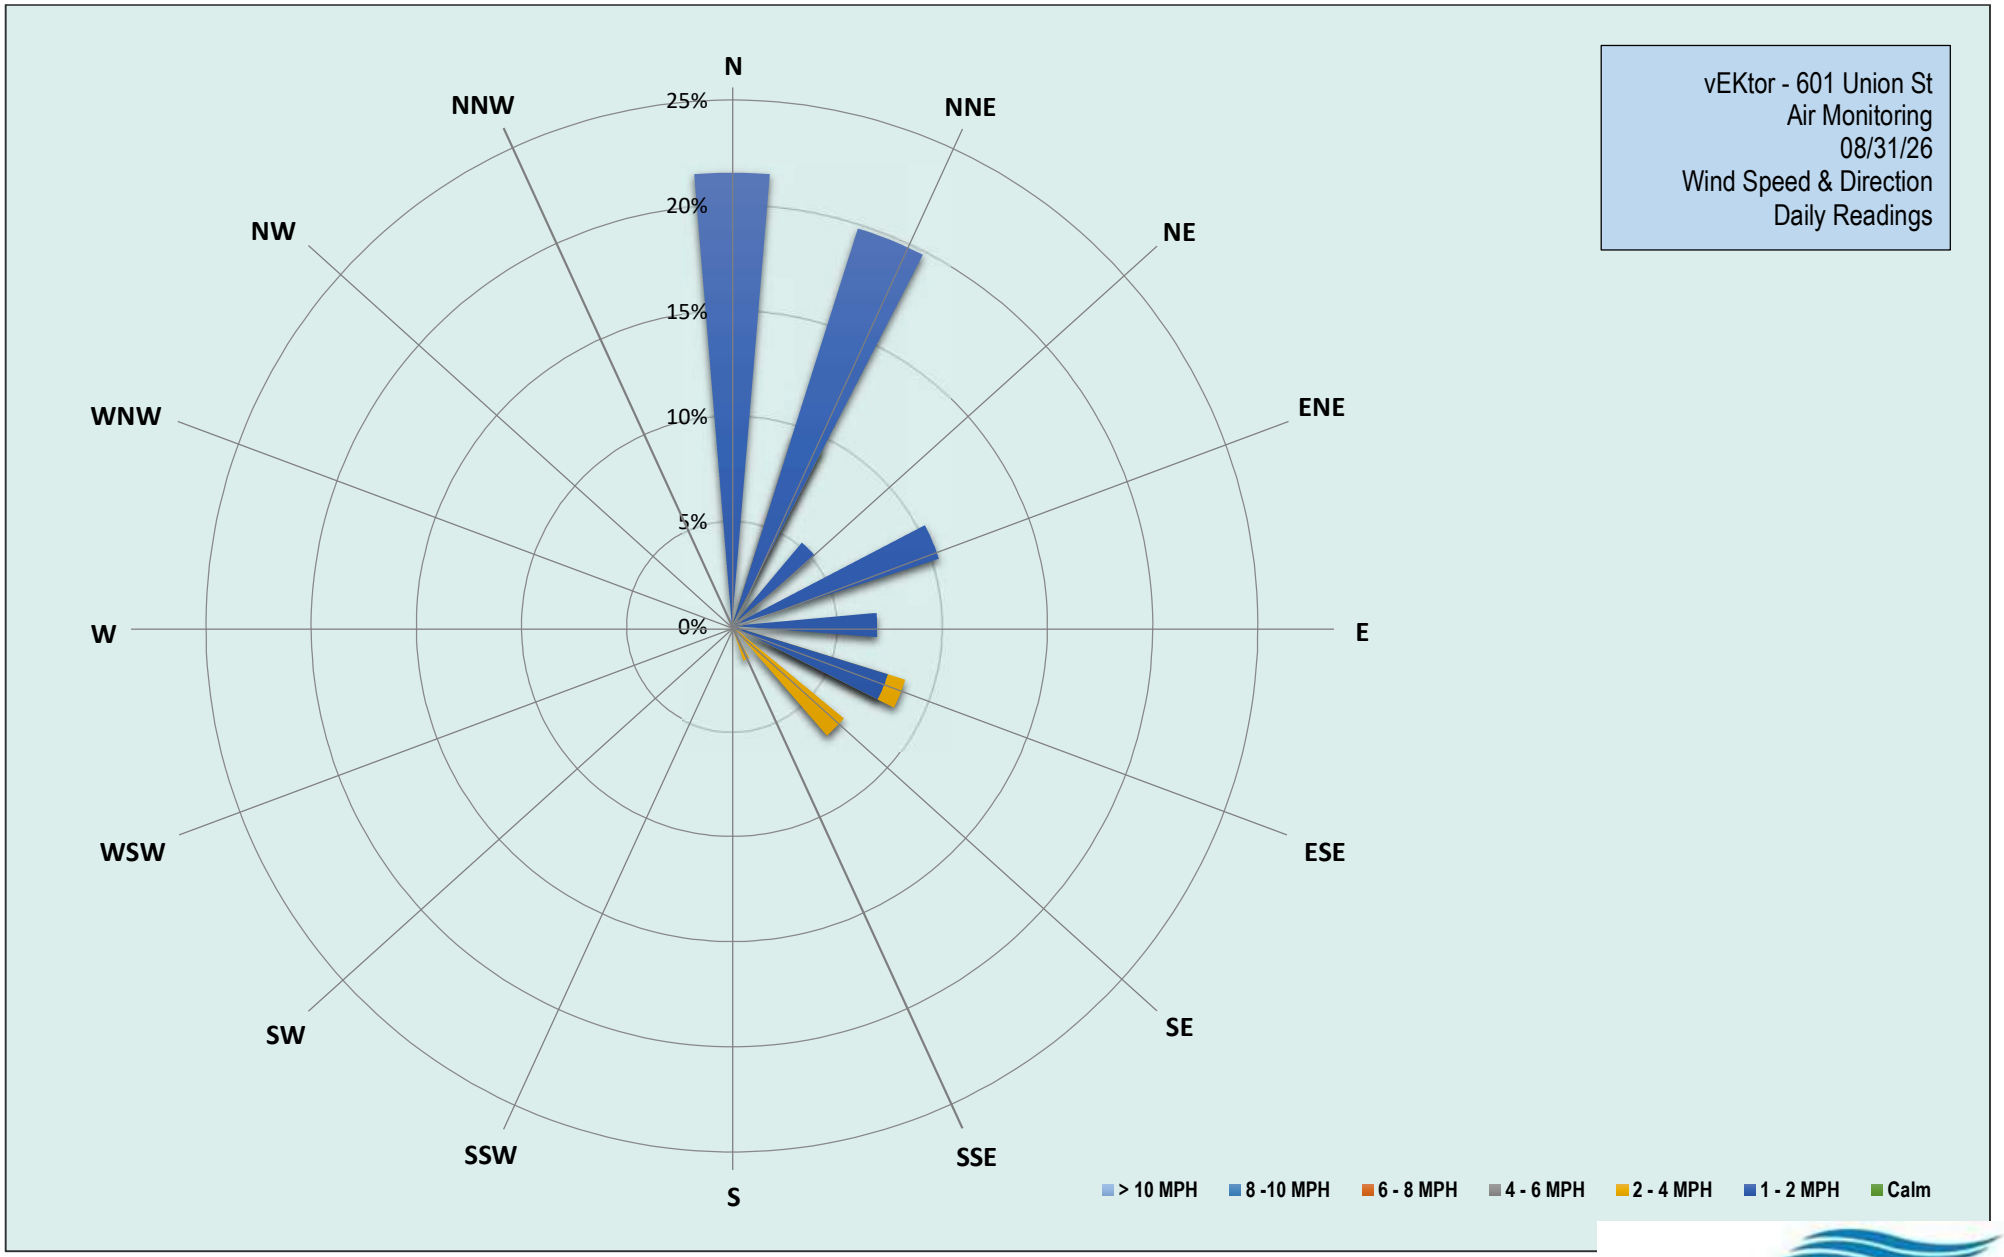


Air Monitoring Notes:

Weather Notes:

EMILCOTT
A Triumvirate Environmental Company

Wind Rose



EMILCOTT
A Triumvirate Environmental Company

Monday, August 31, 2026						
Number of Instances Where Downwind Particulates Exceeds Upwind Particulate +						0
Number of Comparable Data Points =						34
Start Time:						7:17
End Time:						15:32
PARTICULATE DATA						
Upwind		Downwind 1		Downwind 2		Exceeds Particulate Alarm Limit
Time	15-Min Avg Concentration (ug/m^3)	Time	15-Min Avg Concentration (ug/m^3)	Time	15-Min Avg Concentration (ug/m^3)	
7:17	45.5	7:17	-	7:17	41.3	-
7:32	49.0	7:32	28.3	7:32	37.5	-
7:47	51.6	7:47	7.2	7:47	25.8	-
8:02	53.2	8:02	7.3	8:02	23.3	-
8:17	51.6	8:17	2.0	8:17	23.1	-
8:32	69.3	8:32	10.7	8:32	27.7	-
8:47	46.4	8:47	5.3	8:47	29.0	-
9:02	54.3	9:02	0.9	9:02	24.8	-
9:17	47.7	9:17	3.0	9:17	23.8	-
9:32	49.1	9:32	0.5	9:32	20.0	-
9:47	40.6	9:47	4.7	9:47	18.1	-
10:02	36.4	10:02	-0.6	10:02	20.5	-
10:17	44.7	10:17	0.3	10:17	22.6	-
10:32	40.2	10:32	0.8	10:32	22.6	-
10:47	45.0	10:47	11.2	10:47	24.8	-
11:02	52.3	11:02	21.8	11:02	21.9	-
11:17	46.1	11:17	18.4	11:17	27.5	-
11:32	48.4	11:32	19.6	11:32	19.6	-
11:47	48.3	11:47	17.3	11:47	18.7	-
12:02	41.2	12:02	20.4	12:02	19.5	-
12:17	139.6	12:17	19.9	12:17	23.5	-
12:32	166.9	12:32	21.5	12:32	25.4	-
12:47	162.3	12:47	22.7	12:47	22.6	-
13:02	214.5	13:02	18.9	13:02	20.3	-
13:17	24.1	13:17	25.4	13:17	19.9	-
13:32	32.3	13:32	21.3	13:32	22.7	-
13:47	40.2	13:47	21.6	13:47	21.3	-
14:02	85.9	14:02	25.7	14:02	24.1	-
14:17	240.4	14:17	21.3	14:17	24.1	-
14:32	79.5	14:32	28.3	14:32	32.2	-
14:47	33.1	14:47	19.8	14:47	25.0	-
15:02	60.2	15:02	22.4	15:02	24.2	-
15:17	65.5	15:17	19.4	15:17	19.5	-
15:32	79.7	15:32	26.9	15:32	23.5	-

Monday, August 31, 2026						
Number of Instances Where Downwind VOCs Exceeds Upwind VOCs + 5 =						0
Number of Comparable Data Points =						34
Start Time:						7:17
End Time:						15:32
PID DATA						
Upwind		Downwind 1		Downwind 2		
Time	15-Min Avg Concentration (ppm)	Time	15-Min Avg Concentration (ppm)	Time	15-Min Avg Concentration (ppm)	Exceeds Particulate Alarm Limit
7:17	0.0	7:17	-	7:17	0.0	-
7:32	0.0	7:32	0.0	7:32	0.0	-
7:47	0.0	7:47	0.0	7:47	0.0	-
8:02	0.0	8:02	0.0	8:02	0.0	-
8:17	0.0	8:17	0.0	8:17	0.0	-
8:32	0.0	8:32	0.0	8:32	0.0	-
8:47	0.0	8:47	0.0	8:47	0.0	-
9:02	0.0	9:02	0.0	9:02	0.0	-
9:17	0.0	9:17	0.0	9:17	0.0	-
9:32	0.0	9:32	0.0	9:32	0.0	-
9:47	0.0	9:47	0.0	9:47	0.0	-
10:02	0.0	10:02	0.0	10:02	0.0	-
10:17	0.0	10:17	0.0	10:17	0.0	-
10:32	0.0	10:32	0.0	10:32	0.0	-
10:47	0.0	10:47	0.0	10:47	0.0	-
11:02	0.0	11:02	0.0	11:02	0.0	-
11:17	0.0	11:17	0.0	11:17	0.0	-
11:32	0.0	11:32	0.0	11:32	0.0	-
11:47	0.0	11:47	0.0	11:47	0.0	-
12:02	0.0	12:02	0.0	12:02	0.0	-
12:17	0.0	12:17	0.0	12:17	0.0	-
12:32	0.0	12:32	0.0	12:32	0.0	-
12:47	0.0	12:47	0.0	12:47	0.0	-
13:02	0.0	13:02	0.0	13:02	0.0	-
13:17	0.0	13:17	0.0	13:17	0.0	-
13:32	0.0	13:32	0.0	13:32	0.0	-
13:47	0.0	13:47	0.0	13:47	0.0	-
14:02	0.0	14:02	0.0	14:02	0.0	-
14:17	0.0	14:17	0.0	14:17	0.0	-
14:32	0.0	14:32	0.0	14:32	0.0	-
14:47	0.0	14:47	0.0	14:47	0.0	-
15:02	0.0	15:02	0.0	15:02	0.0	-
15:17	0.0	15:17	0.0	15:17	0.0	-
15:32	0.0	15:32	0.0	15:32	0.0	-

GSR EVALUATION

Remedial Oversight - Energy & Air Compiled Results

Category	Total Energy	GHG	NOx	SOx	PM	NOx + SOx + PM	HAPs
	MMbtus	lbs CO2e	lbs	lbs	lbs	lbs	lbs
On-site (Scope 1)	**61**	**9,809**	**74**	**2**	**1**	**78**	**0**
Grid Electricity Generation (Scope 2)	**0.000**	**0**	**0**	**0**	**0**	**0**	**0**
Transportation (Scope 3a)	**250**	**40,434**	**303**	**10**	**6**	**319**	**0**
Other Off-Site (Scope 3b)	**139**	**24,246**	**100**	**62**	**252**	**414**	**3**
Remedy Totals	**449**	**74,490**	**478**	**74**	**259**	**811**	**3**

Values that are forwarded to the "Summary" tab are indicated in orange.

Voluntary Renewable Energy Use	Unit	Quantity	
On-site renewable energy generation or use	MMBtu	**0**	
On-site biodiesel use	MMBtu	**0**	
Biodiesel and other renewable resource use for transportation	MMBtu	**0**	
On-site renewable energy generation or use + on-site biodiesel use + biodiesel and other renewable resource use for transportation	MMBtu	**0**	*(This value is the sum of the three rows above)*
Voluntary purchase of renewable electricity	MWh	**0**	
Voluntary purchase of RECs	MWh	**0**	

This worksheet is not intended for user input. Values on this worksheet are obtained from the following file: SEFA_calculations_(121718).xlsx

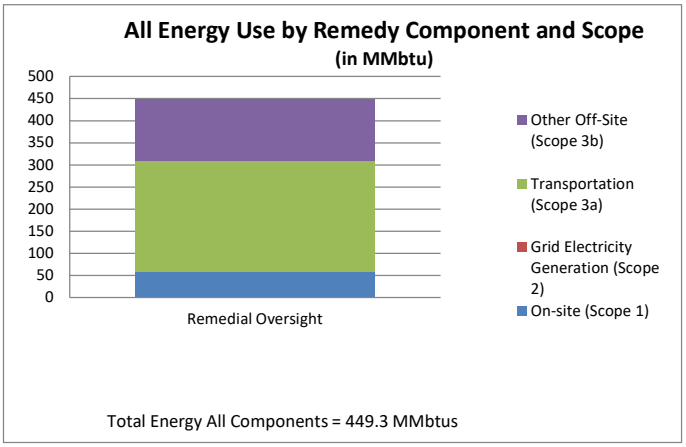
Environmental Footprint Summary

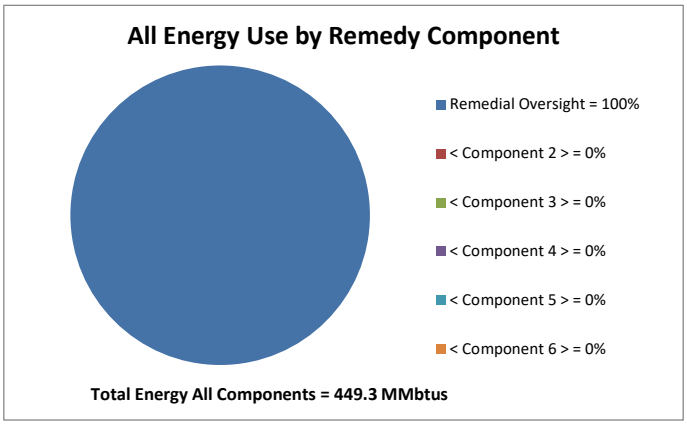
Core Element	Metric		Unit of Measure	Footprint						
				Remedial Oversight	< Component 2 >	< Component 3 >	< Component 4 >	< Component 5 >	< Component 6 >	Total
Materials & Waste	M&W-1	Refined materials used on-site	Tons	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	M&W-2	% of refined materials from recycled or reused material	%							
	M&W-3	Unrefined materials used on-site	Tons	0.000	0.000	0.000	0.000	0.000	0.000	0.0
	M&W-4	% of unrefined materials from recycled or reused material	%							
	M&W-5	On-site hazardous waste disposed of off-site	Tons	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	M&W-6	On-site non-hazardous waste disposed of off-site	Tons	700.0	0.0	0.0	0.0	0.0	0.0	700.0
	M&W-7	Recycled or reused waste	Tons	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	M&W-8	% of total potential waste recycled or reused	%	0.0%						0.0%
Water (used on-site)	W-1	Public water use	MG	0.5	0.0	0.0	0.0	0.0	0.0	0.5
	W-2	Groundwater use	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-3	Surface water use	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-4	Reclaimed water use	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-5	Storm water use	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-6	User-defined water resource #1	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-7	User-defined water resource #2	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	W-8	Wastewater generated	MG	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Energy	E-1	Total energy used (on-site and off-site)	MMBtu	449.3	0.0	0.0	0.0	0.0	0.0	449.3
	E-2	Energy voluntarily derived from renewable resources								
	E-2A	On-site renewable energy generation or use + on-site biodiesel use + biodiesel and other renewable resource use for transportation	MMBtu	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	E-2B	Voluntary purchase of renewable electricity	MWh	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	E-3	Voluntary purchase of RECs	MWh	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	E-4	On-site grid electricity use	MWh	0.000	0.000	0.000	0.000	0.000	0.000	0.0
Air	A-1	On-site NOx, SOx, and PM emissions	Pounds	78.0	0.0	0.0	0.0	0.0	0.0	78.0
	A-2	On-site HAP emissions	Pounds	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	A-3	Total NOx, SOx, and PM emissions	Pounds	810.9	0.0	0.0	0.0	0.0	0.0	810.9
	A-3A	Total NOx emissions	Pounds	477.7	0.0	0.0	0.0	0.0	0.0	477.7
	A-3B	Total SOx emissions	Pounds	73.8	0.0	0.0	0.0	0.0	0.0	73.8
	A-3C	Total PM emissions	Pounds	259.4	0.0	0.0	0.0	0.0	0.0	259.4
	A-4	Total HAP emissions	Pounds	3.4	0.0	0.0	0.0	0.0	0.0	3.4
	A-5	Total greenhouse gas emissions	Tons CO2e*	37.2	0.0	0.0	0.0	0.0	0.0	37.2
Land & Ecosystems	Qualitative Description									

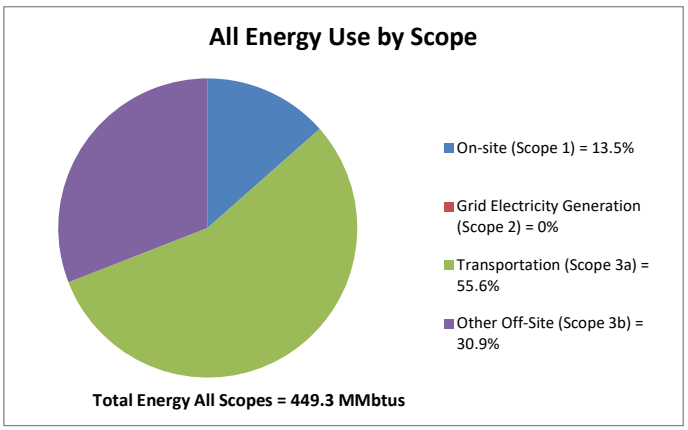
** Total greenhouse gases emissions (in CO2e) include consideration of CO2, CH4, and N2O (Nitrous oxide) emissions.*
"MMBtu" = millions of Btus
"MG" = millions of gallons
"CO2e" = carbon dioxide equivalents of global warming potential
"MWh" = megawatt hours (i.e., thousands of kilowatt-hours or millions of Watt-hours)
"Tons" = short tons (2,000 pounds)

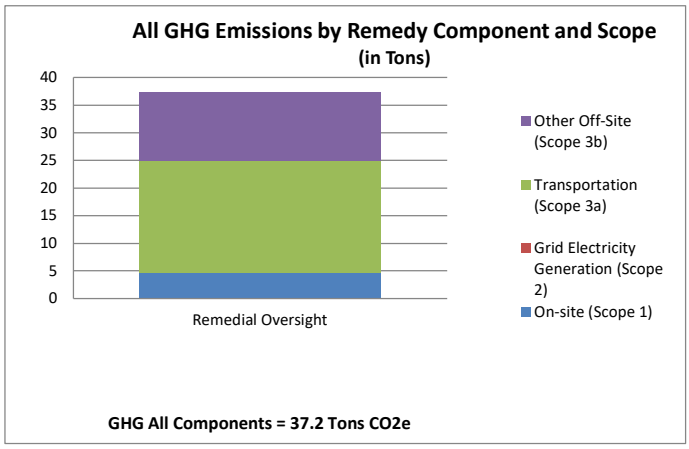
The above metrics are consistent with EPA's Methodology for Understanding and Reducing a Project's Environmental Footprint (EPA 542-R-12-002), February 2012

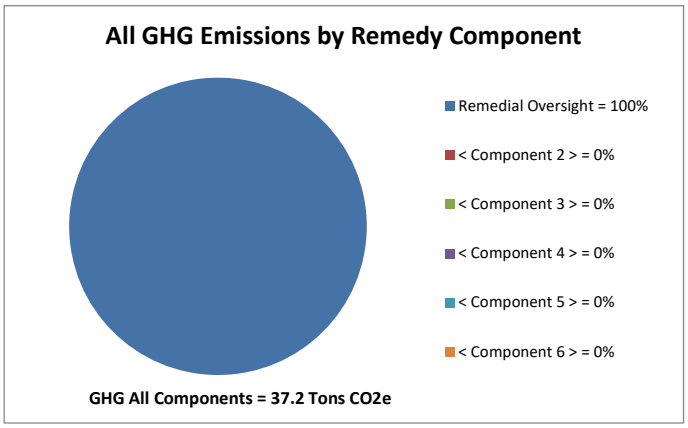
Notes:

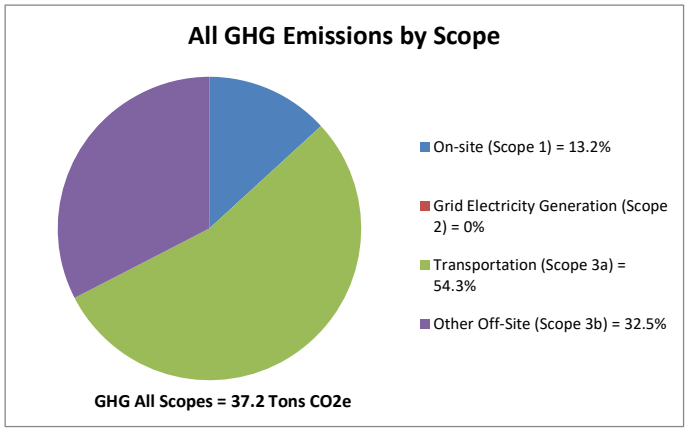

All Energy Use by Remedy Component and Scope
(in MMbtu)
500
450
400
350
300
250
200
150
100
50
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
Total Energy All Components = 449.3 MMbtus

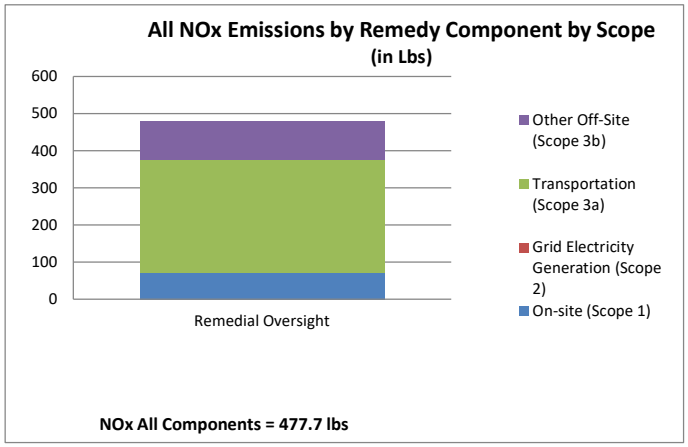

All Energy Use by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
Total Energy All Components = 449.3 MMbtus

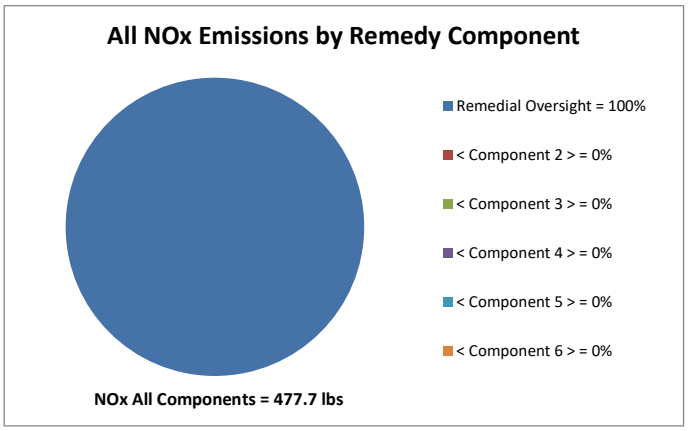

All Energy Use by Scope
On-site (Scope 1) = 13.5%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 55.6%
Other Off-Site (Scope 3b) = 30.9%
Total Energy All Scopes = 449.3 MMbtus

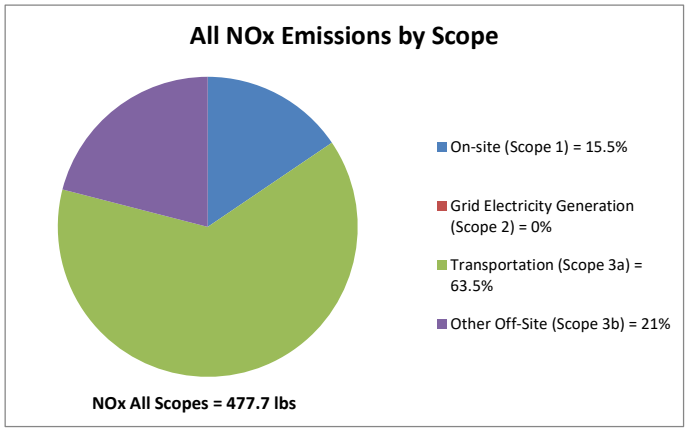

All GHG Emissions by Remedy Component and Scope
(in Tons)
40
35
30
25
20
15
10
5
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
GHG All Components = 37.2 Tons CO2e

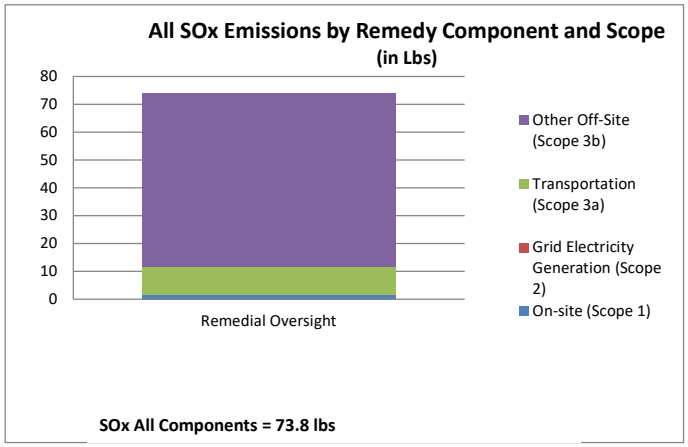

All GHG Emissions by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
GHG All Components = 37.2 Tons CO2e

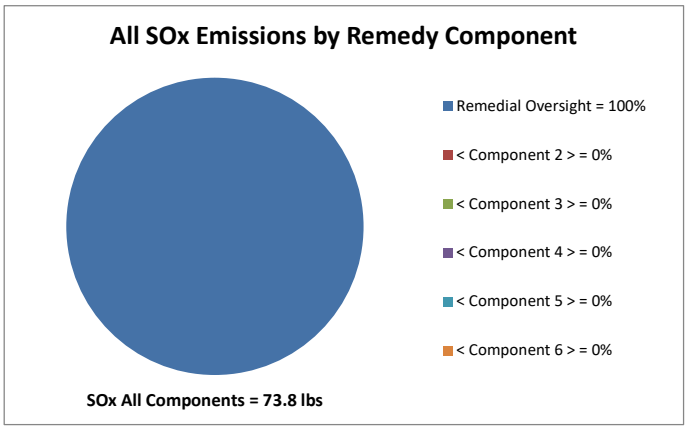

All GHG Emissions by Scope
On-site (Scope 1) = 13.2%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 54.3%
Other Off-Site (Scope 3b) = 32.5%
GHG All Scopes = 37.2 Tons CO2e

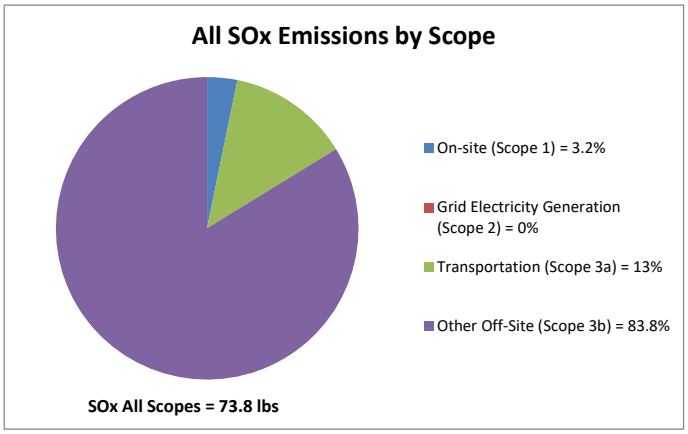

All NOx Emissions by Remedy Component by Scope
(in Lbs)
600
500
400
300
200
100
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
NOx All Components = 477.7 lbs

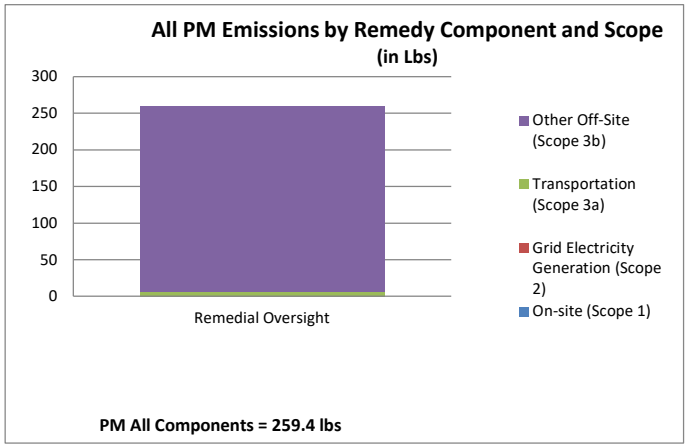

All NOx Emissions by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
NOx All Components = 477.7 lbs

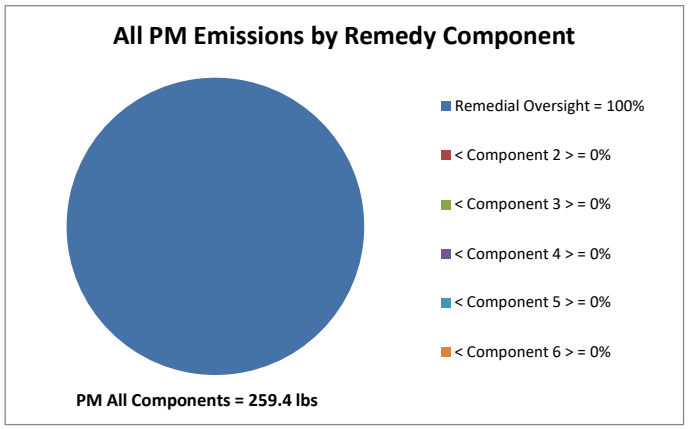

All NOx Emissions by Scope
On-site (Scope 1) = 15.5%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 63.5%
Other Off-Site (Scope 3b) = 21%
NOx All Scopes = 477.7 lbs

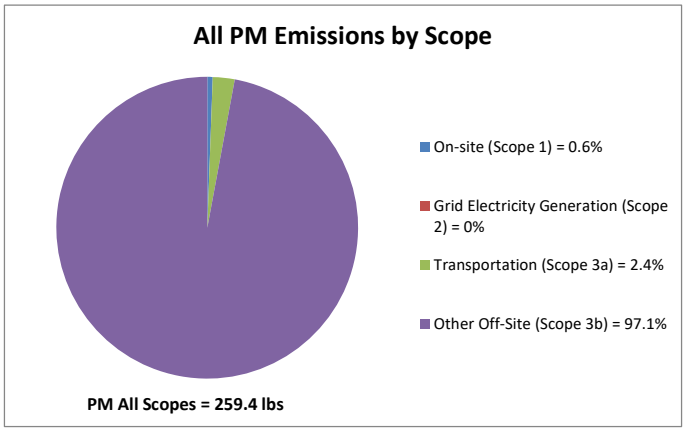

All SOx Emissions by Remedy Component and Scope
(in Lbs)
80
70
60
50
40
30
20
10
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
SOx All Components = 73.8 lbs

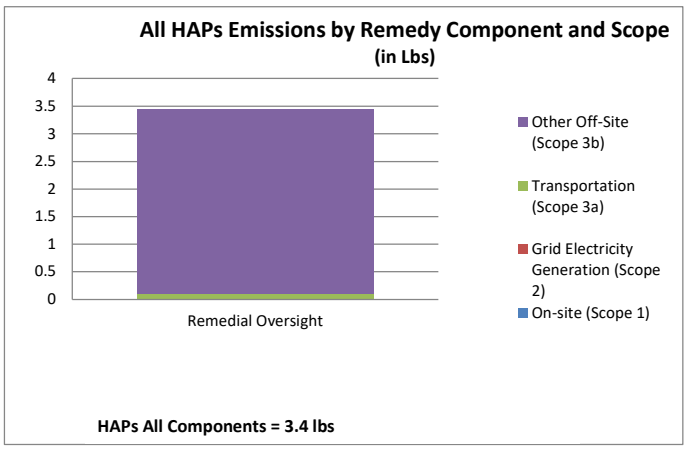

All SOx Emissions by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
SOx All Components = 73.8 lbs

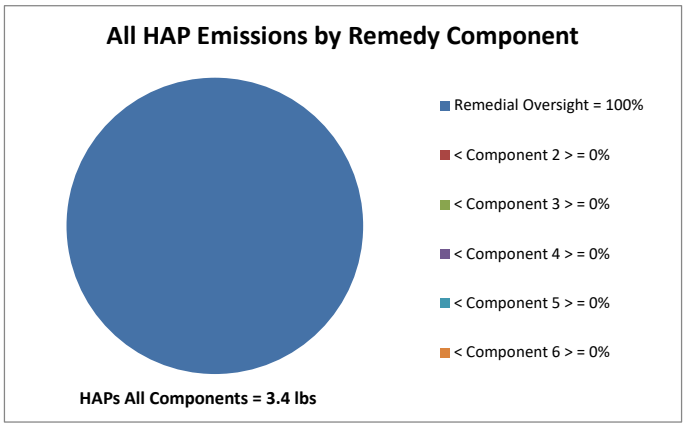

All SOx Emissions by Scope
On-site (Scope 1) = 3.2%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 13%
Other Off-Site (Scope 3b) = 83.8%
SOx All Scopes = 73.8 lbs

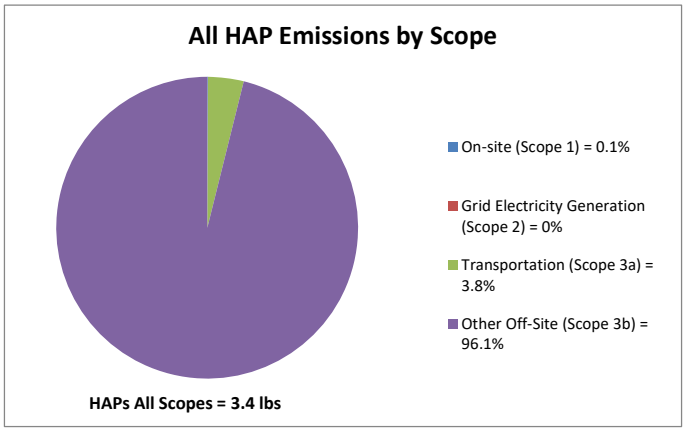

All PM Emissions by Remedy Component and Scope (in Lbs)
300
250
200
150
100
50
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
PM All Components = 259.4 lbs


All PM Emissions by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
PM All Components = 259.4 lbs


All PM Emissions by Scope
On-site (Scope 1) = 0.6%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 2.4%
Other Off-Site (Scope 3b) = 97.1%
PM All Scopes = 259.4 lbs


All HAPs Emissions by Remedy Component and Scope
(in Lbs)
4
3.5
3
2.5
2
1.5
1
0.5
0
Remedial Oversight
Other Off-Site (Scope 3b)
Transportation (Scope 3a)
Grid Electricity Generation (Scope 2)
On-site (Scope 1)
HAPs All Components = 3.4 lbs


All HAP Emissions by Remedy Component
Remedial Oversight = 100%
< Component 2 > = 0%
< Component 3 > = 0%
< Component 4 > = 0%
< Component 5 > = 0%
< Component 6 > = 0%
HAPs All Components = 3.4 lbs


All HAP Emissions by Scope
On-site (Scope 1) = 0.1%
Grid Electricity Generation (Scope 2) = 0%
Transportation (Scope 3a) = 3.8%
Other Off-Site (Scope 3b) = 96.1%
HAPs All Scopes = 3.4 lbs
