APPENDIX I

Digital Project Photo Log

(Provided on DVD in Bound Report)

1. Photo taken on Friday, October 09, 2015. Looking south inside of the garage; concrete staged from test pitting work. Concrete to be removed to staging area prior to concrete demo.

2. Photo taken on Friday, October 09, 2015. Looking north inside the garage; water was applied at point of contact between excavator hammer and concrete to reduce dust generation/migration offsite.

3. Photo taken Friday, October 09, 2015. Looking north inside of the garage; demolition concrete removed potential UST manhole cover.

4. Photo taken on Friday, October 09, 2015. Looking north inside the garage; end of day concrete demolition. Concrete to be removed to staging area at later date prior to UST removal.

5. Photo taken on Saturday, October 10, 2015. Looking north inside of the garage; concrete inside UST excavation footprint to be removed to staging area.

6. Photo taken on Saturday, October 10, 2015. Looking southwest inside the garage; partial removal of loading dock to open area for construction vehicle ingress/egress and to expedite future concrete and UST removal.

7. Photo taken on Saturday, October 10, 2015. Looking south inside of the garage; concrete demolition towards the south (garage opening) with mitigation measures implemented when dust was generated

8. Photo taken on Saturday, October 10, 2015. Looking north inside the garage; end of day concrete demolition. Concrete to be removed to staging area at later date prior to UST removal.

9. Photo taken on Monday, October 12, 2015. Looking south inside of the garage; broken concrete inside UST excavation footprint to be removed to staging area by end of day.

10. Photo taken on Monday, October 12, 2015. Looking northeast in the courtyard; movement of concrete stockpile staging areas to northeast corner of courtyard in front of shed footprint.

11. Photo taken on Monday, October 12, 2015. Inside PFB looking north, double poly liner laid down as foundation of staging area.

12. Photo taken on Monday, October 12, 2015. Looking south inside the garage; UST discovered in approximate area of GT-4. UST located 2-3' BGS after concrete removal. Curved UST dimensions are approx. 20' length and 10' width.

13. Photo taken on Tuesday, October 13, 2015. Looking south inside of the garage; locations of manhole covers associated with one UST (GT-5). UST shown to be split into three separate chambers on interior.

14 Photo taken on Tuesday, October 13, 2015. Looking northeast in the courtyard; movement of concrete stockpile staging areas to northeast corner of courtyard in front of shed footprint.

15. Photo taken on Tuesday, October 13, 2015. Inside garage looking northeast, removed manhole cover from the western chamber of UST-3 (UST-3A)

16. Photo taken on Tuesday, October 13, 2015. Looking north inside the garage; uncovering remainder of UST-3 to determine if additional manhole is present for eastern chamber (UST-3B)

17. Photo taken on Wednesday, October 14, 2015. Looking south inside of the garage; locations of manhole covers for USTs.

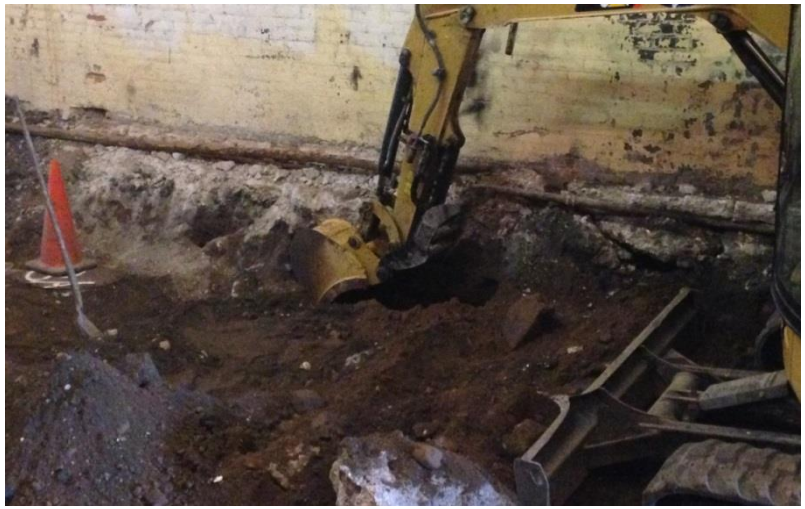

18. Photo taken on Wednesday, October 14, 2015. Looking southwest in the garage; digging test pit next to building to determine footing depth.

19. Photo taken on Wednesday, October 14, 2015. Inside garage looking northwest, begin demo of the remainder of the loading dock.

20. Photo taken on Wednesday, October 14, 2015. Looking southwest inside the garage; material located beneath concrete loading dock did not have odor or staining and will be sampled for reuse onsite.

21. Photo taken on Thursday, October 15, 2015. Looking northeast in courtyard; RCA delivered to site that will need to be confirmed to being DER-10 compliant

22. Photo taken on Thursday, October 15, 2015. Looking northwest in the garage; loading dock removed. Concrete slab located under dock, and above UST GT-1, to be removed once hammer attachment is remobilized.

23. Photo taken on Thursday, October 15, 2015. Inside garage looking south, begin removal of metal and piping located in the garage excavation.

24. Photo taken on Thursday, October 15, 2015. Looking southeast in the courtyard; material removed from the shed footprint to be stockpiled and covered at end of day. No odor or staining resulting from soil source.

25. Photo taken on Friday, October 16, 2015. Looking northwest in courtyard; soil and debris generated from removal of shed foundation covered by 6 mil poly. No odors or staining present on material or soil.

26. Photo taken on Friday, October 16, 2015. On Vernon Blvd looking northwest, delivery of sheet steel piles to be mobilized to the garage.

27. Photo taken on Friday, October 16, 2015. Outside site on 46th Avenue, looking west; removal of steel sheeting piles from delivery truck to be stored inside the garage prior to mobilization to the courtyard.

28. Photo taken on Friday, October 16, 2015. Looking south in the garage; sheet piles inside the garage. Piles to be moved to the courtyard w hen needed for excavation work.

29. Photo taken on Monday, October 19, 2015. Looking southwest in courtyard; x10 sheet piles perimeter of courtyard.

30. Photo taken on Monday, October 19, 2015. In courtyard looking northwest, began removal of concrete in courtyard. Use of dust suppression when moving concrete to reduce generated particulates.

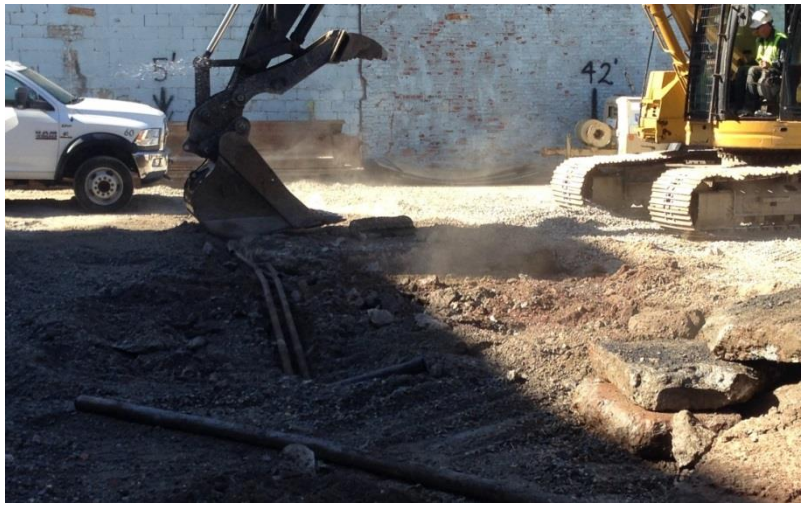

31. Photo taken on Monday, October 19, 2015. Inside courtyard looking west; piping uncovered directly under concrete to the southern perimeter of area to be excavated under the tent.

32. Photo taken on Monday, October 19, 2015. Looking south in the garage; during digging of test pit after removal of pipe run concrete and piping. additional piping excavated at approx. 2-3' below original.

33. Photo taken on Tuesday, October 20, 2015. Looking northwest in courtyard; stockpiling of concrete in courtyard for loadout later in day. Will extend footprint of concrete removal as concrete is taken offsite.

34. Photo taken on Tuesday, October 20, 2015. In garage looking southwest, begin removal of loading dock footprint concrete and widening entrance by removing side of ramp.

35. Photo taken on Tuesday, October 20, 2015. In garage looking southwest, discovery of potential UST. Unconfirmed length but diameter confirmed to be 10' in diameter with 2' of material that smells like fuel.

36. Photo taken on Tuesday, October 20, 2015. Looking west in courtyard, northern extent of concrete removal.

37. Photo taken on Wednesday, October 21, 2015. Looking southeast in courtyard; mobilization of pile driving equipment overnight.

38. Photo taken on Wednesday, October 21, 2015. Looking north in courtyard, begin removing concrete under footprint of the shed. Removal of varnish pot sleeves and piping from underneath slab.

39. Photo taken on Wednesday, October 21, 2015. Piping discovered in the courtyard excavation footprint found to contain grossly contaminated material. Staged on poly to be disposed offsite.

40. Photo taken on Wednesday, October 21, 2015. Looking northeast in courtyard, Removal and stockpiling of concrete from the shed footprint

41. Photo taken on Thursday, October 22, 2015. Looking northwest in courtyard; breaking concrete in courtyard while using water as dust suppression technique.

42. Photo taken on Thursday, October 22, 2015. Looking west in courtyard; moving sheet piles for SOE from garage to courtyard.

43. Photo taken on Thursday, October 22, 2015. Looking north; installation of first sheet pile for SOE in the NE corner of the courtyard.

44. Photo taken on Thursday, October 22, 2015. Looking south in garage; cutting pipes to prepare them for disposal.

45. Photo taken on Friday, October 23, 2015. Looking southeast in PFB; cut piping removed from garage staged on x2 sheets of 6mil poly

46. Photo taken on Friday, October 23, 2015. Looking northeast in courtyard; mechanic repairing Kobelco SK350LC pile driver that was leaking hydraulic fluid from a hose.

47. Photo taken on Friday, October 23, 2015. Looking northeast in the courtyard; SCE laborer checking to make sure sheet pile half is level during installation.

48. Photo taken on Friday, October 23, 2015. Looking northeast in the courtyard; seven full sheet piles installed by end of day on 10/23/2015.

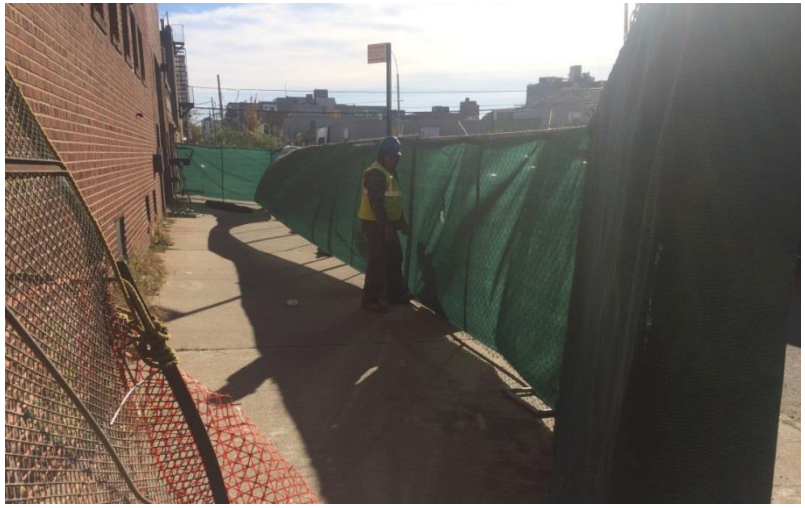

49. Photo taken on Monday, October 26, 2015. Looking east down 46th Avenue; setting up fence to close off sidewalk.

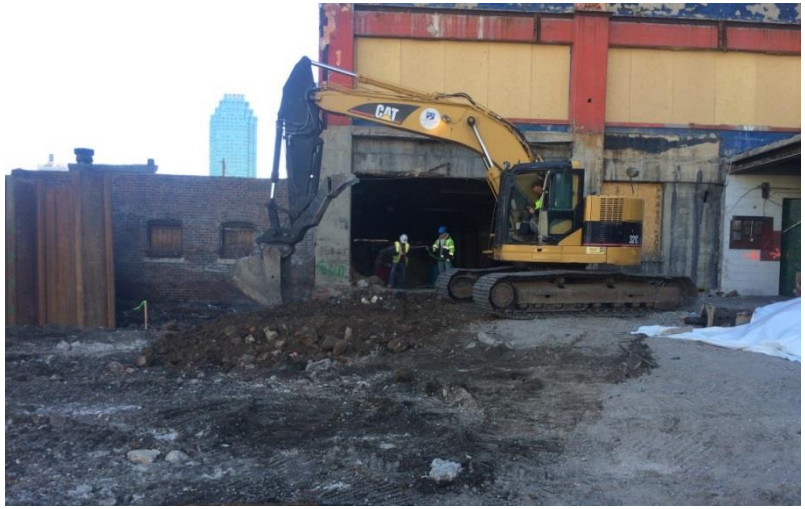

50. Photo taken on Monday, October 26, 2015. Looking east in courtyard; excavator removing ramp from courtyard to PFB.

51. Photo taken on Monday, October 26, 2015. Looking east in the courtyard; SCE laborer cutting excess steel sticking out of the ground following the sheet pile installation.

52. Photo taken on Monday, October 26, 2015. Looking at southeast corner of the courtyard; manhole/ access points for USTs D-1, D-2 and D-3.

53. Photo taken on Tuesday, October 27, 2015. Looking south down driveway at 46th Avenue; unloading 30' long sheet piles.

54. Photo taken on Tuesday, October 27, 2015. Looking southeast in courtyard; excavator with hammer attachment breaking up concrete around UST F-1 (UST D-4).

55. Photo taken on Tuesday, October 27, 2015. Looking north in the courtyard; SCE mobilizing sheet pile to install in NE corner of proposed excavation. Unable to install sheet because of concrete refusal.

56. Photo taken on Tuesday, October 27, 2015. Looking south across 46th Ave; delivery of Adler tank.

57. Photo taken on Wednesday, October 28, 2015. Looking west across the courtyard; loading truck with concrete generated in the courtyard.

58. Photo taken on Wednesday, October 28, 2015. Looking north in courtyard; excavator with hammer attachment breaking up concrete between UST D-1 and D-2.

59. Photo taken on Wednesday, October 28, 2015. Looking north in the courtyard; SCE installing sheeting along the northern wall of the excavation.

60. Photo taken on Wednesday, October 28, 2015. Looking west across courtyard; using shear attachment to cut a hole in UST D-1. The hole will allow SCE to gain access to the inside of the UST to clean out the residual tank bottoms.

61. Photo taken on Thursday, October 29, 2015. Looking south across dished UST excavation; material inside UST D-2.

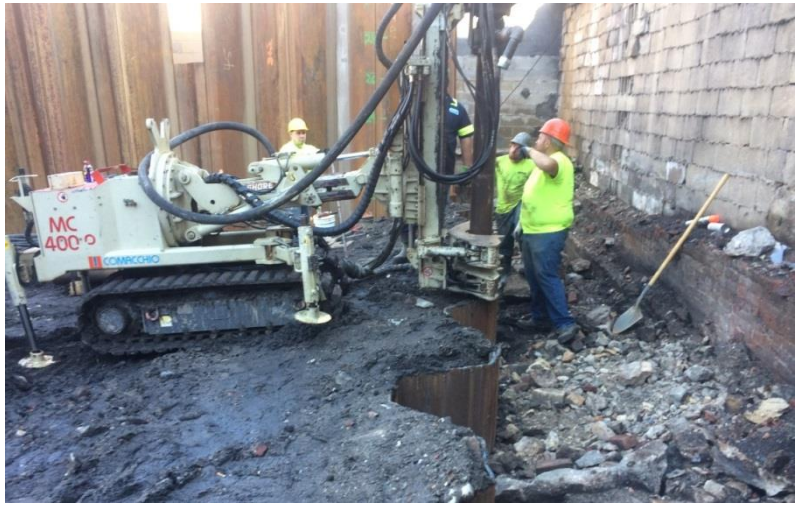

62. Photo taken on Thursday, October 29, 2015. Looking north in courtyard; Shore System Group installing toe pin along eastern sidewall of the proposed excavation.

63. Photo taken on Thursday, October 29, 2015. Looking west across the dished UST excavation; SCE breaking concrete between UST D-3 and D-4.

64. Photo taken on Thursday, October 29, 2015. Looking northeast across courtyard; SCE backfilling tank graves from UST D-1, D-2 and D-3 with soil from Grid SC-01 to prevent undermining the PFB.

65. Photo taken on Friday, October 30, 2015. Looking west down 46th Ave; unloading(x5) sheet piles for SOE.

66. Photo taken on Friday, October 30, 2015. Interior of UST D-1 post-decontamination and cleaning activities. Liquids and solids generated during cleaning were containerized in x2 labeled 55-gallon drums.

67. Photo taken on Friday, October 30, 2015. Looking north across the courtyard excavation; Shore System Group installing toe pin.

68. Photo taken on Friday, October 30, 2015. Looking northwest across courtyard; SCE crushing cleaned UST D-1 with excavator to prepare for disposal.

69. Photo taken on Monday, November 02, 2015. Looking down into the UST D-1 tank grave; rebar discovered in the concrete slab (arrow).

70. Photo taken on Monday, November 02, 2015. Looking north across courtyard; SCE installing sheet pile along the northern side of the excavation.

71. Photo taken on Monday, November 02, 2015. Looking west across the courtyard excavation; SCE staging UST D-2 on poly in courtyard.

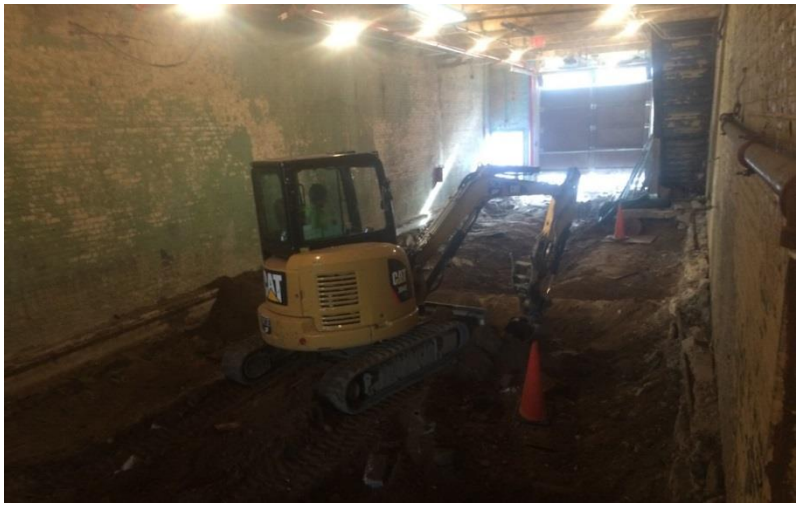

72. Photo taken on Monday, November 02, 2015. Looking south across garage; SCE clearing soil from the tops of the USTs in the garage to prepare for opening and cleaning of interiors.

73. Photo taken on Tuesday, November 03, 2015. Looking west down 46th Ave; tent components staged on sidewalk, as per DOT permits, prior to mobilization and staging in courtyard.

74. Photo taken on Tuesday, November 03, 2015 Looking east across courtyard; Shore System Group installing toe pins along eastern side of the excavation.

75. Photo taken on Tuesday, November 03, 2015. Looking north across the courtyard; installation of sheet piles along the northern extent of the excavation.

76. Photo taken on Tuesday, November 03, 2015. Looking south across garage; cut UST chamber GT-5C and GT-5B to remove contents and clean prior to backfilling to abandon in place.

77. Photo taken on Wednesday, November 04, 2015. Looking into east across the courtyard; cleaned UST D-2 stage in courtyard before it was moved to the 40 CY scrap metal dumpster.

78. Photo taken on Wednesday, November 04, 2015. Looking east across courtyard; Shore System Group installing toe pins along eastern side of the excavation. Laborer applying water for dust suppression.

79. Photo taken on Wednesday, November 04, 2015. Looking north across the courtyard; SP-SHED relocated to the north side of the courtyard to drive sheet piles. The stockpile was covered with poly after it was moved.

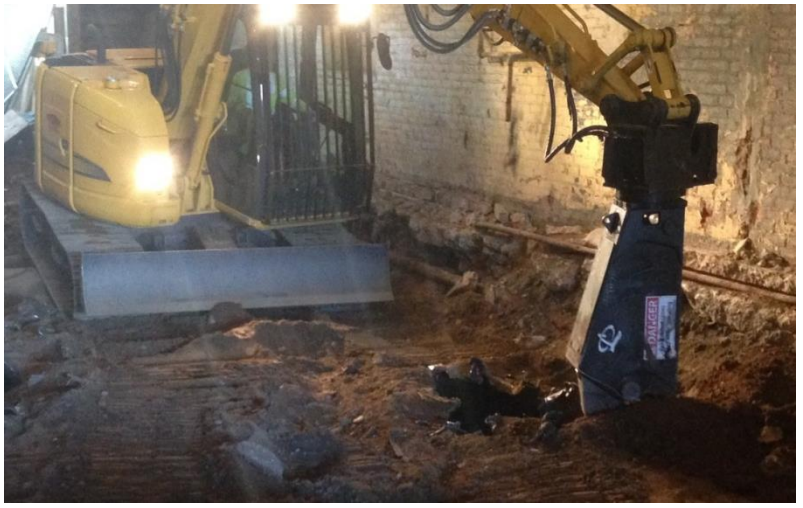

80. Photo taken on Wednesday, November 04, 2015. Looking southwest across garage; SCE using sheer to cut open UST G-1.

81. Photo taken on Thursday, November 05, 2015. Inside the garage facing south looking down into manhole area of UST GT-6; SCE removing concrete and cinderblocks surrounding to access tank.

82. Photo taken on Thursday, November 05, 2015. Looking east across courtyard; Shore System Group installing toe pins along northeast corner perimeter of the excavation. Laborer applying water for dust suppression.

83. Photo taken on Thursday, November 05, 2015. Looking west towards the courtyard; cutting of pipes removed from the concrete located in the garage near UST GT-6. The pipes were free of residual material associated with the site.

84. Photo taken on Thursday, November 05, 2015. Looking north across courtyard; SCE installing sheet piles along the western side of the excavation.

85. Photo taken on Friday, November 06, 2015. Looking northwest across the courtyard; SCE removing concrete obstructions from the path of the sheet pile installation on the west perimeter.

86. Photo taken on Friday, November 06, 2015. Looking northwest across courtyard; SCE installing a sheet pile for SOE on west perimeter of the excavation.

87. Photo taken on Friday, November 06, 2015. Looking northwest towards the courtyard; moving sheet piles from the west side of the courtyard to the north side of the courtyard.

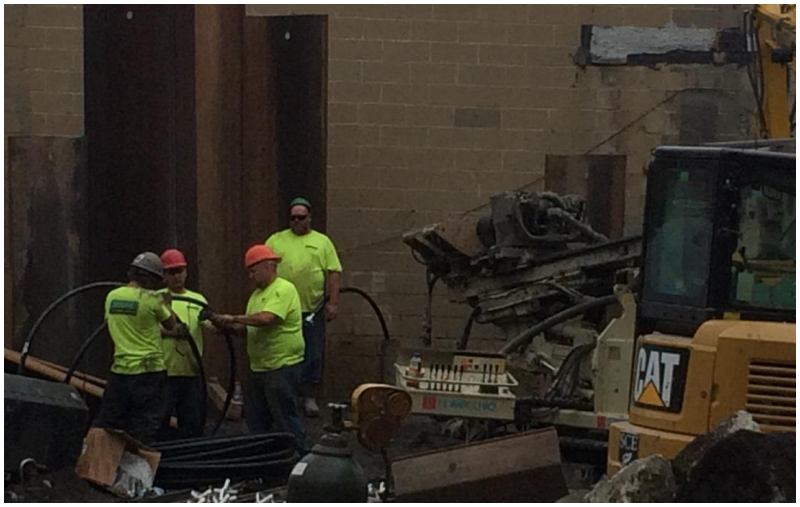

88. Photo taken on Friday, November 06, 2015. Looking northeast across courtyard; Shore System Group preparing to grout a toe pin.

89. Photo taken on Monday, November 09, 2015. Looking northeast across the courtyard; SCE moving concrete stockpile to the western side of the courtyard.

90. Photo taken on Monday, November 09, 2015. Looking north across courtyard; SCE cutting a sheet pile for SOE on the northern perimeter of the excavation.

91. Photo taken on Monday, November 09, 2015. Looking north across the courtyard; leveling the soil behind the installed sheet piles to prepare for the tent installation.

92. Photo taken on Monday, November 09, 2015. Looking north across courtyard; SCE mobilizing part of the tent frame.

93. Photo taken on Tuesday, November 10, 2015. Looking west across the courtyard; SCE loading concrete into truck for disposal offsite.

94. Photo taken on Tuesday, November 10, 2015. Looking northeast across courtyard; SCE lifting the first arch form for the tent.

95. Photo taken on Tuesday, November 10, 2015. Looking southwest across the courtyard; SCE driving one of the eight anchors into the southern base of the first tent arch form.

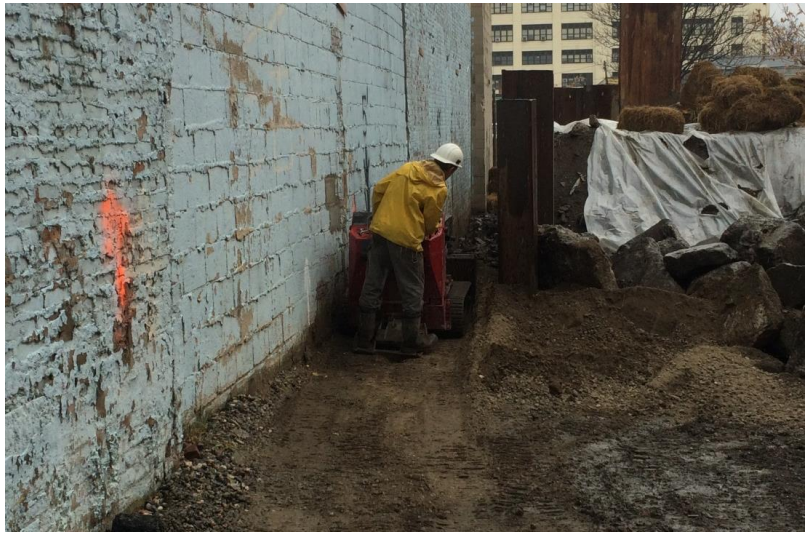

96. Photo taken on Tuesday, November 10, 2015. Looking north across courtyard; SCE leveling the soil behind the installed sheets on the western side of the courtyard.

97. Photo taken on Wednesday, November 11, 2015. Looking west across the courtyard; SCE breaking concrete slab to the west of USTs D-4 and D-5 in preparation of tent installation.

98. Photo taken on Wednesday, November 11, 2015. Looking southeast across courtyard; SCE cutting pipes removed from soil to the west of USTs D-4 and D-5.

99. Photo taken on Wednesday, November 11, 2015. Looking north across the courtyard; SCE attaching cable supports in between the two tent arch forms

100. Photo taken on Wednesday, November 11, 2015. Looking north across courtyard; SCE cutting down installed sheet piles to prepare for future tent installation.

101. Photo taken on Thursday, November 12, 2015. Looking northeast across the courtyard; SCE attaching tent covering over the braces between the two eastern tent arch forms.

102. Photo taken on Thursday, November 12, 2015. Looking west across courtyard; SCE unloading I-beams to be used as rakers and whalers for SOE.

103. Photo taken on Thursday, November 12, 2015. Looking north across the courtyard; SCE lifting the third tent arch form.

104. Photo taken on Thursday, November 12, 2015. Looking northeast across courtyard; Cross supports fully installed between the second and third arch supports from the eastern side of the excavation .

105. Photo taken on Friday, November 13, 2015. Looking northwest across the courtyard; SCE attaching tent covering over the braces between the second and third arch forms from the east.

106. Photo taken on Friday, November 13, 2015. Looking north across courtyard; SCE laborer welding holes in I-beam for pin holes for couplings that will facilitate the installation of the tent covering.

107. Photo taken on Friday, November 13, 2015. Looking east across the courtyard; SCE lifting the fourth tent arch form.

108. Photo taken on Friday, November 13, 2015. Looking northeast across courtyard; cross supports fully installed between third and fourth arch supports from the eastern side of the excavation.

109. Photo taken on Saturday, November 14, 2015. Looking northeast across the courtyard; cross beams between third and fourth arch tightened prior to attaching tent covering.

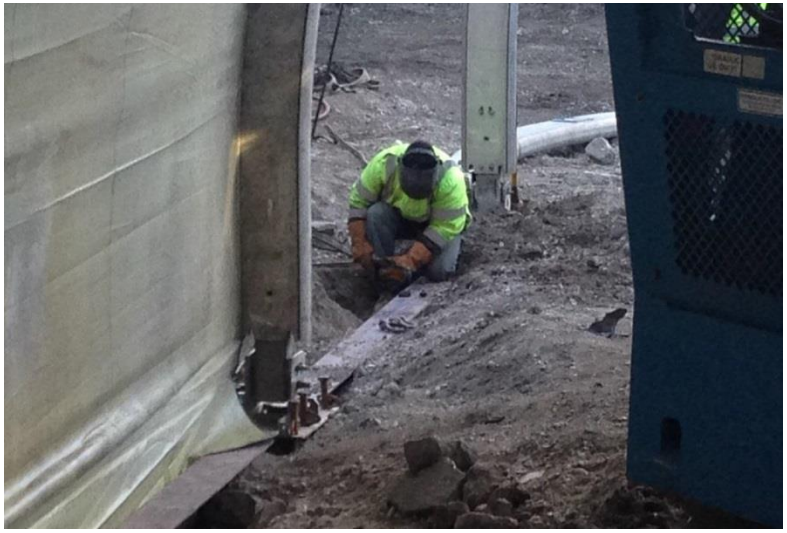

110. Photo taken on Saturday, November 14, 2015. Looking southwest across courtyard; SCE laborer welding holes in I-beam for pin holes for couplings that will facilitate the installation of the tent covering.

111. Photo taken on Saturday, November 14, 2015. Looking northeast across the courtyard; SCE constructing three (3) half arches on the ground that will be installed at future date.

112. Photo taken on Saturday, November 14, 2015. Looking northeast across courtyard; SCE began installation of tent covering between third and fourth arch from the eastern side of the excavation.

113. Photo taken on Monday, November 16, 2015. Looking east across the courtyard; Adler frac tank being loaded on truck for removal from site.

114. Photo taken on Monday, November 16, 2015. Looking down into UST GT-3A; SCE shoveling waste in UST GT-3A into 5-gallon buckets which were then brought to land surface. The waste was containerized in 55-gallon drums.

115. Photo taken on Monday, November 16, 2015. Looking northeast across the courtyard; SCE raising cross supports for eastern sidewall of tent.

116. Photo taken on Monday, November 16, 2015. Looking west across courtyard; SCE mobilizing x2 CY bags of carbon onsite for TIGG air filtration system.

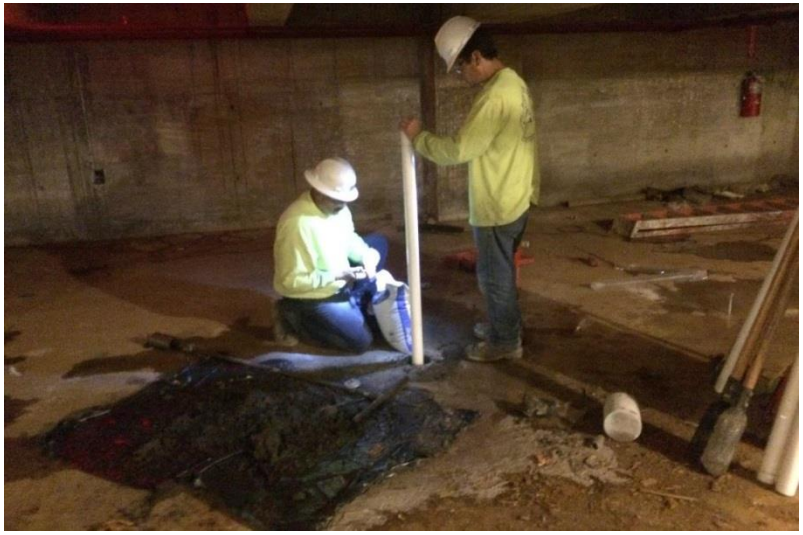

117. Photo taken on Tuesday, November 17, 2015. Looking northeast across the warehouse basement; Zebra installing injection point well IP-3.

118. Photo taken on Tuesday, November 17, 2015. Looking down into UST GT-3B; SCE shoveling waste in UST GT-3B into 5-gallon buckets which were then brought to land surface. The waste was containerized in 55-gallon drums.

119. Photo taken on Tuesday, November 17, 2015. Looking northeast across the courtyard; SCE raising fifth arch support of the tent.

120. Photo taken on Tuesday, November 17, 2015. Looking northeast across courtyard; SCE mobilizing x1 TIGG unit for air purification.

121. Photo taken on Wednesday, November 18, 2015. Looking west across the courtyard; SCE loading a truck with soil from SP-SHED.

122. Photo taken on Wednesday, November 18, 2015. Looking north across the courtyard; SCE installing the tent covering between the fourth and fifth arch supports.

123. Photo taken on Wednesday, November 18, 2015. Looking northeast across the courtyard; SCE raising sixth arch support of the tent.

124. Photo taken on Wednesday, November 18, 2015. Looking east across basement; row of newly installed injection wells IP-7, IP-8, IP-9 and IP-10.

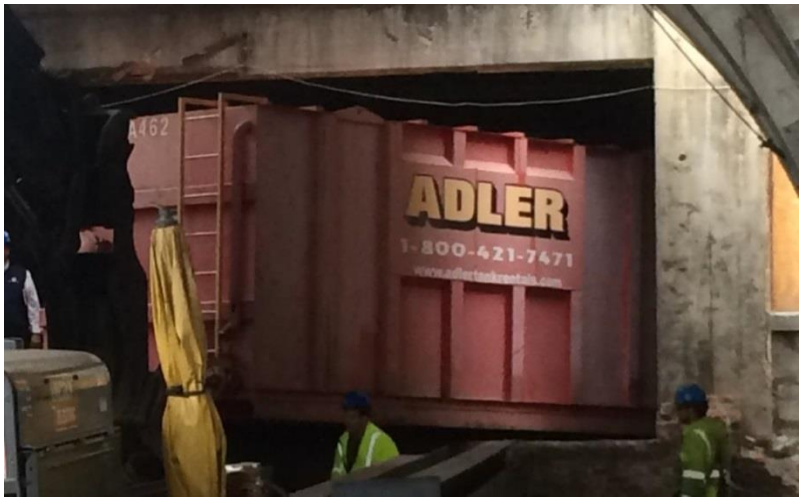

125. Photo taken on Thursday, November 19, 2015. Looking east across the courtyard; SCE staging Adler frac tank A462 in PFB.

126. Photo taken on Thursday, November 19, 2015. Looking northeast across the courtyard; SCE hanging cables between the fifth and sixth arch from the east side of the courtyard.

127. Photo taken on Thursday, November 19, 2015. Looking down in UST GT-4A; SCE shoveling waste out of UST GT-4A. Waste was brought to land surface and containerized in x3 55-gallon drums.

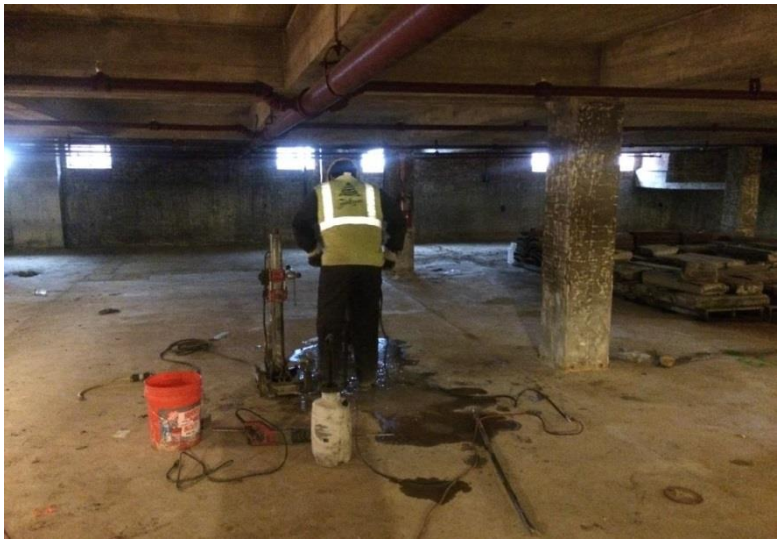

128. Photo taken on Thursday, November 19, 2015. Looking south across warehouse basement; Zebra installing injection well IP-13 in warehouse basement.

129. Photo taken on Friday, November 20, 2015. Looking north in courtyard under tent structure, SCE tightening and installing tarp cover between sixth and seventh tent arch.

130. Photo taken on Friday, November 20, 2015. Looking south inside the basement of warehouse, Zebra Environmental Corp. installing injection point wells.

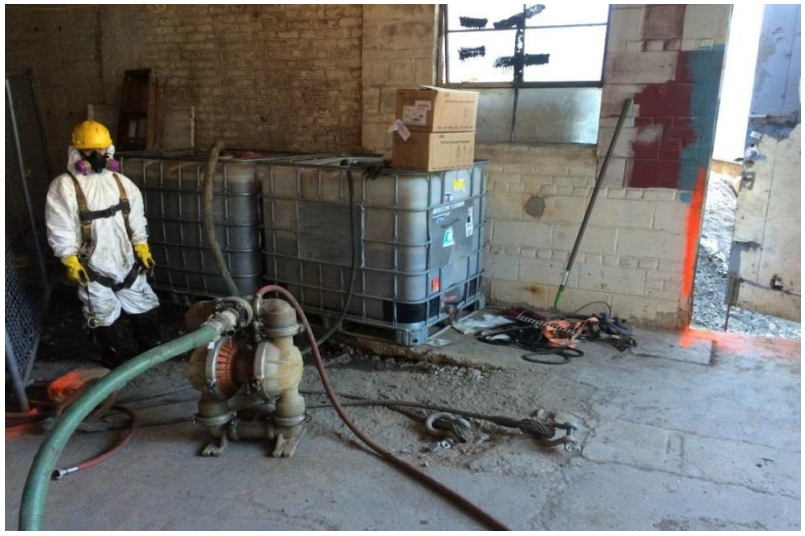

131. Photo taken on Friday, November 20, 2015. Inside the garage looking west, pump out of contents of GT-1 into nearby totes.

132. Photo taken on Friday, November 20, 2015. Looking east inside the tent; SCE installing the side cover of the tent structure

133. Photo taken on Monday, November 23, 2015. Looking east in courtyard, installation of TIGG system hosing between blower and carbon treatment system.

134. Photo taken on Monday, November 23, 2015. Looking northwest inside of tent structure, final loadout of SP-SHED stockpile.

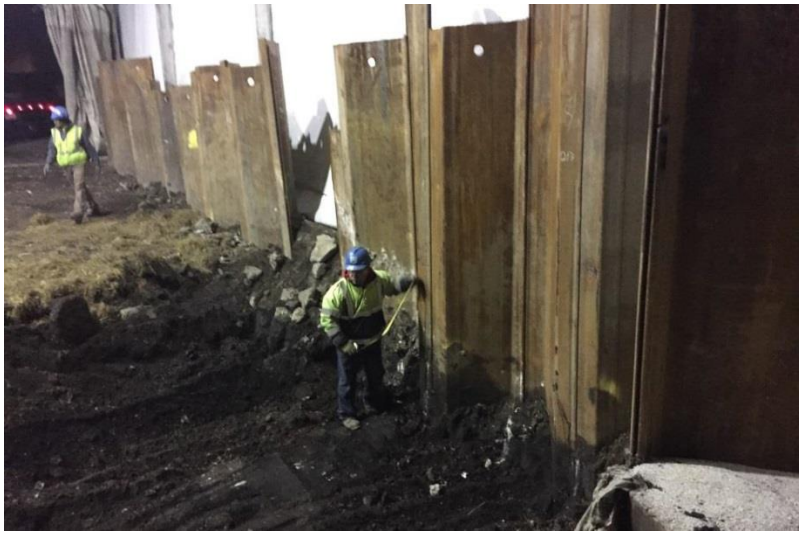

135. Photo taken on Monday, November 23, 2015. Inside tent structure in courtyard looking south; SCE beginning excavation of 5' cut reusable soil from excavation footprint

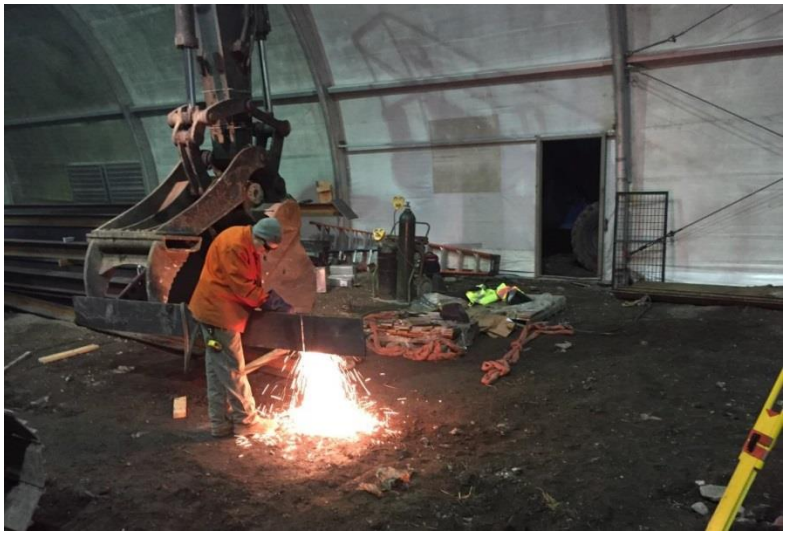

136. Photo taken on Monday, November 23, 2015. Looking southeast inside tent structure in courtyard; SCE continuing to weld whalers that will be used as SOE.

137. Photo taken on Tuesday, November 24, 2015. Looking northeast inside of excavation; setup pump to remove product on surface of recharged groundwater within the excavated area at 13 ft bls.

138. Photo taken on Tuesday, November 24, 2015 Looking northwest inside of tent structure; SCE welding whaler for SOE.

139. Photo taken on Tuesday, November 24, 2015. Inside tent structure in courtyard looking east; SCE stockpiling 5' cut of reusable soil from excavation footprint.

140. Photo taken on Tuesday, November 24, 2015. Looking northwest inside tent structure in courtyard; SCE cutting sheet near truck entrance to facilitate trucks entering and leaving the tent.

141. Photo taken on Wednesday, November 25, 2015. Looking west inside of excavation; implementation of odor suppressant on excavation soil.

142. Photo taken on Wednesday, November 25, 2015. Looking southwest inside of tent structure; SCE tarping trucks using bungee cords prior to truck engaging attached mechanical covering (two covers installed over material).

143. Photo taken on Wednesday, November 25, 2015. Inside tent structure in courtyard looking north; approximate location of sample SC-04-NW-B-14', sample taken at 14 ft bls (surveyed) to confirm excavation vertical extent.

144. Photo taken on Wednesday, November 25, 2015, Looking southwest inside basement; Zebra begins to inject RegenOx oxidant in injection monitoring points. Concentration is a 1:1 ratio of RegenOx Part A and Part B to 115 gallons of water.

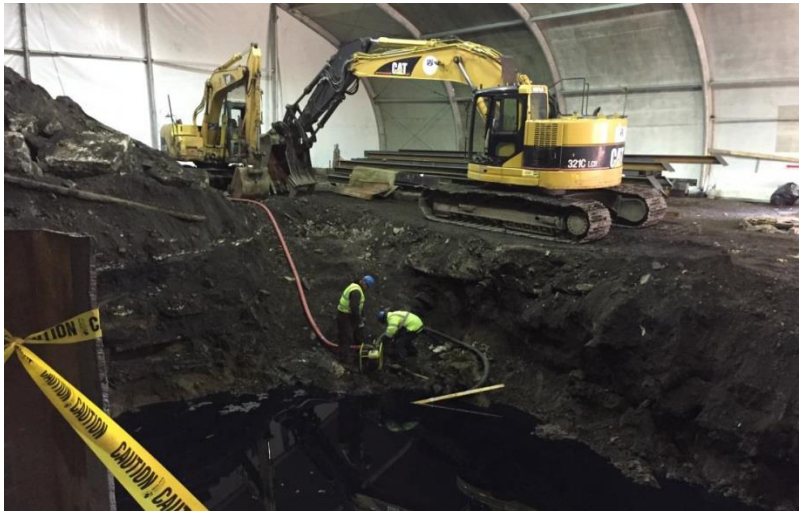

145. Photo taken on Monday, November 30, 2015. Looking northeast inside of excavation; setup pump to remove product on surface of recharged groundwater within the excavated area at 13 ft bls.

146. Photo taken on Monday, November 30, 2015. Looking southwest outside of tent structure; SCE extending truck wash and construction entrance with HDPE liner and clean stone.

147. Photo taken on Monday, November 30, 2015. Inside garage looking down into UST GT-2; removal of gel contents to be containerized in 55-gallon drums that are transported and staged in the PFB for future offsite disposal.

148. Photo taken on Monday, November 30, 2015. Looking north inside the tent structure; installation of whaler along the north perimeter of the sheeting, to be attached by welders prior to rakers installation.

149. Photo taken on Tuesday, December 01, 2015. Looking northwest inside of excavation; product on surface of recharged groundwater to be removed using a pump and stored in frac tank onsite prior to offsite disposal.

150. Photo taken on Tuesday, December 01, 2015. Looking southwest outside of tent structure; SCE reinforcing truck wash and construction entrance with additional load of clean stone.

151. Photo taken on Tuesday, December 01, 2015, Looking northeast inside the tent structure; creation of temporary sump using a perforated 55-gallon drum and clean stone to remove product and recharged groundwater from excavated footprint.

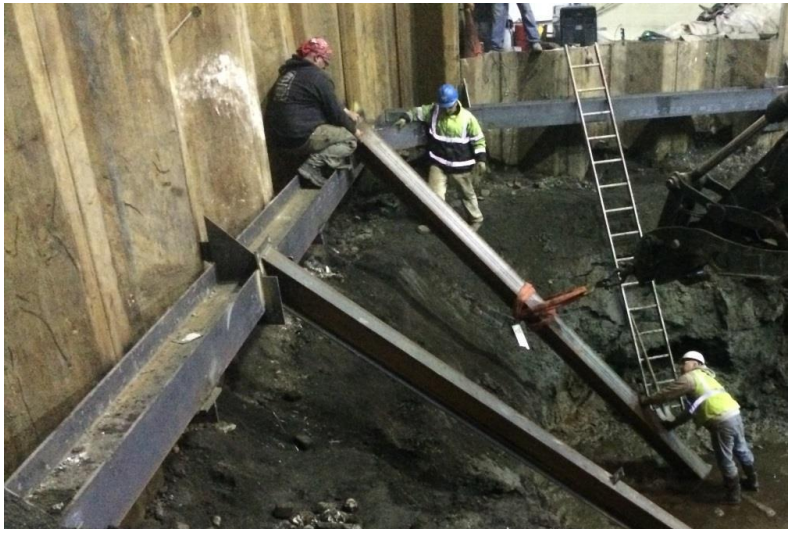

152. Photo taken on Tuesday, December 01, 2015. Looking north inside the tent structure; installation of rakers (x2) along the west wall to be used as support when sloped material (5-9 ft bls) is removed in future.

153. Photo taken on Wednesday, December 02, 2015, Looking south down site driveway; Zebra installing first injection point in driveway using Geoprobe. Injection material (RegenOx) injected using pump

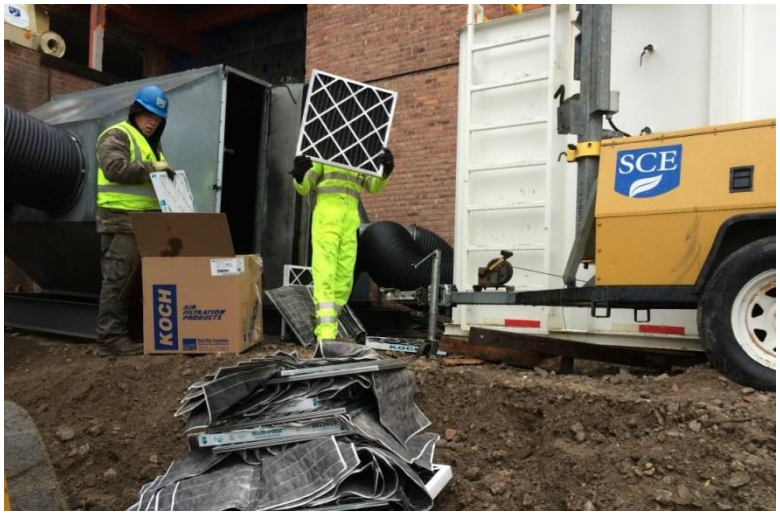

154. Photo taken on Wednesday, December 02, 2015, Looking southeast outside of tent structure; SCE exchanging air filter of TIGG system for continued use to remove vapors/odors

155. Photo taken on Wednesday, December 02, 2015, Looking northeast inside the tent structure; temporary sump removing product and recharged groundwater from excavation footprint, to be containerized in frac tank for future offsite disposal..

156. Photo taken on Wednesday, December 02, 2015, Looking north inside the tent structure; installation of rakers (x2) along the north wall to be used as support when sloped material (5-9 ft bls) is removed in future.

157. Photo taken on Thursday, December 03, 2015. Looking southwest down site driveway; truck leaving site with soil from SC-04 (9-14')

158. Photo taken on Thursday, December 03, 2015. Looking southwest down Site driveway; delivery of thrust blocks and corrugated drainage pipe to be used for rakers installation and dewatering activities.

159. Photo taken on Thursday, December 03, 2015, Looking down into UST GT-4A located inside the garage; encountered concrete when attempting to sample west sidewall.

160. Photo taken on Thursday, December 03, 2015. Looking north inside the tent structure; removal of soil sloping in north section of SC-04 due to raker support and installation.

161. Photo taken on Friday, December 04, 2015. Looking northwest inside of tent structure; SCE double tarped the truck using bungee cords prior to trunk engaging attached mechanical covering.

162. Photo taken on Friday, December 04, 2015. Looking down into UST GT-4; view of patched UST after attempted sampling. No sample collected at this point due to concrete refusal.

163. Photo taken on Friday, December 04, 2015. Looking southeast outside of the tent; SCE changing filters for TIGG unit.

164. Photo taken on Friday, December 04, 2015. Looking NW across the excavation; load of 3"-5" RCA being dumped into the northwest side of SC-04 which was cleared for backfill.

165. Photo taken on Saturday, December 05, 2015. Looking northwest inside of tent structure; SCE loading truck with material from SC-04.

166. Photo taken on Saturday, December 05, 2015. Looking northwest inside of tent structure; SCE double tarped the truck using bungee cords prior to trunk engaging attached mechanical covering.

167. Photo taken on Saturday, December 05, 2015. Looking southwest inside of tent at southern section of SC-04-NE. Bedrock encountered at 16 ft bls. Soil scraped from surface and disposed offsite.

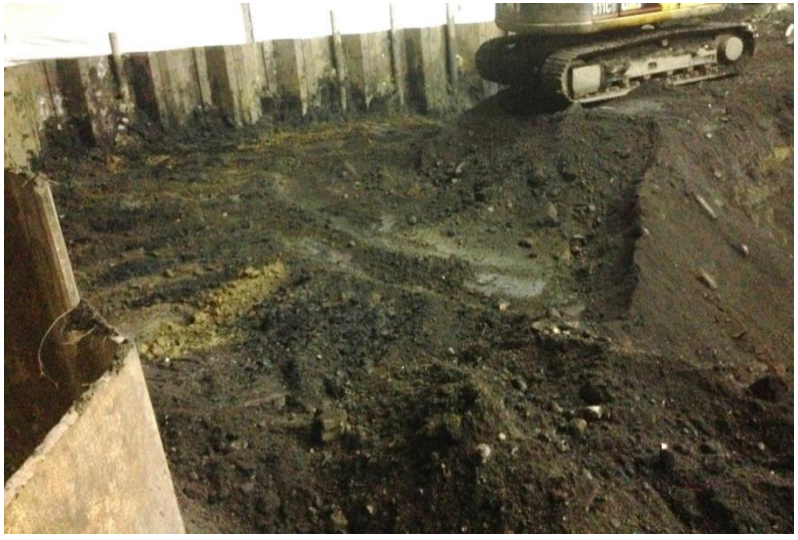

168. Photo taken on Saturday, December 05, 2015. Looking southeast across the excavation inside the tent structure; begin removal of SC-05 (0-5')reusable material; to be stockpiled on backfilled areas to prevent cross-contamination.

169. Photo taken on Monday, December 07, 2015. Looking north down Vernon Blvd.; SCE loading truck with x40 drums of material from USTs GT-2 and GT-4A.

170. Photo taken on Monday, December 07, 2015. Looking northeast inside of tent structure; SCE welding top whaler for SOE.

171. Photo taken on Monday, December 07, 2015. Looking northeast inside of tent; 3-5" RCA delivered to site for backfill.

172. Photo taken on Monday, December 07, 2015. Looking south inside garage; SCE containerizing material from GT-2 into 55-gallon drums.

173. Photo taken on Tuesday, December 08, 2015. Looking northeast in PFB; former area of SP-Garage after stockpile was moved to garage to be used as backfill for the cleaned USTs.

174. Photo taken on Tuesday, December 08, 2015. Looking east inside of tent structure; SCE welding raker to prepare for its installation in the northeast corner of the excavation.

175. Photo taken on Tuesday, December 08, 2015. Looking south inside of garage; SCE backfilling UST GT-3B.

176. Photo taken on Tuesday, December 08, 2015. Looking down inside UST GT-2 in garage; UST GT-2 after being cleaned by SCE.

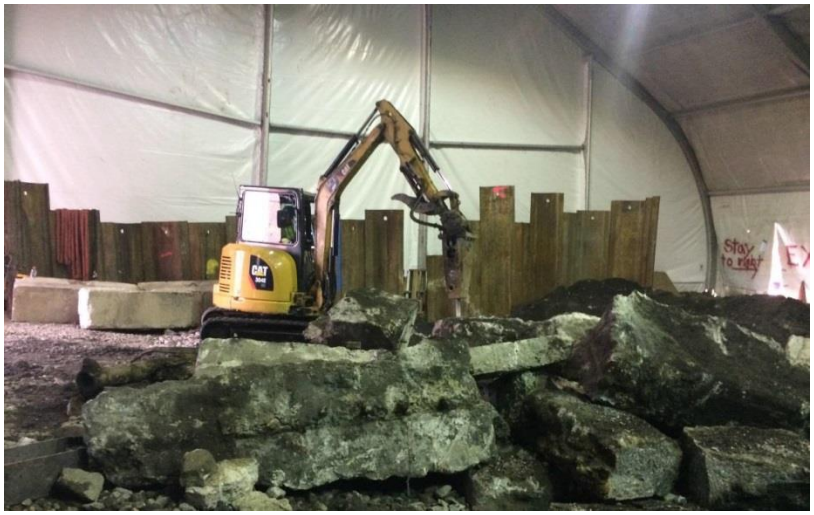

177. Photo taken on Wednesday, December 09, 2015. Looking northwest inside tent; SCE breaking up concrete that was removed from the excavation into smaller pieces to prepare for its disposal offsite.

178. Photo taken on Wednesday, December 09, 2015. Looking northeast inside of tent structure; SCE installing dewatering point in the northeast corner of the SC-05.

179. Photo taken on Thursday, December 10, 2015. Looking Southwest inside tent; Roux sampling SC-06/9-16 for disposal purposes.

180. Photo taken on Thursday, December 10, 2015. Looking northeast inside of tent structure; SCE installing whaler on eastern side of excavation.

181. Photo taken on Friday, December 11, 2015. Looking down into GT-6; SCE laborer cleaning inside of GT-6. It is not visible in photograph but laborer is attached to tripod.

182. Photo taken on Friday, December 11, 2015. Looking west down Vernon Blvd.; Truck loaded with x33 drums and x3 totes from garage UST cleaning.

183. Photo taken on Monday, December 14, 2015. Looking east down into GT-2; concrete refusal at GT-2-E-SW-9.

184. Photo taken on Monday, December 14, 2015. Looking north down driveway; ADT installing RW-02 with sonic rig.

185. Photo taken on Monday, December 14, 2015. Looking south out of garage; pumping out non-hazardous liquid from UST GT-5B into vac truck for disposal at Clean Earth – New Jersey.

186. Photo taken on Monday, December 14, 2015. Looking north inside tent; SCE loading truck with material from SC-05/5-9.

187. Photo taken on Tuesday, December 15, 2015. Looking north in tent; SCE securing tarp on truck carrying soil from SC-05/5-9.

188. Photo taken on Tuesday, December 15, 2015. Looking down in northeast corner of SC-05. Delineation in the color of the material is seen at 15 ft bls.

189. Photo taken on Tuesday, December 15, 2015. Looking northeast into garage; pumping out non-hazardous liquid from UST GT-5C into vac truck for disposal at Clean Earth – New Jersey.

190. Photo taken on Tuesday, December 15, 2015. Looking north in garage; SCE cleaning UST GT-5B.

191. Photo taken on Wednesday, December 16, 2015. Looking north in tent; SCE loading truck carrying soil from SC-05/9-19.

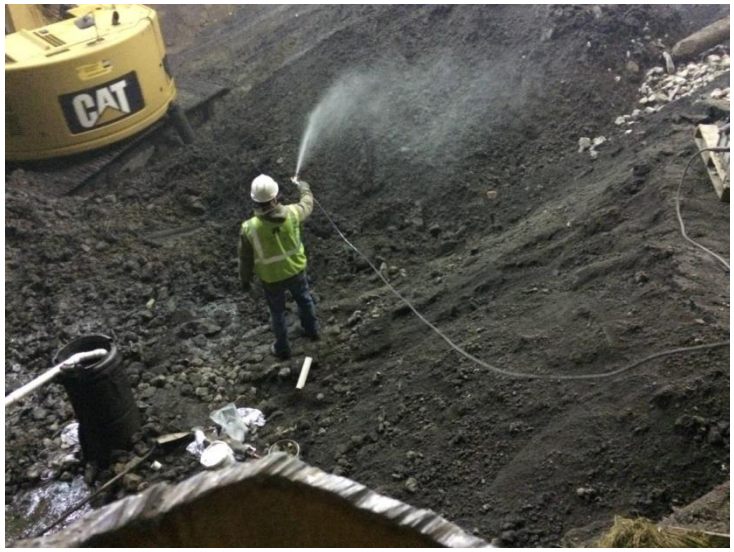

192. Photo taken on Wednesday, December 16, 2015. Looking southeast in SC-05; SCE laborer applying odor suppression in excavation..

193. Photo taken on Wednesday, December 16, 2015. Looking down into UST GT-5C; UST GT-5C is finished being cleaned.

194. Photo taken on Wednesday, December 16, 2015. Looking south in garage; SCE backfilling cleaned USTs.

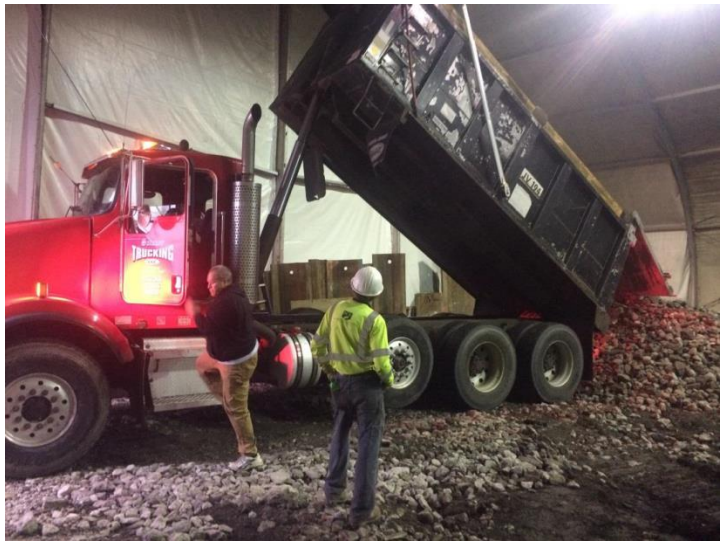

195. Photo taken on Thursday, December 17, 2015. Looking northwest in tent; truck dumping 3-5" RCA into northwest corner of SC-04.

196. Photo taken on Thursday, December 17, 2015. Looking south in garage; SCE laborer backfilling GT-1 with 1.5-2" clean RCA.

197. Photo taken on Thursday, December 17, 2015. Looking northeast in PFB; former area of SP-Garage after stockpile was moved to garage to be used as backfill for the cleaned USTs.

198. Photo taken on Thursday, December 17, 2015. Looking northeast in tent; North section of SC-05 backfilled with 3-5" clean RCA.

199. Photo taken on Friday, December 18, 2015. Looking southeast in tent; example of a massive boulder uncovered during excavation of SC-05. Soil around boulders was removed but boulders were left in place because they couldn't be moved.

200. Photo taken on Friday, December 18, 2015. Looking east down 46th Ave; truck dumping 1.5" RCA into garage to continue backfilling above the filled USTs.

201. Photo taken on Friday, December 18, 2015. Looking north in PFB, oily water unintentionally spilled in PFB from frac tank. Spill was reported to NYSDEC and cleaned within two hours.

202. Photo taken on Friday, December 18, 2015. Looking southeast in tent; concrete slab encountered in south side of SC-05.

203. Photo taken on Saturday, December 19, 2015. Looking northeast in tent; SCE moving newly dumped 3-5" clean RCA to the north side of SC-05.

204. Photo taken on Saturday, December 19, 2015. Looking east in tent; sump pump installed next to northwest corner of concrete slab that used to be beneath the dished USTs for dewatering SC-05.

205. Photo taken on Monday, December 21, 2015. Looking east in tent; product and groundwater collection in the south side of SC-05.

206. Photo taken on Monday, December 21, 2015. Looking northeast in tent; SCE tarping truck filled with soil from SC-05/9-19. The tarp was secured with bungie cords.

207. Photo taken on Monday, December 21, 2015. Looking east in tent; SCE cut hole in the side of the sheeting to allow Roux to collect sidewall sample PD-10/4-6.

208. Photo taken on Monday, December 21, 2015. Looking north in tent; stockpile of the 0-5 ft bls layer of soil from southwest side of SC-04

209. Photo taken on Tuesday, December 22, 2015. Looking east in tent; SCE laborer cleaning UST D-4.

210. Photo taken on Tuesday, December 22, 2015. Looking down under former truck entrance; southwest corner of SC-04 excavated down to 17 ft.

211. Photo taken on Tuesday, December 22, 2015. Looking north in tent; SCE backfilling SC-04 under former tent entrance with 3-5" RCA.

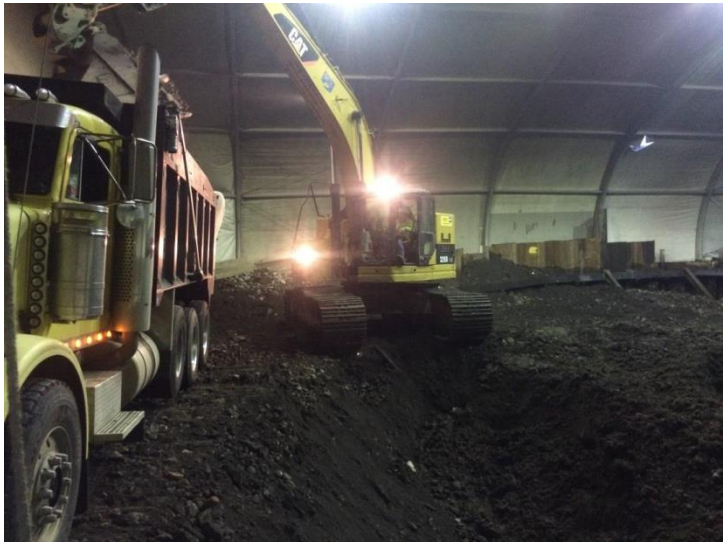

212. Photo taken on Tuesday, December 22, 2015. Looking north in tent; tent entrance reestablished after backfilling the southwest corner of SC-04. Stockpile of excavated material from SC-05/5-13 being loaded into a truck for disposal at Cumberland County Landfill.

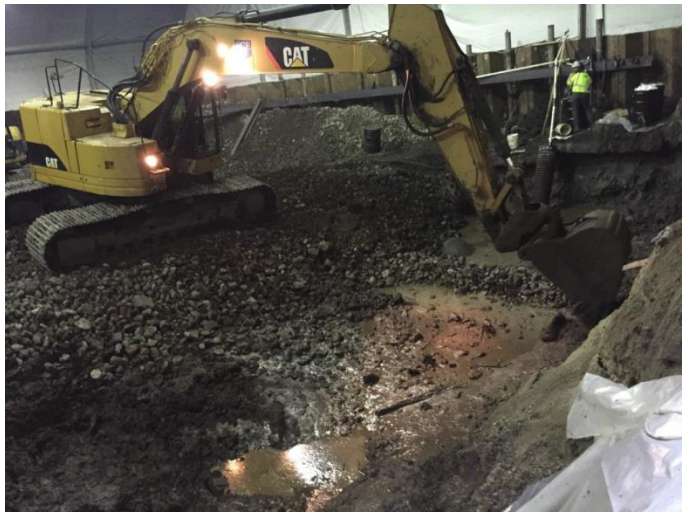

213. Photo taken on Wednesday, December 23, 2015. Looking east in tent; SCE backfilling south side of SC-05 with RCA.

214. Photo taken on Wednesday, December 23, 2015. Looking southwest in tent; SCE loading out soil from SC-04/5-9 into truck for disposal at Cumberland County Landfill.

215. Photo taken on Wednesday, December 23, 2015. Looking down into the southeast corner of the excavation under the tent; SCE installing sump pump for dewatering in southeast corner of SC-05.

216. Photo taken on Wednesday, December 23, 2015. Looking southwest in tent; truck dumping load of 3-5" RCA into corner of SC-04 for use as backfill.

217. Photo taken on Monday, December 28, 2015. Looking northeast in tent; SCE beginning to dewater at the start of day prior to excavation to 17 ft bls.

218. Photo taken on Monday, December 28, 2015. Looking south down driveway; vac out activated carbon from TIGG system. Carbon to be disposed off-site at approved facility.

219. Photo taken on Monday, December 28, 2015. Looking northwest outside of tent; tarped truck leaving site with material from SC-04(9-13).

220. Photo taken on Monday, December 28, 2015. Looking east inside tent; RCA being used to backfill excavation after final depth confirmed.

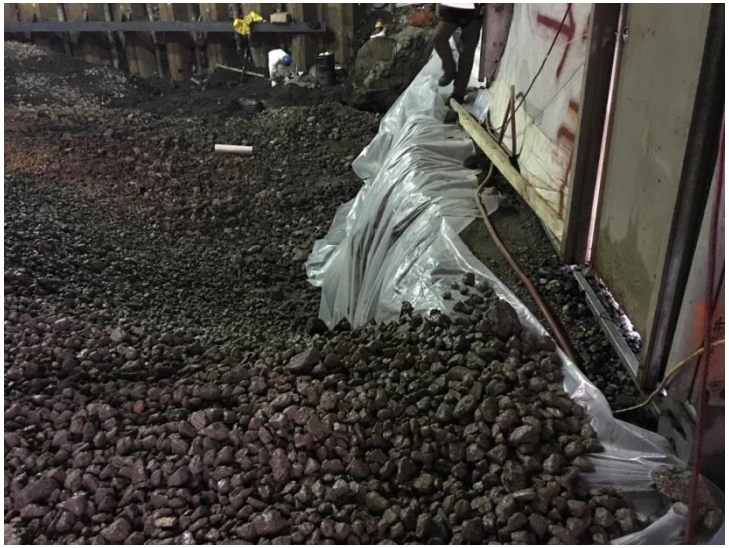

221. Photo taken on Tuesday, December 29, 2015. Looking east in tent; poly laid down between clean RCA and impacted soil to be excavated in future.

222. Photo taken on Tuesday, December 29, 2015. Looking northeast inside tent; continue transport of RCA to site to be used as backfill.

223. Photo taken on Tuesday, December 29, 2015. Looking east inside of tent; cleaning UST D-4 prior to future removal.

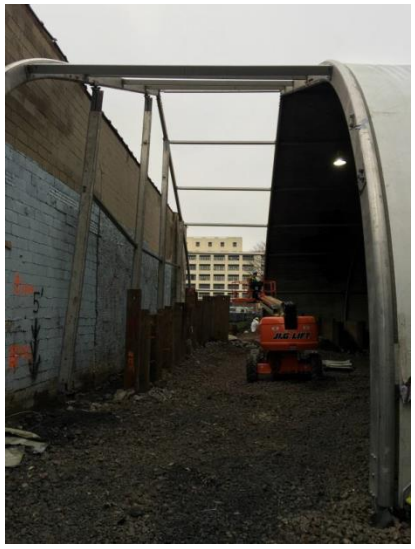

224. Photo taken on Tuesday, December 29, 2015. Looking north outside of tent; begin removal of structure coverings and tension wires.

225. Photo taken on Wednesday, December 30, 2015. Looking north towards tent; continue to remove tent fabric and cross beams from arches.

226. Photo taken on Wednesday, December 30, 2015. Looking northeast inside tent; continue transport of RCA to site to be used as backfill.

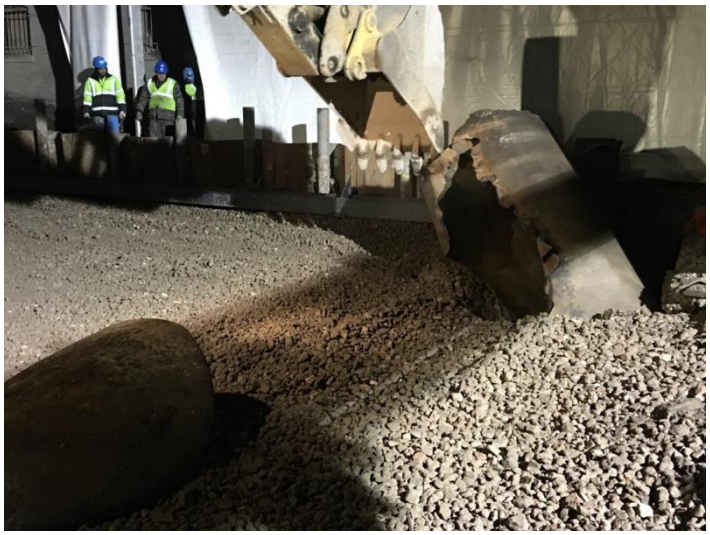

227. Photo taken on Wednesday, December 30, 2015. Looking east inside of tent; removal of dished UST D-4. Staged on poly for future disposal.

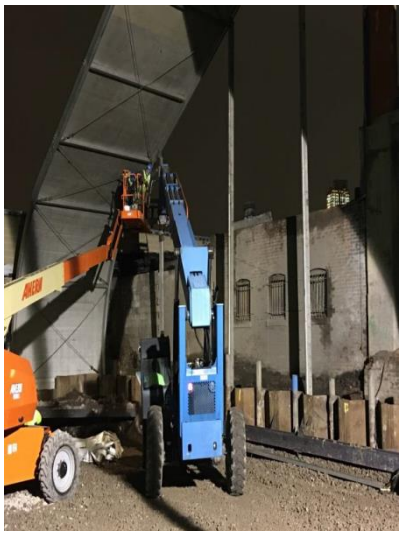

228. Photo taken on Wednesday, December 30, 2015. Looking northeast towards the tent; removal of vertical supports on east of tent.

229. Photo taken on Thursday, December 31, 2015. Looking north across courtyard; continue to demobilize tent arches.

230. Photo taken on Thursday, December 31, 2015. Looking northeast across courtyard; continue to remove cross beams from arches.

231. Photo taken on Monday, January 4, 2016. Looking south across courtyard; blower from TIGG unit prepared for demobilization from site.

232. Photo taken on Monday, January 4, 2016. Looking southwest across 46th Ave; TIGG unit loaded on truck for removal from site.

233. Photo taken on Monday, January 4, 2016. Looking southeast across PFB; SCE laborer setting up hose from vac truck to pump out water from frac tank A462 that was generated from dewatering the courtyard excavation.

234. Photo taken on Monday, January 4, 2016. Looking north across courtyard; disassembled arch stacked and staged for removal from site.

235. Photo taken on Tuesday, January 5, 2016. Looking northeast across courtyard; SCE laborers removing cross beams from remaining arch supports.

236. Photo taken on Tuesday, January 5, 2016. Looking north across courtyard; disassembled tent structure stacked and staged for removal from site.

237. Photo taken on Wednesday, January 6, 2016. Looking northeast across courtyard; truck dumping load of 3-5" RCA into a stockpile in the courtyard.

238. Photo taken on Wednesday, January 6, 2016. Looking west down 46th Avenue; tent components loaded on truck for removal from site.

239. Photo taken on Thursday, January 7, 2016. Looking northeast across courtyard; excavator removing UST D-5 from concrete encasement.

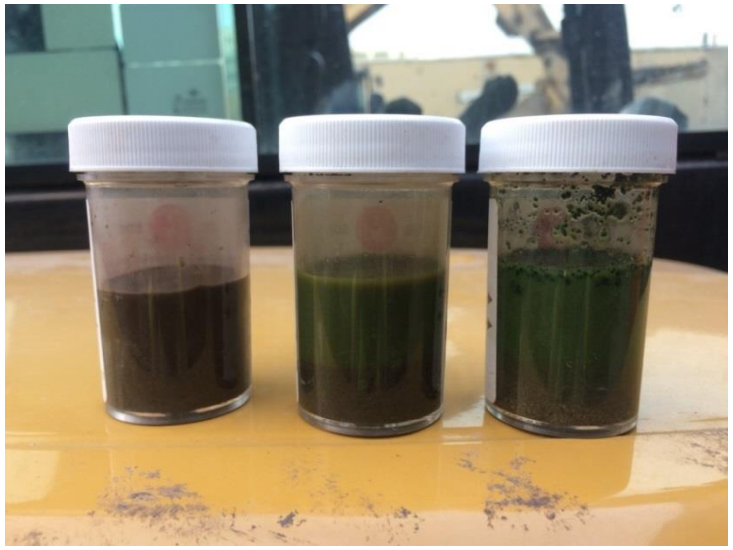

240. Photo taken on Thursday, January 7, 2016. All three oil-in-soil tests that were collected from the UST sidewalls were negative for oil.

241. Photo taken on Thursday, January 7, 2016. Looking northeast into UST D-5; UST D-5 after cleaning.

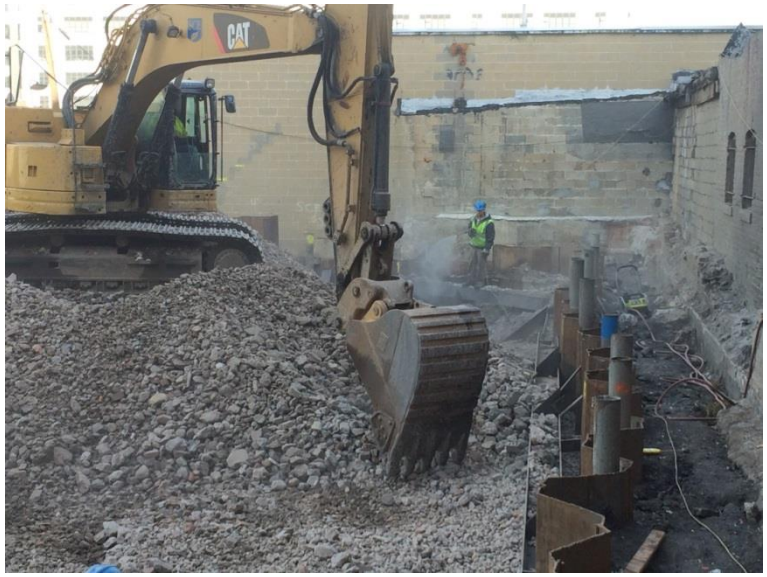

242. Photo taken on Thursday, January 7, 2016. Looking north across the courtyard; SCE applied dust suppression while stockpile of RCA was moved to the northeast corner.

243. Photo taken on Monday, January 11, 2016. Looking southwest out of the garage; Zebra drilling at GT-5C-W-B/MW-40.

244. Photo taken on Monday, January 11, 2016. Looking southwest down 46th Ave; x8 concrete blocks loaded on truck for removal from site.

245. Photo taken on Wednesday, January 13, 2016. Looking southeast in garage; Zebra drilling at GT-6-E-SW. Sample was collected from 6.5-8.5 ft bls.

246. Photo taken on Wednesday, January 13, 2016. Looking north across the courtyard; Zebra drilling to collect sub-slab sample D-1 B/11-13 ft.

247. Photo taken on Monday, January 18, 2016. Looking northwest in courtyard; SCE crushing cleaned UST D-5 to allow it to fit in a roll-off for recycling.

248. Photo taken on Monday, January 18, 2016. Looking north into test pit near former location of MW-13; SCE dug a test pit on behalf of the structural engineer.

249. Photo taken on Monday, January 18, 2016. Looking east in PFB; SCE cleaning frac tank A462 to prepare for its removal from site.

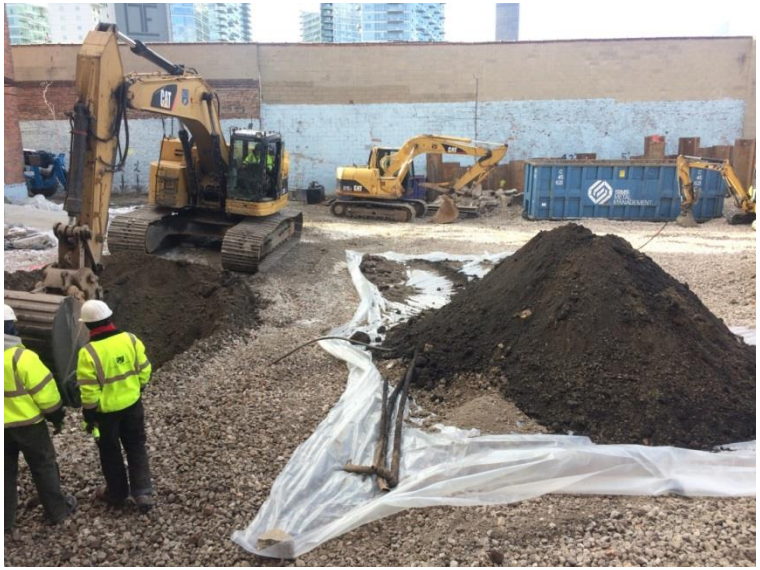

250. Photo taken on Monday, January 18, 2016. Looking west across the courtyard; SCE removing top 5 ft of material that has been approved for reuse onsite to prepare for excavation in the southside of SC-05.

251. Photo taken on Tuesday, January 19, 2016. Looking southeast in courtyard; SCE scraping the bottom of the courtyard UST concrete slab.

252. Photo taken on Tuesday, January 19, 2016. Looking west across the courtyard; SCE backfilling SC-05 with 3-5" RCA.

253. Photo taken on Tuesday, January 19, 2016. Looking east in PFB; SCE cleaning frac tank A6024 to prepare for its removal from site.

254. Photo taken on Tuesday, January 19, 2016. Looking west across the courtyard; SCE loading trucks with material from SC-05/5-13.

255. Photo taken on Wednesday, January 20, 2016. Looking south in courtyard; SCE excavated the area east of UST GT-6 and west of the concrete slab side wall. Northwest side of UST GT-6 was exposed.

256. Photo taken on Wednesday, January 20, 2016. Looking east from courtyard; staining on concrete slab under UST GT-6.

257. Photo taken on Wednesday, January 20, 2016. Looking west across courtyard; SCE loading truck with material from SC-04/5-13.

259. Photo taken on Thursday, January 21, 2016. Looking west in courtyard; SCE loading trucks with material from driveway excavation.

258. Photo taken on Wednesday, January 20, 2016. Looking east across the courtyard; SCE excavating down to the concrete slab that was below the former 20,000 gallon courtyard USTs in SC-04.

260. Photo taken on Thursday, January 21, 2016. Looking west across driveway excavation; SCE backfilling with 3-5" RCA.

261. Photo taken on Thursday, January 21, 2016. Looking northeast across driveway excavation; SCE digging out grossly contaminated material from driveway.

262. Photo taken on Thursday, January 21, 2016. Looking south next to GT-6; SCE excavating material in PD-12 down to 13 ft bls.

263. Photo taken on Friday, January 22, 2016. Looking west across courtyard; SCE loading frac tank A6024 on truck for removal from site.

264. Photo taken on Friday, January 22, 2016. Looking north across courtyard; site secured for upcoming blizzard.

265. Photo taken on Monday, January 25, 2016. Looking west across courtyard; Site prior to snow removal.

266. Photo taken on Monday, January 25, 2016. Looking west across courtyard; SCE moving snow to stockpile it on the NE corner of the courtyard.

267. Photo taken on Tuesday, January 26, 2016. Looking northeast across courtyard; SCE removing soil plug from excavation.

268. Photo taken on Tuesday, January 26, 2016. Looking down at MW-2R; Roux groundwater sampling MW-2R.

269. Photo taken on Wednesday, January 27, 2016. Looking northwest in courtyard; SCE removing soil north of the driveway excavation.

270. Photo taken on Wednesday, January 27, 2016. Looking west across courtyard; SCE laborer laying out delineation material to mark

271. Photo taken on Wednesday, January 27, 2016. Looking south across 46th Avenue; SCE loading CAT 311 excavator for removal from site.

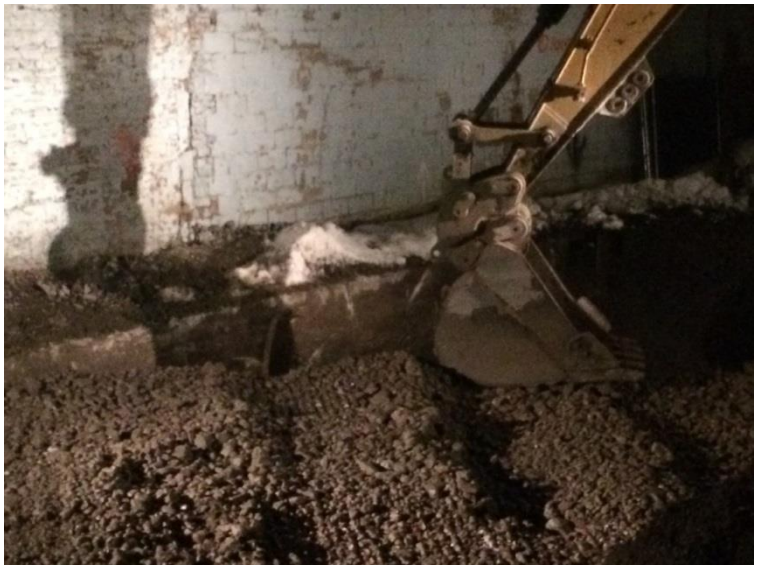

272. Photo taken on Wednesday, January 27, 2016 Looking northwest in courtyard; SCE backfilling excavation north of the driveway.

273. Photo taken on Thursday, January 28, 2016. Looking south down driveway; Truck filled with soil from SC-04 about to leave site.

274. Photo taken on Thursday, January 28, 2016. Looking northwest across courtyard; RCA moved from northwest corner and middle of the site to backfill driveway and SW corner of SC-04.

275. Photo taken on Thursday, January 28, 2016. Looking north down driveway; Genie GTH-1056 staged for removal from site.

276. Photo taken on Thursday, January 28, 2016. Looking east in PFB; SCE transferring purge water from drum into the frac tank.

277. Photo taken on Friday, January 29, 2016. Looking north across the courtyard; Truck dumping ~22 CY of 1.5-2" RCA into courtyard.

278. Photo taken on Friday, January 29, 2016. Looking north across courtyard; SCE grading RCA in northeast corner of the site.

279. Photo taken on Monday, February 1, 2016. Looking east across the courtyard; SCE welder cutting whaler off of sheet piles.

280. Photo taken on Monday, February 1, 2016. Looking south across courtyard; Stockpile of concrete and stacked slide rail.

281. Photo taken on Tuesday, February 2, 2016. Looking north across the courtyard; SCE welder and laborer cutting whaler off of the sheet piles on the western side of the courtyard excavation.

282. Photo taken on Tuesday, February 2, 2016. Looking north across courtyard; Stockpile of toe pin segments staged for removal from site.

283. Photo taken on Thursday, February 4, 2016. Looking south inside garage; SCE operator moving RCA from over the north end of UST GT-1 to provide access to the top of the tank for the surveyor.

284. Photo taken on Thursday, February 4, 2016. Looking south inside garage; SCE operator moving RCA from over UST GT-3B to provide access to the top of the tank for the surveyor.

285. Photo taken on Monday, February 8, 2016. Looking northwest across courtyard; SCE pulling sheet piles out from the eastern side of the courtyard excavation footprint.

286. Photo taken on Monday, February 8, 2016. Looking north across courtyard; SCE welder cutting holes in sheet piles to prepare for their removal from the excavation.

287. Photo taken on Tuesday, February 9, 2016. Looking southeast in PFB; SCE pumping wastewater from dewatering the courtyard excavation into a vac truck.

288. Photo taken on Tuesday, February 9, 2016. Looking southwest across 46th Ave, SCE loading slide rail shoring onto truck for removal from site.

289. Photo taken on Tuesday, February 9, 2016. Looking inside frac tank A273; SCE laborer cleaning sediment from the bottom of the frac tank.

290. Photo taken on Tuesday, February 9, 2016. Looking west across courtyard; SCE grading RCA in the north end of the driveway.

291. Photo taken on Wednesday, February 10, 2016. Looking north across courtyard; Loading concrete into triaxle for removal from site.

292. Photo taken on Wednesday, February 10, 2016. Looking north across courtyard; Triaxle dumping RCA in southwest corner of courtyard.

293. Photo taken on Wednesday, February 10, 2016. Looking northwest across courtyard; SCE removing frac tank A462 from site.

294. Photo taken on Wednesday, February 10, 2016. Looking west across courtyard, SCE grading RCA on south side of courtyard.

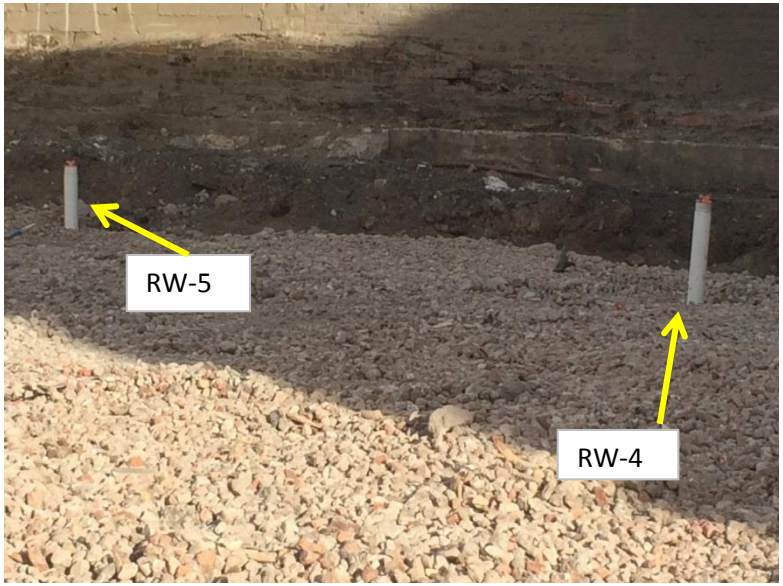

295. Photo taken on Thursday, February 11, 2016. Looking northeast across courtyard; Recovery wells RW-4 and RW-5.

296. Photo taken on Thursday, February 11, 2016. Looking west across courtyard; Zebra preparing to install recovery well RW-3.

297. Photo taken on Thursday, February 11, 2016. Looking down at RW-3; Zebra installing flush-mount box over recovery well RW-3.

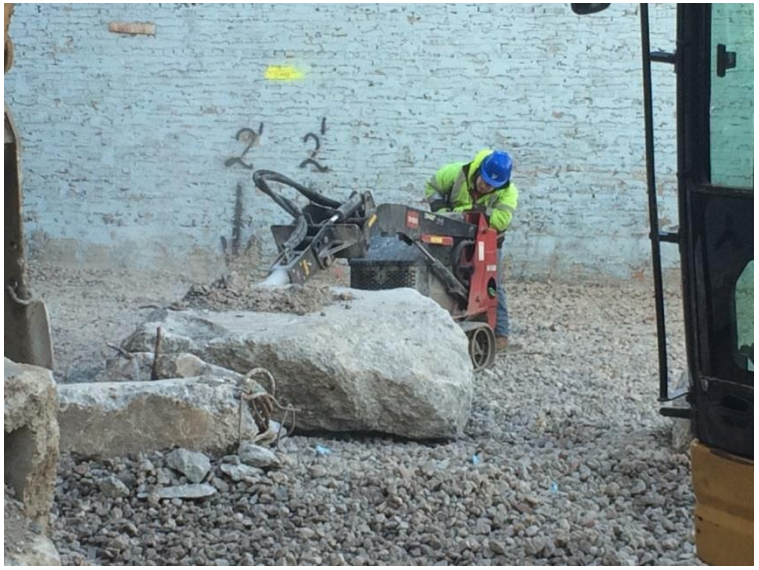

298. Photo taken on Thursday, February 11, 2016. Looking west across courtyard; SCE breaking apart concrete to prepare for its removal from site.

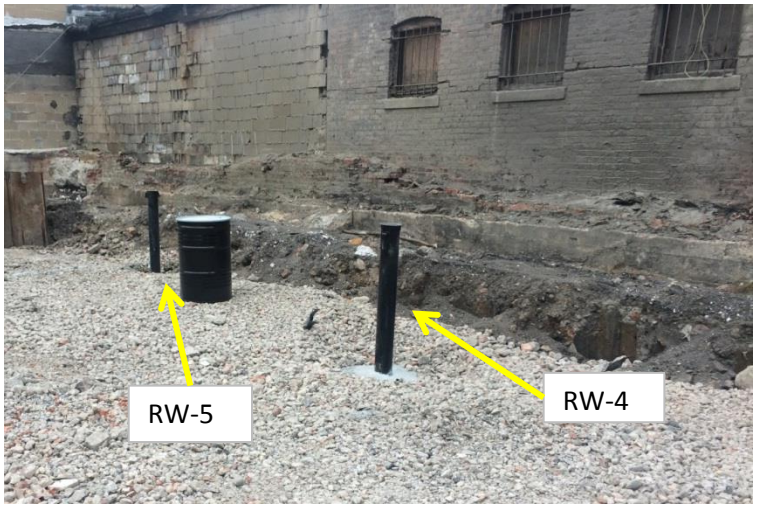

299. Photo taken on Friday, February 12, 2016. Looking northeast across courtyard; Recovery wells RW-4 and RW-5.

300. Photo taken on Friday, February 12, 2016. Looking northwest across driveway; Zebra developing recovery well RW-2.

301. Photo taken on Monday, February 15, 2016. Looking north across driveway; SCE removed RCA from driveway to prepare for asphalt.

302. Photo taken on Monday, February 15, 2016. Looking south across driveway; SCE breaking concrete for recovery well system PVC installation.

303. Photo taken on Tuesday, February 16, 2016. Looking south across southeast corner of courtyard; SCE moving reuse soil from ramp area outside the door from the garage to the former location of UST D-5.

304. Photo taken on Tuesday, February 16, 2016. Looking south across driveway; SCE cutting concrete for recovery well system PVC installation.

305. Photo taken on Wednesday, February 17, 2016. Looking north across courtyard; Truck dumping load of 1.5" RCA.

306. Photo taken on Wednesday, February 17, 2016. Looking south across driveway; SCE finished cutting concrete for recovery well system PVC installation.

307. Photo taken on Thursday, February 18, 2016. Looking south across courtyard; SCE backfilling UST GT-6 with flowable fill.

308. Photo taken on Thursday, February 18, 2016. Looking down at UST GT-6 manway; UST GT-6 completely backfilled with flowable fill.

309. Photo taken on Thursday, February 18, 2016. Looking north across courtyard; SCE removing sheet piles.

310. Photo taken on Thursday, February 18, 2016. Looking south across driveway; SCE removing broken concrete from driveway to prepare for PVC piping

311. Photo taken on Friday, February 19, 2016. Looking northwest across courtyard; Clean sand delivered to site to be used as pipe bedding for recovery well system.

312. Photo taken on Friday, February 19, 2016. Looking north across driveway; SCE digging trench in driveway to prepare for PVC piping installation.

313. Photo taken on Monday, February 22, 2016. Looking northwest across courtyard; removal of sheets from the north perimeter of the excavation.

314. Photo taken on Monday, February 22, 2016. Looking south across driveway; SCE installing conduit for recovery system; backfilling being completed where piping has been

315. Photo taken on Tuesday, February 23, 2016. Looking northwest across courtyard; removal of sheets from the west perimeter of the excavation.

316. Photo taken on Tuesday, February 23, 2016. Looking west across courtyard; 4" PVC installed at approximately 4' bls with clean, virgin-source sand approx. 4" above and below. Area backfilled with RCA following PVC placement.

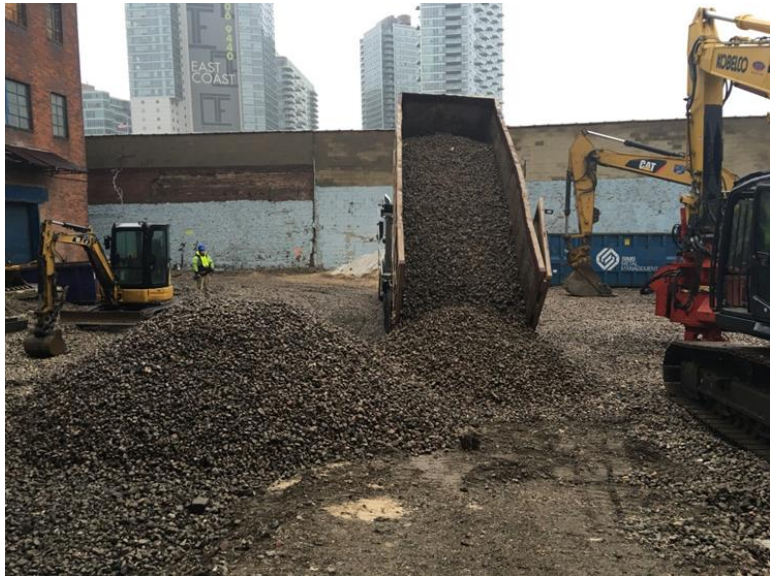

317. Photo taken on Wednesday, February 24, 2016. Looking west across courtyard; approved-RCA onsite to be used for final grading of Site.

318. Photo taken on Wednesday, February 24, 2016. Looking north along east perimeter of courtyard; x2 2" PVC installed at approximately 4' bls. Ramp constructed above backfilled area will be removed for final RCA grading.

319. Photo taken on Thursday, February 25, 2016. Looking west inside PFB; 4" PVC mounted on wall to be used as tubing/cable run for recovery system.

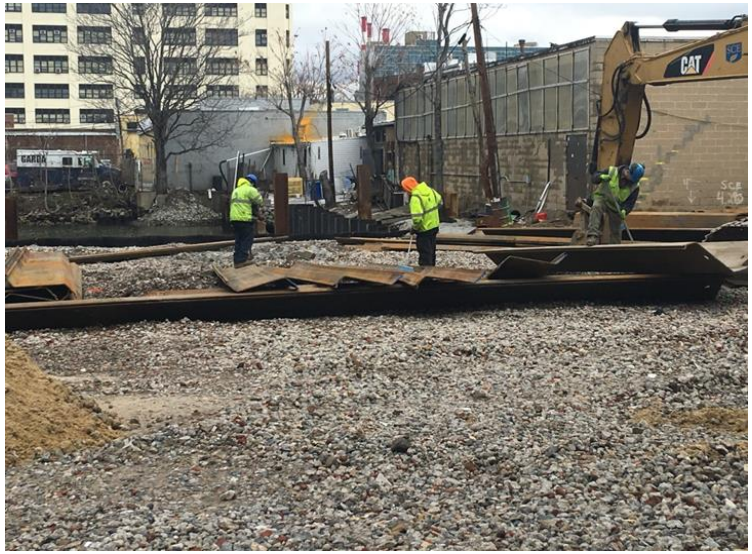

320. Photo taken on Thursday, February 25, 2016. Looking north across courtyard; continued decontamination activities of excavation sheeting.

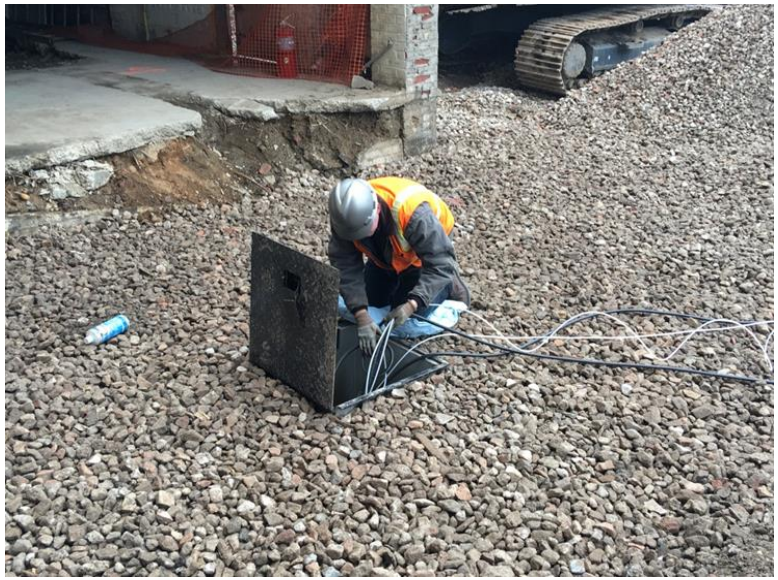

321. Photo taken on Monday, February 29, 2016. Looking southwest in courtyard; begin pulling tubing and electrical components from recovery wells RW-4 and RW-5.

322. Photo taken on Monday, February 29, 2016. Looking west inside PFB; pulling electrical and tubing for recovery well system (RW-1 through RW-5) to Geotech AC Sipper control panel.

323. Photo taken on Tuesday, March 1, 2016. Looking northwest in driveway; excavation around damaged RW-3 vault to be replaced with new vault.

324. Photo taken on Tuesday, March 1, 2016. Looking east inside driveway; proposed concrete collar location to be installed around RW-1, RW-2 and RW-3 vaults following completion of trucking activities.

325. Photo taken on Wednesday, March 2, 2016. Looking down into RW-1 vault; feeding in air line and product recovery hose to be pulled to RW-3 vault.

327. Photo taken on Thursday, March 3, 2016. Looking northwest in courtyard; clean stone mobilized to site to be used as final cover.

326. Photo taken on Wednesday, March 2, 2016. Looking down into main pull box; RW-1 through RW-5 air and product recovery lines pulled. To be pulled into PFB and attached to system or 55-gallon drum.

328. Photo taken on Friday, March 4, 2016. AC Sipper pump fully assembled to be installed in recovery wells (bottom of pump to south of photo). Air line and product recovery line to be attached after pump has been inserted into well.

329. Photo taken on Friday, March 4, 2016. Looking down into vault of RW-1; installation of recovery well pump.

330. Photo taken on Monday, March 7, 2016. Looking northeast across the courtyard; moving decontaminated excavation sheeting from decon area to the middle of courtyard staging area for future offsite demobilization.

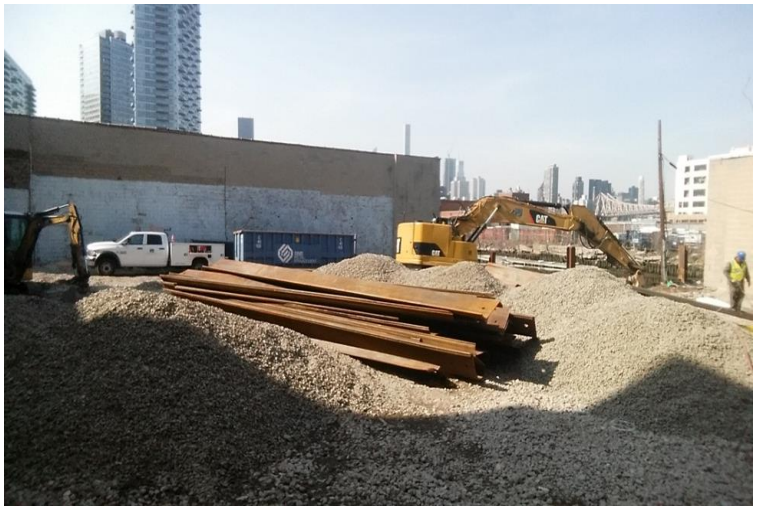

331. Photo taken on Monday, March 7, 2016. Looking northwest across the excavation; staging area for decontaminated sheets to await offsite demobilization.

332. Photo taken on Tuesday, March 8, 2016. Looking southwest across the courtyard; pile of excavation sheeting <20' in length to be wet decon.

333. Photo taken on Tuesday, March 8, 2016. Looking south down the driveway; preparation to pour concrete support for vaults and monitoring well prior to asphalting later in week (no concrete poured on 3/8).

334. Photo taken on Wednesday, March 9, 2016. Looking southwest down driveway; concrete forms poured around RW-1, RW-2 and MW-33.

335. Photo taken on Wednesday, March 9, 2016. Looking southeast across courtyard; mob of last excavation sheet to decon area.

336. Photo taken on Thursday, March 10, 2016. Looking west at north perimeter of courtyard; base asphalt of approved asphalt cap.

337. Photo taken on Thursday, March 10, 2016. Looking southwest down driveway; use of asphalt spreader to pave driveway.

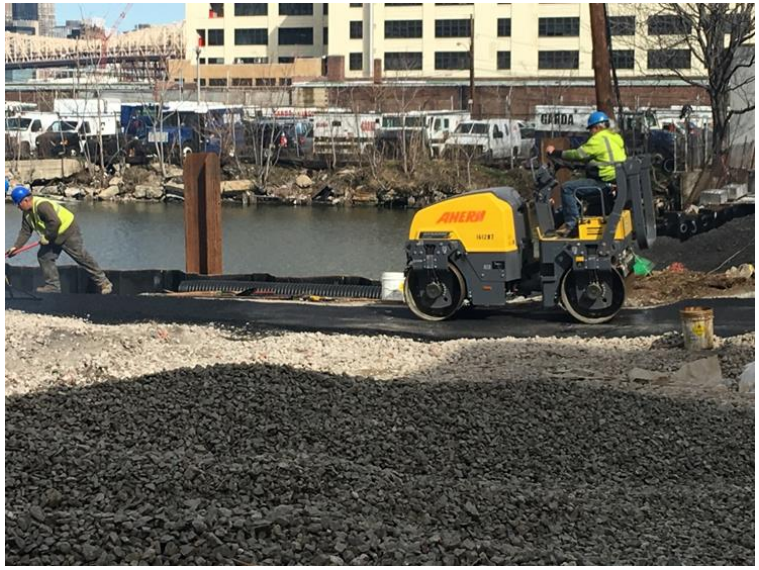

338. Photo taken on Friday, March 11, 2016. Looking north across courtyard; final layer of asphalt and compaction.

339. Photo taken on Friday, March 11, 2016. Looking southwest across courtyard; use of asphalt spreader to install asphalt cap.
