Former Accurate Die Site
547 East Genesee Street, Fayetteville, NY
NYSDEC BCP Site No. C734052

FORMER ACCURATE DIE SITE WEEKLY STATUS REPORT

Reporting Period: 11/1/26-11/7/26 **Report No. 13**

Tasks accomplished this reporting period	
1	Above-grade demolition completed Friday 11/6/26.
2	
3	
4	

Notes

Goals for next reporting period	
1	Remove scrap metal off-site.
2	
3	
4	
5	

Modifications, Deviations from RAWP: None

Submitted By: Natalie Maiorano, James Environmental Management	**Date: 11/9/26**

Attachments: Frederico Demolition Daily Logs

Fayetteville

547 NY-5 Fayetteville , NY 13066

Date Sun 11/01/2026 **Job #** 26018

Weather

6:00 AM	12:00 PM	4:00 PM
33°	55°	65°
Partially cloudy	Partially cloudy	Partially cloudy
Wind: 4 MPH | Precipitation: .0" | Humidity: 92%	Wind: 3 MPH | Precipitation: .0" | Humidity: 62%	Wind: 6 MPH | Precipitation: .0" | Humidity: 33%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/1/26, 2:55 PM	1	6	**102.25**
Total		1	6	**588.82**

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**11**
Doosan DX225 (2014)		0		**10**
Doosan DX350 LC-5		0		**34**
Doosan DX380 LL		0		**34**
Doosan DX490 LC-5		0		**34**
Doosan DX490 LC-5 #2 unit 2		0		**31**
Dozer 1150		0		**34**
Excavator CASE CX330 (#3)		0		**34**
Excavator CAT 330 UHR		0		**11**

FD 1 FD 1	0		**28**
FD 14 0014	0		**28**
FD 16 Flatbed	0		**28**
FD 66 w/ Dump Trailer	0		**11**
FD 72 W/Dump Trailer	0		**7**
Generator 45kV	0		**28**
Grapple Bucket	0		**34**
Hydraulic Hammer HB4200	0		**34**
Magnet 38" ESA 38	0		**34**
Shear Kinshofer	0		**34**
Shear M-28 M-28 K	0		**34**

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	

Fayetteville

547 NY-5 Fayetteville , NY 13066

Date Mon 11/02/2026 **Job #** 26018 **Prepared By** Chuck Cottone



Weather

6:00 AM	12:00 PM	4:00 PM
40°	66°	66°
Partially cloudy	**Clear**	**Clear**
Wind: 5 MPH | Precipitation: .0" | Humidity: 84%	Wind: 0 MPH | Precipitation: .0" | Humidity: 40%	Wind: 1 MPH | Precipitation: .0" | Humidity: 43%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/2/26, 5:41 PM	1	12.75	**135.5**
Carson Melfa	Carson Melfa | 11/2/26, 6:00 PM	1	12.25	**149.75**
Chuck Cottone	Chuck Cottone | 11/2/26, 8:39 PM	1	10.65	**121.47**
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/2/26, 5:30 PM	1	10	**112.25**
Jamey Gerenski	Brenda McMahon | 11/9/26, 9:50 AM	1	10	**108.75**
Total		5	55.65	**644.47**

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date

Clean C&D Chuck Cottone | 11/02/26 | 08:42PM	**1** Load	**1** Load	**14** Load
Clean C&D Chuck Cottone | 11/02/26 | 08:42PM	**9.8** ton	**9.8** ton	**255.32** ton
Scrap Recovery Chuck Cottone | 11/02/26 | 08:41PM	**2** Load	**2** Load	**7** Load

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**12**
Doosan DX225 (2014)		0		**11**
Doosan DX350 LC-5		8		**35**
Doosan DX380 LL		8		**35**
Doosan DX490 LC-5		8		**35**
Doosan DX490 LC-5 #2 unit 2		0		**32**
Dozer 1150		0		**35**
Excavator CASE CX330 (#3)		0		**35**
Excavator CAT 330 UHR		0		**12**
FD 1 FD 1		0		**29**
FD 14 0014		0		**29**
FD 16 Flatbed		0		**29**
FD 66 w/ Dump Trailer		10		**12**
FD 72 W/Dump Trailer		0		**8**
Generator 45kV		0		**29**

Grapple Bucket	0	**35**
Hydraulic Hammer HB4200	0	**35**
Magnet 38" ESA 38	0	**35**
Shear Kinshofer	0	**35**
Shear M-28 M-28 K	0	**35**

General Notes

1. Phone call from Janel Benson to the office in the morning at 10 AM asking about the schedule for pulling slabs and foundations in the building. Claimed she was a neighbor and wanted to know the schedule so she could plan for dust control/air purifiers. Office took her name, phone number, and took the message.

   Matt Schreiber | 11/03/26 | 07:48AM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	

C Cottone

I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/02/26 | 08:42PM

Fayetteville

547 NY-5 Fayetteville , NY 13066

Date Tue 11/03/2026 **Job #** 26018 **Prepared By** Chuck Cottone

Weather

6:00 AM	12:00 PM	4:00 PM
57°	62°	67°
Overcast	Overcast	Partially cloudy
Wind: 4 MPH | Precipitation: .0" | Humidity: 63%	Wind: 5 MPH | Precipitation: .0" | Humidity: 69%	Wind: 6 MPH | Precipitation: .0" | Humidity: 65%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/3/26, 5:46 PM	1	10.5	**146**
Carson Melfa	Carson Melfa | 11/3/26, 5:46 PM	1	10.25	**160**
Chuck Cottone	Chuck Cottone | 11/3/26, 6:58 PM	1	11	**132.47**
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/3/26, 5:30 PM	1	10	**122.25**
Jamey Gerenski	Jamey Gerenski | 11/3/26, 5:57 PM	1	10	**118.75**
Total		5	51.75	**696.22**

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date
Scrap Recovery Chuck Cottone | 11/03/26 | 06:59PM		**3** Load	**5** Load	**10** Load

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site

DA 30 Off Road Truck	0		**13**
Doosan DX225 (2014)	8		**12**
Doosan DX350 LC-5	10		**36**
Doosan DX380 LL	10		**36**
Doosan DX490 LC-5	10		**36**
Doosan DX490 LC-5 #2 unit 2	4		**33**
Dozer 1150	0		**36**
Excavator CASE CX330 (#3)	4		**36**
Excavator CAT 330 UHR	0		**13**
FD 1 FD 1	0		**30**
FD 14 0014	0		**30**
FD 16 Flatbed	0		**30**
FD 66 w/ Dump Trailer	10		**13**
FD 72 W/Dump Trailer	0		**9**
Generator 45kV	0		**30**
Grapple Bucket	0		**36**
Hydraulic Hammer HB4200	0		**36**
Magnet 38" ESA 38	0		**36**
Shear Kinshofer	0		**36**
Shear M-28 M-28 K	0		**36**


General Notes

1. Continue demolition on building. Leave material on slab to process hauling concrete to northside. Loadout steel.
   Walk with Adam to look at monitor locations

   Chuck Cottone | 11/04/26 | 03:17AM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	



I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/04/26 | 03:17AM

Fayetteville


547 NY-5 Fayetteville , NY 13066

Date Wed 11/04/2026 **Job #** 26018 **Prepared By** Chuck Cottone







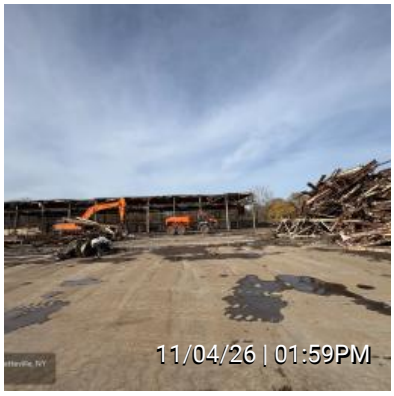

Weather

6:00 AM	12:00 PM	4:00 PM
48°	73°	76°
Partially cloudy	**Partially cloudy**	**Partially cloudy**
Wind: 5 MPH | Precipitation: .0" | Humidity: 88%	Wind: 5 MPH | Precipitation: .0" | Humidity: 50%	Wind: 10 MPH | Precipitation: .0" | Humidity: 46%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/4/26, 5:20 PM	1	9.75	**155.75**
Carson Melfa	Carson Melfa | 11/4/26, 5:27 PM	1	10	**170**
Chuck Cottone	Chuck Cottone | 11/4/26, 9:04 PM	1	10.07	**142.54**
Jamey Gerenski	Jamey Gerenski | 11/4/26, 5:32 PM	1	10	**128.75**
Total		4	39.82	**736.04**

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date
Scrap Recovery		**2** Load	**7** Load	**12** Load

Chuck Cottone | 11/04/26 | 06:25PM

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**14**
Doosan DX225 (2014)		4		**13**
Doosan DX350 LC-5		10		**37**
Doosan DX380 LL		10		**37**
Doosan DX490 LC-5		10		**37**
Doosan DX490 LC-5 #2 unit 2		4		**34**
Dozer 1150		0		**37**
Excavator CASE CX330 (#3)		4		**37**
Excavator CAT 330 UHR		0		**14**
FD 1 FD 1		0		**31**
FD 14 0014		0		**31**
FD 16 Flatbed		0		**31**
FD 66 w/ Dump Trailer		8		**14**
FD 72 W/Dump Trailer		0		**10**
Generator 45kV		0		**31**
Grapple Bucket		0		**37**
Hydraulic Hammer HB4200		0		**37**
Magnet 38" ESA 38		0		**37**
Shear Kinshofer		0		**37**
Shear M-28 M-28 K		0		**37**


General Notes

1. Continue Demo of building hauling on material two northside. Leave north wall and column lines to support roof for selective demo tomorrow.
   Sweep slab on grade

   Chuck Cottone | 11/04/26 | 09:03PM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	



I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/04/26 | 09:03PM


Fayetteville


547 NY-5 Fayetteville , NY 13066

Date Thu 11/05/2026 **Job #** 26018 **Prepared By** Chuck Cottone





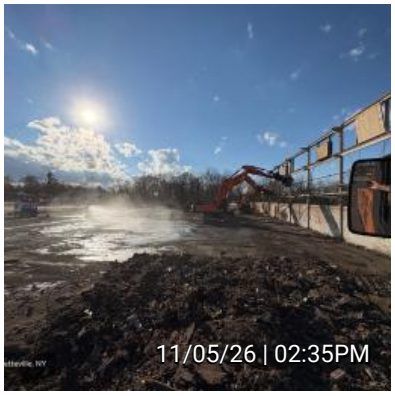

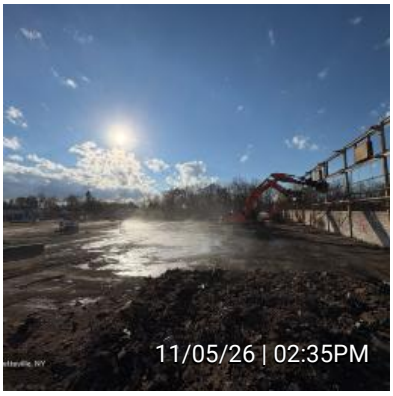

Weather

6:00 AM	12:00 PM	4:00 PM
64°	73°	70°
Overcast	**Partially cloudy**	**Partially cloudy**
Wind: 9 MPH | Precipitation: .01" | Humidity: 77%	Wind: 10 MPH | Precipitation: .0" | Humidity: 60%	Wind: 9 MPH | Precipitation: .0" | Humidity: 62%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/5/26, 5:27 PM	1	10	**165.75**
Carson Melfa	Carson Melfa | 11/5/26, 5:28 PM	1	10.25	**180.25**
Chuck Cottone	Chuck Cottone | 11/5/26, 9:19 PM	1	10.5	**153.04**
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/5/26, 5:30 PM	1	9.75	**132**
Jamey Gerenski	Brenda McMahon | 11/9/26, 10:10 AM	1	5.5	**134.25**
Total		5	46	**782.04**

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**15**
Doosan DX225 (2014)		4		**14**
Doosan DX350 LC-5		10		**38**
Doosan DX380 LL		8		**38**
Doosan DX490 LC-5		10		**38**
Doosan DX490 LC-5 #2 unit 2		4		**35**
Dozer 1150		0		**38**
Excavator CASE CX330 (#3)		6		**38**
Excavator CAT 330 UHR		0		**15**
FD 1 FD 1		0		**32**
FD 14 0014		0		**32**
FD 16 Flatbed		0		**32**
FD 66 w/ Dump Trailer		4		**15**
FD 72 W/Dump Trailer		0		**11**
Generator 45kV		0		**32**
Grapple Bucket		0		**38**
Hydraulic Hammer HB4200		0		**38**
Magnet 38" ESA 38		0		**38**
Shear Kinshofer		0		**38**
Shear M-28 M-28 K		0		**38**

General Notes

1. Complete structural demo leaving north wall standing for selective Demo

   Continue hauling concrete to low side. Sweep slab clean.

Ran water mister throughout the day for structural Demo and Concrete loadout

Matt Schreiber | 11/09/26 | 10:17AM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	

Attachments







C Cottone

I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/05/26 | 09:23PM

Fayetteville

547 NY-5 Fayetteville , NY 13066

Date Fri 11/06/2026 **Job #** 26018 **Prepared By** Chuck Cottone









Weather

6:00 AM	12:00 PM	4:00 PM
48°	66°	61°
Clear	**Overcast**	**Partially cloudy**
Wind: 4 MPH | Precipitation: .0" | Humidity: 91%	Wind: 8 MPH | Precipitation: .0" | Humidity: 50%	Wind: 8 MPH | Precipitation: .0" | Humidity: 63%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/6/26, 6:46 PM	1	11.25	**177**
Carson Melfa	Carson Melfa | 11/6/26, 7:08 PM	1	11.75	**192**
Chuck Cottone	Chuck Cottone | 11/6/26, 8:03 PM	1	10.5	**163.54**
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/6/26, 5:12 PM	1	9.75	**141.75**
Jamey Gerenski	Jamey Gerenski | 11/6/26, 5:21 PM	1	7.75	**142**
Total		5	51	**833.04**

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date

Clean C&D Chuck Cottone | 11/06/26 | 08:04PM	**1** Load	**2** Load	**15** Load
Clean C&D Chuck Cottone | 11/07/26 | 02:41PM	**13.17** ton	**22.97** ton	**268.49** ton

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**16**
Doosan DX225 (2014)		0		**15**
Doosan DX350 LC-5		10		**39**
Doosan DX380 LL		8		**39**
Doosan DX490 LC-5		5		**39**
Doosan DX490 LC-5 #2 unit 2		5		**36**
Dozer 1150		0		**39**
Excavator CASE CX330 (#3)		8		**39**
Excavator CAT 330 UHR		0		**16**
FD 1 FD 1		0		**33**
FD 14 0014		0		**33**
FD 16 Flatbed		0		**33**
FD 66 w/ Dump Trailer		8		**16**
FD 72 W/Dump Trailer		0		**12**
Generator 45kV		0		**33**
Grapple Bucket		0		**39**
Hydraulic Hammer HB4200		0		**39**

Magnet 38" ESA 38	0	**39**
Shear Kinshofer	0	**39**
Shear M-28 M-28 K	0	**39**

General Notes

1. Continue cutting steel for prepared structural.
   Clean up perimeter of building and load out materials in loading dock area. Start sweeping SOG using water and pickup broom.

   Chuck Cottone | 11/06/26 | 08:08PM
2. Walk around with Adam P tried to locate additional monitoring Wells that should remain.
   Could not identify or locate number 14

   Chuck Cottone | 11/06/26 | 08:11PM

Survey


Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	

Attachments









I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/06/26 | 08:10PM

Fayetteville

547 NY-5 Fayetteville , NY 13066

Date Sat 11/07/2026 **Job #** 26018 **Prepared By** Chuck Cottone









Weather

6:00 AM	12:00 PM	4:00 PM
43°	45°	46°
Overcast	**Overcast**	**Rain, Overcast**
Wind: 5 MPH | Precipitation: .0" | Humidity: 88%	Wind: 12 MPH | Precipitation: .0" | Humidity: 93%	Wind: 7 MPH | Precipitation: .01" | Humidity: 88%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Brandon Lewis	Brandon Lewis | 11/7/26, 5:50 PM	1	12.25	**189.25**
Carson Melfa	Carson Melfa | 11/7/26, 5:31 PM	1	11	**203**
Chuck Cottone	Chuck Cottone | 11/7/26, 5:51 PM	1	8	**171.54**
Hugh Carroll, Kevin	Hugh Carroll, Kevin | 11/7/26, 5:09 PM	1	9.75	**151.5**
Jamey Gerenski	Jamey Gerenski | 11/7/26, 2:43 PM	1	3	**145**
Total		5	44	**877.04**

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date

Scrap Recovery Chuck Cottone | 11/07/26 | 05:52PM	**6** Load	**13** Load	**18** Load

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
DA 30 Off Road Truck		0		**17**
Doosan DX225 (2014)		0		**16**
Doosan DX350 LC-5		8		**40**
Doosan DX380 LL		8		**40**
Doosan DX490 LC-5		0		**40**
Doosan DX490 LC-5 #2 unit 2		0		**37**
Dozer 1150		0		**40**
Excavator CASE CX330 (#3)		4		**40**
Excavator CAT 330 UHR		0		**17**
FD 1 FD 1		0		**34**
FD 14 0014		0		**34**
FD 16 Flatbed		0		**34**
FD 66 w/ Dump Trailer		10		**17**
FD 72 W/Dump Trailer		10		**13**
Generator 45kV		0		**34**
Grapple Bucket		0		**40**
Hydraulic Hammer HB4200		0		**40**
Magnet 38" ESA 38		0		**40**
Shear Kinshofer		0		**40**
Shear M-28		0		**40**

General Notes

1. Cutting structural steel. Clean up all accessible slab and p-lot areas. Load out.

   Chuck Cottone | 11/07/26 | 05:54PM

Survey


Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☑	☐	☐	
2. Any visitors on site?	☑	☐	☐	
3. Did weather cause any delays?	☑	☐	☐	
4. Any schedule delays occur?	☑	☐	☐	
5. Any areas that can't be worked on?	☑	☐	☐	


Attachments








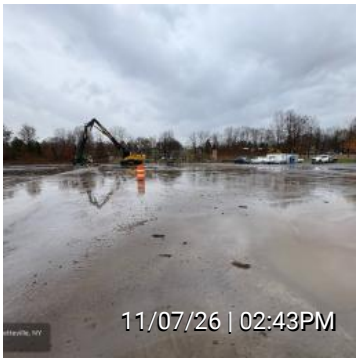

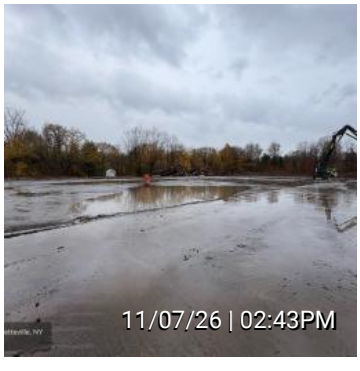



I, Chuck Cottone, have reviewed and completed this report.

Chuck Cottone | 11/07/26 | 05:56PM
