ID	Task Name	Duration	Start	Finish
1	**IRM 5A2 Construction Schedule**	**449 days**	**Fri 9/3/21**	**Tue 6/6/23**
2	Amendment #2 Revision Submittal	0 days	Fri 9/3/21	Fri 9/3/21
3	Receipt of ECSD Comments	0 days	Fri 9/17/21	Fri 9/17/21
4	Receipt of Agency Comments	0 days	Tue 9/21/21	Tue 9/21/21
5	Amendment #2 Revision Submittal	0 days	Fri 10/8/21	Fri 10/8/21
6	Limited Notice to Proceed	0 days	Thu 10/14/21	Thu 10/14/21
7	DEC Notice to Proceed (Approved as Modfied)	0 days	Fri 10/22/21	Fri 10/22/21
8	Monitoring Well Decommissioning Plan Submittal	0 days	Tue 11/23/21	Tue 11/23/21
9	Groundwater Monitoring Well Network Update	0 days	Fri 1/14/22	Fri 1/14/22
10	Dry Well Soil Quality Verification Sampliing Plan	0 days	Fri 1/14/22	Fri 1/14/22
11	**Temporary Infrastructure**	**148 days**	**Tue 3/1/22**	**Tue 9/27/22**
12	Phase 1 Decommission /Phase 2 Construction	5 days	Tue 3/1/22	Mon 3/7/22
13	Temporary Infrastructure Decommissioning Plan (NS property)	0 days	Mon 3/7/22	Mon 3/7/22
14	Phase 3 Site Plan Submittal	0 days	Mon 3/7/22	Mon 3/7/22
15	Phase 1 Post-Decommissioning Sampilng	1 wk	Tue 3/8/22	Mon 3/14/22
16	Completion of ECSD Use of IRM Haul Road	0 days	Fri 5/27/22	Fri 5/27/22
17	Phase 2 Decommission	4 wks	Fri 5/27/22	Fri 6/24/22
18	Phase 2 Post-Decommissioning Sampilng	1 wk	Mon 6/27/22	Fri 7/1/22
19	Phase 3 Construction	1 wk	Tue 7/19/22	Mon 7/25/22
20	Phase 3 Decommission	1 wk	Wed 9/21/22	Tue 9/27/22
21	**Excavation and Backfill**	**235 days**	**Fri 10/22/21**	**Tue 9/27/22**
22	**Phase 1**	**87 days**	**Fri 10/22/21**	**Mon 2/28/22**
23	**Area A-1**	**37 days**	**Fri 10/22/21**	**Wed 12/15/2**
24	Excavation	24 days	Fri 10/22/21	Wed 11/24/2
25	Backfill	8 days	Mon 12/6/21	Wed 12/15/2
26	**Area A-2 + Pods**	**63 days**	**Mon 11/29/2**	**Mon 2/28/22**
27	Excavation	44 days	Mon 11/29/2	Tue 2/1/22
28	Backfill	14 days	Wed 2/9/22	Mon 2/28/22
29	**Phase 2**	**47 days**	**Tue 3/8/22**	**Thu 5/12/22**
30	**Area A-3 + Industrial Sewer**	**13 days**	**Tue 3/8/22**	**Thu 3/24/22**
31	Excavation	6 days	Tue 3/8/22	Tue 3/15/22
32	Industrial Sewer Removal	4 days	Thu 3/10/22	Tue 3/15/22
33	Backfill	2 days	Wed 3/23/22	Thu 3/24/22
34	**Area A-4**	**23 days**	**Wed 3/16/22**	**Mon 4/18/22**
35	Excavation	14 days	Wed 3/16/22	Mon 4/4/22
36	Backfill	4 days	Tue 4/12/22	Mon 4/18/22
37	**Area A-5**	**21 days**	**Tue 4/5/22**	**Wed 5/4/22**
38	Excavation	12 days	Tue 4/5/22	Thu 4/21/22
39	Backfill	4 days	Fri 4/29/22	Wed 5/4/22
40	**Area A-6**	**15 days**	**Fri 4/22/22**	**Thu 5/12/22**
41	Excavation	7 days	Fri 4/22/22	Mon 5/2/22
42	Backfill	3 days	Tue 5/10/22	Thu 5/12/22
43	**Phase 3 (STRA Area)**	**46 days**	**Tue 7/26/22**	**Tue 9/27/22**
44	Excavation	15 days	Tue 7/26/22	Mon 8/15/22
45	Backfill	5 days	Tue 8/23/22	Mon 8/29/22
46	Pre-Final Inspection	0 days	Tue 8/30/22	Tue 8/30/22
47	Punch List (as necessary)	3 wks	Wed 8/31/22	Tue 9/20/22
48	Turnover to ECSD for Capital Improvements	0 days	Tue 9/27/22	Tue 9/27/22
49	**Waste Shipment**	**160 days**	**Thu 11/4/21**	**Mon 6/27/22**
50	Disposal Shipment Start	0 days	Thu 11/4/21	Thu 11/4/21
51	Disposal	160 days	Fri 11/5/21	Mon 6/27/22
52	Disposal Shipment Completion	0 days	Mon 6/27/22	Mon 6/27/22
53	**Soil Cover Verification**	**154 days**	**Fri 10/22/21**	**Fri 6/3/22**
54	Soil Cover Verificaiton Sampling Plan	0 days	Fri 10/22/21	Fri 10/22/21
55	Agency Disapproval	0 days	Mon 11/15/2	Mon 11/15/2
56	Soil Cover Verificaiton Sampling Plan Re-Submittal	0 days	Fri 12/31/21	Fri 12/31/21
57	Agency Approval	0 days	Fri 1/28/22	Fri 1/28/22
58	Soil Cover Verification Sampling	3 wks	Fri 5/13/22	Fri 6/3/22
59	**Ballfied Restoration**	**70 days**	**Fri 5/13/22**	**Mon 8/22/22**
60	Drywell Installation	2 wks	Fri 5/13/22	Thu 5/26/22
61	Grading/Topsoil	2 wks	Fri 5/27/22	Fri 6/10/22
62	Irrigation System Installation	1 mon	Mon 6/13/22	Mon 7/11/22
63	Infield & Dugout Foundation Construction	4 wks	Tue 7/12/22	Mon 8/8/22
64	Sodding & Hydroseed	2 wks	Tue 8/9/22	Mon 8/22/22
65	**STRA Decommissioning**	**20 days**	**Mon 6/27/22**	**Mon 7/25/22**
66	Rally Point Removal (post 2021-22 School Year)	1 wk	Mon 6/27/22	Fri 7/1/22
67	Sod Harvesting (ECSD - post irrigation install)	1 wk	Tue 7/12/22	Mon 7/18/22
68	Fill Removal (Unisys)	1 wk	Tue 7/19/22	Mon 7/25/22
69	**Construction Completion Report**	**180 days**	**Wed 9/28/22**	**Tue 6/6/23**
70	CCR Preparation	6 mons	Wed 9/28/22	Tue 3/14/23
71	CCR Submittal	0 days	Tue 3/14/23	Tue 3/14/23
72	Agency Review	3 mons	Wed 3/15/23	Tue 6/6/23
73	CCR Approval	0 days	Tue 6/6/23	Tue 6/6/23

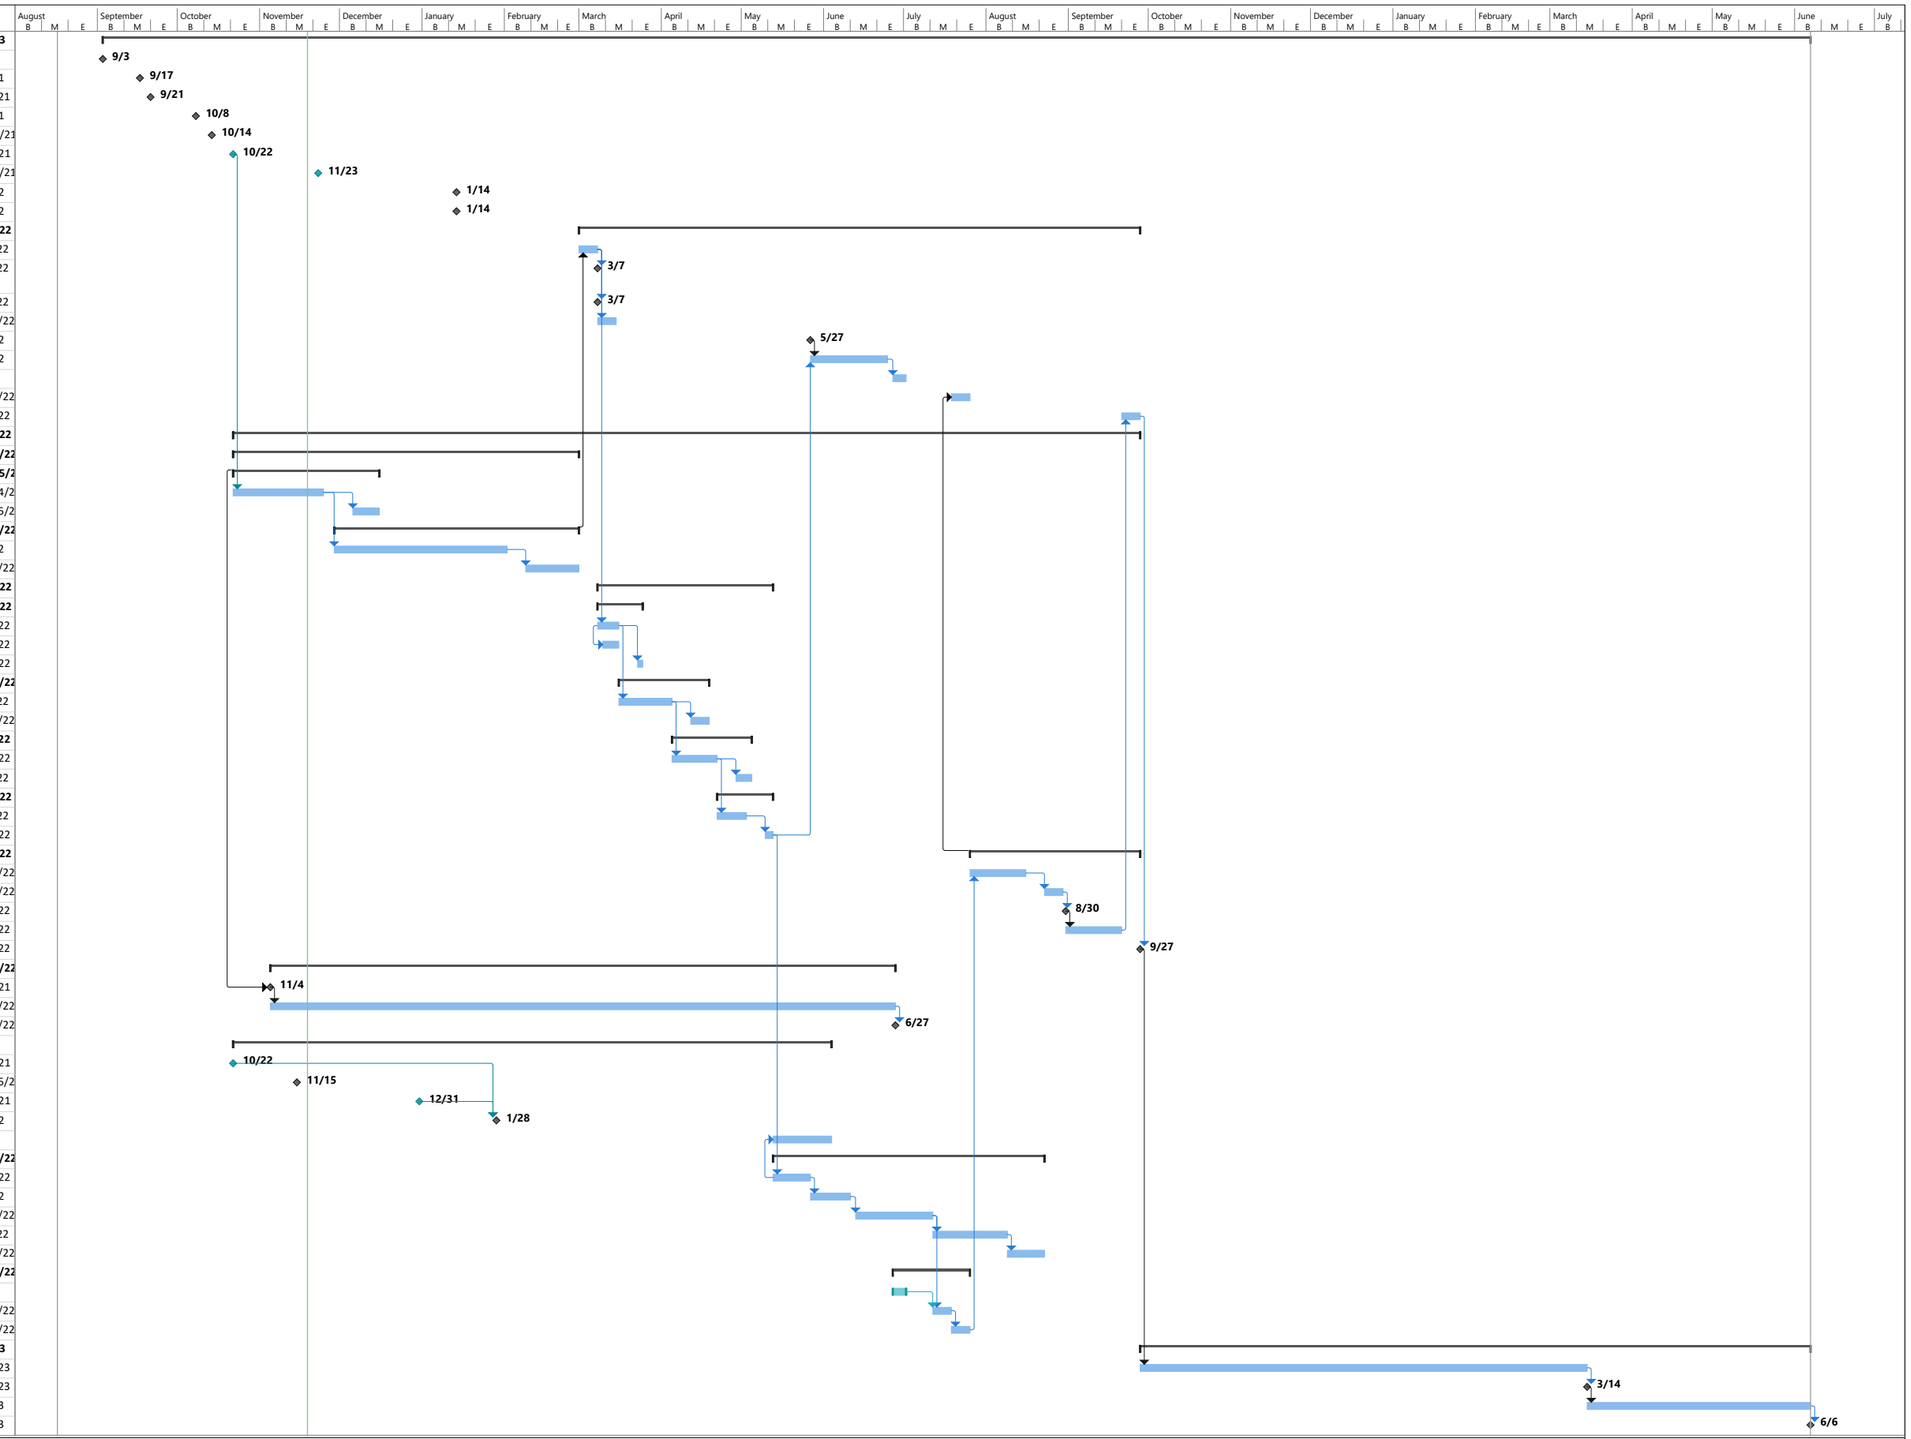

IRM #5 Amendment #2
Project Schedule
Date: Fri 11/19/21

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
