Tanknology
11000 N. MoPac Expressway, Suite 500
Austin, Texas 78759
Phone: (512) 451-6334
Fax: (512) 459-1459

Date Printed and Mailed: 7/31/2025



DEC-SCHENECTADY
REGION 4
1130 NORTH WESTCOTT ROAD
SCHENECTADY, NY 12306

Test Date: 7/24/2025
Order Number: 8610664

Dear Regulator,

Enclosed are the results of recent testing performed at the following facility:

CUMBERLAND FARMS #1559/ 3145
236 MAIN STREET
PO BOX 658, PBS#4-036897
CAIRO, NY 12413

Testing conducted in accordance with paragraph 613-2.3(d)(2) of NYCRR. Technician is a certified Vacutect tank tester and/or a certified TLD-1 line tester in accordance with company protocol. Technician address on file at Tanknology corporate office: 11000 N. MoPac Expressway, Suite 500, Austin, TX 78759

Testing performed:
- IMPACT VALVE
- LEAK DETECTOR
- Line Tightness Test
- MONITOR CERTIFICATION

Sincerely,

Dawn Kohlmeyer

Dawn Kohlmeyer
Manager, Field Reporting

Tanknology

Product Line Tightness Test

Work Order: 8610664 **Date:** 7/24/2025
Site Name/ID: CUMBERLAND FARMS #1559/ 3145 / 3145
Address: 236 MAIN STREET PO BOX 658, PBS#4-036897
City: CAIRO **State:** NY **Zip:** 12413

Tank Information	Tank # 1 Line # 1	Tank # 3 Line # 1	Tank # Line #	Tank # Line #	Tank # Line #	Tank # Line #
Test Method	TLD-1	TLD-1				
Customer Tank ID	1	3				
Product Name	UNLEADED	SUPER				
Delivery Type	Pressure	Pressure				
Test Pressure (psi)	60	60				
Test Start Time	11:22	11:22				
Test End Time	12:22	12:22				
Final Leak Rate (gph)	0.00	0.00				
Test Result(P/F/I)	Pass	Pass				
Test was performed per 3rd party certifications as specified in 40 CFR parts 280 and 281	Yes	Yes				

Technician Comments: Lines tested tight.

Technician Name: Jeffrey Claeys **Certification #:** 133142 exp: 6/18/2026

Technician Signature: 

Environmental Compliance for Petroleum Systems

©2025 Tanknology Inc., Austin, TX. All rights reserved. tanknology.com

Tanknology

LDT 5000 Field Test Apparatus
Line Leak Detector Test

Work Order: 8610664 Date: 7/24/2025
Site Name / ID: CUMBERLAND FARMS #1559/ 3145 / 3145
Address: 236 MAIN STREET PO BOX 658, PBS#4-036897
City: CAIRO State: NY Zip: 12413

Tank ID	1	3				
Product	UNLEADED	SUPER				
Product Line	1	1				
Tested From	2	2				
Existing/New	Existing	Existing				
Mechanical/Electronic	Mechanical	Mechanical				
Manufacturer/Model	FE Petro MLD+G	Veeder Root FX1V				
Serial No.	17E500800358L	5524				
Pump Operating Pressure (psi)	38.00	40.00				
Calibrated Leak (ml/min)	189.0	189.0				
Calibrated Leak (gph)	3.00	3.00				
Holding PSI *N/A for Electronic LD's	15.00	20.00				
Resiliency (ml) *N/A for Electronic LD's	150.00	125.00				
Metering PSI *N/A for Electronic LD's	12	12				
Opening Time (sec) *N/A for Electronic LD's	3	4				
Test Results	Pass	Pass				

Technician Comments:

Technician Name: Jeffrey Claeys **Certification #:** 133137

Technician Signature: **Expire Date:** 6/18/2026

Environmental Compliance for Petroleum Systems

© 2025 Tanknology Inc., Austin, TX. All rights reserved. tanknology.com

Tanknology

Impact Valve Inspection

Impact Valve Operational Inspection

Work Order: 8610664 Date: 7/24/2025
Site Name/ID: CUMBERLAND FARMS #1559/ 3145
Address: 236 MAIN STREET PO BOX 658, PBS#4-036897
City: CAIRO State: NY Zip: 12413

How Inspected: Line Test ☑ NFPA 30A ☐ PEI RP1200 ☐ Other ☐

Dispenser Number	Grade	Secure Mount?	Valve Lock?	Pass/ Fail	Comments
1/2	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
1/2	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
3/4	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
3/4	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
5/6	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
5/6	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
7/8	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
7/8	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
9/10	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
9/10	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	

Technician Comments:

Technician Name: Jeffrey Claeys

Signature:

Environmental Compliance for Petroleum Systems
©2025 Tanknology Inc., Austin, TX. All rights reserved. tanknology.com

MONITORING SYSTEM CERTIFICATION

This form is used to document testing and servicing of tank and piping leak monitoring equipment. If required by applicable law, a copy of the completed form must be provided by the Testing Contractor or owner to the governing UST agency as required by regulation.

A. General Information

Facility Name: CUMBERLAND FARMS #1559/ 3145 Bldg. No.:

Site Address: 236 MAIN STREETPO BOX 658, PBS#4-036897 City: CAIRO State: NY Zip: 12413

Facility Contact Person: ASST MGR... ROXANNE Contact Phone No.: 518-622-3957

Make/Model of Monitoring System: Veeder Root TLS-450 PLUS Date of Testing/Servicing: 7/24/2025

B. Inventory of Equipment Tested/Certified Check the appropriate boxes to indicate specific equipment inspected/serviced:

Tank ID: 1 - UNLEADED

- [x] In-Tank Gauging Probe. Model: 846390-107
- [x] Annular Space or Vault Sensor. Model: 794390-409
- [x] Piping Sump / Trench Sensor(s). Model: smart sensor
- [ ] Fill Sump Sensor(s). Model:
- [x] Mechanical Line Leak Detector. Model: FE Petro MLD+G
- [ ] Electronic Line Leak Detector. Model:
- [ ] Tank Overfill / High-Level Sensor. Model:
- [ ] Other (specify equipment type and model in Section E on Page 2).

Tank ID: 2 - UNLEADED

- [x] In-Tank Gauging Probe. Model: 846390-107
- [x] Annular Space or Vault Sensor. Model: 794390-409
- [x] Piping Sump / Trench Sensor(s). Model: smart sensor
- [ ] Fill Sump Sensor(s). Model:
- [ ] Mechanical Line Leak Detector. Model:
- [ ] Electronic Line Leak Detector. Model:
- [ ] Tank Overfill / High-Level Sensor. Model:
- [ ] Other (specify equipment type and model in Section E on Page 2).

Tank ID: 3 - SUPER

- [x] In-Tank Gauging Probe. Model: 846390-107
- [x] Annular Space or Vault Sensor. Model: 794390-409
- [x] Piping Sump / Trench Sensor(s). Model: smart sensor
- [ ] Fill Sump Sensor(s). Model:
- [x] Mechanical Line Leak Detector. Model: Veeder Root FX1V
- [ ] Electronic Line Leak Detector. Model:
- [ ] Tank Overfill / High-Level Sensor. Model:
- [ ] Other (specify equipment type and model in Section E on Page 2).

Tank ID:

- [ ] In-Tank Gauging Probe. Model:
- [ ] Annular Space or Vault Sensor. Model:
- [ ] Piping Sump / Trench Sensor(s). Model:
- [ ] Fill Sump Sensor(s). Model:
- [ ] Mechanical Line Leak Detector. Model:
- [ ] Electronic Line Leak Detector. Model:
- [ ] Tank Overfill / High-Level Sensor. Model:
- [ ] Other (specify equipment type and model in Section E on Page 2).

Dispenser ID: 1/2

- [x] Dispenser Containment Sensor(s). Model: 847990-001
- [x] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

Dispenser ID: 3/4

- [x] Dispenser Containment Sensor(s). Model: 847990-001
- [x] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

Dispenser ID: 5/6

- [x] Dispenser Containment Sensor(s). Model: 847990-001
- [x] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

Dispenser ID: 7/8

- [x] Dispenser Containment Sensor(s). Model: 847990-001
- [x] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

Dispenser ID: 9/10


- [x] Dispenser Containment Sensor(s). Model: 847990-001
- [x] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

Dispenser ID:

- [ ] Dispenser Containment Sensor(s). Model:
- [ ] Shear Valve(s).
- [ ] Dispenser Containment Float(s) and Chain(s).

*If the facility contains more tanks or dispensers, copy this form. Include information for every tank and dispenser at the facility.

C. Certification - I certify that the equipment identified in this document was inspected/serviced in accordance with the manufacturers' guidelines. Attached to this Certification is a Plot Plan showing the layout of monitoring equipment. For any equipment capable of generating such reports, I have also attached a copy of the report; *(check all that apply)*: [x] System set-up [x] Alarm history report

Technician Name (print): Jeffrey Claeys Signature: 

Certification No.: B48818 License. No.:

Testing Company Name: Tanknology Phone No.: (800) 800-4633

Testing Company Address: 11000 N. MoPac Expressway Suite 500 Date of Testing/Servicing: 7/24/2025

D. Results of Testing/Servicing
Software Version Installed: _____

Complete the following checklist:

☑ Yes	☐ No* ☐ N/A	Is the **visual** alarm on the console operational?
☑ Yes	☐ No* ☐ N/A	Is the **audible** alarm on the console operational?
☐ Yes	☑ No	Is the external **visual** overfill alarm (light unit) present?
☐ Yes	☐ No* ☑ N/A	Is the external **visual** overfill alarm operating properly?
☐ Yes	☑ No	Is the external **audible** overfill alarm present?
☐ Yes	☐ No* ☑ N/A	Is the external **audible** overfill alarm operating properly?
%	☑ N/A	At what percent of tank(s) capacity is the external alarm programmed to trigger? *If different % between tanks, clarify in section E.*
☑ Yes	☐ No* ☐ N/A	Were all sensors visually inspected, functionally tested, and confirmed operational?
☑ Yes	☐ No* ☐ N/A	Were all sensors installed at lowest point of secondary containment and positioned so that other equipment will not interfere with their proper operation?
☐ Yes	☐ No* ☑ N/A	For pressurized piping systems, does the turbine automatically shut down if the piping secondary containment monitoring system detects a leak, fails to operate, or is electrically disconnected? If yes: which sensors initiate positive shut-down? *(Check all that apply)* ☐ Sump/Trench Sensors; ☐ Dispenser Containment Sensors. Did you confirm positive shut-down due to leaks and sensor failure/disconnection? ☐ Yes; ☐ No
☑ Yes*	☐ No	Was any monitoring equipment replaced? If yes, identify specific sensors, probes, or other equipment replaced and list the manufacturer name and model for all replacement parts in Section E, below.
☐ Yes*	☑ No	Was liquid found inside any secondary containment systems designed as dry systems? *(Check all that apply)* ☐ Product; ☐ Water. If yes, describe causes in Section E, below.
☑ Yes	☐ No*	Was monitoring system set-up reviewed to ensure proper settings? Attach set up reports, if applicable
☑ Yes	☐ No*	Is all monitoring equipment operational per manufacturer's specifications?

* In Section E below, describe how and when these deficiencies were or will be corrected.

E. Comments:

Backup Battery reading, if applicable (Required for VR TLS 300/350):replaced sensor l2

F. In-Tank Gauging / SIR Equipment:

☐ Check this box if tank gauging is used only for inventory control.
☐ Check this box if no tank gauging or SIR equipment is installed.

This section must be completed if in-tank gauging equipment is used to perform leak detection monitoring.

Complete the following checklist:

☑ Yes	☐ No*	Were all tank gauging probes visually inspected for damage and residue buildup?
☑ Yes	☐ No*	Was accuracy of system product level readings tested?
☑ Yes	☐ No*	Was accuracy of system water level readings tested?
☑ Yes	☐ No*	Were all probes reinstalled properly?
☑ Yes	☐ No*	Were all items on the equipment manufacturer's maintenance checklist completed?

* In the Section G, below, describe how and when these deficiencies were or will be corrected.

G. Comments:

DID OVERALL MONITOR SYSTEM TESTING PASS (Check One)? YES☑ NO ☐ INCONCLUSIVE ☐


Tanknology

Site Diagram

(This site diagram is for reference only and is not drawn to scale)


Work Order:	8610664
Site ID / Name:	3145 / CUMBERLAND FARMS #1559/ 3145
Address:	236 MAIN STREET PO BOX 658, PBS#4-036897
City:	CAIRO

State: NY Zip: 12413

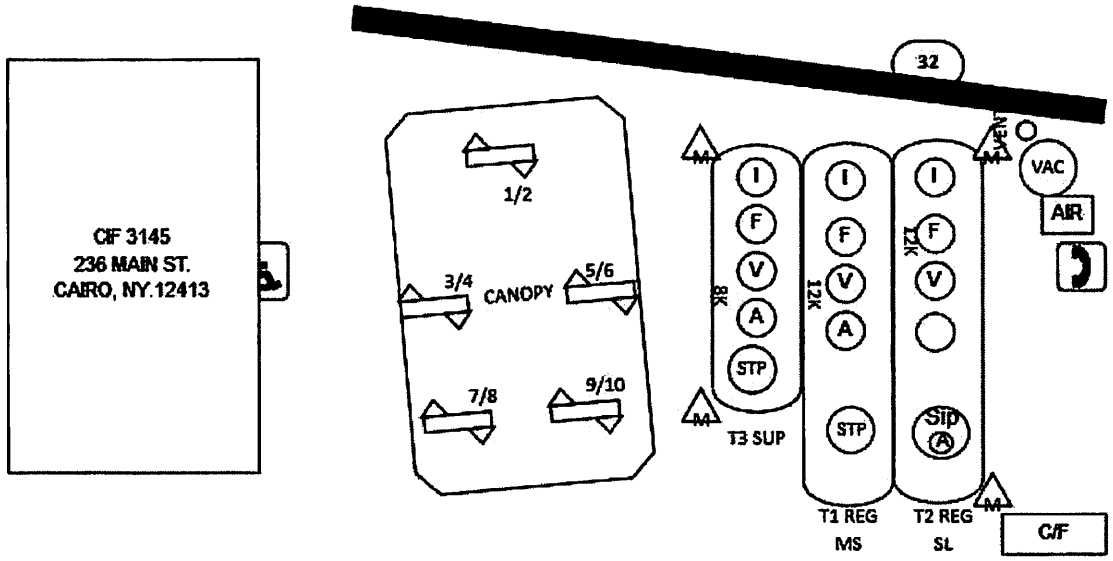

Legend		
F Fill	FV Fill-Vapor	VR Vapor Recovery
ATG Automatic Tank Gauge	I Interstitial	VP Vapor Port
STP Submersible Turbine Pump	T/S Transition Sump	LS Sump Sensor #

W.O.# MA2-8610664 Cust Ref#: 319994548

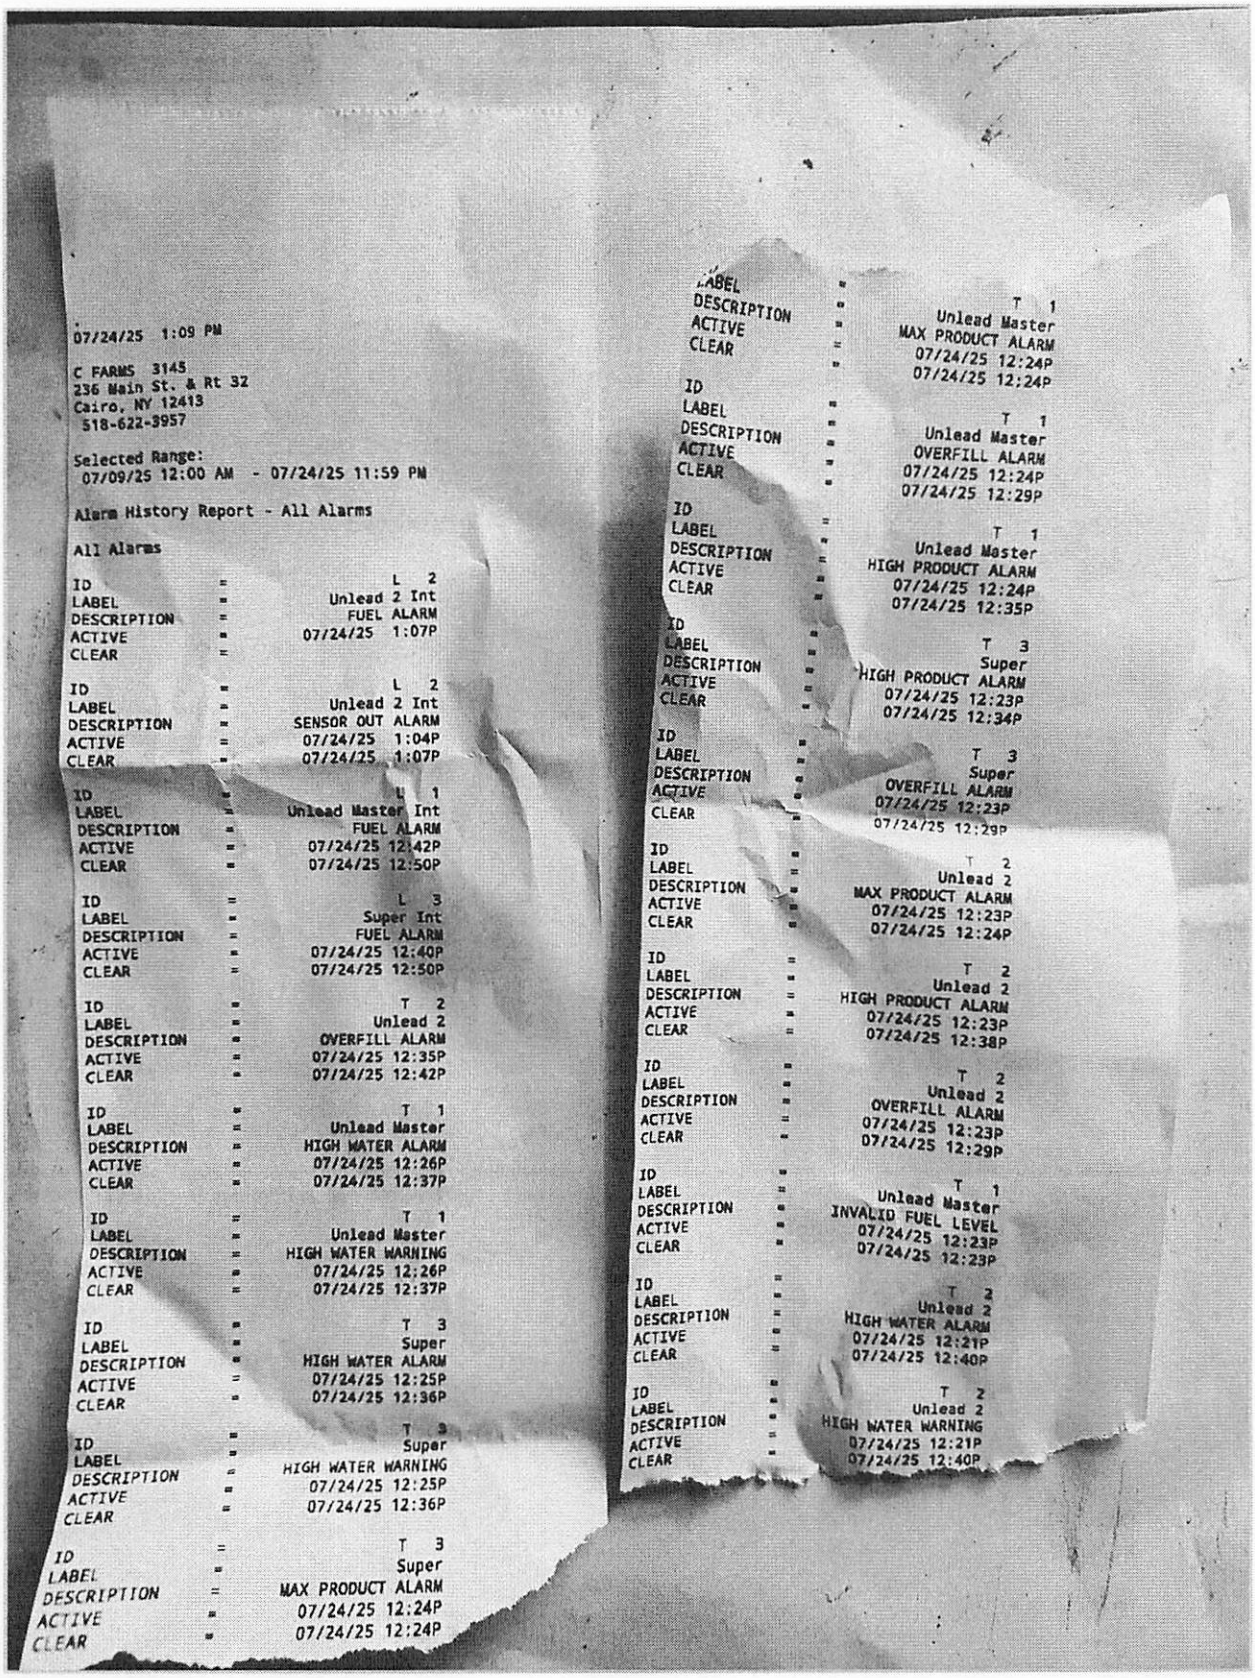

07/24/25 1:09 PM

C FARMS 3145
236 Main St. & Rt 32
Cairo, NY 12413
518-622-3957


Selected Range:
07/09/25 12:00 AM - 07/24/25 11:59 PM

Alarm History Report - All Alarms

All Alarms

ID	L 2
LABEL	Unlead 2 Int
DESCRIPTION	FUEL ALARM
ACTIVE	07/24/25 1:07P
CLEAR	
ID	L 2
LABEL	Unlead 2 Int
DESCRIPTION	SENSOR OUT ALARM
ACTIVE	07/24/25 1:04P
CLEAR	07/24/25 1:07P
ID	L 1
LABEL	Unlead Master Int
DESCRIPTION	FUEL ALARM
ACTIVE	07/24/25 12:42P
CLEAR	07/24/25 12:50P
ID	L 3
LABEL	Super Int
DESCRIPTION	FUEL ALARM
ACTIVE	07/24/25 12:40P
CLEAR	07/24/25 12:50P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	OVERFILL ALARM
ACTIVE	07/24/25 12:35P
CLEAR	07/24/25 12:42P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	HIGH WATER ALARM
ACTIVE	07/24/25 12:26P
CLEAR	07/24/25 12:37P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	HIGH WATER WARNING
ACTIVE	07/24/25 12:26P
CLEAR	07/24/25 12:37P
ID	T 3
LABEL	Super
DESCRIPTION	HIGH WATER ALARM
ACTIVE	07/24/25 12:25P
CLEAR	07/24/25 12:36P
ID	T 3
LABEL	Super
DESCRIPTION	HIGH WATER WARNING
ACTIVE	07/24/25 12:25P
CLEAR	07/24/25 12:36P
ID	T 3
LABEL	Super
DESCRIPTION	MAX PRODUCT ALARM
ACTIVE	07/24/25 12:24P
CLEAR	07/24/25 12:24P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	MAX PRODUCT ALARM
ACTIVE	07/24/25 12:24P
CLEAR	07/24/25 12:24P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	OVERFILL ALARM
ACTIVE	07/24/25 12:24P
CLEAR	07/24/25 12:29P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	HIGH PRODUCT ALARM
ACTIVE	07/24/25 12:24P
CLEAR	07/24/25 12:35P
ID	T 3
LABEL	Super
DESCRIPTION	HIGH PRODUCT ALARM
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:34P
ID	T 3
LABEL	Super
DESCRIPTION	OVERFILL ALARM
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:29P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	MAX PRODUCT ALARM
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:24P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	HIGH PRODUCT ALARM
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:38P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	OVERFILL ALARM
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:29P
ID	T 1
LABEL	Unlead Master
DESCRIPTION	INVALID FUEL LEVEL
ACTIVE	07/24/25 12:23P
CLEAR	07/24/25 12:23P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	HIGH WATER ALARM
ACTIVE	07/24/25 12:21P
CLEAR	07/24/25 12:40P
ID	T 2
LABEL	Unlead 2
DESCRIPTION	HIGH WATER WARNING
ACTIVE	07/24/25 12:21P
CLEAR	07/24/25 12:40P

W.O.# MA2-8610664 Cust Ref#: 319994548

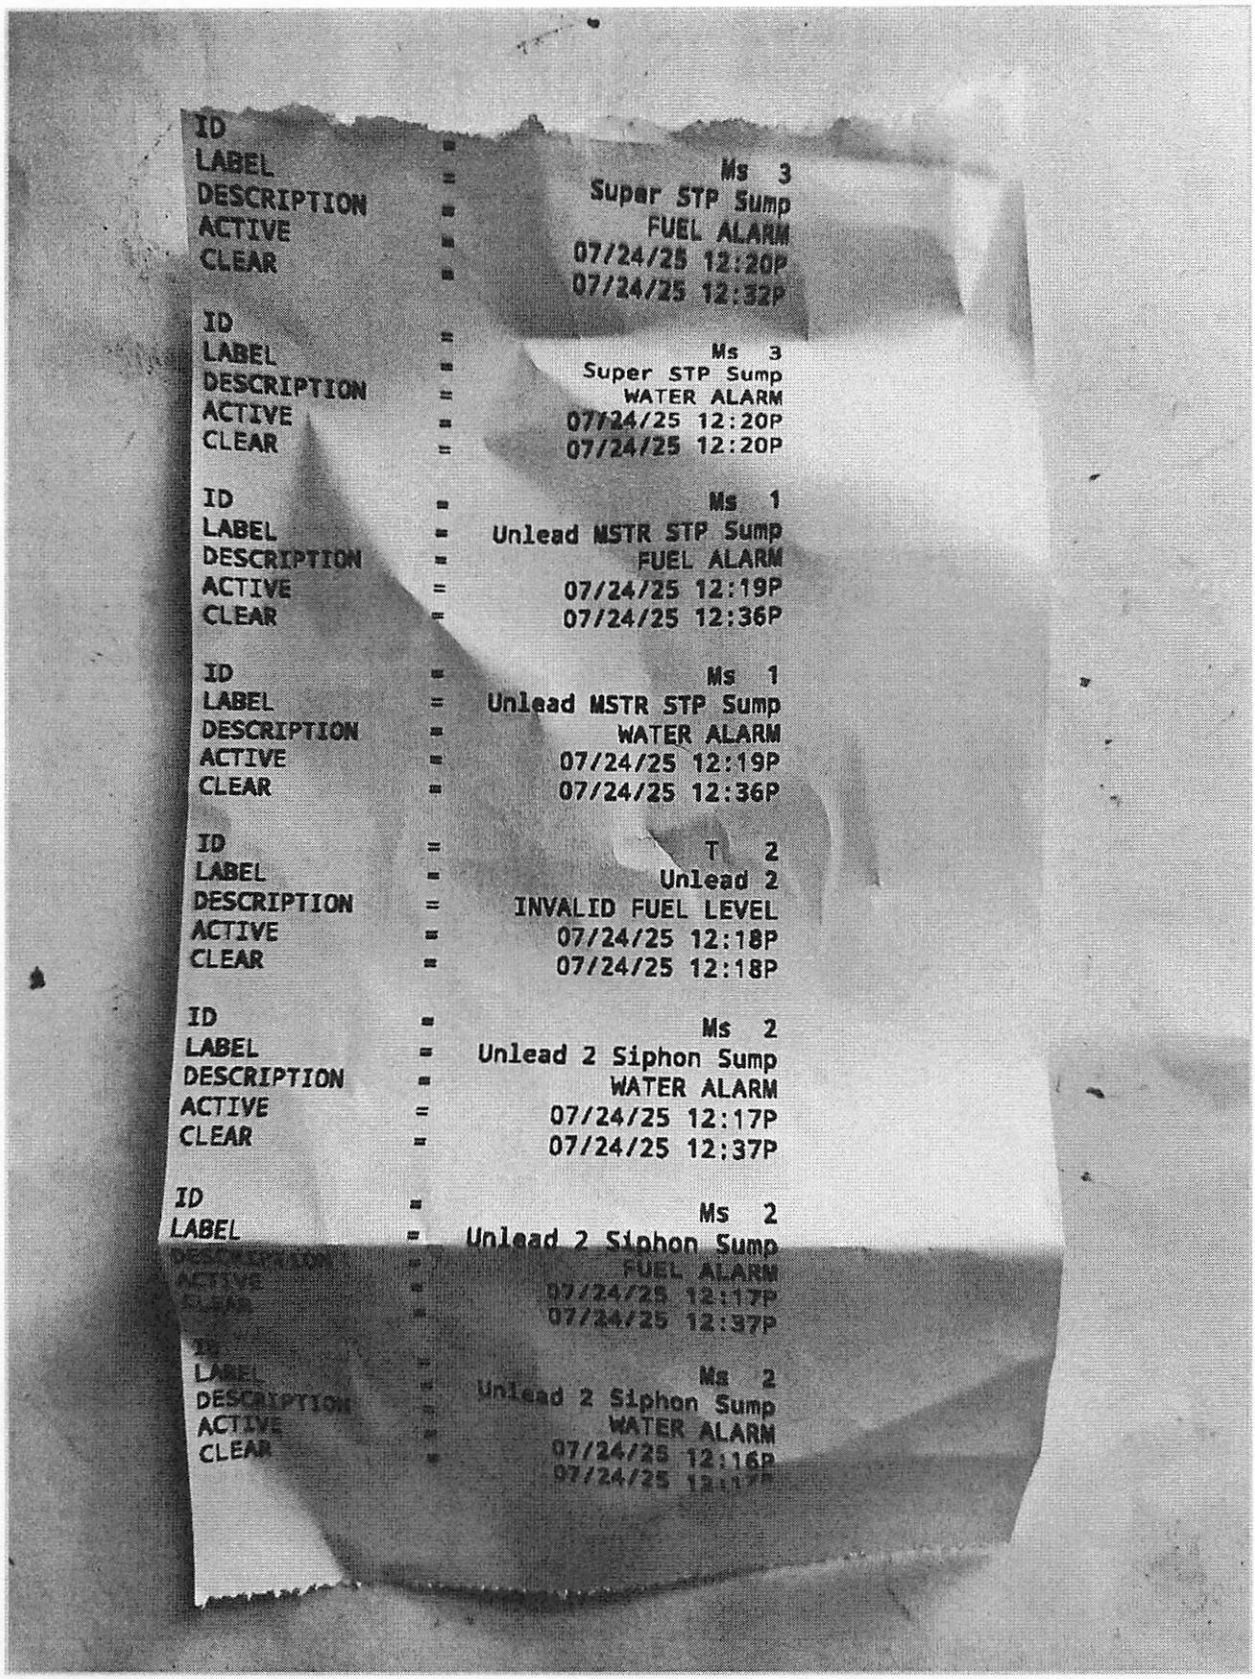

ID = Ms 3
LABEL = Super STP Sump
DESCRIPTION = FUEL ALARM
ACTIVE = 07/24/25 12:20P
CLEAR = 07/24/25 12:32P

ID = Ms 3
LABEL = Super STP Sump
DESCRIPTION = WATER ALARM
ACTIVE = 07/24/25 12:20P
CLEAR = 07/24/25 12:20P

ID = Ms 1
LABEL = Unlead MSTR STP Sump
DESCRIPTION = FUEL ALARM
ACTIVE = 07/24/25 12:19P
CLEAR = 07/24/25 12:36P

ID = Ms 1
LABEL = Unlead MSTR STP Sump
DESCRIPTION = WATER ALARM
ACTIVE = 07/24/25 12:19P
CLEAR = 07/24/25 12:36P

ID = T 2
LABEL = Unlead 2
DESCRIPTION = INVALID FUEL LEVEL
ACTIVE = 07/24/25 12:18P
CLEAR = 07/24/25 12:18P

ID = Ms 2
LABEL = Unlead 2 Siphon Sump
DESCRIPTION = WATER ALARM
ACTIVE = 07/24/25 12:17P
CLEAR = 07/24/25 12:37P

ID = Ms 2
LABEL = Unlead 2 Siphon Sump
DESCRIPTION = FUEL ALARM
ACTIVE = 07/24/25 12:17P
CLEAR = 07/24/25 12:37P

ID = Ms 2
LABEL = Unlead 2 Siphon Sump
DESCRIPTION = WATER ALARM
ACTIVE = 07/24/25 12:16P
CLEAR = 07/24/25 12:17P
