# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Chris Gaule-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: January 8, 2002

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

**Tasks Completed During the Week of December 31, 2001**

*Summary of NAPL Observations*

On January 2 and 4, 2002, URS conducted NAPL checks and recovery at the site (see Table 2 Out of Scope Activities). Table 1 provides the NAPL observations for the wells.

| | Overburden Wells | | Bedrock Well | |
|---|---|---|---|---|
| | MW-26S | RH-1S | MW-35I | MW-10D |
| Cumulative Recovery as of January 4, 2002 | 17.2 L | 12.2 L | 2 L | 206 L |
| Cumulative Recovery All Wells | 237 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

**Tasks to be Completed During the Week of January 7, 2002**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will prepare for the meeting with NYSEG and NYSDEC regarding the November 6, 2001 *Summary Data Package* and discuss the scope and schedule for additional work at the site scheduled for January 18, 2002.

*Privileged & Confidential*

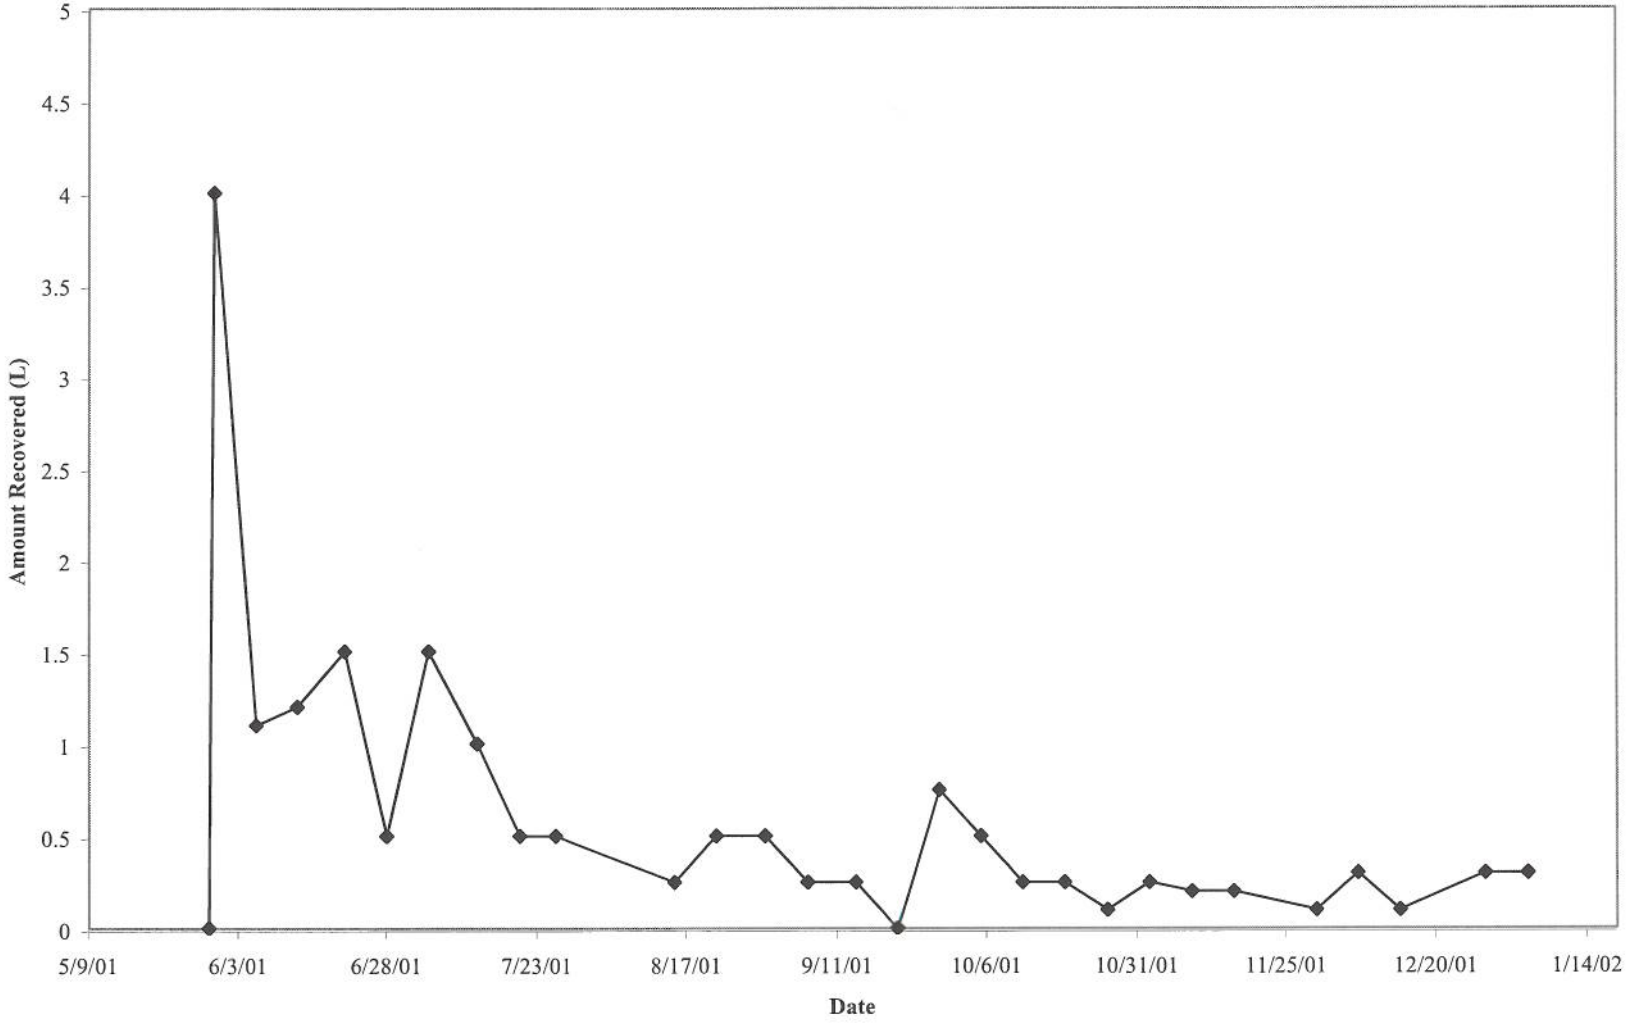
**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| Well Number | Screen Interval (feet bgs) | Type of Screen | Date Checked | NAPL Observation/ Recovery (L) | Total NAPL Recovered To Date (L) |
|---|---|---|---|---|---|
| MW-10 | 8.7 to 19.5 | Screen | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-12 | 14.5 to 25.5 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-12S | 11 to 26 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-14S | 10 to 25 | Screen | 1/2/02 | NAPL Not Present | NAPL Not Present |
| MW-15S | 5 to 10 | Screen | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-16 | 6 to 16 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-17 | 13 to 23 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-21S | 5 to 10 | Screen | 1/2/02 | NAPL Not Present | NAPL Not Present |
| MW-23S | 7.5 to 12.5 | Screen | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-25S | 11 to 26 | Screen | 10/25/01 | NAPL Not Present | Trace NAPL |
| MW-26S | 7.5 to 22.5 | Screen | 1/4/02 | 0.3 | 17.15 |
| MW-30S | 10 to 25 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-31S | 8 to 18 | Screen | 10/4/01 | NAPL Not Present | NAPL Not Present |
| RH-1S | 1.8 to 17.3 | Screen | 1/4/02 | 0.45 | 12.2 |
| MW-1 | 11.6 to 16.85 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-10I | 22 to 43 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-11 | 9.5 to 15 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-13 | 44.7 to 55.5 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-14 | 30 to 41 | Screen | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-15I | 12.5 to 22.5 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-17I | 23 to 45 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-18 | 28 to 38 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-19I | 18 to 38.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-2 | 11.2 to 14.35 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-22I | 17 to 32 | Screen | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-25I | 27 to 47 | Open Hole | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-26I | 24.5 to 45.5 | Open Hole | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-28I | 15 to 25 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-29I | 11.5 to 26 | Open Hole | 1/2/02 | NAPL Not Present | Trace NAPL |
| MW-2I | 11.28 to 32.2 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-35I | 12.5 to 34.5 | Open Hole | 1/2/02 | Trace NAPL | 2 |
| MW-10D | 82 to 114 | Open Hole | 1/4/02 | 3.5 | 206.16 |
| MW-14D | 91 to 121.7 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-15D | 96 to 105.8 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-17D | 121 to 142.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-20D | 90 to 110.1 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-21D | 48.7 to 59.4 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-23D | 56 to 80 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-29D | 90 to 110 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-30D | 90 to 121 | Open Hole | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-31D | 28 to 150 | Open Hole | 10/4/01 | NAPL Not Present | NAPL Not Present |
| MW-32D | 91 to 111.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-33D | 119.7 to 140.5 | Open Hole | 1/2/02 | Trace NAPL | Trace NAPL |
| MW-34D | 100 to 120.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| RH-1D | 86.5 to 107.5 | Open Hole | 12/18/01 | NAPL Not Present | NAPL Not Present |

**SUMMARY OF PRODUCT RECOVERY**
**MW-26S**

*Privileged & Confidential*

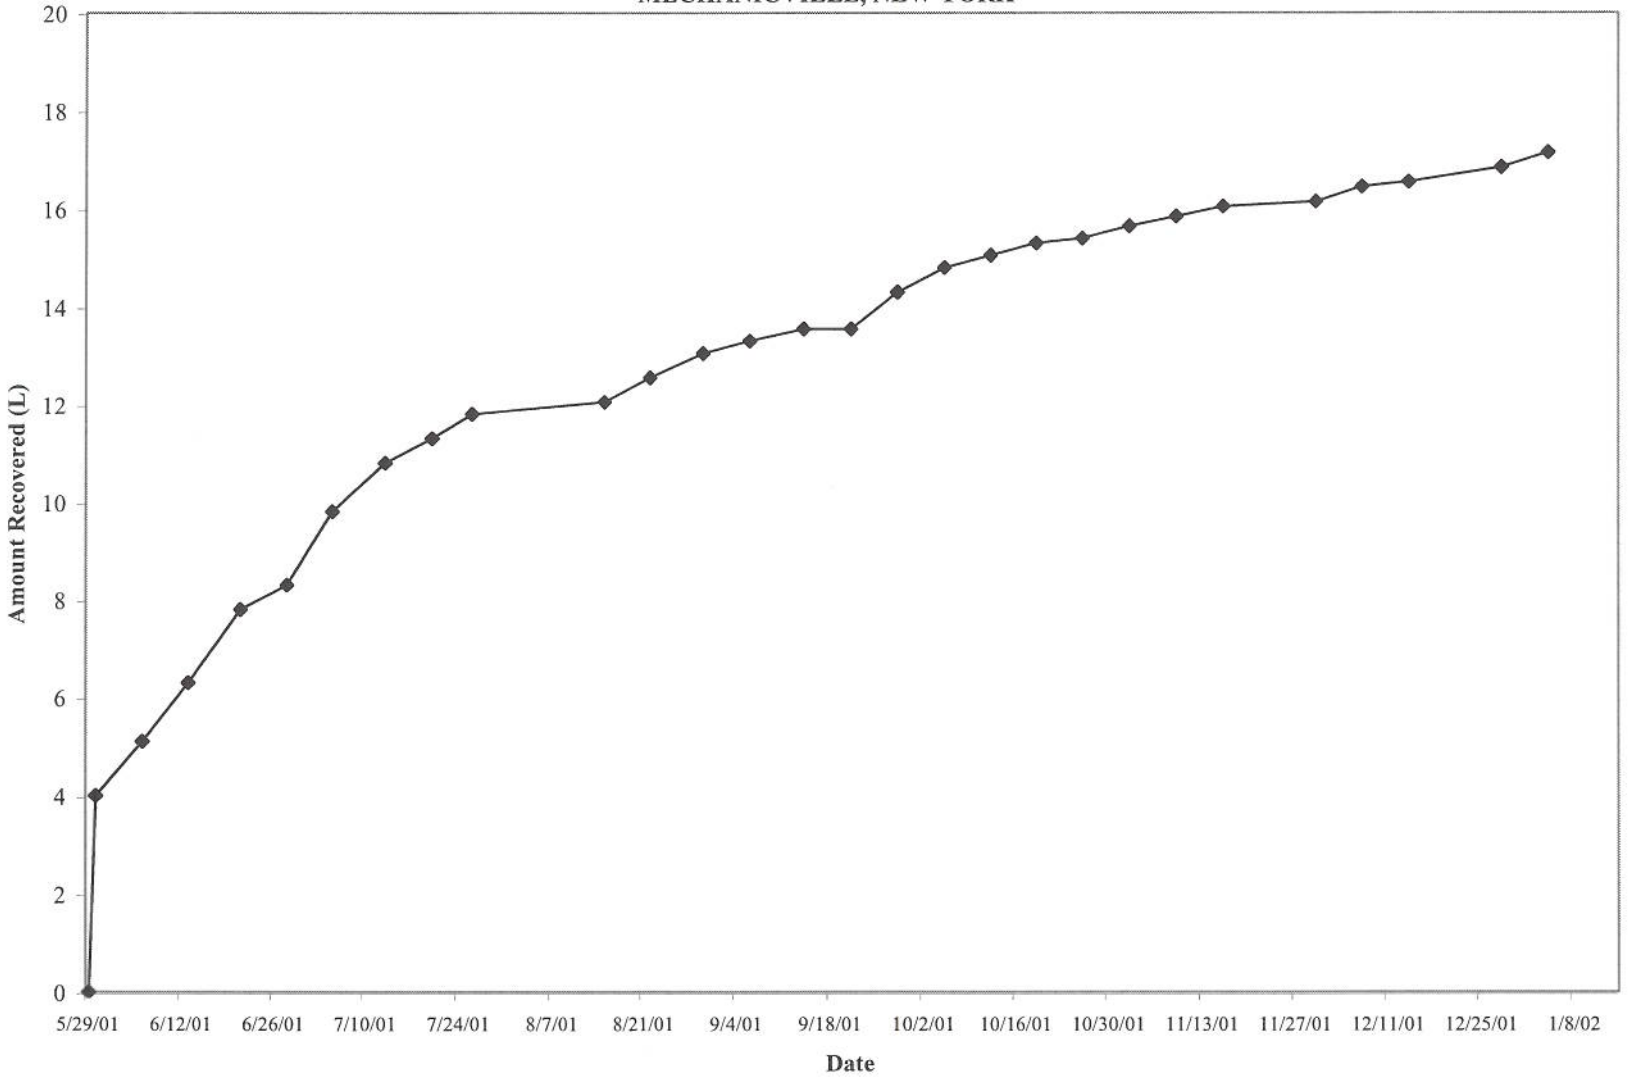
**NYSEG**
**MECHANICVILLE, NEW YORK**



**CUMULATIVE PRODUCT RECOVERY**
**MW-26S**

*Privileged & Confidential*

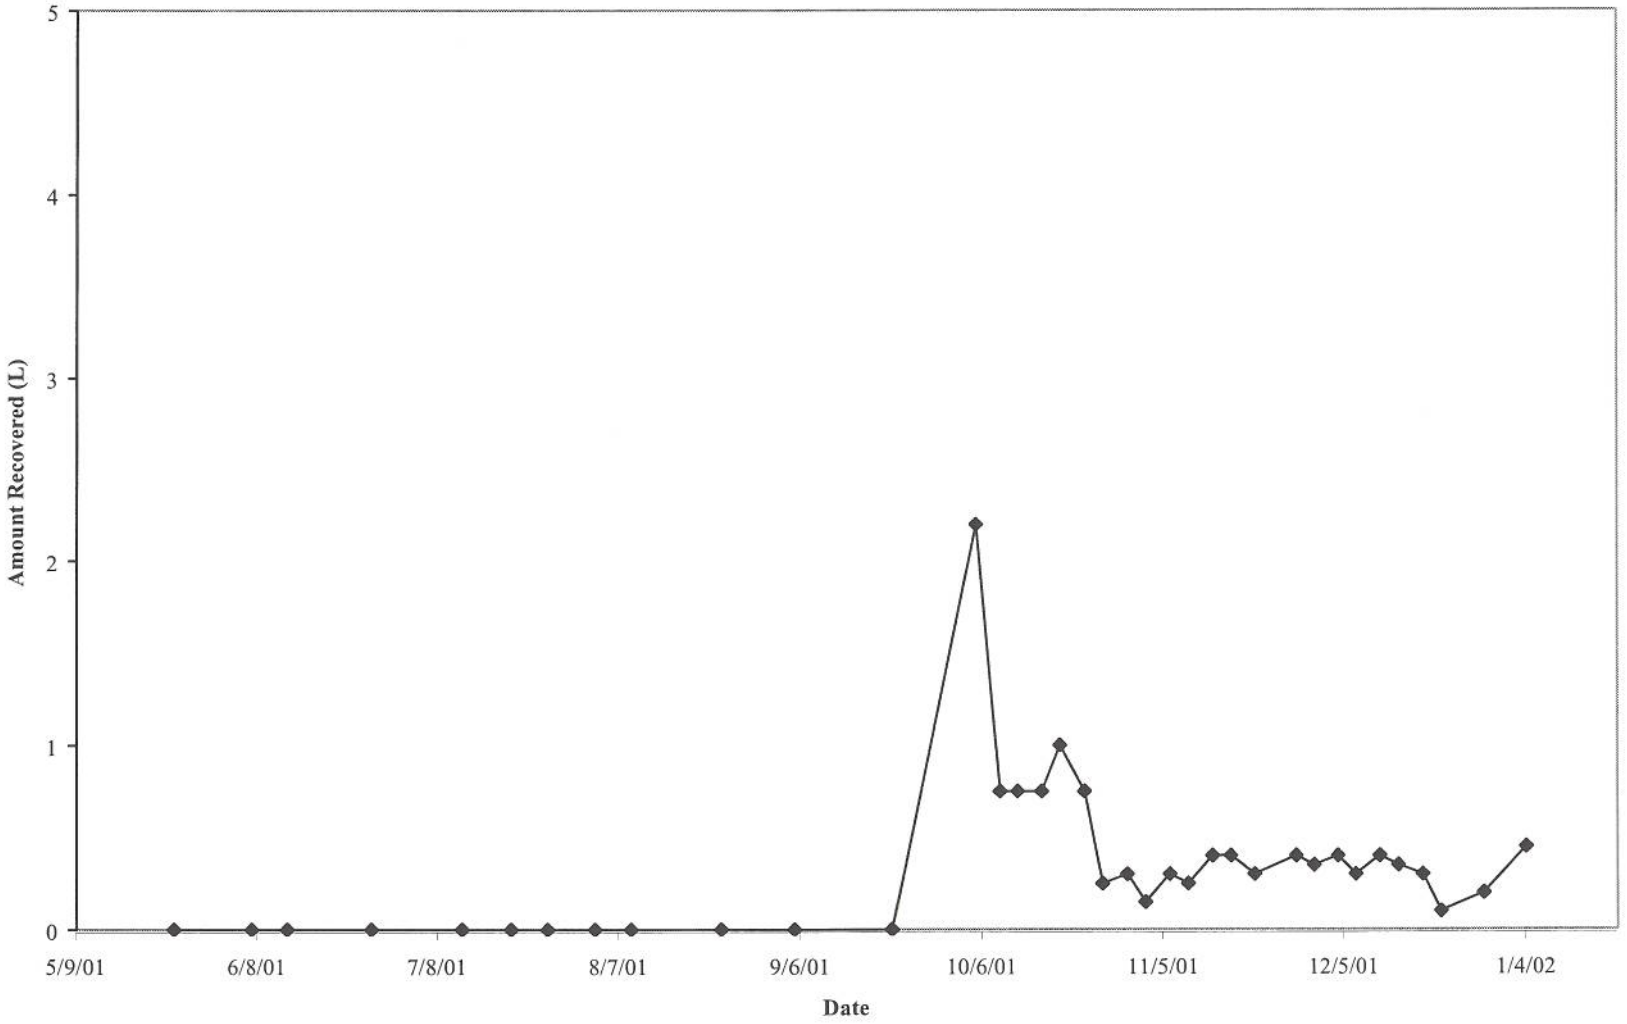
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**SUMMARY OF PRODUCT RECOVERY**
**RH-1S**

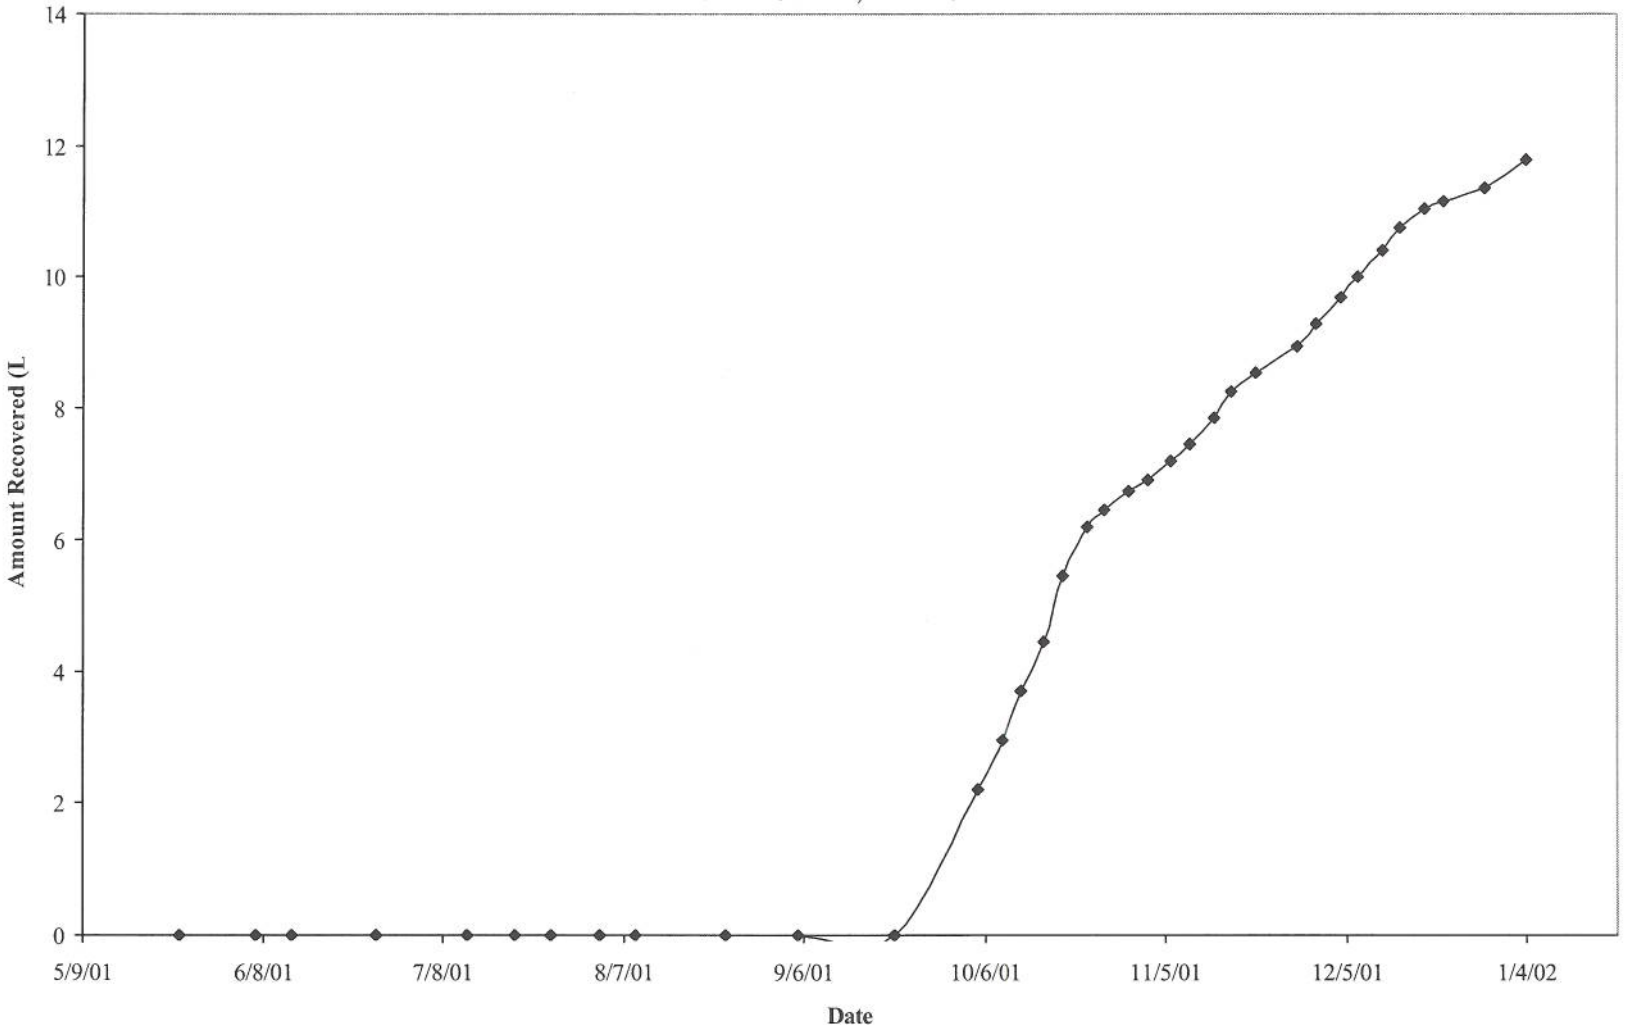
**NYSEG**
**MECHANICVILLE, NEW YORK**



**CUMULATIVE PRODUCT RECOVERY**
**RH-1S**

*Privileged & Confidential*

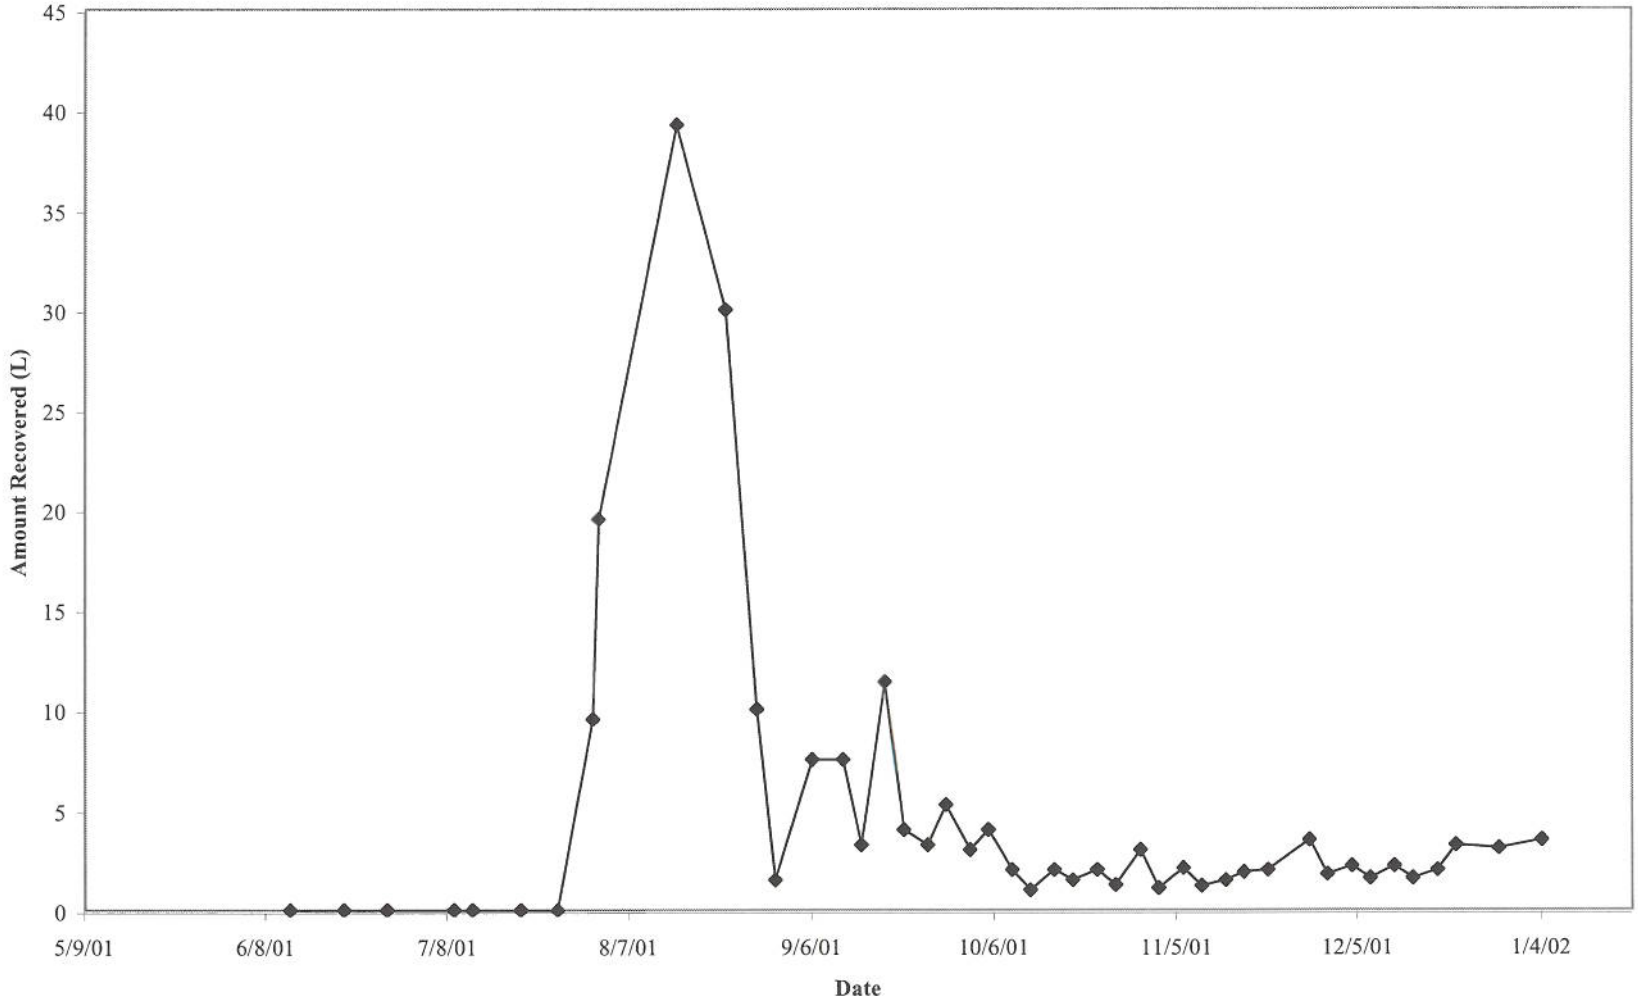
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**MW-10D**

*Privileged & Confidential*

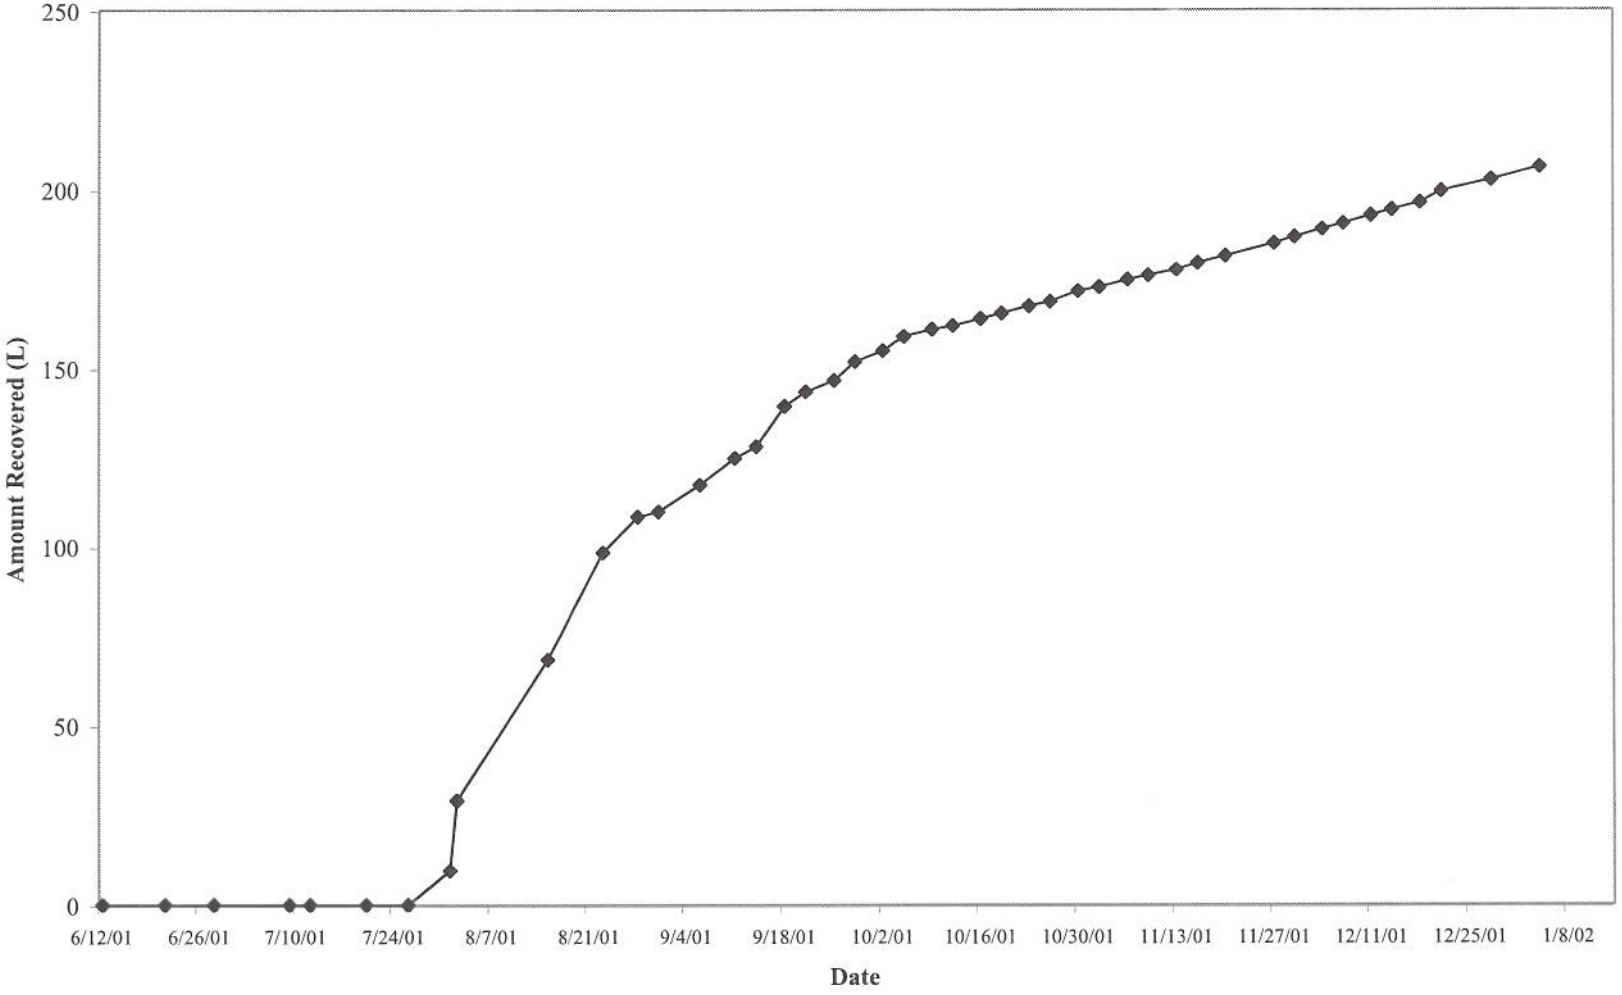
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-10D**

**NYSEG**
**MECHANICVILLE, NEW YORK**



# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 3)
Gardiner Cross-NYSDEC (excluding Table 3)

INFO: Chris Gaule-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: January 3, 2002

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

**Tasks Completed During December 17 through December 28, 2001**

*Summary of NAPL Observations*

Between December 17 through 28, 2001, URS conducted NAPL checks and recovery at the site (see Table 3 Out of Scope Activities). Table 1 provides the NAPL observations for the wells.

| | Overburden Wells | | Bedrock Well | |
|---|---|---|---|---|
| | MW-26S | RH-1S | MW-35I | MW-10D |
| Cumulative Recovery as of December 28, 2001 | 16.9L | 11.8 L | 2 L | 203 L |
| Cumulative Recovery All Wells | 233 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

Table 2 summarizes synoptic water level monitoring round completed between October and December 2001.

**Tasks to be Completed During the Week of December 31, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will be prepared to meet with NYSEG and NYSDEC regarding the November 6, 2001 *Summary Data Package* and discuss the scope and schedule for additional work at the site.

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| Well Number | Screen Interval (feet bgs) | Type of Screen | Date Checked | NAPL Observation/ Recovery (L) | Total NAPL Recovered To Date (L) |
|---|---|---|---|---|---|
| MW-10 | 8.7 to 19.5 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-12 | 14.5 to 25.5 | Screen | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-12S | 11 to 26 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-14S | 10 to 25 | Screen | 12/18/01 | NAPL Not Present | NAPL Not Present |
| MW-15S | 5 to 10 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-16 | 6 to 16 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-17 | 13 to 23 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-21S | 5 to 10 | Screen | 12/18/01 | NAPL Not Present | NAPL Not Present |
| MW-23S | 7.5 to 12.5 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-25S | 11 to 26 | Screen | 10/25/01 | NAPL Not Present | Trace NAPL |
| MW-26S | 7.5 to 22.5 | Screen | 12/28/01 | 0.3 | 16.85 |
| MW-30S | 10 to 25 | Screen | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-31S | 8 to 18 | Screen | 10/4/01 | NAPL Not Present | NAPL Not Present |
| RH-1S | 1.8 to 17.3 | Screen | 12/28/01 | 0.2 | 11.75 |
| MW-1 | 11.6 to 16.85 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-10I | 22 to 43 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-11 | 9.5 to 15 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-13 | 44.7 to 55.5 | Screen | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-14 | 30 to 41 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-15I | 12.5 to 22.5 | Screen | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-17I | 23 to 45 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-18 | 28 to 38 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-19I | 18 to 38.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-2 | 11.2 to 14.35 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-22I | 17 to 32 | Screen | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-25I | 27 to 47 | Open Hole | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-26I | 24.5 to 45.5 | Open Hole | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-28I | 15 to 25 | Screen | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-29I | 11.5 to 26 | Open Hole | 12/18/01 | NAPL Not Present | Trace NAPL |
| MW-2I | 11.28 to 32.2 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-35I | 12.5 to 34.5 | Open Hole | 12/18/01 | Trace NAPL | 2 |
| MW-10D | 82 to 114 | Open Hole | 12/28/01 | 3.1 | 202.66 |
| MW-14D | 91 to 121.7 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-15D | 96 to 105.8 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-17D | 121 to 142.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-20D | 90 to 110.1 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-21D | 48.7 to 59.4 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-23D | 56 to 80 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-29D | 90 to 110 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-30D | 90 to 121 | Open Hole | 12/18/01 | Trace NAPL | Trace NAPL |
| MW-31D | 28 to 150 | Open Hole | 10/4/01 | NAPL Not Present | NAPL Not Present |
| MW-32D | 91 to 111.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| MW-33D | 119.7 to 140.5 | Open Hole | 12/18/01 | NAPL Not Present | NAPL Not Present |
| MW-34D | 100 to 120.5 | Open Hole | 10/18/01 | NAPL Not Present | NAPL Not Present |
| RH-1D | 86.5 to 107.5 | Open Hole | 12/18/01 | NAPL Not Present | NAPL Not Present |

**TABLE 2**
**SUMMARY OF SYNOPTIC**
**WATER LEVEL MEASUREMENTS**

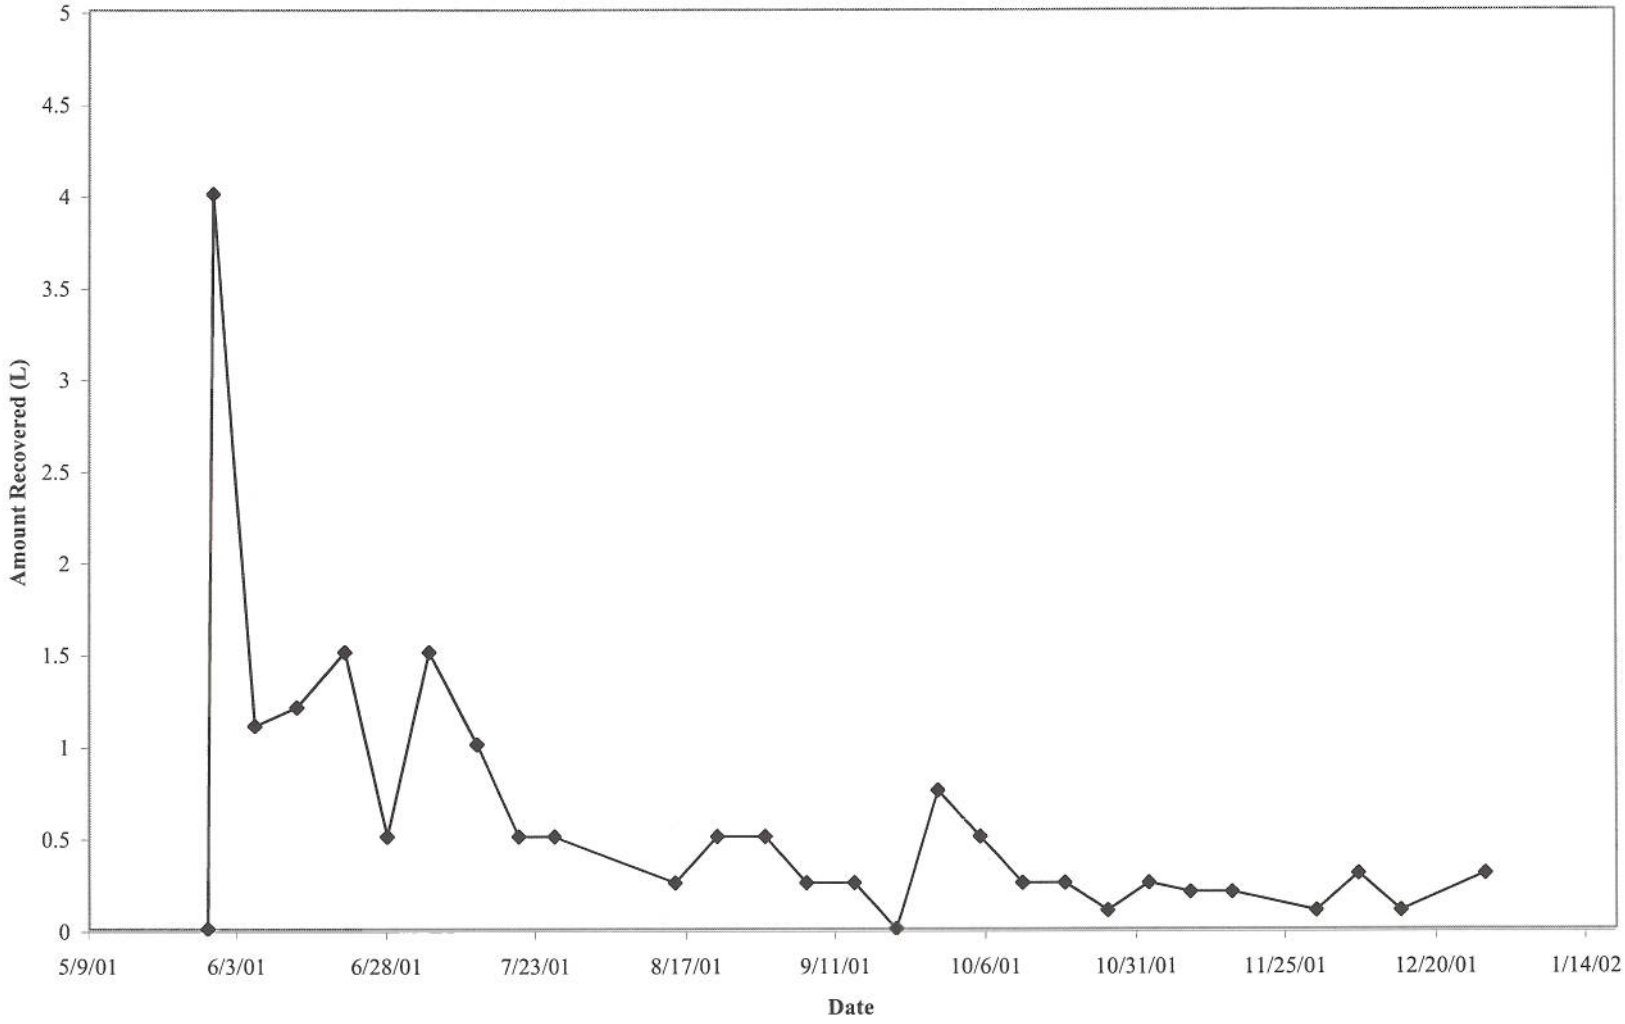
| WELL NUMBER | Water Elevation (feet msl) | | |
|---|---|---|---|
| | 10/10/01 | 10/31/01 | 12/4/01 |
| MW-10 | 80.70 | 80.58 | 80.79 |
| MW-12 | 80.10 | 79.99 | 79.88 |
| MW-12S | 78.60 | 78.52 | 78.59 |
| MW-14S | 78.30 | 78.18 | 78.30 |
| MW-15S | 79.20 | 79.54 | 79.72 |
| MW-16 | 85.78 | 85.82 | 86.10 |
| MW-17 | 79.01 | 78.73 | 78.68 |
| MW-21S | 80.19 | 80.32 | 80.90 |
| MW-23S | 77.38 | 77.25 | 77.44 |
| MW-25S | 78.69 | 78.62 | 78.79 |
| MW-26S | 79.80 | 79.65 | 79.81 |
| MW-30S | 79.28 | 79.02 | 79.13 |
| MW-31S | 80.81 | 80.74 | 80.67 |
| RH-1S | 82.09 | 82.06 | 81.78 |
| MW-1 | 82.35 | 82.34 | 82.60 |
| MW-10I | 79.35 | 79.22 | 79.35 |
| MW-11 | 81.06 | 81.20 | 81.67 |
| MW-13 | 78.56 | 78.49 | 78.55 |
| MW-14 | 78.24 | 78.16 | 78.22 |
| MW-15I | 78.22 | 78.23 | 78.49 |
| MW-17I | 78.21 | 78.12 | 78.19 |
| MW-18 | 78.69 | 78.54 | 78.64 |
| MW-19I | NM | NM | NM |
| MW-2 | 83.35 | 83.39 | 83.92 |
| MW-22I | 74.97 | 74.99 | 75.15 |
| MW-25I | NM | NM | NM |
| MW-26I | 79.49 | 79.38 | 79.50 |
| MW-28I | 73.85 | 74.10 | 74.15 |
| MW-29I | 75.06 | 75.02 | 75.09 |
| MW-2I | 83.34 | 83.37 | 83.95 |
| MW-35I | NM | NM | NM |
| MW-10D | NM | NM | NM |
| MW-14D | -2.46 | 22.79 | 47.02 |
| MW-15D | -3.78 | 18.40 | 44.22 |
| MW-17D | -13.08 | 35.65 | 73.71 |
| MW-20D | NM | 79.03 | 79.36 |
| MW-21D | 76.63 | 76.69 | 76.93 |
| MW-23D | 5.63 | 7.55 | 10.60 |
| MW-29D | 80.25 | 80.43 | 80.80 |
| MW-30D | 22.72 | 26.58 | 31.46 |
| MW-31D | 80.51 | 80.42 | 80.61 |
| MW-32D | -19.02 | -15.78 | -12.06 |
| MW-33D | 34.25 | 51.18 | 67.43 |
| MW-34D | NM | NM | NM |
| RH-1D | -20.65 | -19.16 | -18.83 |
| SG-1 | 72.32 | 72.40 | NM |
| SG-2 | 73.20 | 73.27 | 73.44 |
| SG-3 | 74.22 | 74.28 | 74.37 |

Note:
NM - not measured

**SUMMARY OF PRODUCT RECOVERY**
**MW-26S**

*Privileged & Confidential*

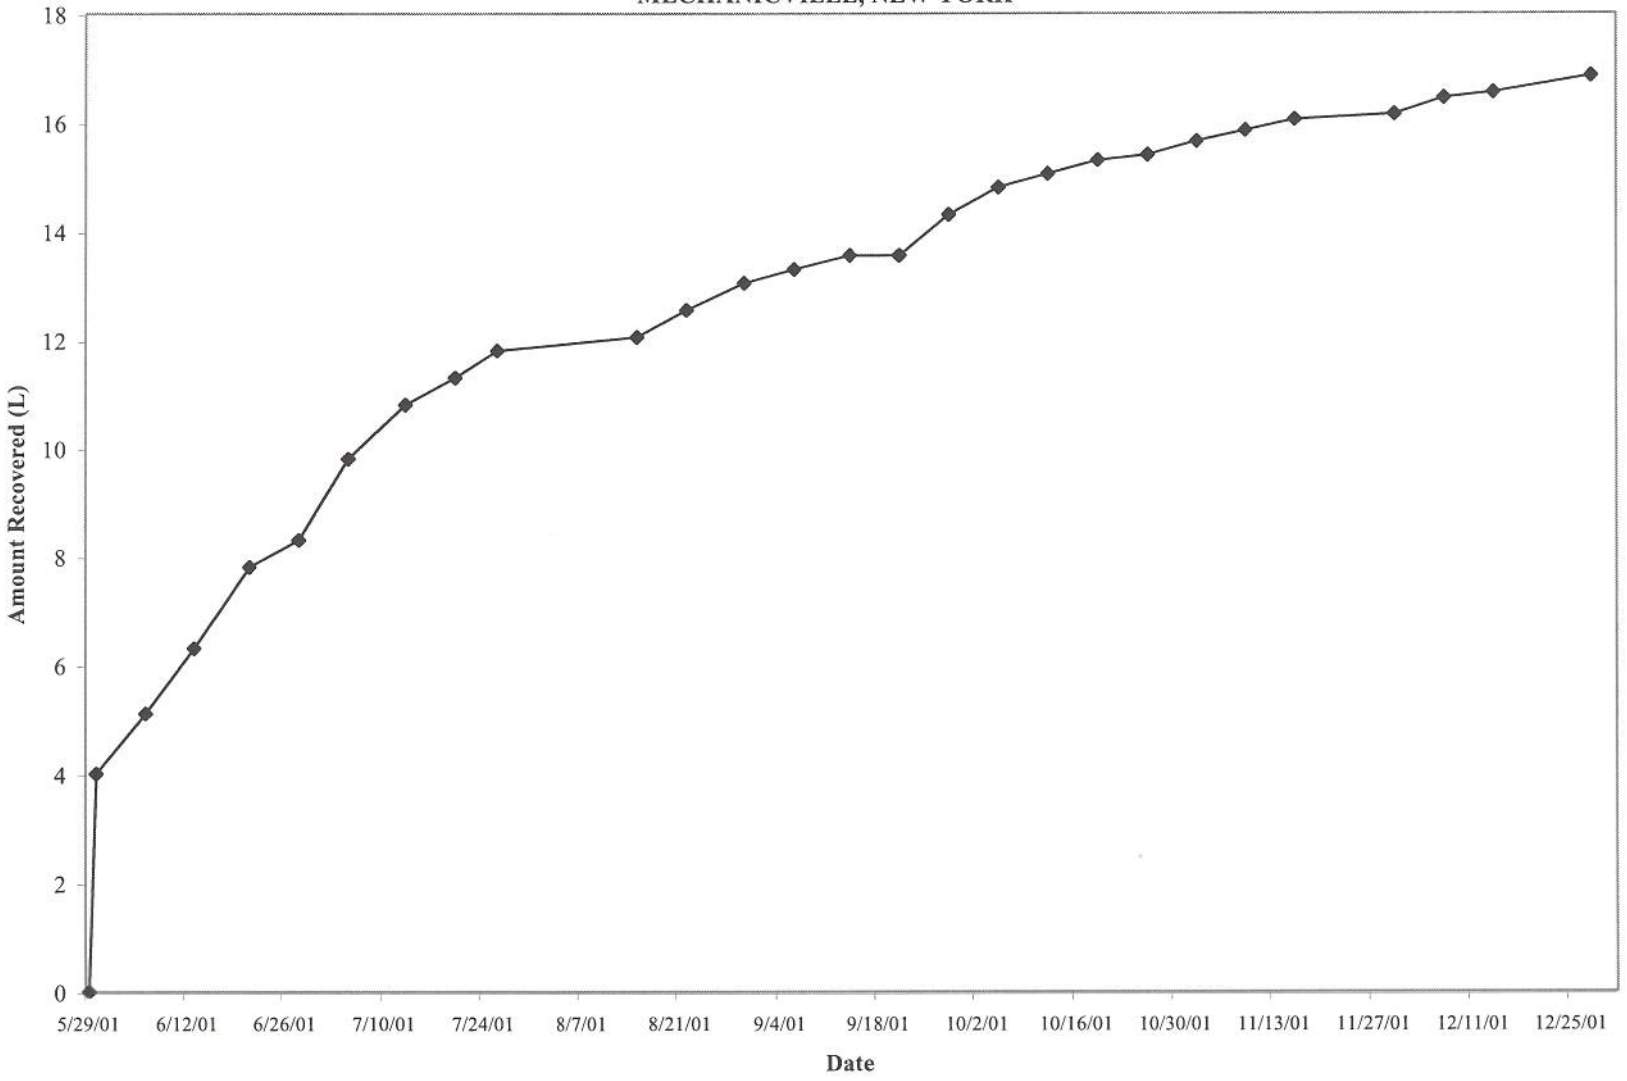
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-26S**

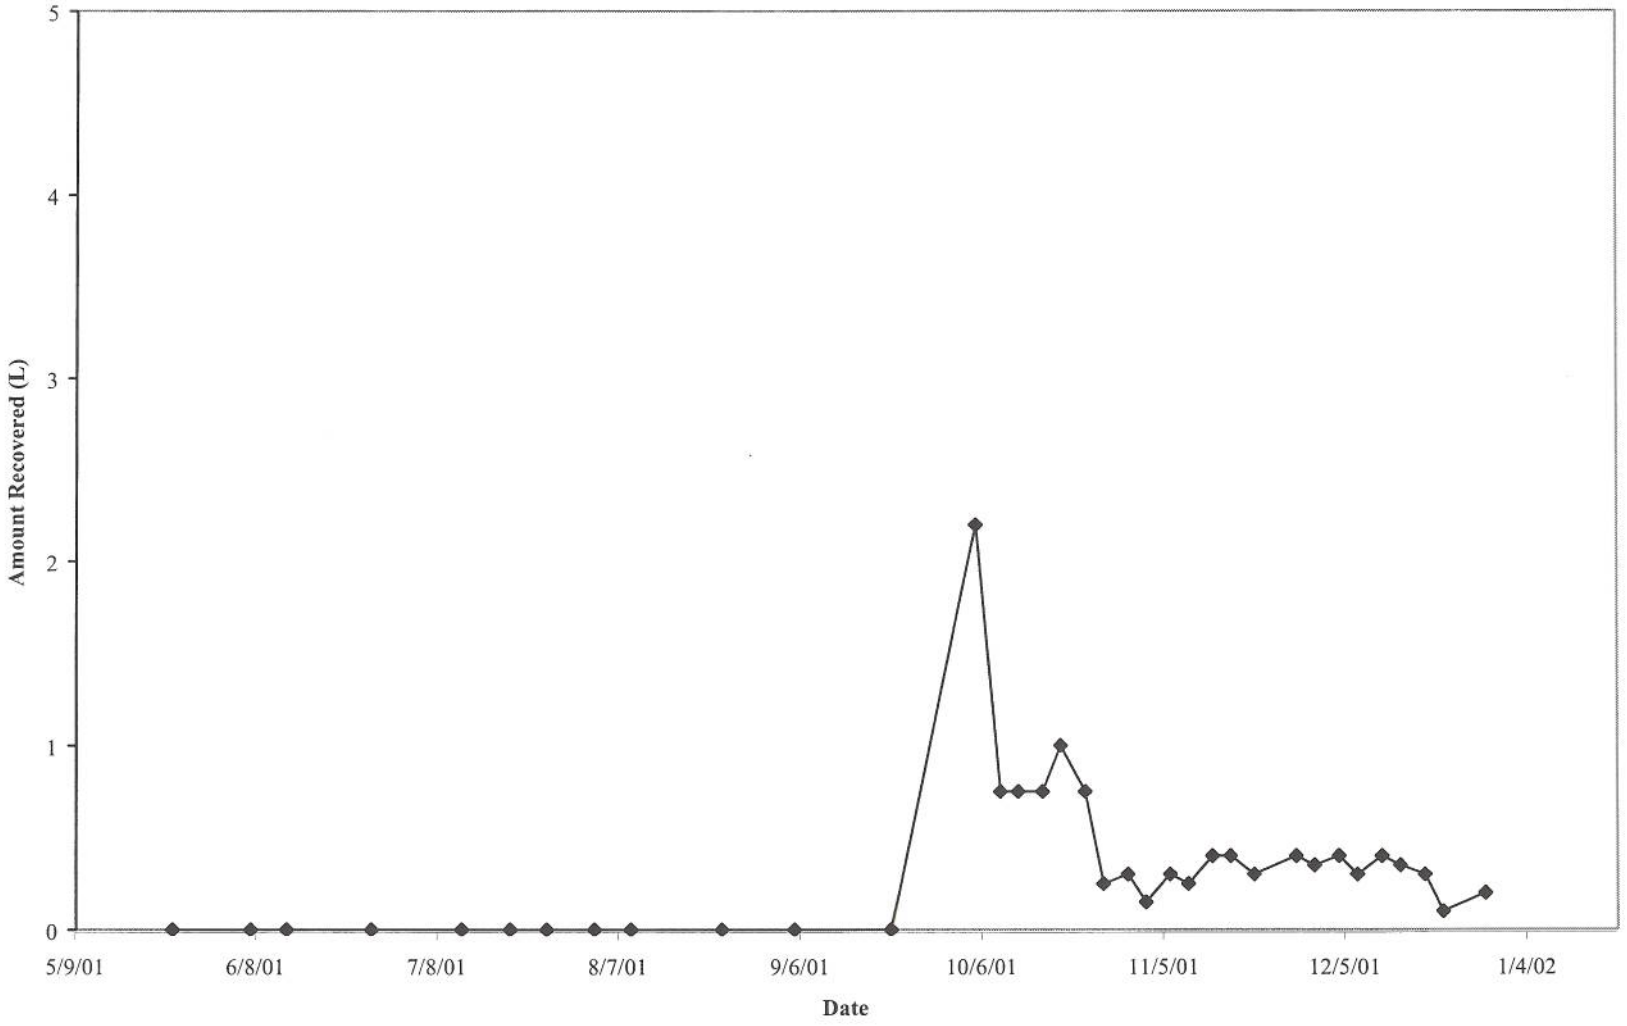
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**RH-1S**

*Privileged & Confidential*

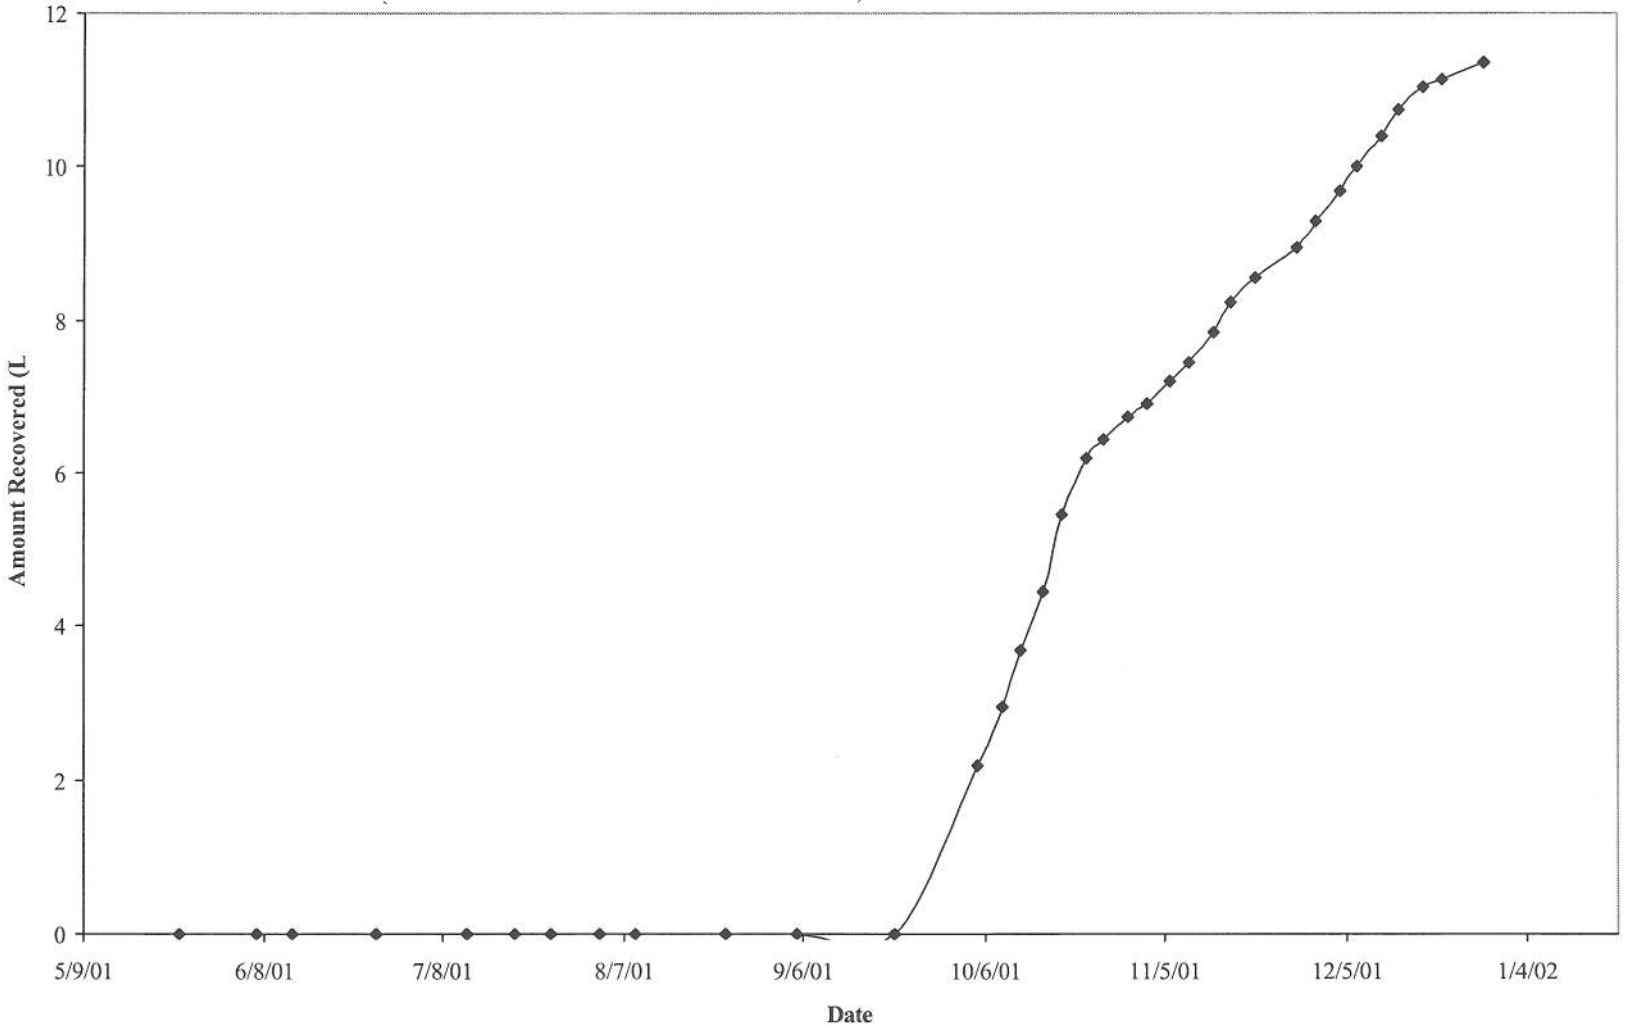
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**RH-1S**

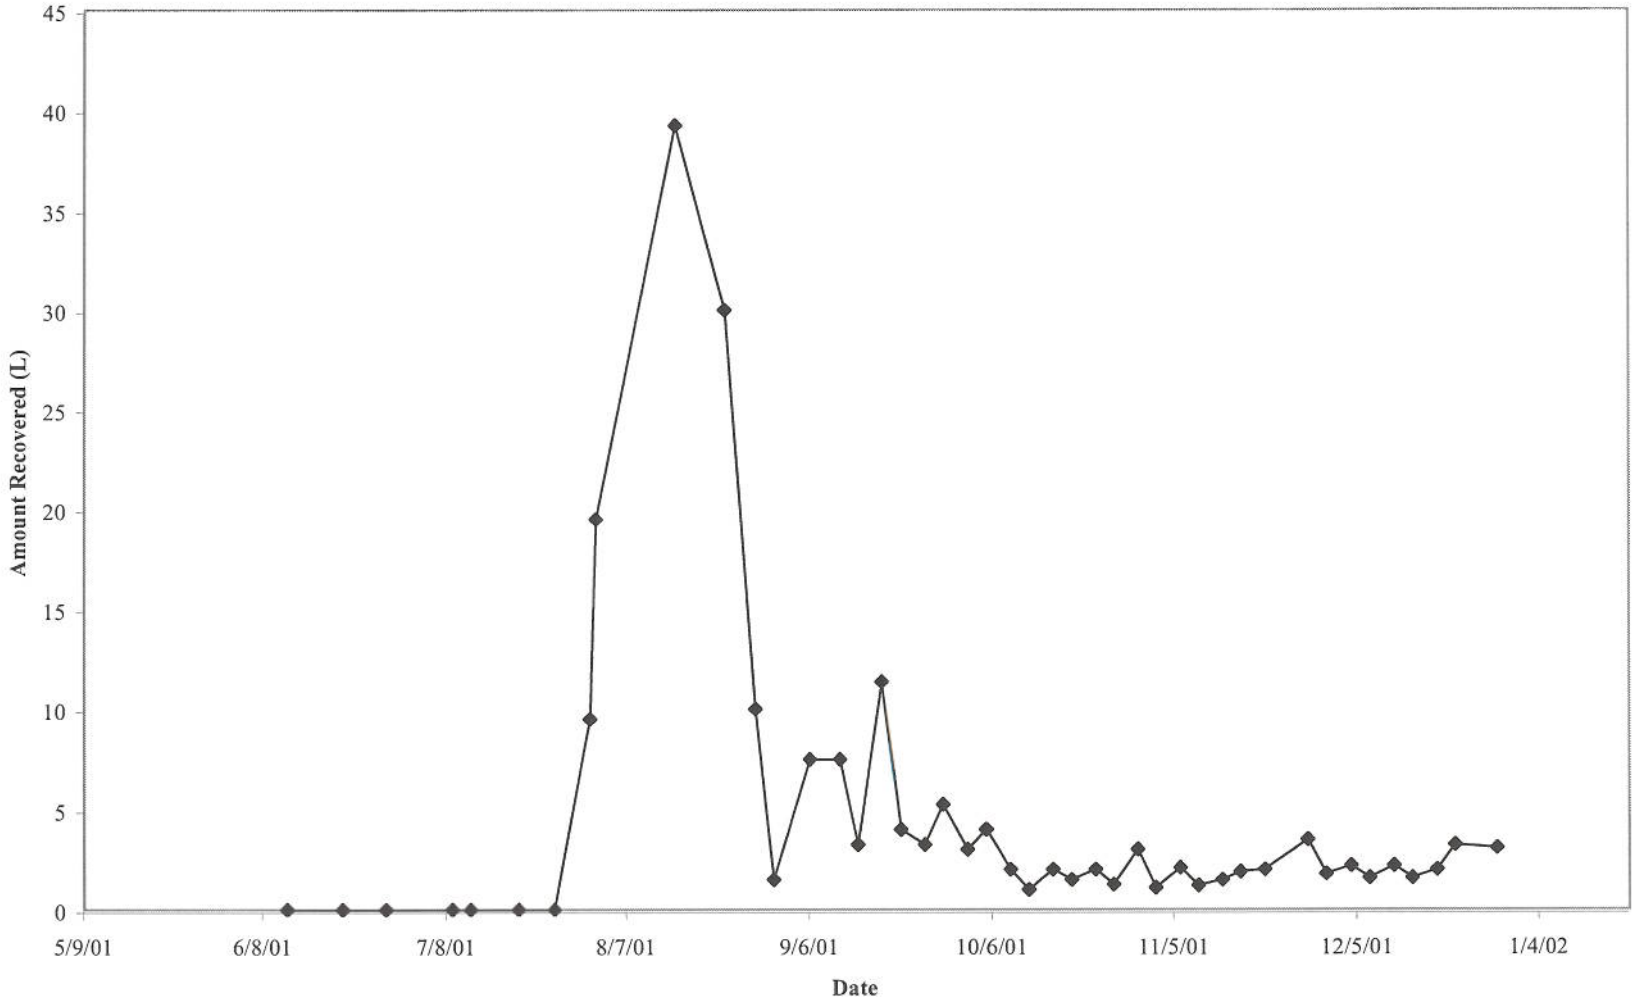
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**MW-10D**

*Privileged & Confidential*

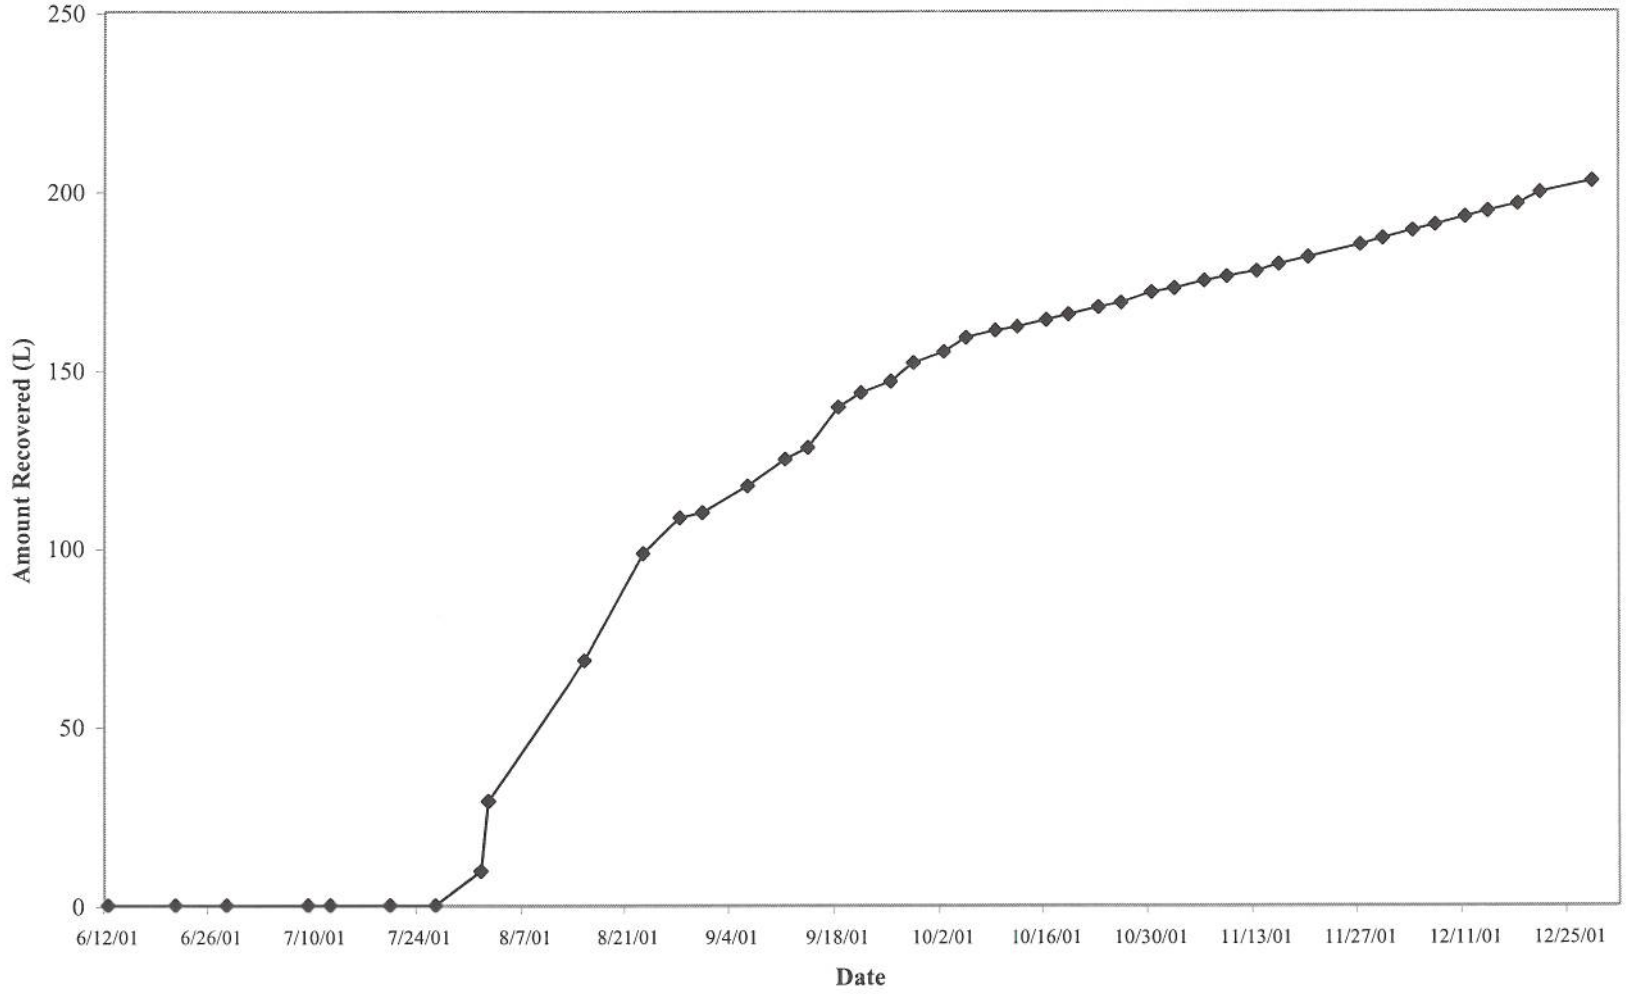
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-10D**

**NYSEG**
**MECHANICVILLE, NEW YORK**



# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS
Chris Gaule-URS

FROM: Eriko Fujita

DATE: December 17, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

**Tasks Completed During the Week of December 10, 2001**

On December 10, 2001, URS was onsite to assist NYSEG's contractor Clean Harbors with the drum pickup of the two drums of NAPL. The pickup was scheduled for 8:00am however, Clean Harbors did not arrive onsite until 9:50 am. (See out of scope activities).

On December 11, 2001, URS spoke to the Army Corps of Engineers who indicated that a joint application was probably warranted to conduct the sediment sampling work in the Hudson River. It was unclear whether sediment probing work would also warrant a permit. URS was also told that the permit review/approval process timing would depend upon the type of work proposed to be conducted. Further, it was suggested that the Canal Corporation (Thruway Authority) and the NYSDEC be contacted.

*Summary of NAPL Observations*

Between December 11 through 14, 2001, URS conducted NAPL checks and recovery at the site (see Table 2 Out of Scope Activities). Table 1 provides the NAPL observations for the wells.

| | **Overburden Wells** | | **Bedrock Well** | |
|---|---|---|---|---|
| | **MW-26S** | **RH-1S** | **MW-35I** | **MW-10D** |
| Cumulative Recovery as of December 7, 2001 | 16.6L | 10.8 L | 2 L | 194 L |
| Cumulative Recovery All Wells | 223 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

**Tasks to be Completed During the Week of December 17, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

Please note that URS will not be issuing a weekly report during the week of December 24, 2001. The next weekly report will be issued during the week of December 31, 2001 and will cover the previous two weeks.

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS
Chris Gaule-URS

FROM: Eriko Fujita

DATE: December 4, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

**Tasks Completed During the Week of November 26, 2001**

On November 27, 2001, the NYSDEC requested that a copy of the *Summary Data Package*, dated November 6, 2001 be forwarded to the NYSDOH. On November 29, 2001, following NYSEG's approval, URS sent a copy of the *Summary Data Package* to Dan Geraghty of the NYSDOH (see Table 2 Out of Scope Activities).

*Summary of NAPL Observations*

On November 27 and 30, 2001, URS conducted NAPL checks and recovery at the site (see Table 2 Out of Scope Activities). Table 1 provides the NAPL observations for the wells.

| | Overburden Wells | | Bedrock Well | |
|---|---|---|---|---|
| | MW-26S | RH-1S | MW-35I | MW-10D |
| Cumulative Recovery as of November 20, 2001 | 16.2 L | 9.30 L | 2 L | 187 L |
| Cumulative Recovery All Wells | 215 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

**Tasks to be Completed During the Week of December 3, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary. URS will collect a synoptic round of water levels from the site.

URS will attempt to gather information from the Army Corps of Engineers regarding the portion of the Hudson River that is to be sampled as part of the sediment sampling task of the SRI work plan. The schedule to conduct the sediment sampling task has not yet been determined.

URS will assist NYSEG with their efforts to remove two drums containing NAPL (hazardous materials) for off-site disposal. The drum pick up by NYSEG's contractor is scheduled for November 10, 2001.

**TABLE 1**

*Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.17 |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 10/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.1 L of NAPL recovered | NA | NA |
| 10/31/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 11/2/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | None | 0.2 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.2 L of NAPL recovered | NA | NA |
| 11/30/01 | Odor, Sheen, Product | None | 0.1 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.15 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.35 L of NAPL recovered | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21 (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1**

*Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-35I (12.5 to 34.5 feet) Open Hole* | | | | | |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/31/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 1 |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.1 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.9 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 11/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.5 L of NAPL recovered | NA | NA |
| 11/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.8 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.5 |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

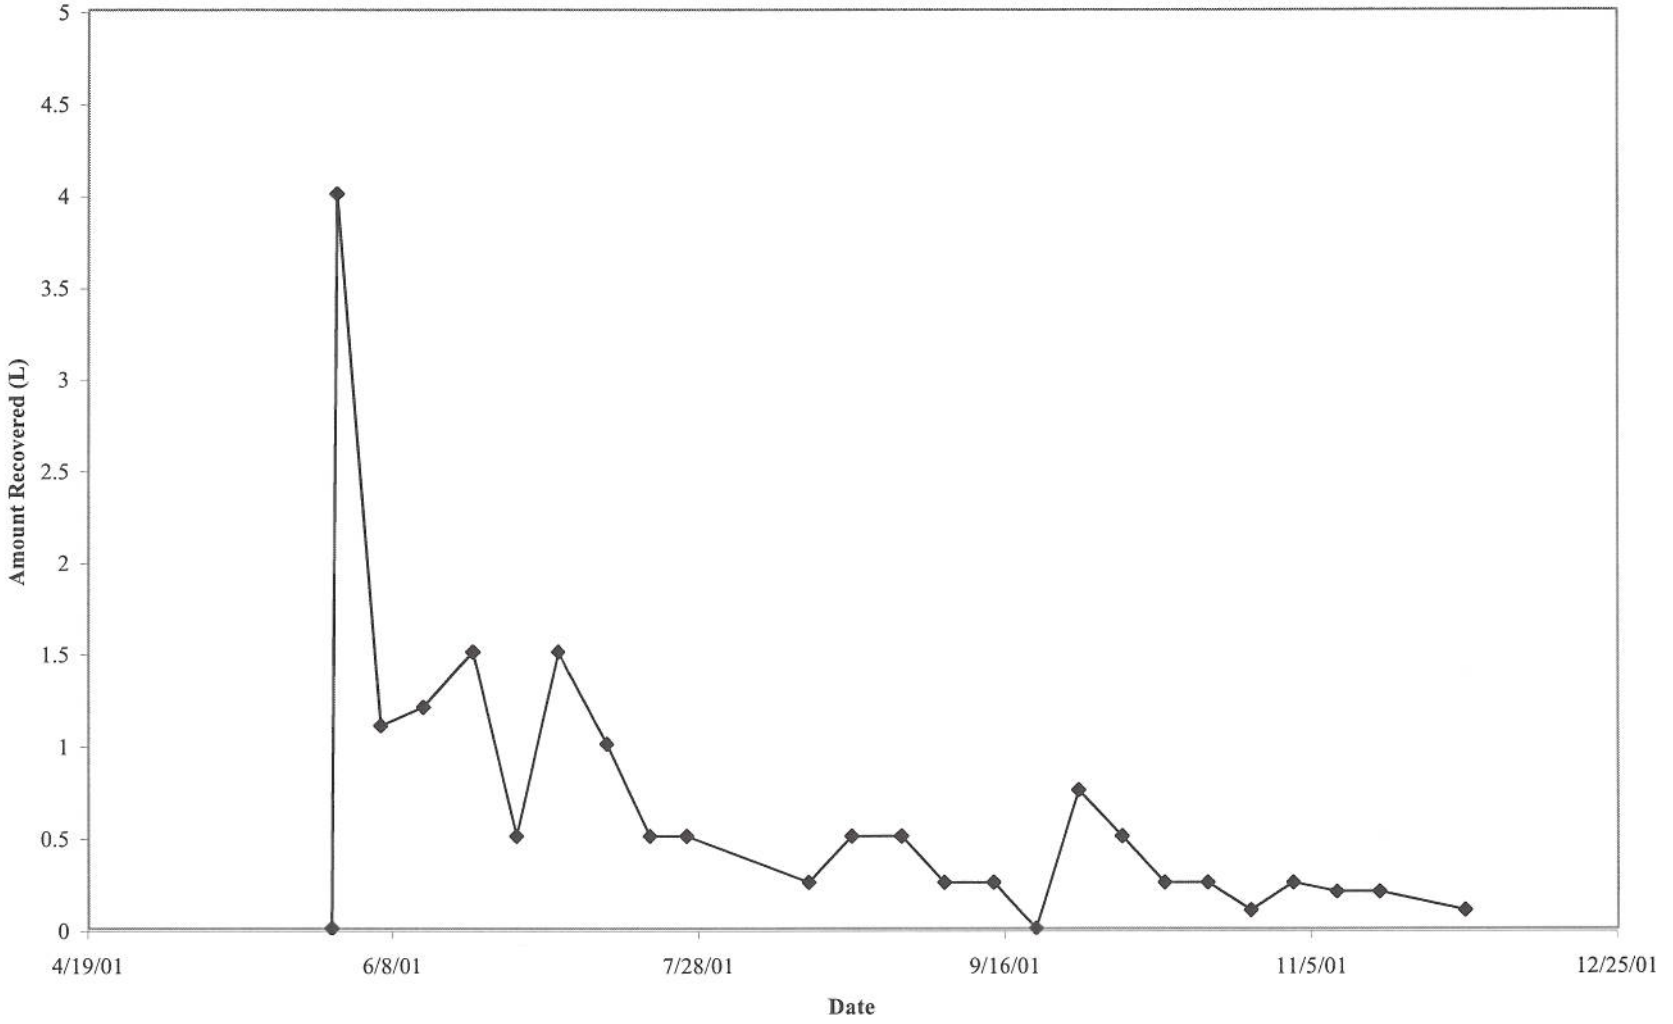
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**SUMMARY OF PRODUCT RECOVERY**
**MW-26S**

*Privileged & Confidential*

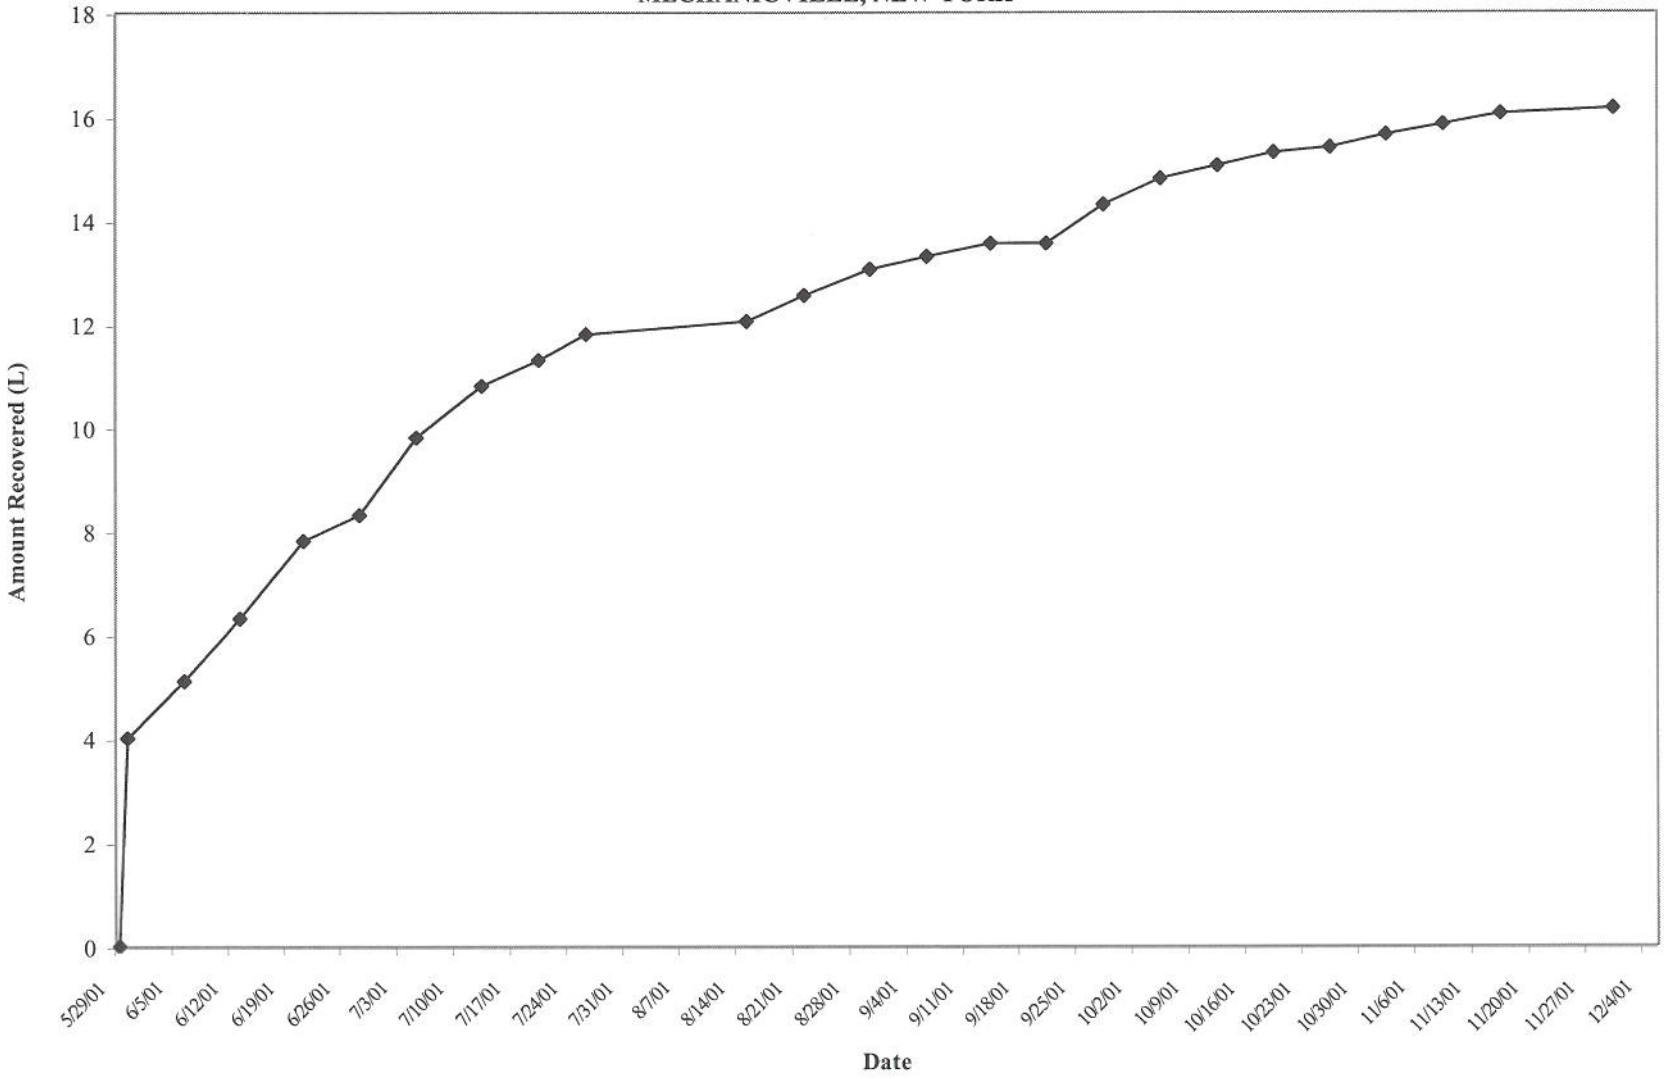
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-26S**

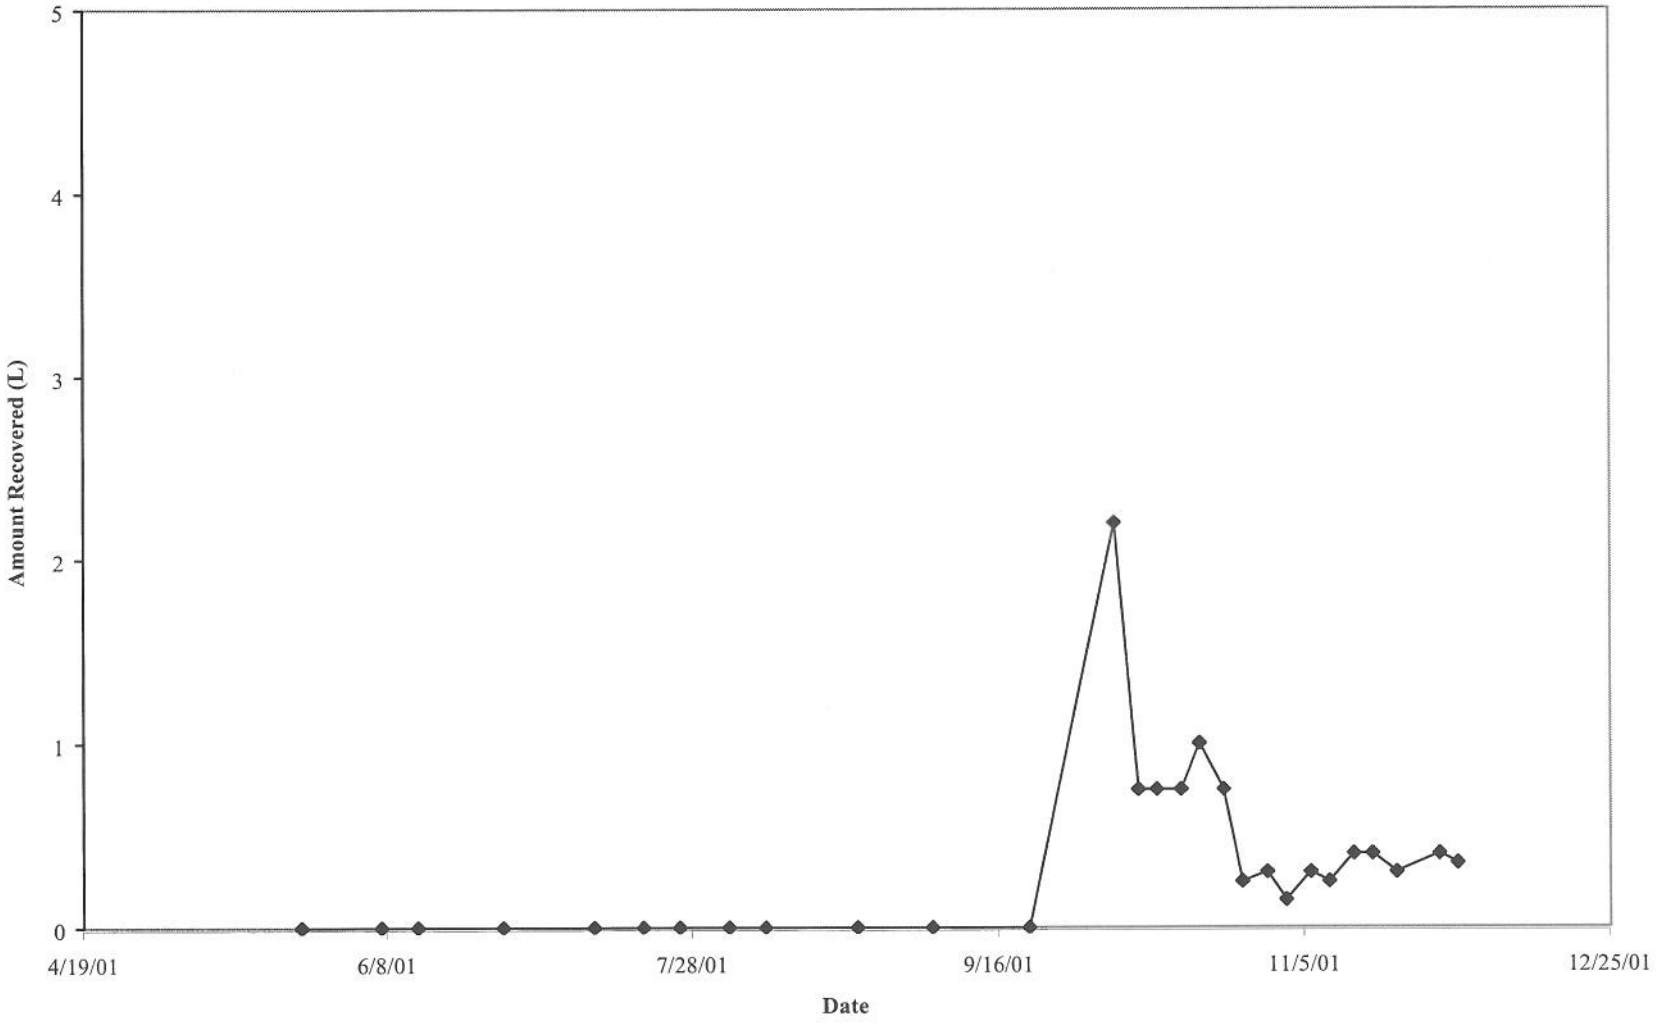
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**RH-1S**

*Privileged & Confidential*

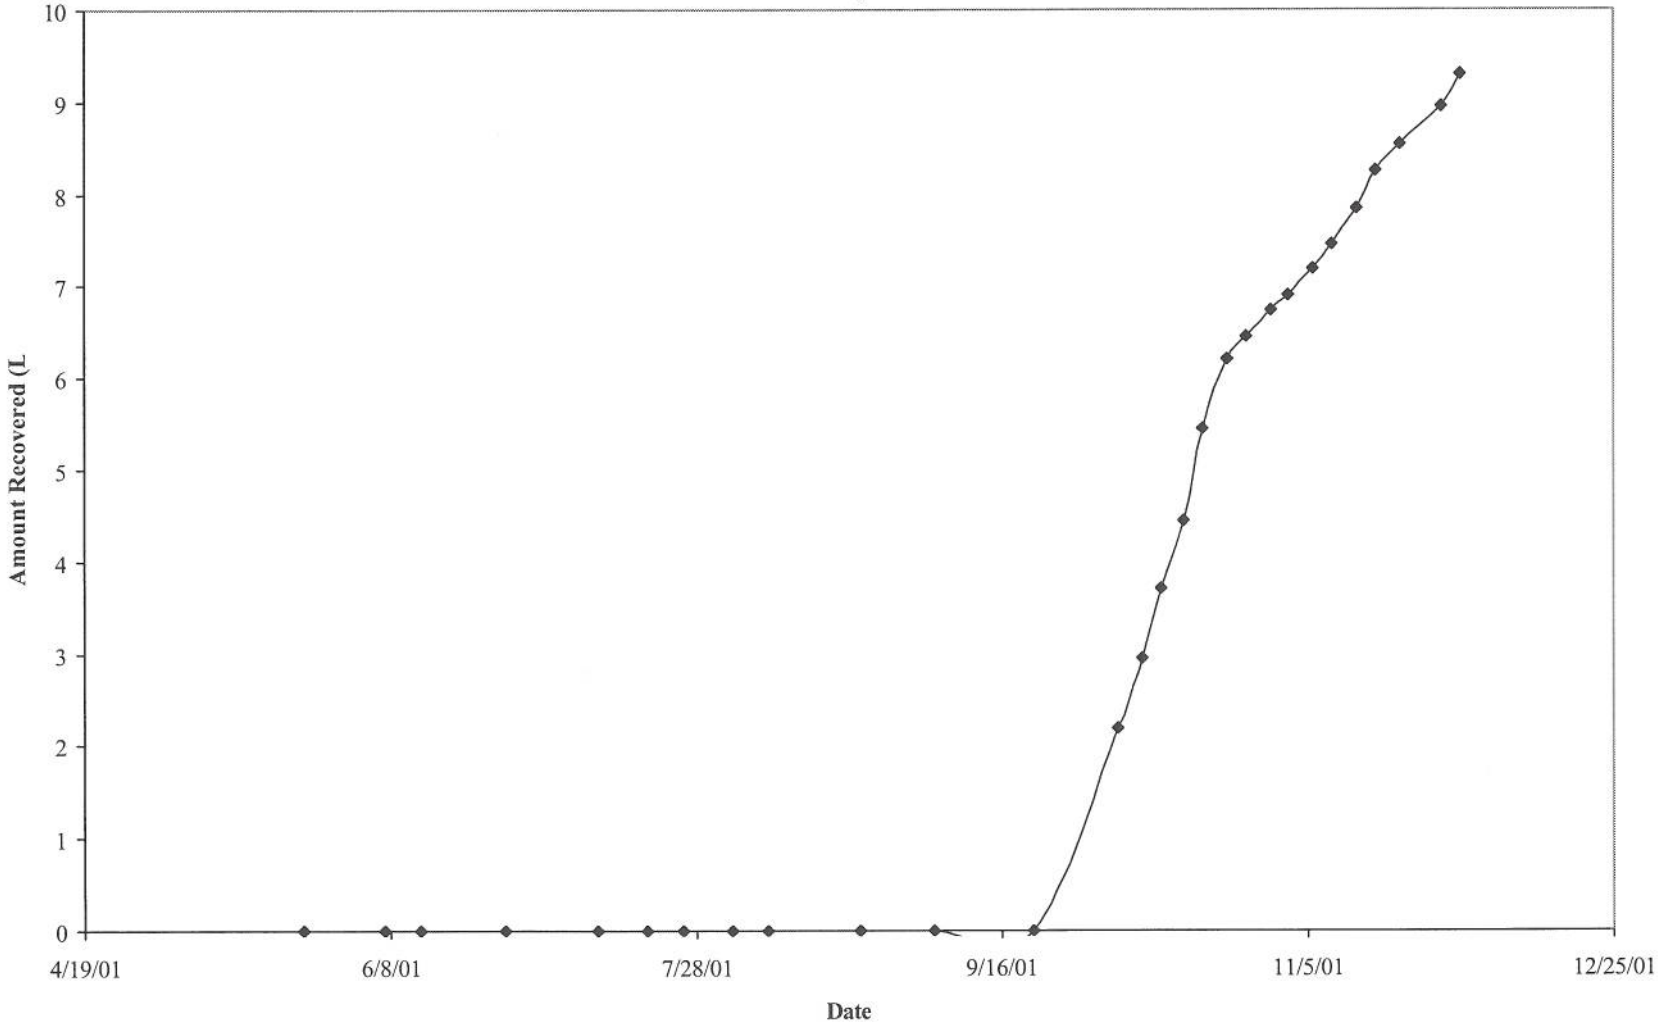
**NYSEG**
**MECHANICVILLE, NEW YORK**



**CUMULATIVE PRODUCT RECOVERY**
**RH-1S**

*Privileged & Confidential*

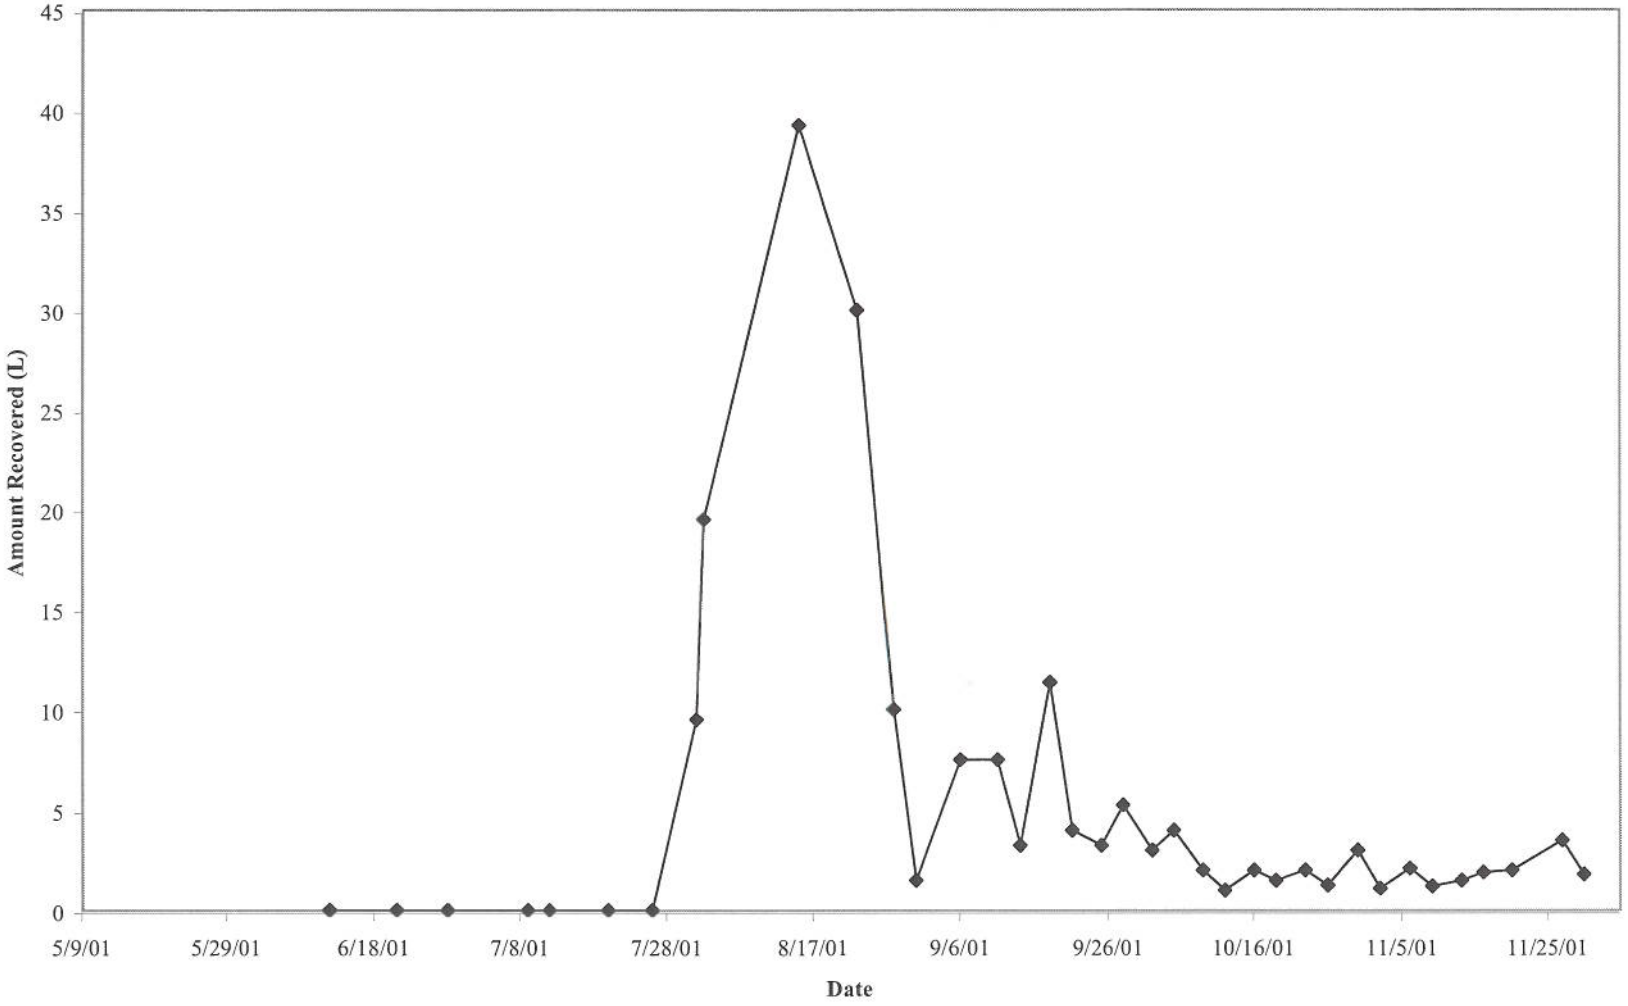
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**MW-10D**

*Privileged & Confidential*

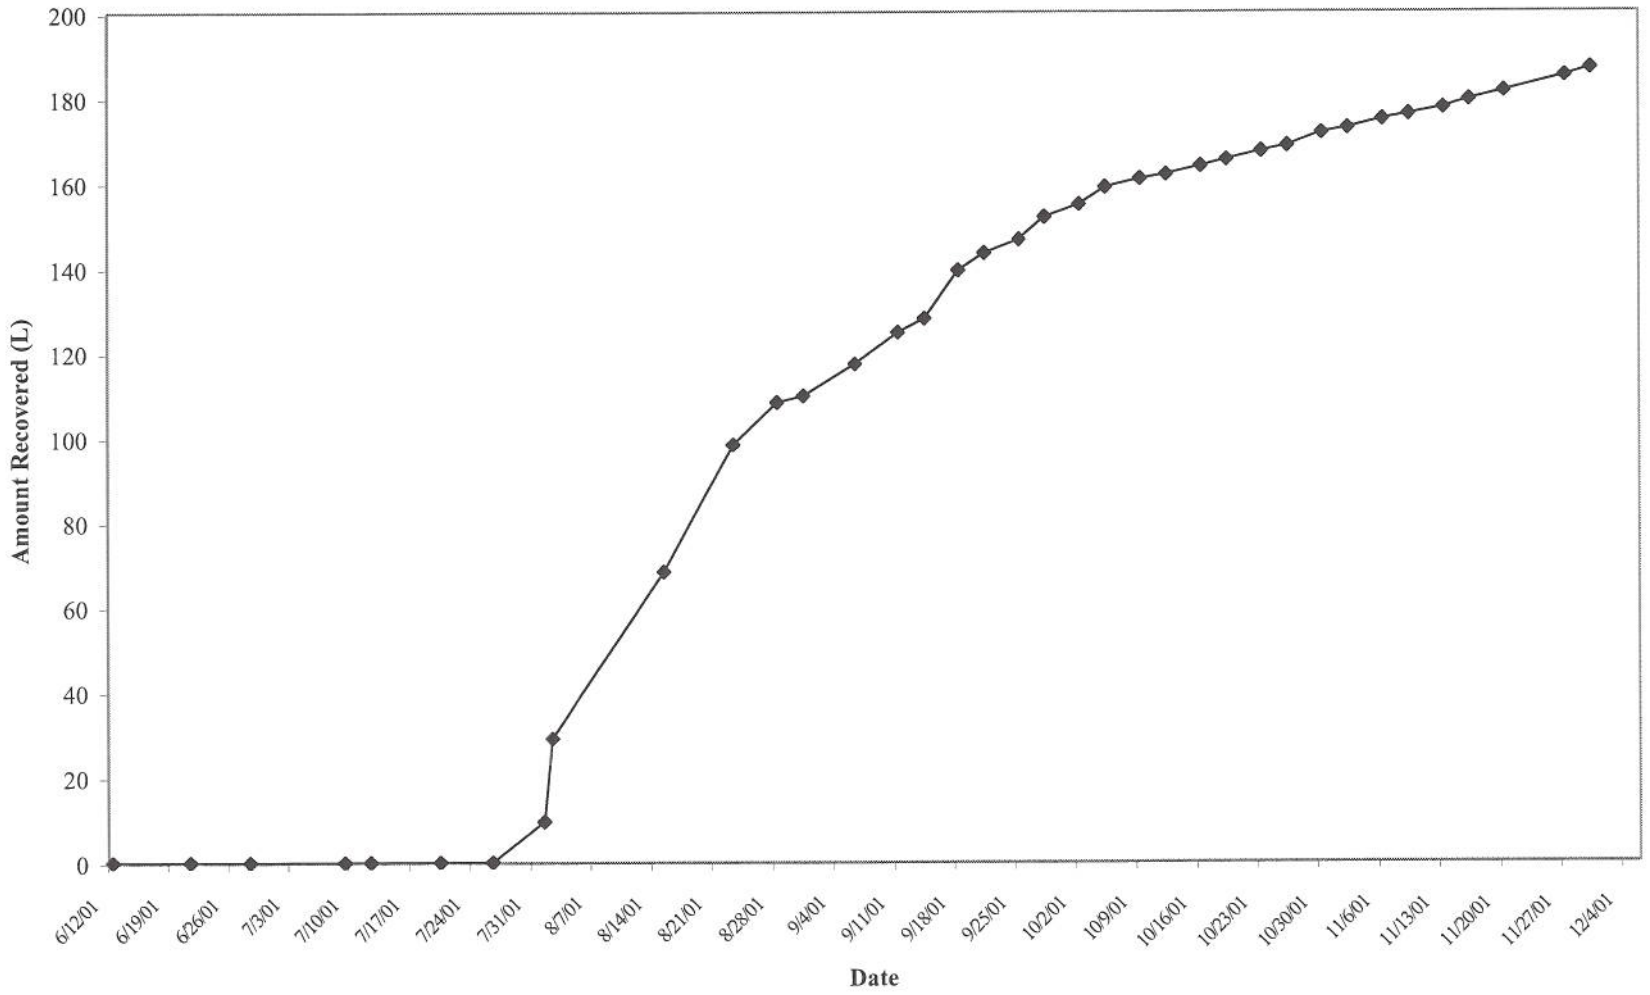
**NYSEG**
**MECHANICVILLE, NEW YORK**



*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-10D**

**NYSEG**
**MECHANICVILLE, NEW YORK**



# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS
Chris Gaule-URS

FROM: Eriko Fujita

DATE: November 26, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of November 19, 2001

On November 19, 2001, at the NYSDEC's request, URS forwarded e-files of the site basemap, the top of bedrock map, and the well location map from the November 6, 2001 *Summary Data Package* to the NYSDEC.

On November 19, 2001, NYSEG confirmed with URS that 191 drums of investigation derived wastes were removed for off-site disposal last week.

### *Summary of NAPL Observations*

On November 20, 2001, URS conducted NAPL checks and recovery at the site (see out of scope activities below). Table 1 provides the NAPL observations for the wells.

| | Overburden Wells | | Bedrock Well | |
|---|---|---|---|---|
| | MW-26S | RH-1S | MW-35I | MW-10D |
| Cumulative Recovery as of November 20, 2001 | 16.1 L | 8.55 L | 2 L | 181 L |
| Cumulative Recovery All Wells | 208 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

### *Out of Scope Activities and Costs*

See attached Table 2.



TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.17 |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 10/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.1 L of NAPL recovered | NA | NA |
| 10/31/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 11/2/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | None | 0.2 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.2 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.15 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | None | NAPL Not Present | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-35I (12.5 to 34.5 feet) Open Hole* | | | | | |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/31/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 1 |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.1 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.9 L of NAPL recovered | NA | NA |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.5 |
| 11/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| 11/20/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

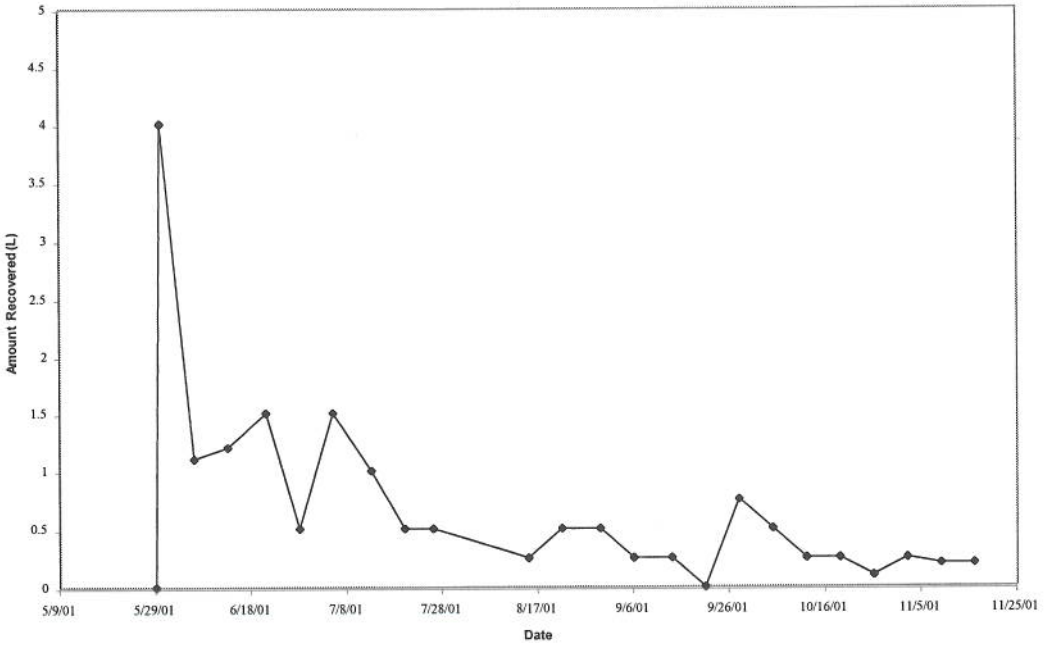


NYSEG-Mechanicville
11035-606/NAPLObs111901.xls

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



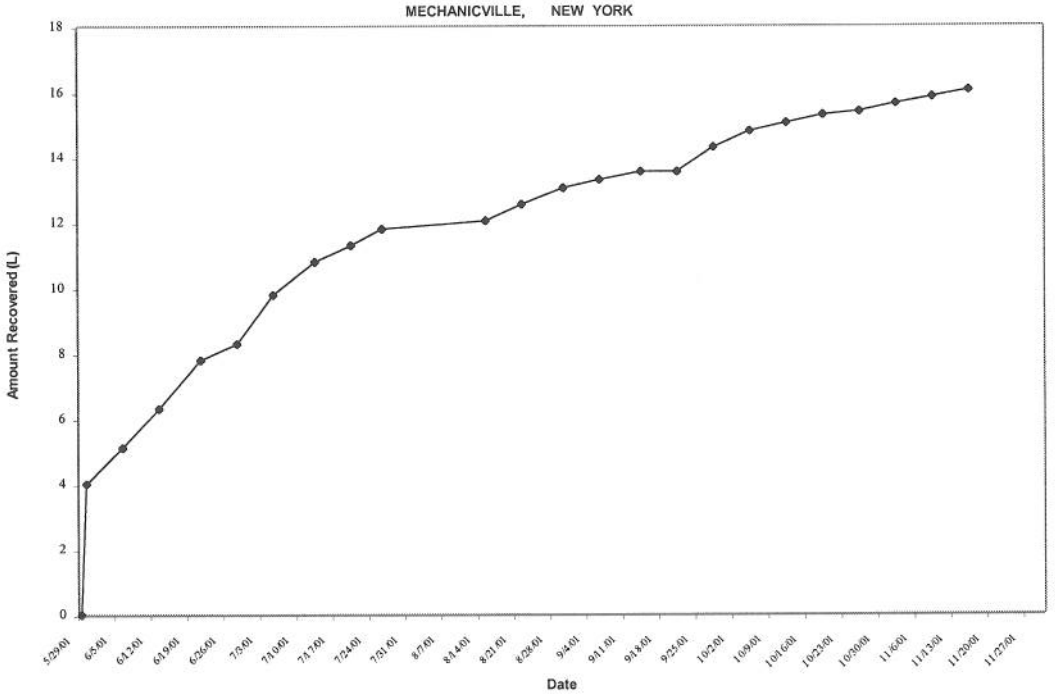

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S

URS
11/26/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



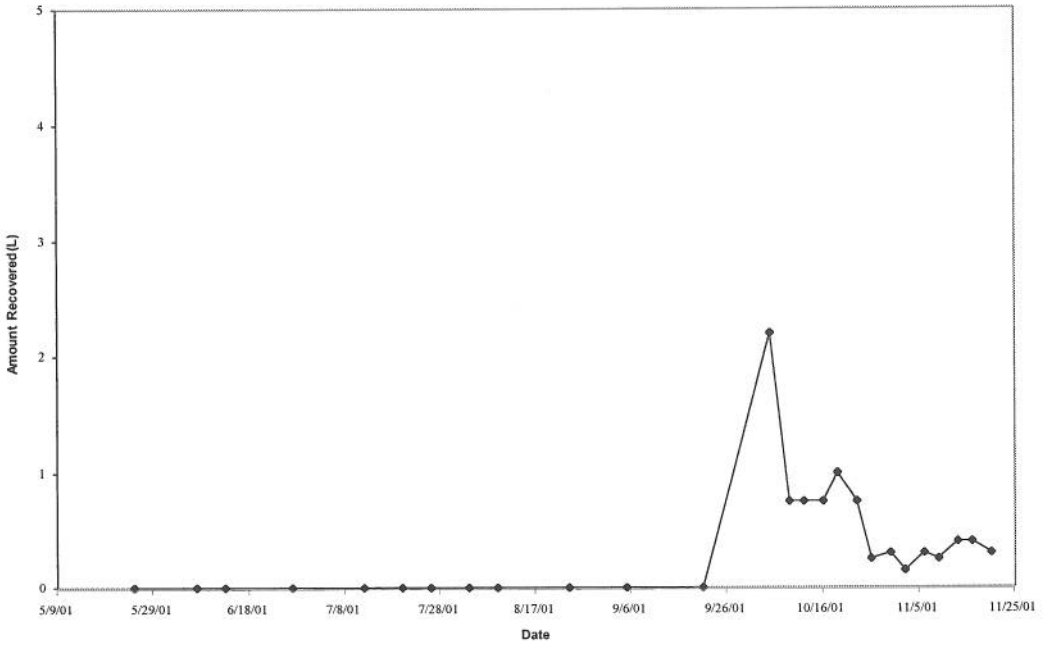

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S Cumulative

URS
11/26/01

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



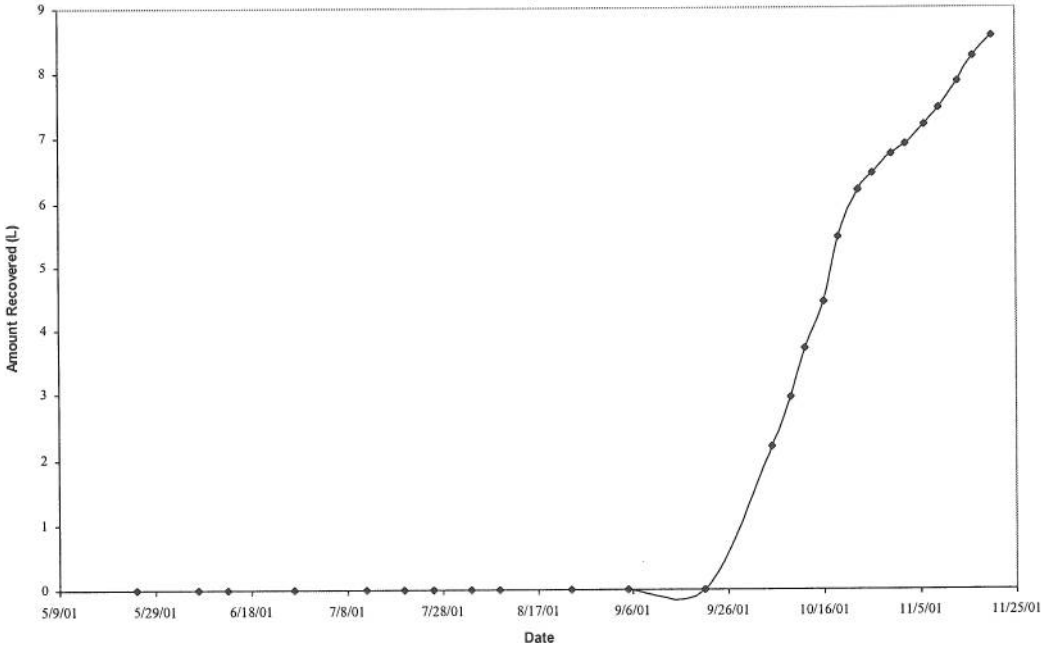

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S

URS
11/26/01

CUMULATIVE PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



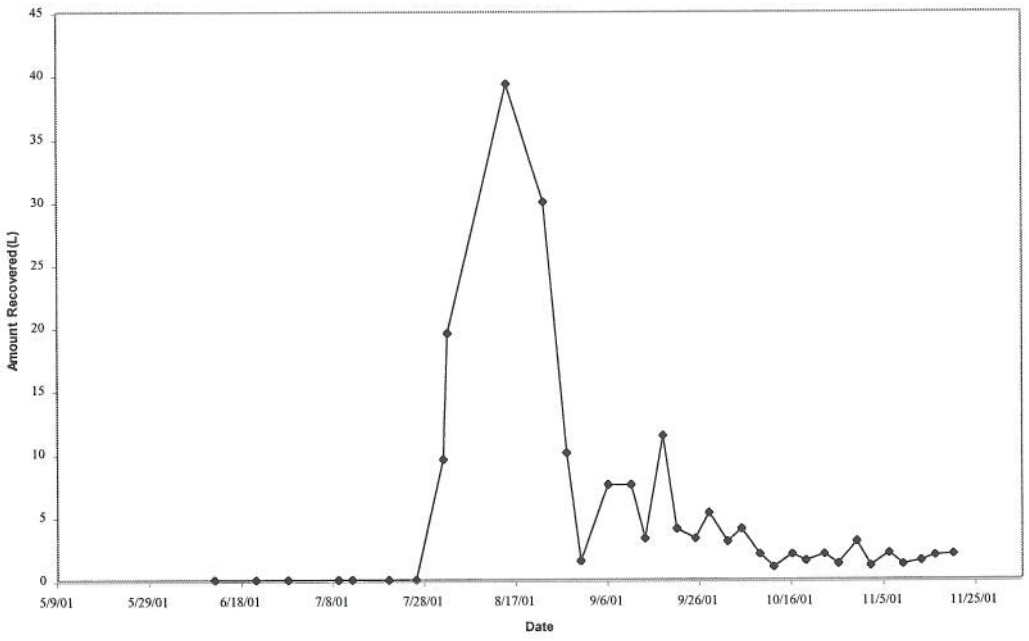

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S Cumulative

URS
11/26/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



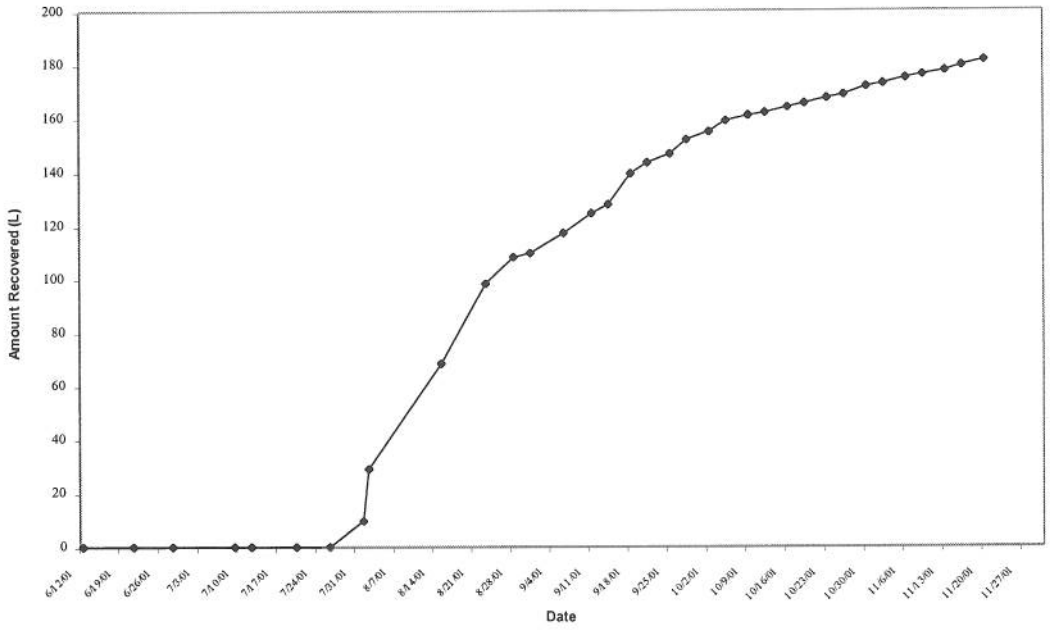

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D

URS
11/26/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D Cumulative

URS
11/26/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS
Chris Gaule-URS

FROM: Eriko Fujita

DATE: November 19, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of November 12, 2001

On November 13, 2001, NYSEG's contractor EPS was onsite to pickup 191 drums of investigation derived wastes for offsite disposal. EPS rented a bobcat to load the drums onto their trucks. One truck was loaded with drums and transported offsite on the first day. On the second day November 14, 2001, two trucks were loaded with drums and transported offsite.

On November 15, 2001, URS assisted NYSEG with loading trucks with the cold batch asphalt for offsite disposal. The loader had been delivered to the site on November 14, 2001. A total of 19 trucks were loaded with the cold batch asphalt between November 15 and 16, 2001. URS signed the non-hazardous waste shipment manifests on NYSEG's behalf.

On November 15, 2001, 6 yards of crushed stone was delivered to the site. With NYSEG's equipment operator's assistance, URS spread the stone over the exposed purifier wastes between the fence and the planter boxes along North Central Avenue.

*Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). Table 1 provides the NAPL observations for the wells.

| | Overburden Wells | | Bedrock Well | |
|---|---|---|---|---|
| | MW-26S | RH-1S | MW-35I | MW-10D |
| Cumulative Recovery as of November 15, 2001 | 16.1 L | 8.25 L | 2 L | 179 L |
| Cumulative Recovery All Wells | 205 L | | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

***Out of ScopeActivitiesand Costs***

See attached Table 2.

**Tasks to be Completed During the Week of November 19, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary. Because of the upcoming holiday, NAPL checks and recovery will only be conducted on Tuesday November 20, 2001.

URS will be prepared to be onsite to meet the hauler to pick up the loader that was used by NYSEG for loading the cold batch asphalt.

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

***Out of ScopeActivitiesand Costs***

See attached Table 2.

**Tasks to be Completed During the Week of November 19, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary. Because of the upcoming holiday, NAPL checks and recovery will only be conducted on Tuesday November 20, 2001.

URS will be prepared to be onsite to meet the hauler to pick up the loader that was used by NYSEG for loading the cold batch asphalt.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted, Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.17 |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 10/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

**TABLE 1** *Privileged & Confidential*

**SUMMARY OF NAPL OBSERVATIONS**

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.1 L of NAPL recovered | NA | NA |
| 10/31/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 11/2/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | None | 0.2 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.2 L of NAPL recovered | NA | NA |
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.15 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.4 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-35I (12.5 to 34.5 feet) Open Hole* | | | | | |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/31/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 1 |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.1 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 11/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 11/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.9 L of NAPL recovered | NA | NA |
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.5 |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

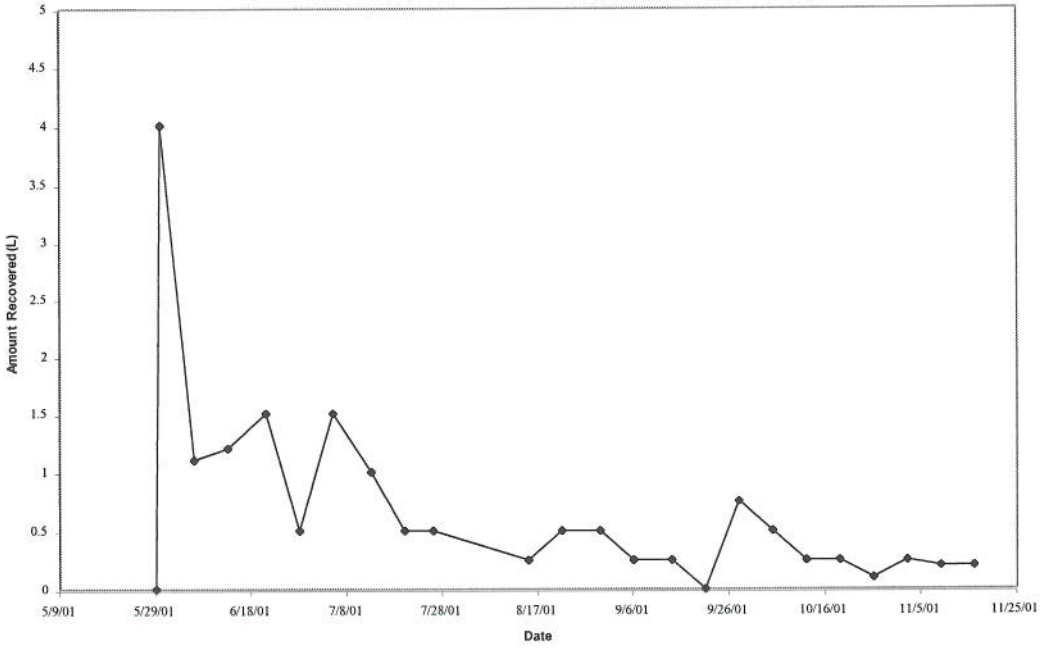
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



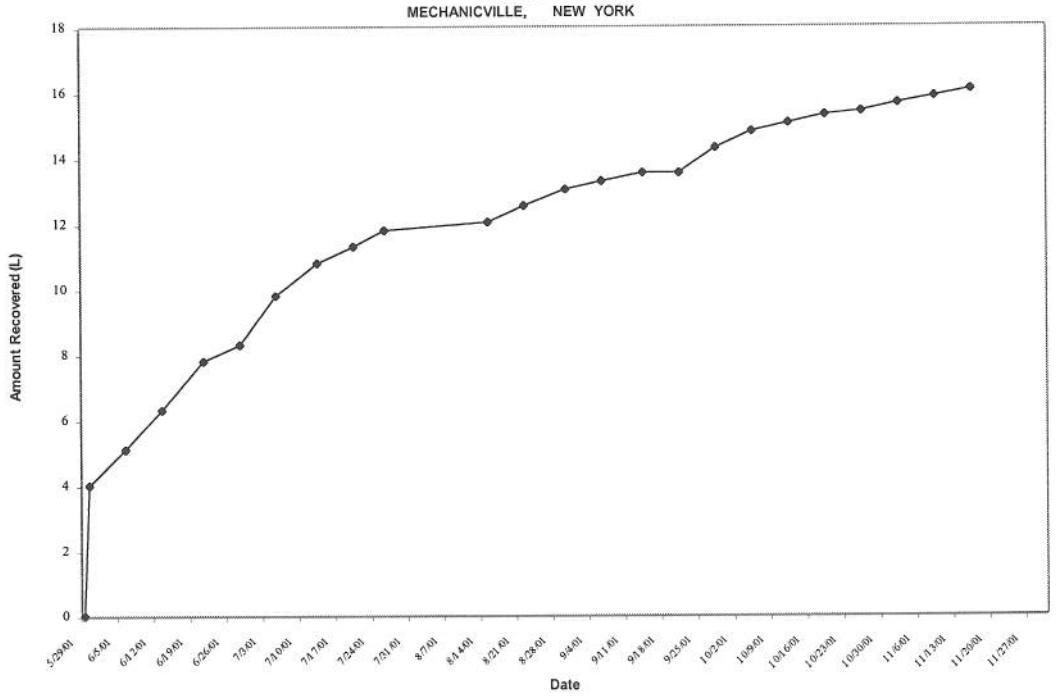

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S

URS
11/19/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



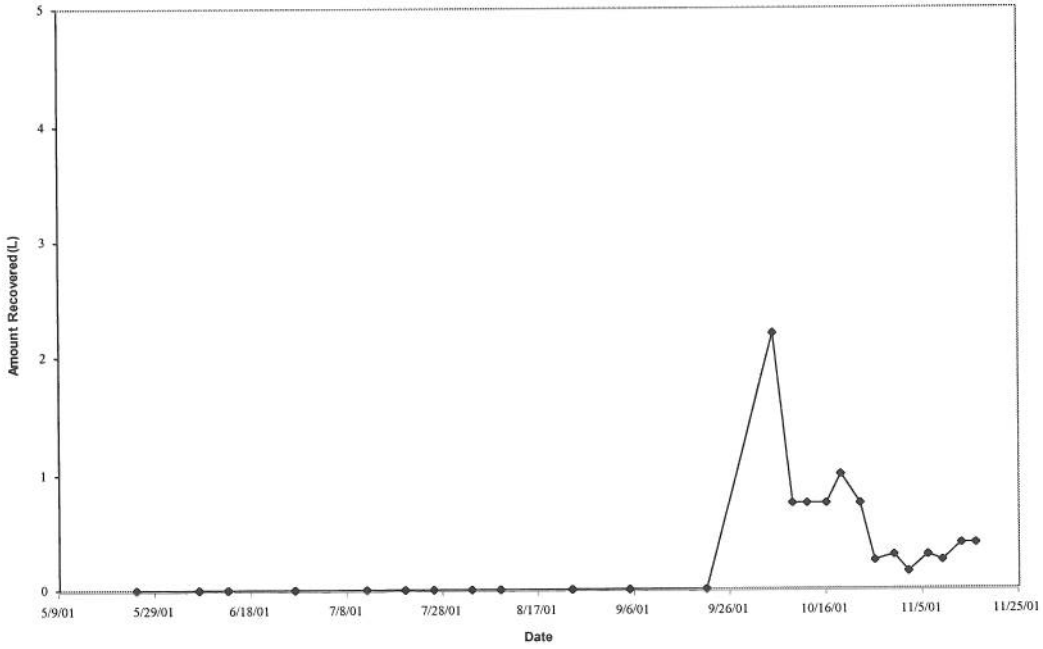

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S Cumulative

URS
11/19/01

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



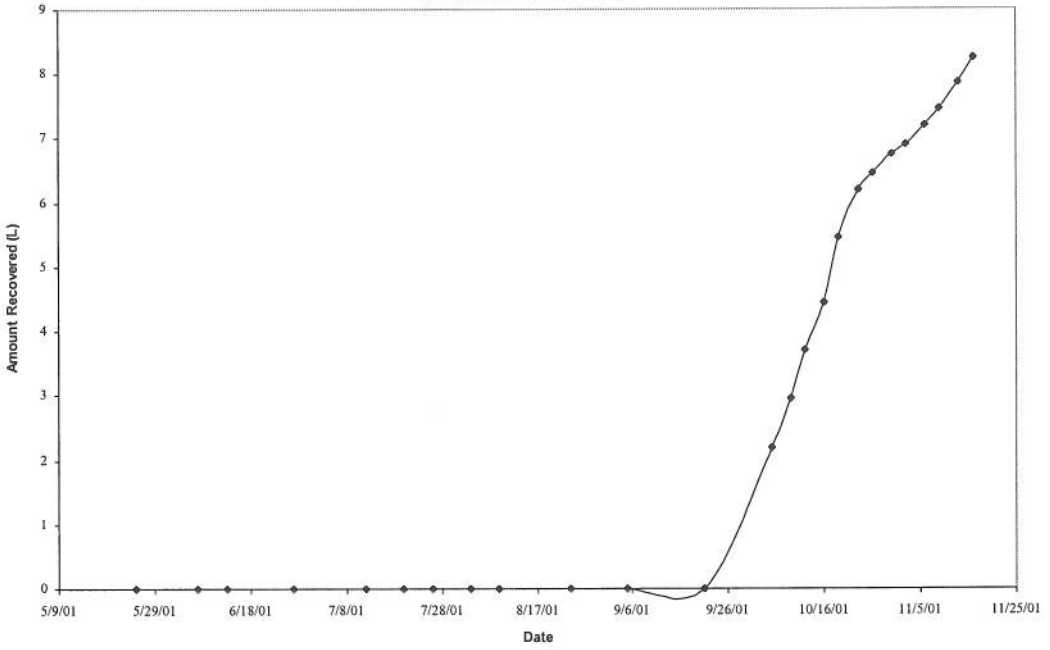

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S

URS
11/19/01

CUMULATIVE PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



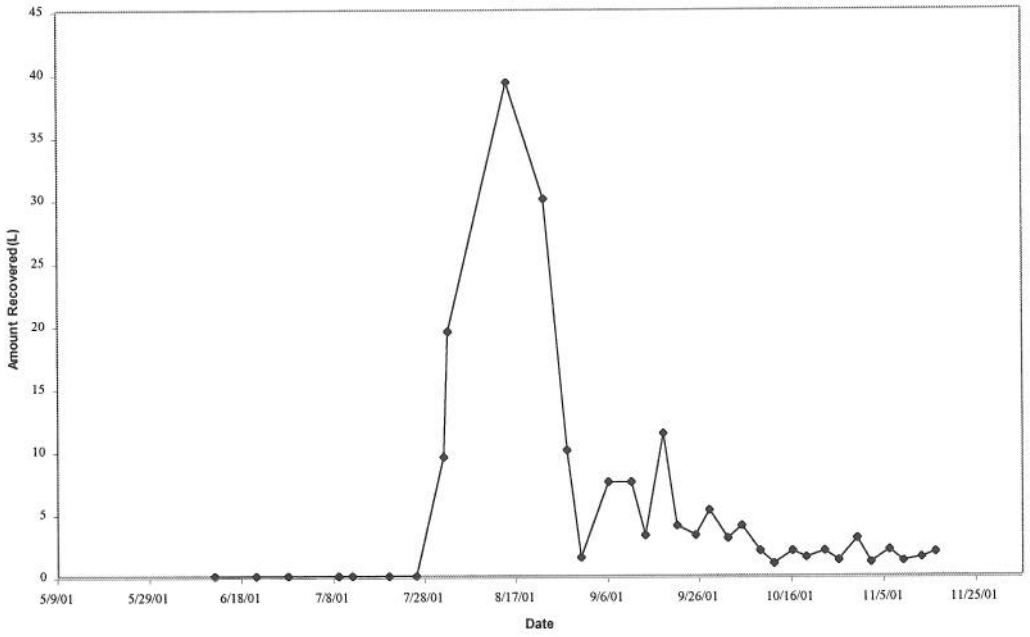

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S Cumulative

URS
11/19/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



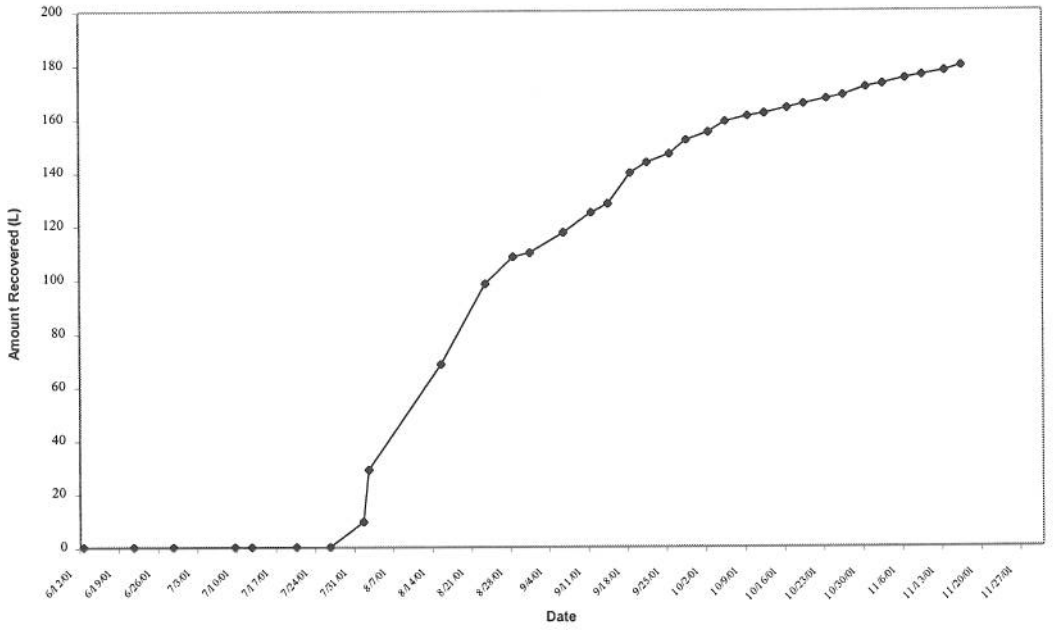

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D

URS
11/19/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

NYSEG
MECHANICVILLE, NEW YORK

*Privileged & Confidential*




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D Cumulative

URS
11/19/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS
Chris Gaule-URS

FROM: Eriko Fujita

DATE: November 12, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of November 5, 2001

On November 6, 2001, NYSEG and URS finalized and submitted two copies of the *Summary Data Package* to NYSDEC.

On November 7, 2001, NYSEG's contractor Clean Harbors was onsite for a water pickup. Throughout the week of November 5, 2001, NYSEG and URS discussed the drum pick up and cold batch asphalt removal work scheduled for the week of November 12, 2001.

### *Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). Table 1 provides the NAPL observations for the wells.

On November 7, 2001, URS measured approximately one-foot of product in well MW-35I. On November 8, 2001, URS removed approximately two liters of accumulated NAPL in well MW-35I using a peristaltic pump and a stainless steel bailer. Note that approximately two feet of soft sediment (bentonite) was detected at the bottom of the well. URS will continue to monitor well MW-35I on a weekly basis for NAPL. URS suggests that the bentonite be removed (possibly with split spoons) and re-developed with the assistance of the drillers during the next investigation phase.

| | Overburden Wells | | Bedrock Well |
|---|---|---|---|
| | MW-26S | RH-1S | MW-10D |
| Cumulative Recovery as of November 8, 2001 | 15.9 L | 7.45 L | 176 L |
| Cumulative Recovery All Wells | 199 L | | |

Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

***Out of ScopeActivitiesand Costs***

See attached Table 2.

**Tasks to be Completed During the Week of November 12, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

Between November 13, 2001 and 15, 2001, URS will be prepared to be onsite to assist NYSEG with oversight of NYSEG's drum removal contractor, delivery of a loader, and the removal of the cold batch asphalt from the site by NYSEG personnel. URS will also have approximately 5 yards of No. 1 crushed stone delivered to the site that will be used as cover material for the purifier waste materials between the planter boxes and the fence along North Central Avenue.



TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Prusent | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.17 |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 10/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | None | NAPL Not Present | NA | NA |
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.1 L of NAPL recovered | NA | NA |
| 10/31/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 11/2/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | None | 0.2 L of NAPL recovered | NA | NA |
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.15 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.3 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 11/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-35I (12.5 to 34.5 feet) Open Hole* | | | | | |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/31/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 1 |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.25 L of NAPL recovered | NA | NA |
| 10/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 11/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 11/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.1 L of NAPL recovered | NA | NA |
| 11/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 11/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | 0.5 |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| 11/7/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

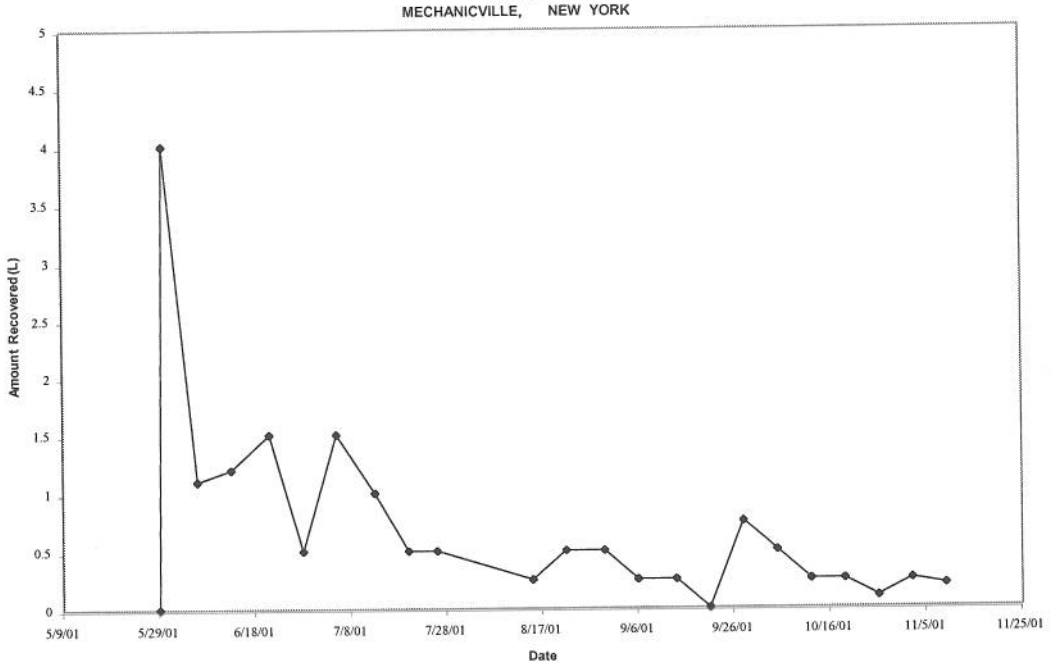
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

*Privileged & Confidential*

SUMMARY OF PRODUCT RECOVERY
MW-26S

NYSEG
MECHANICVILLE, NEW YORK



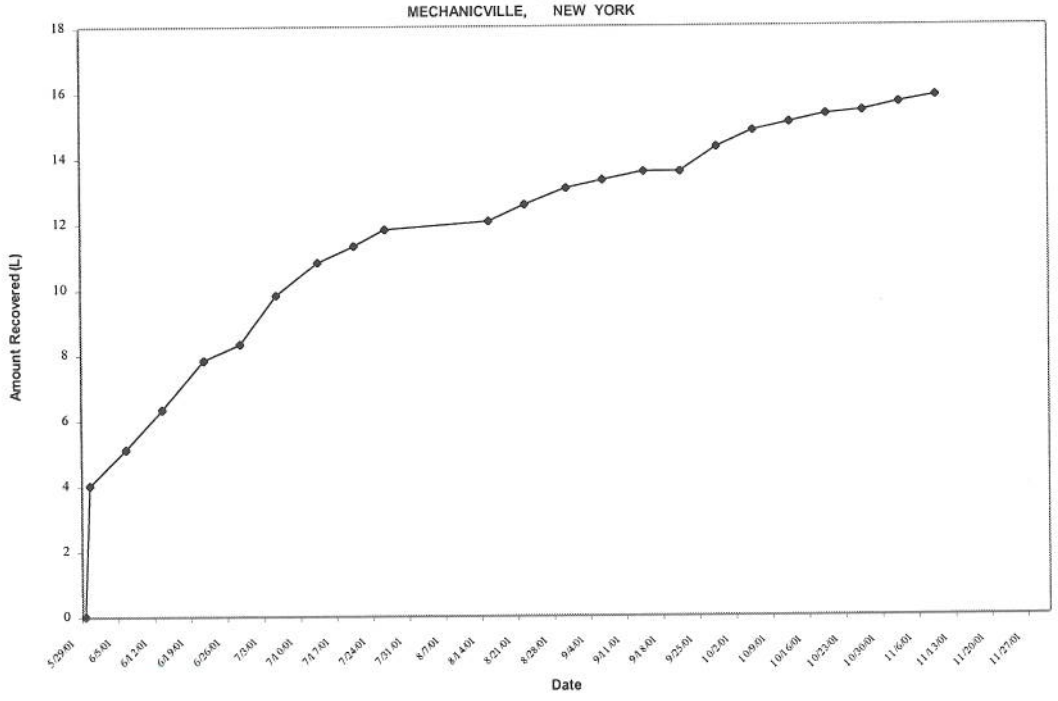

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S

URS
11/12/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



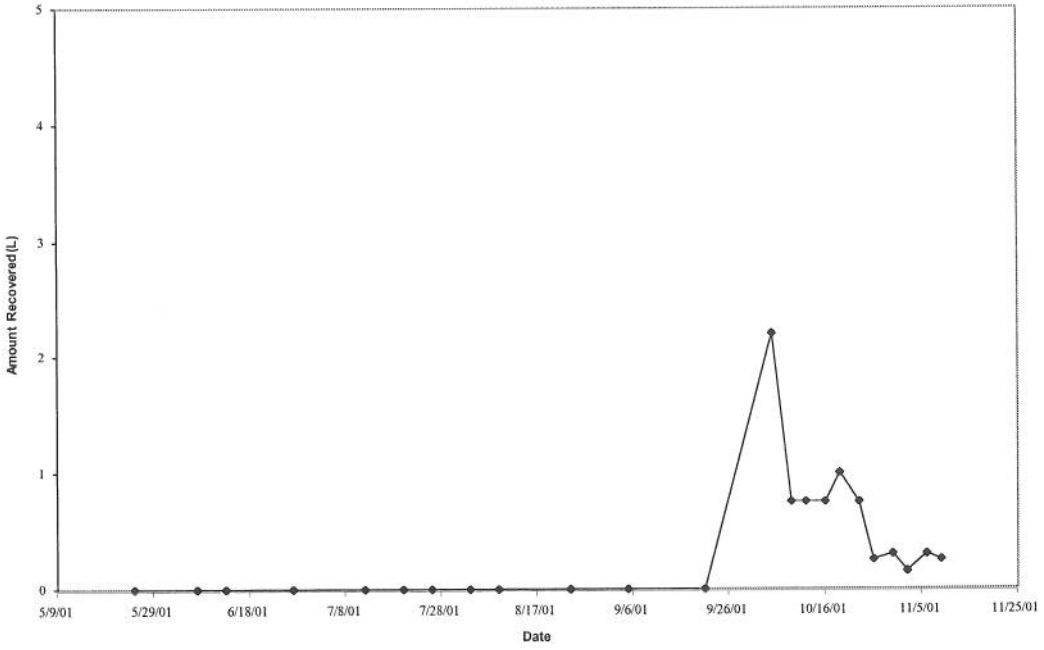

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S Cumulative

URS
11/12/01

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



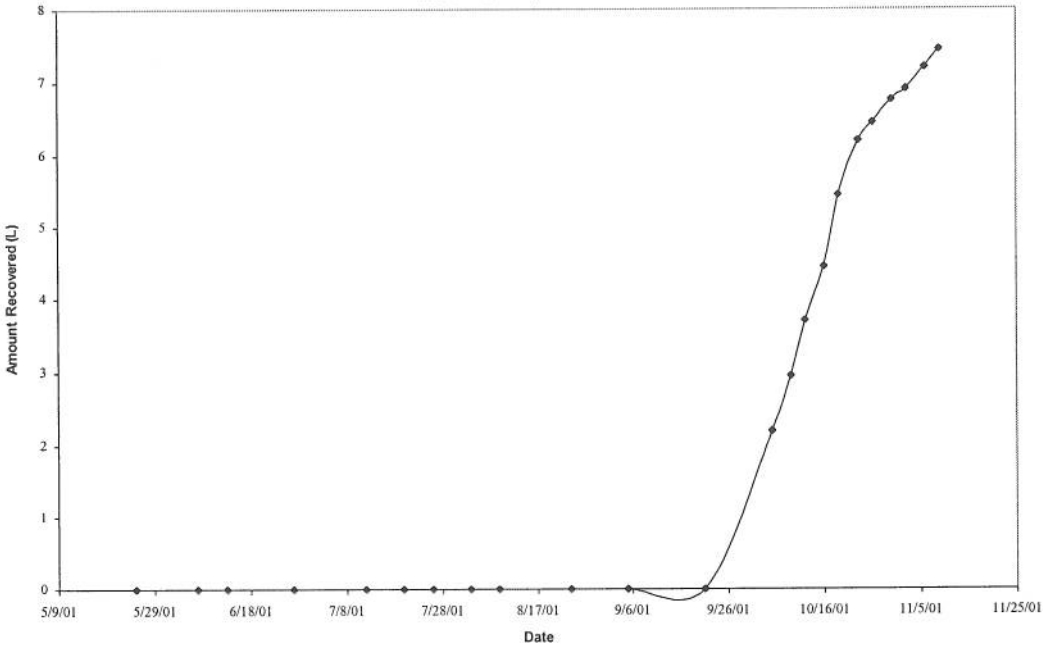

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S

URS
11/12/01

*Privileged & Confidential*

CUMULATIVE PRODUCT RECOVERY
RH-1S

NYSEG
MECHANICVILLE, NEW YORK



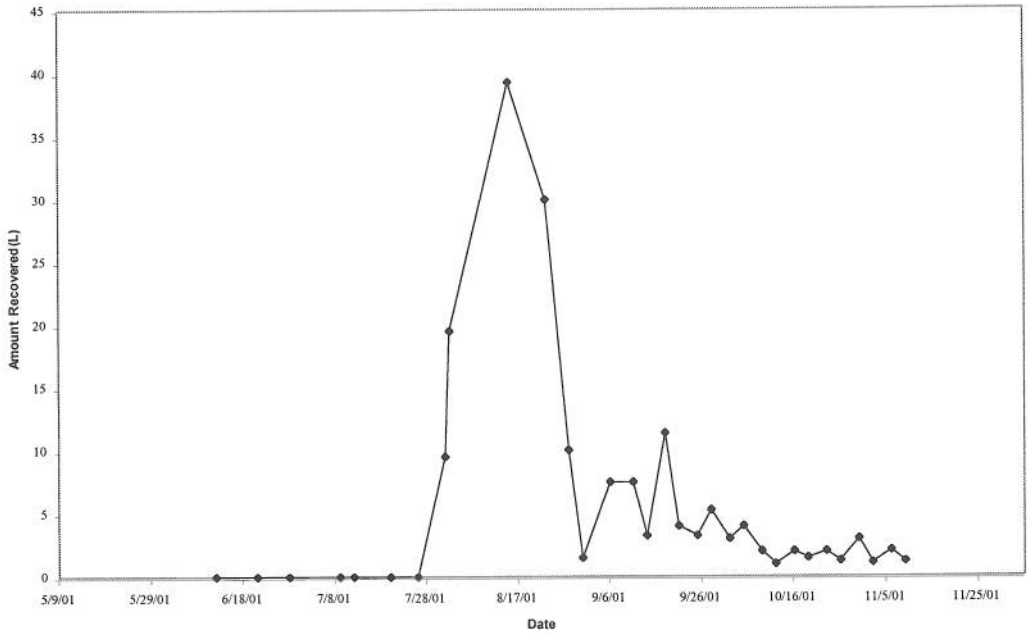

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S Cumulative

URS
11/12/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



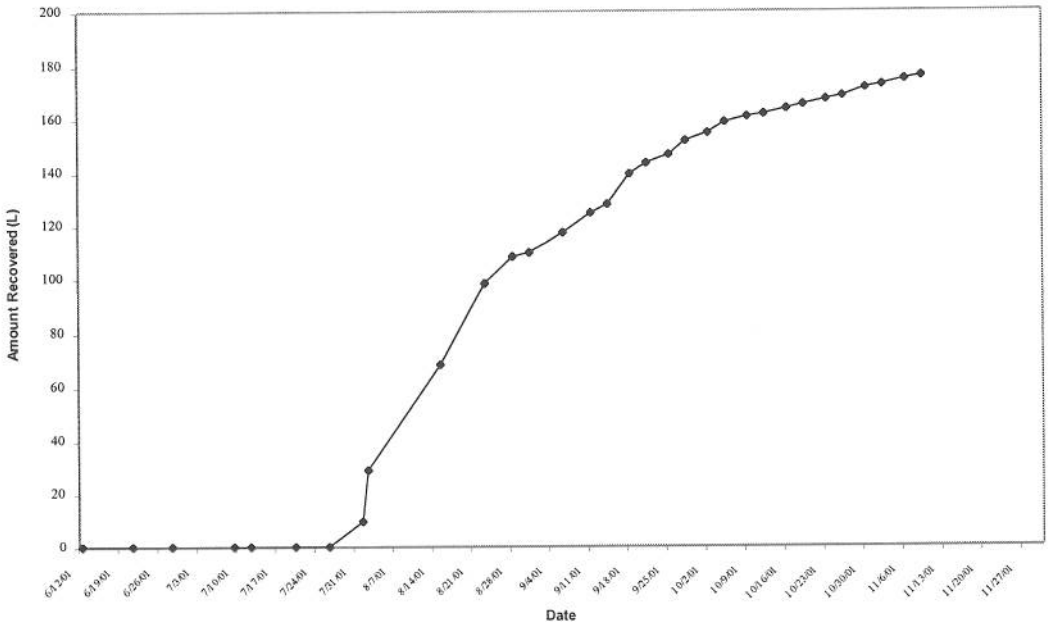

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D

URS
11/12/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

NYSEG
MECHANICVILLE, NEW YORK

*Privileged & Confidential*




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D Cumulative

URS
11/12/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: October 30, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of October 22, 2001

On October 22, 2001, URS developed monitoring well MW-35I using a centrifugal pump. A significant amount of NAPL was observed on the development water as well as MGP odors and sheens.

On October 22, 2001, a URS geologist logged the bedrock core from well MW-35I.

On October 25, 2001, URS collected three water samples from three onsite poly tanks. These three water samples were submitted to the laboratory for total benzene analysis (2-day TAT).

### *Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On October 23 and 26, 2001, URS bailed well MW-10D and recovered a total of 3.25 liters of NAPL. URS recovered approximately 0.1 liters of NAPL from well MW-26S using a peristaltic pump on October 26, 2001. On October 23 and October 26, 2001, URS also recovered approximately 1.0 liters of NAPL from well RH-1S using a peristaltic pump.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

### *Out of Scope Activities and Costs*

See attached Table 2.

**Tasks to be Completed During the Week of October 29, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will be prepared to provide oversight to NYSEG's waste removal contractors.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL | | |

**Tasks to be Completed During the Week of October 29, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will be prepared to provide oversight to NYSEG's waste removal contractors.

| | | | | | |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| | | | Not present | | |
| | | | | NA | NA |
| | | | | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.1 L of NAPL recovered | NA | NA |
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/25/01 | None | None | NAPL Not Present | NA | NA |
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| 10/26/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| *MW-35I (12.5 to 34.5 feet) Open Hole* | | | | | |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 10/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.25 L of NAPL recovered | NA | NA |
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 10/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/26/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1 *Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

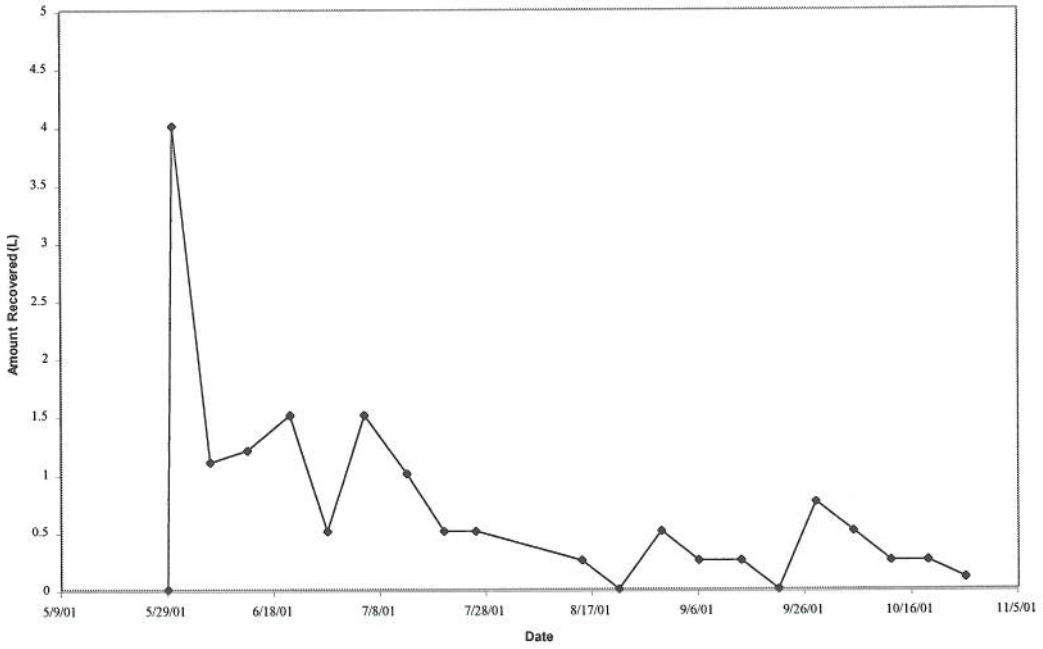
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



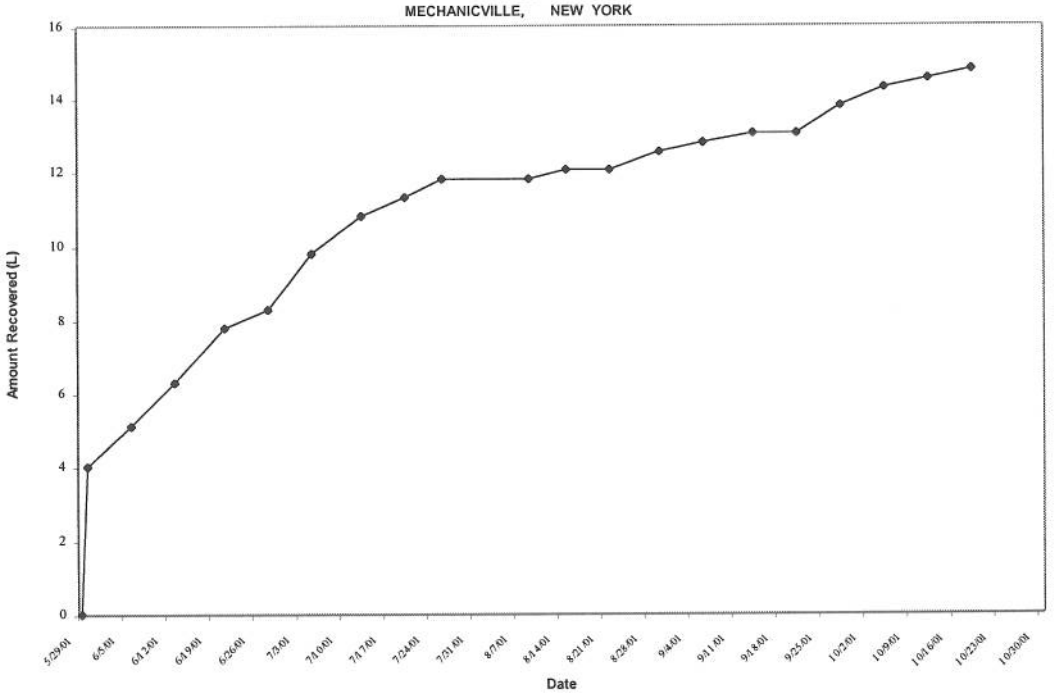

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S

URS
10/31/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



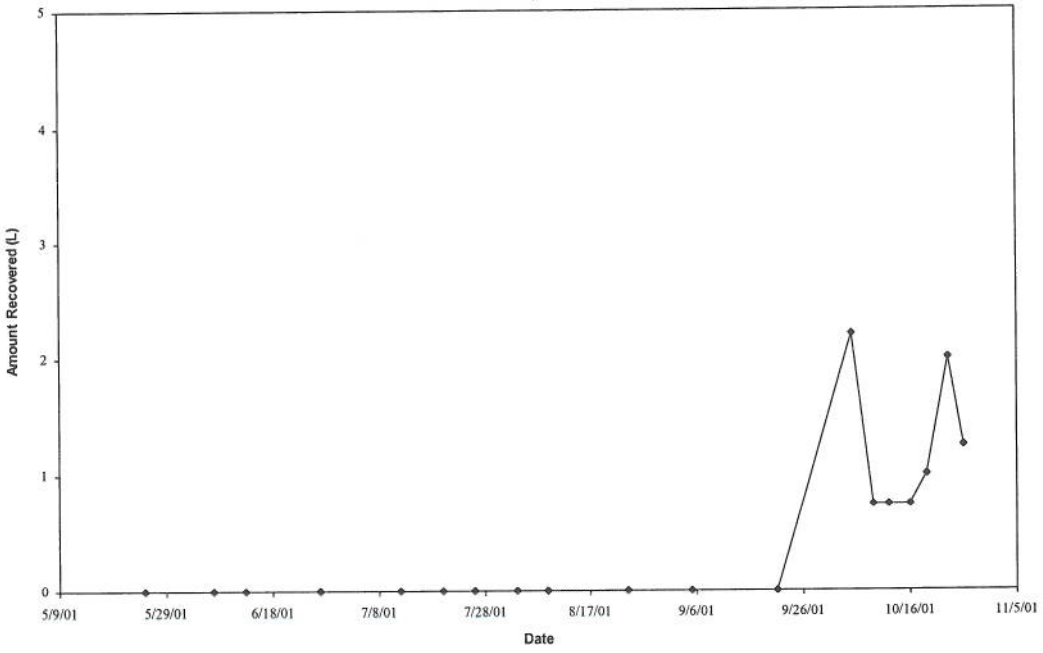

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-26S CUMULATIVE

URS
10/31/01

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



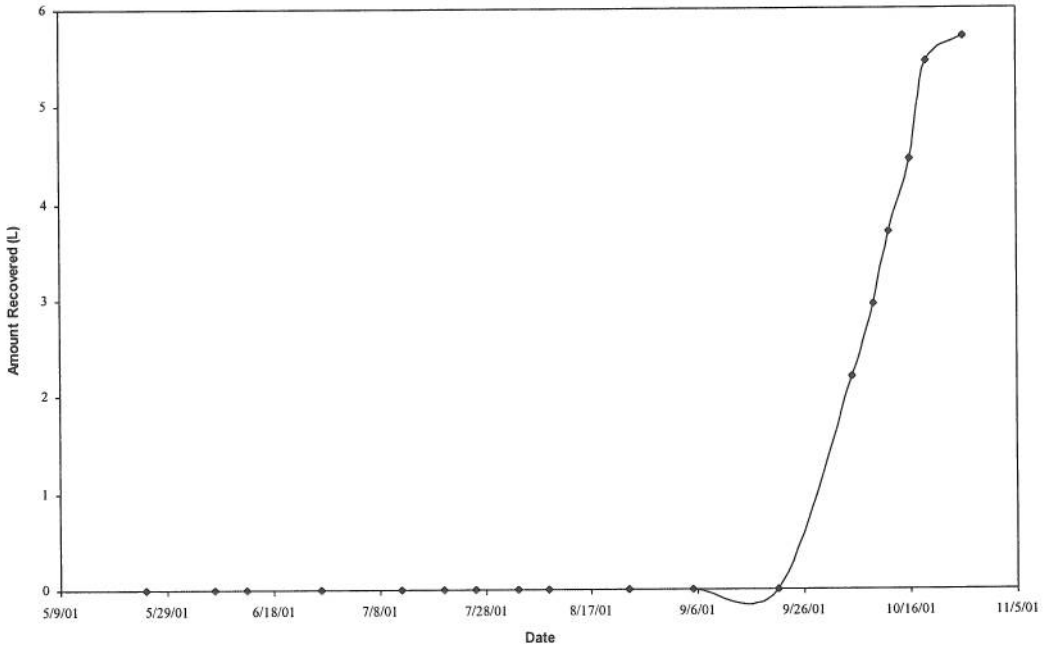

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S recovery

URS
10/31/01

CUMULATIVE PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



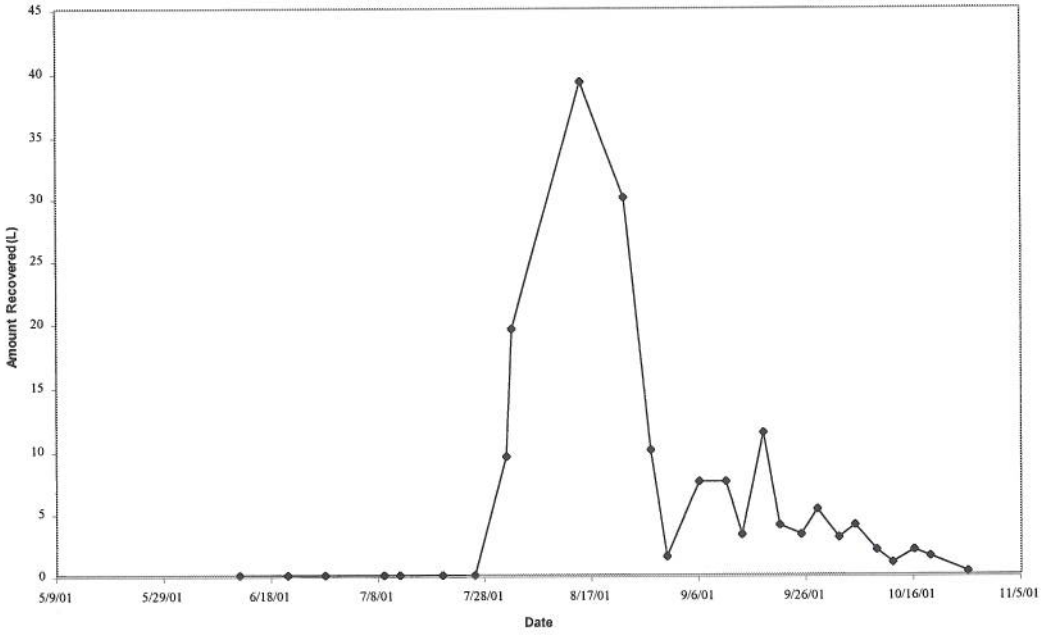

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/RH-1S cumulative

URS
10/31/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



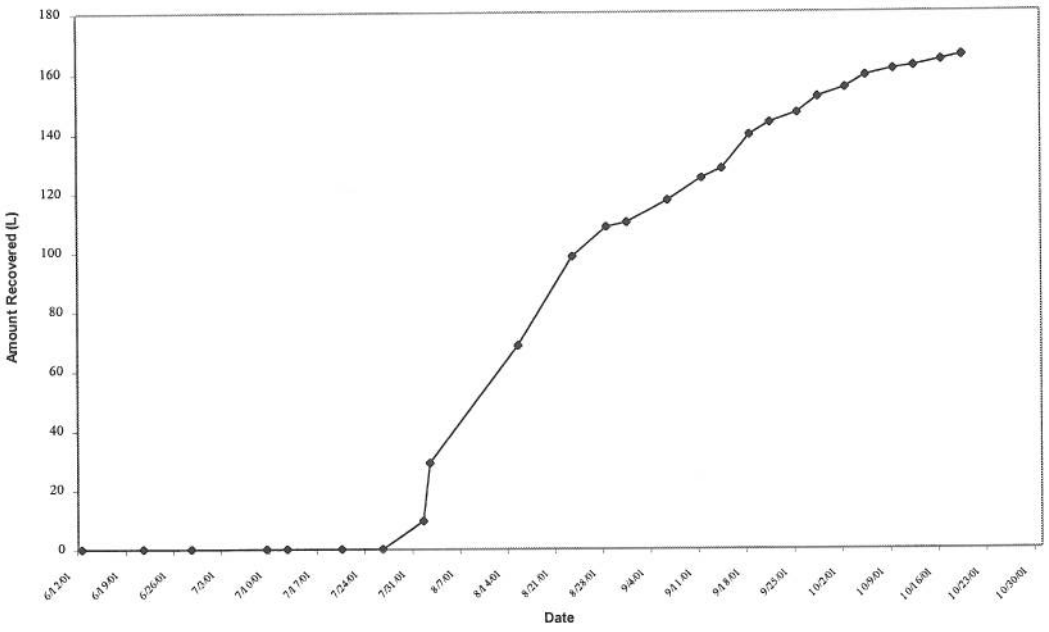

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D

URS
10/31/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

NYSEG
MECHANICVILLE, NEW YORK

*Privileged & Confidential*




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs.xls/MW-10D CUMULATIVE

URS
10/31/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: October 23, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of October 15, 2001

On October 15, 2001, URS purged and sampled well MW-14S. Currently, no additional wells are planned for sampling. To date, URS has purged and sampled the following 21 monitoring wells:

| | | | | | |
|---|---|---|---|---|---|
| MW-1 | MW-11 | MW-16 | MW-19I | MW-28I | MW-34D |
| MW-2 | MW-14S | MW-17 | MW-21S | MW-29D | |
| MW-2I | MW-14D | MW-17I | MW-21D | MW-31S | |
| MW-10I | MW-15D | MW-18 | MW-23D | MW-32D | |

The groundwater analytical data is being evaluated as it is received from the laboratory.

At the NYSDEC's request, on October 17, 2001, URS forward copies of the draft soil boring and well construction logs for wells MW-20D, MW-34D, and MW-35I and a monitoring well location map to the NYSDEC. Jeff Edwards of the NYSDEC was preparing a letter to the Bulls who own the property, where wells MW-20D and MW-35I are located, directly north of the site.

On October 18, 2001, ADT returned to the site to make some final adjustments to the some of the wells and move the drums from the Bull property to the site.

### *Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On October 16 and 19, 2001, URS bailed well MW-10D and recovered a total of 3.5 liters of NAPL. URS recovered approximately 0.25 liters of NAPL from well MW-26S using a peristaltic pump on October 19, 2001. On October 16 and October 19, 2001, URS also recovered approximately 1.75 liters of NAPL from well RH-1S using a peristaltic pump.



TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| 10/15/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

Privileged & Confidential

TABLE 1

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | None | 0.25 L of NAPL recovered | NA | NA |
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 10/16/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/19/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

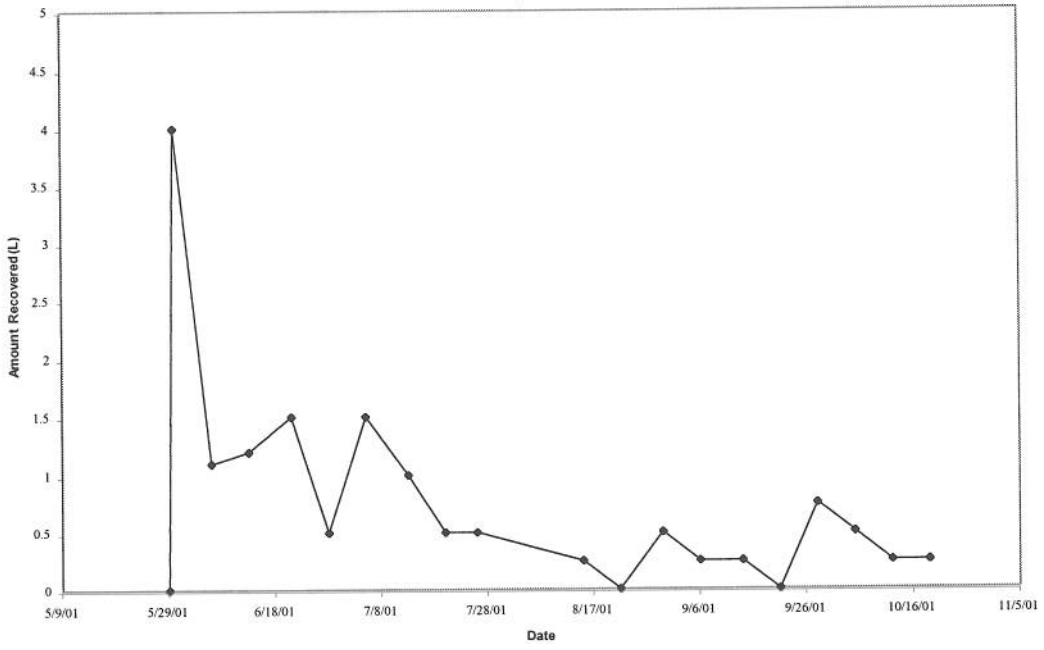
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/18/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



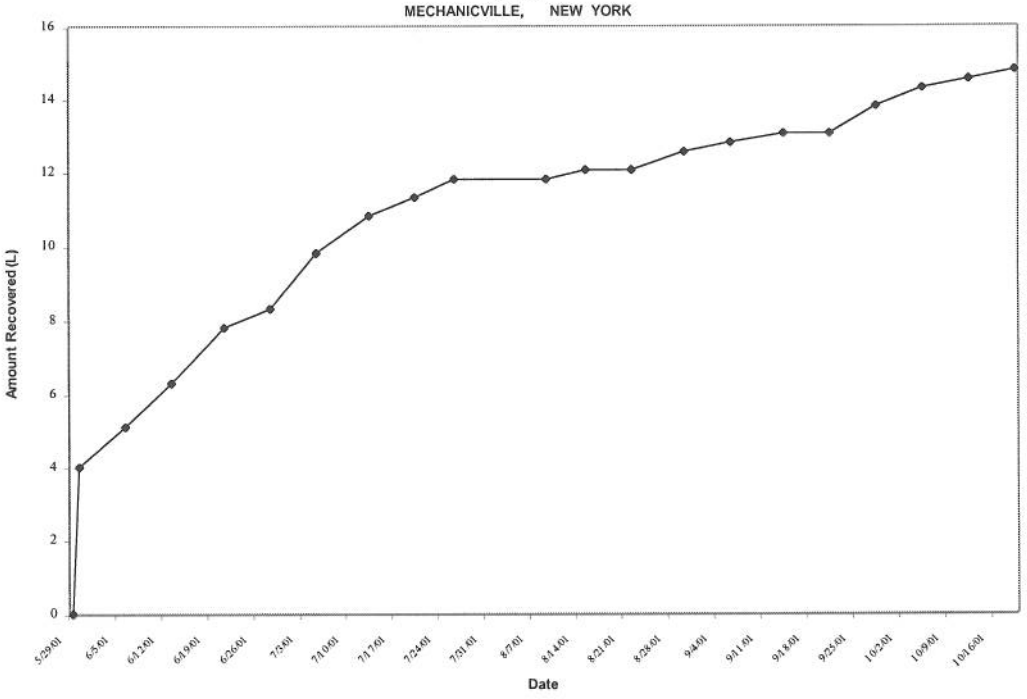

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
10/23/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



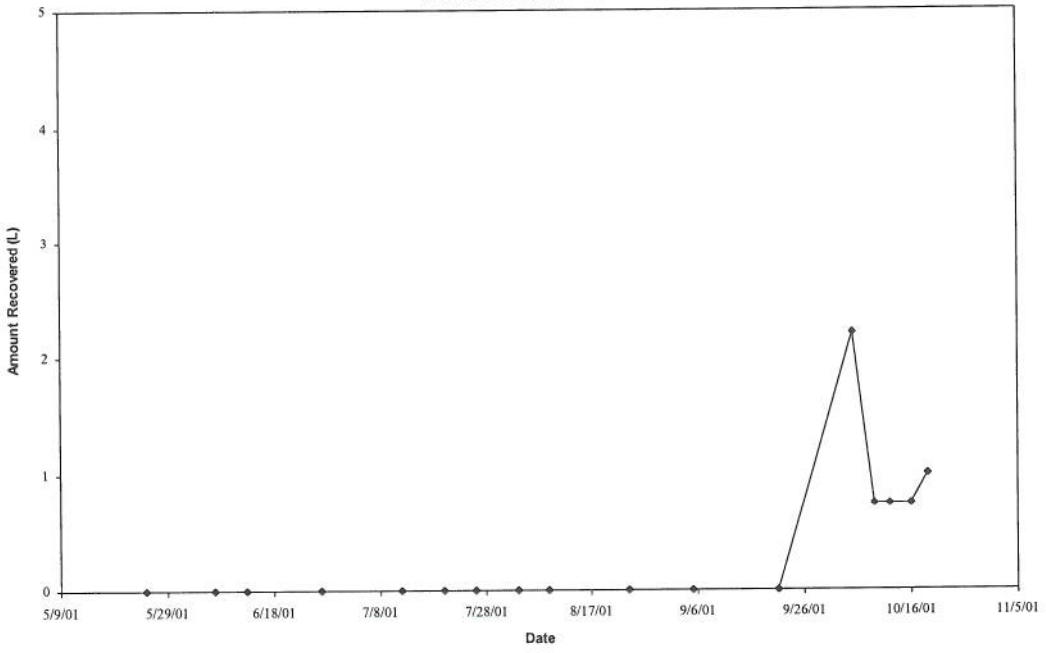

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S CUMULATIVE

URS
10/23/01

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



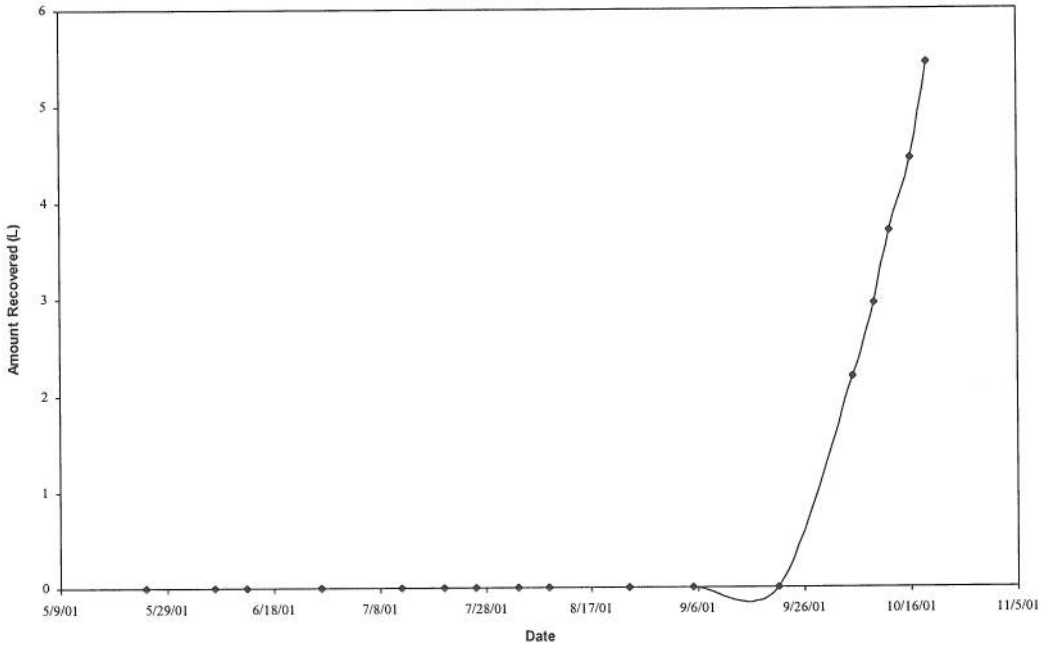

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/RH-1S recovery

URS
10/23/01

CUMULATIVE PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



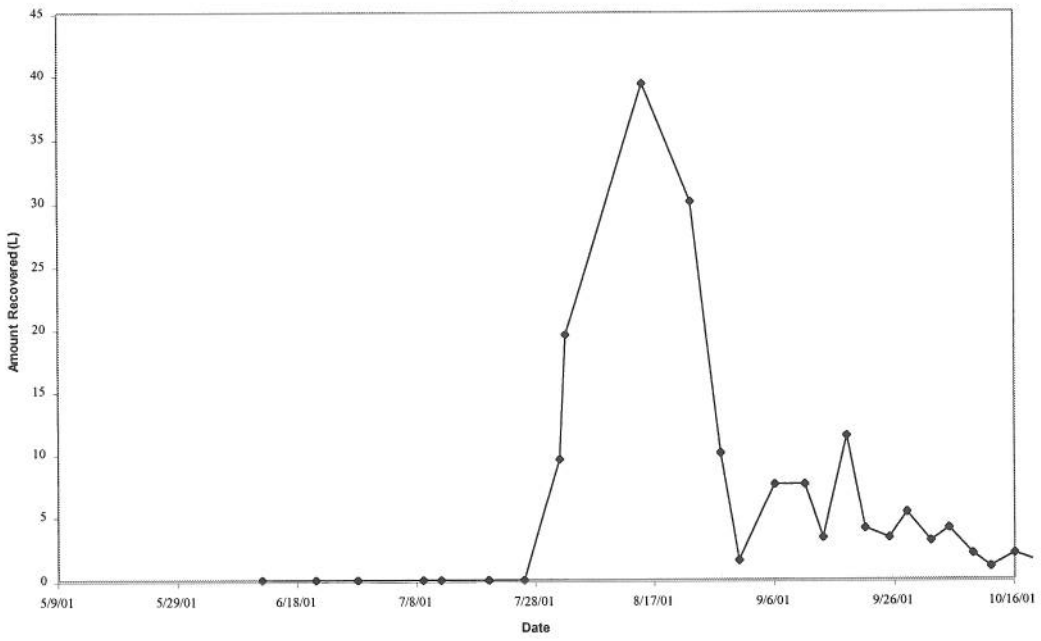

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/RH-1S cumulative

URS
10/23/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



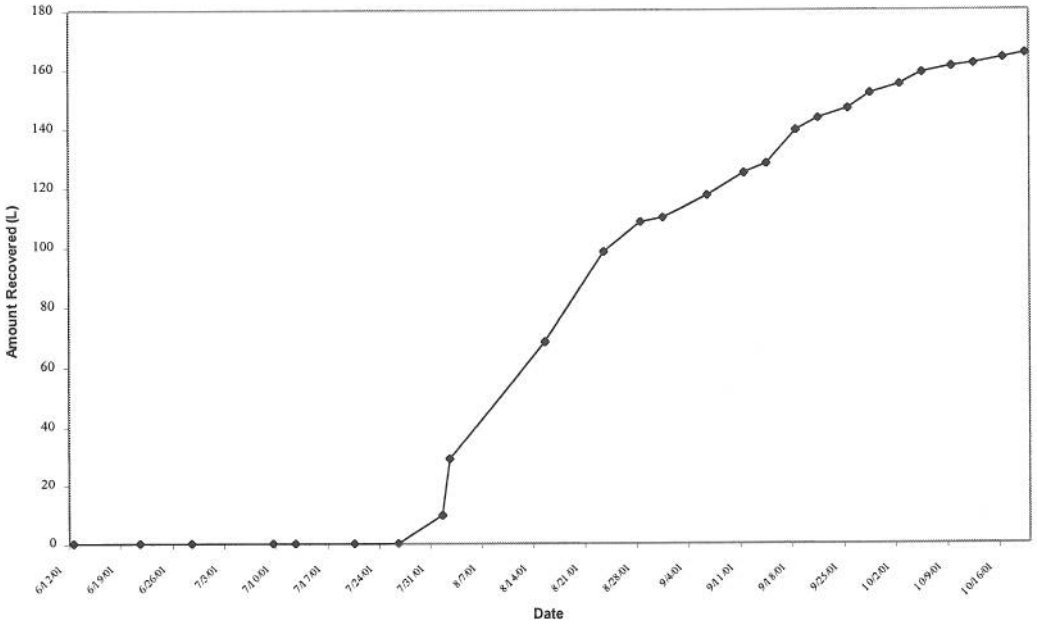

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
10/23/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
10/23/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: October 16, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of October 8, 2001

On October 8, 2001, ADT remobed to the site to set up the decon pad and to initiate drilling at well MW-35D at the Bull property. During drilling of the overburden materials using 10 ¼-inch HSAs there were no signs of odors or staining. The overburden materials at this location were not continuously sampled and no soil samples were collected for laboratory analyses. Bedrock was encountered at approximately 10.5 bgs at well MW-35D. A two-foot rock socket was drilled into the rock to set the 8-inch overburden casing. During drilling of the rock socket, there were very strong MGP odors.

On October 11, 2001, ADT started coring the bedrock at well MW-35D. The bedrock at well MW-35D was cored from approximately 13.3 to 34.3 feet bgs. There were sheens and a small amount of NAPL observed in the return water and on the core between 13.3 and 17.3 feet bgs. During the next core run between 17.3 and 24.3 feet bgs, the bedrock was coated with NAPL and some sheens were observed in the Anthony Kill. The NAPL appeared to be from a fracture at approximately 19 feet bgs. The bedrock core from 13.3 to 24.3 feet bgs exhibited intense pencil cleavage. Prior to coring from 24.3 to 34.3 feet bgs (Run 3), a significantamount of NAPL had accumulated in the core hole. Run 3was almost a solid 10-foot long section of core and the intensity of the pencil cleavage sharply lessened between 27 to 28 feet bgs.

Due to the presence of NAPL in the bedrock at well MW-35D, URS and NYSEG decided to convert this well to a NAPL recovery location and not continue drilling to 150 feet bgs as planned. Ray Crawford of the NYSDEC who was onsite during drilling of well MW-35D and Jeffrey Edwards of the NYSDEC also agreed to this change in scope. On October 12, 2001, the bedrock core hole at well MW-35D was reamed using a 7 7/8-inch roller bit to 34.5 feet bgs. Please note that well MW-35D will be renamed as MW-35I.

Between October 9 and October 10, 2001, URS purged and sampled monitoring well MW-20D.

As of October 10, 2001, there were 175 drums of investigation derived waste at the site. At NYSDEC's request on October 12, 2001, URS collected one composite sample of the materials in the drums and for TCLP VOC, TCLP SVOC, total PCBs, and pH analyses (see out of scope activities).

***Summary of NAPL Observations***

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). Please note that on October 5, 2001, URS recovered 2.2 liters of DNAPL from well RH-1S using a peristaltic pump. This data was inadvertently not provided in the previous weekly report.

On October 10, 2001, URS bailed approximately four gallons of water from wells MW-30S, MW-12S, and MW-14S to evaluate whether there was recoverable amounts of NAPL in these wells and whether these wells should be purged and sampled. The water from wells MW-12S and MW-30S did exhibit odors and sheens, but did not indicate the presence of recoverable NAPL. The water from well MW-14S did not exhibit any sheens, odors, or signs of NAPL. Well MW-14S will be purged and sampled next week. In addition, on October 10, 2001, URS collected a synoptic round of water levels.

On October 9 and October 12, 2001, URS bailed well MW-10D and recovered a total of 3 liters of NAPL. URS recovered approximately 0.25 liters of NAPL from well MW-26S using a peristaltic pump on October 12, 2001. On October 9 and October 12, 2001, URS also recovered approximately 1.50 liters of NAPL from well RH-1S using a peristaltic pump.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S, RH-1S, and MW-10D area also attached.

***Out of Scope Activities and Costs***

See attached Table 2.

**Tasks to be Completed During the Week of October 15, 2001.**

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will purge and sample well MW-14S. URS will also review and evaluate the groundwater analytical data as it arrives from the lab.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | |
| *MW-10 (8.7 to 19.5 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| *MW-12 (14.5 to 25.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| *MW-12S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14S (10 to 25 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-16 (6 to 16 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-17 (13 to 23 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-21S (5 to 10 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/11/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-23S (7.5 to 12.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-25S (11 to 26 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| *MW-26S (7.5 to 22.5 feet) Screen* | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.02 | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-30S (10 to 25 feet) Screen* | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 10/10/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| *MW-31S (8 to 18 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1S (1.8 to 17.3 feet) Screen* | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2.2 L of NAPL recovered | NA | 1.65 |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | |
| *MW-1 (11.6 to 16.85 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-2 (11.2 to 14.35 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-2I (11.28 to 32.2 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-10I (22 to 43 feet) Open Hole* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-11 (9.5 to 15 feet) Screen* | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-13 (44.7 to 55.5 feet) Screen* | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14 (30 to 41 feet) Screen* | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| *MW-15I (12.5 to 22.5 feet) Screen* | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| *MW-17I (23 to 45 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-18 (28 to 38 feet) Screen* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-19I (18 to 38.5 feet) Open Hole* | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-22I (17 to 32 feet) Screen* | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| *MW-25I (27 to 47 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| *MW-26I (24.5 to 45.5 feet) Open Hole* | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-28I (15 to 25 feet) Screen* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29I (11.5 to 26 feet) Open Hole* | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **Deep Bedrock Monitoring Wells** | | | | | |
| *MW-10D (82 to 114 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 10/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | 2 L of NAPL recovered | NA | NA |
| 10/10/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-14D (91 to 121.7 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-15D (96 to 105.8 feet) Open Hole* | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-17D (121 to 142.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-20D (90 to 110.1 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-21D (48.7 to 59.4 feet) Open Hole* | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-23D (56 to 80 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-29D (90 to 110 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/20/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-30D (90 to 121 feet) Open Hole* | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |

Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-31D (28 to 150 feet) Open Hole* | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *MW-32D (91 to 111.5 feet) Open Hole* | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe.

TABLE 1

*Privileged & Confidential*

SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *MW-33D (119.7 to 140.5 feet) Open Hole* | | | | | |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| *MW-34D (100 to 120.5 feet) Open Hole* | | | | | |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| 10/11/01 | None | None | NAPL Not Present | NA | NA |
| *RH-1D (86.5 to 107.5 feet) Open Hole* | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

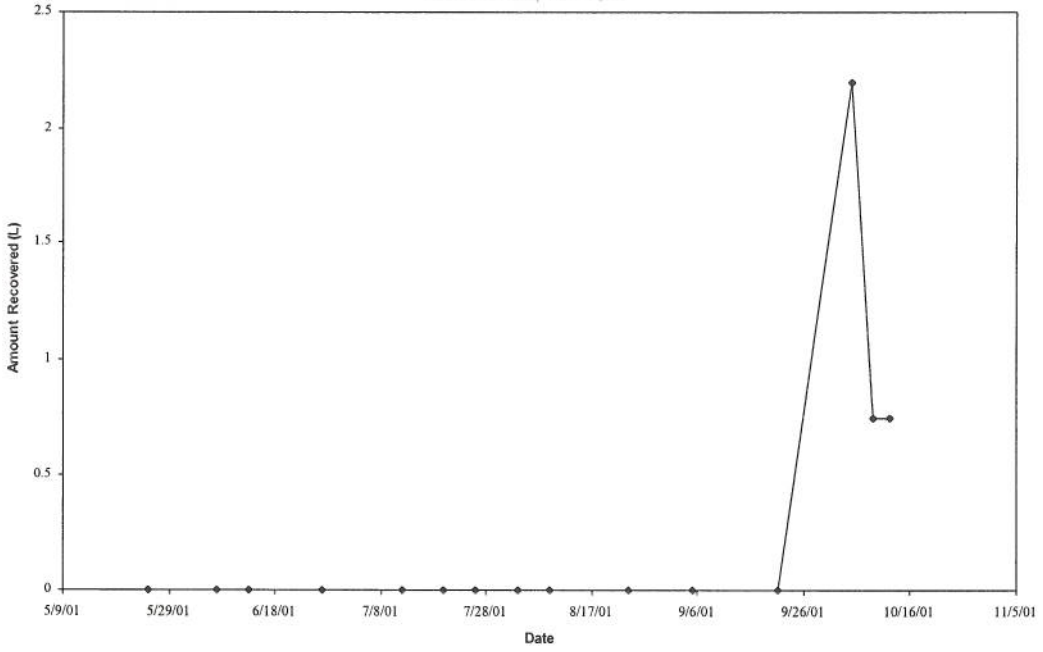
Notes:

1. NA indicates not applicable.
2. IP indicates Interface Probe.

SUMMARY OF PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



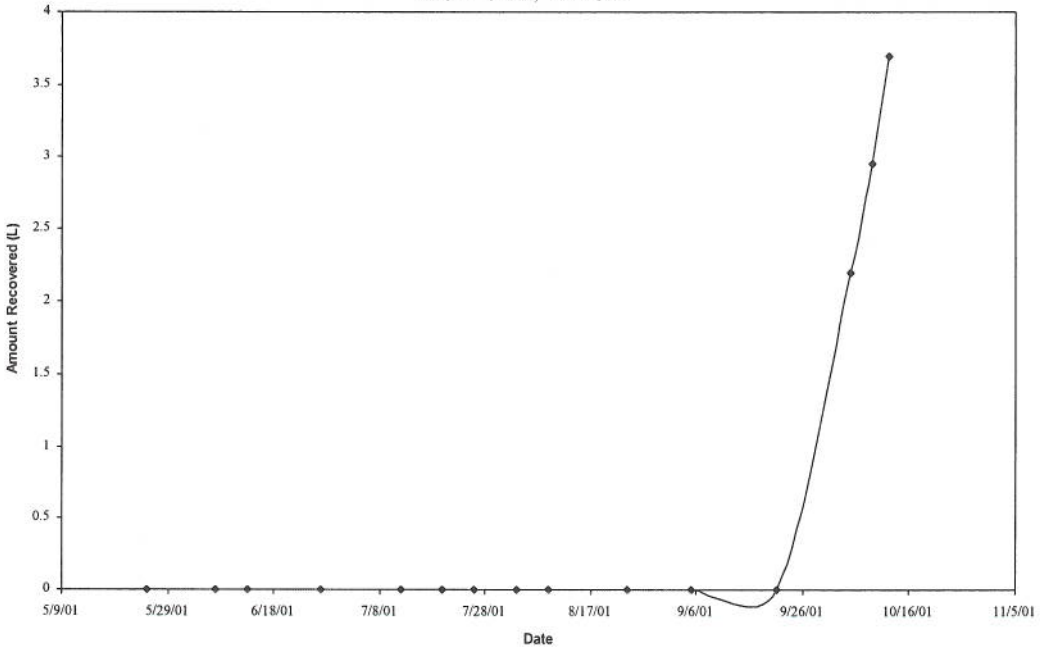

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/RH-1S recovery

URS
10/16/01

CUMULATIVE PRODUCT RECOVERY
RH-1S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



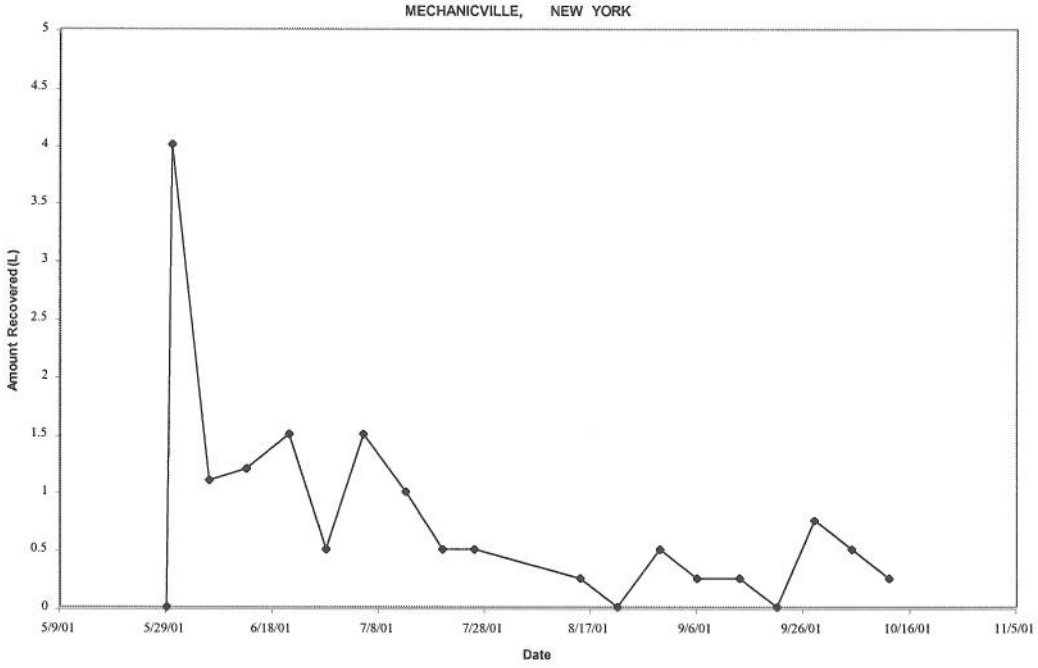

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/RH-1S cumulative

URS
10/16/01

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



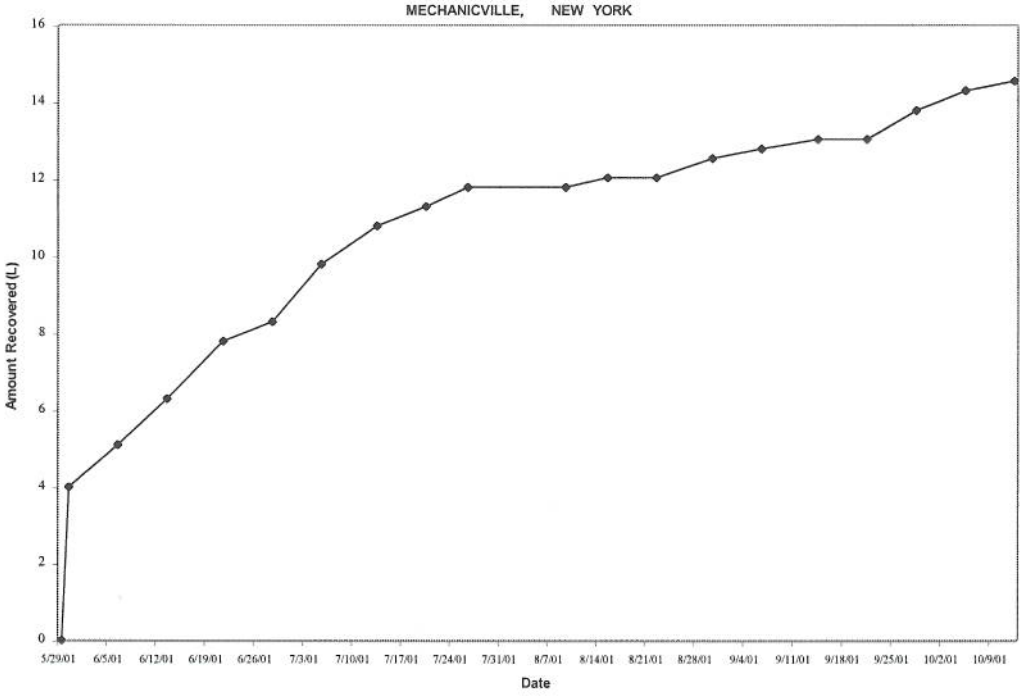

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
10/16/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



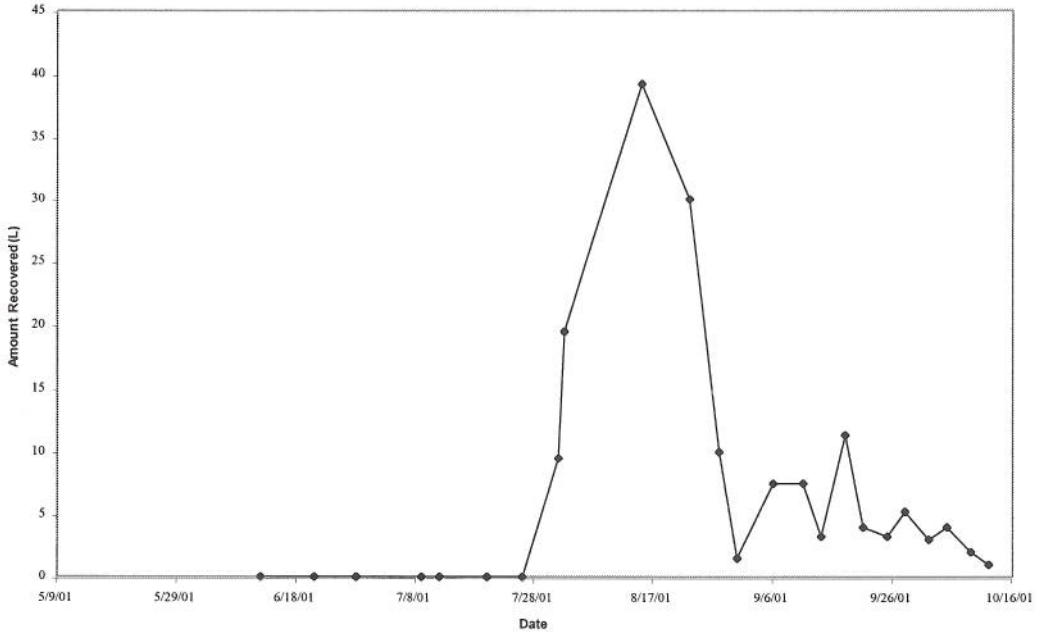

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S CUMULATIVE

URS
10/16/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



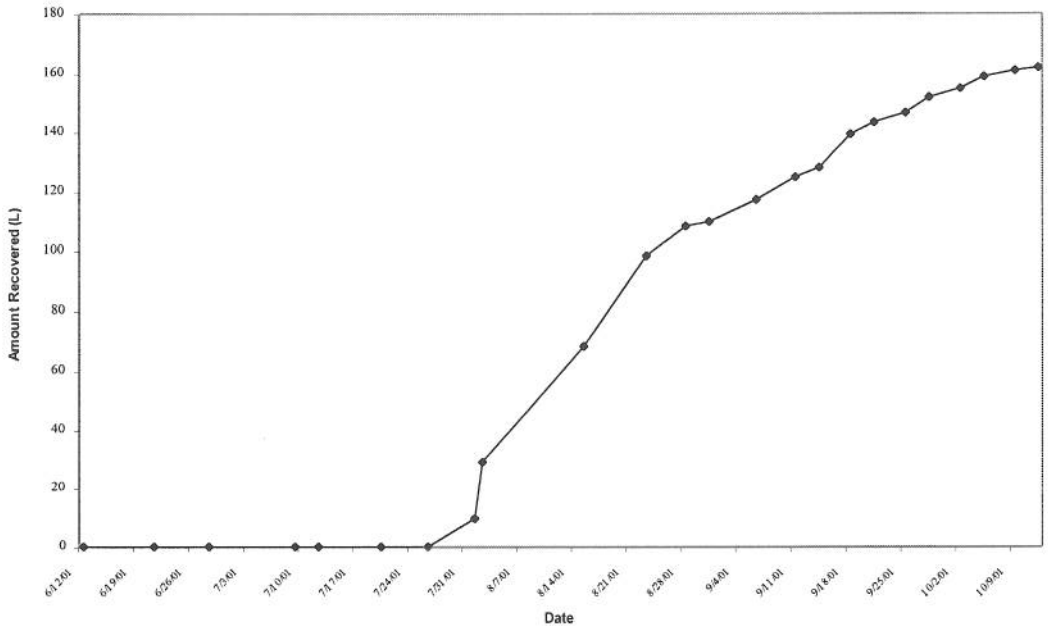

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
10/16/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
10/16/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: October 9, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

**Tasks Completed During the Week of October 1, 2001**

Between October 1 and October 5, 2001, URS purged and sampled monitoring wells MW-16, MW-28I, MW-15D, MW-17D, and MW-34D. On October 4, 2001, URS bailed well RH-1D dry. Well RH-1D had approximately 2-feet of standing water in the well. URS will continue to bail this well dry until at least three well volumes are removed prior sampling this well.

On October 1, 2001, URS and NYSDEC discussed the drilling and installation methodologies for planned well MW-35D at the Bull property. Per the NYSDEC's request, well MW-35D will be drilled to a total depth of 150 feet bgs. URS understands that the NYSDEC does not require the collection of bedrock core from well MW-35D. URS plans to core at least the upper 50 feet of bedrock during drilling of MW-35D and complete the well with an open hole interval from 120 to 150 feet bgs.

On October 2, 2001, URS confirmed that the cars had been moved from the area of the MW-35D. URS and ADT will initiate drilling at the Bull property on Monday October 8, 2001.

***Summary of NAPL Observations***

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On October 2 and 5, 2001, URS bailed well MW-10D and recovered a total of 7 liters of NAPL from well MW-10D. URS recovered approximately 0.5 liters of NAPL from well MW-26S using a peristaltic pump on October 5, 2001.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S and MW-10D area also attached.

*Out of Scope Activities and Costs*

See attached Table 2.

**Tasks to be Completed During the Week of October 8, 2001.**

ADT will install the overburden casing at well MW-35D on the Bull property.

URS will provide oversight during drilling of well MW-35D.

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will continue groundwater sampling of the clean (NAPL-free) wells at the site.

URS will continue to assemble and evaluate the analytical and bedrock core data.

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *Overburden Monitoring Wells* | | | | | |
| **MW-10 (8.7 to 19.5 feet) Screen** | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| **MW-12 (14.5 to 25.5 feet) Screen** | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.45 |
| 8/15/01 | None | None | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| **MW-12S (11 to 26 feet) Screen** | | | | | |
| 5/29/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| **MW-14S (10 to 25 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-15S (5 to 10 feet) Screen** | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/13/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| **MW-16 (6 to 16 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-17 (13 to 23 feet) Screen** | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-21S (5 to 10 feet) Screen** | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |
| **MW-23S (7.5 to 12.5 feet) Screen** | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 5/29/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/19/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/20/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| **MW-25S (11 to 26 feet) Screen** | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen | Trace NAPL Recovered on Chain | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-26S (7.5 to 22.5 feet) Screen** | | | | | |
| 5/29/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 5/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 6/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 L of NAPL recovered | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 L of NAPL recovered | NA | NA |
| 6/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 6/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 7/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1 L of NAPL recovered | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | 0.98 | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 8/22/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 8/30/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | None | 0.5 L of NAPL recovered | 0.03 | NA |
| **MW-30S (10 to 25 feet) Screen** | | | | | |
| 8/24/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | Odor | Odor | NAPL Not Present | NA | NA |
| **MW-31S (8 to 18 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **RH-1S (1.8 to 17.3 feet) Screen** | | | | | |
| 5/25/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | 1.65 |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *Shallow Bedrock Monitoring Wells* | | | | | |
| **MW-1 (11.6 to 16.85 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-2 (11.2 to 14.35 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-2I (11.28 to 32.2 feet) Open Hole** | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/17/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

**TABLE 1** *Privileged & Confidential*

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-10I (22 to 43 feet) Open Hole** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-11 (9.5 to 15 feet) Screen** | | | | | |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-13 (44.7 to 55.5 feet) Screen** | | | | | |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| **MW-14 (30 to 41 feet) Screen** | | | | | |
| 6/28/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | Odor | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-15I (12.5 to 22.5 feet) Screen** | | | | | |
| 5/25/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/27/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/24/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| **MW-18 (28 to 38 feet) Screen** | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-19I (18 to 38.5 feet) Open Hole** | | | | | |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/18/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-22I (17 to 32 feet) Screen** | | | | | |
| 5/25/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 6/7/01 | Odor | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | Odor | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/6/01 | None | Odor | NAPL Not Present | NA | NA |
| 7/12/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 8/3/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor | Odor | NAPL Not Present | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | 0.01 | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |
| **MW-25I (27 to 47 feet) Open Hole** | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/17/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| **MW-26I (24.5 to 45.5 feet) Open Hole** | | | | | |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | Odor, Sheen | Odor, Sheen | NAPL Not Present | NA | NA |
| 8/3/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/9/01 | None | Odor | NAPL Not Present | NA | NA |
| 8/24/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 10/5/01 | None | None | NAPL Not Present | NA | NA |
| **MW-28I (15 to 25 feet) Screen** | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/7/01 | None | None | NAPL Not Present | NA | NA |
| 6/13/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/3/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-29I (11.5 to 26 feet) Open Hole** | | | | | |
| 5/25/01 | Odor, Sheen | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/7/01 | None | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 6/13/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 9/5/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on IP | NA | NA |
| 10/5/01 | Odor | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| *Deep Bedrock Monitoring Wells* | | | | | |
| **MW-10D (82 to 114 feet) Open Hole** | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | Odor, Sheen | NAPL Not Present | NA | NA |
| 7/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/12/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 7/26/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/1/01 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 L of NAPL recovered | NA | NA |
| 8/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 L of NAPL recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/15/01 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 L of NAPL recovered | NA | NA |
| 8/23/01 | Odor, Sheen, Product | Odor, Sheen, Product | 30 L of NAPL recovered | 0.05 | 6.7 |
| 8/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 10 L of NAPL recovered | NA | NA |
| 8/31/01 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 L of NAPL recovered | NA | NA |
| 9/6/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/11/01 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 L of NAPL recovered | NA | NA |
| 9/14/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/18/01 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 L of NAPL recovered | NA | NA |
| 9/21/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| 9/25/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 L of NAPL recovered | NA | NA |
| 9/28/01 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 L of NAPL recovered | NA | NA |
| 10/2/01 | Odor, Sheen, Product | Odor, Sheen, Product | 3 L of NAPL recovered | NA | NA |
| 10/5/01 | Odor, Sheen, Product | Odor, Sheen, Product | 4 L of NAPL recovered | NA | NA |
| **MW-14D (91 to 121.7 feet) Open Hole** | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-15D (96 to 105.8 feet) Open Hole** | | | | | |
| 6/11/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-21D (48.7 to 59.4 feet) Open Hole** | | | | | |
| 5/25/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/5/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-23D (56 to 80 feet) Open Hole** | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **MW-30D (90 to 121 feet) Open Hole** | | | | | |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/13/01 | None | None | NAPL Not Present | NA | NA |
| 7/20/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 8/3/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/9/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on IP | NA | NA |
| 8/17/01 | Odor, Sheen, Product | Odor, Sheen, Product | NAPL Recovery Attempted; Trace NAPL Recovered | NA | NA |
| 8/24/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| 9/21/01 | Odor, Sheen, Product | None | Trace NAPL Recovered on Chain | NA | NA |
| 10/4/01 | Odor, Sheen, Product | Odor, Sheen, Product | Trace NAPL Recovered on Chain | NA | NA |
| **MW-31D (28 to 150 feet) Open Hole** | | | | | |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/12/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/8/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/5/01 | None | None | NAPL Not Present | NA | NA |
| 9/12/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

## SUMMARY OF NAPL OBSERVATIONS

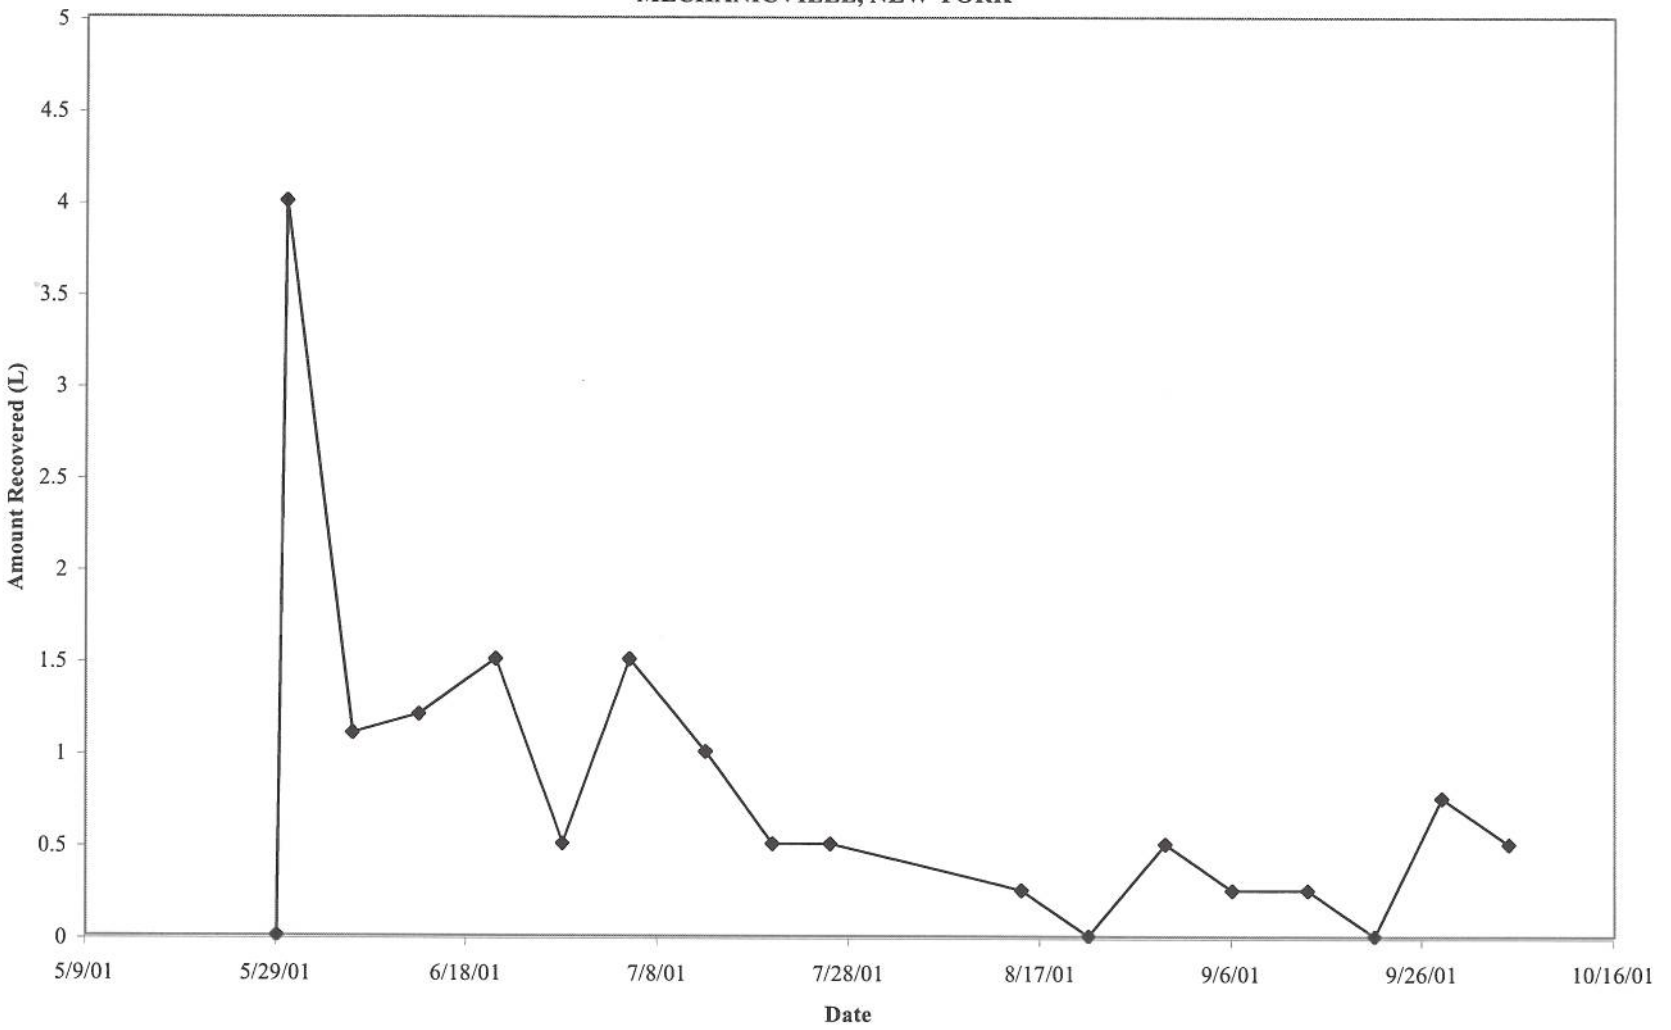
| DATE | LNAPL Observations | DNAPL Observations | NAPL Recovery Comments | LNAPL Thickness (feet) | DNAPL Thickness (feet) |
|---|---|---|---|---|---|
| **MW-32D (91 to 111.5 feet) Open Hole** | | | | | |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/19/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |
| **RH-1D (86.5 to 107.5 feet) Open Hole** | | | | | |
| 6/5/01 | None | None | NAPL Not Present | NA | NA |
| 6/12/01 | None | None | NAPL Not Present | NA | NA |
| 6/21/01 | None | None | NAPL Not Present | NA | NA |
| 6/27/01 | None | None | NAPL Not Present | NA | NA |
| 6/28/01 | None | None | NAPL Not Present | NA | NA |
| 7/6/01 | None | None | NAPL Not Present | NA | NA |
| 7/11/01 | None | None | NAPL Not Present | NA | NA |
| 7/19/01 | None | None | NAPL Not Present | NA | NA |
| 7/26/01 | None | None | NAPL Not Present | NA | NA |
| 8/3/01 | None | None | NAPL Not Present | NA | NA |
| 8/9/01 | None | None | NAPL Not Present | NA | NA |
| 8/15/01 | None | None | NAPL Not Present | NA | NA |
| 8/23/01 | None | None | NAPL Not Present | NA | NA |
| 8/29/01 | None | None | NAPL Not Present | NA | NA |
| 9/7/01 | None | None | NAPL Not Present | NA | NA |
| 9/14/01 | None | None | NAPL Not Present | NA | NA |
| 9/21/01 | None | None | NAPL Not Present | NA | NA |
| 9/28/01 | None | None | NAPL Not Present | NA | NA |
| 10/4/01 | None | None | NAPL Not Present | NA | NA |

Notes:
1. NA indicates not applicable.
2. IP indicates Interface Probe

**SUMMARY OF PRODUCT RECOVERY**
**MW-26S**

*Privileged & Confidential*

**NYSEG**
**MECHANICVILLE, NEW YORK**



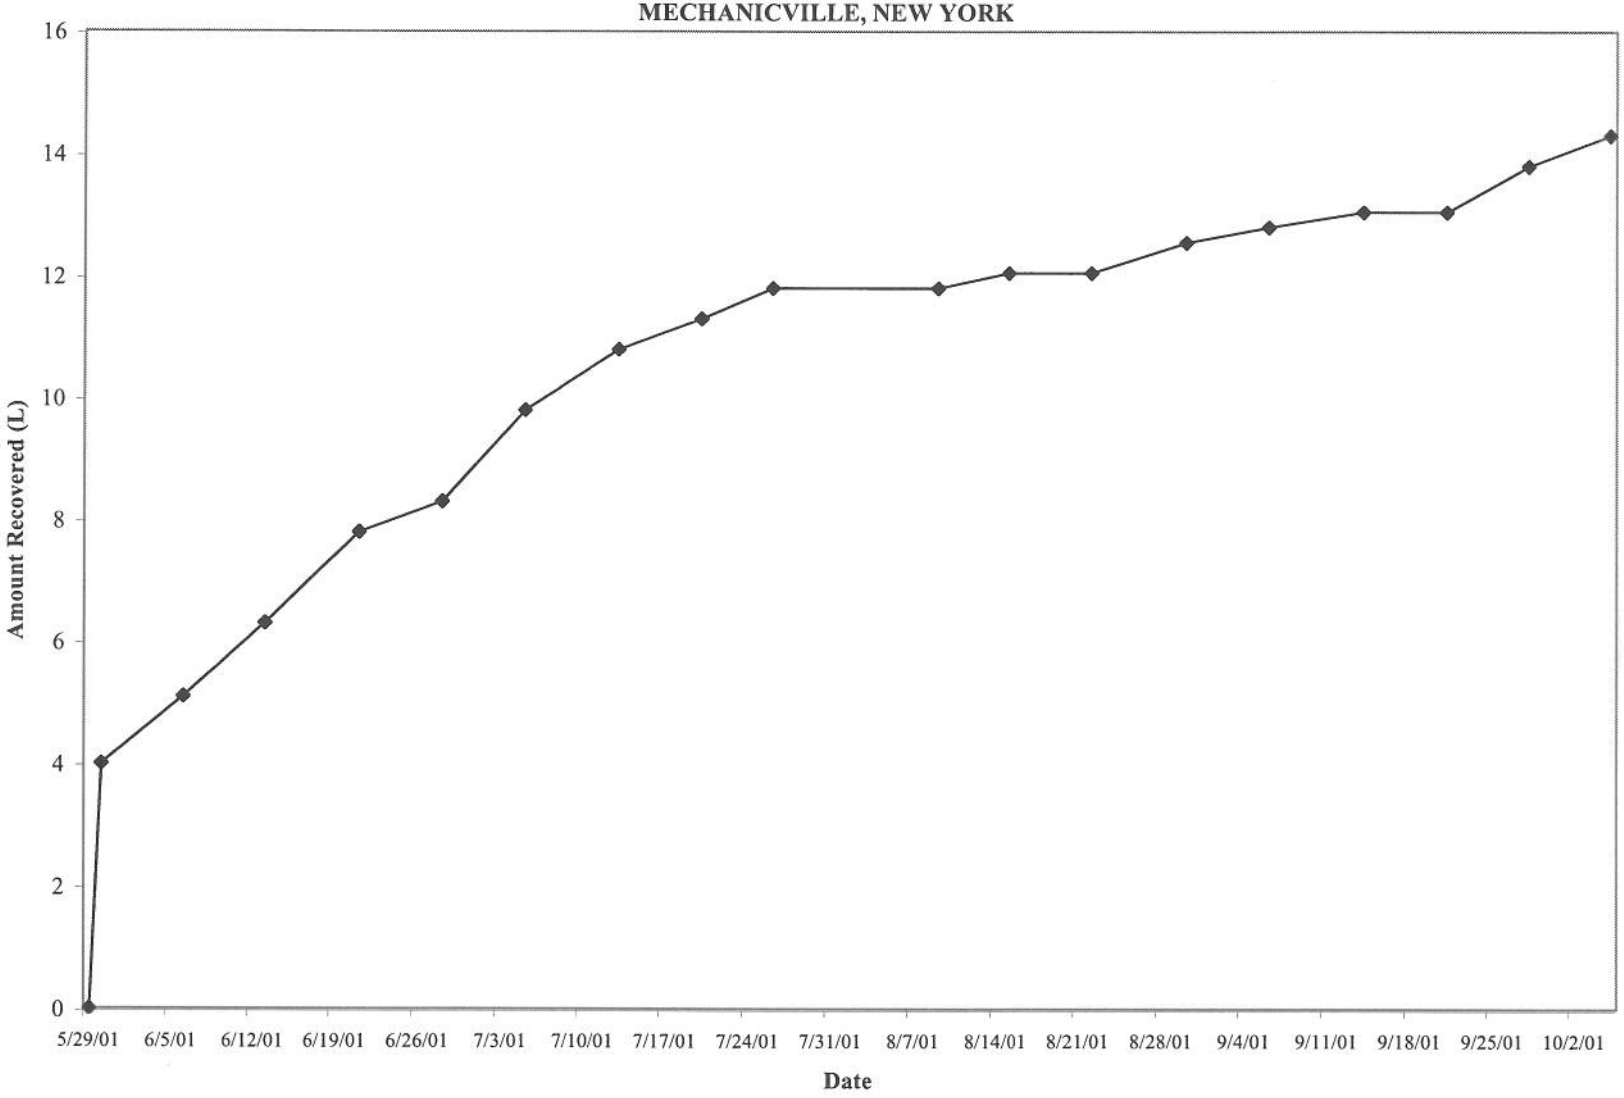

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
10/9/01

*Privileged & Confidential*

**CUMULATIVE PRODUCT RECOVERY**
**MW-26S**

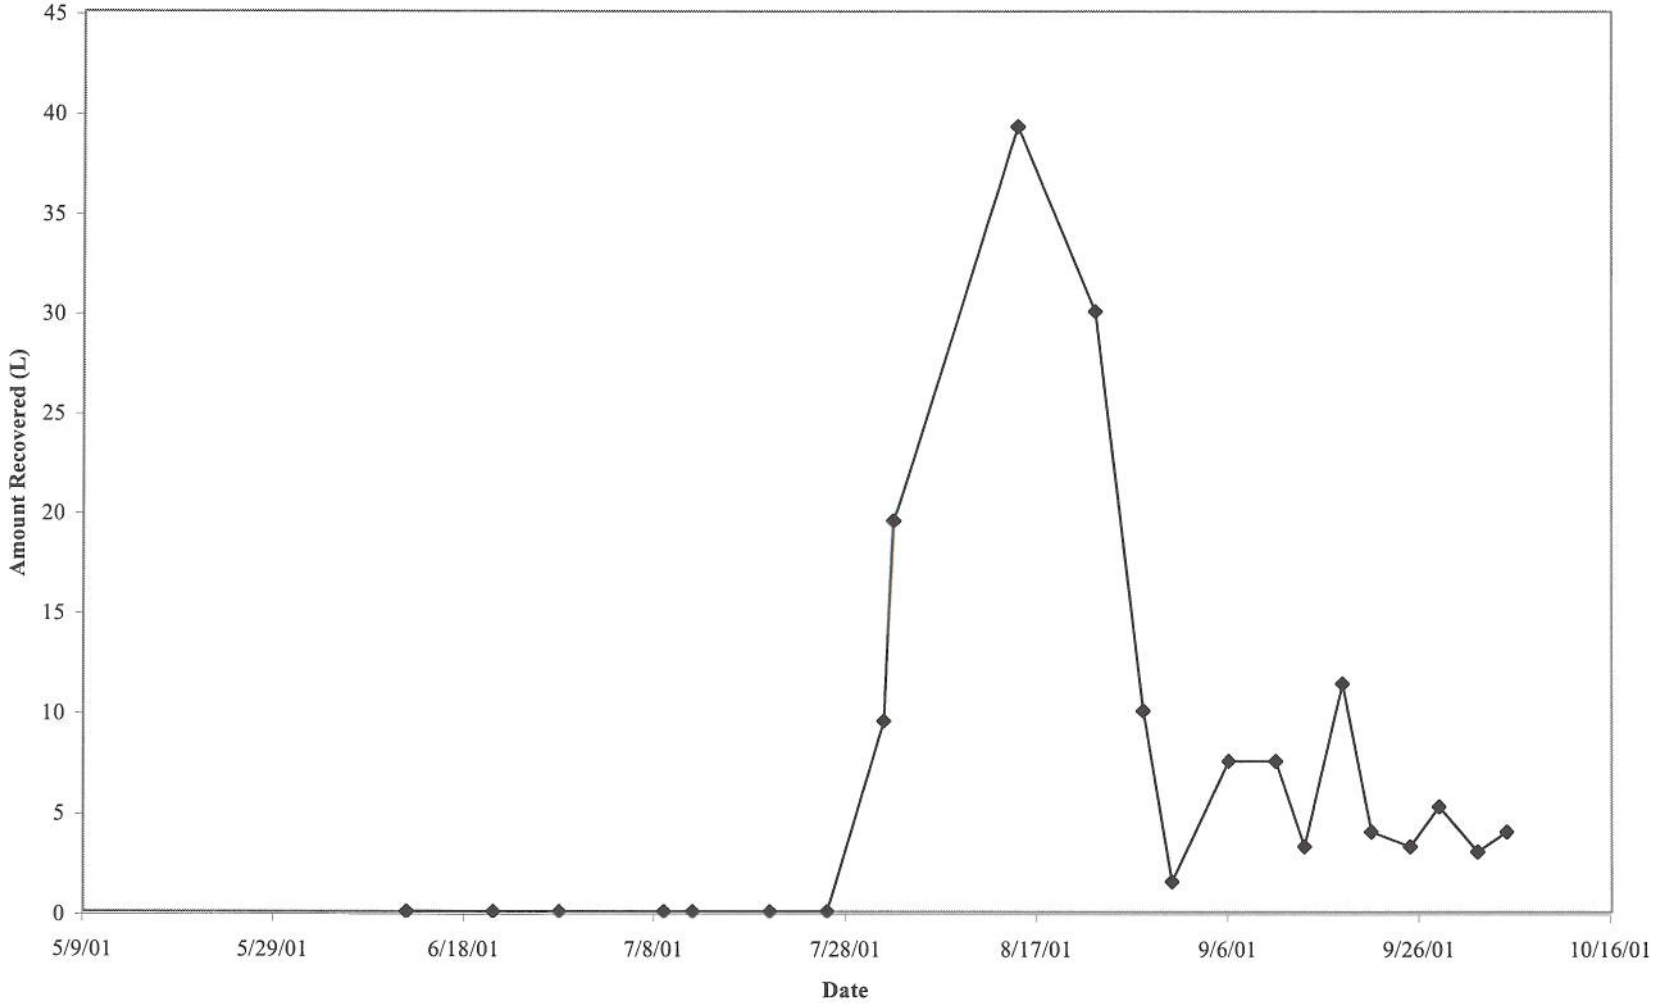
**NYSEG**
**MECHANICVILLE, NEW YORK**



**SUMMARY OF PRODUCT RECOVERY**
**MW-10D**

*Privileged & Confidential*

**NYSEG**
**MECHANICVILLE, NEW YORK**



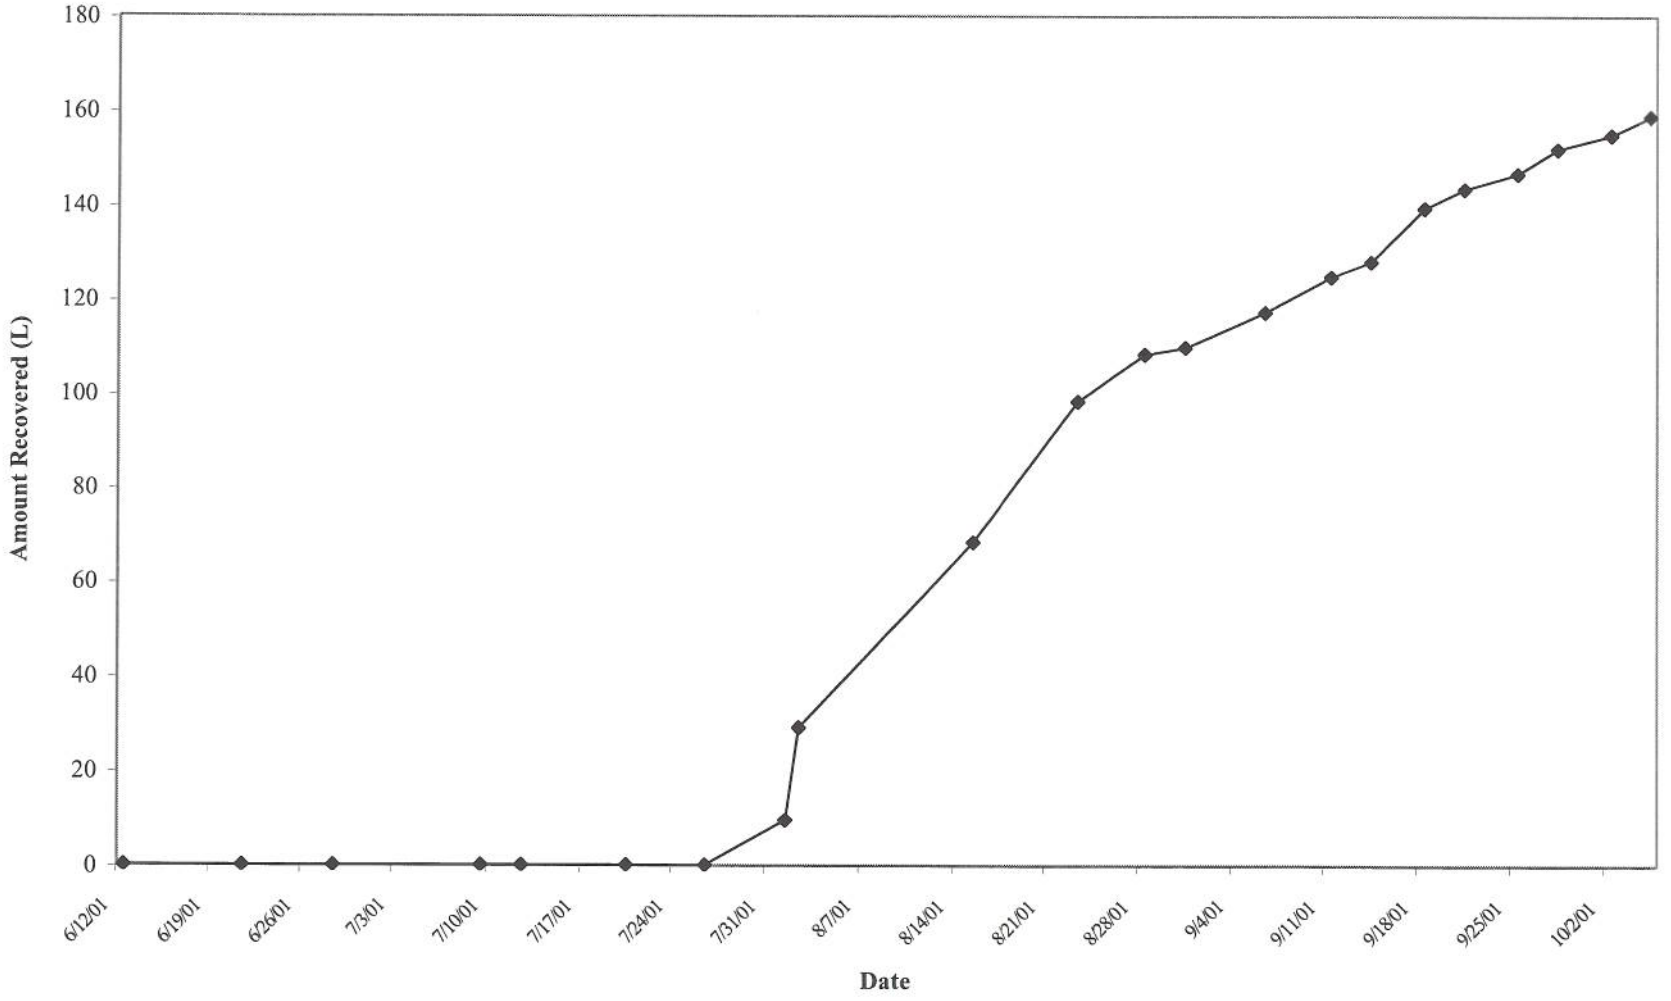

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
10/9/01

**CUMULATIVE PRODUCT RECOVERY**
**MW-10D**

Privileged & Confidential

**NYSEG**
**MECHANICVILLE, NEW YORK**




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
10/9/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: October 2, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of September 24, 2001

Between September 24 and September 28, 2001, URS purged and sampled monitoring wells MW-17, MW-21S, MW-10I, MW17I, MW-18, MW-14D, and MW-21D.

On September 25 and 26, 2001, at NYSEG's request URS collected two composite samples of the cold batch asphalt piles at the site (see out of scope activities). These two composite samples were submitted to the laboratory for full TCLP, reactivity, corrosivity, ignitability, PCBs, and percent solids analyses.

On September 27, 2001, because only one of the cars had been moved from the area of the MW-35D location at the Bull property URS and ADT postponed drilling at the Bull property until Monday October 8, 2001.

### *Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On September 25 and 28, 2001, URS bailed well MW-10D and recovered a total of 8.5 liters of NAPL from well MW-10D. URS recovered approximately 0.75 liters of NAPL from well MW-26S using a peristaltic pump on Friday September 28, 2001.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S and MW-10D area also attached.

***Out of ScopeActivities and Costs***

See attached Table 2.

**Tasks to be Completed During the Week of October 1, 2001.**

URS will continue to coordinate the drilling schedule for well MW-35D.

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will continue groundwater sampling of the clean (NAPL-free) wells at the site.

URS will continue to assemble and evaluate the analytical and bedrock core data.

***Out of ScopeActivities and Costs***

See attached Table 2.

**Tasks to be Completed During the Week of October 1, 2001.**

URS will continue to coordinate the drilling schedule for well MW-35D.

URS will continue to check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

URS will continue groundwater sampling of the clean (NAPL-free) wells at the site.

URS will continue to assemble and evaluate the analytical and bedrock core data.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| Overburden Monitoring Wells | | | | | | |
| MW-1 | 11.6 to 16.85 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-2 | 11.2 to 14.35 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 17, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-10 | 8.7 to 19.5 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-12 | 14.5 to 25.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.23 feet DNAPL |
| | | | August 15, 2001 | None | None | trace [2] |
| | | | August 24, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 21, 2001 | None | Odor, Sheen, Product | trace |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.



NYSEG-Mechanicville
11035-606/092401tl

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-12S | 11 to 26 feet | Screen | May 29, 2001 | Odor | None | NA |
| | | | June 27, 2001 | None | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor | NA |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-14S | 10 to 25 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | None | Odor | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | Odor | Odor | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-15S | 5 to 10 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | Odor | Odor | NA |
| | | | June 13, 2001 | Odor | Odor | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | None | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-16 | 6 to 16 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:

1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-17 | 13 to 23 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-21S | 5 to 10 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | Odor | Odor | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | Odor | NA |
| MW-23S | 7.5 to 12.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | trace |
| | | | May 29, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1** *Privileged & Confidential*
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-25S | 11 to 26 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen | trace |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-26S | 7.5 to 22.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | May 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 4 |
| | | | June 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 |
| | | | June 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | June 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | July 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | .98 feet LNAPL |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | August 22, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | September 21, 2001 | Odor, Sheen, Product | Not Checked | 0.01 feet LNAPL |
| | | | September 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.75 |
| MW-30S | 10 to 25 feet | Screen | August 24, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-31S | 8 to 18 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1** *Privileged & Confidential*
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| RH-1S | 1.8 to 17.3 feet | Screen | May 25, 2001 | Odor | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | September 21, 2001 | Odor, Sheen, Product | None | trace |
| **Shallow Bedrock Monitoring Wells** | | | | | | |
| MW-2I | 11.28 to 32.2 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 17, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-10I | 22 to 43 feet | Open Hole | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-11 | 9.5 to 15 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-13 | 44.7 to 55.5 feet | Screen | July 12, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 21, 2001 | None | None | NA |
| MW-14 | 30 to 41 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-15I | 12.5 to 22.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | trace |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | June 27, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 21, 2001 | None | Odor, Sheen, Product | trace |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-17I | 23 to 45 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-18 | 28 to 38 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-19I | 18 to 38.5 feet | Open Hole | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-22I | 17 to 32 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | Odor | None | NA |
| | | | June 13, 2001 | None | Odor | NA |
| | | | June 28, 2001 | None | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | Odor, Sheen, Product | None | trace |
| | | | September 21, 2001 | Odor, Sheen, Product | None | trace |
| MW-25I | 27 to 47 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 17, 2001 | None | Odor, Sheen, Product | trace [2] |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |

Notes:

1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-26I | 24.5 to 45.5 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | Odor, Sheen | Odor, Sheen | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 9, 2001 | None | Odor | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | trace |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-28I | 15 to 25 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-29I | 11.5 to 26 feet | Open Hole | May 25, 2001 | Odor, Sheen | Odor, Sheen, Product | trace |
| | | | June 7, 2001 | None | Odor, Sheen, Product | trace |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace [2] |
| | | | September 5, 2001 | Odor, Sheen, Product | None | trace |
| | | | September 21, 2001 | Odor, Sheen, Product | None | trace |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| Deep Bedrock Monitoring Wells | | | | | | |
| MW-10D | 82 to 114 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | Odor, Sheen | NA |
| | | | July 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 1, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 |
| | | | August 2, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 |
| | | | August 23, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 30 |
| | | | August 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 10 |
| | | | August 31, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 11, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 |
| | | | September 18, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 |
| | | | September 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 4 |
| | | | September 25, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 |
| | | | September 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 5.25 |
| MW-14D | 91 to 121.7 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-15D | 96 to 105.8 feet | Open Hole | June 11, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-17D | 121 to 142.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-20D | 90 to 110.1 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-21D | 48.7 to 59.4 feet | Open Hole | May 25, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-23D | 56 to 80 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-29D | 90 to 110 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 20, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-30D | 90 to 121 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | Odor, Sheen | Odor, Sheen, Product | trace |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace [2] |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace [2] |
| | | | August 24, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | trace |
| | | | September 21, 2001 | Odor, Sheen, Product | None | trace |
| MW-31D | 28 to 150 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

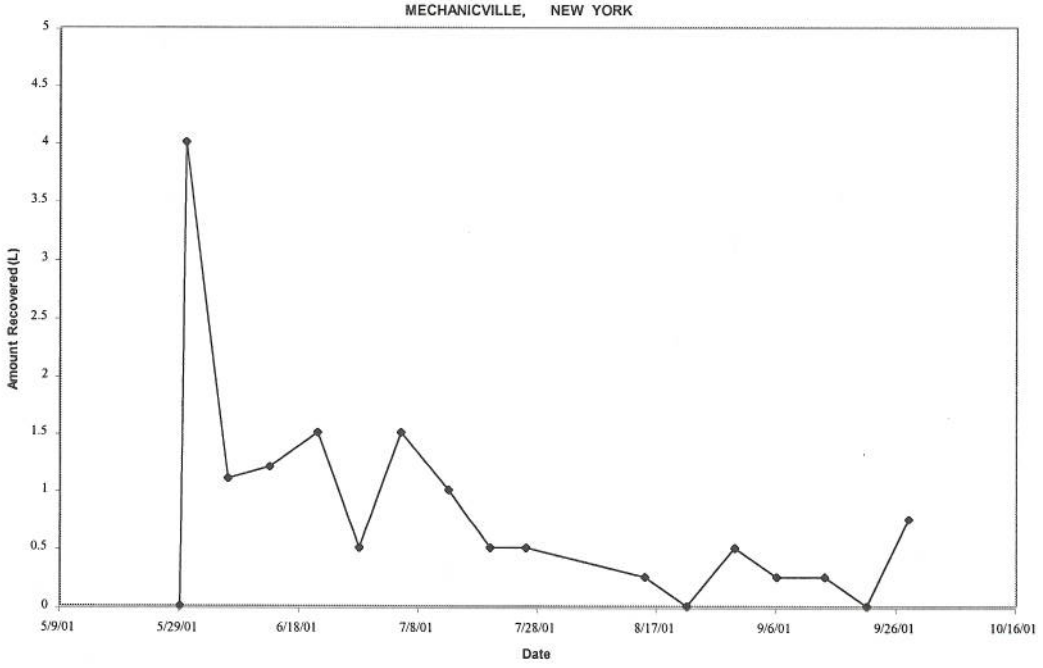
| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-32D | 91 to 111.5 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 19, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| MW-33D | 119.7 to 140.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | Odor, Sheen | NA |
| | | | September 28, 2001 | None | Odor | NA |
| MW-34D | 100 to 120.5 feet | Open Hole | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |
| RH-1D | 86.5 to 107.5 feet | Open Hole | June 5, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 27, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 11, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| | | | September 28, 2001 | None | None | NA |

Notes:
1. NA indicates not applicable.
2. No quantifiable NAPL recovered.

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



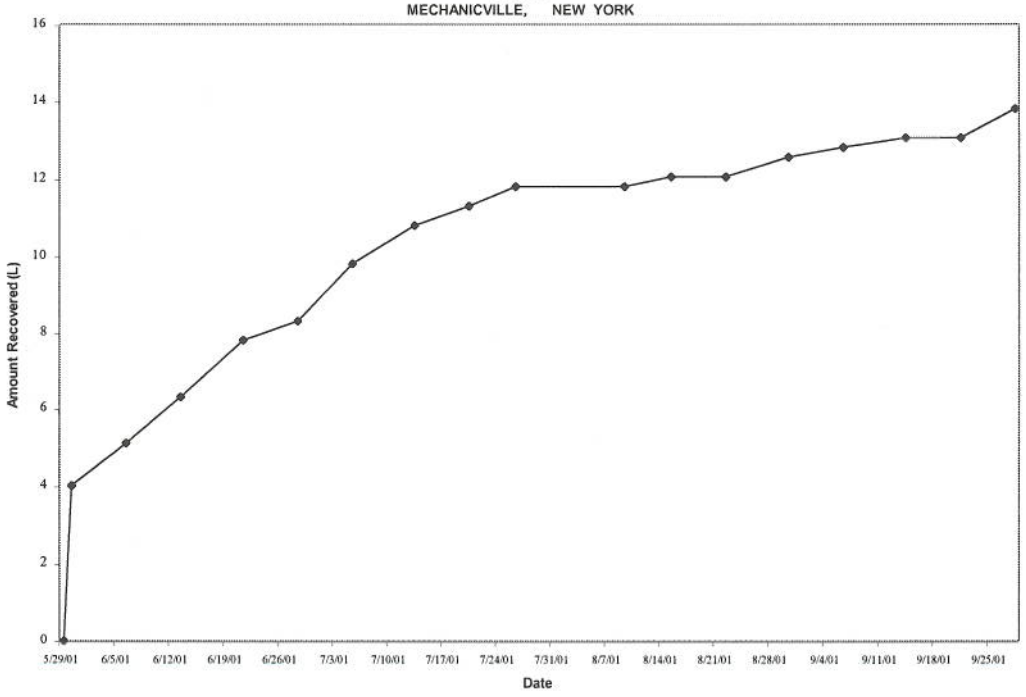

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
10/2/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



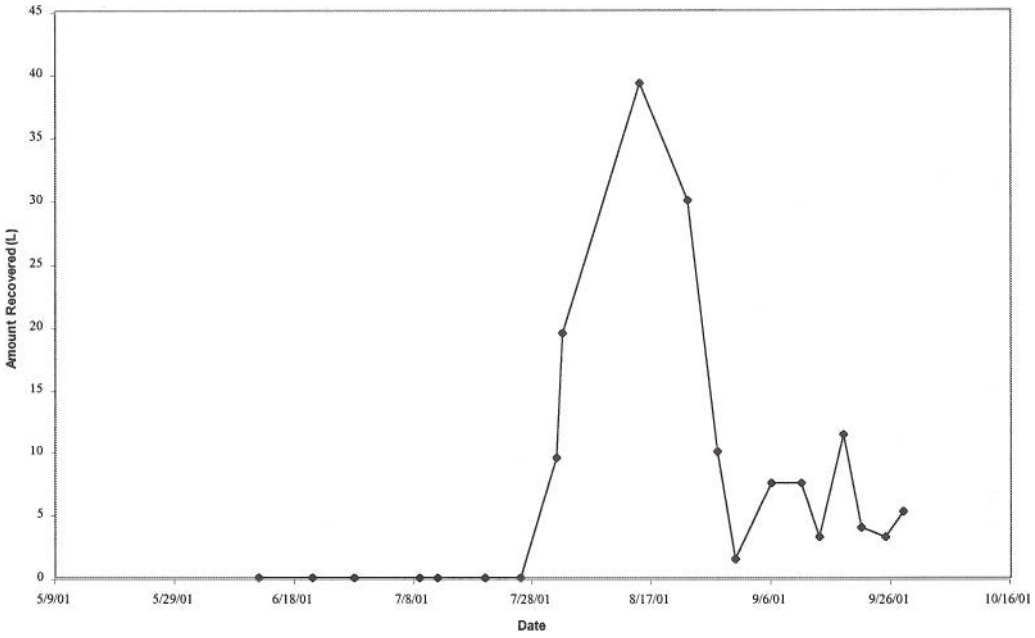

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S CUMULATIVE

URS
10/2/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



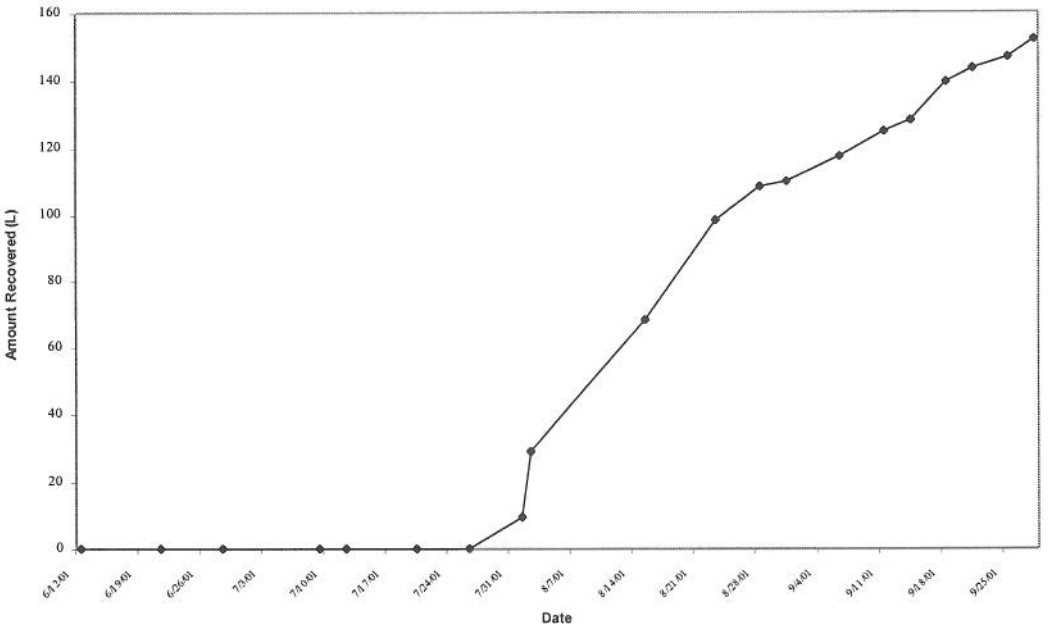

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
10/2/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

Privileged & Confidential

NYSEG
MECHANICVILLE, NEW YORK




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
10/2/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: September 25, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of September 17, 2001

On September 17, 2001, URS initiated groundwater sampling at the site. Between September 17 and 21, 2001, URS purged and sampled monitoring wells MW-1, MW-2, MW-2I, MW-11, MW-19I, MW-29D, and MW-32D.

As of September 21, 2001, URS and NYSEG had not been able to contact the Bulls about moving cars at their service shop to provide access to the MW-35D location. Drilling at the Bull property was postponed until September 25, 2001. However, on September 24, 2001, drilling was again postponed until Monday October 1, 2001.

### *Summary of NAPL Observations*

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On September 18 and 21, 2001, URS bailed well MW-10D and recovered a total of 15.4 liters of NAPL from well MW-10D. URS postponed NAPL recovery efforts at MW-26S until Friday September 28, 2001. URS observed a slight sheen in well MW-33D in the southern portion of the DiSiena parking lot.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S and MW-10D area also attached.

### *Out of Scope Activities and Costs*

See attached Table 2.

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | | |
| MW-1 | 11.6 to 16.85 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |
| MW-2 | 11.2 to 14.35 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 17, 2001 | None | None | NA |
| MW-10 | 8.7 to 19.5 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-12 | 14.5 to 25.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |
| | | | September 21, 2001 | None | Odor, Sheen, Product | NA |

Table 1
Summary of NAPL Observations

*Privileged Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-12S | 11 to 26 feet | Screen | May 29, 2001 | Odor | None | NA |
| | | | June 27, 2001 | None | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor | NA |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-14S | 10 to 25 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | None | Odor | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | Odor | Odor | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-15S | 5 to 10 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | Odor | Odor | NA |
| | | | June 13, 2001 | Odor | Odor | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | None | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-16 | 6 to 16 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-17 | 13 to 23 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-21S | 5 to 10 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | Odor | Odor | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-23S | 7.5 to 12.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | 0 |
| | | | May 29, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-25S | 11 to 26 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen | 0 |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-26S | 7.5 to 22.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | May 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 4 |
| | | | June 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 |
| | | | June 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | June 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | July 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | August 22, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | September 21, 2001 | Odor, Sheen, Product | None | NA |
| MW-30S | 10 to 25 feet | Screen | August 24, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-31S | 8 to 18 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| RH-1S | 1.8 to 17.3 feet | Screen | May 25, 2001 | Odor | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | September 21, 2001 | Odor, Sheen, Product | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| **Shallow Bedrock Monitoring Wells** | | | | | | |
| MW-2I | 11.28 to 32.2 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 17, 2001 | None | None | NA |
| MW-10I | 22 to 43 feet | Open Hole | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-11 | 9.5 to 15 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |
| MW-13 | 44.7 to 55.5 feet | Screen | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-14 | 30 to 41 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-15I | 12.5 to 22.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | 0 |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 27, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |
| | | | September 21, 2001 | None | Odor, Sheen, Product | NA |
| MW-17I | 23 to 45 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-18 | 28 to 38 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-19I | 18 to 38.5 feet | Open Hole | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 18, 2001 | None | None | NA |

**Table 1**
**Summary of NAPL Observations**

*Privileged Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-22I | 17 to 32 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | Odor | None | NA |
| | | | June 13, 2001 | None | Odor | NA |
| | | | June 28, 2001 | None | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | Odor, Sheen, Product | None | NA |
| | | | September 21, 2001 | Odor, Sheen, Product | None | NA |
| MW-25I | 27 to 47 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 17, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-26I | 24.5 to 45.5 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | Odor, Sheen | Odor, Sheen | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 9, 2001 | None | Odor | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-28I | 15 to 25 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

**Table 1**
**Summary of NAPL Observations**

*Privileged Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-29I | 11.5 to 26 feet | Open Hole | May 25, 2001 | Odor, Sheen | Odor, Sheen, Product | 0 |
| | | | June 7, 2001 | None | Odor, Sheen, Product | 0 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | Odor, Sheen, Product | None | NA |
| | | | September 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| **Deep Bedrock Monitoring Wells** | | | | | | |
| MW-10D | 82 to 114 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | Odor, Sheen | NA |
| | | | July 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 1, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 |
| | | | August 2, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 |
| | | | August 23, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 30 |
| | | | August 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 10 |
| | | | August 31, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 11, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 |
| | | | September 18, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 11.36 |
| | | | September 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 4 |
| MW-14D | 91 to 121.7 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-15D | 96 to 105.8 feet | Open Hole | June 11, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-17D | 121 to 142.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-20D | 90 to 110.1 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-21D | 48.7 to 59.4 feet | Open Hole | May 25, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-23D | 56 to 80 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-29D | 90 to 110 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 20, 2001 | None | None | NA |
| MW-30D | 90 to 121 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | Odor, Sheen | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 24, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | September 21, 2001 | Odor, Sheen, Product | None | NA |
| MW-31D | 28 to 150 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

*Privileged Confidential*

**Table 1**
**Summary of NAPL Observations**

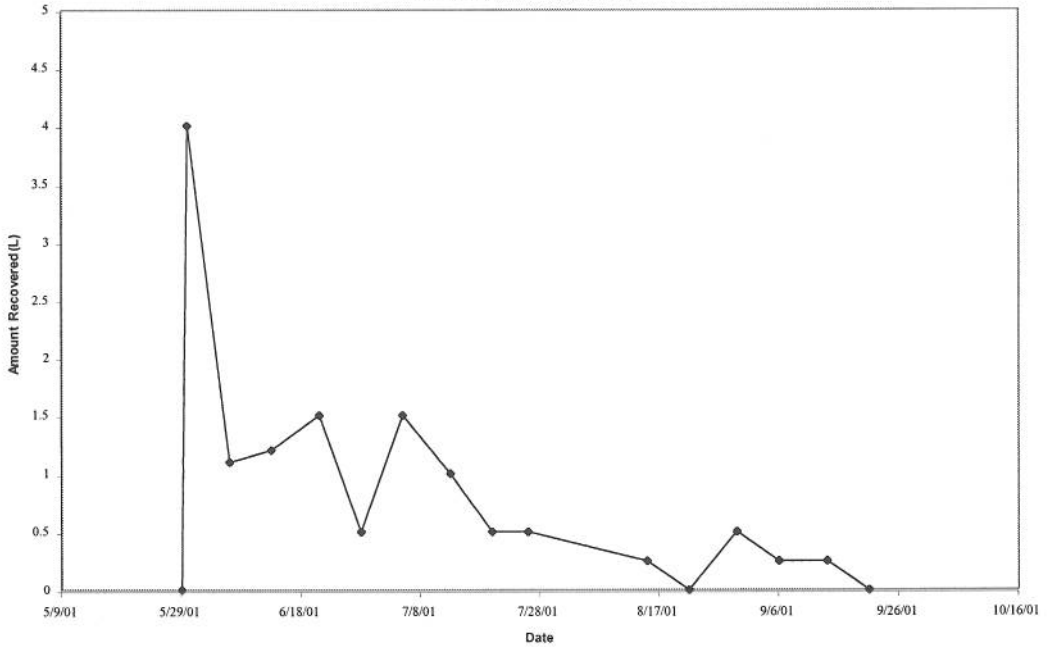
| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-32D | 91 to 111.5 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 19, 2001 | None | None | NA |
| MW-33D | 119.7 to 140.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | Odor, Sheen | NA |
| RH-1D | 86.5 to 107.5 feet | Open Hole | June 5, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 27, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 11, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |
| MW-34D | 100 to 120.5 feet | Open Hole | September 14, 2001 | None | None | NA |
| | | | September 21, 2001 | None | None | NA |

Explanation:
NA indicates not applicable

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



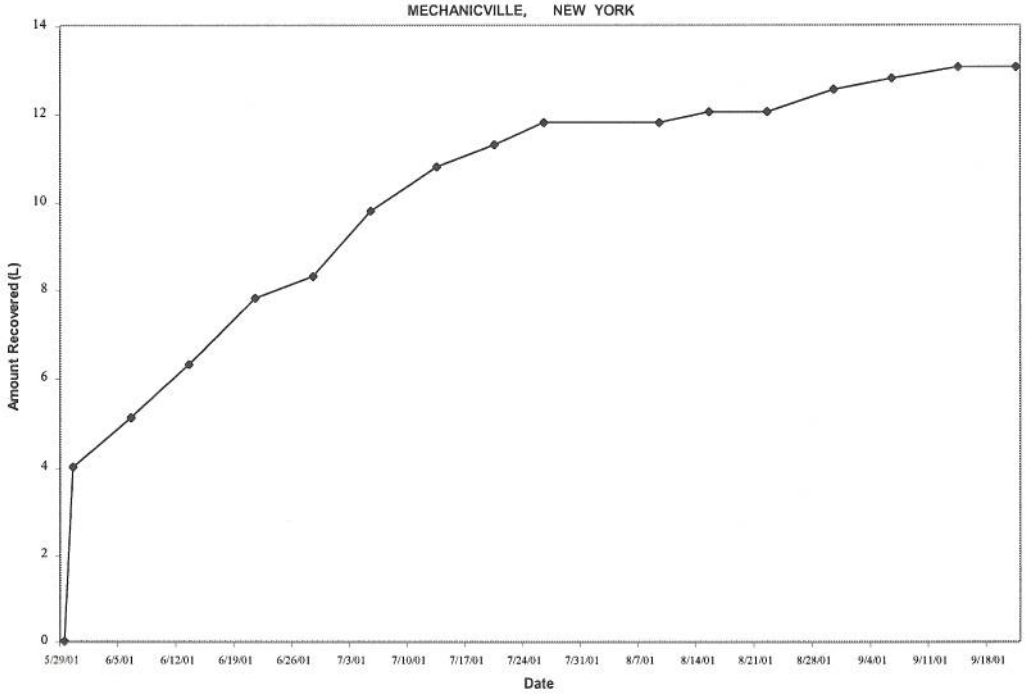

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
9/25/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



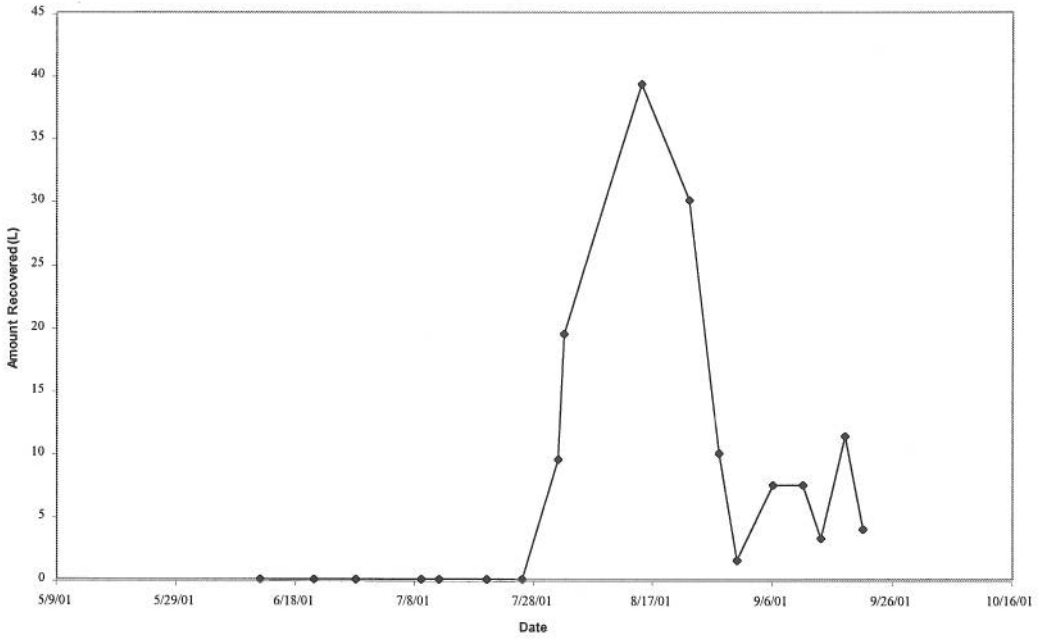

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S CUMULATIVE

URS
9/25/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



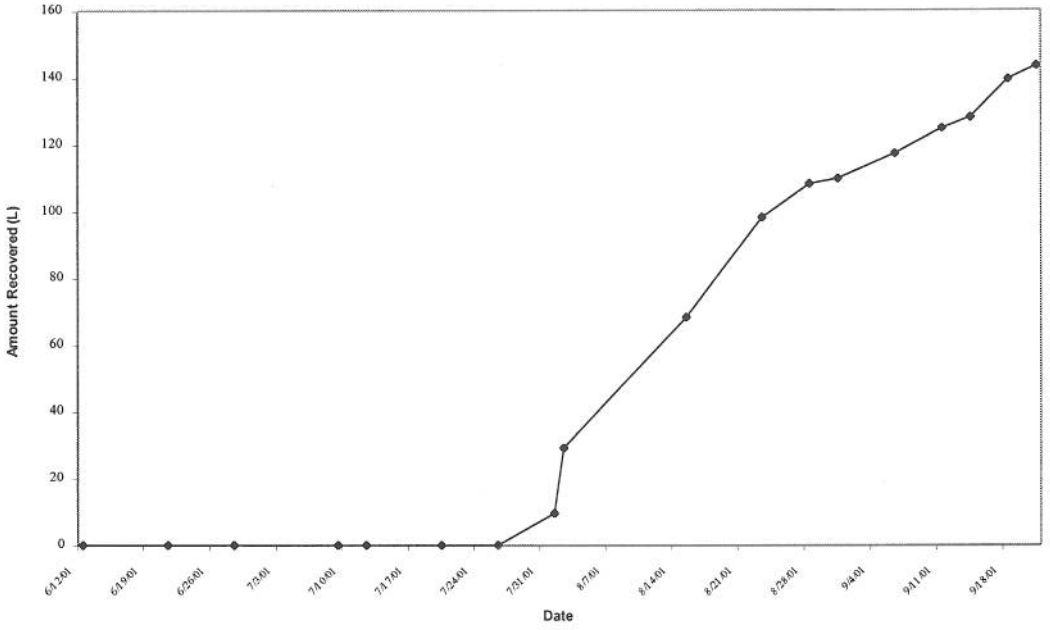

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
9/25/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

Privileged & Confidential

NYSEG
MECHANICVILLE, NEW YORK




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
9/25/01

# Memorandum - Clifton Park

URS Corporation
646 Plank Road, Suite 202
Clifton Park, New York 12065

Telephone - (518) 688-0015
Fax - (518) 688-0022

TO: Tracy Blazicek-NYSEG
Jeff Edwards-NYSDEC (excluding Table 2)
Gardiner Cross-NYSDEC (excluding Table 2)

INFO: Scott Sklenar-URS
Paul Pavone-URS
Scott Hulseapple-URS

FROM: Eriko Fujita

DATE: September 19, 2001

SUBJECT: Progress Report – Supplemental Remedial Investigation Field Work
NYSEG-Mechanicville, NY

## Tasks Completed During the Week of September 10, 2001

On September 10, 2001, the open hole interval from approximately 100 to 120.5 feet bgs was cored at well MW-34D north of the site. The open hole interval was reamed with a 3 7/8-inch roller bit. There were no signs of NAPL or MGP odors during drilling of the open hole interval.

On September 10, 2001, URS received and reviewed the data the survey data related to the Anthony Kill collected from the site last Friday from NYSEG's surveyor CT Male. On September 13, 2001, NYSEG, CT Male, and URS participated in a conference call to discuss the survey data. CT Male returned to the site on Friday, September 14, 2001 to conduct an additional round of surveying. In addition to surveying the reference points for the seeps and well locations, CT Male also surveyed the top of the south bank of the kill and edge of the water on each side of the kill.

On September 11, 2001, URS developed well MW-29I with the peristaltic pump. The development water exhibited MGP odors and sheens. Between September 12 and 13, 2001, ADT developed wells MW-30S, MW-20D, and MW-34D. During development, there were no signs of NAPL or MGP odors in the water from wells MW-30S, MW-20D, and MW-34D.

On September 14, 2001, URS was informed by NYSEG that the NYSDEC is requiring that an additional well be installed on the Bull property north of the site. There is a potential buyer for the Bull property. NYSEG has agreed to install this new well that will be identified as well MW-35D (See out of scope activities) as soon as possible. The location of planned well MW-35D will be east of well MW-20D, and directly across the kill from the MW-29I/MW-29D and RH-1S/RH-1D well clusters. At NYSEG's request, the NYSDEC agreed to tell the Bulls that NYSEG is willing to provide a letter of indemnification and that the installation of well MW-35D does not provide any guarantee that further work on their property will not be warranted. NYSEG, NYSDEC, and URS agreed that additional work will likely be

warranted on the north side of the Bull property or north of Bull property due to the detected sheens and odors in the bedrock at approximately 35 and 38 feet bgs at well MW-34D.

URS contacted ADT to coordinate the remobilization to the site to install MW-35D. ADT anticipated that they would remobe either Tuesday September 18, 2001 or Wednesday September 19, 2001 pending receipt of some replacement parts for the pump on the drill rig. NYSEG and NYSDEC were made aware of ADT's schedule and it was understood that the NYSDEC would contact the Bulls regarding this schedule. As of September 18, 2001, URS and NYSEG have not been able to contact the Bulls about moving cars at their service shop to provide access to the MW-35D location. Drilling at the Bull property has been postponed until Tuesday September 25, 2001.

Between September 11 and 12, 2001, ADT removed the bedrock cuttings from one of the 1,000-gallon and one of the 1,500-gallon poly tanks. ADT drummed the bedrock cuttings. All of the drums are now staged near to the North Central Avenue side of the site. NYSEG is currently arranging for a drum pick up for offsite disposal.

In addition, on September 10, 2001, NYSEG's contractor Clean Harbors was onsite for a water pick up.

***Summary of NAPL Observations***

URS conducted weekly NAPL checks and recovery at the site (see out of scope activities below). On September 11 and 14, 2001, URS bailed well MW-10D and recovered a total of 10.75 liters of NAPL from well MW-10D. On September 14, 2001, approximately 0.25 liters of NAPL was recovered from well MW-26S.

See attached Table 1. Graphs showing periodic product recovery and cumulative product recovery for wells MW-26S and MW-10D area also attached.

***Out of ScopeActivities and Costs***

See attached Table 2.

**Tasks to be Completed During the Week of September 17, 2001.**

URS will continue to provide oversight during drilling at well MW-35D, check wells for NAPL, monitor the kill at the site, and recovery NAPL as necessary.

ADT planned to remobe to the site to install the 8-inch overburden casing at well MW-35D on the Bull property this week. Because URS and NYSEG have not been able to contact the Bulls to request their help with providing access to the MW-35D location, drilling has been postponed until Tuesday September 25, 2001. NYSEG and URS will continue to try to contact the Bulls to coordinate the drilling schedule.

URS will continue to assemble and evaluate the analytical and bedrock core data.

URS will initiate groundwater sampling of the clean (NAPL-free) wells at the site.

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| **Overburden Monitoring Wells** | | | | | | |
| MW-1 | 11.6 to 16.85 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-2 | 11.2 to 14.35 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-10 | 8.7 to 19.5 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| MW-12 | 14.5 to 25.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |
| MW-12S | 11 to 26 feet | Screen | May 29, 2001 | Odor | None | NA |
| | | | June 27, 2001 | None | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor | NA |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| MW-14S | 10 to 25 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | None | Odor | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | Odor | Odor | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-15S | 5 to 10 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | Odor | Odor | NA |
| | | | June 13, 2001 | Odor | Odor | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | None | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| MW-16 | 6 to 16 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-17 | 13 to 23 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-21S | 5 to 10 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | Odor | Odor | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-23S | 7.5 to 12.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | 0 |
| | | | May 29, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor | Odor | NA |
| | | | July 19, 2001 | Odor | Odor | NA |
| | | | July 20, 2001 | Odor | Odor | NA |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | None | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| MW-25S | 11 to 26 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen | 0 |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-26S | 7.5 to 22.5 feet | Screen | May 29, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | May 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 4 |
| | | | June 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.1 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.2 |
| | | | June 21, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | June 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | July 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | August 22, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 30, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0.25 |
| MW-30S | 10 to 25 feet | Screen | August 24, 2001 | None | None | NA |
| MW-31S | 8 to 18 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| RH-1S | 1.8 to 17.3 feet | Screen | May 25, 2001 | Odor | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 27, 2001 | Odor | Odor | NA |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| **Shallow Bedrock Monitoring Wells** | | | | | | |
| MW-2I | 11.28 to 32.2 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-10I | 22 to 43 feet | Open Hole | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-11 | 9.5 to 15 feet | Screen | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-13 | 44.7 to 55.5 feet | Screen | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-14 | 30 to 41 feet | Screen | June 28, 2001 | Odor | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 23, 2001 | None | Odor | NA |
| | | | September 5, 2001 | None | None | NA |
| MW-15I | 12.5 to 22.5 feet | Screen | May 25, 2001 | Odor, Sheen, Product | None | 0 |
| | | | June 7, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | June 27, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor, Sheen, Product | NA |
| | | | August 24, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | Odor, Sheen, Product | NA |
| MW-17I | 23 to 45 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-18 | 28 to 38 feet | Screen | June 5, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-19I | 18 to 38.5 feet | Open Hole | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-22I | 17 to 32 feet | Screen | May 25, 2001 | Odor | Odor | NA |
| | | | June 7, 2001 | Odor | None | NA |
| | | | June 13, 2001 | None | Odor | NA |
| | | | June 28, 2001 | None | Odor | NA |
| | | | July 6, 2001 | None | Odor | NA |
| | | | July 12, 2001 | None | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor | Odor | NA |
| | | | August 3, 2001 | Odor | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor | Odor | NA |
| | | | September 5, 2001 | Odor, Sheen, Product | None | NA |

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

*Privileged & Confidential*

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-25I | 27 to 47 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 17, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| MW-26I | 24.5 to 45.5 feet | Open Hole | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | Odor, Sheen | Odor, Sheen | NA |
| | | | August 3, 2001 | None | Odor | NA |
| | | | August 9, 2001 | None | Odor | NA |
| | | | August 24, 2001 | None | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | None | None | NA |
| MW-28I | 15 to 25 feet | Screen | May 25, 2001 | None | None | NA |
| | | | June 7, 2001 | None | None | NA |
| | | | June 13, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-29I | 11.5 to 26 feet | Open Hole | May 25, 2001 | Odor, Sheen | Odor, Sheen, Product | 0 |
| | | | June 7, 2001 | None | Odor, Sheen, Product | 0 |
| | | | June 13, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | September 5, 2001 | Odor, Sheen, Product | None | NA |
| **Deep Bedrock Monitoring Wells** | | | | | | |
| MW-10D | 82 to 114 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | Odor, Sheen | NA |
| | | | July 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 12, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 20, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | July 26, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 1, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 9.5 |
| | | | August 2, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 19.5 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 15, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 39.25 |
| | | | August 23, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 30 |
| | | | August 28, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 10 |
| | | | August 31, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 1.5 |
| | | | September 6, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 11, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 7.5 |
| | | | September 14, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 3.25 |

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-14D | 91 to 121.7 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-15D | 96 to 105.8 feet | Open Hole | June 11, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-17D | 121 to 142.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-20D | 90 to 110.1 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-21D | 48.7 to 59.4 feet | Open Hole | May 25, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 5, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |

*Privileged & Confidential*

**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| MW-23D | 56 to 80 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-29D | 90 to 110 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-30D | 90 to 121 feet | Open Hole | July 6, 2001 | None | None | NA |
| | | | July 13, 2001 | None | None | NA |
| | | | July 20, 2001 | Odor, Sheen | Odor, Sheen, Product | 0 |
| | | | August 3, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 9, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | NA |
| | | | August 17, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| | | | August 24, 2001 | Odor, Sheen, Product | Odor, Sheen, Product | 0 |
| MW-31D | 28 to 150 feet | Open Hole | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 12, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 8, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 5, 2001 | None | None | NA |
| | | | September 12, 2001 | None | None | NA |
| MW-32D | 91 to 111.5 feet | Open Hole | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-33D | 119.7 to 140.5 feet | Open Hole | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |

*Privileged & Confidential*

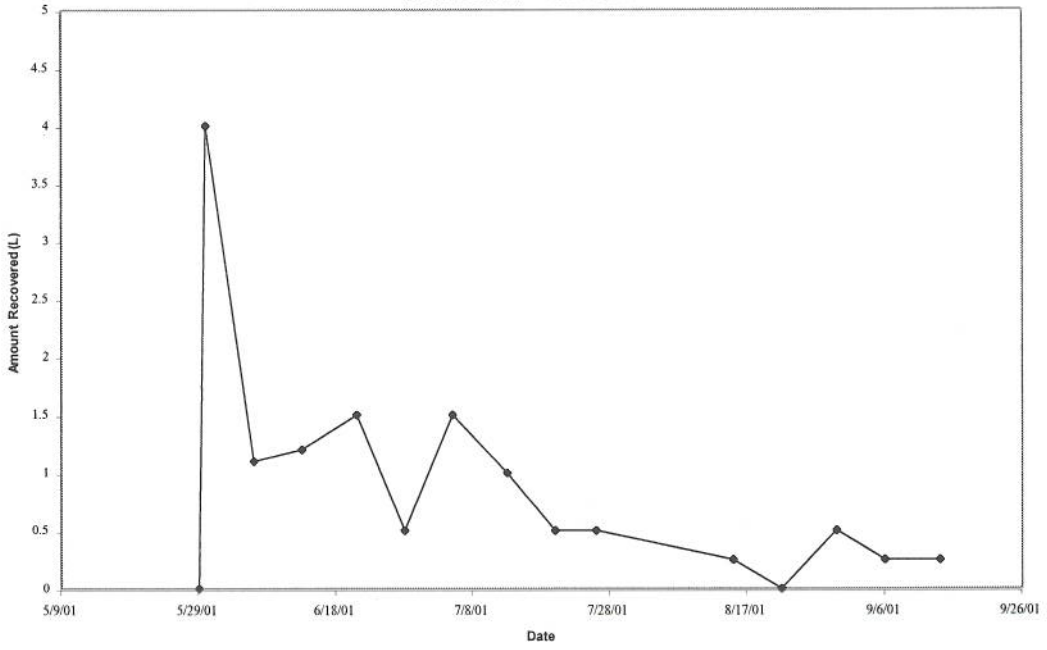
**TABLE 1**
**SUMMARY OF NAPL OBSERVATIONS**

| WELL NUMBER | Screened Interval | Screen or Open Hole | DATE | LNAPL Observations | DNAPL Observations | Amount of NAPL Recovered (L) |
|---|---|---|---|---|---|---|
| RH-1D | 86.5 to 107.5 feet | Open Hole | June 5, 2001 | None | None | NA |
| | | | June 12, 2001 | None | None | NA |
| | | | June 21, 2001 | None | None | NA |
| | | | June 27, 2001 | None | None | NA |
| | | | June 28, 2001 | None | None | NA |
| | | | July 6, 2001 | None | None | NA |
| | | | July 11, 2001 | None | None | NA |
| | | | July 19, 2001 | None | None | NA |
| | | | July 26, 2001 | None | None | NA |
| | | | August 3, 2001 | None | None | NA |
| | | | August 9, 2001 | None | None | NA |
| | | | August 15, 2001 | None | None | NA |
| | | | August 23, 2001 | None | None | NA |
| | | | August 29, 2001 | None | None | NA |
| | | | September 7, 2001 | None | None | NA |
| | | | September 14, 2001 | None | None | NA |
| MW-34D | 100 to 120.5 feet | Open Hole | September 14, 2001 | None | None | NA |

SUMMARY OF PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



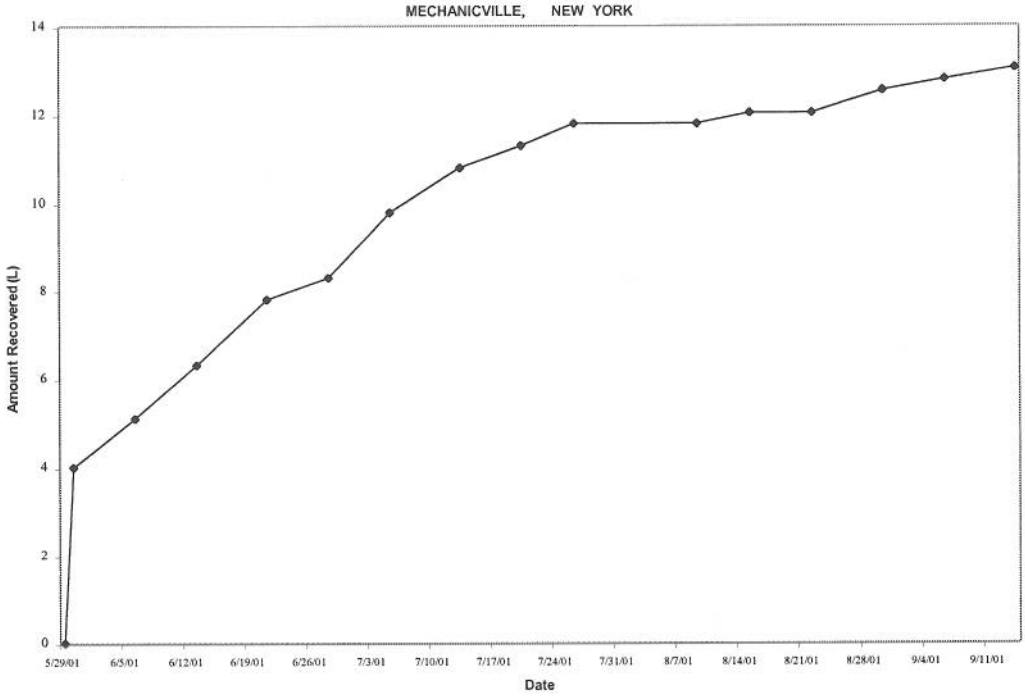

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S

URS
9/19/01

CUMULATIVE PRODUCT RECOVERY
MW-26S

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



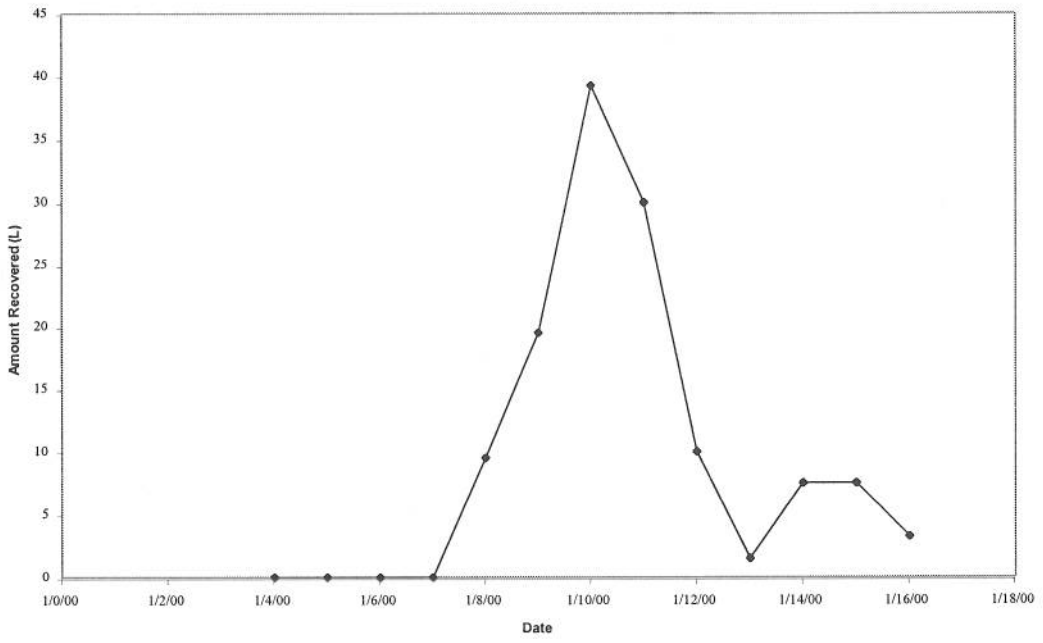

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-26S CUMULATIVE

URS
9/19/01

SUMMARY OF PRODUCT RECOVERY
MW-10D

*Privileged & Confidential*

NYSEG
MECHANICVILLE, NEW YORK



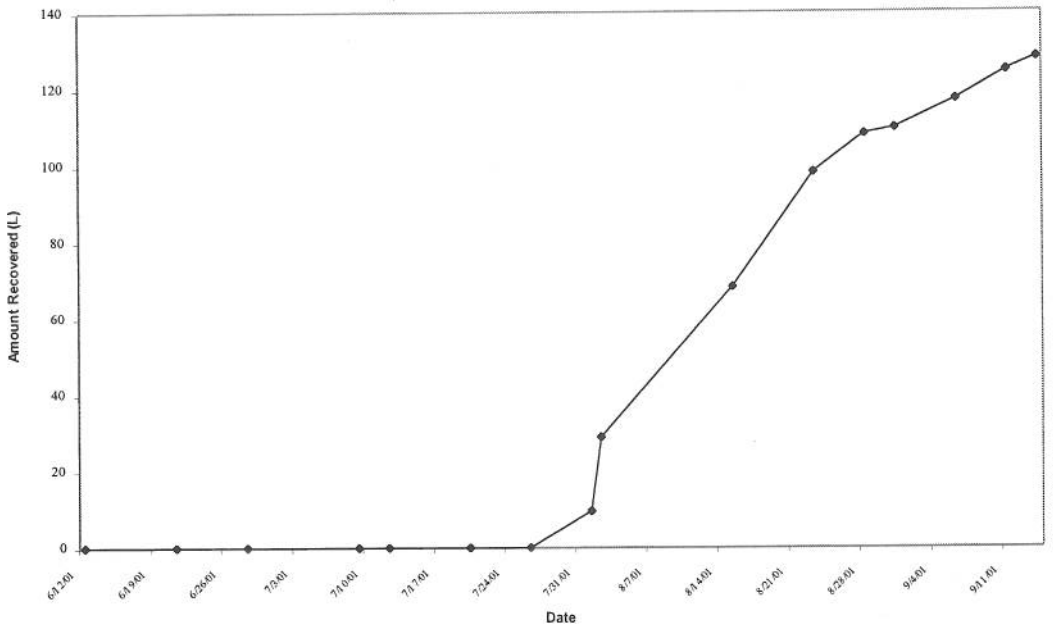

NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D

URS
9/19/01

CUMULATIVE PRODUCT RECOVERY
MW-10D

NYSEG
MECHANICVILLE, NEW YORK

Privileged & Confidential




NYSEG-Mechanicville
11035-606/ProductRecoveryGraphs/MW-10D CUMULATIVE

URS
9/19/01
