11000 N. MoPac Expressway, Suite 500
Austin, Texas 78759
Phone: (512) 451-6334
Fax: (512) 459-1459

Date Printed and Mailed: 6/9/2026

DEC-AVON
REGION 8
6274 EAST AVON-LIMA ROAD
AVON, NY 14414

Test Date: 6/3/2026
Order Number: 8617735

Dear Regulator,


Enclosed are the results of recent testing performed at the following facility:

BJ's Wholesale #185
300 Bellwood Drive
PBS# 8-601258
Rochester, NY 14606

Testing conducted in accordance with paragraph 613-2.3(d)(2) of NYCRR. Technician is a certified Vacutect tank tester and/or a certified TLD-1 line tester in accordance with company protocol. Technician address on file at Tanknology corporate office: 11000 N. MoPac Expressway, Suite 500, Austin, TX 78759

Testing performed:
- IMPACT VALVE
- LEAK DETECTOR
- MONITOR CERTIFICATION

Sincerely,



Dawn Kohlmeyer
Manager, Field Reporting

Tanknology


LDT 5000 Field Test Apparatus
Line Leak Detector Test

Work Order: 8617735 Date: 6/3/2026
Site Name / ID: BJ's Wholesale #185 / 185
Address: 300 Bellwood Drive PBS# 8-601258
City: Rochester State: NY Zip: 14606

Tank ID	1 RUL NYDEC 001	3 PUL NYDEC 003				
Product	REGULAR	PREMIUM				
Product Line	1	1				
Tested From	2	2				
Existing/New	Existing	Existing				
Mechanical/Electronic	Mechanical	Mechanical				
Manufacturer/Model	FE Petro MLD	FE Petro MLD				
Serial No.	UR	UR				
Pump Operating Pressure (psi)	32.00	32.00				
Calibrated Leak (ml/min)	189.0	189.0				
Calibrated Leak (gph)	3.00	3.00				
Holding PSI *N/A for Electronic LD's	20.00	15.00				
Resiliency (ml) *N/A for Electronic LD's	125.00	150.00				
Metering PSI *N/A for Electronic LD's	10	12				
Opening Time (sec) *N/A for Electronic LD's	4	3				
Test Results	Pass	Pass				

Technician Comments:

Technician Name: Jeffrey Claeys **Certification #:** 133137

Technician Signature:  **Expire Date:** 6/18/2026

Environmental Compliance for Petroleum Systems

© 2026 Tanknology Inc., Austin, TX. All rights reserved. tanknology.com

Impact Valve Inspection

Impact Valve Operational Inspection


Work Order: 8617735 Date: 6/3/2026
Site Name/ID: BJ's Wholesale #185
Address: 300 Bellwood Drive PBS# 8-601258
City: Rochester State: NY Zip: 14606

How Inspected: Line Test ☐ NFPA 30A ☑ PEI RP1200 ☐ Other ☐

Dispenser Number	Grade	Secure Mount?	Valve Lock?	Pass/ Fail	Comments
1/2	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
1/2	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
3/4	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
3/4	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
5/6	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
5/6	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
7/8	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
7/8	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
9/10	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
9/10	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
11/12	87	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	
11/12	93	☑	☑	☑ Pass ☐ Fail ☐ Not Tested	

Technician Comments:

Technician Name: Jeffrey Claeys

Signature: 

Environmental Compliance for Petroleum Systems

©2026 Tanknology Inc., Austin, TX. All rights reserved. tanknology.com

MONITORING SYSTEM CERTIFICATION

This form is used to document testing and servicing of tank and piping leak monitoring equipment. If required by applicable law, a copy of the completed form must be provided by the Testing Contractor or owner to the governing UST agency as required by regulation.

A. General Information

Facility Name: BJ's Wholesale #185 Bldg. No.:

Site Address: 300 Bellwood DrivePBS# 8-601258 City: Rochester State: NY Zip: 14606

Facility Contact Person: Contact Phone No.: 585-723-2010


Make/Model of Monitoring System: Veeder Root TLS-350R Date of Testing/Servicing: 6/3/2026

B. Inventory of Equipment Tested/Certified Check the appropriate boxes to indicate specific equipment inspected/serviced:

Tank ID: 1 RUL NYDEC 001 - REGULAR	**Tank ID:** 3 PUL NYDEC 003 - PREMIUM
☑ In-Tank Gauging Probe. Model: 846390-110	☑ In-Tank Gauging Probe. Model: 846390-110
☑ Annular Space or Vault Sensor. Model: 794380-303	☑ Annular Space or Vault Sensor. Model: 794380-303
☑ Piping Sump / Trench Sensor(s). Model: 794380-208	☑ Piping Sump / Trench Sensor(s). Model: 794380-208
☐ Fill Sump Sensor(s). Model:	☐ Fill Sump Sensor(s). Model:
☑ Mechanical Line Leak Detector. Model: FE Petro MLD	☑ Mechanical Line Leak Detector. Model: FE Petro MLD
☐ Electronic Line Leak Detector. Model:	☐ Electronic Line Leak Detector. Model:
☐ Tank Overfill / High-Level Sensor. Model:	☐ Tank Overfill / High-Level Sensor. Model:
☐ Other (specify equipment type and model in Section E on Page 2).	☐ Other (specify equipment type and model in Section E on Page 2).
Tank ID: 2 RUL NYDEC 002 - REGULAR	**Tank ID:**
☑ In-Tank Gauging Probe. Model: 846390-110	☐ In-Tank Gauging Probe. Model:
☑ Annular Space or Vault Sensor. Model: 794380-303	☐ Annular Space or Vault Sensor. Model:
☑ Piping Sump / Trench Sensor(s). Model: 794380-208	☐ Piping Sump / Trench Sensor(s). Model:
☐ Fill Sump Sensor(s). Model:	☐ Fill Sump Sensor(s). Model:
☐ Mechanical Line Leak Detector. Model:	☐ Mechanical Line Leak Detector. Model:
☐ Electronic Line Leak Detector. Model:	☐ Electronic Line Leak Detector. Model:
☐ Tank Overfill / High-Level Sensor. Model:	☐ Tank Overfill / High-Level Sensor. Model:
☐ Other (specify equipment type and model in Section E on Page 2).	☐ Other (specify equipment type and model in Section E on Page 2).
Dispenser ID: 1/2	**Dispenser ID:** 3/4
☑ Dispenser Containment Sensor(s). Model: 794380-208	☑ Dispenser Containment Sensor(s). Model: 794380-208
☑ Shear Valve(s).	☑ Shear Valve(s).
☐ Dispenser Containment Float(s) and Chain(s).	☐ Dispenser Containment Float(s) and Chain(s).
Dispenser ID: 5/6	**Dispenser ID:** 7/8
☑ Dispenser Containment Sensor(s). Model: 794380-208	☑ Dispenser Containment Sensor(s). Model: 794380-208
☑ Shear Valve(s).	☑ Shear Valve(s).
☐ Dispenser Containment Float(s) and Chain(s).	☐ Dispenser Containment Float(s) and Chain(s).
Dispenser ID: 9/10	**Dispenser ID:** 11/12
☑ Dispenser Containment Sensor(s). Model: 794380-208	☑ Dispenser Containment Sensor(s). Model: 794380-208
☑ Shear Valve(s).	☑ Shear Valve(s).
☐ Dispenser Containment Float(s) and Chain(s).	☐ Dispenser Containment Float(s) and Chain(s).

*If the facility contains more tanks or dispensers, copy this form. Include information for every tank and dispenser at the facility.

C. Certification - I certify that the equipment identified in this document was inspected/serviced in accordance with the manufacturers' guidelines. Attached to this Certification is a Plot Plan showing the layout of monitoring equipment. For any equipment capable of generating such reports, I have also attached a copy of the report; *(check all that apply)*: ☑ System set-up ☑ Alarm history report

Technician Name (print): Jeffrey Claeys Signature: 

Certification No.: B48818 License. No.:

Testing Company Name: Tanknology Phone No.: (800) 800-4633

Testing Company Address: 11000 N. MoPac Expressway Suite 500 Date of Testing/Servicing: 6/3/2026

D. Results of Testing/Servicing

Software Version Installed: 326.01

Complete the following checklist:

☑ Yes	☐ No* ☐ N/A	Is the **visual** alarm on the console operational?
☑ Yes	☐ No* ☐ N/A	Is the **audible** alarm on the console operational?
☑ Yes	☐ No	Is the external **visual** overfill alarm (light unit) present?
☑ Yes	☐ No* ☐ N/A	Is the external **visual** overfill alarm operating properly?
☑ Yes	☐ No	Is the external **audible** overfill alarm present?
☑ Yes	☐ No* ☐ N/A	Is the external **audible** overfill alarm operating properly?
90 %	☐ N/A	At what percent of tank(s) capacity is the external alarm programmed to trigger? *If different % between tanks, clarify in section E.*
☑ Yes	☐ No* ☐ N/A	Were all sensors visually inspected, functionally tested, and confirmed operational?
☑ Yes	☐ No* ☐ N/A	Were all sensors installed at lowest point of secondary containment and positioned so that other equipment will not interfere with their proper operation?
☐ Yes	☐ No* ☑ N/A	For pressurized piping systems, does the turbine automatically shut down if the piping secondary containment monitoring system detects a leak, fails to operate, or is electrically disconnected? If yes: which sensors initiate positive shut-down? *(Check all that apply)* ☐ Sump/Trench Sensors; ☐ Dispenser Containment Sensors. Did you confirm positive shut-down due to leaks and sensor failure/disconnection? ☐ Yes; ☐ No
☐ Yes*	☑ No	Was any monitoring equipment replaced? If yes, identify specific sensors, probes, or other equipment replaced and list the manufacturer name and model for all replacement parts in Section E, below.
☐ Yes*	☑ No	Was liquid found inside any secondary containment systems designed as dry systems? *(Check all that apply)* ☐ Product; ☐ Water. If yes, describe causes in Section E, below.
☑ Yes	☐ No*	Was monitoring system set-up reviewed to ensure proper settings? Attach set up reports, if applicable
☑ Yes	☐ No*	Is all monitoring equipment operational per manufacturer's specifications?

* In Section E below, describe how and when these deficiencies were or will be corrected.

E. Comments:

Backup Battery reading, if applicable (Required for VR TLS 300/350):3.66v

F. In-Tank Gauging / SIR Equipment:

☐ Check this box if tank gauging is used only for inventory control.
☐ Check this box if no tank gauging or SIR equipment is installed.

This section must be completed if in-tank gauging equipment is used to perform leak detection monitoring.


Complete the following checklist:

☑ Yes	☐ No*	Were all tank gauging probes visually inspected for damage and residue buildup?
☑ Yes	☐ No*	Was accuracy of system product level readings tested?
☑ Yes	☐ No*	Was accuracy of system water level readings tested?
☑ Yes	☐ No*	Were all probes reinstalled properly?
☑ Yes	☐ No*	Were all items on the equipment manufacturer's maintenance checklist completed?

* In the Section G, below, describe how and when these deficiencies were or will be corrected.

G. Comments:

DID OVERALL MONITOR SYSTEM TESTING PASS (Check One)? YES☑ NO ☐ INCONCLUSIVE ☐

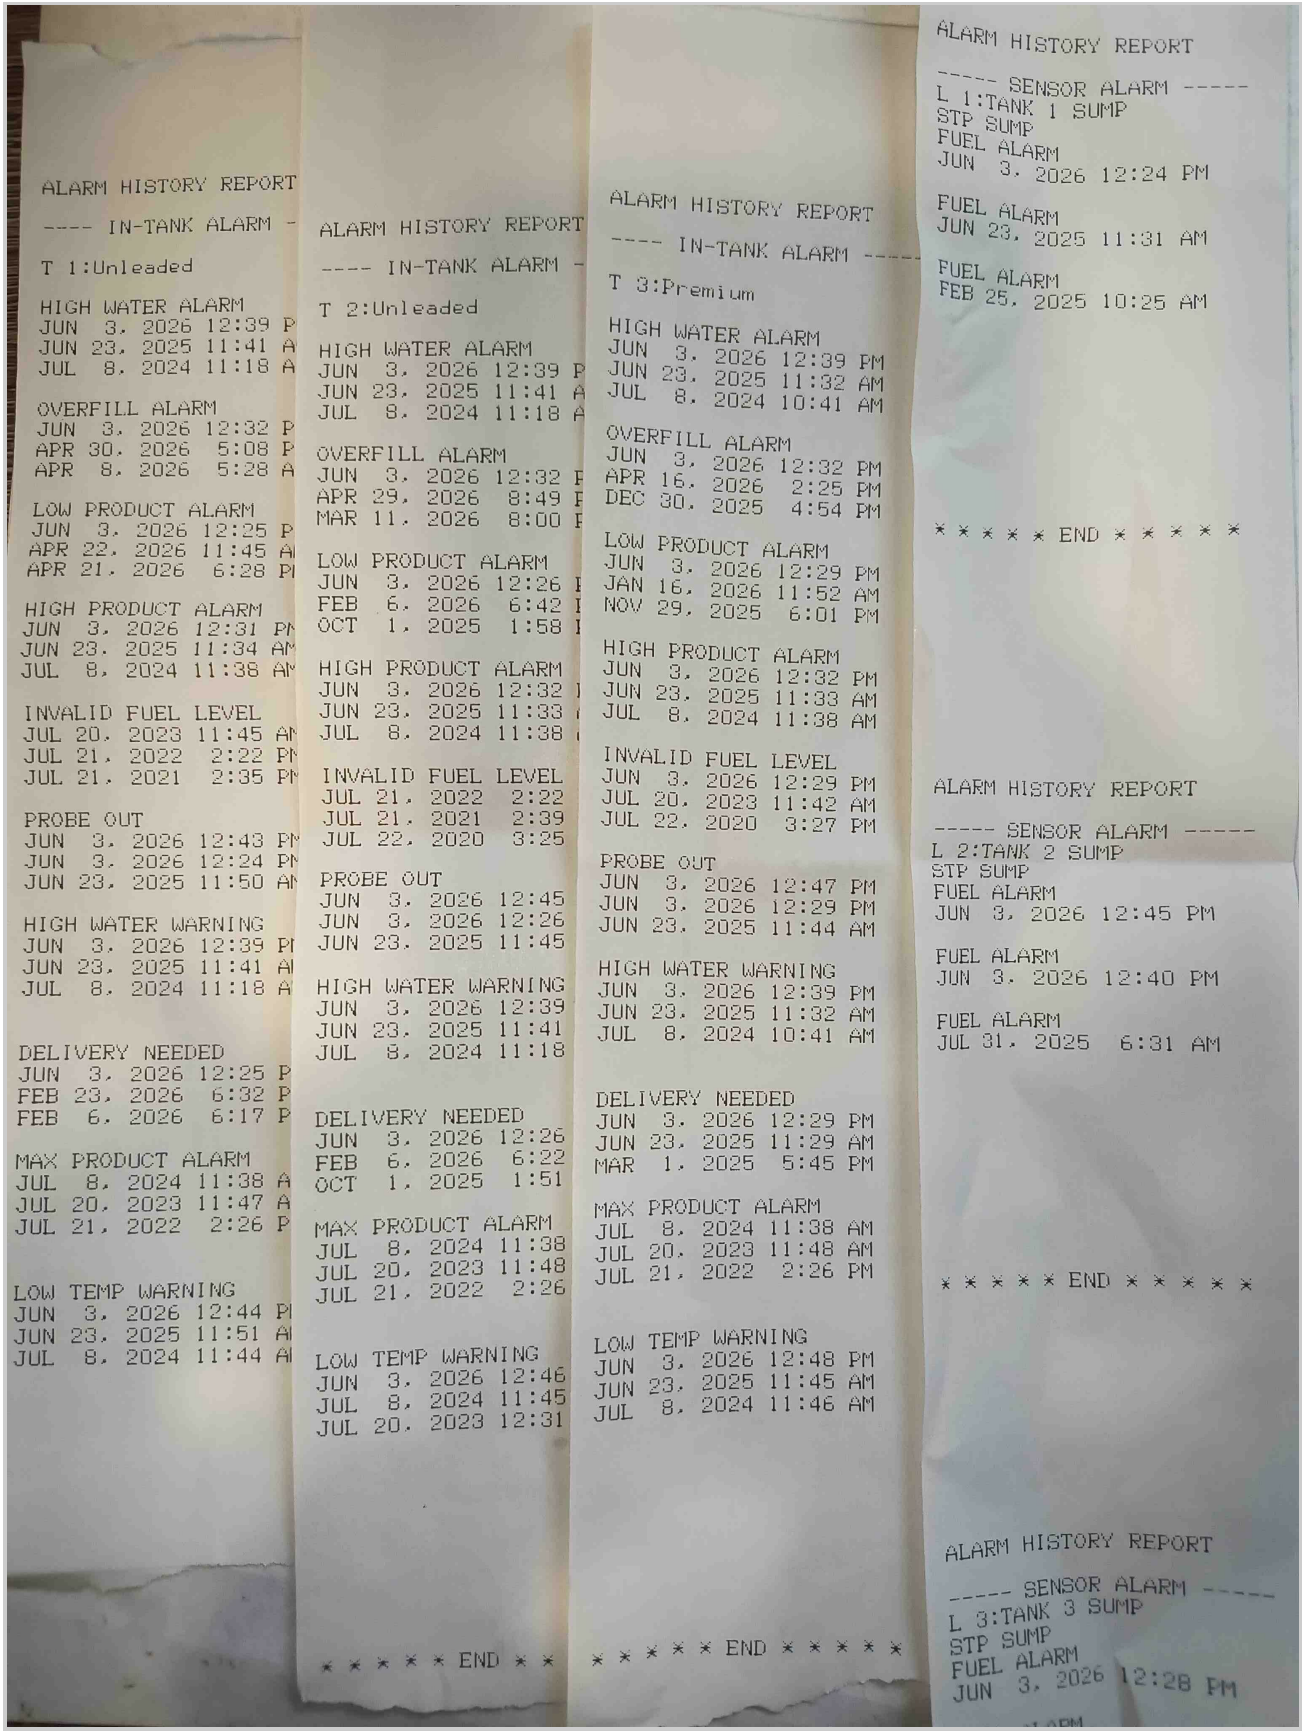

ALARM HISTORY REPORT

---- IN-TANK ALARM -

T 1:Unleaded

HIGH WATER ALARM
JUN 3. 2026 12:39 P
JUN 23. 2025 11:41 A
JUL 8. 2024 11:18 A

OVERFILL ALARM
JUN 3. 2026 12:32 P
APR 30. 2026 5:08 P
APR 8. 2026 5:28 A

LOW PRODUCT ALARM
JUN 3. 2026 12:25 P
APR 22. 2026 11:45 A
APR 21. 2026 6:28 P

HIGH PRODUCT ALARM
JUN 3. 2026 12:31 PM
JUN 23. 2025 11:34 AM
JUL 8. 2024 11:38 AM

INVALID FUEL LEVEL
JUL 20. 2023 11:45 AM
JUL 21. 2022 2:22 PM
JUL 21. 2021 2:35 PM

PROBE OUT
JUN 3. 2026 12:43 PM
JUN 3. 2026 12:24 PM
JUN 23. 2025 11:50 AM

HIGH WATER WARNING
JUN 3. 2026 12:39 P
JUN 23. 2025 11:41 A
JUL 8. 2024 11:18 A

DELIVERY NEEDED
JUN 3. 2026 12:25 P
FEB 23. 2026 6:32 P
FEB 6. 2026 6:17 P

MAX PRODUCT ALARM
JUL 8. 2024 11:38 A
JUL 20. 2023 11:47 A
JUL 21. 2022 2:26 P

LOW TEMP WARNING
JUN 3. 2026 12:44 P
JUN 23. 2025 11:51 A
JUL 8. 2024 11:44 A

ALARM HISTORY REPORT

---- IN-TANK ALARM -

T 2:Unleaded

HIGH WATER ALARM
JUN 3. 2026 12:39 P
JUN 23. 2025 11:41 A
JUL 8. 2024 11:18 A

OVERFILL ALARM
JUN 3. 2026 12:32 P
APR 29. 2026 8:49 P
MAR 11. 2026 8:00 P

LOW PRODUCT ALARM
JUN 3. 2026 12:26 P
FEB 6. 2026 6:42 P
OCT 1. 2025 1:58 P

HIGH PRODUCT ALARM
JUN 3. 2026 12:32 P
JUN 23. 2025 11:33 A
JUL 8. 2024 11:38 A

INVALID FUEL LEVEL
JUL 21. 2022 2:22
JUL 21. 2021 2:39
JUL 22. 2020 3:25

PROBE OUT
JUN 3. 2026 12:45
JUN 3. 2026 12:26
JUN 23. 2025 11:45

HIGH WATER WARNING
JUN 3. 2026 12:39
JUN 23. 2025 11:41
JUL 8. 2024 11:18

DELIVERY NEEDED
JUN 3. 2026 12:26
FEB 6. 2026 6:22
OCT 1. 2025 1:51

MAX PRODUCT ALARM
JUL 8. 2024 11:38
JUL 20. 2023 11:48
JUL 21. 2022 2:26

LOW TEMP WARNING
JUN 3. 2026 12:46
JUL 8. 2024 11:45
JUL 20. 2023 12:31

* * * * * END * *

ALARM HISTORY REPORT

---- IN-TANK ALARM -----

T 3:Premium

HIGH WATER ALARM
JUN 3. 2026 12:39 PM
JUN 23. 2025 11:32 AM
JUL 8. 2024 10:41 AM

OVERFILL ALARM
JUN 3. 2026 12:32 PM
APR 16. 2026 2:25 PM
DEC 30. 2025 4:54 PM

LOW PRODUCT ALARM
JUN 3. 2026 12:29 PM
JAN 16. 2026 11:52 AM
NOV 29. 2025 6:01 PM

HIGH PRODUCT ALARM
JUN 3. 2026 12:32 PM
JUN 23. 2025 11:33 AM
JUL 8. 2024 11:38 AM

INVALID FUEL LEVEL
JUN 3. 2026 12:29 PM
JUL 20. 2023 11:42 AM
JUL 22. 2020 3:27 PM

PROBE OUT
JUN 3. 2026 12:47 PM
JUN 3. 2026 12:29 PM
JUN 23. 2025 11:44 AM

HIGH WATER WARNING
JUN 3. 2026 12:39 PM
JUN 23. 2025 11:32 AM
JUL 8. 2024 10:41 AM

DELIVERY NEEDED
JUN 3. 2026 12:29 PM
JUN 23. 2025 11:29 AM
MAR 1. 2025 5:45 PM

MAX PRODUCT ALARM
JUL 8. 2024 11:38 AM
JUL 20. 2023 11:48 AM
JUL 21. 2022 2:26 PM

LOW TEMP WARNING
JUN 3. 2026 12:48 PM
JUN 23. 2025 11:45 AM
JUL 8. 2024 11:46 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 1:TANK 1 SUMP
STP SUMP
FUEL ALARM
JUN 3. 2026 12:24 PM

FUEL ALARM
JUN 23. 2025 11:31 AM

FUEL ALARM
FEB 25. 2025 10:25 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 2:TANK 2 SUMP
STP SUMP
FUEL ALARM
JUN 3. 2026 12:45 PM


FUEL ALARM
JUN 3. 2026 12:40 PM

FUEL ALARM
JUL 31. 2025 6:31 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 3:TANK 3 SUMP
STP SUMP
FUEL ALARM
JUN 3. 2026 12:28 PM

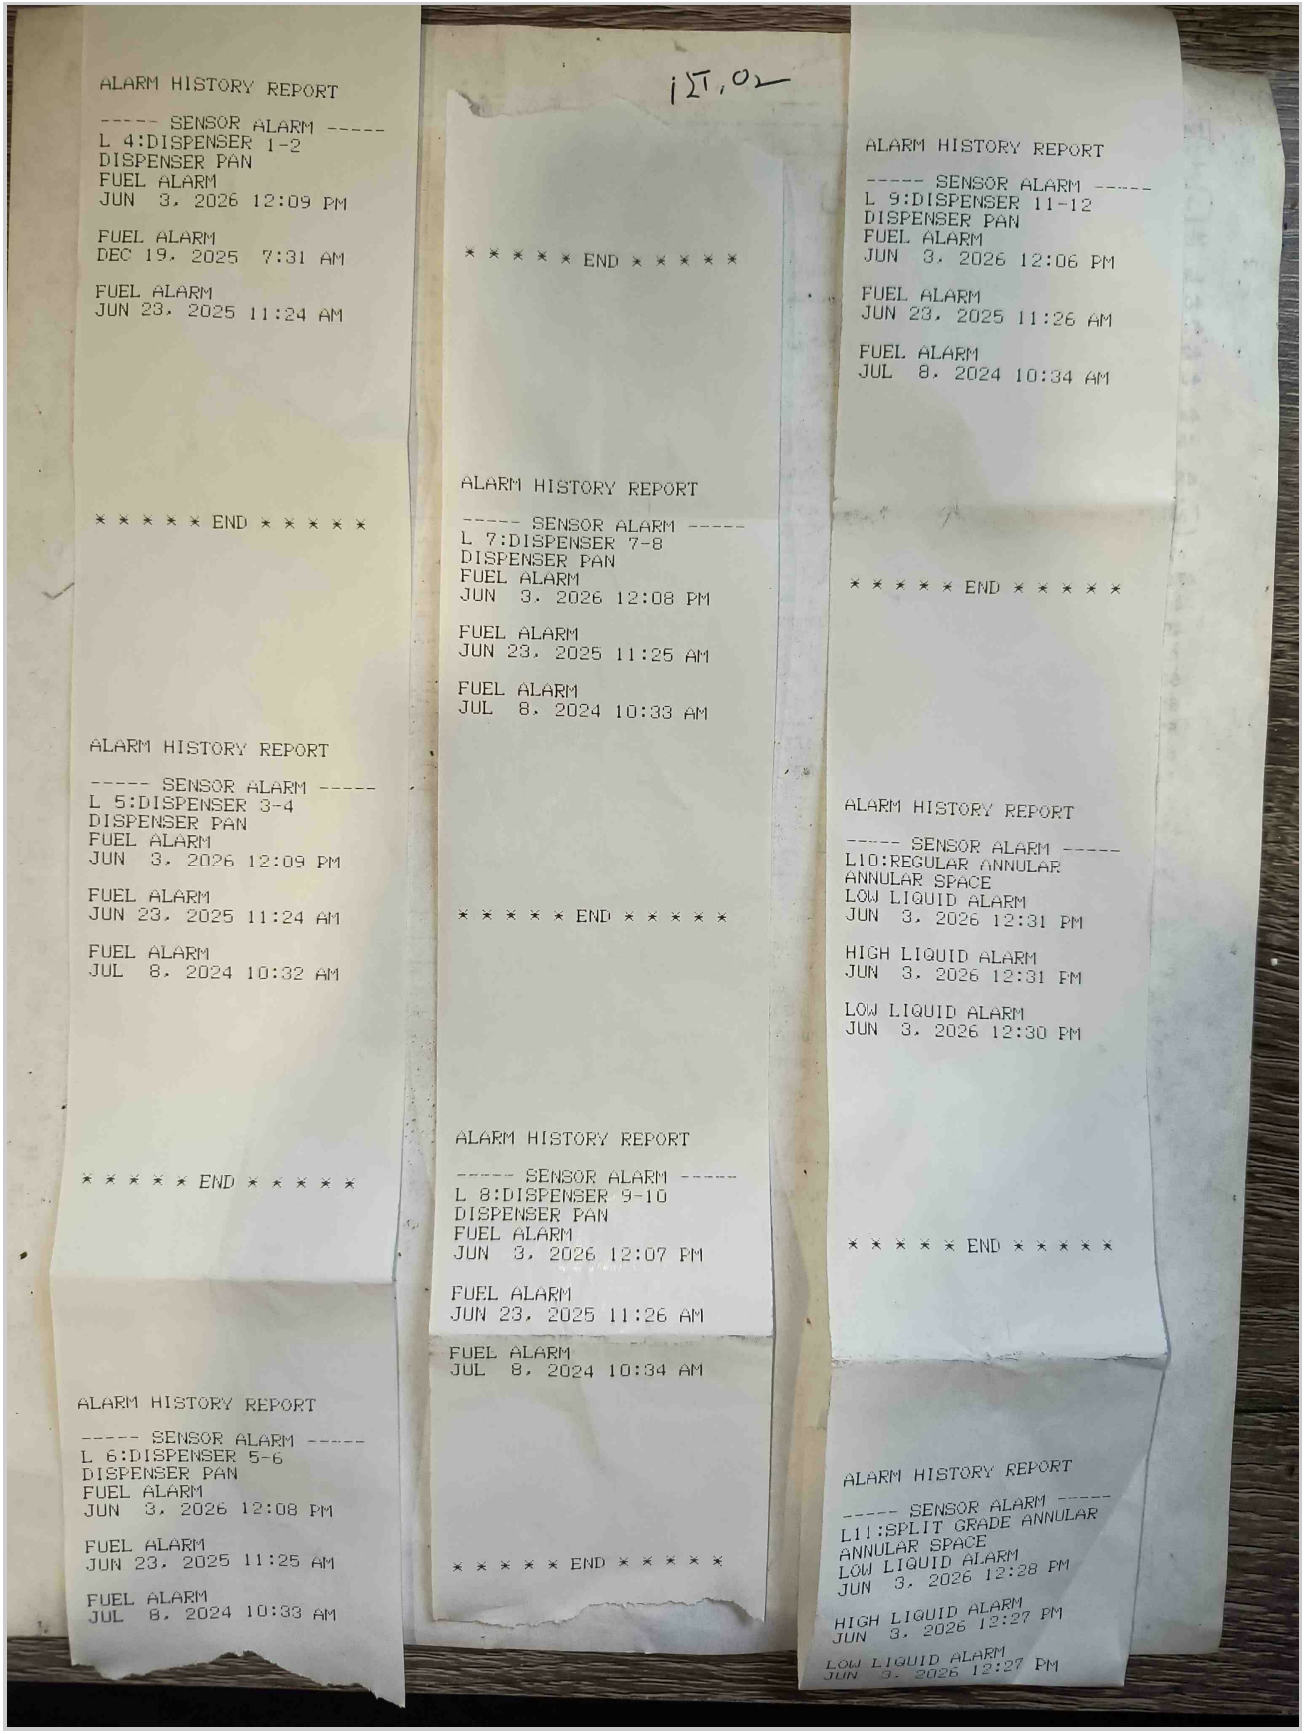

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 4:DISPENSER 1-2
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:09 PM

FUEL ALARM
DEC 19, 2025 7:31 AM

FUEL ALARM
JUN 23, 2025 11:24 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 5:DISPENSER 3-4
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:09 PM

FUEL ALARM
JUN 23, 2025 11:24 AM

FUEL ALARM
JUL 8, 2024 10:32 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 6:DISPENSER 5-6
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:08 PM

FUEL ALARM
JUN 23, 2025 11:25 AM

FUEL ALARM
JUL 8, 2024 10:33 AM

1ST, 02

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 7:DISPENSER 7-8
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:08 PM

FUEL ALARM
JUN 23, 2025 11:25 AM

FUEL ALARM
JUL 8, 2024 10:33 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 8:DISPENSER 9-10
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:07 PM

FUEL ALARM
JUN 23, 2025 11:26 AM

FUEL ALARM
JUL 8, 2024 10:34 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L 9:DISPENSER 11-12
DISPENSER PAN
FUEL ALARM
JUN 3, 2026 12:06 PM

FUEL ALARM
JUN 23, 2025 11:26 AM

FUEL ALARM
JUL 8, 2024 10:34 AM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L10:REGULAR ANNULAR
ANNULAR SPACE
LOW LIQUID ALARM
JUN 3, 2026 12:31 PM

HIGH LIQUID ALARM
JUN 3, 2026 12:31 PM

LOW LIQUID ALARM
JUN 3, 2026 12:30 PM

* * * * * END * * * * *

ALARM HISTORY REPORT

----- SENSOR ALARM -----
L11:SPLIT GRADE ANNULAR
ANNULAR SPACE
LOW LIQUID ALARM
JUN 3, 2026 12:28 PM

HIGH LIQUID ALARM
JUN 3, 2026 12:27 PM

LOW LIQUID ALARM
JUN 3, 2026 12:27 PM
