

From: [Brussel, John](#)
To: [Scharf, Steven \(DEC\)](#)
Cc: [Murphy, Katy H \(DEC\)](#); [Ockerby, Renata E \(HEALTH\)](#); [Scott Krall](#); [Dave Paule \(dave.paule@bayer.com\)](#); [Enigk, Andrew](#); [Kingsley, David](#); [McDermott, Gregory](#); [Hurst, Chris \(churst@posillicoinc.com\)](#); [Julia Schneider \(JSchneider@csfllc.com\)](#)
Subject: For NYSDEC/NYSDOH Information: Updated Project Schedule, Bayer Hicksville (NYSDEC Site #130004)
Date: Wednesday, November 19, 2014 2:52:06 PM
Attachments: [schedule.hw130004.2014-11-19.Bayer Hicksville OU4 RA Project Schedule \(Updated\).pdf](#)

Steve,

As a follow-up to discussions during this morning's weekly construction coordination call, please find the attached PDF file containing an updated project schedule prepared by Bayer's remedial contractor, Posillico Environmental, Inc., for implementation of remedial activities at the Bayer Hicksville site. This is an updated version of the schedule that was most recently provided in Weekly Progress Report #9 (submitted on November 12, 2014).

As indicated during this morning's call, the off-site transportation of TSCA-regulated PCB waste/NYS listed hazardous waste to the Model City Landfill (which is shown on the schedule to take place this week) has been postponed due to the lake effect snow storm in western New York that has closed highways and resulted in a state of emergency. T&D of that waste is now anticipated to begin next week.

The remedial project schedule is subject to further change based on availability of waste transporters and weather conditions. The schedule will continue to be updated as work progresses.

Feel free to call Scott Krall of Bayer at 412.777.5568 or me if you have any questions or need additional information.

Thank you.

-John

John C. Brussel | Principal Engineer/Certified Project Manager | John.Brussel@arcadis-us.com

ARCADIS U.S., Inc. | 6723 Towpath Road, Box 66 | Syracuse, NY 13214-0066

T: 315 671 9441 | M: 315 317 8104 | F: 315 449 4111


www.arcadis-us.com

Professional Affiliate/ ARCADIS of New York, Inc.

Professional Registration/ PE-NY #075208

ARCADIS, Imagine the result

Please consider the environment before printing this email.

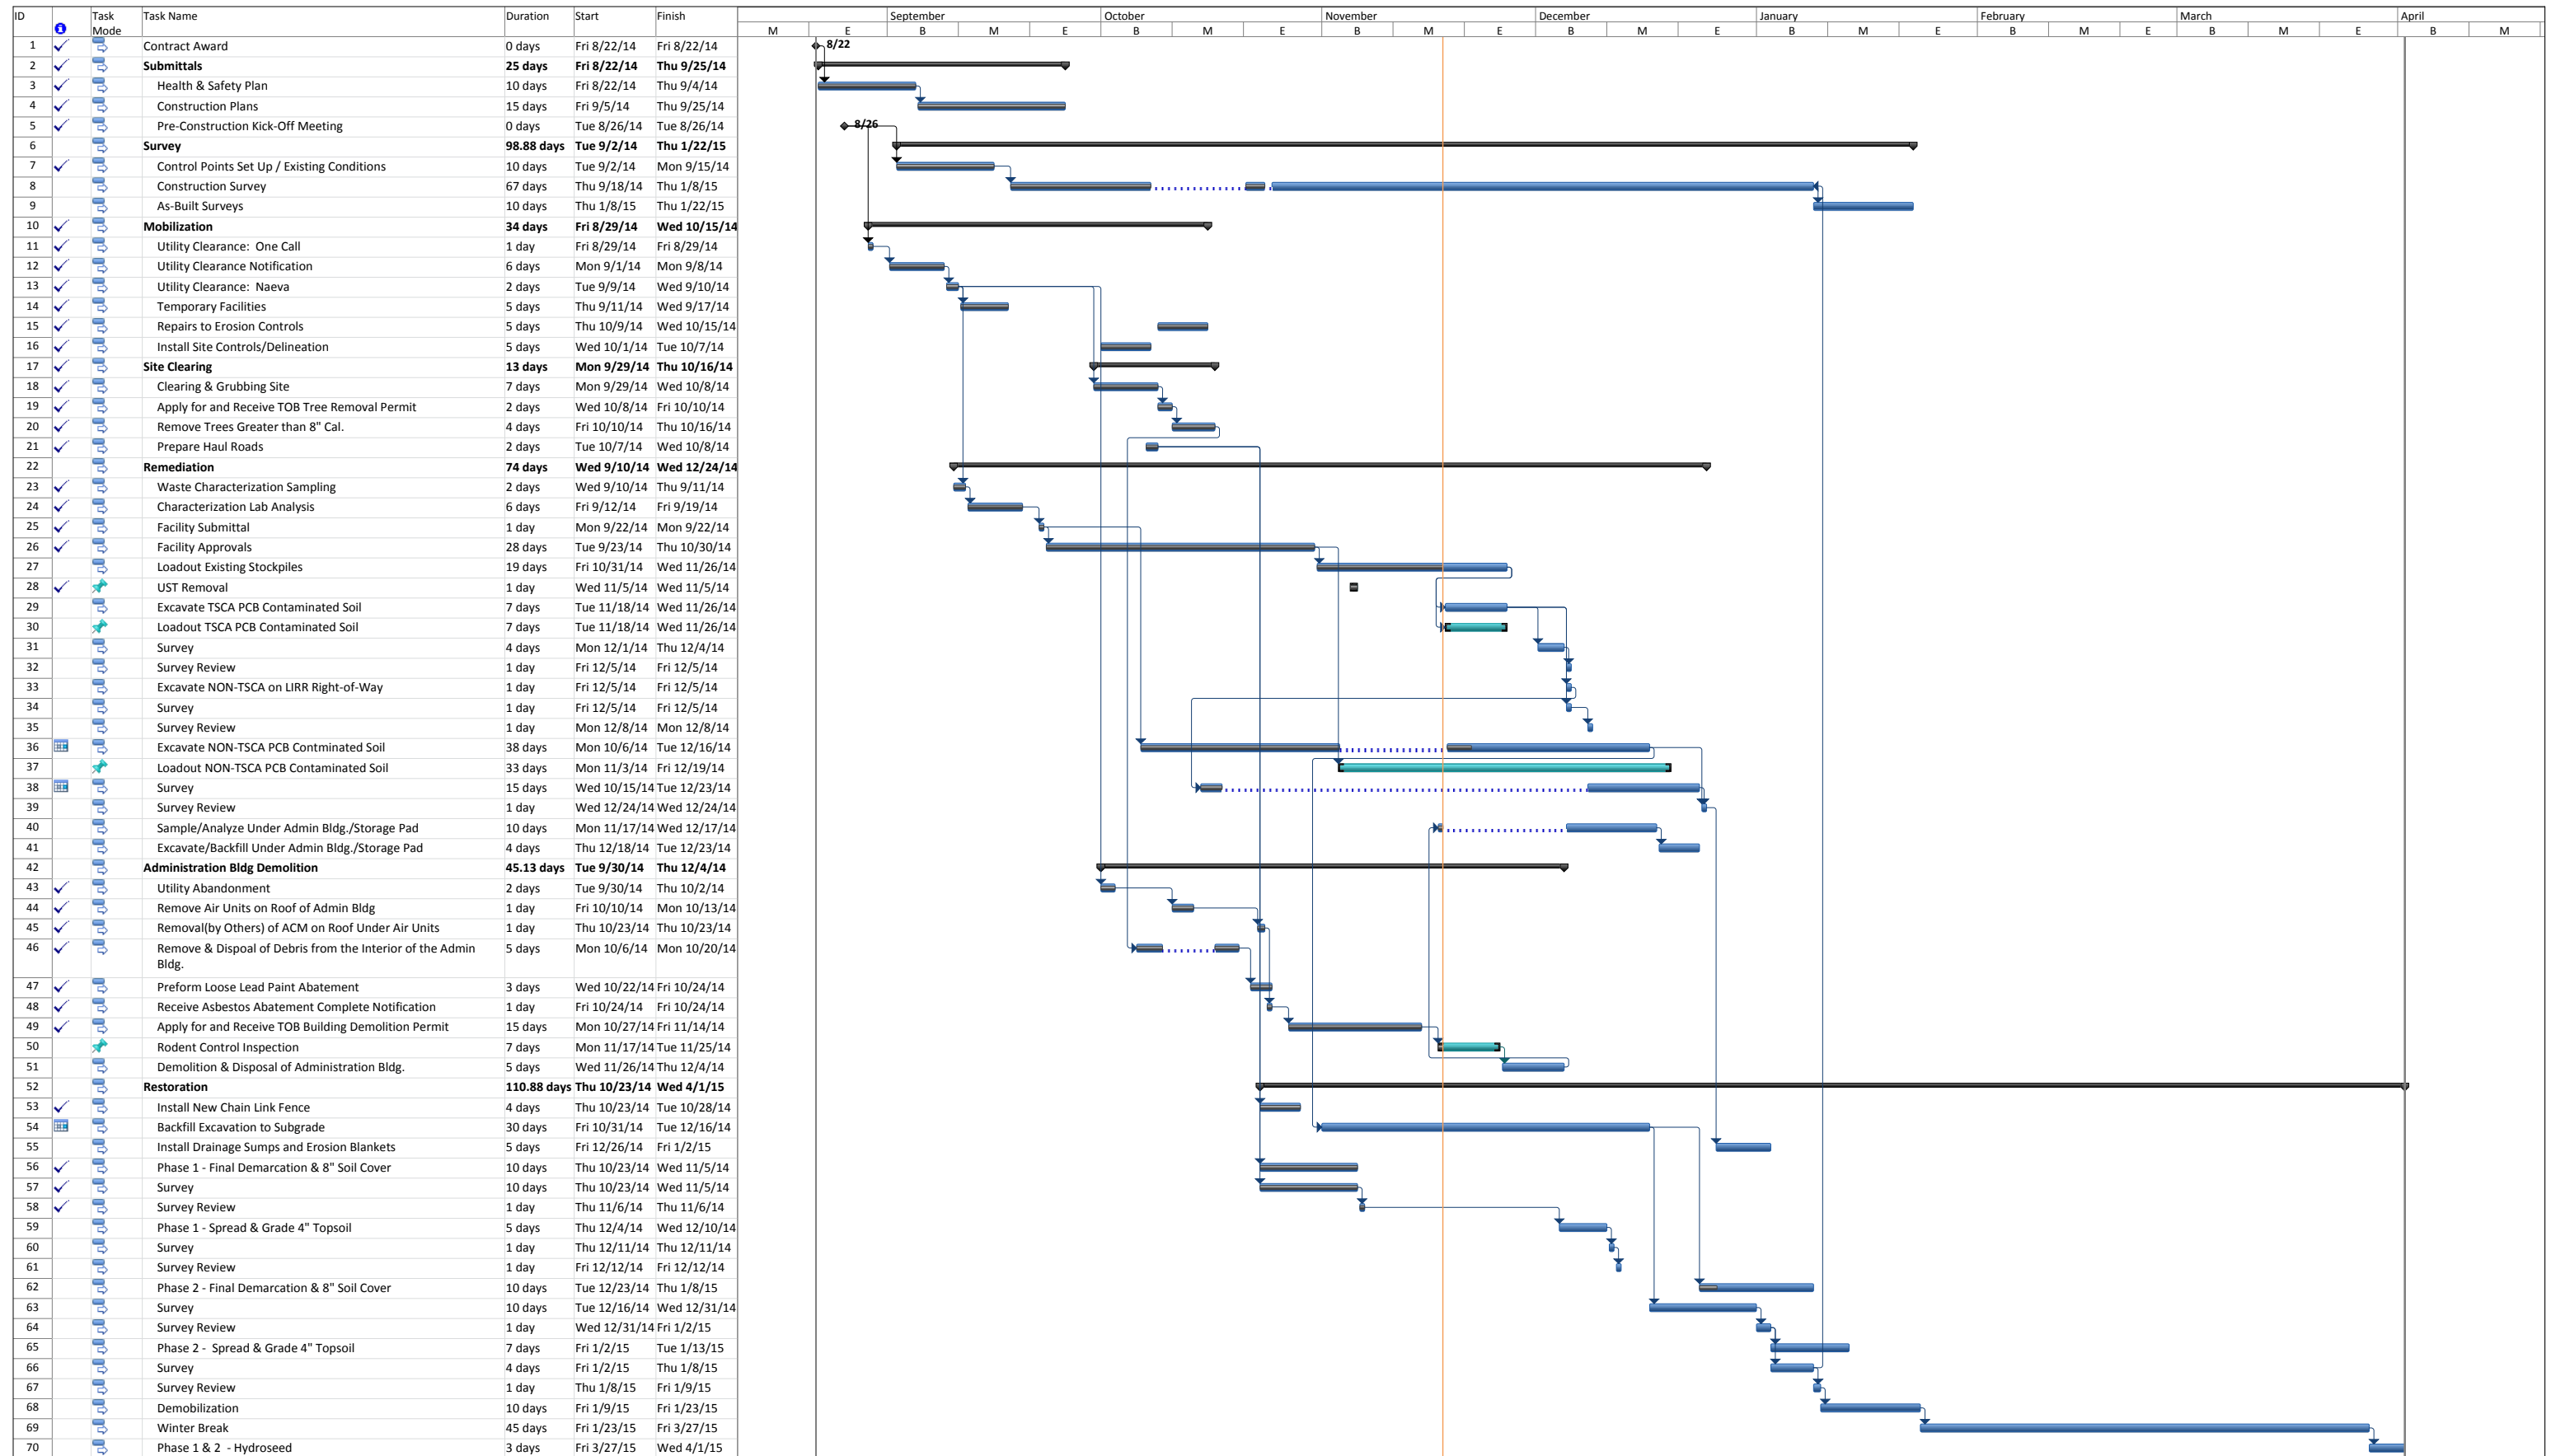

Project: Bayer Revised baseline CP
Date: Tue 11/18/14

Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Baseline Milestone
Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Baseline Summary
Milestone	Inactive Milestone	Duration-only	Start-only	Baseline	Progress
