Avalon Yonkers RAWP Schedule
April 10, 2018

ID	Task Name	Duration	Start	Finish
1				
2	AVALON YONKERS	3 days	Mon 4/2/18	Wed 4/4/18
3				
4	**PC WEST**	**72 days**	**Thu 4/5/18**	**Fri 7/13/18**
5	Contract Award	5 days	Thu 4/5/18	Wed 4/11/18
6	Submittals	5 days	Thu 4/12/18	Wed 4/18/18
7	Pre-Construction Meeting	1 day	Thu 4/12/18	Thu 4/12/18
8	Mobilization	4 days	Mon 4/16/18	Thu 4/19/18
9	Site Grading, Slurry Wall Trench Test Pit, ATI CSO Pipe Vac-Tron Locate	3 days	Fri 4/20/18	Tue 4/24/18
10	Excavate & Backfill Remedial Areas	30 days	Mon 4/23/18	Fri 6/1/18
11	Remediate the Peninsula Area & Install Slurry Wall	8 days	Mon 4/30/18	Wed 5/9/18
12	Install Anti-Seep Collars @ CSO	5 days	Thu 5/10/18	Wed 5/16/18
13	Install Pile Plugs as Required	5 days	Thu 5/17/18	Wed 5/23/18
14	Prep Area @ ISS Locations	2 days	Thu 5/17/18	Fri 5/18/18
15	SOE as Required	2 days	Mon 5/21/18	Tue 5/22/18
16	Install ISS, Bucket Mix	20 days	Wed 5/23/18	Tue 6/19/18
17	Handling, breaking, Placement of ISS Swell-Reuse on Site	25 days	Fri 5/18/18	Thu 6/21/18
18	QA/QC Testing ISS Units	5 days	Wed 6/20/18	Tue 6/26/18
19	Spoils Management, loading T & D	20 days	Wed 5/30/18	Tue 6/26/18
20	Final Grading	3 days	Wed 6/27/18	Fri 6/29/18
21	Close Out	10 days	Mon 7/2/18	Fri 7/13/18
22				
23	**PC EAST**	**44 days**	**Wed 6/6/18**	**Mon 8/6/18**
24	Mobilization	1 day	Wed 6/6/18	Wed 6/6/18
25	Excavate & Backfill Remedial Areas	12 days	Thu 6/7/18	Fri 6/22/18
26	Prep Area @ ISS Locations	2 days	Thu 6/14/18	Fri 6/15/18
27	SOE as Required	2 days	Mon 6/18/18	Tue 6/19/18
28	Install ISS, Bucket Mix	10 days	Wed 6/20/18	Tue 7/3/18
29	Handling, breaking, Placement of ISS Swell-Reuse on Site	8 days	Fri 6/22/18	Tue 7/3/18
30	QA/QC Testing ISS Units	10 days	Wed 7/4/18	Tue 7/17/18
31	Spoils Management, loading T & D	12 days	Wed 7/4/18	Thu 7/19/18
32	Final Grading	2 days	Fri 7/20/18	Mon 7/23/18
33	Close Out	10 days	Tue 7/24/18	Mon 8/6/18

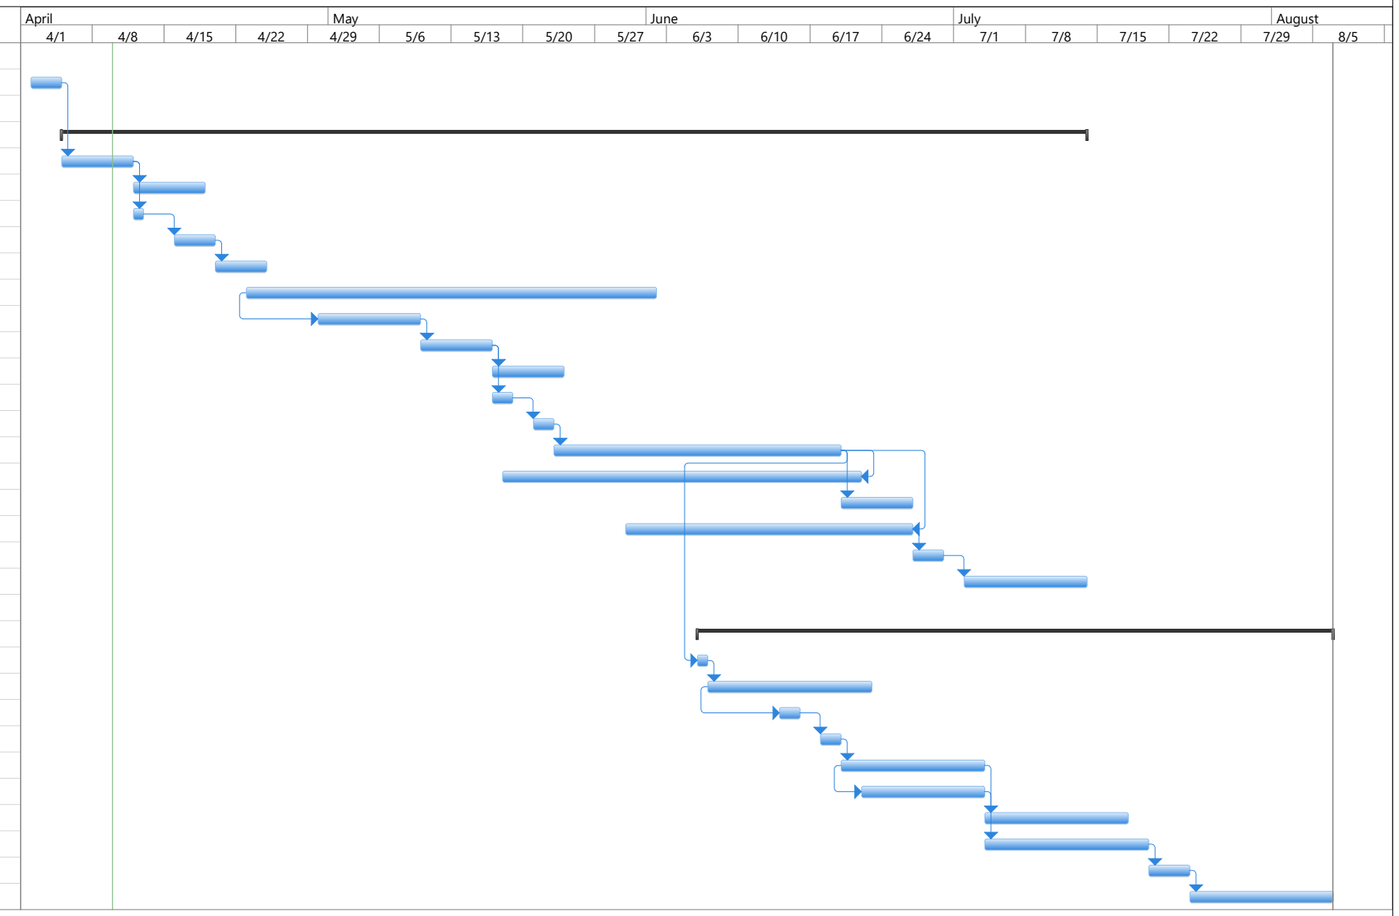

Project: AVB Yonkers Remediat
Date: Tue 4/10/18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
